

**398<sup>th</sup>**  
**FLASH REPORT**  
**ON**  
**CENTRAL SECTOR PROJECTS**  
**(Rs.150 crore and above)**  
**December 2018**



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



Government of India  
**Ministry of Statistics and Programme Implementation**  
**Infrastructure and Project Monitoring Division**  
R.K.Puarm, East Block 6, Level 7  
New Delhi-110066  
Website: [www.cspm.gov.in](http://www.cspm.gov.in)

## **Abbreviations used in the report**

|                |                                            |
|----------------|--------------------------------------------|
| <b>AAI</b>     | Airport Authority of India Ltd.            |
| <b>AERB</b>    | Atomic Energy Regulatory Board             |
| <b>AIBP</b>    | Accelerated Irrigation Benefit Programme   |
| <b>AIR</b>     | All India Radio                            |
| <b>APW</b>     | Active Process Water                       |
| <b>ATU</b>     | Atomic Treating Unit                       |
| <b>BCM</b>     | Billion Cubic Meter                        |
| <b>BHEL</b>    | Bharat Heavy Electricals Ltd.              |
| <b>BHPV</b>    | Bharat Heavy Plates & Vessel Ltd.          |
| <b>BLU</b>     | Boiler Light Up                            |
| <b>BOLT</b>    | Build , Operate, Lease & Transfer          |
| <b>BPST</b>    | Bureau of Parliamentary Studies & Training |
| <b>CCEA</b>    | Cabinet Committee on Economic Affairs      |
| <b>CCU</b>     | Catalytic Cracking Unit                    |
| <b>CDS</b>     | Crude Distribution System                  |
| <b>CDU</b>     | Crude Distillation Unit                    |
| <b>CEA</b>     | Central Electricity Authority              |
| <b>CEC</b>     | Central Empowered Committee                |
| <b>CHP</b>     | Coal Handling Plant                        |
| <b>CLW</b>     | Chittaranjan Locomotive Works              |
| <b>CMPDI</b>   | Central Mine Planning & Design Institute   |
| <b>COS</b>     | Committee of Secretaries                   |
| <b>COR</b>     | Cost Overrun                               |
| <b>CPP</b>     | Captive Power Plant                        |
| <b>CRIS</b>    | Centre for Railway Information System      |
| <b>CRL</b>     | Cochin Refinery Ltd.                       |
| <b>CSL</b>     | Cochin Shipyard Ltd.                       |
| <b>CTU</b>     | Crude Topping Unit                         |
| <b>DAE</b>     | Department of Atomic Energy                |
| <b>DB</b>      | Dumb Barges                                |
| <b>DCME</b>    | Digital Circuit Multiplexing Equipment     |
| <b>DGMS</b>    | Director General Mines Safety              |
| <b>DHDS</b>    | Diesel Hydro Desulphurisation project      |
| <b>DOA</b>     | Date of Approval                           |
| <b>DOC</b>     | Date of Commissioning                      |
| <b>DOT</b>     | Department of Telecommunication            |
| <b>DVC</b>     | Damodar Valley Corporation                 |
| <b>ECL</b>     | Eastern Coalfields Ltd.                    |
| <b>EIL</b>     | Engineers India Ltd.                       |
| <b>EMP</b>     | Environment Management Plan                |
| <b>EOT</b>     | Electrical Overhead Travelling crane       |
| <b>ESP</b>     | Electrostatic Precipitator                 |
| <b>FCCU</b>    | Fluidised Catalytic Cracker Unit           |
| <b>ERP</b>     | Enterprise Resource Planning               |
| <b>FE</b>      | Foreign Exchange                           |
| <b>FOIS</b>    | Freight Operation Information System       |
| <b>FPU</b>     | Feed Preparation Unit                      |
| <b>GAIL</b>    | Gas Authority of India Ltd.                |
| <b>GC</b>      | Gauge Conversion                           |
| <b>GDS</b>     | Gateway Digital Switch                     |
| <b>GIS</b>     | Gas Insulated Station                      |
| <b>GT</b>      | Gas Turbine                                |
| <b>GTPP</b>    | Gas Turbine Power Plant                    |
| <b>HCU</b>     | Hydro- cracker Unit                        |
| <b>HEC</b>     | Heavy Engineering Corporation              |
| <b>HEMM</b>    | Heavy Equipment & Mining Machinery         |
| <b>HEP</b>     | Hydro Electric Project                     |
| <b>HPCL</b>    | Hindustan Petroleum Corporation Ltd.       |
| <b>HRT</b>     | Head Race Tunnel                           |
| <b>HSCL</b>    | Hindustan Steel Construction Ltd.          |
| <b>HVDC</b>    | High Voltage Direct Current                |
| <b>IAAI</b>    | International Airport Authority of India   |
| <b>ICT</b>     | Inter Connecting Transformer               |
| <b>IDC</b>     | Interest During construction               |
| <b>IFFCO</b>   | Indian Farmer Fertilizer Co-operative Ltd. |
| <b>IMG</b>     | Inter Ministerial Group                    |
| <b>IOC</b>     | Indian Oil Corporation Ltd.                |
| <b>IPCL</b>    | Indian Petrochemicals Ltd.                 |
| <b>KV</b>      | Kilo Volts.                                |
| <b>L&amp;T</b> | Larsen & Toubro                            |

|                  |                                               |
|------------------|-----------------------------------------------|
| <b>LEP</b>       | Life Extension Program                        |
| <b>LOI</b>       | Letter of Intent                              |
| <b>LPG</b>       | Liquified Petroleum Gas                       |
| <b>LSTK</b>      | Lump sum Turnkey contract                     |
| <b>MAMC</b>      | Minning & Allied Machinery Corporation.       |
| <b>MFL</b>       | Madras Fertilizer Ltd.                        |
| <b>MGCL</b>      | Madras Gas Cracker Complex                    |
| <b>MIS</b>       | Management Information System                 |
| <b>MMSCMD</b>    | Million Metric Standard Cubic Meter day       |
| <b>MMT</b>       | Million Metric Tonnes                         |
| <b>MOE&amp;F</b> | Ministry of Environment & Forest              |
| <b>MT</b>        | Metric Tonnes                                 |
| <b>MTY</b>       | Metric Tonne per year                         |
| <b>MU</b>        | Million Unit                                  |
| <b>MW</b>        | Mega Watts                                    |
| <b>NAC</b>       | New Anticipated Cost                          |
| <b>NALCO</b>     | National Aluminium Company                    |
| <b>NBCC</b>      | National Building Construction Corporation.   |
| <b>NCL</b>       | Northern Coalfields Ltd                       |
| <b>NEC</b>       | North East Council                            |
| <b>NEEPCO</b>    | North-Eastern Electric Power Corporation Ltd. |
| <b>NFL</b>       | National Fertilizer Ltd.                      |
| <b>NH</b>        | National Highway                              |
| <b>NHPC</b>      | National Hydro-Electric Power Corporation     |
| <b>NIRE</b>      | National Institute of Renewable Energy        |
| <b>NIT</b>       | Notice Inviting Tender                        |
| <b>NJPC</b>      | Nathpa Jhakri Power Corporation Ltd.          |
| <b>NGN</b>       | Next Generation Network                       |
| <b>NLC</b>       | Neyveli Lignite Corporation Ltd.              |
| <b>NMDC</b>      | National Mineral Development Corporation Ltd. |
| <b>NPC</b>       | Nuclear Power Corporation Ltd.                |
| <b>NRL</b>       | Numaligarh Refinery Ltd.                      |
| <b>OB</b>        | Over Burden                                   |
| <b>OC</b>        | Opencast                                      |
| <b>OECE</b>      | Overseas Economic Co-operation Fund           |
| <b>ONGC</b>      | Oil & Natural Gas Commission                  |
| <b>OPGC</b>      | Orissa Power Generation Corporation           |
| <b>P &amp; M</b> | Plant & Machinery                             |
| <b>PERT</b>      | Project Evaluation & Review Technique         |
| <b>PSTN</b>      | Public Switched Telephone Network             |
| <b>PHT</b>       | Primary Heat Transport                        |
| <b>PIB</b>       | Public Investment Board                       |
| <b>PSLW</b>      | Powered Support Longwall                      |
| <b>QRC</b>       | Quick Roll Changer                            |
| <b>RAPP</b>      | Rajasthan Atomic Power Plant                  |
| <b>RCE</b>       | Revised Cost Estimates                        |
| <b>RCF</b>       | Railway Coach Factory                         |
| <b>ROB</b>       | Road Over Bridge                              |
| <b>ROH</b>       | Regular Overhauling                           |
| <b>RTU</b>       | Remote Terminal Unit                          |
| <b>SAIL</b>      | Steel Authority of India Ltd.                 |
| <b>SCI</b>       | Shipping Corporation of India Ltd.            |
| <b>SDH</b>       | Synchronous Digital Hierarchy                 |
| <b>SG</b>        | Steam Generator                               |
| <b>SP</b>        | Self Propelled                                |
| <b>ST</b>        | Steam Turbine                                 |
| <b>STPS</b>      | Super Thermal Power Station                   |
| <b>SUR</b>       | Sulphur Recovery Unit                         |
| <b>SWSU</b>      | Sour Water Stripping Unit                     |
| <b>TBM</b>       | Tunnel Boring Machine                         |
| <b>TG</b>        | Turbo Generator                               |
| <b>TPA</b>       | Tonnes Per Annum                              |
| <b>TPS</b>       | Thermal Power Station                         |
| <b>TOR</b>       | Time Overrun                                  |
| <b>TPY</b>       | Tonnes per year                               |
| <b>UG</b>        | Under Ground                                  |
| <b>ULDCS</b>     | Unified Load Despatch & Communication Scheme  |
| <b>VDU</b>       | Vacuum Distillation Unit                      |
| <b>WHRB</b>      | Waste Heat Recovery Boiler                    |
| <b>WO_DOC</b>    | With out Date of Commissioning                |
| <b>WO_ODC</b>    | With out original Date of Commissioning       |

## EXECUTIVE SUMMARY

1. The Flash Report for December 2018 contains information on the status of the 1424 Central Sector Infrastructure Projects costing ₹150 crore and above. During December 2018, 22 projects (10 projects in Power, 4 projects from Railways, 3 projects are in Petroleum, 2 projects are in Road Transport and Highways, and 1 project each from Coal, Health and Family Welfare and Telecommunication sectors) have reported completion.

2. During the reference month, out of 1424 projects, 384 projects are delayed with respect to their original schedules and 69 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 69 projects, 16 are Mega Projects costing ₹1000 crore and above.

| S.No. | Sector                      | Projects on monitor (No.) | Delayed Projects w.r.t original schedule (No.) | Additionally delayed during the month under report (No.) | Additionally delayed Mega Projects (No.) |
|-------|-----------------------------|---------------------------|------------------------------------------------|----------------------------------------------------------|------------------------------------------|
| 1     | ROAD TRANSPORT AND HIGHWAYS | 605                       | 112                                            | 19                                                       | 2                                        |
| 2     | RAILWAYS                    | 367                       | 94                                             | 8                                                        | 3                                        |
| 3     | PETROLEUM                   | 137                       | 33                                             | 16                                                       | 4                                        |
| 4     | COAL                        | 97                        | 36                                             | 1                                                        | 0                                        |
| 5     | POWER                       | 95                        | 56                                             | 19                                                       | 7                                        |
| 6     | URBAN DEVELOPMENT           | 58                        | 23                                             | 0                                                        | 0                                        |
| 7     | HEALTH AND FAMILY WELFARE   | 20                        | 5                                              | 1                                                        | 0                                        |
| 8     | STEEL                       | 13                        | 9                                              | 0                                                        | 0                                        |
| 9     | FERTILISERS                 | 6                         | 2                                              | 1                                                        | 0                                        |
| 10    | SHIPPING AND PORTS          | 6                         | 3                                              | 0                                                        | 0                                        |
| 11    | TELECOMMUNICATIONS          | 6                         | 4                                              | 3                                                        | 0                                        |
| 12    | MINES                       | 5                         | 0                                              | 1                                                        | 0                                        |
| 13    | ATOMIC ENERGY               | 4                         | 4                                              | 0                                                        | 0                                        |
| 14    | DEFENCE PRODUCTION          | 2                         | 1                                              | 0                                                        | 0                                        |
| 15    | CIVIL AVIATION              | 1                         | 1                                              | 0                                                        | 0                                        |
| 16    | HEAVY INDUSTRY              | 2                         | 1                                              | 0                                                        | 0                                        |
| Total |                             | 1424                      | 384                                            | 69                                                       | 16                                       |

3. Total original cost of implementation of the 1424 projects was ₹18,17,469.76 crore and their anticipated completion cost is likely to be ₹21,33,649.81 crore, which reflects overall cost overruns of ₹3,16,180.05 crore (17.40% of original cost). The expenditure incurred on these projects till December 2018 is ₹8,06,997.78 crore, which is 37.82% of the anticipated cost of the projects. The



sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns (as on 01-01-2019)**

| SN                                 | PROJECT                                                                    | DOA     | COST ORIGINAL (Rs. crore) | COST ANTICIPATED (Rs. crore) | COR (%) |
|------------------------------------|----------------------------------------------------------------------------|---------|---------------------------|------------------------------|---------|
| <b>ATOMIC ENERGY</b>               |                                                                            |         |                           |                              |         |
| 1                                  | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)                          | 09/2003 | 3492.00                   | 6100.00                      | 74.68   |
| 2                                  | KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4                                    | 10/2009 | 11459.00                  | 16580.00                     | 44.69   |
| <b>CIVIL AVIATION</b>              |                                                                            |         |                           |                              |         |
| 1                                  | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR | 10/2013 | 314.61                    | 441.33                       | 40.28   |
| <b>COAL</b>                        |                                                                            |         |                           |                              |         |
| 1                                  | JAGANNATHPOR OCP(3.00MTY)                                                  | 09/2008 | 152.43                    | 459.49                       | 201.44  |
| 2                                  | BHANEGAON OC                                                               | 02/2015 | 187.94                    | 409.68                       | 117.98  |
| 3                                  | RCE OF INDARAM OCP(1.20 MTPA)                                              | 07/2011 | 162.76                    | 349.28                       | 114.60  |
| 4                                  | NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI                    | 10/2007 | 259.40                    | 486.57                       | 87.58   |
| 5                                  | SHANTIKHANI LONGWALL PROJ-SCCL                                             | 10/2006 | 249.03                    | 448.86                       | 80.24   |
| <b>DEFENCE PRODUCTION</b>          |                                                                            |         |                           |                              |         |
| 1                                  | CONSTRUCTION WORKS PHASE 3B                                                | 12/2016 | 285.95                    | 291.29                       | 1.87    |
| 2                                  | CONSTRUCTION WORKS PHASE 4                                                 | 12/2016 | 167.69                    | 170.37                       | 1.60    |
| <b>FERTILISERS</b>                 |                                                                            |         |                           |                              |         |
| 1                                  | NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY                            | 10/2014 | 197.79                    | 209.44                       | 5.89    |
| <b>HEALTH AND FAMILY WELFARE</b>   |                                                                            |         |                           |                              |         |
| 1                                  | LHMC NEW DELHI-RE-DEVELOPMENT                                              | 02/2013 | 414.11                    | 513.89                       | 24.10   |
| 2                                  | CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR                         | 09/2014 | 505.58                    | 523.00                       | 3.45    |
| 3                                  | GERIATRICS BLOCK- AIIMS DLEHI                                              | 12/2017 | 156.56                    | 156.65                       | 0.06    |
| <b>HEAVY INDUSTRY</b>              |                                                                            |         |                           |                              |         |
| 1                                  | NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)         | 04/2011 | 1718.00                   | 3827.30                      | 122.78  |
| <b>PETROLEUM</b>                   |                                                                            |         |                           |                              |         |
| 1                                  | URAN CHAKAN SHIKRAPUR LPG PIPELINE                                         | 12/2009 | 309.81                    | 723.40                       | 133.50  |
| 2                                  | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)    | 03/2011 | 861.79                    | 1577.15                      | 83.01   |
| 3                                  | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR                               | 01/2006 | 993.00                    | 1693.00                      | 70.49   |
| 4                                  | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)     | 06/2010 | 202.94                    | 330.35                       | 62.78   |
| 5                                  | PARADIP HYDERABAD PIPELINE                                                 | 01/2015 | 2321.00                   | 3338.00                      | 43.82   |
| <b>POWER</b>                       |                                                                            |         |                           |                              |         |
| 1                                  | SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)                                    | 09/2003 | 6285.33                   | 19496.34                     | 210.19  |
| 2                                  | TEHRI PUMPED STORAGE PLANT(1000MW)                                         | 07/2006 | 1657.00                   | 4401.90                      | 165.65  |
| 3                                  | TRIPURA GAS BASED POWER PROJECT                                            | 07/2009 | 421.01                    | 1078.31                      | 156.12  |
| 4                                  | KAMENG HYDROELECTRIC PROJECT (NEEPCO)                                      | 12/2004 | 2496.90                   | 6179.96                      | 147.51  |
| 5                                  | PARBATI HEP (4X200 MW) (NHPC) II                                           | 09/2002 | 3919.59                   | 9394.80                      | 139.69  |
| <b>RAILWAYS</b>                    |                                                                            |         |                           |                              |         |
| 1                                  | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)                                     | 09/1998 | 247.66                    | 6093.31                      | 2360.35 |
| 2                                  | MADURAI-TUTICORIN VIA ARUPPUKKOTTAI                                        | 04/2011 | 120.70                    | 1800.00                      | 1391.30 |
| 3                                  | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR                                        | 03/1995 | 2500.00                   | 27949.00                     | 1017.96 |
| 4                                  | BIHTA-AURANGABAD (NL)                                                      | 04/2008 | 326.20                    | 2995.01                      | 818.15  |
| 5                                  | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)                                     | 12/1994 | 124.43                    | 1025.00                      | 723.76  |
| <b>ROAD TRANSPORT AND HIGHWAYS</b> |                                                                            |         |                           |                              |         |

|                           |                                                                                                      |         |          |          |        |
|---------------------------|------------------------------------------------------------------------------------------------------|---------|----------|----------|--------|
| 1                         | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-I)_NEW                                   | 09/2015 | 771.18   | 7558.00  | 880.06 |
| 2                         | GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION                                                  | 03/2010 | 1509.10  | 3237.87  | 114.56 |
| 3                         | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)                                                          | 05/2009 | 1108.00  | 2288.00  | 106.50 |
| 4                         | TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF | 12/2009 | 104.00   | 201.00   | 93.27  |
| 5                         | MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000                                                  | 12/2003 | 199.81   | 385.13   | 92.75  |
| <b>SHIPPING AND PORTS</b> |                                                                                                      |         |          |          |        |
| 1                         | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)                                          | 10/2002 | 150.00   | 600.00   | 300.00 |
| 2                         | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB | 01/2007 | 366.39   | 669.46   | 82.72  |
| 3                         | CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED                                               | 02/2015 | 244.50   | 271.56   | 11.07  |
| <b>STEEL</b>              |                                                                                                      |         |          |          |        |
| 1                         | REVAMPING OF SINTER MACHINES - 1 AND 2                                                               | 12/2009 | 343.00   | 488.40   | 42.39  |
| <b>TELECOMMUNICATIONS</b> |                                                                                                      |         |          |          |        |
| 1                         | NETWORK FOR SPECTRUM                                                                                 | 03/2012 | 13334.00 | 24664.00 | 84.97  |
| <b>URBAN DEVELOPMENT</b>  |                                                                                                      |         |          |          |        |
| 1                         | CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA  | 12/2008 | 114.26   | 266.00   | 132.80 |
| 2                         | CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA                                             | 05/2005 | 768.88   | 1113.34  | 44.80  |
| 3                         | ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI      | 10/2013 | 1219.21  | 1592.00  | 30.58  |
| 4                         | CHENNAI METRO RAIL LTD (PHASE 1)                                                                     | 02/2009 | 14600.00 | 19058.00 | 30.53  |
| 5                         | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII                                    | 10/2011 | 175.49   | 206.71   | 17.79  |

**N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.**

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)**  
(as on 01-01-2019)

| SN                        | PROJECT                                                                    | DOA     | COST ORIGINAL<br>(Rs. crore) | COST ANTICIPATED<br>(Rs. crore) | COR<br>(Rs.crore) |
|---------------------------|----------------------------------------------------------------------------|---------|------------------------------|---------------------------------|-------------------|
| <b>ATOMIC ENERGY</b>      |                                                                            |         |                              |                                 |                   |
| 1                         | KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4                                    | 10/2009 | 11459.00                     | 16580.00                        | 5121.00           |
| 2                         | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)                          | 09/2003 | 3492.00                      | 6100.00                         | 2608.00           |
| <b>CIVIL AVIATION</b>     |                                                                            |         |                              |                                 |                   |
| 1                         | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR | 10/2013 | 314.61                       | 441.33                          | 126.72            |
| <b>COAL</b>               |                                                                            |         |                              |                                 |                   |
| 1                         | JAGANNATHPOR OCP(3.00MTY)                                                  | 09/2008 | 152.43                       | 459.49                          | 307.06            |
| 2                         | NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI                     | 10/2007 | 259.40                       | 486.57                          | 227.17            |
| 3                         | BHANEAGAON OC                                                              | 02/2015 | 187.94                       | 409.68                          | 221.74            |
| 4                         | SHANTIKHANI LONGWALL PROJ-SCCL                                             | 10/2006 | 249.03                       | 448.86                          | 199.83            |
| 5                         | RCE OF INDARAM OCP(1.20 MTPA)                                              | 07/2011 | 162.76                       | 349.28                          | 186.52            |
| <b>DEFENCE PRODUCTION</b> |                                                                            |         |                              |                                 |                   |

|   |                                                                                                      |         |          |          |          |
|---|------------------------------------------------------------------------------------------------------|---------|----------|----------|----------|
| 1 | CONSTRUCTION WORKS PHASE 3B                                                                          | 12/2016 | 285.95   | 291.29   | 5.34     |
| 2 | CONSTRUCTION WORKS PHASE 4                                                                           | 12/2016 | 167.69   | 170.37   | 2.68     |
|   | <b>FERTILISERS</b>                                                                                   |         |          |          |          |
| 1 | NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY                                                      | 10/2014 | 197.79   | 209.44   | 11.65    |
|   | <b>HEALTH AND FAMILY WELFARE</b>                                                                     |         |          |          |          |
| 1 | LHMC NEW DELHI-RE-DEVELOPMENT                                                                        | 02/2013 | 414.11   | 513.89   | 99.78    |
| 2 | CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR                                                   | 09/2014 | 505.58   | 523.00   | 17.42    |
| 3 | GERIATRICS BLOCK- AIIMS DLEHI                                                                        | 12/2017 | 156.56   | 156.65   | 0.09     |
|   | <b>HEAVY INDUSTRY</b>                                                                                |         |          |          |          |
| 1 | NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)                                   | 04/2011 | 1718.00  | 3827.30  | 2109.30  |
|   | <b>PETROLEUM</b>                                                                                     |         |          |          |          |
| 1 | DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY                                      | 03/2014 | 3076.00  | 4190.00  | 1114.00  |
| 2 | PARADIP HYDERABAD PIPELINE                                                                           | 01/2015 | 2321.00  | 3338.00  | 1017.00  |
| 3 | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)                              | 03/2011 | 861.79   | 1577.15  | 715.36   |
| 4 | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR                                                         | 01/2006 | 993.00   | 1693.00  | 700.00   |
| 5 | PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY                                  | 11/2014 | 4588.29  | 5245.96  | 657.67   |
|   | <b>POWER</b>                                                                                         |         |          |          |          |
| 1 | SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)                                                              | 09/2003 | 6285.33  | 19496.34 | 13211.01 |
| 2 | BARH STPP(3X660MW) NTPC                                                                              | 02/2005 | 8692.97  | 15095.67 | 6402.70  |
| 3 | PARBATI HEP (4X200 MW) (NHPC) II                                                                     | 09/2002 | 3919.59  | 9394.80  | 5475.21  |
| 4 | COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P        | 12/2014 | 4754.42  | 9141.97  | 4387.55  |
| 5 | BONGAIGAON THERMAL POWER PROJECT                                                                     | 01/2008 | 4375.35  | 8150.00  | 3774.65  |
|   | <b>RAILWAYS</b>                                                                                      |         |          |          |          |
| 1 | WESTERN DEDICATED FREIGHT CORRIDOR                                                                   | 11/2007 | 16592.00 | 51101.00 | 34509.00 |
| 2 | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR                                                                  | 03/1995 | 2500.00  | 27949.00 | 25449.00 |
| 3 | EASTERN DEDICATED FREIGHT CORRIDOR PROJECT                                                           | 10/2006 | 11589.00 | 28181.00 | 16592.00 |
| 4 | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)                                                                  | 04/2003 | 4454.17  | 13809.00 | 9354.83  |
| 5 | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)                                                               | 09/1998 | 247.66   | 6093.31  | 5845.65  |
|   | <b>ROAD TRANSPORT AND HIGHWAYS</b>                                                                   |         |          |          |          |
| 1 | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-I)_NEW                                   | 09/2015 | 771.18   | 7558.00  | 6786.82  |
| 2 | GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION                                                  | 03/2010 | 1509.10  | 3237.87  | 1728.77  |
| 3 | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)                                                          | 05/2009 | 1108.00  | 2288.00  | 1180.00  |
| 4 | DELHI AGRA APPROVED LENGTH 180.0 KM                                                                  | 10/2012 | 1928.22  | 2945.00  | 1016.78  |
| 5 | FOUR LANING OF GWALIOR-SHIVPURI                                                                      | 05/2013 | 1055.00  | 1601.77  | 546.77   |
|   | <b>SHIPPING AND PORTS</b>                                                                            |         |          |          |          |
| 1 | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)                                          | 10/2002 | 150.00   | 600.00   | 450.00   |
| 2 | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB | 01/2007 | 366.39   | 669.46   | 303.07   |
| 3 | CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED                                               | 02/2015 | 244.50   | 271.56   | 27.06    |
|   | <b>STEEL</b>                                                                                         |         |          |          |          |
| 1 | REVAMPING OF SINTER MACHINES - 1 AND 2                                                               | 12/2009 | 343.00   | 488.40   | 145.40   |
|   | <b>TELECOMMUNICATIONS</b>                                                                            |         |          |          |          |
| 1 | NETWORK FOR SPECTRUM                                                                                 | 03/2012 | 13334.00 | 24664.00 | 11330.00 |
|   | <b>URBAN DEVELOPMENT</b>                                                                             |         |          |          |          |
| 1 | CHENNAI METRO RAIL LTD (PHASE 1)                                                                     | 02/2009 | 14600.00 | 19058.00 | 4458.00  |
| 2 | ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI      | 10/2013 | 1219.21  | 1592.00  | 372.79   |
| 3 | CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA                                             | 05/2005 | 768.88   | 1113.34  | 344.46   |
| 4 | REDEVELOPMENT OF EAST KIDWAI NAGAR                                                                   | 06/2012 | 4264.00  | 4439.23  | 175.23   |

|   |                                                                                                     |         |        |        |        |
|---|-----------------------------------------------------------------------------------------------------|---------|--------|--------|--------|
| 5 | CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA | 12/2008 | 114.26 | 266.00 | 151.74 |
|---|-----------------------------------------------------------------------------------------------------|---------|--------|--------|--------|

**N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.**

5. Out of the 1424 projects, 328 are on schedule, 384 are delayed, 344 projects reported cost overrun and 132 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 326 if delay is calculated on the basis of latest schedule of completion. Further, for 686 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 384 delayed projects, 113(29.42%) projects have overall delay in the range of 1 to 12 months, 61 (15.88%) projects have delay in the range of 13 to 24 months, 101 (26.30%) projects have delay in the range of 25 to 60 months and 109 (28.39%) projects have delay of 61 months and above. **The average time overrun in these 384 delayed projects is 44.78 months.** The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)  
(as on 01-01-2019)**

| SN                               | PROJECT                                                                    | DOA     | DOC ORIGINAL | DOC ANTICIPATED | TOR (IN MONTHS) |
|----------------------------------|----------------------------------------------------------------------------|---------|--------------|-----------------|-----------------|
| <b>ATOMIC ENERGY</b>             |                                                                            |         |              |                 |                 |
| 1                                | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)                          | 09/2003 | 09/2010      | 03/2019         | 102             |
| 2                                | KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4                                    | 10/2009 | 12/2015      | 06/2020         | 54              |
| 3                                | RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)                         | 10/2009 | 12/2016      | 12/2020         | 48              |
| 4                                | KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4                              | 03/2013 | 11/2020      | 11/2023         | 36              |
| <b>CIVIL AVIATION</b>            |                                                                            |         |              |                 |                 |
| 1                                | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR | 10/2013 | 09/2018      | 06/2020         | 21              |
| <b>COAL</b>                      |                                                                            |         |              |                 |                 |
| 1                                | SHANTIKHANI LONGWALL PROJ-SCCL                                             | 10/2006 | 03/2012      | 03/2024         | 144             |
| 2                                | RAMAGUNDAM OC-II EXTENSION                                                 | 12/2009 | 03/2012      | 03/2023         | 132             |
| 3                                | BALRAM OCP EXTENSION,MCL 8.00 MTY                                          | 12/2007 | 03/2010      | 03/2020         | 120             |
| 4                                | CHURI BENTI UG (0.81 MTY)                                                  | 08/2007 | 03/2011      | 03/2020         | 108             |
| 5                                | ANANTA OC EXPANSION PH-III (15.0 MTY)                                      | 08/2008 | 03/2012      | 03/2021         | 108             |
| <b>DEFENCE PRODUCTION</b>        |                                                                            |         |              |                 |                 |
| 1                                | CONSTRUCTION WORKS PHASE 4                                                 | 12/2016 | 05/2018      | 01/2019         | 8               |
| <b>FERTILISERS</b>               |                                                                            |         |              |                 |                 |
| 1                                | NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY                            | 10/2014 | 11/2016      | 04/2019         | 29              |
| 2                                | GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL.    | 02/2016 | 12/2017      | 01/2019         | 13              |
| <b>HEALTH AND FAMILY WELFARE</b> |                                                                            |         |              |                 |                 |
| 1                                | LHMC NEW DELHI-RE-DEVELOPMENT                                              | 02/2013 | 11/2013      | 10/2020         | 83              |
| 2                                | AIIMS - MOTHER AND CHILD BLOCK                                             | 12/2013 | 05/2017      | 07/2019         | 26              |
| 3                                | AIIMS - OPD(NEW)                                                           | 08/2014 | 05/2017      | 03/2019         | 22              |
| 4                                | SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB                             | 07/2016 | 02/2018      | 06/2019         | 16              |
| 5                                | NEIGRIHMS SHILLONG MEGHALYA                                                | 10/2016 | 05/2018      | 08/2019         | 15              |
| <b>HEAVY INDUSTRY</b>            |                                                                            |         |              |                 |                 |

|                                    |                                                                                                      |         |         |         |     |
|------------------------------------|------------------------------------------------------------------------------------------------------|---------|---------|---------|-----|
| 1                                  | NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)                                   | 04/2011 | 09/2011 | 06/2019 | 93  |
| <b>PETROLEUM</b>                   |                                                                                                      |         |         |         |     |
| 1                                  | KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II                                                | 06/2009 | 12/2012 | 06/2019 | 78  |
| 2                                  | ASSAM RENEWAL PROJECT FOR GROUP A                                                                    | 03/2009 | 03/2013 | 03/2019 | 72  |
| 3                                  | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)                              | 03/2011 | 05/2013 | 03/2019 | 70  |
| 4                                  | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)                               | 06/2010 | 01/2014 | 11/2019 | 70  |
| 5                                  | INTEGRATED DEVELOPMENT OF B-127 FIELDS                                                               | 12/2011 | 03/2015 | 12/2019 | 57  |
| <b>POWER</b>                       |                                                                                                      |         |         |         |     |
| 1                                  | PARBATI HEP (4X200 MW) (NHPC) II                                                                     | 09/2002 | 09/2009 | 12/2021 | 147 |
| 2                                  | KUNADANKULAM APP TRANS SYSTEM (PGCIL)                                                                | 05/2005 | 11/2008 | 03/2019 | 124 |
| 3                                  | BARH STPP(3X660MW) NTPC                                                                              | 02/2005 | 01/2011 | 04/2021 | 123 |
| 4                                  | KAMENG HYDROELECTRIC PROJECT (NEEPCO)                                                                | 12/2004 | 12/2009 | 03/2019 | 111 |
| 5                                  | NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT                                                   | 02/2009 | 08/2013 | 03/2022 | 103 |
| <b>RAILWAYS</b>                    |                                                                                                      |         |         |         |     |
| 1                                  | BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL                                            | 04/1998 | 03/2003 | 03/2030 | 324 |
| 2                                  | BANGLORE - SATYAMANGALAM (NL)(SWR)                                                                   | 04/1996 | 03/2002 | 03/2024 | 264 |
| 3                                  | MANDHANA - BRAHMAWART NEW LINE PROJECT.                                                              | 04/1997 | 04/1999 | 03/2019 | 239 |
| 4                                  | MUNEERABAD-MAHABOONNAGAR(NL),SCR                                                                     | 04/1997 | 03/2000 | 03/2019 | 228 |
| 5                                  | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR                                                                  | 03/1995 | 11/2002 | 03/2021 | 220 |
| <b>ROAD TRANSPORT AND HIGHWAYS</b> |                                                                                                      |         |         |         |     |
| 1                                  | NALBARI T BIJNI (AS-7)                                                                               | 12/2003 | 04/2008 | 03/2019 | 131 |
| 2                                  | SONAPUR TO GUWAHTI (AS-3)                                                                            | 12/2003 | 03/2008 | 01/2019 | 130 |
| 3                                  | NALBARI TO BIJNI (AS-6)                                                                              | 12/2003 | 06/2008 | 04/2019 | 130 |
| 4                                  | DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)                                                              | 12/2003 | 05/2008 | 02/2019 | 129 |
| 5                                  | GWALIOR-JHANSI, NH-75                                                                                | 12/2003 | 12/2009 | 08/2020 | 128 |
| <b>SHIPPING AND PORTS</b>          |                                                                                                      |         |         |         |     |
| 1                                  | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)                                          | 10/2002 | 03/2006 | 02/2019 | 155 |
| 2                                  | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB | 01/2007 | 12/2010 | 12/2018 | 96  |
| 3                                  | CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT                                                  | 03/2016 | 12/2017 | 05/2020 | 29  |
| <b>STEEL</b>                       |                                                                                                      |         |         |         |     |
| 1                                  | NMDC INTEGRATED STEEL PLANT                                                                          | 01/2010 | 05/2015 | 06/2019 | 49  |
| 2                                  | NEW SINTER PLANT AT BOKARO STEEL PLANT                                                               | 03/2015 | 10/2017 | 06/2020 | 32  |
| 3                                  | COKE OVEN BATTERY-5                                                                                  | 12/2011 | 12/2017 | 09/2019 | 21  |
| 4                                  | MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT                                       | 05/2015 | 12/2017 | 06/2019 | 18  |
| 5                                  | INSTALLATION OF NEW HOT STRIP MILL AT RSP                                                            | 04/2015 | 04/2018 | 05/2019 | 13  |
| <b>TELECOMMUNICATIONS</b>          |                                                                                                      |         |         |         |     |
| 1                                  | NETWORK FOR SPECTRUM                                                                                 | 03/2012 | 07/2015 | 05/2020 | 58  |
| 2                                  | MAHARASHTRA CORE (LOT1)                                                                              | 08/2017 | 04/2018 | 02/2019 | 10  |
| 3                                  | MADHYA PRADESH ACCESS (LOT1)                                                                         | 08/2017 | 05/2018 | 02/2019 | 9   |
| 4                                  | MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT                                                     | 01/2018 | 10/2018 | 02/2019 | 4   |
| <b>URBAN DEVELOPMENT</b>           |                                                                                                      |         |         |         |     |
| 1                                  | CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA                                                | 01/2010 | 10/2012 | 03/2019 | 77  |
| 2                                  | IRRIGATION WORK OF BAGMATI                                                                           | 10/2005 | 03/2015 | 03/2021 | 72  |
| 3                                  | CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA  | 12/2008 | 12/2013 | 10/2019 | 70  |
| 4                                  | MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)                                                            | 07/2013 | 01/2015 | 05/2020 | 64  |
| 5                                  | NIT ACADEMIC BUILDING AT IMPHAL MANIPUR                                                              | 02/2014 | 03/2015 | 11/2019 | 56  |

**N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further time overruns.**

6. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

7. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones  
(as on 01-01-2019)**

| S<br>N                           | PROJECTS                                                                                     | DATE OF<br>APPROVA<br>L | COST<br>ORIGINA<br>L (Rs.<br>Crore) | COST<br>ANTICIPATE<br>D (Rs. Crore) | CUMULATIVE<br>EXPENDITUR<br>E (Rs. Crore) | ORIGINAL DATE<br>OF<br>COMMISSIONIN<br>G | ANTICIPATED<br>DATE OF<br>COMMISSIONIN<br>G |
|----------------------------------|----------------------------------------------------------------------------------------------|-------------------------|-------------------------------------|-------------------------------------|-------------------------------------------|------------------------------------------|---------------------------------------------|
| <b>CIVIL AVIATION</b>            |                                                                                              |                         |                                     |                                     |                                           |                                          |                                             |
| 1                                | CONSTRUCTION<br>OF NEW<br>INTEGRATED<br>TERMINAL<br>BUILDING AT VSI<br>AIRPORT,<br>PORTBLAIR | 10/2013                 | 314.61                              | 441.33                              | 85.79                                     | 09/2018                                  | 06/2020                                     |
| <b>COAL</b>                      |                                                                                              |                         |                                     |                                     |                                           |                                          |                                             |
| 1                                | BITHNOK LIGNITE<br>MINE PROJECT<br>(2.25 MTPA)                                               | 03/2015                 | 513.63                              | 513.63                              | 173.06                                    | 12/2019                                  | 12/2019                                     |
| 2                                | HADLA LIGNITE<br>MINE<br>PROJECT(1.90<br>MTPA)                                               | 03/2015                 | 522.45                              | 522.45                              | 8.71                                      | 09/2019                                  | 09/2019                                     |
| 3                                | COAL PROJECT<br>NAME JAMUNIA<br>UG (0.84 MTY)                                                | 07/2016                 | 409.87                              | 409.87                              | 17.50                                     | 03/2022                                  | 03/2022                                     |
| 4                                | NEYVELI UTTAR<br>PRADESH POWER<br>PROJECT LIMITED<br>1980 MW                                 | 07/2016                 | 17237.00                            | 17237.80                            | 4026.50                                   | 11/2021                                  | 11/2021                                     |
| 5                                | KOLAR PIMPRI<br>EXTENSION OC                                                                 | 03/2017                 | 362.73                              | 362.73                              | 258.23                                    | 03/2020                                  | 03/2020                                     |
| <b>HEALTH AND FAMILY WELFARE</b> |                                                                                              |                         |                                     |                                     |                                           |                                          |                                             |
| 1                                | LGBRIMH-<br>TEZPUR, ASSAM                                                                    | 07/2012                 | 175.57                              | 175.57                              | 113.50                                    | 12/2014                                  | N.A.                                        |
| 2                                | LHMC NEW<br>DELHI-RE-<br>DEVELOPMENT                                                         | 02/2013                 | 414.11                              | 513.89                              | 141.00                                    | 11/2013                                  | 10/2020                                     |
| 3                                | ALL INDIA<br>INSTITUTE OF<br>MEDICAL<br>SCIENCE AT<br>BATHINDA,<br>PUNJAB                    | 07/2016                 | 703.00                              | 703.00                              | 272.00                                    | 06/2020                                  | 06/2020                                     |
| 4                                | ALL INDIA<br>INSTITUTE OF<br>MEDICAL<br>SCIENCE AT                                           | 07/2016                 | 785.00                              | 785.00                              | 39.35                                     | 04/2020                                  | 04/2020                                     |

|   |                                                                                           |         |         |          |          |         |         |
|---|-------------------------------------------------------------------------------------------|---------|---------|----------|----------|---------|---------|
|   | GORAKHPUR (U.P.)                                                                          |         |         |          |          |         |         |
| 5 | CNCI KOLKATA WEST BENGAL                                                                  | 08/2016 | 244.00  | 244.00   | 238.97   | 09/2018 | 09/2018 |
|   | HEAVY INDUSTRY                                                                            |         |         |          |          |         |         |
| 1 | LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA    | 08/2016 | 1554.00 | 1554.00  | 161.86   | 09/2019 | 09/2019 |
|   | PETROLEUM                                                                                 |         |         |          |          |         |         |
| 1 | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR                                              | 01/2006 | 993.00  | 1693.00  | 1549.85  | 01/2012 | N.A.    |
| 2 | CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN                                        | 07/2011 | 350.00  | 350.00   | 2.06     | 01/2019 | 09/2019 |
| 3 | IRUGUR-DEVANGONTHI POL PIPELINE                                                           | 11/2012 | 678.00  | 678.00   | 5.12     | 02/2017 | N.A.    |
| 4 | MMPL PIPELINE REROUTING PROJECT                                                           | 04/2013 | 449.58  | 449.58   | 118.17   | 12/2019 | 12/2019 |
| 5 | ENNORE-TRICHY-MADURAI LPG PIPELINE                                                        | 05/2013 | 711.00  | 711.00   | 11.12    | 06/2020 | 06/2020 |
|   | POWER                                                                                     |         |         |          |          |         |         |
| 1 | SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)                                                   | 09/2003 | 6285.33 | 19496.34 | 10421.62 | 09/2010 | N.A.    |
| 2 | PAKRI BARWADIH COAL MINING PROJECT                                                        | 10/2004 | 4237.96 | 4552.00  | 2922.12  | 10/2017 | 12/2016 |
| 3 | 400KV D/C TEESTA III - KISHANGANJ TRANSMISSIAN LINE (JV)                                  | 08/2008 | 771.00  | 1624.00  | 1577.20  | 02/2013 | 12/2018 |
| 4 | TRANMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)-DRASS- KARGIL- KHALSTI-LEH PROJECT | 01/2014 | 1788.41 | 2333.71  | 1697.38  | 09/2017 | 11/2018 |
| 5 | UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I                                       | 01/2014 | 374.63  | 374.63   | 187.24   | 04/2016 | 03/2019 |
|   | RAILWAYS                                                                                  |         |         |          |          |         |         |
| 1 | HOWRAH-AMTA-CHAMPADANGA NL (SER)                                                          | 04/1974 | 393.46  | 1026.00  | 182.49   | 03/2007 | N.A.    |
| 2 | NANGALDAM-TALWARA(NL),NR                                                                  | 03/1981 | 450.00  | 2100.00  | 484.14   | 07/2012 | N.A.    |
| 3 | NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR                   | 04/1983 | 297.32  | 614.00   | 270.27   | 03/2019 | 03/2020 |
| 4 | TAMLUK DIGHA,LINE DOUBLING (SER)                                                          | 03/1984 | 293.97  | 749.69   | 0.00     | 06/2005 | N.A.    |
| 5 | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)                                         | 04/1986 | 158.77  | 634.48   | 629.43   | 03/1994 | N.A.    |
|   | ROAD TRANSPORT AND HIGHWAYS                                                               |         |         |          |          |         |         |

|                           |                                                                                                      |         |          |          |         |         |         |
|---------------------------|------------------------------------------------------------------------------------------------------|---------|----------|----------|---------|---------|---------|
| 1                         | 4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52                          | 01/1991 | 520.01   | 520.01   | 0.00    | N.A.    | N.A.    |
| 2                         | FOUR LANING OF BHOJPUR TO BUXAR                                                                      | 01/1991 | 642.41   | 642.41   | 9.45    | N.A.    | 10/2020 |
| 3                         | REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF                 | 01/1991 | 478.35   | 478.35   | 0.00    | N.A.    | N.A.    |
| 4                         | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104  | 01/1991 | 319.68   | 319.68   | 0.00    | N.A.    | N.A.    |
| 5                         | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB | 01/1991 | 219.40   | 219.40   | 0.00    | 01/2018 | N.A.    |
| <b>SHIPPING AND PORTS</b> |                                                                                                      |         |          |          |         |         |         |
| 1                         | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)                                          | 10/2002 | 150.00   | 600.00   | 550.78  | 03/2006 | 02/2019 |
| 2                         | SETHUSAMUDRAM SHIP CHANNEL PROJECT                                                                   | 06/2005 | 2427.40  | 2427.40  | 831.21  | 10/2008 | N.A.    |
| 3                         | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB | 01/2007 | 366.39   | 669.46   | 413.91  | 12/2010 | 12/2018 |
| 4                         | CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT                                                  | 03/2016 | 600.00   | 257.90   | 1.45    | 12/2017 | 05/2020 |
| 5                         | JAL MARG VIKAS PROJECT                                                                               | 01/2018 | 4200.00  | 4200.00  | 0.00    | 03/2023 | 03/2023 |
| <b>STEEL</b>              |                                                                                                      |         |          |          |         |         |         |
| 1                         | EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT            | 02/2014 | 4749.00  | 4749.00  | 108.28  | 09/2017 | N.A.    |
| <b>TELECOMMUNICATIONS</b> |                                                                                                      |         |          |          |         |         |         |
| 1                         | NETWORK FOR SPECTRUM                                                                                 | 03/2012 | 13334.00 | 24664.00 | 8397.00 | 07/2015 | 05/2020 |
| 2                         | GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)                                                            | 06/2016 | 418.26   | 418.26   | 172.30  | 06/2017 | N.A.    |
| 3                         | MADHYA PRADESH ACCESS (LOT1)                                                                         | 08/2017 | 215.30   | 214.10   | 33.46   | 05/2018 | 02/2019 |
| 4                         | MAHARASHTRA CORE (LOT1)                                                                              | 08/2017 | 167.68   | 167.68   | 32.44   | 04/2018 | 02/2019 |
| 5                         | MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT                                                     | 01/2018 | 231.80   | 231.80   | 77.65   | 10/2018 | 02/2019 |



| URBAN DEVELOPMENT |                                                                                                 |         |        |         |         |         |         |
|-------------------|-------------------------------------------------------------------------------------------------|---------|--------|---------|---------|---------|---------|
| 1                 | CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA                                        | 05/2005 | 768.88 | 1113.34 | 1085.64 | 02/2014 | N.A.    |
| 2                 | IRRIGATION WORK OF BAGMATI                                                                      | 10/2005 | 956.00 | 956.00  | 651.21  | 03/2015 | 03/2021 |
| 3                 | CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V                                 | 03/2007 | 149.73 | 175.94  | 178.65  | 12/2015 | N.A.    |
| 4                 | REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 | 08/2007 | 246.90 | 246.90  | 0.00    | N.A.    | N.A.    |
| 5                 | CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI                                | 12/2007 | 202.61 | 227.00  | 199.95  | 12/2016 | N.A.    |

N.A.: Not Available.

**N.B.: The concerned administrative Ministry may like review these Projects in order to firm-up milestones.**

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 01-01-2019)**

| SN                   | PROJECTS                                                            | DATE OF APPROVAL | COST ORIGINAL (Rs. Crore) | COST REVISED(Rs. Crore) | CUMULATIVE EXPENDITURE (Rs. Crore) |
|----------------------|---------------------------------------------------------------------|------------------|---------------------------|-------------------------|------------------------------------|
| <b>ATOMIC ENERGY</b> |                                                                     |                  |                           |                         |                                    |
| 1                    | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)                   | 09/2003          | 3492.00                   | 0.00                    | 5687.52                            |
| <b>COAL</b>          |                                                                     |                  |                           |                         |                                    |
| 1                    | NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI              | 10/2007          | 259.40                    | 0.00                    | 266.38                             |
| 2                    | BALRAM OCP EXTENSION, MCL 8.00 MTY                                  | 12/2007          | 172.08                    | 0.00                    | 267.19                             |
| 3                    | KANIHA OCP, MCL, (10.0 MTY)                                         | 12/2007          | 457.77                    | 0.00                    | 584.85                             |
| 4                    | ANANTA OC EXPANSION PH-III (15.0 MTY)                               | 08/2008          | 207.28                    | 0.00                    | 235.50                             |
| 5                    | JAGANNATHPOR OCP(3.00MTY)                                           | 09/2008          | 152.43                    | 0.00                    | 178.93                             |
| <b>PETROLEUM</b>     |                                                                     |                  |                           |                         |                                    |
| 1                    | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR                        | 01/2006          | 993.00                    | 0.00                    | 1549.85                            |
| 2                    | FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY | 07/2015          | 822.66                    | 0.00                    | 868.92                             |
| <b>POWER</b>         |                                                                     |                  |                           |                         |                                    |
| 1                    | PARBATI HEP (4X200 MW) (NHPC) II                                    | 09/2002          | 3919.59                   | 0.00                    | 7145.69                            |
| 2                    | SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)                             | 09/2003          | 6285.33                   | 0.00                    | 10421.62                           |
| 3                    | KAMENG HYDROELECTRIC PROJECT (NEEPCO)                               | 12/2004          | 2496.90                   | 6179.96                 | 6881.48                            |
| 4                    | BARH STPP(3X660MW) NTPC                                             | 02/2005          | 8692.97                   | 15095.67                | 15278.98                           |
| 5                    | TAPOVAN-VISHNUGAD HEP (4X130MW)                                     | 11/2006          | 2978.48                   | 0.00                    | 3775.64                            |

| RAILWAYS                    |                                                                                                      |         |          |         |          |
|-----------------------------|------------------------------------------------------------------------------------------------------|---------|----------|---------|----------|
| 1                           | NANGALDAM-TALWARA(NL),NR                                                                             | 03/1981 | 450.00   | 0.00    | 484.14   |
| 2                           | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)                                                    | 04/1986 | 158.77   | 274.56  | 629.43   |
| 3                           | MUZAFFARPUR-SITAMARHI NEW LINE                                                                       | 01/1991 | 332.15   | 0.00    | 538.21   |
| 4                           | FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, | 04/1991 | 329.39   | 0.00    | 759.20   |
| 5                           | AMRAVATI-NARKHER NL(CR)                                                                              | 06/1994 | 663.01   | 668.34  | 716.80   |
| ROAD TRANSPORT AND HIGHWAYS |                                                                                                      |         |          |         |          |
| 1                           | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700                                               | 12/2003 | 280.00   | 0.00    | 410.32   |
| 2                           | MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54                                            | 12/2003 | 167.64   | 0.00    | 268.94   |
| 3                           | DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)                                                              | 12/2003 | 160.00   | 0.00    | 198.82   |
| 4                           | NALBARI T BIJNI (AS-7)                                                                               | 12/2003 | 208.00   | 0.00    | 297.81   |
| 5                           | NALBARI TO BIJNI (AS-6)                                                                              | 12/2003 | 225.00   | 0.00    | 312.79   |
| SHIPPING AND PORTS          |                                                                                                      |         |          |         |          |
| 1                           | CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED                                               | 02/2015 | 244.50   | 258.33  | 271.56   |
| URBAN DEVELOPMENT           |                                                                                                      |         |          |         |          |
| 1                           | CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA                                             | 05/2005 | 768.88   | 1070.97 | 1085.64  |
| 2                           | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V                                       | 03/2007 | 149.73   | 173.00  | 178.65   |
| 3                           | CHENNAI METRO RAIL LTD (PHASE 1)                                                                     | 02/2009 | 14600.00 | 0.00    | 16352.77 |
| 4                           | CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB                     | 02/2014 | 388.00   | 0.00    | 395.14   |

**N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised cost estimates.**

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on as on 01-01-2019)**

| SN                               | SECTOR/ PROJECT                                         | DATE OF APPROVAL | ORIGINAL DATE OF COMMISSIONING | REVISED DATE OF COMMISSIONING | ANTICIPATED DATE OF COMMISSIONING |
|----------------------------------|---------------------------------------------------------|------------------|--------------------------------|-------------------------------|-----------------------------------|
| <b>COAL</b>                      |                                                         |                  |                                |                               |                                   |
| 1                                | KULDA OCP (MAHANADI COALFIELDS LTD)                     | 01/2005          | 03/2010                        | N.A.                          | 03/2018                           |
| 2                                | NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI | 10/2007          | 03/2012                        | N.A.                          | N.A.                              |
| 3                                | KAKATIYA LONGWALL                                       | 12/2008          | 12/2012                        | N.A.                          | N.A.                              |
| 4                                | MANUGURU OC-II EXTENSION PHASE-II                       | 03/2010          | 03/2012                        | N.A.                          | N.A.                              |
| 5                                | MADHUBAND NLW WASHERY                                   | 08/2010          | 05/2014                        | N.A.                          | 04/2018                           |
| <b>HEALTH AND FAMILY WELFARE</b> |                                                         |                  |                                |                               |                                   |
| 1                                | LGBRIMH-TEZPUR, ASSAM                                   | 07/2012          | 12/2014                        | N.A.                          | N.A.                              |
| 2                                | CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR      | 09/2014          | 03/2018                        | N.A.                          | N.A.                              |
| 3                                | CNCI KOLKATA WEST BENGAL                                | 08/2016          | 09/2018                        | N.A.                          | 09/2018                           |
| <b>PETROLEUM</b>                 |                                                         |                  |                                |                               |                                   |
| 1                                | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR            | 01/2006          | 01/2012                        | N.A.                          | N.A.                              |

|                                    |                                                                                                      |         |         |         |      |
|------------------------------------|------------------------------------------------------------------------------------------------------|---------|---------|---------|------|
| 2                                  | CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)                                                      | 06/2007 | 09/2011 | N.A.    | N.A. |
| 3                                  | PARADIP-RAIPUR- RANCHI PIPELINE                                                                      | 08/2009 | 12/2016 | N.A.    | N.A. |
| 4                                  | RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)                                      | 04/2011 | 05/2015 | N.A.    | N.A. |
| 5                                  | 50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II                                                     | 11/2011 | 03/2013 | N.A.    | N.A. |
| <b>POWER</b>                       |                                                                                                      |         |         |         |      |
| 1                                  | SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)                                                              | 09/2003 | 09/2010 | N.A.    | N.A. |
| 2                                  | PAKRI BARWADIH COAL MINING PROJECT                                                                   | 10/2004 | 10/2017 | N.A.    | N.A. |
| 3                                  | TRIPURA GAS BASED POWER PROJECT                                                                      | 07/2009 | 07/2013 | N.A.    | N.A. |
| 4                                  | COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L | 09/2011 | 09/2014 | N.A.    | N.A. |
| 5                                  | KUDGI STPP STAGE 1                                                                                   | 01/2012 | 01/2017 | N.A.    | N.A. |
| <b>RAILWAYS</b>                    |                                                                                                      |         |         |         |      |
| 1                                  | HOWRAH-AMTA-CHAMPADANGA NL (SER)                                                                     | 04/1974 | 03/2007 | 03/2007 | N.A. |
| 2                                  | NANGALDAM-TALWARA(NL),NR                                                                             | 03/1981 | 07/2012 | N.A.    | N.A. |
| 3                                  | TAMLUK DIGHA,LINE DOUBLING (SER)                                                                     | 03/1984 | 06/2005 | N.A.    | N.A. |
| 4                                  | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)                                                    | 04/1986 | 03/1994 | N.A.    | N.A. |
| 5                                  | LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG | 04/1987 | 03/2006 | N.A.    | N.A. |
| <b>ROAD TRANSPORT AND HIGHWAYS</b> |                                                                                                      |         |         |         |      |
| 1                                  | REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O | 01/1991 | 04/2014 | N.A.    | N.A. |
| 2                                  | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI  | 01/1991 | 05/2016 | N.A.    | N.A. |
| 3                                  | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG | 01/1991 | 08/2016 | N.A.    | N.A. |
| 4                                  | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG | 01/1991 | 10/2016 | N.A.    | N.A. |
| 5                                  | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI | 01/1991 | 10/2016 | N.A.    | N.A. |
| <b>SHIPPING AND PORTS</b>          |                                                                                                      |         |         |         |      |
| 1                                  | SETHUSAMUDRAM SHIP CHANNEL PROJECT                                                                   | 06/2005 | 10/2008 | N.A.    | N.A. |
| 2                                  | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB | 01/2007 | 12/2010 | N.A.    | N.A. |
| 3                                  | CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED                                               | 02/2015 | 12/2017 | 03/2018 | N.A. |
| <b>STEEL</b>                       |                                                                                                      |         |         |         |      |
| 1                                  | REVAMPING OF SINTER MACHINES - 1 AND 2                                                               | 12/2009 | 10/2016 | N.A.    | N.A. |
| 2                                  | EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT            | 02/2014 | 09/2017 | N.A.    | N.A. |
| 3                                  | DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT                                 | 04/2014 | 04/2015 | N.A.    | N.A. |
| <b>TELECOMMUNICATIONS</b>          |                                                                                                      |         |         |         |      |
| 1                                  | NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY                                | 09/2014 | 09/2014 | N.A.    | N.A. |
| 2                                  | GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)                                                            | 06/2016 | 06/2017 | N.A.    | N.A. |

| URBAN DEVELOPMENT |                                                                                                 |         |         |      |      |
|-------------------|-------------------------------------------------------------------------------------------------|---------|---------|------|------|
| 1                 | CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA                                        | 05/2005 | 02/2014 | N.A. | N.A. |
| 2                 | CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V                                 | 03/2007 | 12/2015 | N.A. | N.A. |
| 3                 | REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 | 08/2007 | N.A.    | N.A. | N.A. |
| 4                 | CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND                   | 12/2007 | 06/2016 | N.A. | N.A. |
| 5                 | CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI                                | 12/2007 | 12/2016 | N.A. | N.A. |

N.A.: Not Available.


**N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised commissioning schedule.**

11. The status as on 31.12.2018 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

12. This has the approval of Competent Authority, Ministry of Statistics and Programme Implementation.

TABLE-1

| EXECUTIVE SUMMARY COSTING Rs.150 Crore and above |                             |                     |                               |
|--------------------------------------------------|-----------------------------|---------------------|-------------------------------|
| Sl.No.                                           | Sector                      | Projects on Monitor | Projects Additionally Delayed |
| 1                                                | ROAD TRANSPORT AND HIGHWAYS | 605                 | 19                            |
| 2                                                | RAILWAYS                    | 367                 | 8                             |
| 3                                                | PETROLEUM                   | 137                 | 16                            |
| 4                                                | COAL                        | 97                  | 1                             |
| 5                                                | POWER                       | 95                  | 19                            |
| 6                                                | URBAN DEVELOPMENT           | 58                  | 0                             |
| 7                                                | HEALTH AND FAMILY WELFARE   | 20                  | 1                             |
| 8                                                | STEEL                       | 13                  | 0                             |
| 9                                                | FERTILISERS                 | 6                   | 1                             |
| 10                                               | SHIPPING AND PORTS          | 6                   | 0                             |
| 11                                               | TELECOMMUNICATIONS          | 6                   | 3                             |
| 12                                               | MINES                       | 5                   | 1                             |
| 13                                               | ATOMIC ENERGY               | 4                   | 0                             |
| 14                                               | HEAVY INDUSTRY              | 2                   | 0                             |
| 15                                               | DEFENCE PRODUCTION          | 2                   | 0                             |
| 16                                               | CIVIL AVIATION              | 1                   | 0                             |
|                                                  | Total                       | 1424                | 69                            |

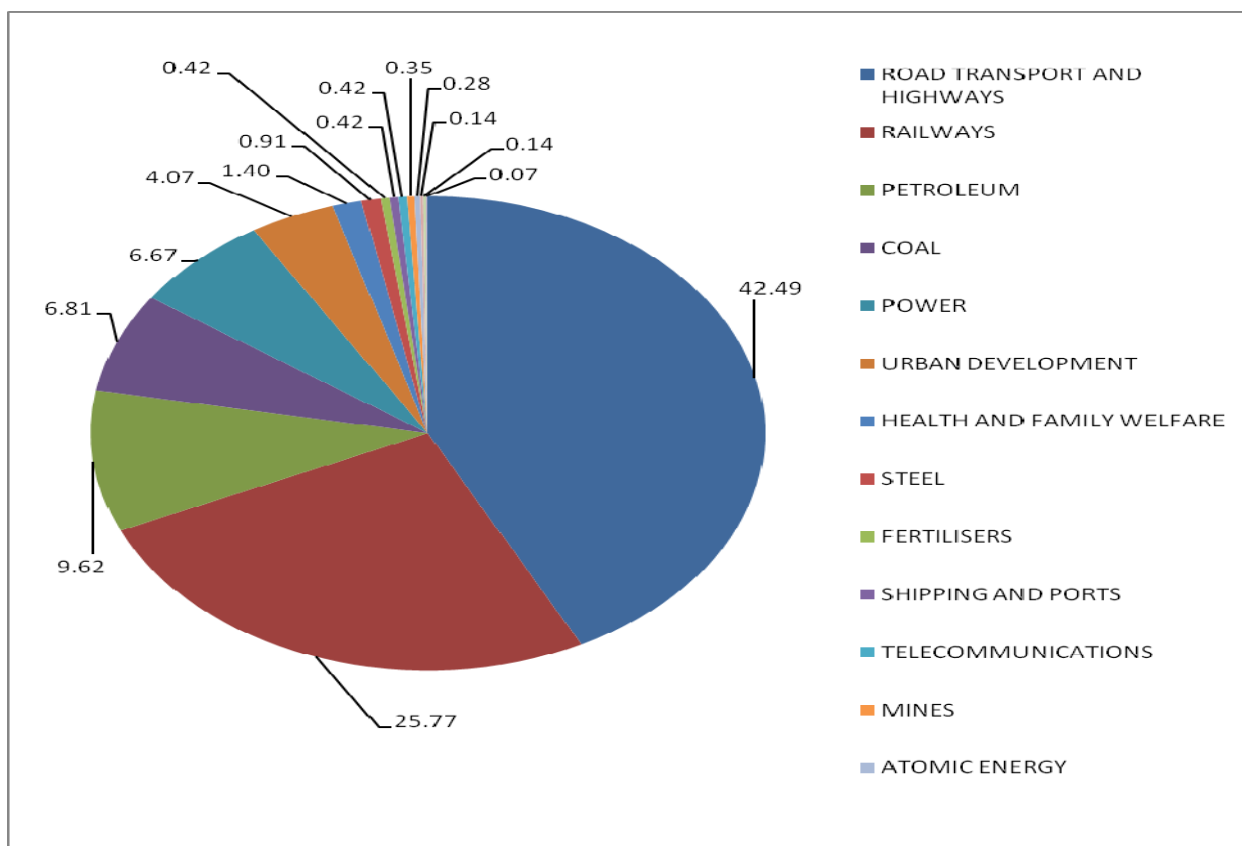

**TABLE-2**

| Month wise List of Completed Projects Costing Rs. 150 crore and above during |                                                                                                                              |                           |                                |                                    |
|------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------|---------------------------|--------------------------------|------------------------------------|
| 2018-2019                                                                    |                                                                                                                              |                           |                                |                                    |
| Sl. No                                                                       | Project Name                                                                                                                 | Original Cost (Rs. crore) | Original Date of commissioning | Cumulative Expenditure (Rs. crore) |
|                                                                              |                                                                                                                              |                           |                                |                                    |
|                                                                              | April,2018                                                                                                                   |                           |                                |                                    |
|                                                                              |                                                                                                                              |                           |                                |                                    |
|                                                                              | <u>STEEL</u>                                                                                                                 |                           |                                |                                    |
| 1                                                                            | ALTERNATE GAS NETWORK AT BSL (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000093]                                         | 255.19                    | 03/2018                        | 177.21                             |
|                                                                              |                                                                                                                              |                           |                                |                                    |
|                                                                              | <u>PETROLEUM</u>                                                                                                             |                           |                                |                                    |
| 2                                                                            | ENNORE TERMINAL (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000224]                                                         | 393.00                    | 04/2018                        | 281.45                             |
|                                                                              |                                                                                                                              |                           |                                |                                    |
|                                                                              | <u>POWER</u>                                                                                                                 |                           |                                |                                    |
| 3                                                                            | ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000123] | 198.63                    | 09/2014                        | 127.13                             |
| 4                                                                            | INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000179]     | 6,517.36                  | 04/2018                        | 3,772.80                           |
| 5                                                                            | REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000210] | 207.88                    | 07/2018                        | 17.00                              |
|                                                                              |                                                                                                                              |                           |                                |                                    |
|                                                                              | <u>HEALTH AND FAMILY WELFARE</u>                                                                                             |                           |                                |                                    |
| 6                                                                            | AIIMS-RAE BARELI-HOUSING (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000006]                                       | 159.50                    | 11/2013                        | 158.65                             |
|                                                                              |                                                                                                                              |                           |                                |                                    |
|                                                                              | <u>RAILWAYS</u>                                                                                                              |                           |                                |                                    |
| 7                                                                            | VILLUPURAM-DINDIGUL WITH ELECTRIFICATION (RAIL VIKAS NIGAM LTD.) - [N22000189]                                               | 822.39                    | -                              | 1,713.20                           |
| 8                                                                            | NEW COOCHBEHAR TO SAMUKTALA (NORTH EAST FRONTIER RAILWAY) - [N22000197]                                                      | 209.77                    | -                              | 620.04                             |
| 9                                                                            | DELANG-PURI DOUBLING (EAST COAST RAILWAY) - [N22000320]                                                                      | 165.16                    | 03/2015                        | 226.35                             |
| 10                                                                           | THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) (RAIL VIKAS NIGAM LTD.) - [N22000322]  | 190.10                    | -                              | 320.41                             |
|                                                                              |                                                                                                                              |                           |                                |                                    |
|                                                                              | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                           |                           |                                |                                    |
| 11                                                                           | TALEGAON-AMRAVATI PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000140]                                              | 567.00                    | 11/2013                        | 1,055.94                           |
| 12                                                                           | MURADABAD-BAREILY PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000154]                                              | 1,267.00                  | 06/2013                        | 2,667.96                           |
|                                                                              |                                                                                                                              |                           |                                |                                    |
|                                                                              | <u>SHIPPING AND PORTS</u>                                                                                                    |                           |                                |                                    |

## Month wise List of Completed Projects Costing Rs. 150 crore and above during

2018-2019

| Sl. No | Project Name                                                                                                                                                          | Original Cost<br>(Rs. crore) | Original Date of<br>commissioning | Cumulative<br>Expenditure<br>(Rs. crore) |
|--------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------|-----------------------------------|------------------------------------------|
| 13     | CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED<br>PPP (ANNUITY)(KAMARAJAR PORT LIMITED) - [N25000065]                                                         | 198.94                       | 06/2017                           | 255.02                                   |
| 14     | CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED<br>(KAMARAJAR PORT LIMITED) - [N25000067]                                                                        | 274.85                       | 04/2017                           | 251.64                                   |
|        |                                                                                                                                                                       |                              |                                   |                                          |
|        | <u>URBAN DEVELOPMENT</u>                                                                                                                                              |                              |                                   |                                          |
| 15     | DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN Central Sector<br>Projects(CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000091] | 350.02                       | 03/2015                           | 452.35                                   |
|        |                                                                                                                                                                       |                              |                                   |                                          |
|        | May,2018                                                                                                                                                              |                              |                                   |                                          |
|        |                                                                                                                                                                       |                              |                                   |                                          |
|        | <u>PETROLEUM</u>                                                                                                                                                      |                              |                                   |                                          |
| 16     | TWENTY NOS. FEEDER GAS LINES<br>(OIL INDIA LIMITED) - [N16000192]                                                                                                     | 228.64                       | 12/2016                           | 149.73                                   |
| 17     | PETCOKE EVACUATION PROJECT AT PARADIP REFINERY<br>(INDIAN OIL CORPORATION LIMITED) - [N16000201]                                                                      | 238.50                       | 03/2017                           | 203.98                                   |
| 18     | SIX PIPELINE REPLACEMENT PROJECT<br>Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) -<br>[N16000214]                                                   | 181.02                       | 01/2017                           | 174.88                                   |
| 19     | FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT<br>REFINERY (INDIAN OIL CORPORATION<br>LIMITED) - [N16000245]                                                 | 931.00                       | 07/2017                           | 684.74                                   |
|        |                                                                                                                                                                       |                              |                                   |                                          |
|        | <u>POWER</u>                                                                                                                                                          |                              |                                   |                                          |
| 20     | PARE HYDRO ELECTRIC PROJECT<br>(NORTH EAST ELECTRIC POWER CORPORATION) - [N18000045]                                                                                  | 573.99                       | 08/2013                           | 1,637.60                                 |
|        |                                                                                                                                                                       |                              |                                   |                                          |
|        | <u>RAILWAYS</u>                                                                                                                                                       |                              |                                   |                                          |
| 21     | GADWAL - RAICHUR (NL), SCR<br>(SOUTH CENTRAL RAILWAY) - [220100270]                                                                                                   | 92.63                        | 02/2011                           | 319.43                                   |
| 22     | JAGGAYYAPET - MELLACHERUVU<br>(SOUTH CENTRAL RAILWAY) - [N22000304]                                                                                                   | 313.24                       | 01/1999                           | 578.00                                   |
|        |                                                                                                                                                                       |                              |                                   |                                          |
|        | June,2018                                                                                                                                                             |                              |                                   |                                          |
|        |                                                                                                                                                                       |                              |                                   |                                          |
|        | <u>POWER</u>                                                                                                                                                          |                              |                                   |                                          |
| 23     | GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME<br>(ISTS) - PART A (POWER GRID CORPORATION OF<br>INDIA LIMITED) - [N18000197]                                  | 1,479.30                     | 04/2017                           | 897.12                                   |
| 24     | AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN<br>REGION (POWER GRID CORPORATION OF<br>INDIA LIMITED) - [N18000237]                                              | 167.75                       | 04/2019                           | 86.62                                    |
|        |                                                                                                                                                                       |                              |                                   |                                          |
|        | <u>RAILWAYS</u>                                                                                                                                                       |                              |                                   |                                          |
| 25     | RANCHI-LOHARDAGA(GC),SER<br>(SOUTH EASTERN RAILWAY) - [220100214]                                                                                                     | 194.07                       | 06/2004                           | 194.07                                   |
| 26     | BHOPAL BINA 3D LINE DOUBLING<br>(RAIL VIKAS NIGAM LTD.) - [N22000077]                                                                                                 | 687.20                       | 03/2010                           | 1,033.77                                 |

# Month wise List of Completed Projects Costing Rs. 150 crore and above during

2018-2019

| Sl. No | Project Name                                                                                                                                              | Original Cost (Rs. crore) | Original Date of commissioning | Cumulative Expenditure (Rs. crore) |
|--------|-----------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------|--------------------------------|------------------------------------|
|        |                                                                                                                                                           |                           |                                |                                    |
|        | July, 2018                                                                                                                                                |                           |                                |                                    |
|        |                                                                                                                                                           |                           |                                |                                    |
|        | <u>STEEL</u>                                                                                                                                              |                           |                                |                                    |
| 27     | EXPANSION OF BHILAI STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000057]                                                                   | 17,265.00                 | 03/2013                        | 19,855.23                          |
|        |                                                                                                                                                           |                           |                                |                                    |
|        | <u>PETROLEUM</u>                                                                                                                                          |                           |                                |                                    |
| 28     | DEVELOPMENT OF C-26 CLUSTER FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000133]                                                                  | 2,592.17                  | 05/2014                        | 2,049.26                           |
| 29     | CONSTRUCTION OF ONE ETP AT GGS-NADA, ANKLESHWAR (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000134]                                                     | 200.69                    | 07/2014                        | 109.58                             |
| 30     | CONSTRUCTION OF THREE ETPS, MEHSANA (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000135]                                                                 | 260.74                    | 11/2014                        | 83.44                              |
| 31     | PIPELINE REPLACEMENT PROJECT, AHMEDABAD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000159]                                                             | 202.25                    | 07/2016                        | 130.21                             |
| 32     | INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000172]                                                   | 4,124.35                  | 04/2016                        | 5,347.49                           |
| 33     | MH NORTH REDEVELOPMENT PHASE III (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000188]                                                                    | 5,706.47                  | 05/2017                        | 5,724.54                           |
| 34     | SONAMURA GGS AND PIPELINE PROJECT ( PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000246]   | 215.38                    | 06/2017                        | 198.98                             |
|        |                                                                                                                                                           |                           |                                |                                    |
|        | <u>POWER</u>                                                                                                                                              |                           |                                |                                    |
| 35     | BOKARO THERMAL POWER STATION-A (DAMODAR VALLEY CORPORATION) - [N18000199]                                                                                 | 2,313.00                  | 12/2011                        | 3,965.00                           |
| 36     | RAGHUNATHPUR THERMAL POWER STATION PHASE-I (DAMODAR VALLEY CORPORATION) - [N18000202]                                                                     | 4,122.00                  | 02/2011                        | 8,479.00                           |
|        |                                                                                                                                                           |                           |                                |                                    |
|        | September, 2018                                                                                                                                           |                           |                                |                                    |
|        |                                                                                                                                                           |                           |                                |                                    |
|        | <u>PETROLEUM</u>                                                                                                                                          |                           |                                |                                    |
| 37     | NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY (CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000199]                                 | 257.87                    | 11/2016                        | 243.30                             |
| 38     | NAWAGAM-KOYALI PIPELINE PROJECT Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000211]                                              | 195.63                    | 09/2018                        | 174.68                             |
| 39     | LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000264]                         | 337.06                    | 08/2018                        | 167.16                             |
|        |                                                                                                                                                           |                           |                                |                                    |
|        | <u>POWER</u>                                                                                                                                              |                           |                                |                                    |
| 40     | COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000143] | 514.20                    | 06/2015                        | 605.50                             |
| 41     | SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000169]                                               | 288.49                    | 02/2017                        | 276.10                             |



## Month wise List of Completed Projects Costing Rs. 150 crore and above during

2018-2019

| Sl. No | Project Name                                                                                                                                                  | Original Cost (Rs. crore) | Original Date of commissioning | Cumulative Expenditure (Rs. crore) |
|--------|---------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------|--------------------------------|------------------------------------|
| 42     | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000220]                 | 810.48                    | 12/2018                        | 528.50                             |
| 43     | TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) Central Sector Projects(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000254] | 2,525.00                  | 11/2017                        | 2,015.38                           |
| 44     | TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B Central Sector Projects(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000255]              | 2,225.00                  | 01/2018                        | 1,655.02                           |
|        |                                                                                                                                                               |                           |                                |                                    |
|        | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                                                            |                           |                                |                                    |
| 45     | CHAMBAL BRIDGE, NH-76 (RJ-5) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000068]                                                                             | 275.00                    | 02/2010                        | 252.25                             |
| 46     | DEOLI KOTA PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000148]                                                                                      | 593.00                    | 07/2013                        | 1,073.73                           |
| 47     | 2-LANNING WITH PS KHAGARIA-PURNEA PPP (ANNUITY)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000184]                                                           | 664.00                    | 02/2014                        | 654.59                             |
| 48     | 2-LANING WITH PS BHILWARA-LODPURA SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000240]                                                                | 240.10                    | 03/2016                        | 194.69                             |
| 49     | TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER ( UP TO GANDHAV BRIDGE) SECTION OF N (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000337]     | 538.08                    | 02/2018                        | 335.24                             |
| 50     | JAISALMER - BARMER (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000348]                                                                                       | 482.27                    | 02/2018                        | 308.83                             |
| 51     | TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 ( NEW NH NO -50) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000352]                    | 455.60                    | 07/2017                        | 202.68                             |
| 52     | JODHPUR - BARMER SECTION OF PACKAGE -I (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000354]                                                                   | 264.72                    | 04/2017                        | 98.18                              |
| 53     | UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA (PKG - 2) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000358]                                    | 562.34                    | 04/2018                        | 109.07                             |
| 54     | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-VI) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000433]                                          | 768.56                    | 03/2018                        | 774.99                             |
| 55     | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-V) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000436]                                           | 664.53                    | 03/2018                        | 702.97                             |
| 56     | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-IV) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000440]                                          | 789.31                    | 03/2018                        | 867.54                             |
| 57     | FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000481]                                                | 1,232.00                  | 08/2015                        | 1,091.17                           |
| 58     | FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000484]                                                          | 239.23                    | 12/2017                        | 123.47                             |
| 59     | FOUR LANING OF KAITHAL - RAJASTHAN BORDER PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000487]                                                       | 1,393.00                  | -                              | 1,917.40                           |
| 60     | FOUR LANING OF SHIVPURI - GUNA PACKAGE - I PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000500]                                                      | 830.36                    | 07/2018                        | 326.23                             |

# Month wise List of Completed Projects Costing Rs. 150 crore and above during

2018-2019

| Sl. No | Project Name                                                                                                                                           | Original Cost (Rs. crore) | Original Date of commissioning | Cumulative Expenditure (Rs. crore) |
|--------|--------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------|--------------------------------|------------------------------------|
| 61     | UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA ( PKG - 1) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000597]                            | 600.85                    | 05/2018                        | 109.84                             |
|        | October,2018                                                                                                                                           |                           |                                |                                    |
|        | <u>COAL</u>                                                                                                                                            |                           |                                |                                    |
| 62     | NEYVELI SOLAR POWER PROJECT 130 MW (NEYVELI LIGNITE CORPORATION) - [N06000151]                                                                         | 687.28                    | 06/2017                        | 758.30                             |
|        | <u>PETROLEUM</u>                                                                                                                                       |                           |                                |                                    |
| 63     | DIESEL HYDROTREATOR Central Sector Projects(NUMALIGARH REFINERY LIMITED) - [N16000207]                                                                 | 1,031.37                  | 01/2018                        | 562.77                             |
|        | <u>RAILWAYS</u>                                                                                                                                        |                           |                                |                                    |
| 64     | UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) (WESTERN RAILWAY) - [N22000122]                                                                      | 1,389.62                  | 03/2014                        | 2,140.08                           |
|        | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                                                     |                           |                                |                                    |
| 65     | PADI - DAHOD (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000353]                                                                                      | 279.14                    | 05/2017                        | 212.40                             |
|        | <u>TELECOMMUNICATIONS</u>                                                                                                                              |                           |                                |                                    |
| 66     | UP (EAST) ACCESS LOT1 (BHARAT SANCHAR NIGAM LIMITED) - [N26000112]                                                                                     | 169.45                    | 08/2018                        | 78.34                              |
|        | <u>URBAN DEVELOPMENT</u>                                                                                                                               |                           |                                |                                    |
| 67     | CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY EPC(CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000095] | 164.00                    | 11/2018                        | 123.90                             |
|        | November,2018                                                                                                                                          |                           |                                |                                    |
|        | <u>CIVIL AVIATION</u>                                                                                                                                  |                           |                                |                                    |
| 68     | CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000050]                                              | 309.46                    | 01/2011                        | 546.69                             |
|        | <u>PETROLEUM</u>                                                                                                                                       |                           |                                |                                    |
| 69     | LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000262]                     | 193.40                    | 01/2019                        | 106.79                             |
|        | <u>RAILWAYS</u>                                                                                                                                        |                           |                                |                                    |
| 70     | GOELKERA-MANOHARPUR,(LD)(SER) (RAIL VIKAS NIGAM LTD.) - [N22000045]                                                                                    | 261.70                    | 02/2006                        | 393.23                             |
| 71     | TINPAHAR - SAHIBGANJ (ER) (EASTERN RAILWAYS) - [N22000115]                                                                                             | 167.73                    | 03/2012                        | 238.53                             |

## Month wise List of Completed Projects Costing Rs. 150 crore and above during

2018-2019

| Sl. No | Project Name                                                                                                                                   | Original Cost<br>(Rs. crore) | Original Date of<br>commissioning | Cumulative<br>Expenditure<br>(Rs. crore) |
|--------|------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------|-----------------------------------|------------------------------------------|
| 72     | BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)<br>(EASTERN RAILWAYS) - [N22000119]                                  | 207.52                       | 12/2012                           | 335.35                                   |
| 73     | VIRAMGAM-SURENDRANAGAR (DL)<br>(WESTERN RAILWAY) - [N22000146]                                                                                 | 279.40                       | -                                 | 334.93                                   |
| 74     | PLASSEY-JIAGANJ DOUBLING<br>(EASTERN RAILWAYS) - [N22000220]                                                                                   | 248.07                       | 03/2015                           | 266.25                                   |
| 75     | SAINTHIA-TARAPITH 3RD LINE<br>(EASTERN RAILWAYS) - [N22000237]                                                                                 | 193.44                       | -                                 | 280.68                                   |
| 76     | KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC<br>(EASTERN RAILWAYS) - [N22000245]                                                    | 423.66                       | 03/2017                           | 652.79                                   |
|        |                                                                                                                                                |                              |                                   |                                          |
|        | <u>TELECOMMUNICATIONS</u>                                                                                                                      |                              |                                   |                                          |
| 77     | MAHARASHTRA ACESS (LOT 1)<br>Central Sector Projects(BHARAT SANCHAR NIGAM LIMITED) - [N26000109]                                               | 212.70                       | 05/2018                           | 37.25                                    |
| 78     | GUJARAT ACCESS (LOT 1)<br>Central Sector Projects(BHARAT SANCHAR NIGAM LIMITED) - [N26000111]                                                  | 171.54                       | 05/2018                           | 72.46                                    |
|        |                                                                                                                                                |                              |                                   |                                          |
|        | <u>URBAN DEVELOPMENT</u>                                                                                                                       |                              |                                   |                                          |
| 79     | OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C-41-43 G BLOCK BANDRA<br>(CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000068]                 | 241.33                       | 03/2016                           | 357.50                                   |
|        |                                                                                                                                                |                              |                                   |                                          |
|        | December,2018                                                                                                                                  |                              |                                   |                                          |
|        |                                                                                                                                                |                              |                                   |                                          |
|        | <u>COAL</u>                                                                                                                                    |                              |                                   |                                          |
| 80     | RAJMAHAL OC EXP.<br>(EASTERN COAL FIELDS LIMITED) - [N06000056]                                                                                | 153.82                       | 03/2014                           | 131.07                                   |
|        |                                                                                                                                                |                              |                                   |                                          |
|        | <u>PETROLEUM</u>                                                                                                                               |                              |                                   |                                          |
| 81     | PARADIP HALDIA DURGAPUR LPG PIPELINE<br>(INDIAN OIL CORPORATION LIMITED) - [N16000148]                                                         | 913.00                       | 06/2018                           | 1,323.53                                 |
| 82     | PIPELINE REPLACEMENT PROJECT -4<br>(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000203]                                                       | 2,899.93                     | 05/2017                           | 2,183.66                                 |
| 83     | ANKLESHWAR BARODA PIPELINE PROJECT<br>(GAS AUTHORITY OF INDIA LIMITED) - [N16000232]                                                           | 199.95                       | 03/2018                           | 156.83                                   |
|        |                                                                                                                                                |                              |                                   |                                          |
|        | <u>POWER</u>                                                                                                                                   |                              |                                   |                                          |
| 84     | TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.<br>(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000080]                        | 2,144.00                     | 12/2012                           | 2,669.96                                 |
| 85     | EASTERN REGION STRENGTHENING SCHEME-III<br>(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000100]                                             | 1,272.80                     | 11/2012                           | 1,473.05                                 |
| 86     | INSTALLATION OF STATCOMS IN WESTERN REGION<br>(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000185]                                          | 1,071.24                     | 09/2017                           | 649.26                                   |
| 87     | CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1)<br>(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000195] | 780.33                       | 10/2018                           | 499.05                                   |

# Month wise List of Completed Projects Costing Rs. 150 crore and above during

2018-2019

| Sl. No | Project Name                                                                                                                                                       | Original Cost<br>(Rs. crore) | Original Date of<br>commissioning | Cumulative<br>Expenditure<br>(Rs. crore) |
|--------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------|-----------------------------------|------------------------------------------|
| 88     | GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000200]                                    | 2,247.37                     | 07/2018                           | 1,531.89                                 |
| 89     | S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000221]               | 287.99                       | 06/2018                           | 164.22                                   |
| 90     | EASTERN REGION STRENGTHENING SCHEME XIV (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000224]                                                                    | 167.01                       | 11/2018                           | 119.23                                   |
| 91     | PROVISION OF SERIES REACTORS IN NORTHERN REGION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000232]                                                            | 177.52                       | 02/2019                           | 87.48                                    |
| 92     | TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A Central Sector Projects (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000253] | 955.00                       | 12/2015                           | 1,247.66                                 |
| 93     | TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V Central Sector Projects (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000256]                    | 1,750.00                     | 06/2018                           | 1,335.04                                 |
|        |                                                                                                                                                                    |                              |                                   |                                          |
|        | <u>HEALTH AND FAMILY WELFARE</u>                                                                                                                                   |                              |                                   |                                          |
| 94     | NCI AIIMS JHAJJAR RESIDENTIAL HARYANA (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000014]                                                                | 312.99                       | 08/2018                           | 318.00                                   |
|        |                                                                                                                                                                    |                              |                                   |                                          |
|        | <u>RAILWAYS</u>                                                                                                                                                    |                              |                                   |                                          |
| 95     | BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR (NORTH EAST FRONTIER RAILWAY) - [220100201]                                                                           | 3,230.02                     | 04/2008                           | 5,298.09                                 |
| 96     | RANI-MARWAR JN. PATCH DOUBLING (NORTH WESTERN RAILWAY) - [N22000156]                                                                                               | 288.97                       | 11/2018                           | 315.60                                   |
| 97     | NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT (NORTH EAST FRONTIER RAILWAY) - [N22000198]                                                                        | 283.55                       | 03/2019                           | 480.81                                   |
| 98     | BANKURA DAMODAR VALLEY RIVER 96 KM WITH MM FOR EXTENSION OF NEW LINE FROM BOWAICHANDI KHANA 24. (SOUTH EASTERN RAILWAY) - [N22000491]                              | 1,027.40                     | 03/2022                           | 195.00                                   |
|        |                                                                                                                                                                    |                              |                                   |                                          |
|        | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                                                                 |                              |                                   |                                          |
| 99     | MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106281]                                                            | 200.00                       | 04/2009                           | 248.60                                   |
| 100    | JALANDHAR - AMRITSAR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000351]                                                                                          | 523.85                       | 01/2016                           | 170.68                                   |
|        |                                                                                                                                                                    |                              |                                   |                                          |
|        | <u>TELECOMMUNICATIONS</u>                                                                                                                                          |                              |                                   |                                          |
| 101    | MAHARASHTRA NODAL (LOT 1) Central Sector Projects (BHARAT SANCHAR NIGAM LIMITED) - [N26000107]                                                                     | 159.30                       | 04/2018                           | 60.27                                    |
|        |                                                                                                                                                                    |                              |                                   |                                          |
|        |                                                                                                                                                                    |                              |                                   |                                          |
|        |                                                                                                                                                                    |                              |                                   |                                          |

**TABLE-3**

**Projects Added / Completed / Dropped / Frozen Rs.150 Crore and above**

|                                                          |      |
|----------------------------------------------------------|------|
| No of Projects in Previous Month                         | 1443 |
| No of Projects Completed/Dropped/Frozen in Current Month | 22   |
| No of                                                    | 1    |
| No of Projects added in Current Month                    | 4    |
| No of Projects in Current Month                          | 1424 |

| Project status Rs.150 Crore and above |               |             |              |                               |               |       |
|---------------------------------------|---------------|-------------|--------------|-------------------------------|---------------|-------|
| Number of Projects                    |               |             |              |                               |               |       |
| With Respect To                       | Delayed       | Ahead       | On schedule  | Without ODC but DOC available | Without D.O.C | Total |
| Original ( Date )                     | 384 ( 26.97%) | 26 ( 1.83%) | 328( 23.03%) | 79 ( 5.55%)                   | 607( 2.63%)   | 1424  |
| Latest Approved ( Date)               | 326 ( 22.89%) | 27 ( 1.90%) | 398( 27.95%) | 66 ( 4.63%)                   | 607( 2.63%)   | 1424  |

| Project cost Rs.150 Crore and above   |                 |                 |                  |                  |                               |             |       |
|---------------------------------------|-----------------|-----------------|------------------|------------------|-------------------------------|-------------|-------|
| (All Cost/ Expenditure in Rs. crore ) |                 |                 |                  |                  |                               |             |       |
| Cost overrun                          |                 |                 |                  |                  |                               |             |       |
|                                       | No. of Projects | Sanctioned Cost | Anticipated Cost | Expenditure Cost | % cost w.r.t anticipated cost | Rs crore    | %     |
| Project with No Revision in Cost      | 1213            | 15,09,197.92    | 17,11,478.57     | 5,97,421.76      | 34.90                         | 2,02,280.65 | 13.40 |
| Project with Revision in Cost         | 211             | 4,57,159.01     | 4,22,171.24      | 2,09,576.02      | 49.60                         | -34,987.77  | -7.70 |
| Total                                 | 1,424           | 19,66,356.93    | 21,33,649.81     | 8,06,997.78      | 37.82                         | 1,67,292.88 | 8.51  |
| Original Cost of All Projects         |                 |                 |                  |                  |                               |             |       |
| Original Cost                         | 1,424           | 18,17,469.76    | 21,33,649.81     | 8,06,997.78      | 37.82                         | 3,16,180.05 | 17.40 |

| Delayed Project cost Rs.150 Crore and above |                 |                 |                  |                  |                               |             |       |
|---------------------------------------------|-----------------|-----------------|------------------|------------------|-------------------------------|-------------|-------|
| (All Cost/ Expenditure in Rs. crore )       |                 |                 |                  |                  |                               |             |       |
| Cost overrun                                |                 |                 |                  |                  |                               |             |       |
| With Respect to                             | No. of Projects | Sanctioned Cost | Anticipated Cost | Expenditure Cost | % cost w.r.t anticipated cost | Rs crore    | %     |
| Original (OCE)                              | 384             | 7,44,405.01     | 8,92,170.35      | 4,81,926.04      | 54.00                         | 1,47,765.34 | 19.85 |
| Latest Approved (RCE)                       | 326             | 5,06,637.61     | 6,04,354.05      | 2,93,394.51      | 48.50                         | 97,716.44   | 19.29 |
|                                             |                 |                 |                  |                  |                               |             |       |

| Additional Delayed Project cost Rs.150 Crore and above |                 |                 |                  |                  |                               |          |       |
|--------------------------------------------------------|-----------------|-----------------|------------------|------------------|-------------------------------|----------|-------|
| (All Cost/ Expenditure in Rs. crore )                  |                 |                 |                  |                  |                               |          |       |
| Cost overrun                                           |                 |                 |                  |                  |                               |          |       |
| With Respect to                                        | No. of Projects | Sanctioned Cost | Anticipated Cost | Expenditure Cost | % cost w.r.t anticipated cost | Rs crore | %     |
| Latest Approved                                        | 69              | 68,133.12       | 77,451.51        | 56,359.07        | 72.80                         | 9,318.39 | 13.70 |
| Total                                                  | 69              | 68,133.12       | 77,451.51        | 56,359.07        | 72.77                         | 9,318.39 | 13.68 |


## Summary of projects in the Flash Report for the month of December, 2018

### Project Implementation - Current Status:

|                                                                                     |      |
|-------------------------------------------------------------------------------------|------|
| Number of Projects in Previous Month                                                | 1443 |
| Number of Projects completed/dropped/frozen in Current Month                        | 22   |
| Number of Projects elevated to the status of Major project during the current month | 1    |
| Number of Projects Added in Current Month                                           | 4    |
| Number of Projects in Current Month                                                 | 1424 |

### Brief Analysis

**Project Status with respect to Original Schedule:** Out of 1424 projects, 26 projects are ahead of schedule, 328 projects are on schedule 384 projects are delayed. 607 projects do not have fixed dates of commissioning. 79 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

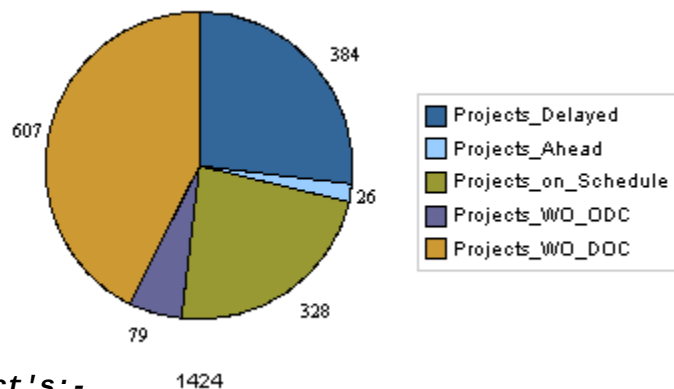


Total No Of Project's:-

### Investment Scenario

**Total original cost of implementation of 1424 projects when sanctioned, was of the order of Rs. 1817469.76 crore but this was subsequently revised to Rs. 2133649.81 crore implying a cost overrun of 17.4%. The expenditure incurred on these projects till December, 2018 is Rs. 806997.78 crore, which is 37.8% of the anticipated cost of the projects.**

Figures are in Rs. Crore

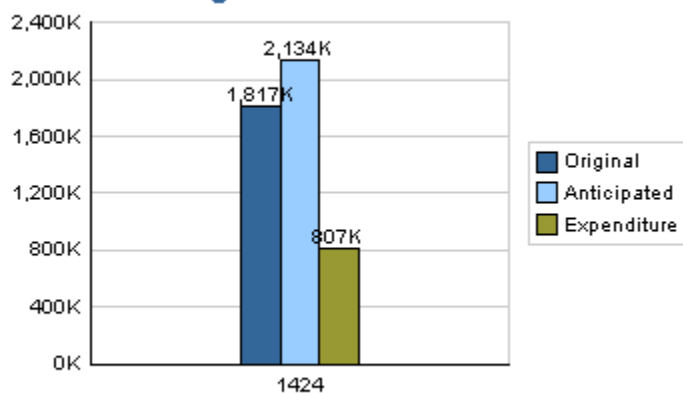

**TABLE-4**

| Extent of cost overrun in projects with respect to original schedule(Sector Wise)RS. 150 Crore and above<br>(All Cost/ Expenditure in Rs. crore ) |                             |                 |               |                  |                  |                             |               |                  |                  |
|---------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------|-----------------|---------------|------------------|------------------|-----------------------------|---------------|------------------|------------------|
|                                                                                                                                                   |                             |                 |               |                  |                  | Projects with cost overrun^ |               |                  |                  |
| Sl.No                                                                                                                                             | Sector                      | No. of Projects | Original Cost | Anticipated cost | Cost overrun (%) | No.                         | Original Cost | Anticipated Cost | Cost overrun (%) |
| 1                                                                                                                                                 | ATOMIC ENERGY               | 4               | 67,120.00     | 74,849.00        | 11.52            | 2                           | 14,951.00     | 22,680.00        | 51.70            |
| 2                                                                                                                                                 | CIVIL AVIATION              | 1               | 314.61        | 441.33           | 40.28            | 1                           | 314.61        | 441.33           | 40.28            |
| 3                                                                                                                                                 | COAL                        | 97              | 96,954.88     | 96,426.38        | -0.55            | 10                          | 19,631.17     | 20,970.49        | 6.82             |
| 4                                                                                                                                                 | FERTILISERS                 | 6               | 1,781.92      | 1,793.57         | 0.65             | 1                           | 197.79        | 209.44           | 5.89             |
| 5                                                                                                                                                 | MINES                       | 5               | 7,078.62      | 7,078.62         | 0.00             | 0                           | 0.00          | 0.00             | 0.00             |
| 6                                                                                                                                                 | STEEL                       | 13              | 32,529.65     | 32,317.05        | -0.65            | 1                           | 343.00        | 488.40           | 42.39            |
| 7                                                                                                                                                 | PETROLEUM                   | 137             | 2,21,562.48   | 2,23,009.33      | 0.65             | 15                          | 20,537.74     | 26,814.72        | 30.56            |
| 8                                                                                                                                                 | POWER                       | 95              | 2,96,370.25   | 3,59,705.13      | 21.37            | 40                          | 1,72,830.59   | 2,36,165.47      | 36.65            |
| 9                                                                                                                                                 | HEAVY INDUSTRY              | 2               | 3,272.00      | 5,381.30         | 64.47            | 1                           | 1,718.00      | 3,827.30         | 122.78           |
| 10                                                                                                                                                | HEALTH AND FAMILY WELFARE   | 20              | 8,129.23      | 8,246.52         | 1.44             | 3                           | 1,076.25      | 1,193.54         | 10.90            |
| 11                                                                                                                                                | RAILWAYS                    | 367             | 4,85,710.46   | 6,96,269.31      | 43.35            | 205                         | 1,68,116.34   | 3,89,745.97      | 131.83           |
| 12                                                                                                                                                | ROAD TRANSPORT AND HIGHWAYS | 605             | 4,11,159.45   | 4,25,383.97      | 3.46             | 49                          | 29,654.32     | 44,654.88        | 50.58            |
| 13                                                                                                                                                | SHIPPING AND PORTS          | 6               | 7,988.29      | 8,426.32         | 5.48             | 3                           | 760.89        | 1,541.02         | 102.53           |
| 14                                                                                                                                                | TELECOMMUNICATIONS          | 6               | 16,478.21     | 27,707.01        | 68.14            | 1                           | 13,334.00     | 24,664.00        | 84.97            |
| 15                                                                                                                                                | URBAN DEVELOPMENT           | 58              | 1,60,566.07   | 1,66,153.31      | 3.48             | 10                          | 22,323.08     | 27,919.21        | 25.07            |
| 16                                                                                                                                                | DEFENCE PRODUCTION          | 2               | 453.64        | 461.66           | 1.77             | 2                           | 453.64        | 461.66           | 1.77             |
|                                                                                                                                                   |                             |                 |               |                  |                  |                             |               |                  |                  |
| Total                                                                                                                                             |                             | 1424            | 18,17,469.76  | 21,33,649.81     | 17.40            | 344                         | 4,66,242.42   | 8,01,777.43      | 71.97            |

^ - Cost Overrun = Anticipated Cost minus Original Cost

**TABLE-5**

| <b>Extent of cost overrun in projects with respect to original schedule(State Wise) Rs. 150 Crore and above</b><br>(All Cost/ Expenditure in Rs. Crore) |                   |                 |                     |                     |                  |                                               |                    |                    |                  |
|---------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------|-----------------|---------------------|---------------------|------------------|-----------------------------------------------|--------------------|--------------------|------------------|
|                                                                                                                                                         |                   |                 |                     |                     |                  | <b>Projects with cost overrun<sup>^</sup></b> |                    |                    |                  |
| Sl.No                                                                                                                                                   | State             | No. of Projects | Original Cost       | Anticipated Cost    | Cost overrun (%) | No.                                           | Original Cost      | Anticipated Cost   | Cost overrun (%) |
| 1                                                                                                                                                       | ANDHRA PRADESH    | 69              | 1,07,461.29         | 1,11,065.37         | 3.35             | 9                                             | 7,934.53           | 12,408.72          | 56.39            |
| 2                                                                                                                                                       | ARUNACHAL PRADESH | 31              | 16,421.02           | 33,547.53           | 104.30           | 5                                             | 9,181.79           | 26,308.30          | 186.53           |
| 3                                                                                                                                                       | ASSAM             | 45              | 27,704.18           | 33,843.20           | 22.16            | 13                                            | 7,811.37           | 14,278.59          | 82.79            |
| 4                                                                                                                                                       | BIHAR             | 91              | 76,252.26           | 1,11,749.59         | 46.55            | 33                                            | 40,972.00          | 76,544.96          | 86.82            |
| 5                                                                                                                                                       | GOA               | 10              | 4,292.52            | 4,300.54            | 0.19             | 2                                             | 453.64             | 461.66             | 1.77             |
| 6                                                                                                                                                       | GUJARAT           | 49              | 51,576.03           | 57,377.20           | 11.25            | 5                                             | 13,724.36          | 21,201.45          | 54.48            |
| 7                                                                                                                                                       | HARYANA           | 29              | 21,083.41           | 22,987.06           | 9.03             | 4                                             | 2,139.14           | 4,176.00           | 95.22            |
| 8                                                                                                                                                       | HIMACHAL PRADESH  | 13              | 17,058.17           | 26,566.39           | 55.74            | 2                                             | 6,886.58           | 16,394.80          | 138.07           |
| 9                                                                                                                                                       | JAMMU AND KASHMIR | 10              | 25,238.37           | 51,232.67           | 103.00           | 2                                             | 4,288.41           | 30,282.71          | 606.15           |
| 10                                                                                                                                                      | KARNATAKA         | 46              | 82,156.70           | 87,206.53           | 6.15             | 11                                            | 20,744.24          | 25,990.82          | 25.29            |
| 11                                                                                                                                                      | KERALA            | 22              | 25,879.48           | 28,054.10           | 8.40             | 6                                             | 7,475.98           | 9,846.14           | 31.70            |
| 12                                                                                                                                                      | MADHYA PRADESH    | 60              | 67,550.02           | 72,708.48           | 7.64             | 10                                            | 26,531.45          | 35,146.93          | 32.47            |
| 13                                                                                                                                                      | MAHARASHTRA       | 129             | 1,85,696.80         | 1,97,861.32         | 6.55             | 25                                            | 31,645.68          | 45,825.52          | 44.81            |
| 14                                                                                                                                                      | MANIPUR           | 2               | 4,670.86            | 14,025.69           | 200.28           | 1                                             | 4,454.17           | 13,809.00          | 210.02           |
| 15                                                                                                                                                      | MEGHALAYA         | 7               | 4,484.97            | 9,578.51            | 113.57           | 1                                             | 906.46             | 6,000.00           | 561.92           |
| 16                                                                                                                                                      | MIZORAM           | 4               | 3,406.61            | 5,981.14            | 75.57            | 1                                             | 2,393.47           | 4,968.00           | 107.56           |
| 17                                                                                                                                                      | NAGALAND          | 21              | 13,711.07           | 14,384.55           | 4.91             | 1                                             | 2,326.52           | 3,000.00           | 28.95            |
| 18                                                                                                                                                      | ODISHA            | 84              | 96,187.70           | 1,01,748.66         | 5.78             | 19                                            | 24,847.39          | 30,409.01          | 22.38            |
| 19                                                                                                                                                      | PUNJAB            | 33              | 17,042.04           | 17,047.77           | 0.03             | 2                                             | 1,328.50           | 1,361.27           | 2.47             |
| 20                                                                                                                                                      | RAJASTHAN         | 56              | 46,045.92           | 48,245.10           | 4.78             | 11                                            | 5,160.21           | 7,368.28           | 42.79            |
| 21                                                                                                                                                      | SIKKIM            | 9               | 3,476.73            | 6,281.03            | 80.66            | 2                                             | 1,727.48           | 4,532.06           | 162.35           |
| 22                                                                                                                                                      | TAMIL NADU        | 76              | 1,19,890.58         | 1,37,033.24         | 14.30            | 26                                            | 29,413.59          | 47,647.46          | 61.99            |
| 23                                                                                                                                                      | TRIPURA           | 9               | 4,422.36            | 8,345.05            | 88.70            | 7                                             | 3,555.47           | 7,478.16           | 110.33           |
| 24                                                                                                                                                      | UTTAR PRADESH     | 110             | 1,34,449.08         | 1,35,916.30         | 1.09             | 18                                            | 25,563.98          | 29,709.84          | 16.22            |
| 25                                                                                                                                                      | WEST BENGAL       | 53              | 57,557.73           | 66,897.02           | 16.23            | 18                                            | 16,956.22          | 26,615.20          | 56.96            |
| 26                                                                                                                                                      | A & N ISLANDS     | 8               | 2,385.01            | 2,492.59            | 4.51             | 2                                             | 552.41             | 679.33             | 22.98            |
| 27                                                                                                                                                      | D & N HAVELI      | 1               | 6,086.08            | 5,842.31            | -4.01            | 0                                             | 0.00               | 0.00               | 0.00             |
| 28                                                                                                                                                      | DELHI             | 22              | 55,263.55           | 62,738.78           | 13.53            | 6                                             | 6,981.71           | 14,456.94          | 107.07           |
| 29                                                                                                                                                      | CHHATISGARH       | 45              | 78,684.04           | 82,085.57           | 4.32             | 7                                             | 17,333.75          | 22,308.14          | 28.70            |
| 30                                                                                                                                                      | JHARKHAND         | 47              | 47,231.00           | 51,136.74           | 8.27             | 9                                             | 22,304.03          | 26,213.55          | 17.53            |
| 31                                                                                                                                                      | UTTARAKHAND       | 28              | 33,689.40           | 39,554.65           | 17.41            | 9                                             | 9,874.84           | 15,740.60          | 59.40            |
| 32                                                                                                                                                      | TELANGANA         | 42              | 34,502.53           | 38,040.07           | 10.25            | 12                                            | 5,455.32           | 9,323.89           | 70.91            |
| 33                                                                                                                                                      | MULTI STATE       | 163             | 3,45,912.25         | 4,47,775.06         | 29.45            | 65                                            | 1,05,317.73        | 2,11,290.10        | 100.62           |
|                                                                                                                                                         |                   |                 |                     |                     |                  |                                               |                    |                    |                  |
| <b>Total</b>                                                                                                                                            |                   | <b>1424</b>     | <b>18,17,469.76</b> | <b>21,33,649.81</b> | <b>17.40</b>     | <b>344</b>                                    | <b>4,66,242.42</b> | <b>8,01,777.43</b> | <b>71.97</b>     |

<sup>^</sup> - Cost Overrun = Anticipated Cost minus Original Cost



**TABLE-6**

| Extent of time overrun in projects with respect to original schedule Rs.150 Crore and above<br>(All Cost/ Expenditure in Rs. crore) |                             |                 |               |                  |                  |                               |               |                  |                            |
|-------------------------------------------------------------------------------------------------------------------------------------|-----------------------------|-----------------|---------------|------------------|------------------|-------------------------------|---------------|------------------|----------------------------|
|                                                                                                                                     |                             |                 |               |                  |                  | Projects with time overruns\$ |               |                  |                            |
| Sl.No                                                                                                                               | Sector                      | No. of Projects | Original Cost | Anticipated Cost | Cost overrun (%) | No.                           | Original Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1                                                                                                                                   | ATOMIC ENERGY               | 4               | 67,120.00     | 74,849.00        | 11.52            | 4                             | 67,120.00     | 74,849.00        | 36 - 102                   |
| 2                                                                                                                                   | CIVIL AVIATION              | 1               | 314.61        | 441.33           | 40.28            | 1                             | 314.61        | 441.33           | 21 - 21                    |
| 3                                                                                                                                   | COAL                        | 97              | 96,954.88     | 96,426.38        | -0.55            | 36                            | 20,727.79     | 20,687.07        | 12 - 144                   |
| 4                                                                                                                                   | FERTILISERS                 | 6               | 1,781.92      | 1,793.57         | 0.65             | 2                             | 680.64        | 692.29           | 13 - 29                    |
| 5                                                                                                                                   | MINES                       | 5               | 7,078.62      | 7,078.62         | 0.00             | 0                             | 0.00          | 0.00             | -                          |
| 6                                                                                                                                   | STEEL                       | 13              | 32,529.65     | 32,317.05        | -0.65            | 9                             | 26,430.72     | 26,072.72        | 6 - 49                     |
| 7                                                                                                                                   | PETROLEUM                   | 137             | 2,21,562.48   | 2,23,009.33      | 0.65             | 33                            | 90,253.71     | 92,254.95        | 1 - 78                     |
| 8                                                                                                                                   | POWER                       | 95              | 2,96,370.25   | 3,59,705.13      | 21.37            | 56                            | 1,95,032.96   | 2,38,881.23      | 2 - 147                    |
| 9                                                                                                                                   | HEAVY INDUSTRY              | 2               | 3,272.00      | 5,381.30         | 64.47            | 1                             | 1,718.00      | 3,827.30         | 93 - 93                    |
| 10                                                                                                                                  | HEALTH AND FAMILY WELFARE   | 20              | 8,129.23      | 8,246.52         | 1.44             | 5                             | 1,429.14      | 1,528.92         | 15 - 83                    |
| 11                                                                                                                                  | RAILWAYS                    | 367             | 4,85,710.46   | 6,96,269.31      | 43.35            | 94                            | 1,20,608.03   | 1,96,974.52      | 1 - 324                    |
| 12                                                                                                                                  | ROAD TRANSPORT AND HIGHWAYS | 605             | 4,11,159.45   | 4,25,383.97      | 3.46             | 112                           | 96,101.97     | 99,712.68        | 1 - 131                    |
| 13                                                                                                                                  | SHIPPING AND PORTS          | 6               | 7,988.29      | 8,426.32         | 5.48             | 3                             | 1,116.39      | 1,527.36         | 29 - 155                   |
| 14                                                                                                                                  | TELECOMMUNICATIONS          | 6               | 16,478.21     | 27,707.01        | 68.14            | 4                             | 13,948.78     | 25,277.58        | 4 - 58                     |
| 15                                                                                                                                  | URBAN DEVELOPMENT           | 58              | 1,60,566.07   | 1,66,153.31      | 3.48             | 23                            | 1,08,754.58   | 1,09,273.03      | 2 - 77                     |
| 16                                                                                                                                  | DEFENCE PRODUCTION          | 2               | 453.64        | 461.66           | 1.77             | 1                             | 167.69        | 170.37           | 8 - 8                      |
| Total                                                                                                                               |                             | 1424            | 18,17,469.76  | 21,33,649.81     | 17.40            | 384                           | 7,44,405.01   | 8,92,170.35      |                            |

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

**TABLE-7**

**Extent of time overrun in projects with respect to original schedule(State Wise) Rs.150 Crore and above**

(All Cost/ Expenditure in Rs. crore)

|       |                   |                 |               |                  |                  | Projects with time overruns\$ |               |                  |                            |
|-------|-------------------|-----------------|---------------|------------------|------------------|-------------------------------|---------------|------------------|----------------------------|
| Sl.No | State             | No. of Projects | Original Cost | Anticipated cost | Cost overrun (%) | No.                           | Original Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1     | ANDHRA PRADESH    | 69              | 1,07,461.29   | 1,11,065.37      | 3.35             | 16                            | 51,825.14     | 53,592.31        | 2 - 168                    |
| 2     | ARUNACHAL PRADESH | 31              | 16,421.02     | 33,547.53        | 104.30           | 2                             | 2,635.83      | 6,334.96         | 36 - 111                   |
| 3     | ASSAM             | 45              | 27,704.18     | 33,843.20        | 22.16            | 12                            | 9,314.06      | 14,645.50        | 8 - 131                    |
| 4     | BIHAR             | 91              | 76,252.26     | 1,11,749.59      | 46.55            | 23                            | 40,000.83     | 56,549.81        | 4 - 123                    |
| 5     | GOA               | 10              | 4,292.52      | 4,300.54         | 0.19             | 1                             | 167.69        | 170.37           | 8 - 8                      |
| 6     | GUJARAT           | 49              | 51,576.03     | 57,377.20        | 11.25            | 10                            | 16,488.02     | 22,022.92        | 2 - 84                     |
| 7     | HARYANA           | 29              | 21,083.41     | 22,987.06        | 9.03             | 4                             | 2,534.20      | 3,714.20         | 3 - 91                     |
| 8     | HIMACHAL PRADESH  | 13              | 17,058.17     | 26,566.39        | 55.74            | 4                             | 7,041.67      | 12,516.88        | 12 - 147                   |
| 9     | JAMMU AND KASHMIR | 10              | 25,238.37     | 51,232.67        | 103.00           | 5                             | 16,904.75     | 42,353.75        | 10 - 220                   |
| 10    | KARNATAKA         | 46              | 82,156.70     | 87,206.53        | 6.15             | 18                            | 43,316.14     | 44,347.14        | 3 - 264                    |
| 11    | KERALA            | 22              | 25,879.48     | 28,054.10        | 8.40             | 8                             | 16,401.45     | 17,142.27        | 8 - 79                     |
| 12    | MADHYA PRADESH    | 60              | 67,550.02     | 72,708.48        | 7.64             | 10                            | 18,086.19     | 20,646.25        | 4 - 96                     |
| 13    | MAHARASHTRA       | 129             | 1,85,696.80   | 1,97,861.32      | 6.55             | 41                            | 82,006.02     | 88,174.36        | 2 - 192                    |
| 14    | MANIPUR           | 2               | 4,670.86      | 14,025.69        | 200.28           | 2                             | 4,670.86      | 14,025.69        | 56 - 108                   |
| 15    | MEGHALAYA         | 7               | 4,484.97      | 9,578.51         | 113.57           | 4                             | 1,530.52      | 1,530.52         | 10 - 60                    |
| 16    | MIZORAM           | 4               | 3,406.61      | 5,981.14         | 75.57            | 1                             | 2,393.47      | 4,968.00         | 81 - 81                    |
| 17    | NAGALAND          | 21              | 13,711.07     | 14,384.55        | 4.91             | 4                             | 3,525.63      | 4,199.11         | 36 - 79                    |
| 18    | ODISHA            | 84              | 96,187.70     | 1,01,748.66      | 5.78             | 25                            | 36,131.33     | 41,375.05        | 3 - 147                    |
| 19    | PUNJAB            | 33              | 17,042.04     | 17,047.77        | 0.03             | 5                             | 2,036.78      | 2,038.51         | 1 - 22                     |
| 20    | RAJASTHAN         | 56              | 46,045.92     | 48,245.10        | 4.78             | 19                            | 24,193.54     | 25,140.63        | 1 - 89                     |
| 21    | SIKKIM            | 9               | 3,476.73      | 6,281.03         | 80.66            | 1                             | 1,339.48      | 4,084.69         | 51 - 51                    |
| 22    | TAMIL NADU        | 76              | 1,19,890.58   | 1,37,033.24      | 14.30            | 22                            | 67,513.71     | 70,171.21        | 1 - 155                    |
| 23    | TRIPURA           | 9               | 4,422.36      | 8,345.05         | 88.70            | 2                             | 1,711.63      | 4,057.00         | 31 - 60                    |
| 24    | UTTAR PRADESH     | 110             | 1,34,449.08   | 1,35,916.30      | 1.09             | 24                            | 41,292.86     | 41,864.05        | 2 - 239                    |
| 25    | WEST BENGAL       | 53              | 57,557.73     | 66,897.02        | 16.23            | 19                            | 23,724.45     | 27,243.66        | 5 - 324                    |
| 26    | A & N ISLANDS     | 8               | 2,385.01      | 2,492.59         | 4.51             | 1                             | 314.61        | 441.33           | 21 - 21                    |
| 27    | D & N HAVELI      | 1               | 6,086.08      | 5,842.31         | -4.01            | 1                             | 6,086.08      | 5,842.31         | 5 - 5                      |
| 28    | DELHI             | 22              | 55,263.55     | 62,738.78        | 13.53            | 7                             | 42,308.26     | 42,780.83        | 5 - 83                     |
| 29    | CHHATISGARH       | 45              | 78,684.04     | 82,085.57        | 4.32             | 11                            | 30,819.18     | 32,754.74        | 13 - 117                   |
| 30    | JHARKHAND         | 47              | 47,231.00     | 51,136.74        | 8.27             | 17                            | 24,303.13     | 25,545.67        | 9 - 108                    |
| 31    | UTTARAKHAND       | 28              | 33,689.40     | 39,554.65        | 17.41            | 6                             | 23,935.83     | 29,313.50        | 15 - 102                   |
| 32    | TELANGANA         | 42              | 34,502.53     | 38,040.07        | 10.25            | 15                            | 18,452.17     | 19,234.54        | 3 - 144                    |
| 33    | MULTI STATE       | 163             | 3,45,912.25   | 4,47,775.06      | 29.45            | 44                            | 81,399.50     | 1,13,348.59      | 1 - 228                    |
|       |                   |                 |               |                  |                  |                               |               |                  |                            |
| Total |                   | 1424            | 18,17,469.76  | 21,33,649.81     | 17.40            | 384                           | 7,44,405.01   | 8,92,170.35      |                            |

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

**TABLE-8**

| Extent of time overrun in projects with respect to latest schedule Rs.150 Crore and above<br>(All Cost/ Expenditure in Rs. crore) |                             |                 |                      |                  |                  |                               |                      |                  |                            |
|-----------------------------------------------------------------------------------------------------------------------------------|-----------------------------|-----------------|----------------------|------------------|------------------|-------------------------------|----------------------|------------------|----------------------------|
|                                                                                                                                   |                             |                 |                      |                  |                  | Projects with time overruns\$ |                      |                  |                            |
| Sl.No                                                                                                                             | Sector                      | No. of Projects | Latest Approved Cost | Anticipated Cost | Cost overrun (%) | No.                           | Latest Approved Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1                                                                                                                                 | ATOMIC ENERGY               | 4               | 72,241.00            | 74,849.00        | 3.61             | 4                             | 72,241.00            | 74,849.00        | 36 - 102                   |
| 2                                                                                                                                 | CIVIL AVIATION              | 1               | 314.61               | 441.33           | 40.28            | 1                             | 314.61               | 441.33           | 21 - 21                    |
| 3                                                                                                                                 | COAL                        | 97              | 96,507.73            | 96,426.38        | -0.08            | 35                            | 19,426.09            | 20,054.26        | 0 - 144                    |
| 4                                                                                                                                 | FERTILISERS                 | 6               | 1,793.57             | 1,793.57         | 0.00             | 0                             | 0.00                 | 0.00             | -                          |
| 5                                                                                                                                 | MINES                       | 5               | 7,078.62             | 7,078.62         | 0.00             | 0                             | 0.00                 | 0.00             | -                          |
| 6                                                                                                                                 | STEEL                       | 13              | 32,529.65            | 32,317.05        | -0.65            | 8                             | 10,905.72            | 10,547.72        | 6 - 32                     |
| 7                                                                                                                                 | PETROLEUM                   | 137             | 2,25,033.26          | 2,23,009.33      | -0.90            | 16                            | 21,251.19            | 20,323.66        | 1 - 78                     |
| 8                                                                                                                                 | POWER                       | 95              | 3,71,673.80          | 3,59,705.13      | -3.22            | 38                            | 93,174.07            | 1,11,192.25      | 2 - 147                    |
| 9                                                                                                                                 | HEAVY INDUSTRY              | 2               | 5,281.30             | 5,381.30         | 1.89             | 0                             | 0.00                 | 0.00             | -                          |
| 10                                                                                                                                | HEALTH AND FAMILY WELFARE   | 20              | 8,129.23             | 8,246.52         | 1.44             | 3                             | 651.04               | 651.04           | 16 - 26                    |
| 11                                                                                                                                | RAILWAYS                    | 367             | 5,47,601.88          | 6,96,269.31      | 27.15            | 87                            | 1,16,825.55          | 1,79,084.26      | -12 - 239                  |
| 12                                                                                                                                | ROAD TRANSPORT AND HIGHWAYS | 605             | 4,11,729.58          | 4,25,383.97      | 3.32             | 112                           | 96,047.38            | 99,712.68        | 1 - 131                    |
| 13                                                                                                                                | SHIPPING AND PORTS          | 6               | 8,413.09             | 8,426.32         | 0.16             | 2                             | 1,269.46             | 1,269.46         | 96 - 155                   |
| 14                                                                                                                                | TELECOMMUNICATIONS          | 6               | 16,477.01            | 27,707.01        | 68.16            | 1                             | 13,334.00            | 24,664.00        | 58 - 58                    |
| 15                                                                                                                                | URBAN DEVELOPMENT           | 58              | 1,61,098.60          | 1,66,153.31      | 3.14             | 19                            | 61,197.50            | 61,564.39        | 2 - 77                     |
| 16                                                                                                                                | DEFENCE PRODUCTION          | 2               | 454.00               | 461.66           | 1.69             | 0                             | 0.00                 | 0.00             | -                          |
| Total                                                                                                                             |                             | 1424            | 19,66,356.93         | 21,33,649.81     | 8.51             | 326                           | 5,06,637.61          | 6,04,354.05      |                            |

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

**TABLE-9**

| Extent of cost overrun in projects with respect to latest schedule RS. 150 Crore and above<br>(All Cost/ Expenditure in Rs. crore) |                             |                 |                      |                  |                  |                              |                      |                  |                  |
|------------------------------------------------------------------------------------------------------------------------------------|-----------------------------|-----------------|----------------------|------------------|------------------|------------------------------|----------------------|------------------|------------------|
|                                                                                                                                    |                             |                 |                      |                  |                  | Projects with cost overruns^ |                      |                  |                  |
| Sl.No.                                                                                                                             | Sector                      | No. of projects | Latest Approved Cost | Anticipated Cost | Cost overrun (%) | No.                          | Latest Approved Cost | Anticipated Cost | Cost overrun (%) |
| 1                                                                                                                                  | ATOMIC ENERGY               | 4               | 72,241.00            | 74,849.00        | 3.61             | 1                            | 3,492.00             | 6,100.00         | 74.69            |
| 2                                                                                                                                  | CIVIL AVIATION              | 1               | 314.61               | 441.33           | 40.28            | 1                            | 314.61               | 441.33           | 40.28            |
| 3                                                                                                                                  | COAL                        | 97              | 96,507.73            | 96,426.38        | -0.08            | 7                            | 18,876.68            | 19,914.04        | 5.50             |
| 4                                                                                                                                  | FERTILISERS                 | 6               | 1,793.57             | 1,793.57         | 0.00             | 0                            | 0.00                 | 0.00             | 0.00             |
| 5                                                                                                                                  | MINES                       | 5               | 7,078.62             | 7,078.62         | 0.00             | 0                            | 0.00                 | 0.00             | 0.00             |
| 6                                                                                                                                  | STEEL                       | 13              | 32,529.65            | 32,317.05        | -0.65            | 1                            | 343.00               | 488.40           | 42.39            |
| 7                                                                                                                                  | PETROLEUM                   | 137             | 2,25,033.26          | 2,23,009.33      | -0.90            | 7                            | 6,531.66             | 7,870.53         | 20.50            |
| 8                                                                                                                                  | POWER                       | 95              | 3,71,673.80          | 3,59,705.13      | -3.22            | 22                           | 1,35,123.57          | 1,77,622.72      | 31.45            |
| 9                                                                                                                                  | HEAVY INDUSTRY              | 2               | 5,281.30             | 5,381.30         | 1.89             | 1                            | 3,727.30             | 3,827.30         | 2.68             |
| 10                                                                                                                                 | HEALTH AND FAMILY WELFARE   | 20              | 8,129.23             | 8,246.52         | 1.44             | 3                            | 1,076.25             | 1,193.54         | 10.90            |
| 11                                                                                                                                 | RAILWAYS                    | 367             | 5,47,601.88          | 6,96,269.31      | 27.15            | 193                          | 1,36,561.60          | 2,97,140.92      | 117.59           |
| 12                                                                                                                                 | ROAD TRANSPORT AND HIGHWAYS | 605             | 4,11,729.58          | 4,25,383.97      | 3.32             | 39                           | 27,295.62            | 41,914.00        | 53.56            |
| 13                                                                                                                                 | SHIPPING AND PORTS          | 6               | 8,413.09             | 8,426.32         | 0.16             | 1                            | 258.33               | 271.56           | 5.12             |
| 14                                                                                                                                 | TELECOMMUNICATIONS          | 6               | 16,477.01            | 27,707.01        | 68.16            | 1                            | 13,334.00            | 24,664.00        | 84.97            |
| 15                                                                                                                                 | URBAN DEVELOPMENT           | 58              | 1,61,098.60          | 1,66,153.31      | 3.14             | 7                            | 22,155.90            | 27,219.50        | 22.85            |
| 16                                                                                                                                 | DEFENCE PRODUCTION          | 2               | 454.00               | 461.66           | 1.69             | 2                            | 454.00               | 461.66           | 1.69             |
| Total                                                                                                                              |                             | 1424            | 19,66,356.93         | 21,33,649.81     | 8.51             | 286                          | 3,69,544.52          | 6,09,129.50      | 64.83            |

^ - Cost Overrun = Anticipated Cost minus Original Cost

**TABLE-10**

| Extent of time & cost overrun in projects with respect to latest schedule Rs.150 Crore and above<br>(All Cost/ Expenditure in Rs. crore) |                             |                 |                      |                  |                  |                                       |                      |                  |                            |
|------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------|-----------------|----------------------|------------------|------------------|---------------------------------------|----------------------|------------------|----------------------------|
|                                                                                                                                          |                             |                 |                      |                  |                  | Projects with time\$ & cost overruns^ |                      |                  |                            |
| Sl.No.                                                                                                                                   | Sector                      | No. of projects | Latest Approved Cost | Anticipated Cost | Cost Overrun (%) | No.                                   | Latest Approved Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1                                                                                                                                        | ATOMIC ENERGY               | 4               | 72,241.00            | 74,849.00        | 3.61             | 1                                     | 3,492.00             | 6,100.00         | 102- 102                   |
| 2                                                                                                                                        | CIVIL AVIATION              | 1               | 314.61               | 441.33           | 40.28            | 1                                     | 314.61               | 441.33           | 21- 21                     |
| 3                                                                                                                                        | COAL                        | 97              | 96,507.73            | 96,426.38        | -0.08            | 4                                     | 983.19               | 1,747.25         | 60- 144                    |
| 4                                                                                                                                        | FERTILISERS                 | 6               | 1,793.57             | 1,793.57         | 0.00             | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| 5                                                                                                                                        | MINES                       | 5               | 7,078.62             | 7,078.62         | 0.00             | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| 6                                                                                                                                        | STEEL                       | 13              | 32,529.65            | 32,317.05        | -0.65            | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| 7                                                                                                                                        | PETROLEUM                   | 137             | 2,25,033.26          | 2,23,009.33      | -0.90            | 1                                     | 607.06               | 714.25           | 17- 17                     |
| 8                                                                                                                                        | POWER                       | 95              | 3,71,673.80          | 3,59,705.13      | -3.22            | 8                                     | 38,010.06            | 56,028.24        | 12- 147                    |
| 9                                                                                                                                        | HEAVY INDUSTRY              | 2               | 5,281.30             | 5,381.30         | 1.89             | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| 10                                                                                                                                       | HEALTH AND FAMILY WELFARE   | 20              | 8,129.23             | 8,246.52         | 1.44             | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| 11                                                                                                                                       | RAILWAYS                    | 367             | 5,47,601.88          | 6,96,269.31      | 27.15            | 45                                    | 47,596.48            | 1,12,726.10      | 1- 239                     |
| 12                                                                                                                                       | ROAD TRANSPORT AND HIGHWAYS | 605             | 4,11,729.58          | 4,25,383.97      | 3.32             | 17                                    | 13,477.20            | 17,143.52        | 1- 131                     |
| 13                                                                                                                                       | SHIPPING AND PORTS          | 6               | 8,413.09             | 8,426.32         | 0.16             | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| 14                                                                                                                                       | TELECOMMUNICATIONS          | 6               | 16,477.01            | 27,707.01        | 68.16            | 1                                     | 13,334.00            | 24,664.00        | 58- 58                     |
| 15                                                                                                                                       | URBAN DEVELOPMENT           | 58              | 1,61,098.60          | 1,66,153.31      | 3.14             | 2                                     | 1,715.21             | 2,090.99         | 5- 36                      |
| 16                                                                                                                                       | DEFENCE PRODUCTION          | 2               | 454.00               | 461.66           | 1.69             | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| Total                                                                                                                                    |                             | 1424            | 19,66,356.93         | 21,33,649.81     | 8.51             | 80                                    | 1,19,529.81          | 2,21,655.68      |                            |

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

**TABLE-11**

| Extent of time & cost overrun in projects with respect to original schedule Rs.150 Crore and above<br>(All Cost/ Expenditure in Rs. crore ) |                             |                 |               |                  |                  |                                       |               |                  |                            |
|---------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------|-----------------|---------------|------------------|------------------|---------------------------------------|---------------|------------------|----------------------------|
|                                                                                                                                             |                             |                 |               |                  |                  | Projects with time\$ & cost overruns^ |               |                  |                            |
| Sl.No.                                                                                                                                      | Sector                      | No. of projects | Original Cost | Anticipated Cost | Cost Overrun (%) | No.                                   | Original Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1                                                                                                                                           | ATOMIC ENERGY               | 4               | 67,120.00     | 74,849.00        | 11.52            | 2                                     | 14,951.00     | 22,680.00        | 54- 102                    |
| 2                                                                                                                                           | CIVIL AVIATION              | 1               | 314.61        | 441.33           | 40.28            | 1                                     | 314.61        | 441.33           | 21- 21                     |
| 3                                                                                                                                           | COAL                        | 97              | 96,954.88     | 96,426.38        | -0.55            | 6                                     | 1,549.74      | 2,394.02         | 12- 144                    |
| 4                                                                                                                                           | FERTILISERS                 | 6               | 1,781.92      | 1,793.57         | 0.65             | 1                                     | 197.79        | 209.44           | 29- 29                     |
| 5                                                                                                                                           | MINES                       | 5               | 7,078.62      | 7,078.62         | 0.00             | 0                                     | 0.00          | 0.00             | 0- 0                       |
| 6                                                                                                                                           | STEEL                       | 13              | 32,529.65     | 32,317.05        | -0.65            | 0                                     | 0.00          | 0.00             | 0- 0                       |
| 7                                                                                                                                           | PETROLEUM                   | 137             | 2,21,562.48   | 2,23,009.33      | 0.65             | 9                                     | 15,248.77     | 19,132.79        | 13- 70                     |
| 8                                                                                                                                           | POWER                       | 95              | 2,96,370.25   | 3,59,705.13      | 21.37            | 30                                    | 1,28,289.04   | 1,72,137.31      | 10- 147                    |
| 9                                                                                                                                           | HEAVY INDUSTRY              | 2               | 3,272.00      | 5,381.30         | 64.47            | 1                                     | 1,718.00      | 3,827.30         | 93- 93                     |
| 10                                                                                                                                          | HEALTH AND FAMILY WELFARE   | 20              | 8,129.23      | 8,246.52         | 1.44             | 1                                     | 414.11        | 513.89           | 83- 83                     |
| 11                                                                                                                                          | RAILWAYS                    | 367             | 4,85,710.46   | 6,96,269.31      | 43.35            | 56                                    | 57,564.52     | 1,35,364.56      | 1- 324                     |
| 12                                                                                                                                          | ROAD TRANSPORT AND HIGHWAYS | 605             | 4,11,159.45   | 4,25,383.97      | 3.46             | 18                                    | 13,616.13     | 17,298.52        | 1- 131                     |
| 13                                                                                                                                          | SHIPPING AND PORTS          | 6               | 7,988.29      | 8,426.32         | 5.48             | 2                                     | 516.39        | 1,269.46         | 96- 155                    |
| 14                                                                                                                                          | TELECOMMUNICATIONS          | 6               | 16,478.21     | 27,707.01        | 68.14            | 1                                     | 13,334.00     | 24,664.00        | 58- 58                     |
| 15                                                                                                                                          | URBAN DEVELOPMENT           | 58              | 1,60,566.07   | 1,66,153.31      | 3.48             | 3                                     | 1,829.65      | 2,356.99         | 5- 70                      |
| 16                                                                                                                                          | DEFENCE PRODUCTION          | 2               | 453.64        | 461.66           | 1.77             | 1                                     | 167.69        | 170.37           | 8- 8                       |
|                                                                                                                                             |                             |                 |               |                  |                  |                                       |               |                  |                            |
| Total                                                                                                                                       |                             | 1424            | 18,17,469.76  | 21,33,649.81     | 17.40            | 132                                   | 2,49,711.44   | 4,02,459.98      |                            |

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

**TABLE-12**


| State-Wise Position of Central Sector Projects costing Rs. 150 Crore and above showing Both Time and Cost Overruns<br>(All Cost/ Expenditure in Rs. crore) |                   |                 |               |                  |                  |                               |               |                  |                            |
|------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------|-----------------|---------------|------------------|------------------|-------------------------------|---------------|------------------|----------------------------|
|                                                                                                                                                            |                   |                 |               |                  |                  | Projects with time overruns\$ |               |                  |                            |
| Sl.No                                                                                                                                                      | State             | No. of Projects | Original Cost | Anticipated cost | Cost overrun (%) | No.                           | Original Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1                                                                                                                                                          | ANDHRA PRADESH    | 69              | 1,07,461.29   | 1,11,065.37      | 3.35             | 4                             | 3,054.13      | 5,392.26         | 2 - 168                    |
| 2                                                                                                                                                          | ARUNACHAL PRADESH | 31              | 16,421.02     | 33,547.53        | 104.30           | 2                             | 2,635.83      | 6,334.96         | 36 - 111                   |
| 3                                                                                                                                                          | ASSAM             | 45              | 27,704.18     | 33,843.20        | 22.16            | 8                             | 6,028.91      | 11,517.30        | 12 - 131                   |
| 4                                                                                                                                                          | BIHAR             | 91              | 76,252.26     | 1,11,749.59      | 46.55            | 11                            | 31,379.06     | 47,928.04        | 12 - 123                   |
| 5                                                                                                                                                          | GOA               | 10              | 4,292.52      | 4,300.54         | 0.19             | 1                             | 167.69        | 170.37           | 8 - 8                      |
| 6                                                                                                                                                          | GUJARAT           | 49              | 51,576.03     | 57,377.20        | 11.25            | 3                             | 12,097.90     | 17,760.58        | 36 - 84                    |
| 7                                                                                                                                                          | HARYANA           | 29              | 21,083.41     | 22,987.06        | 9.03             | 1                             | 1,108.00      | 2,288.00         | 91 - 91                    |
| 8                                                                                                                                                          | HIMACHAL PRADESH  | 13              | 17,058.17     | 26,566.39        | 55.74            | 1                             | 3,919.59      | 9,394.80         | 147 - 147                  |
| 9                                                                                                                                                          | JAMMU AND KASHMIR | 10              | 25,238.37     | 51,232.67        | 103.00           | 1                             | 2,500.00      | 27,949.00        | 220 - 220                  |
| 10                                                                                                                                                         | KARNATAKA         | 46              | 82,156.70     | 87,206.53        | 6.15             | 3                             | 2,469.52      | 3,500.52         | 3 - 36                     |
| 11                                                                                                                                                         | KERALA            | 22              | 25,879.48     | 28,054.10        | 8.40             | 2                             | 5,195.35      | 5,960.21         | 15 - 17                    |
| 12                                                                                                                                                         | MADHYA PRADESH    | 60              | 67,550.02     | 72,708.48        | 7.64             | 3                             | 13,250.09     | 15,810.15        | 21 - 96                    |
| 13                                                                                                                                                         | MAHARASHTRA       | 129             | 1,85,696.80   | 1,97,861.32      | 6.55             | 14                            | 17,692.54     | 23,862.59        | 2 - 192                    |
| 14                                                                                                                                                         | MANIPUR           | 2               | 4,670.86      | 14,025.69        | 200.28           | 1                             | 4,454.17      | 13,809.00        | 108 - 108                  |
| 15                                                                                                                                                         | MEGHALAYA         | 7               | 4,484.97      | 9,578.51         | 113.57           | 0                             | 0.00          | 0.00             | -                          |
| 16                                                                                                                                                         | MIZORAM           | 4               | 3,406.61      | 5,981.14         | 75.57            | 1                             | 2,393.47      | 4,968.00         | 81 - 81                    |
| 17                                                                                                                                                         | NAGALAND          | 21              | 13,711.07     | 14,384.55        | 4.91             | 1                             | 2,326.52      | 3,000.00         | 79 - 79                    |
| 18                                                                                                                                                         | ODISHA            | 84              | 96,187.70     | 1,01,748.66      | 5.78             | 9                             | 20,893.26     | 26,136.98        | 3 - 147                    |
| 19                                                                                                                                                         | PUNJAB            | 33              | 17,042.04     | 17,047.77        | 0.03             | 1                             | 754.54        | 756.27           | 1 - 1                      |
| 20                                                                                                                                                         | RAJASTHAN         | 56              | 46,045.92     | 48,245.10        | 4.78             | 3                             | 1,725.02      | 2,681.00         | 1 - 63                     |
| 21                                                                                                                                                         | SIKKIM            | 9               | 3,476.73      | 6,281.03         | 80.66            | 1                             | 1,339.48      | 4,084.69         | 51 - 51                    |
| 22                                                                                                                                                         | TAMIL NADU        | 76              | 1,19,890.58   | 1,37,033.24      | 14.30            | 5                             | 6,104.29      | 9,853.00         | 69 - 155                   |
| 23                                                                                                                                                         | TRIPURA           | 9               | 4,422.36      | 8,345.05         | 88.70            | 2                             | 1,711.63      | 4,057.00         | 31 - 60                    |
| 24                                                                                                                                                         | UTTAR PRADESH     | 110             | 1,34,449.08   | 1,35,916.30      | 1.09             | 6                             | 3,328.93      | 4,872.83         | 5 - 239                    |
| 25                                                                                                                                                         | WEST BENGAL       | 53              | 57,557.73     | 66,897.02        | 16.23            | 5                             | 10,651.12     | 14,170.34        | 12 - 324                   |
| 26                                                                                                                                                         | A & N ISLANDS     | 8               | 2,385.01      | 2,492.59         | 4.51             | 1                             | 314.61        | 441.33           | 21 - 21                    |
| 27                                                                                                                                                         | D & N HAVELI      | 1               | 6,086.08      | 5,842.31         | -4.01            | 0                             | 0.00          | 0.00             | -                          |
| 28                                                                                                                                                         | DELHI             | 22              | 55,263.55     | 62,738.78        | 13.53            | 2                             | 1,633.32      | 2,105.89         | 5 - 83                     |
| 29                                                                                                                                                         | CHHATISGARH       | 45              | 78,684.04     | 82,085.57        | 4.32             | 4                             | 13,013.75     | 14,949.31        | 24 - 117                   |
| 30                                                                                                                                                         | JHARKHAND         | 47              | 47,231.00     | 51,136.74        | 8.27             | 4                             | 15,950.68     | 17,193.22        | 20 - 48                    |
| 31                                                                                                                                                         | UTTARAKHAND       | 28              | 33,689.40     | 39,554.65        | 17.41            | 4                             | 7,241.32      | 12,619.50        | 63 - 102                   |
| 32                                                                                                                                                         | TELANGANA         | 42              | 34,502.53     | 38,040.07        | 10.25            | 5                             | 2,730.04      | 3,648.31         | 33 - 144                   |
| 33                                                                                                                                                         | MULTI STATE       | 163             | 3,45,912.25   | 4,47,775.06      | 29.45            | 23                            | 51,646.68     | 85,244.53        | 1 - 178                    |
|                                                                                                                                                            |                   |                 |               |                  |                  |                               |               |                  |                            |
| Total                                                                                                                                                      |                   | 1424            | 18,17,469.76  | 21,33,649.81     | 17.40            | 132                           | 2,49,711.44   | 4,02,459.98      |                            |

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

| EXECUTIVE SUMMARY COSTING Rs.1000 Crore and above |                             |                     |                               |
|---------------------------------------------------|-----------------------------|---------------------|-------------------------------|
| Sl.No.                                            | Sector                      | Projects on Monitor | Projects Additionally Delayed |
| 1                                                 | RAILWAYS                    | 163                 | 3                             |
| 2                                                 | ROAD TRANSPORT AND HIGHWAYS | 136                 | 2                             |
| 3                                                 | POWER                       | 50                  | 7                             |
| 4                                                 | PETROLEUM                   | 49                  | 4                             |
| 5                                                 | COAL                        | 15                  | 0                             |
| 6                                                 | URBAN DEVELOPMENT           | 13                  | 0                             |
| 7                                                 | STEEL                       | 7                   | 0                             |
| 8                                                 | ATOMIC ENERGY               | 4                   | 0                             |
| 9                                                 | HEAVY INDUSTRY              | 2                   | 0                             |
| 10                                                | SHIPPING AND PORTS          | 2                   | 0                             |
| 11                                                | TELECOMMUNICATIONS          | 2                   | 0                             |
| 12                                                | MINES                       | 1                   | 0                             |
|                                                   | Total                       | 444                 | 16                            |

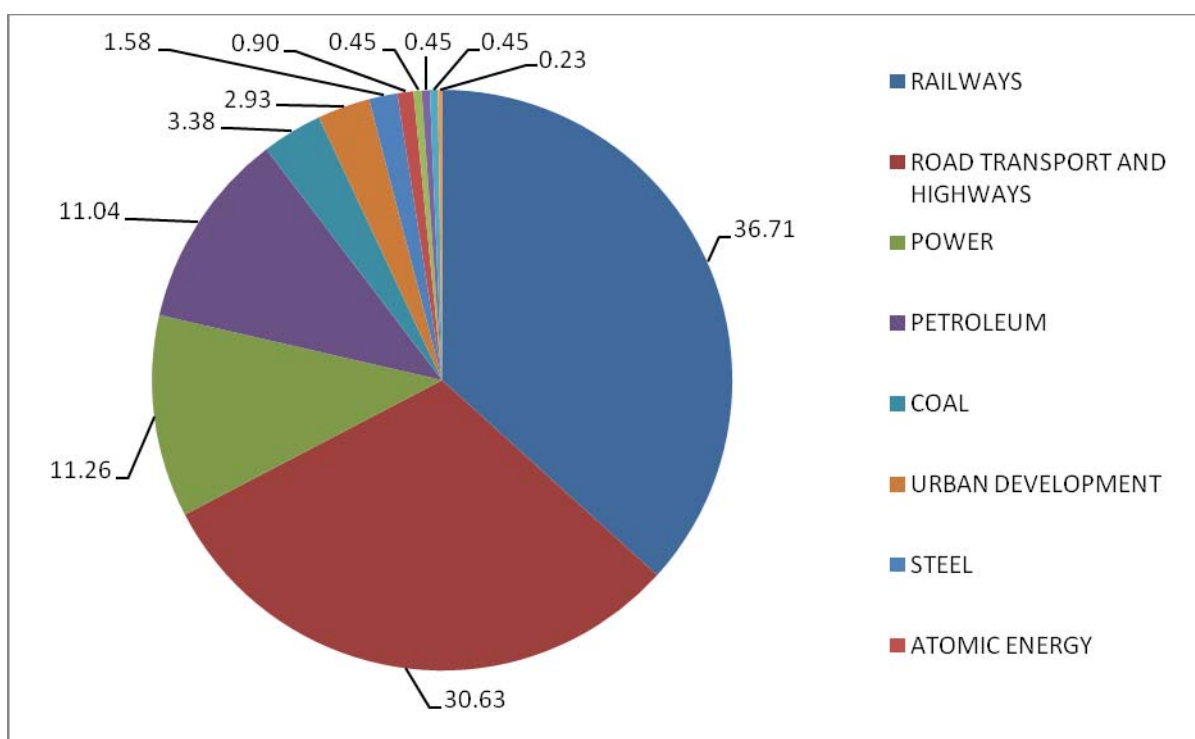



**TABLE-14**

**Projects Added / Completed / Dropped / Frozen Rs.1000 Crore and above**

|                                                          |     |
|----------------------------------------------------------|-----|
| No of Projects in Previous Month                         | 451 |
| No of Projects Completed/Dropped/Frozen in Current Month | 9   |
| No of Projects added in Current Month                    | 3   |
| No of Projects in Current Month                          | 444 |

| Project status Rs.1000 Crore and above |               |            |              |                               |               |       |
|----------------------------------------|---------------|------------|--------------|-------------------------------|---------------|-------|
| Number of Projects                     |               |            |              |                               |               |       |
| With Respect To                        | Delayed       | Ahead      | On schedule  | Without ODC but DOC available | Without D.O.C | Total |
| Original ( Date )                      | 161 ( 36.26%) | 7 ( 1.58%) | 120( 27.03%) | 29 ( 6.53%)                   | 127( 8.60%)   | 444   |
| Latest Approved ( Date)                | 129 ( 29.05%) | 7 ( 1.58%) | 156( 35.14%) | 25 ( 5.63%)                   | 127( 8.60%)   | 444   |

| Project cost Rs.1000 Crore and above  |                 |                 |                  |                  |                               |             |       |
|---------------------------------------|-----------------|-----------------|------------------|------------------|-------------------------------|-------------|-------|
| (All Cost/ Expenditure in Rs. crore ) |                 |                 |                  |                  |                               |             |       |
| Cost overrun                          |                 |                 |                  |                  |                               |             |       |
|                                       | No. of Projects | Sanctioned Cost | Anticipated Cost | Expenditure Cost | % cost w.r.t anticipated cost | Rs crore    | %     |
| Project with No Revision in Cost      | 367             | 11,45,862.18    | 13,35,536.45     | 4,87,925.33      | 36.50                         | 1,89,674.27 | 16.60 |
| Project with Revision in Cost         | 77              | 3,48,311.51     | 3,65,898.83      | 1,81,242.26      | 49.50                         | 17,587.32   | 5.00  |
| Total                                 | 444             | 14,94,173.69    | 17,01,435.28     | 6,69,167.59      | 39.33                         | 2,07,261.59 | 13.87 |
| Original Cost of All Projects         |                 |                 |                  |                  |                               |             |       |
| Original Cost                         | 444             | 14,01,239.42    | 17,01,435.28     | 6,69,167.59      | 39.33                         | 3,00,195.86 | 21.42 |

| Delayed Project cost Rs.1000 Crore and above |                 |                 |                  |                  |                               |             |       |
|----------------------------------------------|-----------------|-----------------|------------------|------------------|-------------------------------|-------------|-------|
| (All Cost/ Expenditure in Rs. crore )        |                 |                 |                  |                  |                               |             |       |
| Cost overrun                                 |                 |                 |                  |                  |                               |             |       |
| With Respect to                              | No. of Projects | Sanctioned Cost | Anticipated Cost | Expenditure Cost | % cost w.r.t anticipated cost | Rs crore    | %     |
| Original (OCE)                               | 161             | 6,42,742.09     | 7,86,012.23      | 4,24,915.28      | 54.10                         | 1,43,270.14 | 22.29 |
| Latest Approved (RCE)                        | 129             | 4,15,579.60     | 5,09,865.44      | 2,41,414.76      | 47.30                         | 94,285.84   | 22.69 |
|                                              |                 |                 |                  |                  |                               |             |       |

| Additional Delayed Project cost Rs.1000 Crore and above |                 |                 |                  |                  |                               |          |       |
|---------------------------------------------------------|-----------------|-----------------|------------------|------------------|-------------------------------|----------|-------|
| (All Cost/ Expenditure in Rs. crore )                   |                 |                 |                  |                  |                               |          |       |
| Cost overrun                                            |                 |                 |                  |                  |                               |          |       |
| With Respect to                                         | No. of Projects | Sanctioned Cost | Anticipated Cost | Expenditure Cost | % cost w.r.t anticipated cost | Rs crore | %     |
| Latest Approved                                         | 16              | 44,578.99       | 52,991.98        | 42,295.67        | 79.80                         | 8,412.99 | 18.90 |
| Total                                                   | 16              | 44,578.99       | 52,991.98        | 42,295.67        | 79.82                         | 8,412.99 | 18.87 |

**TABLE-15**

| Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs. 1000 Crore and above<br>(All Cost/ Expenditure in Rs. crore ) |                             |                 |               |                  |                  |                             |               |                  |                  |
|-----------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------|-----------------|---------------|------------------|------------------|-----------------------------|---------------|------------------|------------------|
|                                                                                                                                                     |                             |                 |               |                  |                  | Projects with cost overrun^ |               |                  |                  |
| Sl.No                                                                                                                                               | Sector                      | No. of Projects | Original Cost | Anticipated cost | Cost overrun (%) | No.                         | Original Cost | Anticipated Cost | Cost overrun (%) |
| 1                                                                                                                                                   | ATOMIC ENERGY               | 4               | 67,120.00     | 74,849.00        | 11.52            | 2                           | 14,951.00     | 22,680.00        | 51.70            |
| 2                                                                                                                                                   | COAL                        | 15              | 62,755.83     | 62,756.63        | 0.00             | 1                           | 17,237.00     | 17,237.80        | 0.00             |
| 3                                                                                                                                                   | MINES                       | 1               | 5,540.00      | 5,540.00         | 0.00             | 0                           | 0.00          | 0.00             | 0.00             |
| 4                                                                                                                                                   | STEEL                       | 7               | 30,130.34     | 29,772.34        | -1.19            | 0                           | 0.00          | 0.00             | 0.00             |
| 5                                                                                                                                                   | PETROLEUM                   | 49              | 1,83,363.73   | 1,85,991.56      | 1.43             | 8                           | 17,961.75     | 23,156.95        | 28.92            |
| 6                                                                                                                                                   | POWER                       | 50              | 2,79,164.95   | 3,41,349.00      | 22.28            | 29                          | 1,68,799.33   | 2,30,983.38      | 36.84            |
| 7                                                                                                                                                   | HEAVY INDUSTRY              | 2               | 3,272.00      | 5,381.30         | 64.47            | 1                           | 1,718.00      | 3,827.30         | 122.78           |
| 8                                                                                                                                                   | RAILWAYS                    | 163             | 3,99,835.50   | 5,95,855.43      | 49.03            | 97                          | 1,33,422.20   | 3,34,681.44      | 150.84           |
| 9                                                                                                                                                   | ROAD TRANSPORT AND HIGHWAYS | 136             | 2,00,332.48   | 2,13,634.95      | 6.64             | 17                          | 20,393.80     | 33,696.27        | 65.23            |
| 10                                                                                                                                                  | SHIPPING AND PORTS          | 2               | 6,627.40      | 6,627.40         | 0.00             | 0                           | 0.00          | 0.00             | 0.00             |
| 11                                                                                                                                                  | TELECOMMUNICATIONS          | 2               | 15,445.17     | 26,675.17        | 72.71            | 1                           | 13,334.00     | 24,664.00        | 84.97            |
| 12                                                                                                                                                  | URBAN DEVELOPMENT           | 13              | 1,47,652.02   | 1,53,002.50      | 3.62             | 4                           | 20,852.09     | 26,202.57        | 25.66            |
| Total                                                                                                                                               |                             | 444             | 14,01,239.42  | 17,01,435.28     | 21.42            | 160                         | 4,08,669.17   | 7,17,129.71      | 75.48            |

^ - Cost Overrun = Anticipated Cost minus Original Cost

**TABLE-16**

| Extent of cost overrun in projects with respect to original schedule(State Wise) Rs. 1000 Crore and above<br>(All Cost/ Expenditure in Rs. Crore) |                   |                 |               |                  |                  |                                         |               |                  |                  |
|---------------------------------------------------------------------------------------------------------------------------------------------------|-------------------|-----------------|---------------|------------------|------------------|-----------------------------------------|---------------|------------------|------------------|
|                                                                                                                                                   |                   |                 |               |                  |                  | Projects with cost overrun <sup>^</sup> |               |                  |                  |
| Sl.No                                                                                                                                             | State             | No. of Projects | Original Cost | Anticipated Cost | Cost overrun (%) | No.                                     | Original Cost | Anticipated Cost | Cost overrun (%) |
| 1                                                                                                                                                 | ANDHRA PRADESH    | 22              | 90,958.16     | 94,896.23        | 4.33             | 6                                       | 7,059.25      | 11,355.32        | 60.86            |
| 2                                                                                                                                                 | ARUNACHAL PRADESH | 3               | 10,035.33     | 26,929.40        | 168.35           | 2                                       | 8,782.23      | 25,676.30        | 192.37           |
| 3                                                                                                                                                 | ASSAM             | 7               | 14,133.37     | 19,246.86        | 36.18            | 3                                       | 5,631.90      | 10,882.00        | 93.22            |
| 4                                                                                                                                                 | BIHAR             | 25              | 46,998.89     | 79,080.11        | 68.26            | 17                                      | 34,744.64     | 66,825.86        | 92.33            |
| 5                                                                                                                                                 | GUJARAT           | 14              | 33,092.23     | 39,942.00        | 20.70            | 2                                       | 12,968.10     | 19,817.87        | 52.82            |
| 6                                                                                                                                                 | HARYANA           | 6               | 10,890.69     | 12,070.69        | 10.83            | 1                                       | 1,108.00      | 2,288.00         | 106.50           |
| 7                                                                                                                                                 | HIMACHAL PRADESH  | 6               | 14,146.19     | 23,654.41        | 67.21            | 2                                       | 6,886.58      | 16,394.80        | 138.07           |
| 8                                                                                                                                                 | JAMMU AND KASHMIR | 10              | 25,238.37     | 51,232.67        | 103.00           | 2                                       | 4,288.41      | 30,282.71        | 606.15           |
| 9                                                                                                                                                 | KARNATAKA         | 20              | 68,819.94     | 73,410.38        | 6.67             | 6                                       | 18,932.46     | 23,702.90        | 25.20            |
| 10                                                                                                                                                | KERALA            | 8               | 19,741.86     | 21,625.11        | 9.54             | 2                                       | 6,154.29      | 8,061.58         | 30.99            |
| 11                                                                                                                                                | MADHYA PRADESH    | 19              | 44,612.91     | 50,527.82        | 13.26            | 9                                       | 26,272.05     | 34,660.36        | 31.93            |
| 12                                                                                                                                                | MAHARASHTRA       | 43              | 1,49,592.87   | 1,60,291.40      | 7.15             | 15                                      | 28,028.61     | 40,609.03        | 44.88            |
| 13                                                                                                                                                | MANIPUR           | 1               | 4,454.17      | 13,809.00        | 210.02           | 1                                       | 4,454.17      | 13,809.00        | 210.02           |
| 14                                                                                                                                                | MEGHALAYA         | 2               | 2,400.94      | 7,494.48         | 212.15           | 1                                       | 906.46        | 6,000.00         | 561.92           |
| 15                                                                                                                                                | MIZORAM           | 1               | 2,393.47      | 4,968.00         | 107.56           | 1                                       | 2,393.47      | 4,968.00         | 107.56           |
| 16                                                                                                                                                | NAGALAND          | 3               | 7,896.52      | 8,570.00         | 8.53             | 1                                       | 2,326.52      | 3,000.00         | 28.95            |
| 17                                                                                                                                                | ODISHA            | 29              | 71,914.25     | 76,515.33        | 6.40             | 7                                       | 20,821.88     | 25,422.96        | 22.10            |
| 18                                                                                                                                                | PUNJAB            | 2               | 2,557.95      | 2,557.95         | 0.00             | 0                                       | 0.00          | 0.00             | 0.00             |
| 19                                                                                                                                                | RAJASTHAN         | 13              | 25,544.64     | 26,900.58        | 5.31             | 4                                       | 3,178.64      | 4,534.58         | 42.66            |
| 20                                                                                                                                                | SIKKIM            | 1               | 1,339.48      | 4,084.69         | 204.95           | 1                                       | 1,339.48      | 4,084.69         | 204.95           |
| 21                                                                                                                                                | TAMIL NADU        | 27              | 99,477.88     | 1,14,389.14      | 14.99            | 11                                      | 25,501.52     | 40,412.78        | 58.47            |
| 22                                                                                                                                                | TRIPURA           | 3               | 2,458.01      | 6,218.51         | 152.99           | 3                                       | 2,458.01      | 6,218.51         | 152.99           |
| 23                                                                                                                                                | UTTAR PRADESH     | 41              | 1,00,801.99   | 1,02,948.61      | 2.13             | 5                                       | 21,465.64     | 24,384.21        | 13.60            |
| 24                                                                                                                                                | WEST BENGAL       | 24              | 46,282.76     | 53,304.29        | 15.17            | 8                                       | 13,999.31     | 21,035.27        | 50.26            |
| 25                                                                                                                                                | D & N HAVELI      | 1               | 6,086.08      | 5,842.31         | -4.01            | 0                                       | 0.00          | 0.00             | 0.00             |
| 26                                                                                                                                                | DELHI             | 7               | 50,481.91     | 57,816.75        | 14.53            | 3                                       | 6,254.39      | 13,589.23        | 117.28           |
| 27                                                                                                                                                | CHHATISGARH       | 14              | 64,313.38     | 68,809.25        | 6.99             | 5                                       | 16,797.78     | 21,293.65        | 26.76            |
| 28                                                                                                                                                | JHARKHAND         | 12              | 34,294.40     | 37,394.25        | 9.04             | 4                                       | 20,763.50     | 23,863.35        | 14.93            |
| 29                                                                                                                                                | UTTARAKHAND       | 6               | 26,313.06     | 31,813.57        | 20.90            | 4                                       | 8,654.06      | 14,154.57        | 63.56            |
| 30                                                                                                                                                | TELANGANA         | 7               | 20,115.45     | 23,093.25        | 14.80            | 3                                       | 2,503.03      | 5,480.84         | 118.97           |
| 31                                                                                                                                                | MULTI STATE       | 67              | 3,03,852.27   | 4,01,998.24      | 32.30            | 31                                      | 93,994.79     | 1,94,321.34      | 106.74           |
|                                                                                                                                                   |                   |                 |               |                  |                  |                                         |               |                  |                  |
| Total                                                                                                                                             |                   | 444             | 14,01,239.42  | 17,01,435.28     | 21.42            | 160                                     | 4,08,669.17   | 7,17,129.71      | 75.48            |

<sup>^</sup> - Cost Overrun = Anticipated Cost minus Original Cost

**TABLE-17**

| Extent of time overrun in projects with respect to original schedule Rs.1000 Crore and above<br>(All Cost/ Expenditure in Rs. crore) |                             |                 |               |                  |                  |                               |               |                  |                            |
|--------------------------------------------------------------------------------------------------------------------------------------|-----------------------------|-----------------|---------------|------------------|------------------|-------------------------------|---------------|------------------|----------------------------|
|                                                                                                                                      |                             |                 |               |                  |                  | Projects with time overruns\$ |               |                  |                            |
| Sl.No                                                                                                                                | Sector                      | No. of Projects | Original Cost | Anticipated Cost | Cost overrun (%) | No.                           | Original Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1                                                                                                                                    | ATOMIC ENERGY               | 4               | 67,120.00     | 74,849.00        | 11.52            | 4                             | 67,120.00     | 74,849.00        | 36 - 102                   |
| 2                                                                                                                                    | COAL                        | 15              | 62,755.83     | 62,756.63        | 0.00             | 4                             | 9,323.71      | 9,323.71         | 12 - 48                    |
| 3                                                                                                                                    | MINES                       | 1               | 5,540.00      | 5,540.00         | 0.00             | 0                             | 0.00          | 0.00             | -                          |
| 4                                                                                                                                    | STEEL                       | 7               | 30,130.34     | 29,772.34        | -1.19            | 6                             | 25,381.34     | 25,023.34        | 6 - 49                     |
| 5                                                                                                                                    | PETROLEUM                   | 49              | 1,83,363.73   | 1,85,991.56      | 1.43             | 15                            | 81,610.45     | 83,845.90        | 3 - 78                     |
| 6                                                                                                                                    | POWER                       | 50              | 2,79,164.95   | 3,41,349.00      | 22.28            | 30                            | 1,85,156.78   | 2,27,854.39      | 2 - 147                    |
| 7                                                                                                                                    | HEAVY INDUSTRY              | 2               | 3,272.00      | 5,381.30         | 64.47            | 1                             | 1,718.00      | 3,827.30         | 93 - 93                    |
| 8                                                                                                                                    | RAILWAYS                    | 163             | 3,99,835.50   | 5,95,855.43      | 49.03            | 57                            | 1,02,256.43   | 1,76,185.36      | 3 - 324                    |
| 9                                                                                                                                    | ROAD TRANSPORT AND HIGHWAYS | 136             | 2,00,332.48   | 2,13,634.95      | 6.64             | 37                            | 53,634.24     | 56,859.30        | 2 - 91                     |
| 10                                                                                                                                   | SHIPPING AND PORTS          | 2               | 6,627.40      | 6,627.40         | 0.00             | 0                             | 0.00          | 0.00             | -                          |
| 11                                                                                                                                   | TELECOMMUNICATIONS          | 2               | 15,445.17     | 26,675.17        | 72.71            | 1                             | 13,334.00     | 24,664.00        | 58 - 58                    |
| 12                                                                                                                                   | URBAN DEVELOPMENT           | 13              | 1,47,652.02   | 1,53,002.50      | 3.62             | 6                             | 1,03,207.14   | 1,03,579.93      | 5 - 64                     |
|                                                                                                                                      |                             |                 |               |                  |                  |                               |               |                  |                            |
| Total                                                                                                                                |                             | 444             | 14,01,239.42  | 17,01,435.28     | 21.42            | 161                           | 6,42,742.09   | 7,86,012.23      |                            |

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

**TABLE-18**

| Extent of time overrun in projects with respect to original schedule(State Wise) Rs.1000 Crore and above<br>(All Cost/ Expenditure in Rs. crore) |                   |                 |               |                  |                  |                               |               |                  |                            |
|--------------------------------------------------------------------------------------------------------------------------------------------------|-------------------|-----------------|---------------|------------------|------------------|-------------------------------|---------------|------------------|----------------------------|
|                                                                                                                                                  |                   |                 |               |                  |                  | Projects with time overruns\$ |               |                  |                            |
| Sl.No                                                                                                                                            | State             | No. of Projects | Original Cost | Anticipated cost | Cost overrun (%) | No.                           | Original Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1                                                                                                                                                | ANDHRA PRADESH    | 22              | 90,958.16     | 94,896.23        | 4.33             | 9                             | 48,698.04     | 50,677.67        | 2 - 168                    |
| 2                                                                                                                                                | ARUNACHAL PRADESH | 3               | 10,035.33     | 26,929.40        | 168.35           | 1                             | 2,496.90      | 6,179.96         | 111 - 111                  |
| 3                                                                                                                                                | ASSAM             | 7               | 14,133.37     | 19,246.86        | 36.18            | 3                             | 7,225.70      | 12,060.86        | 12 - 88                    |
| 4                                                                                                                                                | BIHAR             | 25              | 46,998.89     | 79,080.11        | 68.26            | 10                            | 32,659.99     | 48,769.28        | 12 - 123                   |
| 5                                                                                                                                                | GUJARAT           | 14              | 33,092.23     | 39,942.00        | 20.70            | 2                             | 13,417.88     | 18,538.88        | 2 - 54                     |
| 6                                                                                                                                                | HARYANA           | 6               | 10,890.69     | 12,070.69        | 10.83            | 1                             | 1,108.00      | 2,288.00         | 91 - 91                    |
| 7                                                                                                                                                | HIMACHAL PRADESH  | 6               | 14,146.19     | 23,654.41        | 67.21            | 2                             | 5,836.38      | 11,311.59        | 29 - 147                   |
| 8                                                                                                                                                | JAMMU AND KASHMIR | 10              | 25,238.37     | 51,232.67        | 103.00           | 5                             | 16,904.75     | 42,353.75        | 10 - 220                   |
| 9                                                                                                                                                | KARNATAKA         | 20              | 68,819.94     | 73,410.38        | 6.67             | 8                             | 36,654.45     | 37,440.71        | 3 - 264                    |
| 10                                                                                                                                               | KERALA            | 8               | 19,741.86     | 21,625.11        | 9.54             | 4                             | 14,207.19     | 14,840.82        | 8 - 33                     |
| 11                                                                                                                                               | MADHYA PRADESH    | 19              | 44,612.91     | 50,527.82        | 13.26            | 5                             | 16,026.92     | 18,586.98        | 19 - 96                    |
| 12                                                                                                                                               | MAHARASHTRA       | 43              | 1,49,592.87   | 1,60,291.40      | 7.15             | 19                            | 71,883.89     | 77,398.21        | 2 - 192                    |
| 13                                                                                                                                               | MANIPUR           | 1               | 4,454.17      | 13,809.00        | 210.02           | 1                             | 4,454.17      | 13,809.00        | 108 - 108                  |
| 14                                                                                                                                               | MEGHALAYA         | 2               | 2,400.94      | 7,494.48         | 212.15           | 0                             | 0.00          | 0.00             | -                          |
| 15                                                                                                                                               | MIZORAM           | 1               | 2,393.47      | 4,968.00         | 107.56           | 1                             | 2,393.47      | 4,968.00         | 81 - 81                    |
| 16                                                                                                                                               | NAGALAND          | 3               | 7,896.52      | 8,570.00         | 8.53             | 1                             | 2,326.52      | 3,000.00         | 79 - 79                    |
| 17                                                                                                                                               | ODISHA            | 29              | 71,914.25     | 76,515.33        | 6.40             | 11                            | 29,596.73     | 34,065.88        | 3 - 147                    |
| 18                                                                                                                                               | PUNJAB            | 2               | 2,557.95      | 2,557.95         | 0.00             | 0                             | 0.00          | 0.00             | -                          |
| 19                                                                                                                                               | RAJASTHAN         | 13              | 25,544.64     | 26,900.58        | 5.31             | 5                             | 16,906.01     | 17,755.08        | 2 - 89                     |
| 20                                                                                                                                               | SIKKIM            | 1               | 1,339.48      | 4,084.69         | 204.95           | 1                             | 1,339.48      | 4,084.69         | 51 - 51                    |
| 21                                                                                                                                               | TAMIL NADU        | 27              | 99,477.88     | 1,14,389.14      | 14.99            | 8                             | 59,728.51     | 62,744.54        | 18 - 124                   |
| 22                                                                                                                                               | TRIPURA           | 3               | 2,458.01      | 6,218.51         | 152.99           | 1                             | 1,142.00      | 3,407.00         | 60 - 60                    |
| 23                                                                                                                                               | UTTAR PRADESH     | 41              | 1,00,801.99   | 1,02,948.61      | 2.13             | 13                            | 35,489.37     | 36,664.49        | 2 - 239                    |
| 24                                                                                                                                               | WEST BENGAL       | 24              | 46,282.76     | 53,304.29        | 15.17            | 10                            | 19,262.22     | 22,464.75        | 11 - 324                   |
| 25                                                                                                                                               | D & N HAVELI      | 1               | 6,086.08      | 5,842.31         | -4.01            | 1                             | 6,086.08      | 5,842.31         | 5 - 5                      |
| 26                                                                                                                                               | DELHI             | 7               | 50,481.91     | 57,816.75        | 14.53            | 3                             | 41,198.73     | 41,571.52        | 5 - 38                     |
| 27                                                                                                                                               | CHHATISGARH       | 14              | 64,313.38     | 68,809.25        | 6.99             | 3                             | 28,002.78     | 29,459.82        | 24 - 111                   |
| 28                                                                                                                                               | JHARKHAND         | 12              | 34,294.40     | 37,394.25        | 9.04             | 6                             | 20,635.13     | 21,433.07        | 9 - 48                     |
| 29                                                                                                                                               | UTTARAKHAND       | 6               | 26,313.06     | 31,813.57        | 20.90            | 4                             | 23,343.06     | 28,569.50        | 15 - 102                   |
| 30                                                                                                                                               | TELANGANA         | 7               | 20,115.45     | 23,093.25        | 14.80            | 4                             | 14,450.02     | 14,727.41        | 3 - 144                    |
| 31                                                                                                                                               | MULTI STATE       | 67              | 3,03,852.27   | 4,01,998.24      | 32.30            | 19                            | 69,267.72     | 1,00,998.46      | 3 - 178                    |
|                                                                                                                                                  |                   |                 |               |                  |                  |                               |               |                  |                            |
| Total                                                                                                                                            |                   | 444             | 14,01,239.42  | 17,01,435.28     | 21.42            | 161                           | 6,42,742.09   | 7,86,012.23      |                            |

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

**TABLE-19**

| Extent of time overrun in projects with respect to latest schedule Rs.1000 Crore and above<br>(All Cost/ Expenditure in Rs. crore) |                             |                 |                      |                  |                  |                               |                      |                  |                            |
|------------------------------------------------------------------------------------------------------------------------------------|-----------------------------|-----------------|----------------------|------------------|------------------|-------------------------------|----------------------|------------------|----------------------------|
|                                                                                                                                    |                             |                 |                      |                  |                  | Projects with time overruns\$ |                      |                  |                            |
| Sl.No                                                                                                                              | Sector                      | No. of Projects | Latest Approved Cost | Anticipated Cost | Cost overrun (%) | No.                           | Latest Approved Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1                                                                                                                                  | ATOMIC ENERGY               | 4               | 72,241.00            | 74,849.00        | 3.61             | 4                             | 72,241.00            | 74,849.00        | 36 - 102                   |
| 2                                                                                                                                  | COAL                        | 15              | 62,755.83            | 62,756.63        | 0.00             | 4                             | 9,323.71             | 9,323.71         | 12 - 48                    |
| 3                                                                                                                                  | MINES                       | 1               | 5,540.00             | 5,540.00         | 0.00             | 0                             | 0.00                 | 0.00             | -                          |
| 4                                                                                                                                  | STEEL                       | 7               | 30,130.34            | 29,772.34        | -1.19            | 5                             | 9,856.34             | 9,498.34         | 6 - 32                     |
| 5                                                                                                                                  | PETROLEUM                   | 49              | 1,86,924.97          | 1,85,991.56      | -0.50            | 4                             | 15,278.00            | 14,999.00        | 3 - 78                     |
| 6                                                                                                                                  | POWER                       | 50              | 2,99,015.61          | 3,41,349.00      | 14.16            | 17                            | 84,647.42            | 1,02,499.84      | 2 - 147                    |
| 7                                                                                                                                  | HEAVY INDUSTRY              | 2               | 5,281.30             | 5,381.30         | 1.89             | 0                             | 0.00                 | 0.00             | -                          |
| 8                                                                                                                                  | RAILWAYS                    | 163             | 4,61,925.48          | 5,95,855.43      | 28.99            | 53                            | 1,01,322.75          | 1,60,857.32      | -12 - 239                  |
| 9                                                                                                                                  | ROAD TRANSPORT AND HIGHWAYS | 136             | 2,00,332.48          | 2,13,634.95      | 6.64             | 37                            | 53,634.24            | 56,859.30        | 2 - 91                     |
| 10                                                                                                                                 | SHIPPING AND PORTS          | 2               | 6,627.40             | 6,627.40         | 0.00             | 0                             | 0.00                 | 0.00             | -                          |
| 11                                                                                                                                 | TELECOMMUNICATIONS          | 2               | 15,445.17            | 26,675.17        | 72.71            | 1                             | 13,334.00            | 24,664.00        | 58 - 58                    |
| 12                                                                                                                                 | URBAN DEVELOPMENT           | 13              | 1,47,954.11          | 1,53,002.50      | 3.41             | 4                             | 55,942.14            | 56,314.93        | 5 - 64                     |
| Total                                                                                                                              |                             | 444             | 14,94,173.69         | 17,01,435.28     | 13.87            | 129                           | 4,15,579.60          | 5,09,865.44      |                            |

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

**TABLE-20**

| Extent of cost overrun in projects with respect to latest schedule RS. 1000 Crore and above<br>(All Cost/ Expenditure in Rs. crore) |                             |                 |                      |                  |                  |                              |                      |                  |                  |
|-------------------------------------------------------------------------------------------------------------------------------------|-----------------------------|-----------------|----------------------|------------------|------------------|------------------------------|----------------------|------------------|------------------|
|                                                                                                                                     |                             |                 |                      |                  |                  | Projects with cost overruns^ |                      |                  |                  |
| Sl.No.                                                                                                                              | Sector                      | No. of projects | Latest Approved Cost | Anticipated Cost | Cost overrun (%) | No.                          | Latest Approved Cost | Anticipated Cost | Cost overrun (%) |
| 1                                                                                                                                   | ATOMIC ENERGY               | 4               | 72,241.00            | 74,849.00        | 3.61             | 1                            | 3,492.00             | 6,100.00         | 74.69            |
| 2                                                                                                                                   | COAL                        | 15              | 62,755.83            | 62,756.63        | 0.00             | 1                            | 17,237.00            | 17,237.80        | 0.00             |
| 3                                                                                                                                   | MINES                       | 1               | 5,540.00             | 5,540.00         | 0.00             | 0                            | 0.00                 | 0.00             | 0.00             |
| 4                                                                                                                                   | STEEL                       | 7               | 30,130.34            | 29,772.34        | -1.19            | 0                            | 0.00                 | 0.00             | 0.00             |
| 5                                                                                                                                   | PETROLEUM                   | 49              | 1,86,924.97          | 1,85,991.56      | -0.50            | 3                            | 5,055.04             | 6,140.19         | 21.47            |
| 6                                                                                                                                   | POWER                       | 50              | 2,99,015.61          | 3,41,349.00      | 14.16            | 21                           | 1,34,686.89          | 1,77,020.28      | 31.43            |
| 7                                                                                                                                   | HEAVY INDUSTRY              | 2               | 5,281.30             | 5,381.30         | 1.89             | 1                            | 3,727.30             | 3,827.30         | 2.68             |
| 8                                                                                                                                   | RAILWAYS                    | 163             | 4,61,925.48          | 5,95,855.43      | 28.99            | 90                           | 1,03,608.91          | 2,44,571.29      | 136.05           |
| 9                                                                                                                                   | ROAD TRANSPORT AND HIGHWAYS | 136             | 2,00,332.48          | 2,13,634.95      | 6.64             | 17                           | 20,393.80            | 33,696.27        | 65.23            |
| 10                                                                                                                                  | SHIPPING AND PORTS          | 2               | 6,627.40             | 6,627.40         | 0.00             | 0                            | 0.00                 | 0.00             | 0.00             |
| 11                                                                                                                                  | TELECOMMUNICATIONS          | 2               | 15,445.17            | 26,675.17        | 72.71            | 1                            | 13,334.00            | 24,664.00        | 84.97            |
| 12                                                                                                                                  | URBAN DEVELOPMENT           | 13              | 1,47,954.11          | 1,53,002.50      | 3.41             | 4                            | 21,154.18            | 26,202.57        | 23.86            |
|                                                                                                                                     |                             |                 |                      |                  |                  |                              |                      |                  |                  |
| Total                                                                                                                               |                             | 444             | 14,94,173.69         | 17,01,435.28     | 13.87            | 139                          | 3,22,689.12          | 5,39,459.70      | 67.18            |

^ - Cost Overrun = Anticipated Cost minus Original Cost

**TABLE-21**

| Extent of time & cost overrun in projects with respect to latest schedule Rs. 1000 Crore and above<br>(All Cost/ Expenditure in Rs. crore) |                             |                 |                      |                  |                  |                                       |                      |                  |                            |
|--------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------|-----------------|----------------------|------------------|------------------|---------------------------------------|----------------------|------------------|----------------------------|
|                                                                                                                                            |                             |                 |                      |                  |                  | Projects with time\$ & cost overruns^ |                      |                  |                            |
| Sl.No.                                                                                                                                     | Sector                      | No. of projects | Latest Approved Cost | Anticipated Cost | Cost Overrun (%) | No.                                   | Latest Approved Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1                                                                                                                                          | ATOMIC ENERGY               | 4               | 72,241.00            | 74,849.00        | 3.61             | 1                                     | 3,492.00             | 6,100.00         | 102- 102                   |
| 2                                                                                                                                          | COAL                        | 15              | 62,755.83            | 62,756.63        | 0.00             | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| 3                                                                                                                                          | MINES                       | 1               | 5,540.00             | 5,540.00         | 0.00             | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| 4                                                                                                                                          | STEEL                       | 7               | 30,130.34            | 29,772.34        | -1.19            | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| 5                                                                                                                                          | PETROLEUM                   | 49              | 1,86,924.97          | 1,85,991.56      | -0.50            | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| 6                                                                                                                                          | POWER                       | 50              | 2,99,015.61          | 3,41,349.00      | 14.16            | 7                                     | 37,573.38            | 55,425.80        | 12- 147                    |
| 7                                                                                                                                          | HEAVY INDUSTRY              | 2               | 5,281.30             | 5,381.30         | 1.89             | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| 8                                                                                                                                          | RAILWAYS                    | 163             | 4,61,925.48          | 5,95,855.43      | 28.99            | 27                                    | 41,541.67            | 1,03,523.77      | 3- 239                     |
| 9                                                                                                                                          | ROAD TRANSPORT AND HIGHWAYS | 136             | 2,00,332.48          | 2,13,634.95      | 6.64             | 11                                    | 11,657.24            | 14,882.30        | 2- 91                      |
| 10                                                                                                                                         | SHIPPING AND PORTS          | 2               | 6,627.40             | 6,627.40         | 0.00             | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| 11                                                                                                                                         | TELECOMMUNICATIONS          | 2               | 15,445.17            | 26,675.17        | 72.71            | 1                                     | 13,334.00            | 24,664.00        | 58- 58                     |
| 12                                                                                                                                         | URBAN DEVELOPMENT           | 13              | 1,47,954.11          | 1,53,002.50      | 3.41             | 1                                     | 1,219.21             | 1,592.00         | 5- 5                       |
| Total                                                                                                                                      |                             | 444             | 14,94,173.69         | 17,01,435.28     | 13.87            | 48                                    | 1,08,817.50          | 2,06,187.87      |                            |

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning



**TABLE-22**

| Extent of time & cost overrun in projects with respect to original schedule Rs. 1000 Crore and above<br>(All Cost/ Expenditure in Rs. crore ) |                             |                 |               |                  |                  |                                       |               |                  |                            |
|-----------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------|-----------------|---------------|------------------|------------------|---------------------------------------|---------------|------------------|----------------------------|
|                                                                                                                                               |                             |                 |               |                  |                  | Projects with time\$ & cost overruns^ |               |                  |                            |
| Sl.No.                                                                                                                                        | Sector                      | No. of projects | Original Cost | Anticipated Cost | Cost Overrun (%) | No.                                   | Original Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1                                                                                                                                             | ATOMIC ENERGY               | 4               | 67,120.00     | 74,849.00        | 11.52            | 2                                     | 14,951.00     | 22,680.00        | 54- 102                    |
| 2                                                                                                                                             | COAL                        | 15              | 62,755.83     | 62,756.63        | 0.00             | 0                                     | 0.00          | 0.00             | 0- 0                       |
| 3                                                                                                                                             | MINES                       | 1               | 5,540.00      | 5,540.00         | 0.00             | 0                                     | 0.00          | 0.00             | 0- 0                       |
| 4                                                                                                                                             | STEEL                       | 7               | 30,130.34     | 29,772.34        | -1.19            | 0                                     | 0.00          | 0.00             | 0- 0                       |
| 5                                                                                                                                             | PETROLEUM                   | 49              | 1,83,363.73   | 1,85,991.56      | 1.43             | 5                                     | 13,776.40     | 16,925.95        | 13- 70                     |
| 6                                                                                                                                             | POWER                       | 50              | 2,79,164.95   | 3,41,349.00      | 22.28            | 20                                    | 1,25,047.91   | 1,67,745.52      | 10- 147                    |
| 7                                                                                                                                             | HEAVY INDUSTRY              | 2               | 3,272.00      | 5,381.30         | 64.47            | 1                                     | 1,718.00      | 3,827.30         | 93- 93                     |
| 8                                                                                                                                             | RAILWAYS                    | 163             | 3,99,835.50   | 5,95,855.43      | 49.03            | 35                                    | 49,307.78     | 1,23,385.74      | 3- 324                     |
| 9                                                                                                                                             | ROAD TRANSPORT AND HIGHWAYS | 136             | 2,00,332.48   | 2,13,634.95      | 6.64             | 11                                    | 11,657.24     | 14,882.30        | 2- 91                      |
| 10                                                                                                                                            | SHIPPING AND PORTS          | 2               | 6,627.40      | 6,627.40         | 0.00             | 0                                     | 0.00          | 0.00             | 0- 0                       |
| 11                                                                                                                                            | TELECOMMUNICATIONS          | 2               | 15,445.17     | 26,675.17        | 72.71            | 1                                     | 13,334.00     | 24,664.00        | 58- 58                     |
| 12                                                                                                                                            | URBAN DEVELOPMENT           | 13              | 1,47,652.02   | 1,53,002.50      | 3.62             | 1                                     | 1,219.21      | 1,592.00         | 5- 5                       |
| Total                                                                                                                                         |                             | 444             | 14,01,239.42  | 17,01,435.28     | 21.42            | 76                                    | 2,31,011.54   | 3,75,702.81      |                            |

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

**TABLE-23**

| State-Wise Position of Central Sector Projects costing Rs.1000 Crore and above showing Both Time and Cost Overruns<br>(All Cost/ Expenditure in Rs. crore) |                   |                 |               |                  |                  |                               |               |                  |                            |
|------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------|-----------------|---------------|------------------|------------------|-------------------------------|---------------|------------------|----------------------------|
|                                                                                                                                                            |                   |                 |               |                  |                  | Projects with time overruns\$ |               |                  |                            |
| Sl.No                                                                                                                                                      | State             | No. of Projects | Original Cost | Anticipated cost | Cost overrun (%) | No.                           | Original Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1                                                                                                                                                          | ANDHRA PRADESH    | 22              | 90,958.16     | 94,896.23        | 4.33             | 3                             | 2,819.63      | 5,157.26         | 2 - 168                    |
| 2                                                                                                                                                          | ARUNACHAL PRADESH | 3               | 10,035.33     | 26,929.40        | 168.35           | 1                             | 2,496.90      | 6,179.96         | 111 - 111                  |
| 3                                                                                                                                                          | ASSAM             | 7               | 14,133.37     | 19,246.86        | 36.18            | 2                             | 4,760.55      | 9,682.00         | 12 - 88                    |
| 4                                                                                                                                                          | BIHAR             | 25              | 46,998.89     | 79,080.11        | 68.26            | 8                             | 29,968.32     | 46,077.61        | 12 - 123                   |
| 5                                                                                                                                                          | GUJARAT           | 14              | 33,092.23     | 39,942.00        | 20.70            | 1                             | 11,459.00     | 16,580.00        | 54 - 54                    |
| 6                                                                                                                                                          | HARYANA           | 6               | 10,890.69     | 12,070.69        | 10.83            | 1                             | 1,108.00      | 2,288.00         | 91 - 91                    |
| 7                                                                                                                                                          | HIMACHAL PRADESH  | 6               | 14,146.19     | 23,654.41        | 67.21            | 1                             | 3,919.59      | 9,394.80         | 147 - 147                  |
| 8                                                                                                                                                          | JAMMU AND KASHMIR | 10              | 25,238.37     | 51,232.67        | 103.00           | 1                             | 2,500.00      | 27,949.00        | 220 - 220                  |
| 9                                                                                                                                                          | KARNATAKA         | 20              | 68,819.94     | 73,410.38        | 6.67             | 2                             | 1,824.74      | 2,611.00         | 3 - 3                      |
| 10                                                                                                                                                         | KERALA            | 8               | 19,741.86     | 21,625.11        | 9.54             | 1                             | 4,588.29      | 5,245.96         | 15 - 15                    |
| 11                                                                                                                                                         | MADHYA PRADESH    | 19              | 44,612.91     | 50,527.82        | 13.26            | 3                             | 13,250.09     | 15,810.15        | 21 - 96                    |
| 12                                                                                                                                                         | MAHARASHTRA       | 43              | 1,49,592.87   | 1,60,291.40      | 7.15             | 9                             | 16,084.12     | 21,598.44        | 2 - 192                    |
| 13                                                                                                                                                         | MANIPUR           | 1               | 4,454.17      | 13,809.00        | 210.02           | 1                             | 4,454.17      | 13,809.00        | 108 - 108                  |
| 14                                                                                                                                                         | MEGHALAYA         | 2               | 2,400.94      | 7,494.48         | 212.15           | 0                             | 0.00          | 0.00             | -                          |
| 15                                                                                                                                                         | MIZORAM           | 1               | 2,393.47      | 4,968.00         | 107.56           | 1                             | 2,393.47      | 4,968.00         | 81 - 81                    |
| 16                                                                                                                                                         | NAGALAND          | 3               | 7,896.52      | 8,570.00         | 8.53             | 1                             | 2,326.52      | 3,000.00         | 79 - 79                    |
| 17                                                                                                                                                         | ODISHA            | 29              | 71,914.25     | 76,515.33        | 6.40             | 6                             | 19,533.81     | 24,002.96        | 3 - 147                    |
| 18                                                                                                                                                         | PUNJAB            | 2               | 2,557.95      | 2,557.95         | 0.00             | 0                             | 0.00          | 0.00             | -                          |
| 19                                                                                                                                                         | RAJASTHAN         | 13              | 25,544.64     | 26,900.58        | 5.31             | 2                             | 1,482.93      | 2,332.00         | 60 - 63                    |
| 20                                                                                                                                                         | SIKKIM            | 1               | 1,339.48      | 4,084.69         | 204.95           | 1                             | 1,339.48      | 4,084.69         | 51 - 51                    |
| 21                                                                                                                                                         | TAMIL NADU        | 27              | 99,477.88     | 1,14,389.14      | 14.99            | 2                             | 5,271.29      | 8,287.32         | 102 - 124                  |
| 22                                                                                                                                                         | TRIPURA           | 3               | 2,458.01      | 6,218.51         | 152.99           | 1                             | 1,142.00      | 3,407.00         | 60 - 60                    |
| 23                                                                                                                                                         | UTTAR PRADESH     | 41              | 1,00,801.99   | 1,02,948.61      | 2.13             | 2                             | 1,793.75      | 3,117.88         | 5 - 239                    |
| 24                                                                                                                                                         | WEST BENGAL       | 24              | 46,282.76     | 53,304.29        | 15.17            | 4                             | 10,353.80     | 13,556.34        | 18 - 324                   |
| 25                                                                                                                                                         | D & N HAVELI      | 1               | 6,086.08      | 5,842.31         | -4.01            | 0                             | 0.00          | 0.00             | -                          |
| 26                                                                                                                                                         | DELHI             | 7               | 50,481.91     | 57,816.75        | 14.53            | 1                             | 1,219.21      | 1,592.00         | 5 - 5                      |
| 27                                                                                                                                                         | CHHATISGARH       | 14              | 64,313.38     | 68,809.25        | 6.99             | 2                             | 12,477.78     | 13,934.82        | 24 - 111                   |
| 28                                                                                                                                                         | JHARKHAND         | 12              | 34,294.40     | 37,394.25        | 9.04             | 2                             | 15,492.47     | 16,290.41        | 20 - 48                    |
| 29                                                                                                                                                         | UTTARAKHAND       | 6               | 26,313.06     | 31,813.57        | 20.90            | 3                             | 7,127.06      | 12,353.50        | 63 - 102                   |
| 30                                                                                                                                                         | TELANGANA         | 7               | 20,115.45     | 23,093.25        | 14.80            | 1                             | 1,266.60      | 1,544.00         | 33 - 33                    |
| 31                                                                                                                                                         | MULTI STATE       | 67              | 3,03,852.27   | 4,01,998.24      | 32.30            | 13                            | 48,557.97     | 80,848.71        | 12 - 178                   |
|                                                                                                                                                            |                   |                 |               |                  |                  |                               |               |                  |                            |
| Total                                                                                                                                                      |                   | 444             | 14,01,239.42  | 17,01,435.28     | 21.42            | 76                            | 2,31,011.54   | 3,75,702.81      |                            |

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

**TABLE-24**

| List of projects completed/dropped/Frozen during current month |                                                                                                             |         |          |         | Rs. 150 Crore and above<br>(All Cost/ Expenditure in Rs. crore) |         |                   |
|----------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------|---------|----------|---------|-----------------------------------------------------------------|---------|-------------------|
|                                                                |                                                                                                             |         | Original |         | Now anticipated                                                 |         |                   |
| Sl.No                                                          | Project                                                                                                     | DOA     | Cost     | DOC     | Cost                                                            | DOC     | Final Expenditure |
|                                                                | <u>COAL</u>                                                                                                 |         |          |         |                                                                 |         |                   |
| 1                                                              | RAJMAHAL OC EXP.                                                                                            | 09/2009 | 153.82   | 03/2014 | 153.82                                                          | N.A.    | 131.07            |
|                                                                | <u>HEALTH AND FAMILY WELFARE</u>                                                                            |         |          |         |                                                                 |         |                   |
| 2                                                              | NCI AIIMS JHAJJAR RESIDENTIAL HARYANA                                                                       | 07/2016 | 312.99   | 08/2018 | 322.00                                                          | 12/2018 | 318.00            |
|                                                                | <u>PETROLEUM</u>                                                                                            |         |          |         |                                                                 |         |                   |
| 3                                                              | PIPELINE REPLACEMENT PROJECT -4                                                                             | 02/2015 | 2,899.93 | 05/2017 | 2,504.61                                                        | 12/2018 | 2,183.66          |
| 4                                                              | ANKLESHWAR BARODA PIPELINE PROJECT                                                                          | 07/2014 | 199.95   | 03/2018 | 199.95                                                          | 12/2018 | 156.83            |
| 5                                                              | PARADIP HALDIA DURGAPUR LPG PIPELINE                                                                        | 02/2011 | 913.00   | 06/2018 | 1,330.00                                                        | 12/2018 | 1,323.53          |
|                                                                | <u>POWER</u>                                                                                                |         |          |         |                                                                 |         |                   |
| 6                                                              | TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.                                                | 02/2010 | 2,144.00 | 12/2012 | 2,932.88                                                        | N.A.    | 2,669.96          |
| 7                                                              | EASTERN REGION STRENGTHENING SCHEME-III                                                                     | 07/2010 | 1,272.80 | 11/2012 | 1,731.10                                                        | N.A.    | 1,473.05          |
| 8                                                              | INSTALLATION OF STATCOMS IN WESTERN REGION                                                                  | 03/2015 | 1,071.24 | 09/2017 | 1,071.24                                                        | 12/2018 | 649.26            |
| 9                                                              | GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C                                     | 07/2015 | 2,247.37 | 07/2018 | 2,247.37                                                        | 12/2018 | 1,531.89          |
| 10                                                             | EASTERN REGION STRENGTHENING SCHEME XIV                                                                     | 05/2016 | 167.01   | 11/2018 | 167.01                                                          | 12/2018 | 119.23            |
| 11                                                             | TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V Central Sector Projects                     | 02/2015 | 1,750.00 | 06/2018 | 1,750.00                                                        | 12/2018 | 1,335.04          |
| 12                                                             | TRANSMISSION SYSTEM ASSOCIATED WITH IPSPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A Central Sector Projects | 03/2015 | 955.00   | 12/2015 | 1,364.00                                                        | 12/2018 | 1,247.66          |
| 13                                                             | PROVISION OF SERIES REACTORS IN NORTHERN REGION                                                             | 08/2016 | 177.52   | 02/2019 | 177.52                                                          | 12/2018 | 87.48             |
| 14                                                             | S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B)                | 04/2016 | 287.99   | 06/2018 | 287.99                                                          | 12/2018 | 164.22            |
| 15                                                             | CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1)                         | 05/2015 | 780.33   | 10/2018 | 780.33                                                          | 11/2018 | 499.05            |
|                                                                |                                                                                                             |         |          |         |                                                                 |         |                   |

| <u>List of projects completed/dropped/Frozen during current month</u> |                                                                                                 |         |          |         | Rs. 150 Crore and above<br>(All Cost/ Expenditure in Rs. crore) |         |                   |
|-----------------------------------------------------------------------|-------------------------------------------------------------------------------------------------|---------|----------|---------|-----------------------------------------------------------------|---------|-------------------|
|                                                                       |                                                                                                 |         | Original |         | Now anticipated                                                 |         |                   |
| Sl.No                                                                 | Project                                                                                         | DOA     | Cost     | DOC     | Cost                                                            | DOC     | Final Expenditure |
|                                                                       | <u>RAILWAYS</u>                                                                                 |         |          |         |                                                                 |         |                   |
| 16                                                                    | BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR                                                    | 09/1997 | 3,230.02 | 04/2008 | 5,820.00                                                        | 06/2018 | 5,298.09          |
| 17                                                                    | BANKURA DAMODAR VALLEY RIVER 96 KM WITH MM FOR EXTENSION OF NEW LINE FROM BOWAICHANDI KHANA 24. | 04/1998 | 1,027.40 | 03/2022 | 195.00                                                          | 03/2022 | 195.00            |
| 18                                                                    | NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT                                                 | 04/2012 | 283.55   | 03/2019 | 451.00                                                          | 12/2018 | 480.81            |
| 19                                                                    | RANI-MARWAR JN. PATCH DOUBLING                                                                  | 04/2012 | 288.97   | 11/2018 | 346.35                                                          | 12/2018 | 315.60            |
|                                                                       |                                                                                                 |         |          |         |                                                                 |         |                   |
|                                                                       | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                              |         |          |         |                                                                 |         |                   |
| 20                                                                    | MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500                                              | 12/2003 | 200.00   | 04/2009 | 200.00                                                          | 12/2018 | 248.60            |
| 21                                                                    | JALANDHAR - AMRITSAR                                                                            | 01/2014 | 523.85   | 01/2016 | 523.85                                                          | 12/2018 | 170.68            |
|                                                                       |                                                                                                 |         |          |         |                                                                 |         |                   |
|                                                                       | <u>TELECOMMUNICATIONS</u>                                                                       |         |          |         |                                                                 |         |                   |
| 22                                                                    | MAHARASHTRA NODAL (LOT 1) Central Sector Projects                                               | 08/2017 | 159.30   | 04/2018 | 159.30                                                          | 12/2018 | 60.27             |
|                                                                       |                                                                                                 |         |          |         |                                                                 |         |                   |

**TABLE-25**

| List of projects added Rs.150 Crore and above |                                          |         |          |         | (December 2018) |         |
|-----------------------------------------------|------------------------------------------|---------|----------|---------|-----------------|---------|
|                                               |                                          |         | Original |         | Anticipated     |         |
| Sl.No                                         | Project                                  | DOA     | Cost     | DOC     | Cost            | DOC     |
|                                               |                                          |         |          |         |                 |         |
|                                               | <u>COAL</u>                              |         |          |         |                 |         |
| 1                                             | JHIRIA WEST OPENCAST PROJECT             | 11/2018 | 389.97   | 3/2026  | 389.97          | 3/2026  |
| 2                                             | INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP | 5/2018  | 2,434.75 | 3/2027  | 2,434.75        | 3/2027  |
|                                               |                                          |         |          |         |                 |         |
|                                               | <u>PETROLEUM</u>                         |         |          |         |                 |         |
| 3                                             | PARADIP SOMNATHPUR HALDIA PIPELINE       | 10/2018 | 1,297.50 | 10/2021 | 1,297.50        | 10/2021 |
|                                               |                                          |         |          |         |                 |         |
|                                               | <u>SHIPPING AND PORTS</u>                |         |          |         |                 |         |
| 4                                             | JAL MARG VIKAS PROJECT                   | 1/2018  | 4,200.00 | 3/2023  | 4,200.00        | 3/2023  |
|                                               |                                          |         |          |         |                 |         |

**TABLE-26**

Milestones (Cumulative due & achieved) Rs.150 Crore and above

|                      |      |
|----------------------|------|
| Total                | 4505 |
| Achieved up to month | 2330 |

**TABLE-27**

| List of projects reporting additional delayed Rs.150 Crore and above |                                                                                                         |                  |             |              |            |            | (December 2018)   |
|----------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------|------------------|-------------|--------------|------------|------------|-------------------|
|                                                                      |                                                                                                         |                  |             |              |            |            |                   |
|                                                                      |                                                                                                         | Cost ( Rs.crore) |             | DOC reported |            |            |                   |
| Sl. No                                                               | Project name                                                                                            | Original         | Anticipated | Original     | Last month | This month | Delay (in months) |
|                                                                      |                                                                                                         |                  |             |              |            |            |                   |
|                                                                      | <u>COAL</u>                                                                                             |                  |             |              |            |            |                   |
| 1                                                                    | ADASA UG TO OC WCL                                                                                      | 288.90           | 333.43      | 03/2023      | 03/2023    | 03/2024    | 12                |
|                                                                      |                                                                                                         |                  |             |              |            |            |                   |
|                                                                      | <u>FERTILISERS</u>                                                                                      |                  |             |              |            |            |                   |
| 2                                                                    | GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. RCF                             | 482.85           | 482.85      | 12/2017      | 12/2018    | 01/2019    | 1                 |
|                                                                      |                                                                                                         |                  |             |              |            |            |                   |
|                                                                      | <u>MINES</u>                                                                                            |                  |             |              |            |            |                   |
| 3                                                                    | 25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU NALCO                                               | 166.62           | 166.62      | 06/2019      | 12/2018    | 06/2019    | 6                 |
|                                                                      |                                                                                                         |                  |             |              |            |            |                   |
|                                                                      | <u>PETROLEUM</u>                                                                                        |                  |             |              |            |            |                   |
| 4                                                                    | RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH IOCL                                              | 247.52           | 247.52      | 02/2019      | 12/2018    | 01/2019    | 1                 |
| 5                                                                    | CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP IOCL                                            | 356.00           | 356.00      | 05/2019      | 12/2018    | 01/2019    | 1                 |
| 6                                                                    | PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I GAIL                                                            | 3,957.00         | 3,397.00    | 12/2018      | 12/2018    | 03/2019    | 3                 |
| 7                                                                    | AURAIYA PHULPUR PIPELINE PROJECT GAIL                                                                   | 1,427.94         | 800.00      | 12/2018      | 12/2018    | 03/2019    | 3                 |
| 8                                                                    | CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE GAIL                                                       | 327.78           | 200.00      | 04/2018      | 12/2018    | 03/2019    | 3                 |
| 9                                                                    | ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE IOCL  | 212.00           | 212.00      | 01/2021      | 01/2021    | 04/2021    | 3                 |
| 10                                                                   | REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR IOCL                | 318.80           | 318.80      | 08/2021      | 08/2021    | 11/2021    | 3                 |
| 11                                                                   | CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU IOCL                                           | 466.43           | 466.43      | 10/2020      | 05/2021    | 08/2021    | 3                 |
| 12                                                                   | CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH IOCL                           | 466.00           | 466.00      | 04/2021      | 04/2021    | 07/2021    | 3                 |
| 13                                                                   | FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY IOCL                                | 822.66           | 822.66      | 11/2018      | 11/2018    | 03/2019    | 4                 |
| 14                                                                   | PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND IOCL | 236.00           | 236.00      | 06/2020      | 06/2020    | 10/2020    | 4                 |

| List of projects reporting additional delayed Rs.150 Crore and above |                                                                                                                              |                  |             |              |            |            | (December 2018)   |
|----------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------|------------------|-------------|--------------|------------|------------|-------------------|
| Sl. No                                                               | Project name                                                                                                                 | Cost ( Rs.crore) |             | DOC reported |            |            | Delay (in months) |
|                                                                      |                                                                                                                              | Original         | Anticipated | Original     | Last month | This month |                   |
| 15                                                                   | HALDIA LPG IMPORT FACILITY BPCL                                                                                              | 694.00           | 694.00      | 10/2018      | 12/2018    | 06/2019    | 6                 |
| 16                                                                   | PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY BPCL                                                     | 4,588.29         | 5,245.96    | 08/2018      | 05/2019    | 11/2019    | 6                 |
| 17                                                                   | DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY IOCL                                                         | 3,076.00         | 4,190.00    | 09/2017      | 06/2018    | 03/2019    | 9                 |
| 18                                                                   | ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE IOCL                     | 348.00           | 348.00      | 01/2021      | 01/2021    | 10/2021    | 9                 |
| 19                                                                   | ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA ONGC Central Sector Projects | 4,619.94         | 4,619.94    | 12/2017      | 03/2019    | 03/2020    | 12                |
|                                                                      |                                                                                                                              |                  |             |              |            |            |                   |
|                                                                      | <u>POWER</u>                                                                                                                 |                  |             |              |            |            |                   |
| 20                                                                   | BONGAIGAON THERMAL POWER PROJECT NTPC                                                                                        | 4,375.35         | 8,150.00    | 09/2011      | 12/2018    | 01/2019    | 1                 |
| 21                                                                   | WESTERN REGION STRENGTHENING SCHEME-V PGCIL                                                                                  | 477.69           | 738.48      | 09/2010      | 12/2018    | 02/2019    | 2                 |
| 22                                                                   | SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV PGCIL                                                                          | 297.33           | 534.02      | 08/2014      | 12/2018    | 02/2019    | 2                 |
| 23                                                                   | EASTERN REGION STRENGTHENING SCHEME-V PGCIL                                                                                  | 1,364.52         | 1,891.41    | 04/2016      | 12/2018    | 02/2019    | 2                 |
| 24                                                                   | GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B PGCIL                                                         | 3,705.61         | 3,705.61    | 04/2018      | 12/2018    | 02/2019    | 2                 |
| 25                                                                   | EASTERN REGION STRENGTHENING SCHEME-XV PGCIL                                                                                 | 454.11           | 454.11      | 04/2018      | 11/2019    | 01/2020    | 2                 |
| 26                                                                   | TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN PGCIL                                                                 | 1,429.38         | 1,429.38    | 01/2019      | 01/2019    | 03/2019    | 2                 |
| 27                                                                   | TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) PGCIL                                                 | 300.94           | 300.94      | 12/2018      | 12/2018    | 02/2019    | 2                 |
| 28                                                                   | KUNADANKULAM APP TRANS SYSTEM (PGCIL) PGCIL                                                                                  | 1,779.29         | 2,187.32    | 11/2008      | 12/2018    | 03/2019    | 3                 |
| 29                                                                   | SYSTEM STRENGTHENING XIII OF SR GRID PGCIL                                                                                   | 487.49           | 639.46      | 06/2014      | 12/2018    | 03/2019    | 3                 |
| 30                                                                   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX PGCIL                                                                      | 539.82           | 539.82      | 06/2016      | 12/2018    | 03/2019    | 3                 |
| 31                                                                   | TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH PGCIL                              | 5,151.37         | 5,151.37    | 03/2018      | 03/2019    | 06/2019    | 3                 |



| List of projects reporting additional delayed Rs.150 Crore and above |                                                                                                                               |                  |             |              |            |            | (December 2018)   |
|----------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------|------------------|-------------|--------------|------------|------------|-------------------|
| Sl. No                                                               | Project name                                                                                                                  | Cost ( Rs.crore) |             | DOC reported |            |            | Delay (in months) |
|                                                                      |                                                                                                                               | Original         | Anticipated | Original     | Last month | This month |                   |
| 32                                                                   | ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO PGCIL                    | 197.40           | 197.40      | 03/2018      | 12/2018    | 03/2019    | 3                 |
| 33                                                                   | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT SJVN                                                         | 436.68           | 602.44      | 12/2016      | 12/2018    | 03/2019    | 3                 |
| 34                                                                   | WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) SJVN                                                            | 330.00           | 330.00      | 11/2017      | 12/2018    | 03/2019    | 3                 |
| 35                                                                   | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) PGCIL                       | 408.46           | 408.46      | 01/2019      | 03/2019    | 06/2019    | 3                 |
| 36                                                                   | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT PGCIL                                                              | 4,824.12         | 5,071.94    | 10/2012      | 02/2019    | 06/2019    | 4                 |
| 37                                                                   | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) PGCIL Central Sector Projects | 445.89           | 445.89      | 02/2019      | 02/2019    | 06/2019    | 4                 |
| 38                                                                   | TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR PGCIL                    | 808.63           | 808.63      | 01/2018      | 03/2019    | 09/2019    | 6                 |
|                                                                      |                                                                                                                               |                  |             |              |            |            |                   |
|                                                                      | <u>HEALTH AND FAMILY WELFARE</u>                                                                                              |                  |             |              |            |            |                   |
| 39                                                                   | SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB HSCC                                                                           | 152.95           | 152.95      | 02/2018      | 12/2018    | 06/2019    | 6                 |
|                                                                      |                                                                                                                               |                  |             |              |            |            |                   |
|                                                                      | <u>RAILWAYS</u>                                                                                                               |                  |             |              |            |            |                   |
| 40                                                                   | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) RVNL                                                                                | 133.41           | 385.00      | 03/2009      | 12/2018    | 02/2019    | 2                 |
| 41                                                                   | DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING SER                                                                                   | 309.44           | 525.81      | 12/2015      | 12/2018    | 02/2019    | 2                 |
| 42                                                                   | HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR) NWR                                                                              | 829.74           | 1,216.00    | 03/2015      | 03/2020    | 06/2020    | 3                 |
| 43                                                                   | MANDHANA - BRAHMAWART NEW LINE PROJECT. NER                                                                                   | 609.04           | 1,807.88    | 04/1999      | 12/2018    | 03/2019    | 3                 |
| 44                                                                   | AUNRIHAR MANDUADIH GAZIPUR VARANASI NER                                                                                       | 199.75           | 270.00      | 08/2018      | 08/2018    | 01/2019    | 5                 |
| 45                                                                   | HARIDASPUR-PARADEEP(NL) RVNL                                                                                                  | 1,185.64         | 1,844.47    | 12/2017      | 06/2019    | 03/2020    | 9                 |
| 46                                                                   | RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND SER                                                                     | 148.77           | 377.00      | 12/2016      | 12/2018    | 09/2019    | 9                 |


| List of projects reporting additional delayed Rs.150 Crore and above |                                                                                                                     |                  |             |              |            |            | (December 2018)   |
|----------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------|------------------|-------------|--------------|------------|------------|-------------------|
| Sl. No                                                               | Project name                                                                                                        | Cost ( Rs.crore) |             | DOC reported |            |            | Delay (in months) |
|                                                                      |                                                                                                                     | Original         | Anticipated | Original     | Last month | This month |                   |
| 47                                                                   | MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING SER                                                                         | 258.20           | 365.00      | N.A.         | 12/2018    | 01/2020    | 13                |
|                                                                      | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                  |                  |             |              |            |            |                   |
| 48                                                                   | SONAPUR TO GUWAHTI (AS-3) NHAI                                                                                      | 245.00           | 174.34      | 03/2008      | 12/2018    | 01/2019    | 1                 |
| 49                                                                   | PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS NHAI                                                   | 567.51           | 567.51      | 03/2018      | 12/2018    | 01/2019    | 1                 |
| 50                                                                   | 2 LANING WITH PS OF GULABPURA - UNIARA NHAI                                                                         | 597.00           | 597.00      | 10/2017      | 12/2018    | 01/2019    | 1                 |
| 51                                                                   | CONSTRUCTION OF ISLAMPUR BY PASS NHAI                                                                               | 361.15           | 361.15      | N.A.         | 12/2019    | 01/2020    | 1                 |
| 52                                                                   | 2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR NHAI                                                                  | 320.30           | 320.30      | 01/2019      | 01/2019    | 02/2019    | 1                 |
| 53                                                                   | PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 NHAI PPP (BOT)                                                               | 574.00           | 574.00      | 03/2014      | 09/2018    | 12/2018    | 3                 |
| 54                                                                   | 2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA NHAI PPP (BOT) | 530.07           | 530.07      | 08/2016      | 11/2018    | 02/2019    | 3                 |
| 55                                                                   | BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM NHAI PPP (BOT)  | 822.90           | 822.90      | 04/2018      | 12/2018    | 03/2019    | 3                 |
| 56                                                                   | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II NHAI                                                           | 795.76           | 795.76      | N.A.         | 12/2018    | 03/2019    | 3                 |
| 57                                                                   | GURGAON - KOTPUTLI - JAIPUR (SIX LANE) NHAI PPP (BOT)                                                               | 1,673.70         | 1,673.70    | 10/2011      | 12/2018    | 03/2019    | 3                 |
| 58                                                                   | FOUR LANING OF JABALPUR - LAKHNADON NHAI                                                                            | 928.83           | 928.83      | N.A.         | 12/2018    | 03/2019    | 3                 |
| 59                                                                   | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV NHAI                                                           | 810.22           | 810.22      | N.A.         | 12/2018    | 03/2019    | 3                 |
| 60                                                                   | TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR NHAI                                                | 275.90           | 275.90      | N.A.         | 12/2018    | 03/2019    | 3                 |
| 61                                                                   | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I NHAI                                                            | 794.30           | 794.30      | N.A.         | 12/2018    | 05/2019    | 5                 |
| 62                                                                   | CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA NHAI                                                               | 229.37           | 229.37      | 11/2018      | 11/2018    | 04/2019    | 5                 |
| 63                                                                   | PATNA-MUZZAFFARPUR NHAI PPP (ANNUITY)                                                                               | 671.30           | 671.30      | 02/2013      | 12/2018    | 06/2019    | 6                 |
| 64                                                                   | 4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI NHAI           | 400.25           | 400.25      | 03/2019      | 03/2019    | 09/2019    | 6                 |

| List of projects reporting additional delayed Rs.150 Crore and above |                                                                                                              |                  |             |              |            |            | (December 2018)   |
|----------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------|------------------|-------------|--------------|------------|------------|-------------------|
|                                                                      |                                                                                                              |                  |             |              |            |            |                   |
|                                                                      |                                                                                                              | Cost ( Rs.crore) |             | DOC reported |            |            |                   |
| Sl. No                                                               | Project name                                                                                                 | Original         | Anticipated | Original     | Last month | This month | Delay (in months) |
| 65                                                                   | FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITATION NHA | 767.03           | 767.03      | 08/2018      | 08/2018    | 09/2019    | 13                |
| 66                                                                   | PANIKHOLI-RIMOLI NHA PPP (BOT)                                                                               | 1,410.00         | 1,410.00    | 09/2014      | 10/2015    | 03/2019    | 41                |
|                                                                      |                                                                                                              |                  |             |              |            |            |                   |
|                                                                      | <u>TELECOMMUNICATIONS</u>                                                                                    |                  |             |              |            |            |                   |
| 67                                                                   | MAHARASHTRA CORE (LOT1) BSNL Central Sector Projects                                                         | 167.68           | 167.68      | 04/2018      | 12/2018    | 02/2019    | 2                 |
| 68                                                                   | MADHYA PRADESH ACCESS (LOT1) BSNL Central Sector Projects                                                    | 215.30           | 214.10      | 05/2018      | 12/2018    | 02/2019    | 2                 |
| 69                                                                   | MAHARASHTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT BSNL Central Sector Projects                               | 231.80           | 231.80      | 10/2018      | 12/2018    | 02/2019    | 2                 |
|                                                                      |                                                                                                              |                  |             |              |            |            |                   |
|                                                                      |                                                                                                              |                  |             |              |            |            |                   |
|                                                                      |                                                                                                              |                  |             |              |            |            |                   |


**TABLE-28**

| <u>Sector wise analysis of projects</u> Rs.150 Crore and above |                    |                  |              |              |                        |
|----------------------------------------------------------------|--------------------|------------------|--------------|--------------|------------------------|
|                                                                |                    | Cost (Rs. crore) |              |              |                        |
| Sector                                                         | Number of projects | Original         | Latest       | Anticipated  | Cumulative Expenditure |
| ATOMIC ENERGY                                                  | 4                  | 67,120.00        | 722,41.00    | 74,849.00    | 40,488.52              |
| CIVIL AVIATION                                                 | 1                  | 314.61           | 3,14.61      | 441.33       | 85.79                  |
| COAL                                                           | 97                 | 96,954.88        | 965,07.73    | 96,426.38    | 28,901.32              |
| FERTILISERS                                                    | 6                  | 1,781.92         | 17,93.57     | 1,793.57     | 690.15                 |
| MINES                                                          | 5                  | 7,078.62         | 70,78.62     | 7,078.62     | 556.50                 |
| STEEL                                                          | 13                 | 32,529.65        | 325,29.65    | 32,317.05    | 21,213.14              |
| PETROLEUM                                                      | 137                | 2,21,562.48      | 2,250,33.26  | 2,23,009.33  | 72,956.33              |
| POWER                                                          | 95                 | 2,96,370.25      | 3,716,73.80  | 3,59,705.13  | 2,36,102.37            |
| HEAVY INDUSTRY                                                 | 2                  | 3,272.00         | 52,81.30     | 5,381.30     | 3,095.09               |
| HEALTH AND FAMILY WELFARE                                      | 20                 | 8,129.23         | 81,29.23     | 8,246.52     | 2,779.69               |
| RAILWAYS                                                       | 367                | 4,85,710.46      | 5,476,01.88  | 6,96,269.31  | 1,66,896.81            |
| ROAD TRANSPORT AND HIGHWAYS                                    | 605                | 4,11,159.45      | 4,117,29.58  | 4,25,383.97  | 1,48,784.68            |
| SHIPPING AND PORTS                                             | 6                  | 7,988.29         | 84,13.09     | 8,426.32     | 2,068.91               |
| TELECOMMUNICATIONS                                             | 6                  | 16,478.21        | 164,77.01    | 27,707.01    | 8,966.75               |
| URBAN DEVELOPMENT                                              | 58                 | 1,60,566.07      | 1,610,98.60  | 1,66,153.31  | 73,250.95              |
| DEFENCE PRODUCTION                                             | 2                  | 453.64           | 4,54.00      | 461.66       | 160.78                 |
|                                                                |                    |                  |              |              |                        |
| Grand total                                                    | 1424               | 18,17,469.76     | 19,66,356.93 | 21,33,649.81 | 8,06,997.78            |

## Graphical Presentation of All Projects w.r.t. Original Schedule

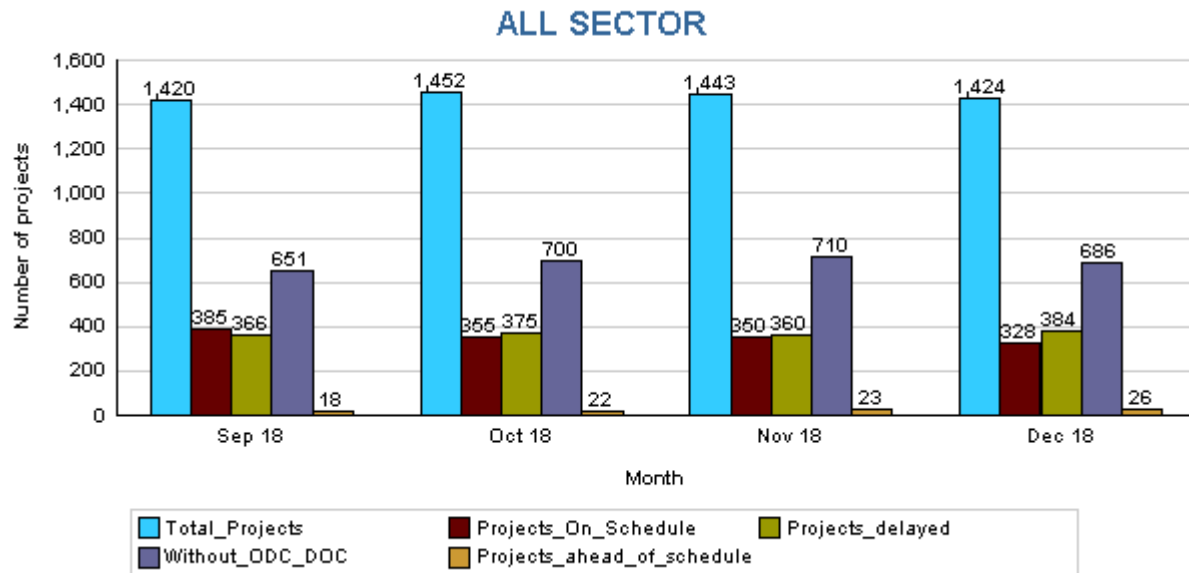


**Break-up of 384 Delayed projects in December 2018**

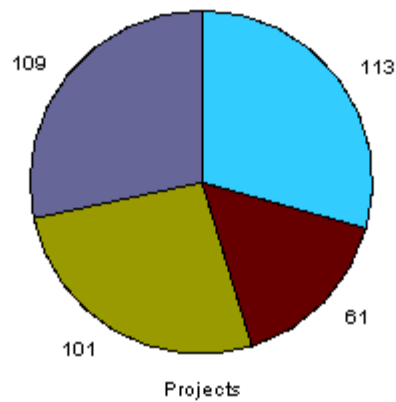


Delay in Months



# Graphical Presentation of All Projects w.r.t. Original Schedule

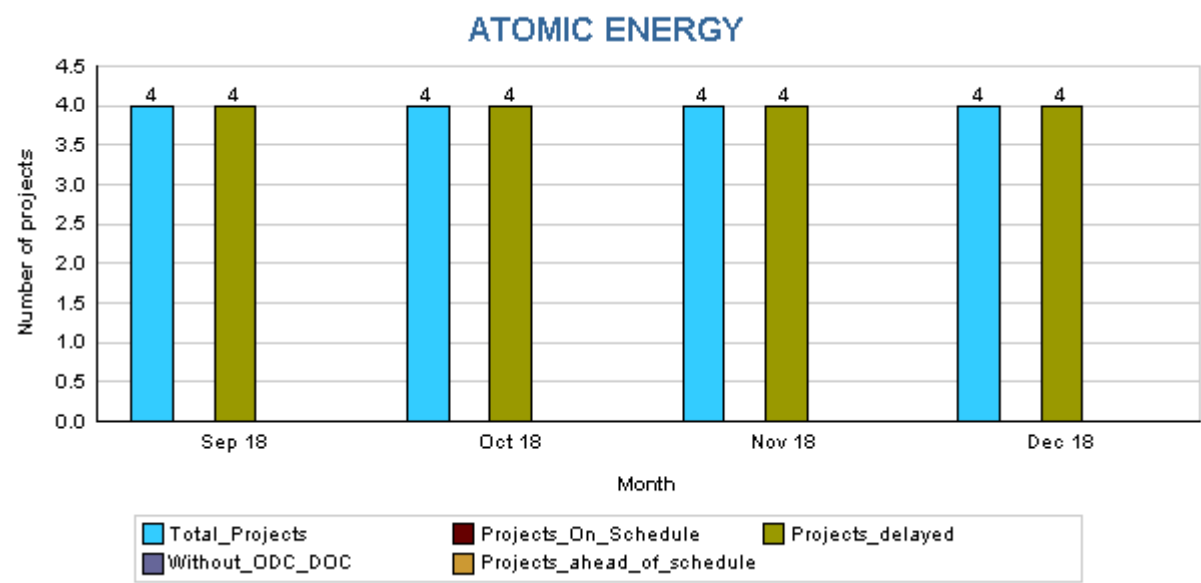


**Break-up of 4 Delayed projects in December 2018**

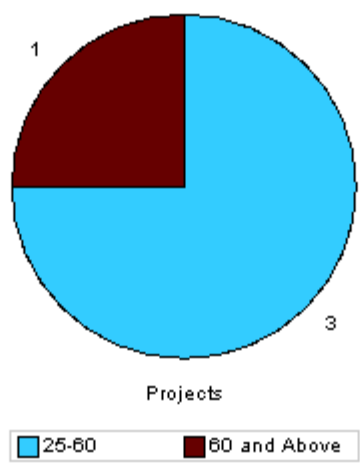


Delay in Months


# Graphical Presentation of All Projects w.r.t. Original Schedule

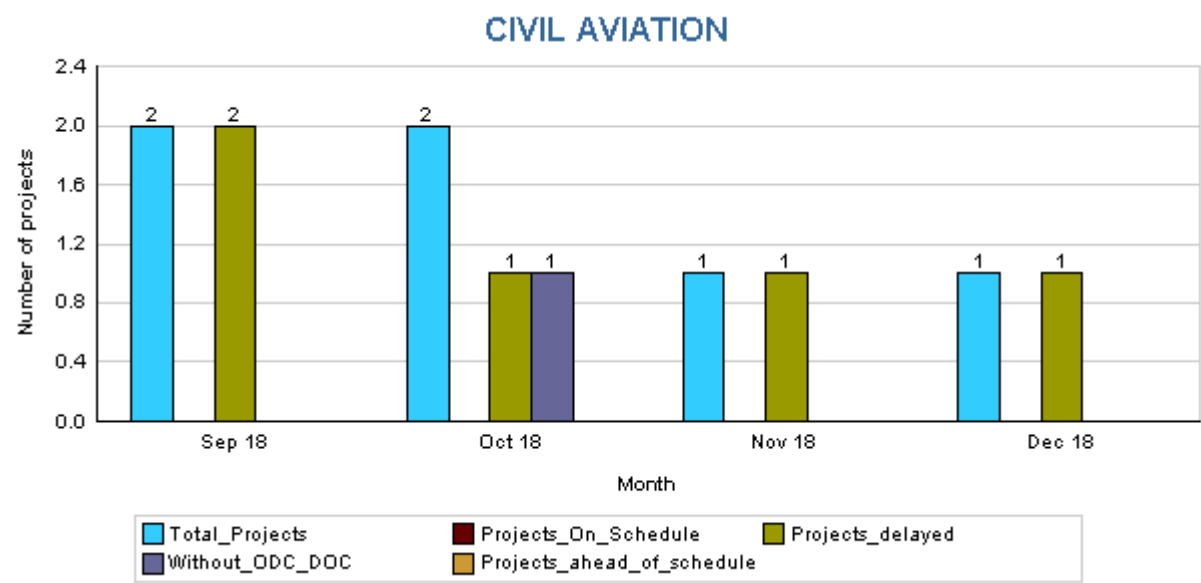


Break-up of 1 Delayed projects in December 2018




Delay in Months



# Graphical Presentation of All Projects w.r.t. Original Schedule

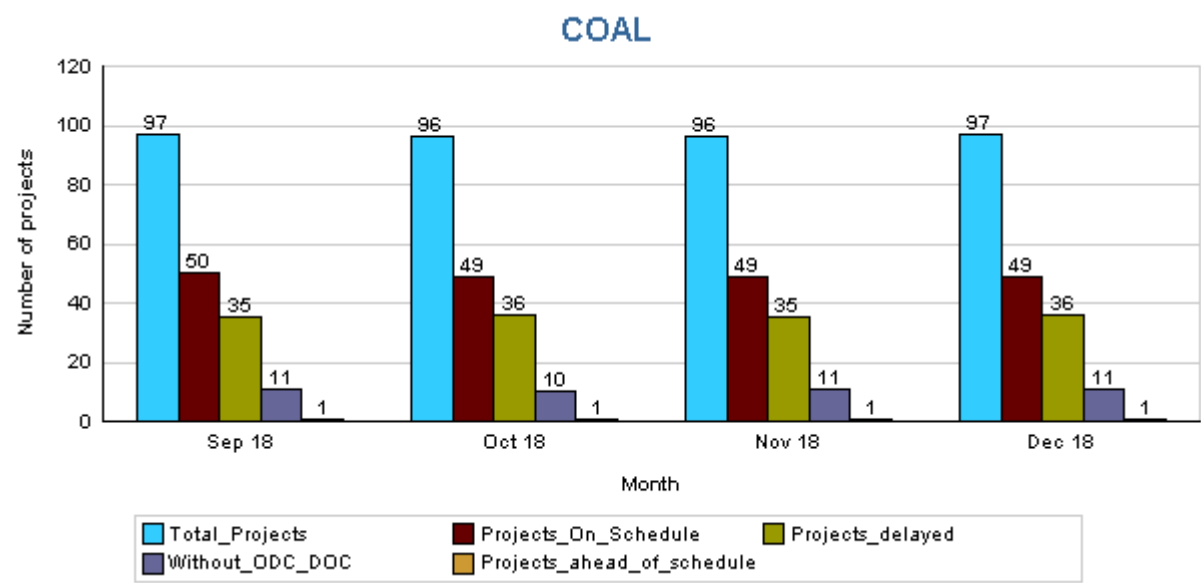

**Break-up of 36 Delayed projects in December 2018**

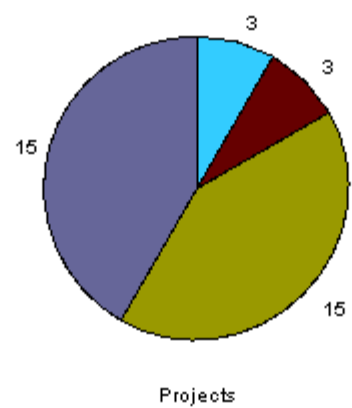


Delay in Months


| 1-12 | 13-24 | 25-60 | 60 and Above |
|------|-------|-------|--------------|
|      |       |       |              |



# Graphical Presentation of All Projects w.r.t. Original Schedule

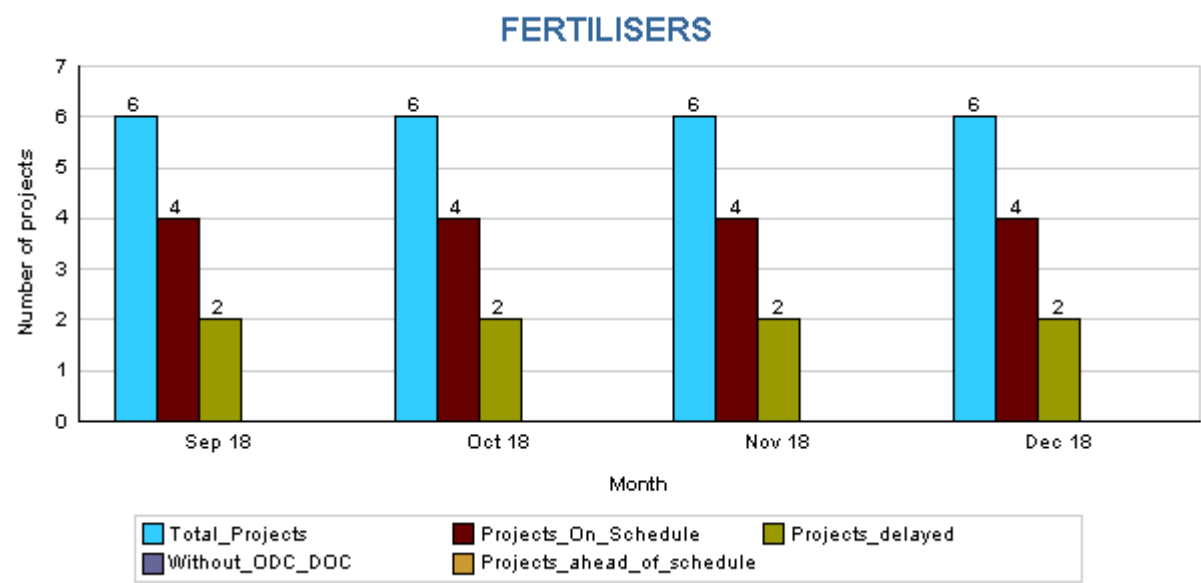


**Break-up of 2 Delayed projects in December 2018**

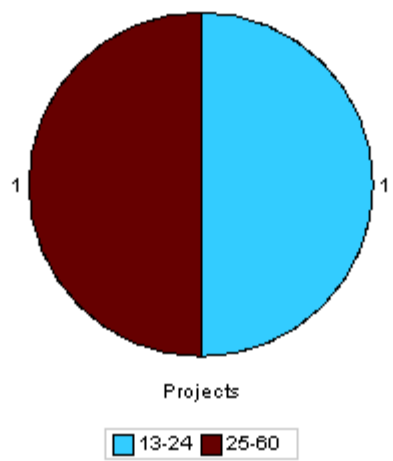


Delay in Months

# Graphical Presentation of All Projects w.r.t. Original Schedule

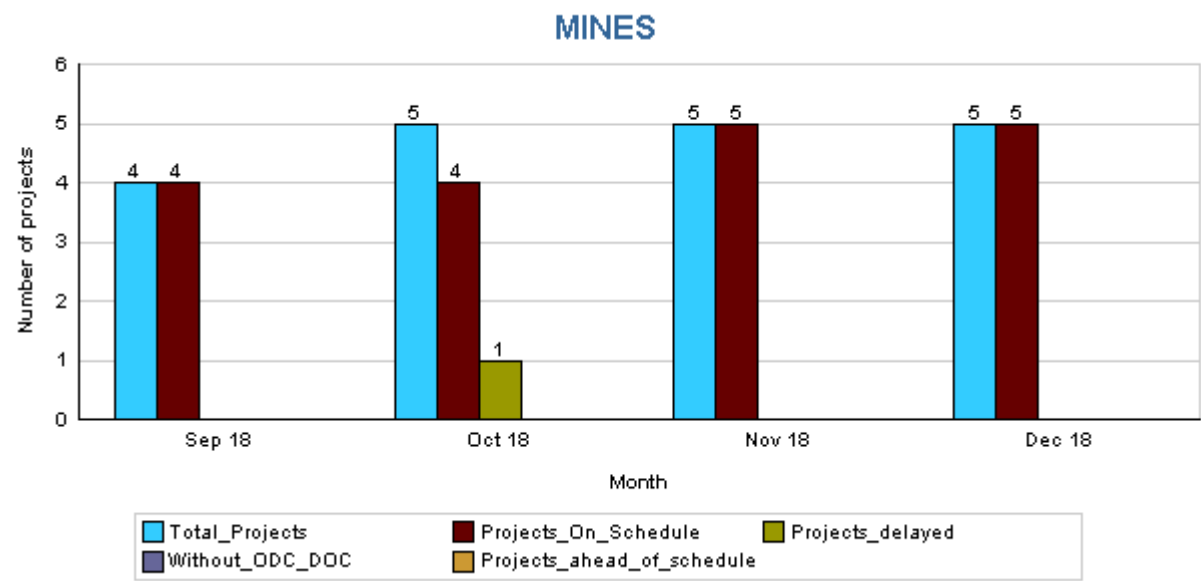


Delay in Months

# Graphical Presentation of All Projects w.r.t. Original Schedule

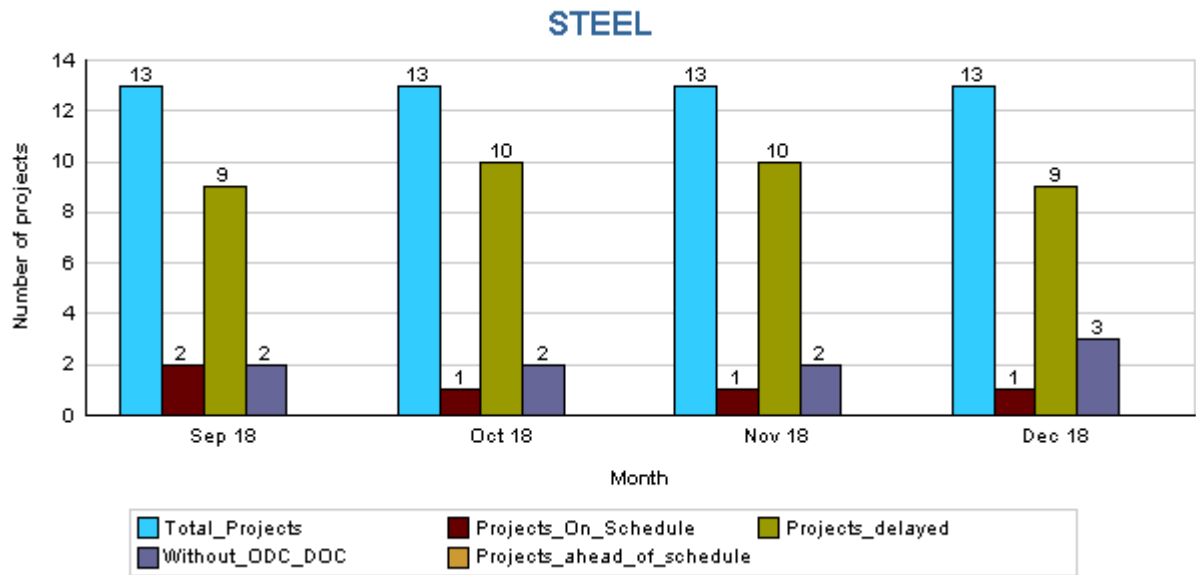


**Break-up of 9 Delayed projects in December 2018**

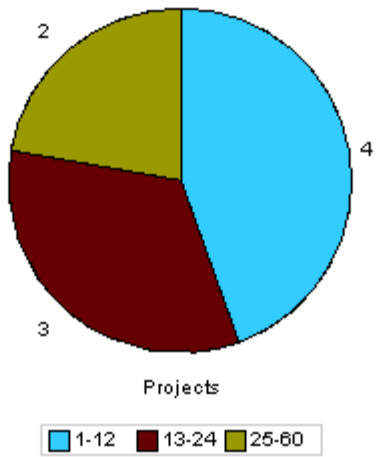


Delay in Months

## Graphical Presentation of All Projects w.r.t. Original Schedule

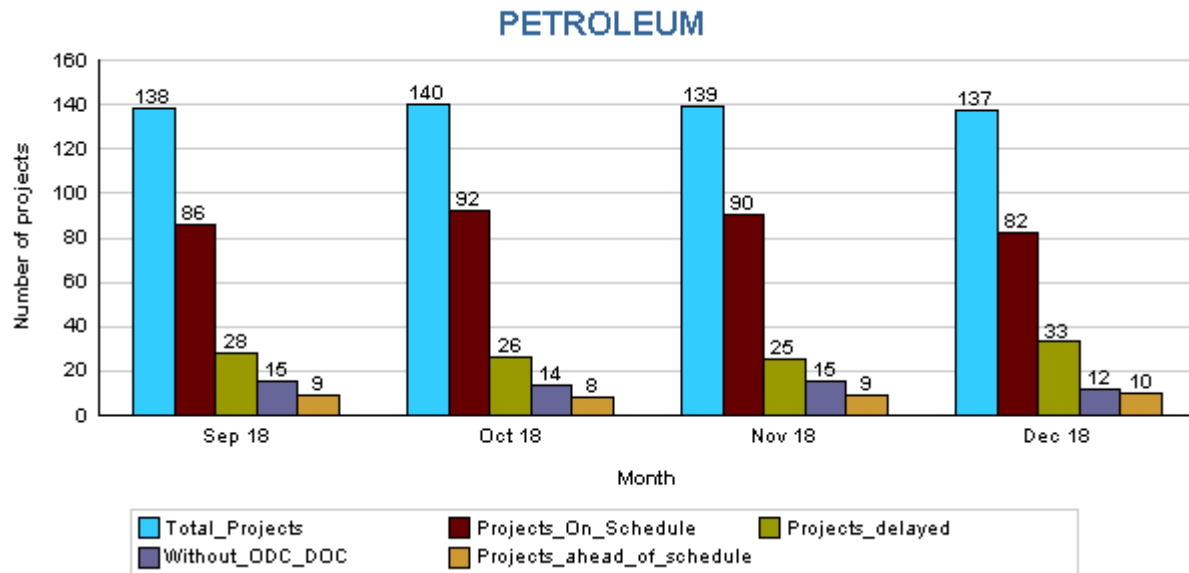


**Break-up of 33 Delayed projects in December 2018**

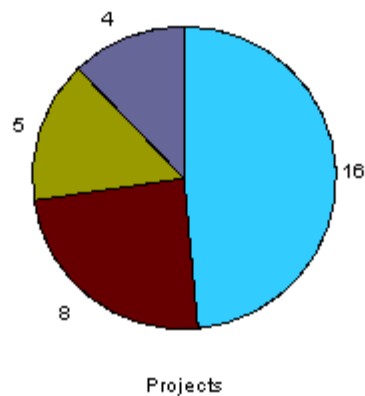


Delay in Months



# Graphical Presentation of All Projects w.r.t. Original Schedule

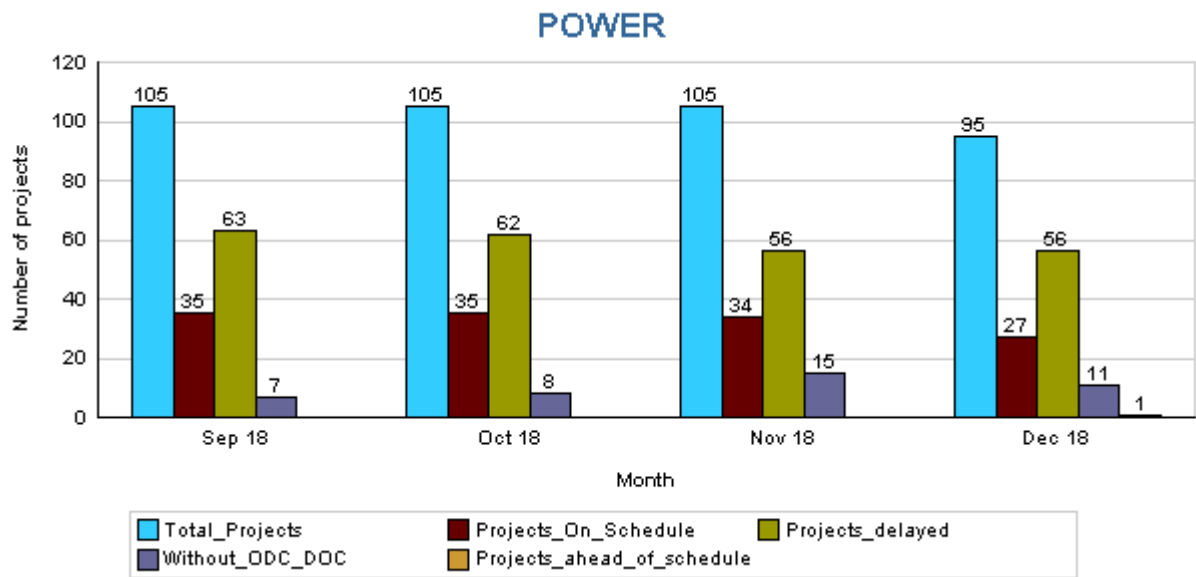


**Break-up of 56 Delayed projects in December 2018**

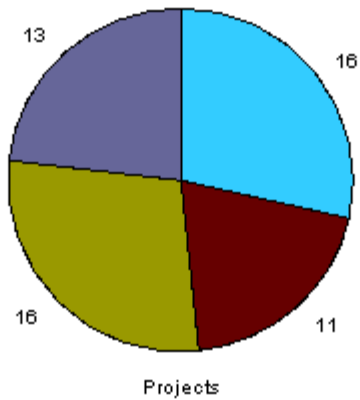


Delay in Months

| Delay in Months | 1-12 | 13-24 | 25-60 | 60 and Above |
|-----------------|------|-------|-------|--------------|
| Projects        | 16   | 11    | 16    | 13           |

# Graphical Presentation of All Projects w.r.t. Original Schedule

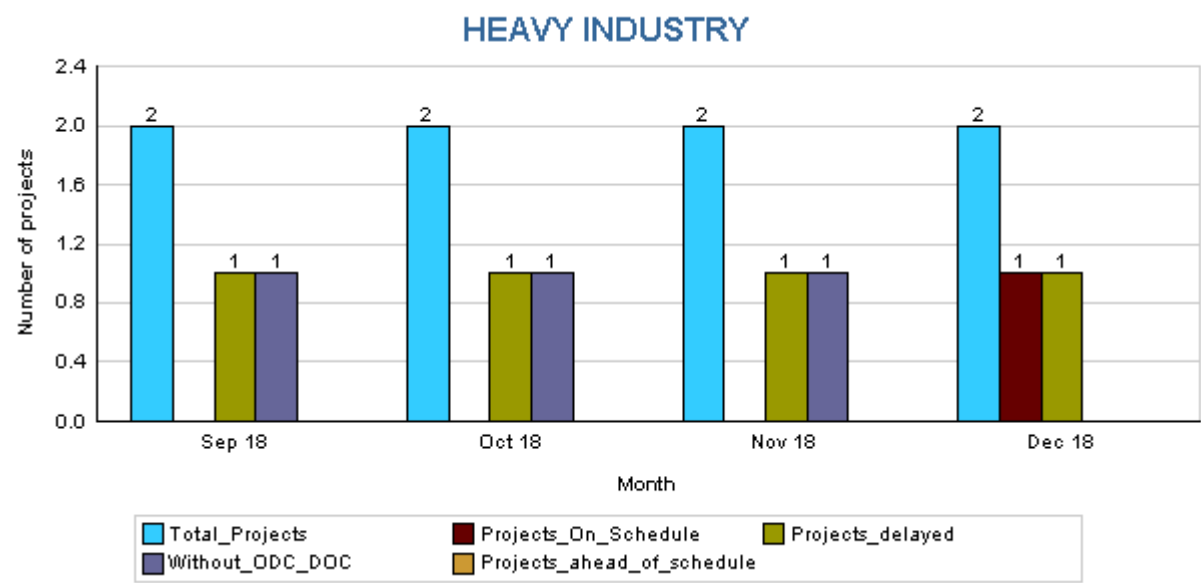


Break-up of 1 Delayed projects in December 2018

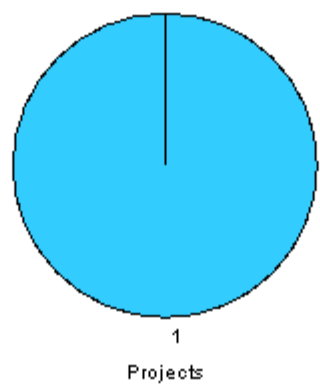


Delay in Months

60 and Above


# Graphical Presentation of All Projects w.r.t. Original Schedule

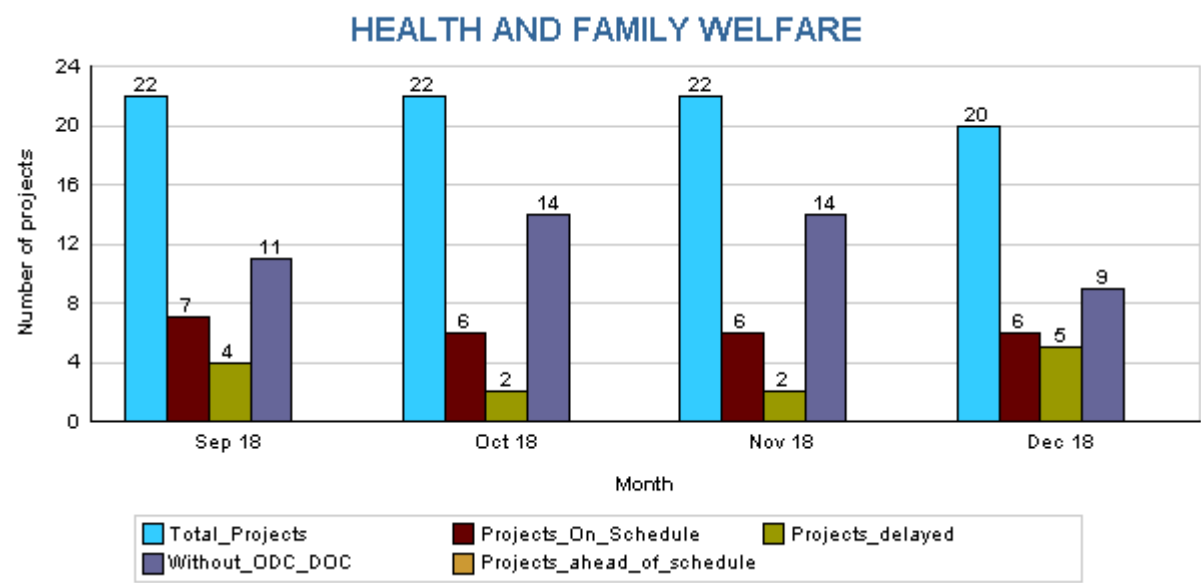


Break-up of 5 Delayed projects in December 2018

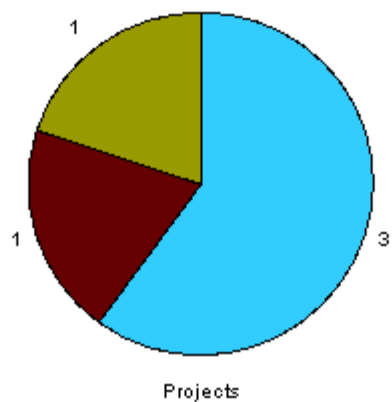


Delay in Months



## Graphical Presentation of All Projects w.r.t. Original Schedule

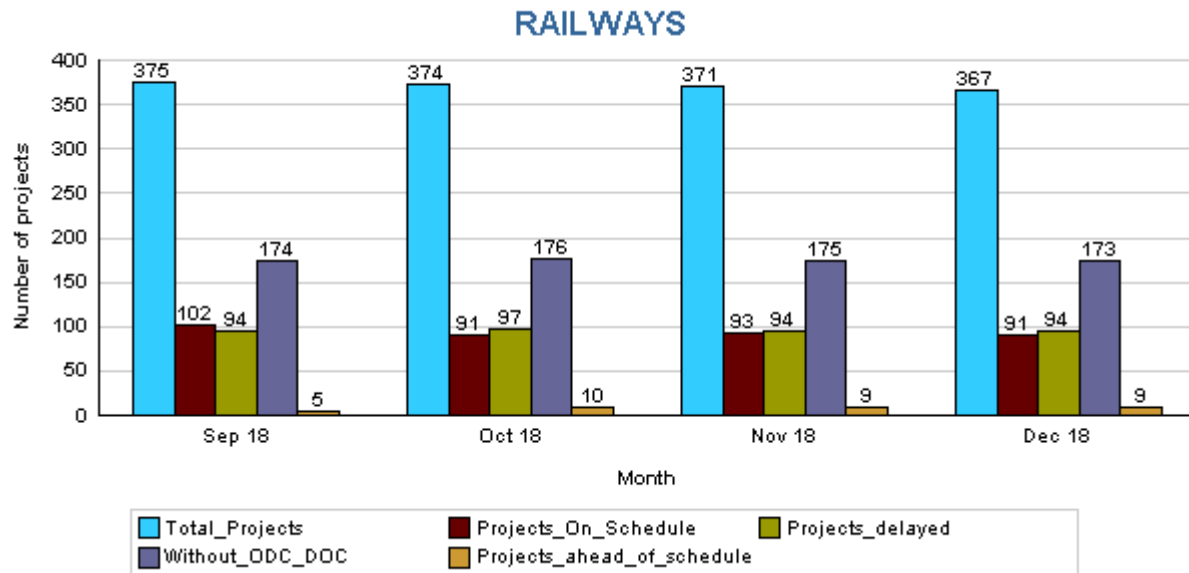

**Break-up of 94 Delayed projects in December 2018**

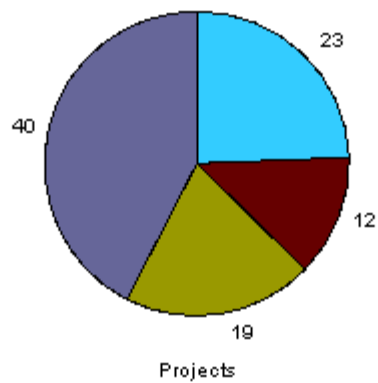


Delay in Months






## Graphical Presentation of All Projects w.r.t. Original Schedule

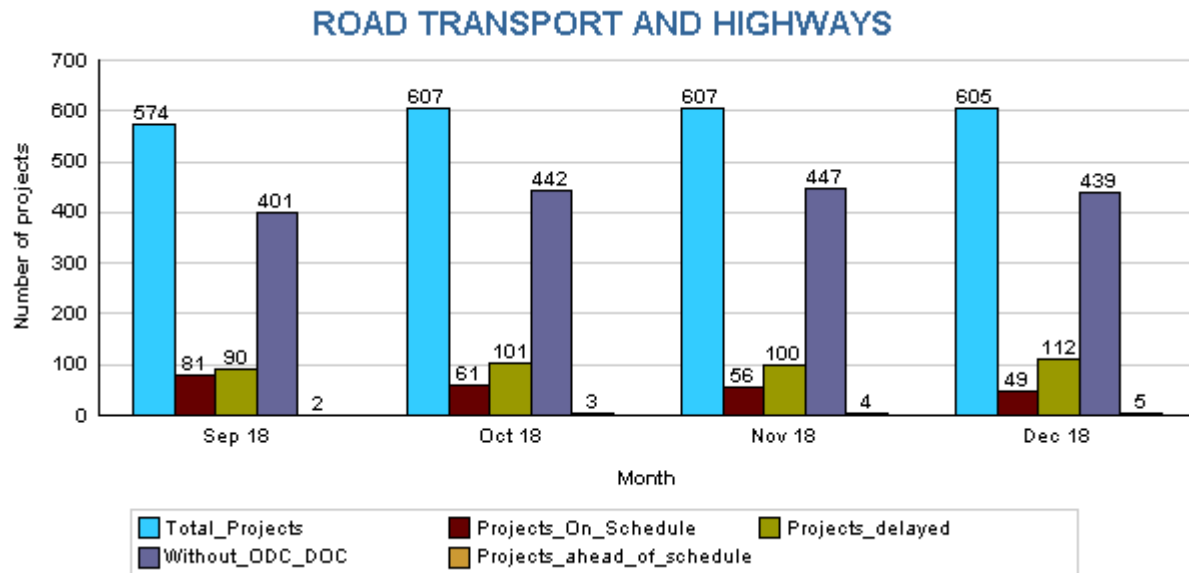


### Break-up of 112 Delayed projects in December 2018

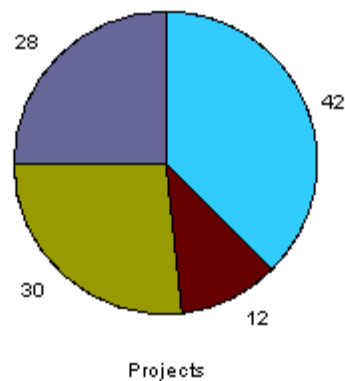


Delay in Months




# Graphical Presentation of All Projects w.r.t. Original Schedule

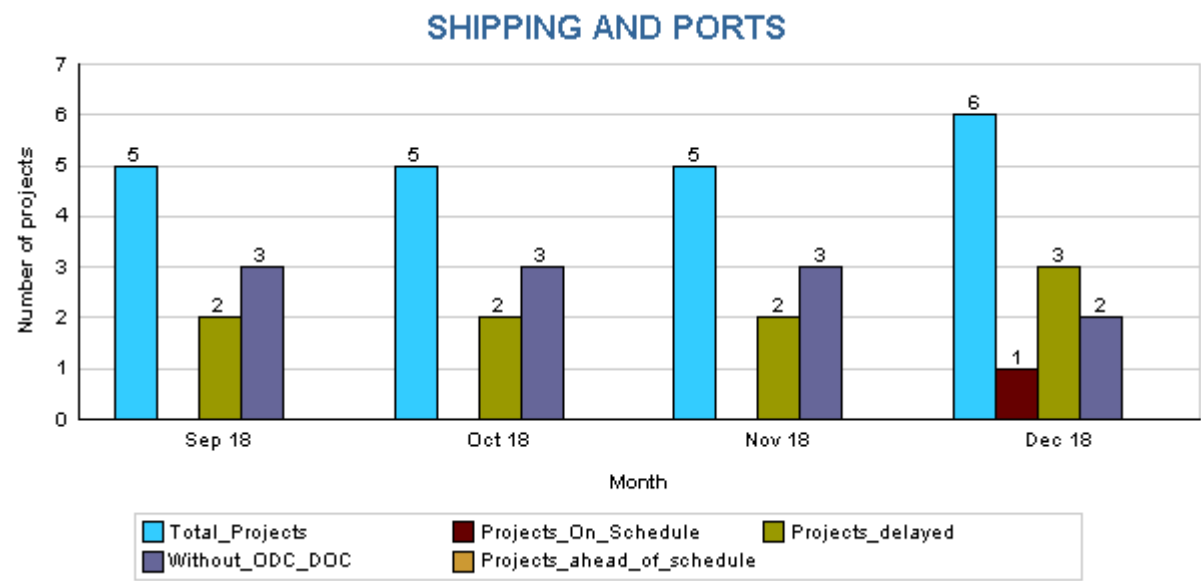


Break-up of 3 Delayed projects in December 2018

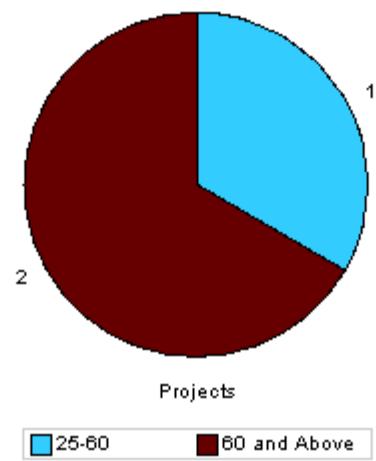

# Graphical Presentation of All Projects w.r.t. Original Schedule

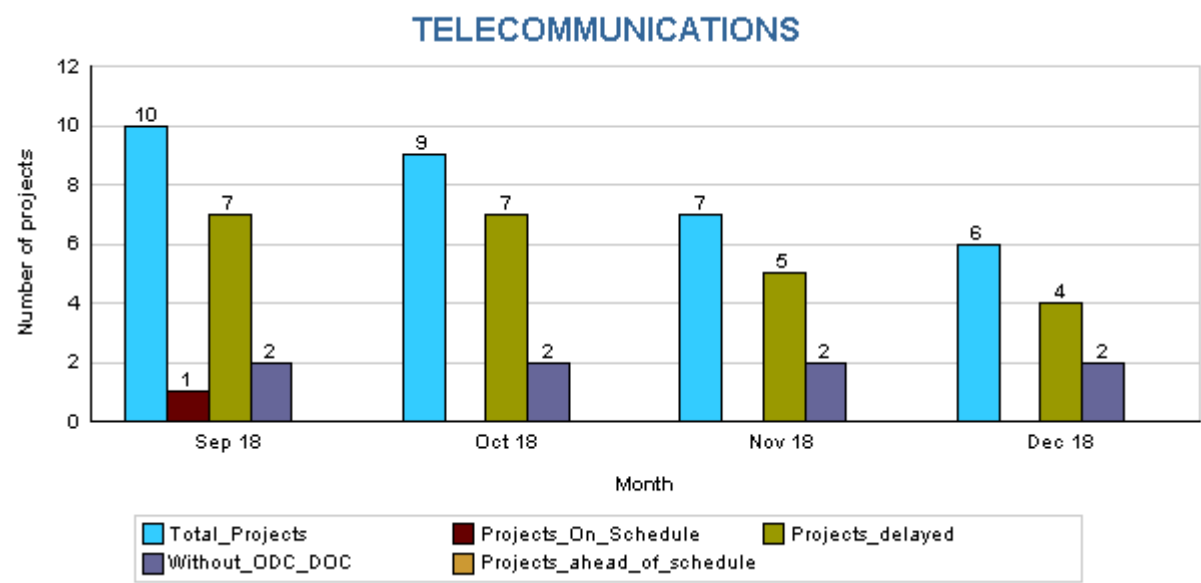


**Break-up of 4 Delayed projects in December 2018**

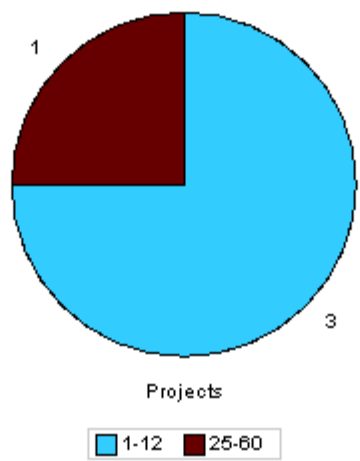


Delay in Months

## Graphical Presentation of All Projects w.r.t. Original Schedule

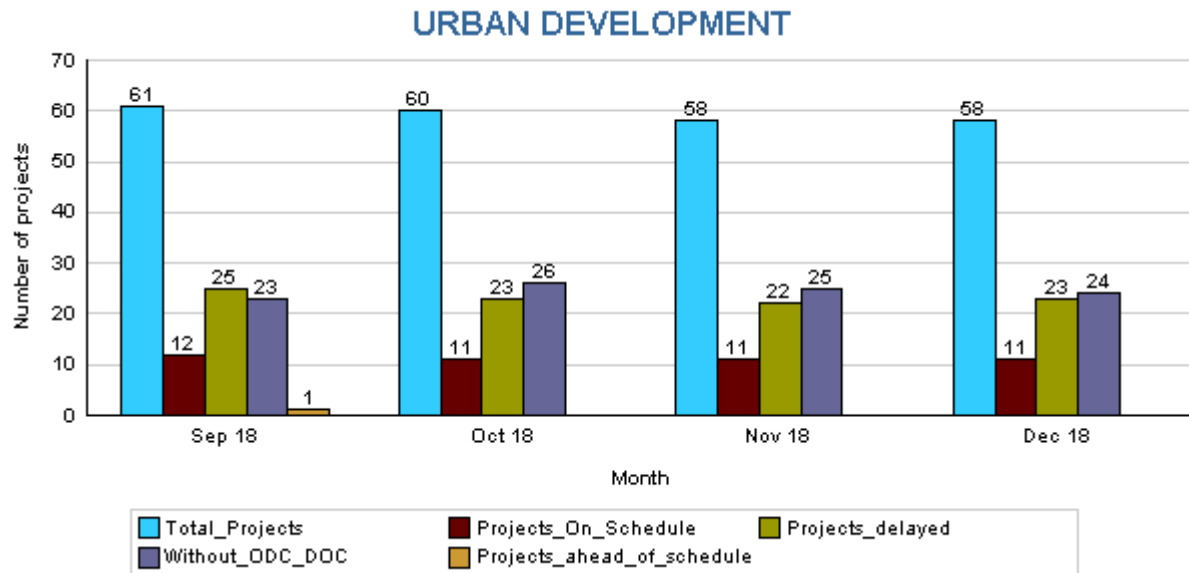


**Break-up of 23 Delayed projects in December 2018**

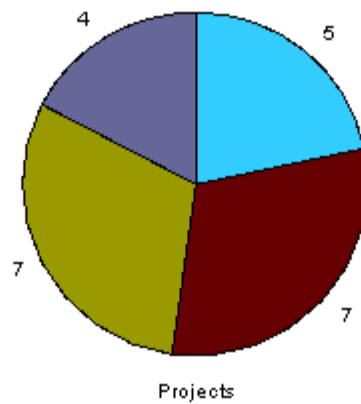


Delay in Months



# Graphical Presentation of All Projects w.r.t. Original Schedule

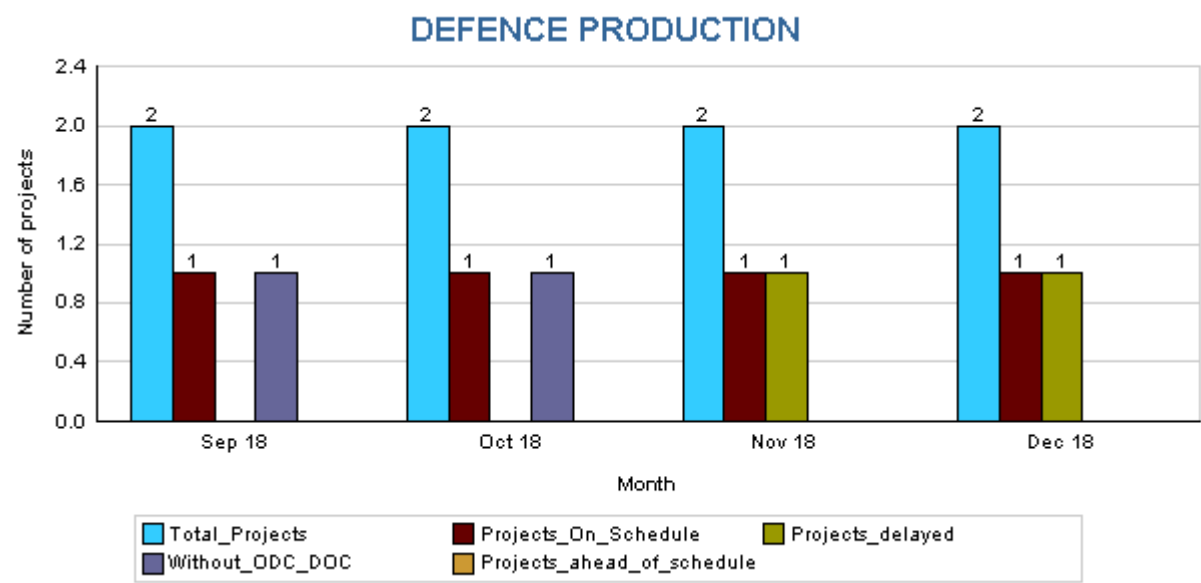

**Break-up of 1 Delayed projects in December 2018**



Delay in Months



## Table-29

| Detail of ongoing Projects Costing Rs.150 Crore and above. |                                                                                                            |                  |                         |                  |                             |                       |             |                                            |                             |
|------------------------------------------------------------|------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
|                                                            |                                                                                                            |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
| Sl.No                                                      | Project                                                                                                    | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1                                                          | 2                                                                                                          | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
|                                                            |                                                                                                            |                  |                         |                  |                             |                       |             |                                            |                             |
|                                                            | <u>ATOMIC ENERGY</u>                                                                                       |                  |                         |                  |                             |                       |             |                                            |                             |
| 1                                                          | KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,                                       | 10/2009          | 11,459.00<br>16,580.00  | 16,580.00        | 12,848.00                   | 12/2015<br>11/2016    | 06/2020     | 54(O)<br>43(R)                             | 50/70                       |
| 2                                                          | RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,                          | 10/2009          | 12,320.00<br>-          | 12,320.00        | 10,138.00                   | 12/2016<br>03/2017    | 12/2020     | 48(O)<br>45(R)                             | 38/68                       |
| 3                                                          | PROTOTYPE FAST BREEDER REACTOR (BHAVINI 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,                          | 09/2003          | 3,492.00<br>-           | 6,100.00         | 5,687.52                    | 09/2010<br>-          | 03/2019     | 102(O)<br>-                                | 83/87                       |
| 4                                                          | KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects      | 03/2013          | 39,849.00<br>-          | 39,849.00        | 11,815.00                   | 11/2020<br>-          | 11/2023     | 36(O)<br>-                                 | 18/76                       |
|                                                            | Total                                                                                                      |                  | 67,120.00<br>-          | 74,849.00        | 40,488.52                   |                       |             |                                            | 189/301                     |
|                                                            |                                                                                                            |                  |                         |                  |                             |                       |             |                                            |                             |
|                                                            | <u>CIVIL AVIATION</u>                                                                                      |                  |                         |                  |                             |                       |             |                                            |                             |
| 5                                                          | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT PORTBLAIR - [N04000073]AAI,A & N ISLANDS , | 10/2013          | 314.61<br>-             | 441.33           | 85.79                       | 09/2018<br>-          | 06/2020     | 21(O)<br>-                                 | 0/0                         |
|                                                            | Total                                                                                                      |                  | 314.61<br>-             | 441.33           | 85.79                       |                       |             |                                            | 0/0                         |
|                                                            |                                                                                                            |                  |                         |                  |                             |                       |             |                                            |                             |
|                                                            | <u>COAL</u>                                                                                                |                  |                         |                  |                             |                       |             |                                            |                             |
| 6                                                          | GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,                                     | 06/2010          | 11,816.40<br>-          | 11,816.40        | 2,848.30                    | 03/2023<br>-          | 03/2023     | 0(O)<br>-                                  | 14/18                       |
| 7                                                          | KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH ,                                          | 08/2013          | 7,612.33<br>-           | 7,612.33         | 1,913.96                    | 03/2023<br>-          | 03/2023     | 0(O)<br>-                                  | 6/20                        |
| 8                                                          | PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH ,                                                        | 11/2014          | 1,624.59<br>-           | 1,624.59         | 6.13                        | 03/2023<br>-          | 03/2023     | 0(O)<br>-                                  | 1/12                        |
| 9                                                          | JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH ,                                                  | 09/2008          | 152.43<br>-             | 459.49           | 178.93                      | 03/2015<br>-          | 03/2020     | 60(O)<br>-                                 | 5/9                         |
| 10                                                         | KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH ,                                              | 07/2008          | 178.44<br>-             | 178.44           | 5.16                        | 03/2014<br>-          | 03/2020     | 72(O)<br>-                                 | 1/7                         |
| 11                                                         | MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH ,                                            | 12/2009          | 321.50<br>-             | 321.50           | 202.68                      | 03/2014<br>-          | 03/2020     | 72(O)<br>-                                 | 0/4                         |
| 12                                                         | AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH ,                                     | 11/2009          | 198.59<br>-             | 198.59           | 169.50                      | 03/2016<br>-          | 03/2019     | 36(O)<br>-                                 | 7/9                         |
| 13                                                         | BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH ,                                            | 04/2012          | 258.56<br>-             | 258.56           | 167.63                      | 03/2016<br>-          | 03/2019     | 36(O)<br>-                                 | 4/7                         |
| 14                                                         | CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH ,                                              | 12/2013          | 610.63<br>-             | 610.63           | 81.27                       | 03/2022<br>-          | 03/2022     | 0(O)<br>-                                  | 2/9                         |
| 15                                                         | BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH ,                                                   | 05/2014          | 164.49<br>-             | 164.49           | 67.20                       | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 4/8                         |
| 16                                                         | AMERA OC RCE - [N06000123]SECL,CHHATISGARH ,                                                               | 02/2015          | 335.97<br>-             | 335.97           | 52.41                       | 03/2018<br>-          | 03/2018     | -                                          | 1/7                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                         |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-----------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                 | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                       | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 17    | AMGAON OPENCAST PROJECT RCE - [N06000135]SECL,CHHATISGARH ,                             | 07/2015          | 316.10 -                | 316.10           | 59.99                       | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/6                         |
| 18    | DURGAPUR OPENCAST PROJECT - [N06000136]SECL,CHHATISGARH ,                               | 02/2015          | 916.24 -                | 916.24           | 3.81                        | 03/2023 -             | 03/2023     | 0(O) -                                     | 1/10                        |
| 19    | MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH ,                             | 10/2015          | 1,875.32 -              | 1,875.32         | .00                         | 03/2024 -             | 03/2024     | 0(O) -                                     | 0/4                         |
| 20    | VIJAY WEST OPENCAST PROJECT - [N06000158]SECL,CHHATISGARH ,                             | 05/2017          | 976.95 -                | 976.95           | 75.96                       | 03/2026 -             | 03/2026     | 0(O) -                                     | 0/1                         |
| 21    | MAHAMAYA OPENCAST PROJECT - [N06000164]SECL,CHHATISGARH ,                               | 05/2018          | 410.26 -                | 410.26           | 9.53                        | 03/2026 -             | 03/2026     | 0(O) -                                     | 0/0                         |
| 22    | JHIRIA WEST OPENCAST PROJECT - [N06000166]SECL,CHHATISGARH ,                            | 11/2018          | 389.97 -                | 389.97           | .00                         | 03/2026 -             | 03/2026     | 0(O) -                                     | 0/0                         |
| 23    | MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND ,                                     | 08/2008          | 706.40 -                | 706.40           | 185.62                      | 07/2012 -             | 03/2021     | 104(O) -                                   | 4/5                         |
| 24    | CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND ,                                  | 08/2007          | 163.51 -                | 163.51           | 103.41                      | 03/2011 -             | 03/2020     | 108(O) -                                   | 3/5                         |
| 25    | NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND ,                                | 12/2007          | 179.87 -                | 179.87           | 174.69                      | 03/2012 -             | 03/2019     | 84(O) -                                    | 3/5                         |
| 26    | TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND ,                                        | 08/2008          | 264.68 -                | 264.68           | 178.37                      | 03/2012 -             | 03/2019     | 84(O) -                                    | 4/5                         |
| 27    | RAJRAPPA RCE OCP ( 3.0 MTY) - [N06000087]CCL,JHARKHAND ,                                | 12/2009          | 510.85 -                | 510.85           | 340.29                      | 03/2016 -             | 03/2019     | 36(O) -                                    | 5/5                         |
| 28    | KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND ,                                         | 06/2009          | 162.46 -                | 162.46           | 89.21                       | 03/2014 -             | 03/2019     | 60(O) -                                    | 5/5                         |
| 29    | MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,                             | 02/2011          | 339.88 -                | 339.88           | 12.08                       | 04/2014 -             | 10/2018     | -                                          | 4/7                         |
| 30    | MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,                                       | 08/2011          | 1,230.27 -              | 1,230.27         | 326.22                      | 04/2015 -             | 04/2019     | 48(O) -                                    | 2/6                         |
| 31    | AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND ,                                         | 02/2012          | 858.11 -                | 858.11           | 184.43                      | 03/2020 -             | 03/2020     | 0(O) -                                     | 6/6                         |
| 32    | NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,          | 02/2014          | 555.52 -                | 555.52           | 5.01                        | 03/2021 -             | 03/2021     | 0(O) -                                     | 0/2                         |
| 33    | KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND ,                                          | 08/2011          | 988.35 -                | 988.35           | 45.26                       | 04/2017 -             | -           | -                                          | 1/3                         |
| 34    | MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,                                     | 08/2010          | 289.45 -                | 289.45           | 194.20                      | 05/2014 -             | 04/2018     | -                                          | 0/8                         |
| 35    | PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,                                     | 10/2012          | 269.82 -                | 269.82           | 179.30                      | 04/2014 -             | 04/2018     | -                                          | 0/10                        |
| 36    | HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,                                        | 10/2015          | 359.69 -                | 359.69           | 42.44                       | 03/2022 -             | 03/2022     | 0(O) -                                     | 1/22                        |
| 37    | NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY SINGRAULI - [N06000033]NCL,MADHYA PRADESH , | 10/2007          | 259.40 -                | 486.57           | 266.38                      | 03/2012 -             | -           | -                                          | 1/3                         |
| 38    | BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH ,                                 | 08/2015          | 1,186.64 -              | 203.82           | 103.85                      | 03/2023 -             | 03/2021     | -24(O) -                                   | 3/10                        |
| 39    | AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,                                | 02/2015          | 481.60 -                | 481.60           | .00                         | 03/2023 -             | 03/2023     | 0(O) -                                     | 2/8                         |
| 40    | RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,                          | 12/2014          | 357.80 -                | 357.80           | 113.19                      | 03/2021 -             | 03/2021     | 0(O) -                                     | 3/9                         |
| 41    | KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,                                 | 12/2014          | 371.04 -                | 371.04           | 41.52                       | 03/2021 -             | 03/2021     | 0(O) -                                     | 1/7                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                              |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|----------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                      | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                            | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 42    | BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,                                   | 07/2015          | 231.92 -                | 231.92           | .00                         | 03/2022 -             | 03/2022     | 0(O) -                                     | 1/7                         |
| 43    | MALACHUA OPENCAST PROJECT - [N06000139]SECL,MADHYA PRADESH ,                                 | 10/2015          | 488.33 -                | 488.33           | 24.16                       | 03/2023 -             | 03/2023     | 0(O) -                                     | 0/4                         |
| 44    | AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,                        | 03/2016          | 869.44 -                | 869.44           | 111.89                      | 03/2021 -             | 03/2021     | 0(O) -                                     | 2/4                         |
| 45    | COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH ,                    | 07/2016          | 409.87 -                | 409.87           | 17.50                       | 03/2022 -             | 03/2022     | 0(O) -                                     | 0/0                         |
| 46    | JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects | 05/2017          | 1,783.09 -              | 1,783.09         | 229.76                      | 03/2021 -             | 03/2021     | 0(O) -                                     | 0/9                         |
| 47    | DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH ,                    | 11/2017          | 1,255.17 -              | 1,255.17         | 94.68                       | 03/2022 -             | 03/2022     | 0(O) -                                     | 0/9                         |
| 48    | PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA ,                                         | 09/2014          | 441.82 -                | 441.82           | 187.02                      | 03/2020 -             | 03/2020     | 0(O) -                                     | 7/11                        |
| 49    | DINESH OCP - [N06000118]WCL,MAHARASHTRA ,                                                    | 11/2014          | 611.16 -                | 611.16           | 395.73                      | 03/2020 -             | 03/2020     | 0(O) -                                     | 3/8                         |
| 50    | MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA ,                                              | 09/2014          | 266.23 -                | 266.23           | 143.29                      | 03/2021 -             | 03/2021     | 0(O) -                                     | 12/12                       |
| 51    | GOKUL - [N06000120]WCL,MAHARASHTRA ,                                                         | 11/2014          | 267.67 -                | 267.67           | 207.74                      | 03/2018 -             | 03/2018     | -                                          | 7/7                         |
| 52    | BHANEGAON OC - [N06000121]WCL,MAHARASHTRA ,                                                  | 02/2015          | 187.94 409.68           | 409.68           | 95.83                       | 03/2023 02/2017       | 03/2023     | 0(O) 73(R)                                 | 7/11                        |
| 53    | NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,                                            | 05/2015          | 295.56 -                | 295.56           | 88.13                       | 03/2019 -             | 03/2019     | 0(O) -                                     | 10/13                       |
| 54    | SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,                                              | 06/2015          | 205.49 -                | 205.49           | 105.34                      | 03/2020 -             | 03/2020     | 0(O) -                                     | 5/10                        |
| 55    | AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA ,                              | 06/2015          | 483.69 -                | 483.69           | 89.91                       | 03/2021 -             | 03/2021     | 0(O) -                                     | 2/6                         |
| 56    | AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,                                | 08/2015          | 727.28 -                | 727.28           | 238.43                      | 03/2025 -             | 03/2025     | 0(O) -                                     | 5/13                        |
| 57    | ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,                                                | 08/2015          | 288.90 333.43           | 333.43           | .02                         | 03/2023 03/2024       | 03/2024     | 12(O) 0(R)                                 | 3/10                        |
| 58    | KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA ,                                          | 11/2015          | 277.65 313.34           | 313.34           | 6.12                        | 03/2021 09/2018       | 03/2024     | 36(O) 66(R)                                | 3/6                         |
| 59    | MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA ,                     | 11/2015          | 498.42 -                | 498.42           | 59.20                       | 03/2020 -             | 03/2020     | 0(O) -                                     | 2/6                         |
| 60    | AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,                            | 02/2016          | 198.68 -                | 198.68           | 254.72                      | 03/2019 -             | 03/2019     | 0(O) -                                     | 2/9                         |
| 61    | BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,                                     | 02/2016          | 304.52 -                | 304.52           | 129.39                      | 03/2019 -             | 03/2019     | 0(O) -                                     | 2/8                         |
| 62    | KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA ,                                     | 03/2017          | 362.73 -                | 362.73           | 258.23                      | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/0                         |
| 63    | NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,                          | 08/2016          | 319.76 -                | 319.76           | 58.04                       | 03/2022 -             | 03/2022     | 0(O) -                                     | 0/3                         |
| 64    | DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,                                        | 09/2016          | 458.07 -                | 458.07           | 16.00                       | 03/2022 -             | 03/2022     | 0(O) -                                     | 1/12                        |
| 65    | DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,                        | 02/2017          | 328.00 -                | 328.00           | 90.65                       | 03/2021 -             | 03/2021     | 0(O) -                                     | 1/6                         |
| 66    | KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA ,                                | 01/2005          | 302.96 -                | 302.96           | 302.96                      | 03/2010 -             | 03/2018     | -                                          | 10/10                       |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                        | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                              | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 67    | BHUBANESWARI OCP MCL (20.0 MTY) - [N06000034]MCL,ODISHA ,                                      | 12/2007          | 490.10                  | 490.10           | 413.37                      | 03/2017               | 03/2020     | 36(O)                                      | 11/12                       |
| 68    | KANIHA OCP MCL (10.0 MTY) - [N06000035]MCL,ODISHA ,                                            | 12/2007          | 457.77                  | 457.77           | 584.85                      | 03/2013               | 03/2020     | 84(O)                                      | 8/9                         |
| 69    | BALRAM OCP EXTENSION MCL 8.00 MTY - [N06000044]MCL,ODISHA ,                                    | 12/2007          | 172.08                  | 172.08           | 267.19                      | 03/2010               | 03/2020     | 120(O)                                     | 3/4                         |
| 70    | ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,                                | 08/2008          | 207.28                  | 207.28           | 235.50                      | 03/2012               | 03/2021     | 108(O)                                     | 5/5                         |
| 71    | HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,                                   | 11/2008          | 479.53                  | 479.53           | 336.08                      | 03/2013               | 03/2020     | 84(O)                                      | 6/9                         |
| 72    | BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N060000112]MCL,ODISHA ,                                 | 05/2014          | 479.15                  | 479.15           | 120.51                      | 03/2019               | 03/2024     | 60(O)                                      | 2/9                         |
| 73    | SIARMAL OCP (40.00MTY) - [N060000113]MCL,ODISHA ,                                              | 05/2014          | 3,756.36                | 3,756.36         | 689.33                      | 03/2026               | 03/2026     | 0(O)                                       | 5/15                        |
| 74    | JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N060000114]MCL,ODISHA ,                             | 05/2014          | 337.66                  | 337.66           | 65.58                       | 03/2019               | 03/2021     | 24(O)                                      | 5/6                         |
| 75    | KULDA EXPN OC. (5.00 MTY) - [N060000115]MCL,ODISHA ,                                           | 06/2014          | 289.03                  | 289.03           | 28.56                       | 03/2018               | 03/2020     | 24(O)                                      | 3/5                         |
| 76    | GARJANBAHAL OCP - [N060000117]MCL,ODISHA ,                                                     | 11/2014          | 1,375.38                | 1,375.38         | 424.90                      | 03/2021               | 03/2021     | 0(O)                                       | 5/9                         |
| 77    | INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N060000167]MCL,ODISHA ,                            | 05/2018          | 2,434.75                | 2,434.75         | .00                         | 03/2027               | 03/2027     | 0(O)                                       | 0/0                         |
| 78    | HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N060000144]NLC,RAJASTHAN , Central Sector Projects    | 03/2015          | 522.45                  | 522.45           | 8.71                        | 09/2019               | 09/2019     | 0(O)                                       | 0/0                         |
| 79    | BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N060000145]NLC,RAJASTHAN , Central Sector Projects | 03/2015          | 513.63                  | 513.63           | 173.06                      | 12/2019               | 12/2019     | 0(O)                                       | 0/0                         |
| 80    | NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N060000095]NLC,TAMIL NADU ,                     | 06/2011          | 5,907.11                | 5,907.11         | 5,828.01                    | 12/2015               | 03/2019     | 39(O)                                      | 27/35                       |
| 81    | EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N060000138]NLC,TAMIL NADU , | 04/2013          | 1,458.17                | 709.06           | 399.03                      | 06/2015               | 09/2019     | 51(O)                                      | 5/7                         |
| 82    | SHANTIKHANI LONGWALL PROJ-SCCL - [N060000017]SCCL,TELANGANA ,                                  | 10/2006          | 249.03                  | 448.86           | 186.91                      | 03/2012               | 03/2024     | 144(O)                                     | 35/42                       |
| 83    | KAKATIYA LONGWALL - [N060000048]SCCL,TELANGANA ,                                               | 12/2008          | 453.63                  | 453.63           | 121.91                      | 12/2012               | -           | -                                          | 11/44                       |
| 84    | RAMAGUNDAM OC-II EXTENSION - [N060000078]SCCL,TELANGANA ,                                      | 12/2009          | 418.97                  | 489.62           | 477.74                      | 03/2012               | 03/2023     | 132(O)                                     | 0/2                         |
| 85    | RKP OCP PHASE-I - [N060000079]SCCL,TELANGANA ,                                                 | 03/2010          | 209.78                  | 209.78           | 154.21                      | 03/2015               | 03/2019     | 48(O)                                      | 30/31                       |
| 86    | MANUGURU OC-II EXTENSION PHASE-II - [N060000080]SCCL,TELANGANA ,                               | 03/2010          | 181.19                  | 181.19           | 159.87                      | 03/2012               | -           | -                                          | 5/6                         |
| 87    | KISTARAM OCP - [N060000089]SCCL,TELANGANA ,                                                    | 11/2010          | 242.29                  | 164.04           | 12.69                       | 03/2015               | 03/2021     | 72(O)                                      | 0/5                         |
| 88    | RCE OF INDARAM OCP(1.20 MTPA) - [N060000093]SCCL,TELANGANA ,                                   | 07/2011          | 162.76                  | 349.28           | 1.31                        | 03/2015               | 03/2021     | 72(O)                                      | 4/29                        |
| 89    | JALAGAM VENGALA RAO OCP-II - [N060000094]SCCL,TELANGANA ,                                      | 07/2011          | 447.06                  | 437.51           | 353.61                      | 03/2015               | 03/2021     | 72(O)                                      | 6/13                        |
| 90    | RG OC -III EXTENSION (PHASE -II) PROJECT - [N060000100]SCCL,TELANGANA ,                        | 06/2012          | 365.01                  | 365.01           | 204.26                      | 06/2015               | 03/2019     | 45(O)                                      | 35/36                       |
| 91    | KALYANIKHANI OPENCAST PROJECT - [N060000101]SCCL,TELANGANA ,                                   | 07/2012          | 417.33                  | 384.32           | 146.45                      | 07/2016               | 03/2020     | 44(O)                                      | 21/28                       |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                               |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|---------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                       | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                             | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 92    | RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,                                                      | 11/2012          | 430.45 -                | 415.37           | 160.45                      | 03/2016 -             | 03/2019     | 36(O) -                                    | 37/39                       |
| 93    | KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA ,                                                | 05/2015          | 397.09 -                | 442.42           | 79.96                       | 03/2019 -             | 03/2019     | 0(O) -                                     | 10/18                       |
| 94    | KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects                              | 10/2015          | 426.79 -                | 426.79           | .00                         | 03/2018 -             | 03/2019     | 12(O) -                                    | 0/9                         |
| 95    | KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL,TELANGANA ,                                                  | 12/2015          | 477.65 -                | 477.65           | .00                         | 03/2020 -             | 03/2020     | 0(O) -                                     | 1/17                        |
| 96    | KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA ,                                      | 03/2017          | 413.84 -                | 413.84           | .00                         | 03/2019 -             | 03/2019     | 0(O) -                                     | 0/11                        |
| 97    | KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA 6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH ,            | 06/2011          | 1,131.28 -              | 1,131.28         | 711.45                      | 03/2018 -             | 03/2019     | 12(O) -                                    | 10/10                       |
| 98    | NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,                          | 07/2016          | 17,237.00 -             | 17,237.80        | 4,026.50                    | 11/2021 -             | 11/2021     | 0(O) -                                     | 0/0                         |
| 99    | JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL,WEST BENGAL ,                                                  | 11/2015          | 602.86 -                | 602.86           | 298.21                      | 03/2022 -             | 03/2022     | 0(O) -                                     | 8/13                        |
| 100   | SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,                                            | 08/2012          | 1,055.05 -              | 1,055.05         | 383.30                      | 03/2018 -             | 03/2020     | 24(O) -                                    | 11/16                       |
| 101   | RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL ,                                                           | 08/2009          | 2,661.73 -              | 2,661.73         | 215.14                      | 08/2019 -             | -           | -                                          | 0/19                        |
| 102   | SIDULI MINE (OC AND UG) - [N06000165]ECL,WEST BENGAL ,                                                        | 05/2018          | 535.18 -                | 535.18           | .00                         | 03/2026 -             | 03/2026     | 0(O) -                                     | 0/21                        |
|       | Total                                                                                                         |                  | 96,954.88 -             | 96,426.38        | 28,901.32                   |                       |             |                                            | 488/990                     |
|       |                                                                                                               |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>FERTILISERS</u>                                                                                            |                  |                         |                  |                             |                       |             |                                            |                             |
| 103   | GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA ,          | 01/2018          | 215.92 -                | 215.92           | 27.51                       | 11/2019 -             | 11/2019     | 0(O) -                                     | 0/2                         |
| 104   | NEW SEWAGE TREATMENT PLANT PACKAGE RCF TROMBAY - [N08000009]RCF,MAHARASHTRA ,                                 | 10/2014          | 197.79 209.44           | 209.44           | 140.10                      | 11/2016 04/2019       | 04/2019     | 29(O) 0(R)                                 | 1/13                        |
| 105   | GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF,MAHARASHTRA ,        | 02/2016          | 482.85 482.85           | 482.85           | 413.00                      | 12/2017 01/2019       | 01/2019     | 13(O) 0(R)                                 | 0/1                         |
| 106   | GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA , | 04/2018          | 426.72 -                | 426.72           | 50.89                       | 04/2020 -             | 04/2020     | 0(O) -                                     | 1/14                        |
| 107   | GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB ,          | 01/2018          | 218.83 -                | 218.83           | 26.47                       | 11/2019 -             | 11/2019     | 0(O) -                                     | 0/2                         |
| 108   | GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB ,            | 01/2018          | 239.81 -                | 239.81           | 32.18                       | 11/2019 -             | 11/2019     | 0(O) -                                     | 0/2                         |
|       | Total                                                                                                         |                  | 1,781.92 -              | 1,793.57         | 690.15                      |                       |             |                                            | 2/34                        |
|       |                                                                                                               |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>MINES</u>                                                                                                  |                  |                         |                  |                             |                       |             |                                            |                             |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                          |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|----------------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                                  | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                                        | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 109   | 5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,                                                                                | 12/2014          | 5,540.00<br>5,540.00    | 5,540.00         | 96.98                       | 04/2021<br>04/2021    | 04/2021     | 0(O)<br>0(R)                               | 3/3                         |
| 110   | UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA ,                                                                                                     | 05/2016          | 534.00<br>534.00        | 534.00           | 302.60                      | 01/2020<br>01/2020    | 01/2020     | 0(O)<br>0(R)                               | 1/2                         |
| 111   | CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA , Central Sector Projects | 12/2015          | 355.00<br>-             | 355.00           | 31.92                       | 11/2020<br>-          | 11/2020     | 0(O)<br>-                                  | 2/2                         |
| 112   | SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA , Central Sector Projects | 11/2017          | 483.00<br>483.00        | 483.00           | .00                         | 04/2021<br>04/2021    | 04/2021     | 0(O)<br>0(R)                               | 1/1                         |
| 113   | 25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU ,                                                                      | 09/2017          | 166.62<br>166.62        | 166.62           | 125.00                      | 06/2019<br>06/2019    | 06/2019     | 0(O)<br>0(R)                               | 0/1                         |
|       | Total                                                                                                                                                    |                  | 7,078.62<br>-           | 7,078.62         | 556.50                      |                       |             |                                            | 7/9                         |
|       |                                                                                                                                                          |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>STEEL</u>                                                                                                                                             |                  |                         |                  |                             |                       |             |                                            |                             |
| 114   | REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH ,                                                                                | 12/2009          | 343.00<br>-             | 488.40           | 239.65                      | 10/2016<br>-          | -           | -                                          | 1/2                         |
| 115   | COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,                                                                                                   | 12/2011          | 2,858.00<br>-           | 2,500.00         | 1,053.76                    | 12/2017<br>-          | 09/2019     | 21(O)<br>-                                 | 4/6                         |
| 116   | CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH ,                                                                                                 | 08/2015          | 320.66<br>-             | 320.66           | 125.36                      | 08/2018<br>-          | 02/2019     | 6(O)<br>-                                  | 2/4                         |
| 117   | ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH ,                                                                            | 07/2015          | 465.85<br>-             | 465.85           | 276.25                      | 07/2018<br>-          | 01/2019     | 6(O)<br>-                                  | 2/4                         |
| 118   | DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH ,                                                     | 04/2014          | 188.93<br>-             | 188.93           | 124.84                      | 04/2015<br>-          | -           | -                                          | 4/5                         |
| 119   | NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,                                                                                              | 01/2010          | 15,525.00<br>-          | 15,525.00        | 14,566.77                   | 05/2015<br>06/2019    | 06/2019     | 49(O)<br>0(R)                              | 62/86                       |
| 120   | 2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]NMDC,CHHATISGARH ,                                                                                          | 11/2015          | 818.00<br>-             | 818.00           | 31.60                       | 06/2020<br>-          | 06/2020     | 0(O)<br>-                                  | 5/12                        |
| 121   | NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,                                                                                     | 03/2015          | 1,034.01<br>-           | 1,034.01         | 367.64                      | 10/2017<br>-          | 06/2020     | 32(O)<br>-                                 | 0/2                         |
| 122   | MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND ,                                                             | 05/2015          | 1,154.18<br>-           | 1,154.18         | 862.45                      | 12/2017<br>-          | 06/2019     | 18(O)<br>-                                 | 1/2                         |
| 123   | EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND ,                                  | 02/2014          | 4,749.00<br>-           | 4,749.00         | 108.28                      | 09/2017<br>-          | -           | -                                          | 0/0                         |
| 124   | REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,                                                                                | 11/2016          | 262.87<br>-             | 262.87           | 77.06                       | 06/2019<br>-          | 06/2020     | 12(O)<br>-                                 | 0/1                         |
| 125   | INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA ,                                                                                     | 04/2015          | 3,127.30<br>-           | 3,127.30         | 2,527.38                    | 04/2018<br>-          | 05/2019     | 13(O)<br>-                                 | 3/3                         |
| 126   | FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH ,                                                                                                     | 04/2014          | 1,682.85<br>-           | 1,682.85         | 852.10                      | 09/2018<br>-          | 03/2019     | 6(O)<br>-                                  | 3/5                         |
|       | Total                                                                                                                                                    |                  | 32,529.65<br>-          | 32,317.05        | 21,213.14                   |                       |             |                                            | 87/132                      |
|       |                                                                                                                                                          |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>PETROLEUM</u>                                                                                                                                         |                  |                         |                  |                             |                       |             |                                            |                             |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                               |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                       | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                             | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 127   | VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,                                                      | 07/2016          | 20,928.00 -             | 20,928.00        | 2,757.64                    | 07/2020 -             | 07/2020     | 0(O) -                                     | 72/111                      |
| 128   | VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]HPCL,ANDHRA PRADESH ,                        | 09/2016          | 407.00 -                | 407.00           | 262.64                      | 09/2019 -             | 09/2019     | 0(O) -                                     | 19/27                       |
| 129   | KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,                                                 | 03/2016          | 34,012.00 -             | 34,012.00        | 1,647.21                    | 06/2020 08/2021       | 08/2021     | 14(O) 0(R)                                 | 0/20                        |
| 130   | ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH ,    | 01/2015          | 342.00 -                | 342.00           | .00                         | 03/2021 -             | 03/2021     | 0(O) -                                     | 0/0                         |
| 131   | REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH ,                                          | 07/2014          | 247.00 -                | 247.00           | .00                         | 03/2021 -             | 03/2021     | 0(O) -                                     | 0/0                         |
| 132   | FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003 NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH ,                                 | 04/2017          | 420.76 207.80           | 207.80           | 32.71                       | 09/2018 02/2019       | 02/2019     | 5(O) 0(R)                                  | 0/5                         |
| 133   | CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL AP - [N16000302]IOCL,ANDHRA PRADESH ,                                              | 08/2017          | 384.58 -                | 384.58           | 41.38                       | 04/2021 -             | 04/2021     | 0(O) -                                     | 0/0                         |
| 134   | CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH ,                    | 08/2018          | 466.00 -                | 466.00           | 1.53                        | 04/2021 -             | 07/2021     | 3(O) -                                     | 0/0                         |
| 135   | REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH ,                                                  | 04/2018          | 355.00 -                | 355.00           | .00                         | 04/2022 -             | 04/2022     | 0(O) -                                     | 0/0                         |
| 136   | RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]IOCL,ARUNACHAL PRADESH ,                                   | 01/2016          | 247.52 -                | 247.52           | 144.38                      | 02/2019 -             | 01/2019     | -1(O) -                                    | 3/10                        |
| 137   | ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM ,                                                                   | 03/2009          | 2,465.15 -              | 2,378.86         | 2,107.69                    | 03/2013 03/2019       | 03/2019     | 72(O) 0(R)                                 | 6/15                        |
| 138   | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM ,                              | 06/2010          | 202.94 341.70           | 330.35           | 81.98                       | 01/2014 11/2019       | 11/2019     | 70(O) 0(R)                                 | 6/7                         |
| 139   | DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) CACHAR ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,      | 06/2016          | 423.00 -                | 423.00           | 217.07                      | 08/2019 -             | 08/2019     | 0(O) -                                     | 4/13                        |
| 140   | INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM ,                                                               | 02/2016          | 2,582.00 -              | 2,582.00         | 1,281.75                    | 11/2019 -             | 11/2019     | 0(O) -                                     | 12/17                       |
| 141   | PIPELINE NETWORK PROJECT GELEKI ASSAM - [N16000278]ONGC,ASSAM ,                                                               | 07/2016          | 249.85 249.85           | 244.70           | 101.71                      | 05/2020 05/2020       | 05/2020     | 0(O) 0(R)                                  | 0/5                         |
| 142   | CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM ,                                                   | 07/2011          | 350.00 -                | 350.00           | 2.06                        | 01/2019 -             | 09/2019     | 8(O) -                                     | 0/0                         |
| 143   | BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]IOCL,ASSAM ,                                                                | 05/2018          | 1,222.00 -              | 1,222.00         | 287.90                      | 09/2019 -             | 09/2019     | 0(O) -                                     | 6/7                         |
| 144   | DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM , | 01/2018          | 543.91 -                | 543.91           | 1.65                        | 02/2020 -             | 02/2020     | 0(O) -                                     | 1/14                        |
| 145   | BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM ,                                                                  | 08/2018          | 557.00 -                | 557.00           | 71.41                       | 02/2020 -             | 02/2020     | 0(O) -                                     | 0/0                         |
| 146   | UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM ,               | 09/2012          | 871.35 -                | 1,200.00         | 565.63                      | 03/2015 -             | -           | -                                          | 0/5                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                             |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|---------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                     | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                           | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 147   | FUEL QUALITY UPGRADE (DHD/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR ,                                                    | 07/2015          | 822.66                  | 822.66           | 868.92                      | 11/2018               | 03/2019     | 4(O)                                       | 7/8                         |
| 148   | BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]IOCL,BIHAR ,                                                          | 05/2016          | 664.00                  | 664.00           | 455.62                      | 12/2020               | 02/2020     | -10(O)                                     | 4/4                         |
| 149   | MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL,BIHAR ,                                                                                      | 09/2015          | 324.00                  | 324.00           | 96.21                       | 06/2020               | 06/2020     | 0(O)                                       | 3/3                         |
| 150   | LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR ,                                                                                           | 05/2018          | 206.50                  | 206.50           | .00                         | 03/2021               | 03/2021     | 0(O)                                       | 7/26                        |
| 151   | DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR ,                         | 12/2017          | 199.36                  | 199.36           | .00                         | 10/2020               | 10/2020     | 0(O)                                       | 0/0                         |
| 152   | CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR ,                                                                         | 10/2017          | 359.25                  | 359.25           | 38.05                       | 10/2022               | 10/2022     | 0(O)                                       | 0/0                         |
| 153   | INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR ,                                                                 | 07/2018          | 189.00                  | 189.00           | 4.04                        | 01/2021               | 01/2021     | 0(O)                                       | 0/0                         |
| 154   | CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI BIHAR - [N16000344]IOCL,BIHAR ,                                                         | 04/2018          | 522.00                  | 522.00           | 2.56                        | 03/2021               | 03/2021     | 0(O)                                       | 0/0                         |
| 155   | CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL,CHHATISGARH ,          | 12/2016          | 300.00                  | 300.00           | .00                         | 04/2021               | 04/2021     | 0(O)                                       | 0/0                         |
| 156   | DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI ,                                                                                  | 08/2014          | 6,086.08                | 5,842.31         | 4,513.89                    | 05/2019               | 10/2019     | 5(O)                                       | 0/14                        |
| 157   | GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT ,                                                                                     | 05/2015          | 1,671.22                | 567.22           | 449.95                      | 11/2019               | 11/2019     | 0(O)                                       | 0/5                         |
| 158   | CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,                                                                    | 04/2016          | 327.78                  | 200.00           | 116.19                      | 04/2018               | 03/2019     | 11(O)                                      | 18/20                       |
| 159   | REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT ,                                                                                  | 02/2017          | 1,162.56                | 1,162.56         | 294.16                      | 03/2026               | 03/2026     | 0(O)                                       | 0/10                        |
| 160   | INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL,GUJARAT , Central Sector Projects | 09/2016          | 208.35                  | 208.35           | 67.71                       | 07/2020               | 07/2020     | 0(O)                                       | 0/0                         |
| 161   | REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL,GUJARAT , Central Sector Projects                                                       | 10/2014          | 279.00                  | 279.00           | 200.05                      | 08/2018               | -           | -                                          | 0/0                         |
| 162   | CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]IOCL,GUJARAT ,                           | 08/2017          | 1,342.00                | 1,342.00         | 3.90                        | 08/2020               | 08/2020     | 0(O)                                       | 1/1                         |
| 163   | BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]IOCL,GUJARAT ,                                                                               | 03/2018          | 3,380.00                | 3,380.00         | 1,246.09                    | 09/2019               | 09/2019     | 0(O)                                       | 0/9                         |
| 164   | CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT ,                    | 10/2017          | 906.00                  | 906.00           | 13.52                       | 02/2020               | 02/2020     | 0(O)                                       | 0/0                         |
| 165   | AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA GUJARAT - [N16000336]IOCL,GUJARAT ,                               | 03/2018          | 588.20                  | 588.20           | .00                         | -                     | -           | -                                          | 3/17                        |
| 166   | CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL,HARYANA ,                                    | 11/2017          | 255.00                  | 255.00           | 15.68                       | 11/2020               | 11/2020     | 0(O)                                       | 0/46                        |
| 167   | CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA ,                                           | 04/2018          | 206.63                  | 206.63           | .52                         | 02/2020               | 02/2020     | 0(O)                                       | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                     |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                             | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                   | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 168   | BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA ,                                                                       | 12/2017          | 3,529.00<br>-           | 3,529.00         | 952.69                      | 07/2019<br>-          | 07/2019     | 0(O)<br>-                                  | 0/9                         |
| 169   | NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA ,                                                            | 08/2018          | 1,636.00<br>-           | 1,636.00         | 128.78                      | 08/2020<br>-          | 08/2020     | 0(O)<br>-                                  | 0/0                         |
| 170   | CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA HP - [N16000226]IOCL,HIMACHAL PRADESH ,                                         | 02/2016          | 356.00<br>-             | 356.00           | 205.41                      | 05/2019<br>-          | 01/2019     | -4(O)<br>-                                 | 4/13                        |
| 171   | BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL,HIMACHAL PRADESH ,                                                                | 02/2016          | 151.00<br>-             | 151.00           | 112.58                      | 09/2019<br>-          | 02/2019     | -7(O)<br>-                                 | 3/3                         |
| 172   | RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND ,                                       | 04/2011          | 191.96<br>-             | 191.96           | 176.28                      | 05/2015<br>-          | -           | -                                          | 8/12                        |
| 173   | DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,                                                                | 12/2015          | 658.62<br>910.23        | 910.23           | 109.60                      | 03/2023<br>03/2022    | 03/2022     | -12(O)<br>0(R)                             | 0/10                        |
| 174   | 120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND ,                                                        | 06/2017          | 161.50<br>-             | 161.50           | 17.78                       | 06/2020<br>-          | 06/2020     | 0(O)<br>-                                  | 0/0                         |
| 175   | CITY GAS DISTRIBUTION (CGD) NETWORK RANCHI - [N16000329]GAIL,JHARKHAND ,                                                            | 10/2017          | 226.45<br>-             | 226.45           | 25.11                       | 10/2022<br>-          | 10/2022     | 0(O)<br>-                                  | 6/9                         |
| 176   | CITY GAS DISTRIBUTION (CGD) NETWORK JAMSHEDPUR - [N16000330]GAIL,JHARKHAND ,                                                        | 10/2017          | 221.45<br>-             | 221.45           | 23.92                       | 10/2022<br>-          | 10/2022     | 0(O)<br>-                                  | 0/0                         |
| 177   | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA ,                                                         | 01/2006          | 993.00<br>-             | 1,693.00         | 1,549.85                    | 01/2012<br>-          | -           | -                                          | 0/0                         |
| 178   | GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA , Central Sector Projects                                            | 02/2015          | 749.00<br>-             | 749.00           | 733.62                      | 02/2020<br>-          | 02/2020     | 0(O)<br>-                                  | 0/0                         |
| 179   | CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA ,                         | 05/2015          | 224.00<br>207.00        | 207.25           | 99.99                       | 04/2019<br>-          | 04/2019     | 0(O)<br>-                                  | 6/8                         |
| 180   | RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA ,                                           | 10/2015          | 135.00<br>171.00        | 170.70           | 124.25                      | 03/2019<br>-          | 03/2019     | 0(O)<br>-                                  | 5/11                        |
| 181   | BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,                                                                           | 09/2016          | 1,810.00<br>1,810.00    | 1,810.00         | 130.79                      | 12/2019<br>-          | 12/2019     | 0(O)<br>-                                  | 7/9                         |
| 182   | SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA , Central Sector Projects                                       | 11/2017          | 581.00<br>-             | 581.00           | .00                         | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 183   | LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,                                                                                    | 10/2015          | 607.06<br>-             | 714.25           | 352.32                      | 10/2017<br>-          | 03/2019     | 17(O)<br>-                                 | 39/52                       |
| 184   | PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA ,                                      | 11/2014          | 4,588.29<br>5,245.96    | 5,245.96         | 2,543.09                    | 08/2018<br>11/2019    | 11/2019     | 15(O)<br>0(R)                              | 0/20                        |
| 185   | MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA ,                                   | 02/2016          | 3,313.00<br>3,288.96    | 3,288.96         | 404.03                      | 02/2020<br>10/2020    | 10/2020     | 8(O)<br>0(R)                               | 0/20                        |
| 186   | KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA ,                                                                         | 12/2015          | 1,112.00<br>-           | 1,112.00         | 108.79                      | 06/2019<br>-          | 06/2019     | 0(O)<br>-                                  | 0/0                         |
| 187   | PROVISION OF 2ND SPUR FOR TWL GANTRY TWD FACILITY FOR MS AND HSD ADDITIONAL TANKS FOR MS HSD AND - [N16000304]IOCL,MADHYA PRADESH , | 08/2017          | 236.00<br>-             | 236.00           | 11.66                       | 06/2020<br>-          | 10/2020     | 4(O)<br>-                                  | 0/0                         |
| 188   | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,                             | 03/2011          | 861.79<br>1,577.15      | 1,577.15         | 1,195.62                    | 05/2013<br>03/2019    | 03/2019     | 70(O)<br>0(R)                              | 1/8                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                        |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|--------------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                                      | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 189   | INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA ,                                                                                 | 12/2011          | 2,059.63<br>2,665.65    | 2,665.65         | 1,842.42                    | 03/2015<br>12/2019    | 12/2019     | 57(O)<br>0(R)                              | 0/17                        |
| 190   | MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA ,                                                                        | 11/2014          | 6,068.80<br>6,068.80    | 5,296.93         | 4,576.40                    | 04/2019<br>03/2019    | 03/2019     | -1(O)<br>0(R)                              | 0/9                         |
| 191   | NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA ,                                                    | 08/2015          | 2,818.88<br>-           | 2,818.88         | 1,724.53                    | 03/2019<br>05/2020    | 05/2020     | 14(O)<br>0(R)                              | 0/5                         |
| 192   | ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects | 01/2015          | 4,619.94<br>4,619.94    | 4,619.94         | 3,951.60                    | 12/2017<br>03/2020    | 03/2020     | 27(O)<br>0(R)                              | 4/5                         |
| 193   | LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects                               | 12/2015          | 3,190.69<br>-           | 3,247.19         | 2,110.87                    | 04/2018<br>05/2019    | 05/2019     | 13(O)<br>0(R)                              | 0/10                        |
| 194   | KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,                                                                                     | 05/2016          | 1,945.00<br>-           | 1,945.00         | 514.20                      | 08/2021<br>-          | 08/2021     | 0(O)<br>-                                  | 3/4                         |
| 195   | INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA ,                               | 02/2016          | 554.00<br>-             | 554.00           | 158.76                      | 02/2020<br>-          | 02/2020     | 0(O)<br>-                                  | 0/10                        |
| 196   | MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA ,                                                                                        | 04/2013          | 449.58<br>-             | 449.58           | 118.17                      | 12/2019<br>-          | 12/2019     | 0(O)<br>-                                  | 0/0                         |
| 197   | ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA ,                      | 05/2016          | 212.00<br>-             | 212.00           | 14.11                       | 01/2021<br>-          | 04/2021     | 3(O)<br>-                                  | 0/0                         |
| 198   | ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,                    | 05/2016          | 348.00<br>-             | 348.00           | 9.20                        | 01/2021<br>-          | 10/2021     | 9(O)<br>-                                  | 0/0                         |
| 199   | ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA ,                 | 05/2016          | 261.00<br>-             | 261.00           | 8.48                        | 01/2021<br>-          | 01/2021     | 0(O)<br>-                                  | 0/0                         |
| 200   | MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA , Central Sector Projects                                                              | 09/2015          | 4,199.00<br>-           | 4,199.00         | 194.97                      | 03/2020<br>-          | 07/2019     | -8(O)<br>-                                 | 0/0                         |
| 201   | NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]ONGC,MAHARASHTRA , Central Sector Projects                                       | 01/2017          | 474.15<br>474.15        | 474.15           | 299.26                      | 05/2019<br>05/2019    | 05/2019     | 0(O)<br>0(R)                               | 0/5                         |
| 202   | DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA , Central Sector Projects                                                                     | 02/2017          | 546.15<br>546.15        | 546.15           | 226.78                      | 11/2019<br>11/2019    | 11/2019     | 0(O)<br>0(R)                               | 0/5                         |
| 203   | DEVELOPMENT OF BSE-11 BLOCK - [N16000293]ONGC,MAHARASHTRA , Central Sector Projects                                                                    | 02/2017          | 511.30<br>511.30        | 511.30           | 197.90                      | 11/2019<br>11/2019    | 11/2019     | 0(O)<br>0(R)                               | 0/5                         |
| 204   | 4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]ONGC,MAHARASHTRA , Central Sector Projects                                                             | 02/2017          | 968.61<br>968.61        | 968.61           | 601.19                      | 11/2019<br>11/2019    | 11/2019     | 0(O)<br>0(R)                               | 0/5                         |
| 205   | DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA ,                                                       | 02/2017          | 4,006.83<br>4,006.83    | 4,006.83         | 1,651.58                    | 05/2021<br>05/2021    | 05/2021     | 0(O)<br>0(R)                               | 0/15                        |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                   |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                           | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                 | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 206   | PUNE POL STORAGE DEPOT - [N16000313]BPCL,MAHARASHTRA ,                                                                            | 08/2016          | 282.64 -                | 282.64           | 63.91                       | 08/2020 -             | 08/2020     | 0(O) -                                     | 0/15                        |
| 207   | 180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD) MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA ,                                     | 06/2017          | 249.26 -                | 249.26           | 58.33                       | 06/2020 -             | 06/2020     | 0(O) -                                     | 0/0                         |
| 208   | PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]ONGC,MAHARASHTRA ,                                                         | 04/2018          | 766.37 -                | 766.37           | .00                         | 12/2019 -             | 12/2019     | 0(O) -                                     | 4/5                         |
| 209   | PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE ,                                                           | 03/2015          | 3,957.00<br>3,561.00    | 3,397.00         | 2,382.96                    | 12/2018 -             | 03/2019     | 3(O) -                                     | 35/39                       |
| 210   | CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE ,                                                   | 06/2007          | 736.65 -                | 571.47           | 543.05                      | 09/2011 -             | -           | -                                          | 0/3                         |
| 211   | PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE ,                                                                   | 08/2009          | 1,793.00 -              | 1,793.00         | 1,788.86                    | 12/2016 -             | -           | -                                          | 8/8                         |
| 212   | URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE ,                                                                | 12/2009          | 309.81<br>723.40        | 723.40           | 586.10                      | 10/2014<br>02/2019    | 02/2019     | 52(O)<br>0(R)                              | 32/40                       |
| 213   | SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE ,             | 07/2011          | 352.56 -                | 438.84           | 196.39                      | 03/2017<br>06/2019    | 06/2019     | 27(O)<br>0(R)                              | 2/15                        |
| 214   | AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE , | 01/2015          | 1,823.00 -              | 1,823.00         | 579.41                      | 12/2020 -             | 12/2020     | 0(O) -                                     | 3/4                         |
| 215   | PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,                                                                        | 01/2015          | 2,321.00<br>3,338.00    | 3,338.00         | 941.59                      | 12/2020 -             | 08/2020     | -4(O) -                                    | 4/4                         |
| 216   | JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE ,       | 02/2015          | 890.00 -                | 887.00           | 551.16                      | 10/2019 -             | 03/2019     | -7(O) -                                    | 5/5                         |
| 217   | PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,                                                                       | 01/2015          | 690.00 -                | 690.00           | 191.48                      | 07/2018<br>10/2020    | 10/2020     | 27(O)<br>0(R)                              | 21/36                       |
| 218   | MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE ,                                  | 09/2016          | 1,879.00 -              | 1,879.00         | 1,015.35                    | 06/2020 -             | 06/2020     | 0(O) -                                     | 14/24                       |
| 219   | RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB HARYANA) - [N16000242]HPCL,MULTI STATE ,                       | 11/2016          | 230.00 -                | 230.00           | 114.14                      | 02/2019 -             | 02/2019     | 0(O) -                                     | 11/13                       |
| 220   | PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,                                                | 05/2016          | 406.00 -                | 406.00           | 23.61                       | 10/2020 -             | 10/2020     | 0(O) -                                     | 6/12                        |
| 221   | AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,                             | 09/2016          | 571.66 -                | 571.66           | 42.33                       | 12/2019 -             | 12/2019     | 0(O) -                                     | 6/22                        |
| 222   | LAYING OF VIJAIIPUR-AURAIYA PIPELINE SECTION OF VIJAIIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,        | 07/2015          | 2,881.40 -              | 2,000.00         | 1,090.43                    | 12/2019<br>12/2020    | 12/2019     | 0(O)<br>-12(R)                             | 15/24                       |
| 223   | DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,                                                                   | 03/2017          | 2,433.00 -              | 2,433.00         | 956.29                      | 12/2020 -             | 12/2020     | 0(O) -                                     | 14/24                       |
| 224   | BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,                                                                     | 03/2017          | 3,437.00 -              | 3,437.00         | 1,006.30                    | 12/2020 -             | 12/2020     | 0(O) -                                     | 14/24                       |
| 225   | KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE ,<br>Central Sector Projects                  | 06/2009          | 2,915.00<br>3,030.00    | 2,915.00         | 2,009.30                    | 12/2012<br>02/2019    | 06/2019     | 78(O)<br>4(R)                              | 16/42                       |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                      |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|--------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                              | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                    | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 226   | EXTENSION OF VISAKH-VIJAYAWADA- SECUNDERABAD PIPELINE (VVSP) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE , | 09/2017          | 2,677.00                | 2,677.00         | 49.88                       | 03/2021               | 03/2021     | 0(O)                                       | 3/26                        |
| 227   | 50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE ,                                                                        | 11/2015          | 500.00                  | 500.00           | .00                         | 06/2017               | -           | -                                          | 0/0                         |
| 228   | BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE ,                                                                            | 06/2018          | 3,308.00                | 3,308.00         | 2.63                        | 12/2021               | 12/2021     | 0(O)                                       | 0/0                         |
| 229   | POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA ,                                                                   | 03/2014          | 3,150.00                | 3,150.00         | 2,494.51                    | 09/2017               | 12/2018     | 15(O)                                      | 5/6                         |
| 230   | DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,                                                                             | 03/2017          | 1,933.00                | 1,933.00         | 814.01                      | 12/2020               | 12/2020     | 0(O)                                       | 16/24                       |
| 231   | INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA ,                                        | 05/2016          | 429.00                  | 429.00           | 291.90                      | 01/2019               | 01/2019     | 0(O)                                       | 6/6                         |
| 232   | LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects                                                            | 12/2016          | 161.59                  | 161.59           | 33.93                       | 12/2019               | 12/2019     | 0(O)                                       | 17/26                       |
| 233   | CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA , Central Sector Projects                                  | 07/2017          | 243.53                  | 243.53           | 35.47                       | 07/2022               | 07/2022     | 0(O)                                       | 0/0                         |
| 234   | CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA ,                                                | 08/2017          | 315.00                  | 315.00           | 2.87                        | 12/2021               | 12/2021     | 0(O)                                       | 0/2                         |
| 235   | CITY GAS DISTRIBUTION (CGD) NETWORK CUTTACK - [N16000328]GAIL,ODISHA ,                                                               | 07/2017          | 181.20                  | 181.20           | 15.72                       | 07/2022               | 07/2022     | 0(O)                                       | 0/0                         |
| 236   | ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA ,                                                                        | 04/2018          | 4,807.08                | 4,807.08         | 24.09                       | 07/2021               | 07/2021     | 0(O)                                       | 0/0                         |
| 237   | 2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]BPCL,ODISHA ,                                                                        | 08/2017          | 750.00                  | 750.00           | 24.43                       | 12/2020               | 12/2020     | 0(O)                                       | 0/14                        |
| 238   | PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA ,                                                                        | 10/2018          | 1,297.50                | 1,297.50         | .00                         | 10/2021               | 10/2021     | 0(O)                                       | 0/0                         |
| 239   | 50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN ,                                                       | 11/2011          | 310.00                  | 370.00           | 17.84                       | 03/2013               | -           | -                                          | 0/24                        |
| 240   | LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN ,                                                                                 | 03/2018          | 229.80                  | 229.80           | 69.04                       | -                     | -           | -                                          | 3/26                        |
| 241   | ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU ,                                                                    | 05/2013          | 711.00                  | 711.00           | 11.12                       | 06/2020               | 06/2020     | 0(O)                                       | 0/0                         |
| 242   | RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU ,                                                                             | 03/2013          | 3,110.36                | 3,110.36         | 2,915.42                    | 11/2015               | -           | -                                          | 52/52                       |
| 243   | IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU ,                                                                       | 11/2012          | 678.00                  | 678.00           | 5.12                        | 02/2017               | -           | -                                          | 0/0                         |
| 244   | Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU ,                                           | 11/2015          | 390.52                  | 390.52           | 174.22                      | 03/2019               | 04/2019     | 1(O)                                       | 0/5                         |
| 245   | ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU ,                    | 05/2016          | 4,497.00                | 4,497.00         | 349.40                      | 12/2018               | 12/2020     | 24(O)                                      | 4/4                         |
| 246   | AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU , Central Sector Projects                                                         | 12/2016          | 228.00                  | 228.00           | 1.84                        | 06/2020               | 06/2020     | 0(O)                                       | 4/4                         |
| 247   | BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU ,                                                                                        | 09/2017          | 1,858.00                | 1,858.00         | 620.25                      | 12/2019               | 12/2019     | 0(O)                                       | 0/0                         |
| 248   | RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU ,                                                                              | 08/2017          | 421.00                  | 421.00           | 19.68                       | 08/2020               | 08/2020     | 0(O)                                       | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                        |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|----------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                      | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 249   | CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR TAMIL NADU - [N16000305]IOCL,TAMIL NADU ,                                                 | 12/2017          | 466.43 -                | 466.43           | 1.18                        | 10/2020 -             | 08/2021     | 10(O) -                                    | 0/0                         |
| 250   | AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]GAIL,UTTAR PRADESH ,                                                                     | 07/2015          | 1,427.94 -              | 800.00           | 603.92                      | 12/2018 -             | 03/2019     | 3(O) -                                     | 17/20                       |
| 251   | CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH , Central Sector Projects                                 | 04/2017          | 287.49 -                | 287.49           | 102.07                      | 04/2022 -             | 04/2022     | 0(O) -                                     | 28/33                       |
| 252   | REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH ,                  | 08/2017          | 318.80 -                | 318.80           | 13.93                       | 08/2021 -             | 11/2021     | 3(O) -                                     | 0/0                         |
| 253   | BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL,UTTAR PRADESH ,                                                                    | 01/2018          | 666.64 -                | 666.64           | 223.54                      | 09/2019 -             | 09/2019     | 0(O) -                                     | 0/6                         |
| 254   | INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH ,     | 08/2017          | 255.40 -                | 255.40           | .06                         | 08/2020 -             | 08/2020     | 0(O) -                                     | 0/0                         |
| 255   | AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH , | 03/2018          | 676.00 -                | 676.00           | 4.83                        | 12/2021 -             | 12/2021     | 0(O) -                                     | 2/2                         |
| 256   | SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects                                                          | 02/2017          | 160.10 -                | 160.10           | 27.35                       | 02/2020 -             | 02/2020     | 0(O) -                                     | 18/26                       |
| 257   | DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL ,                                        | 03/2014          | 3,076.00<br>4,190.00    | 4,190.00         | 3,224.62                    | 09/2017<br>06/2018    | 03/2019     | 18(O)<br>9(R)                              | 6/7                         |
| 258   | HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL ,                                                                             | 03/2015          | 694.00<br>1,097.54      | 694.00           | 530.79                      | 10/2018<br>06/2019    | 06/2019     | 8(O)<br>0(R)                               | 0/15                        |
| 259   | HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL ,                                                                        | 04/2016          | 1,021.00 -              | 1,021.00         | 4.45                        | 12/2020 -             | 12/2020     | 0(O) -                                     | 0/0                         |
| 260   | DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL ,                                                                       | 03/2017          | 1,740.00 -              | 1,740.00         | 22.96                       | 12/2020 -             | 12/2020     | 0(O) -                                     | 11/24                       |
| 261   | KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL ,                                                                           | 04/2017          | 163.02 -                | 163.02           | 32.69                       | 04/2020 -             | 04/2020     | 0(O) -                                     | 17/26                       |
| 262   | BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]IOCL,WEST BENGAL ,                                                             | 05/2018          | 2,934.40 -              | 2,934.40         | 843.32                      | 09/2019 -             | 09/2019     | 0(O) -                                     | 0/11                        |
| 263   | 30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL,WEST BENGAL ,   | 03/2018          | 3,712.00 -              | 3,712.00         | 6.28                        | 09/2022 -             | 06/2021     | -15(O) -                                   | 1/1                         |
|       | Total                                                                                                                                  |                  | 2,21,562.48 -           | 2,23,009.33      | 72,956.33                   |                       |             |                                            | 678/1447                    |
|       |                                                                                                                                        |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>POWER</u>                                                                                                                           |                  |                         |                  |                             |                       |             |                                            |                             |
| 264   | SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,                                                          | 09/2003          | 6,285.33 -              | 19,496.34        | 10,421.62                   | 09/2010 -             | -           | -                                          | 0/0                         |
| 265   | KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH ,                                                          | 12/2004          | 2,496.90<br>6,179.96    | 6,179.96         | 6,881.48                    | 12/2009<br>03/2019    | 03/2019     | 111(O)<br>0(R)                             | 30/30                       |
| 266   | BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM ,                                                                             | 01/2008          | 4,375.35<br>8,150.00    | 8,150.00         | 7,220.84                    | 09/2011<br>06/2018    | 01/2019     | 88(O)<br>7(R)                              | 36/37                       |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                        |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|--------------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                                      | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 267   | BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR ,                                                                                                      | 02/2005          | 8,692.97<br>15,095.67   | 15,095.67        | 15,278.98                   | 01/2011<br>04/2021    | 04/2021     | 123(O)<br>0(R)                             | 26/47                       |
| 268   | BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR ,                                                                                           | 01/2007          | 5,353.00<br>-           | 7,998.00         | 7,511.72                    | 05/2014<br>-          | 05/2019     | 60(O)<br>-                                 | 3/18                        |
| 269   | NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture                                                                          | 01/2013          | 12,964.60<br>-          | 13,731.26        | 12,593.00                   | 01/2018<br>-          | 05/2020     | 28(O)<br>-                                 | 31/34                       |
| 270   | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR ,                                                             | 05/2015          | 436.68<br>-             | 602.44           | 537.08                      | 12/2016<br>-          | 03/2019     | 27(O)<br>-                                 | 14/19                       |
| 271   | ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR ,                                                                        | 04/2016          | 790.13<br>790.30        | 790.30           | 524.14                      | 06/2019<br>06/2019    | 06/2019     | 0(O)<br>0(R)                               | 0/0                         |
| 272   | LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH ,                                                                  | 12/2012          | 11,846.00<br>-          | 12,739.82        | 10,831.46                   | 06/2017<br>06/2019    | 06/2019     | 24(O)<br>0(R)                              | 35/40                       |
| 273   | TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH ,                                                                                         | 09/2015          | 3,004.00<br>-           | 3,004.00         | 1,293.72                    | 11/2019<br>-          | 11/2019     | 0(O)<br>-                                  | 0/0                         |
| 274   | CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,                                         | 03/2015          | 1,394.52<br>1,394.52    | 1,394.52         | 260.99                      | 05/2017<br>06/2019    | 06/2019     | 25(O)<br>0(R)                              | 4/9                         |
| 275   | TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT ,                                                    | 07/2016          | 300.94<br>300.94        | 300.94           | 219.36                      | 12/2018<br>12/2018    | 02/2019     | 2(O)<br>2(R)                               | 0/0                         |
| 276   | WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT ,                                                              | 11/2016          | 330.00<br>-             | 330.00           | 310.99                      | 11/2017<br>-          | 03/2019     | 16(O)<br>-                                 | 1/4                         |
| 277   | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT , Central Sector Projects           | 05/2017          | 175.64<br>175.64        | 175.64           | 73.94                       | 09/2018<br>09/2018    | 06/2019     | 9(O)<br>9(R)                               | 0/0                         |
| 278   | SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT ,                                                  | 12/2017          | 193.14<br>193.14        | 193.14           | 4.00                        | 06/2019<br>06/2019    | 06/2019     | 0(O)<br>0(R)                               | 0/0                         |
| 279   | PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH ,                                                                                  | 09/2002          | 3,919.59<br>-           | 9,394.80         | 7,145.69                    | 09/2009<br>-          | 12/2021     | 147(O)<br>-                                | 2/3                         |
| 280   | PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR ,                                                                     | 10/2014          | 8,112.12<br>-           | 8,112.12         | 982.71                      | 04/2020<br>-          | 10/2023     | 42(O)<br>-                                 | 0/0                         |
| 281   | TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI- LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR ,                     | 01/2014          | 1,788.41<br>1,788.41    | 2,333.71         | 1,697.38                    | 09/2017<br>09/2017    | 11/2018     | -                                          | 0/0                         |
| 282   | NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND ,                                                                                          | 02/2014          | 14,366.58<br>-          | 15,164.05        | 7,916.41                    | 02/2019<br>10/2020    | 10/2020     | 20(O)<br>0(R)                              | 22/23                       |
| 283   | PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND ,                                                                                       | 10/2004          | 4,237.96<br>4,238.00    | 4,552.00         | 2,922.12                    | 10/2017<br>-          | 12/2016     | -                                          | 0/0                         |
| 284   | KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA ,                                                                                                       | 01/2012          | 15,166.19<br>-          | 16,934.65        | 15,364.00                   | 01/2017<br>-          | -           | -                                          | 48/48                       |
| 285   | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA , Central Sector Projects | 05/2017          | 445.89<br>445.89        | 445.89           | 220.56                      | 02/2019<br>02/2019    | 06/2019     | 4(O)<br>4(R)                               | 0/0                         |
| 286   | GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH ,                                                                       | 03/2013          | 11,638.55<br>-          | 12,865.92        | 10,375.32                   | 09/2017<br>06/2019    | 06/2019     | 21(O)<br>0(R)                              | 36/41                       |
| 287   | KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH ,                                                                                     | 03/2015          | 9,870.51<br>-           | 11,148.86        | 6,693.90                    | 09/2019<br>-          | 09/2019     | 0(O)<br>-                                  | 27/31                       |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                       |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|---------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                               | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                     | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 288   | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH ,                                            | 01/2016          | 305.04<br>305.04        | 305.04           | 229.91                      | 03/2017<br>09/2018    | 01/2019     | 22(O)<br>4(R)                              | 0/0                         |
| 289   | AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects                                                         | 01/2017          | 2,104.21<br>-           | 2,104.21         | 66.05                       | 09/2020<br>-          | 09/2020     | 0(O)<br>-                                  | 9/16                        |
| 290   | WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA ,                                                                | 12/2007          | 477.69<br>738.48        | 738.48           | 686.26                      | 09/2010<br>12/2018    | 02/2019     | 101(O)<br>2(R)                             | 5/8                         |
| 291   | MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA ,                                                                                    | 03/2012          | 7,921.47<br>-           | 7,921.47         | 5,302.00                    | 09/2016<br>-          | -           | -                                          | 41/41                       |
| 292   | SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA ,                                                                                          | 03/2012          | 9,395.18<br>-           | 9,395.18         | 9,026.43                    | 11/2016<br>03/2019    | 03/2019     | 28(O)<br>0(R)                              | 35/38                       |
| 293   | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE ,                                           | 10/2008          | 4,824.12<br>5,071.94    | 5,071.94         | 4,545.57                    | 10/2012<br>12/2018    | 06/2019     | 80(O)<br>6(R)                              | 8/11                        |
| 294   | NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,                                                   | 02/2009          | 11,130.19<br>13,762.80  | 13,762.80        | 12,723.70                   | 08/2013<br>03/2022    | 03/2022     | 103(O)<br>0(R)                             | 23/26                       |
| 295   | SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE ,                                                                  | 10/2011          | 487.49<br>639.46        | 639.46           | 509.60                      | 06/2014<br>12/2018    | 03/2019     | 57(O)<br>3(R)                              | 10/12                       |
| 296   | SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE ,                                                         | 12/2011          | 297.33<br>534.02        | 534.02           | 441.08                      | 08/2014<br>09/2018    | 02/2019     | 54(O)<br>5(R)                              | 8/10                        |
| 297   | COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE ,    | 03/2013          | 2,514.88<br>-           | 3,190.27         | 2,281.28                    | 12/2015<br>-          | -           | -                                          | 15/18                       |
| 298   | EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE ,                                                                | 10/2013          | 1,364.52<br>1,891.41    | 1,891.41         | 1,216.98                    | 04/2016<br>12/2018    | 02/2019     | 34(O)<br>2(R)                              | 8/12                        |
| 299   | UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,                                                  | 01/2014          | 374.63<br>374.63        | 374.63           | 187.24                      | 04/2016<br>12/2017    | 03/2019     | 35(O)<br>15(R)                             | 0/0                         |
| 300   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE ,                                                    | 02/2014          | 539.82<br>539.82        | 539.82           | 423.73                      | 06/2016<br>09/2018    | 03/2019     | 33(O)<br>6(R)                              | 9/11                        |
| 301   | EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,                                                              | 05/2014          | 522.29<br>55,018.00     | 550.18           | 445.93                      | 11/2016<br>06/2019    | 06/2019     | 31(O)<br>0(R)                              | 8/12                        |
| 302   | AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE ,                                             | 03/2014          | 155.57<br>206.42        | 206.42           | 145.82                      | 03/2016<br>09/2018    | 02/2019     | 35(O)<br>5(R)                              | 4/6                         |
| 303   | TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE ,            | 06/2014          | 5,151.37<br>5,151.37    | 5,151.37         | 2,892.80                    | 03/2018<br>03/2019    | 06/2019     | 15(O)<br>3(R)                              | 9/12                        |
| 304   | EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE ,                                                              | 02/2014          | 196.58<br>225.28        | 225.28           | 151.02                      | 02/2016<br>09/2018    | 03/2019     | 37(O)<br>6(R)                              | 16/17                       |
| 305   | TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE ,                                                 | 01/2015          | 268.80<br>340.88        | 340.88           | 241.30                      | 03/2018<br>09/2018    | 02/2019     | 11(O)<br>5(R)                              | 1/3                         |
| 306   | TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE ,                                   | 01/2015          | 871.62<br>871.62        | 871.62           | 432.72                      | 10/2017<br>09/2019    | 09/2019     | 23(O)<br>0(R)                              | 0/5                         |
| 307   | SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,                                                      | 01/2015          | 203.28<br>260.03        | 260.03           | 187.06                      | 07/2017<br>06/2019    | 06/2019     | 23(O)<br>0(R)                              | 3/5                         |
| 308   | ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE , | 03/2015          | 197.40<br>197.40        | 197.40           | 74.71                       | 03/2018<br>-          | 03/2019     | 12(O)<br>-                                 | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                       |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|---------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                               | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                     | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 309   | GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE ,                                       | 04/2015          | 3,705.61<br>3,705.61    | 3,705.61         | 2,549.30                    | 04/2018<br>09/2018    | 02/2019     | 10(O)<br>5(R)                              | 5/9                         |
| 310   | SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE ,                                                         | 01/2016          | 1,455.47<br>-           | 1,455.47         | 1,028.69                    | 07/2018<br>-          | -           | -                                          | 0/0                         |
| 311   | TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE , | 03/2016          | 808.63<br>808.63        | 808.63           | 348.56                      | 01/2018<br>03/2019    | 09/2019     | 20(O)<br>6(R)                              | 0/0                         |
| 312   | EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE ,                                                               | 05/2016          | 766.21<br>766.21        | 766.21           | 454.34                      | 11/2018<br>11/2018    | 02/2019     | 3(O)<br>3(R)                               | 0/0                         |
| 313   | GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,                                      | 05/2016          | 3,519.59<br>3,519.59    | 3,519.59         | 2,073.40                    | 05/2019<br>05/2019    | 05/2019     | 0(O)<br>0(R)                               | 0/0                         |
| 314   | HVDC BIPOLE LINK BETWEEN WR (RAIGARH CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,  | 05/2016          | 14,733.37<br>14,733.37  | 14,733.37        | 5,084.05                    | 11/2019<br>11/2019    | 11/2019     | 0(O)<br>0(R)                               | 0/0                         |
| 315   | WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE ,                                                              | 07/2016          | 150.99<br>150.99        | 150.99           | 95.16                       | 07/2018<br>07/2018    | 02/2019     | 7(O)<br>7(R)                               | 0/0                         |
| 316   | POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL,MULTI STATE , | 07/2016          | 333.17<br>333.17        | 333.17           | 257.53                      | 03/2019<br>03/2019    | 03/2019     | 0(O)<br>0(R)                               | 0/0                         |
| 317   | PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL,MULTI STATE ,                                     | 08/2016          | 431.89<br>431.89        | 431.89           | 213.66                      | 02/2019<br>02/2019    | 02/2019     | 0(O)<br>0(R)                               | 0/0                         |
| 318   | SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE ,                                                             | 09/2016          | 562.25<br>562.25        | 562.25           | 103.00                      | 03/2019<br>03/2019    | 03/2019     | 0(O)<br>0(R)                               | 0/0                         |
| 319   | INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE ,           | 03/2017          | 251.60<br>251.60        | 251.60           | 112.11                      | 06/2019<br>06/2019    | 06/2019     | 0(O)<br>0(R)                               | 0/0                         |
| 320   | S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE , | 03/2017          | 283.72<br>283.72        | 283.72           | 109.75                      | 11/2019<br>11/2019    | 11/2019     | 0(O)<br>0(R)                               | 0/0                         |
| 321   | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE ,    | 10/2016          | 408.46<br>408.46        | 408.46           | 184.94                      | 01/2019<br>01/2019    | 06/2019     | 5(O)<br>5(R)                               | 0/0                         |
| 322   | SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE ,                | 10/2016          | 608.24<br>608.24        | 608.24           | 376.20                      | 04/2019<br>04/2019    | 04/2019     | 0(O)<br>0(R)                               | 0/0                         |
| 323   | WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE ,                                                            | 02/2017          | 195.05<br>195.05        | 195.05           | 92.00                       | 02/2020<br>02/2020    | 02/2020     | 0(O)<br>0(R)                               | 0/0                         |
| 324   | ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE , | 02/2017          | 322.30<br>322.30        | 322.30           | 119.48                      | 02/2019<br>02/2019    | 02/2019     | 0(O)<br>0(R)                               | 0/0                         |
| 325   | PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243]PGCIL,MULTI STATE ,  | 03/2017          | 162.31<br>162.31        | 162.31           | 86.70                       | 03/2019<br>03/2019    | 03/2019     | 0(O)<br>0(R)                               | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                               |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|---------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                                       | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                                             | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 326   | EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,                                                                             | 02/2017          | 235.53<br>235.53        | 235.53           | 42.49                       | 06/2019<br>06/2019    | 06/2019     | 0(O)<br>0(R)                               | 0/0                         |
| 327   | SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,                                                                           | 03/2017          | 379.95<br>379.95        | 379.95           | 22.22                       | 12/2019<br>12/2019    | 12/2019     | 0(O)<br>0(R)                               | 0/0                         |
| 328   | WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL,MULTI STATE ,                                                                                     | 02/2017          | 204.12<br>204.12        | 204.12           | 102.17                      | 09/2019<br>09/2019    | 03/2019     | -6(O)<br>-6(R)                             | 0/0                         |
| 329   | HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH CHATTISGARH) AND SOUTHERN REGION (PUGALAR TM) NOR - [N18000247]PGCIL,MULTI STATE ,                           | 02/2017          | 5,070.13<br>5,070.13    | 5,070.13         | 1,044.71                    | 04/2020<br>04/2020    | 04/2020     | 0(O)<br>0(R)                               | 0/0                         |
| 330   | SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE ,                                                                       | 03/2017          | 337.75<br>337.75        | 337.75           | 26.00                       | 06/2019<br>06/2019    | 06/2019     | 0(O)<br>0(R)                               | 0/0                         |
| 331   | COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,                                | 12/2014          | 4,754.42<br>4,754.42    | 9,141.97         | 993.85                      | 12/2018<br>12/2018    | 12/2019     | 12(O)<br>12(R)                             | 0/0                         |
| 332   | NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,                                           | 12/2014          | 5,111.33<br>5,111.33    | 6,652.57         | 922.25                      | 12/2018<br>12/2018    | 12/2019     | 12(O)<br>12(R)                             | 0/0                         |
| 333   | STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects                                                 | 12/2015          | 3,654.00<br>-           | 3,654.00         | 2,873.42                    | 04/2019<br>-          | 04/2019     | 0(O)<br>-                                  | 0/0                         |
| 334   | EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects                                                            | 03/2017          | 3,500.00<br>3,500.00    | 3,500.00         | 690.00                      | 07/2020<br>-          | 07/2020     | 0(O)<br>-                                  | 0/0                         |
| 335   | HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects | 08/2017          | 1,931.39<br>1,931.39    | 1,931.39         | 592.69                      | 02/2020<br>02/2020    | 02/2020     | 0(O)<br>0(R)                               | 0/0                         |
| 336   | 400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE ,                                                  | 09/2017          | 198.49<br>198.49        | 198.49           | 15.70                       | 09/2019<br>02/2020    | 02/2020     | 5(O)<br>0(R)                               | 0/0                         |
| 337   | EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE ,                                                                                       | 11/2017          | 358.83<br>358.83        | 358.83           | .00                         | 05/2020<br>05/2020    | 05/2020     | 0(O)<br>0(R)                               | 0/0                         |
| 338   | 400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270]PGCIL,MULTI STATE ,                                                                     | 08/2008          | 771.00<br>1,624.00      | 1,624.00         | 1,577.20                    | 02/2013<br>07/2018    | 12/2018     | 70(O)<br>5(R)                              | 0/0                         |
| 339   | DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,                                                                                                 | 02/2014          | 12,532.44<br>-          | 13,740.53        | 8,441.41                    | 08/2018<br>06/2019    | 06/2019     | 10(O)<br>0(R)                              | 30/37                       |
| 340   | PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA ,                                     | 04/2016          | 844.64<br>-             | 844.64           | 303.70                      | 04/2019<br>-          | 04/2019     | 0(O)<br>-                                  | 0/0                         |
| 341   | TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN ,                                                                      | 07/2015          | 307.18<br>307.18        | 307.18           | 210.91                      | 11/2017<br>10/2018    | 01/2019     | 14(O)<br>3(R)                              | 0/0                         |
| 342   | TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN ,                                                                         | 07/2016          | 1,429.38<br>1,429.38    | 1,429.38         | 849.56                      | 01/2019<br>01/2019    | 03/2019     | 2(O)<br>2(R)                               | 0/0                         |
| 343   | KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU ,                                                                                         | 05/2005          | 1,779.29<br>2,187.32    | 2,187.32         | 2,092.52                    | 11/2008<br>09/2018    | 03/2019     | 124(O)<br>6(R)                             | 20/22                       |
| 344   | COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU ,                          | 09/2011          | 1,940.13<br>-           | 2,702.65         | 2,529.92                    | 09/2014<br>-          | -           | -                                          | 11/13                       |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                               |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|---------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                                       | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                                             | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 345   | TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects | 05/2017          | 186.17<br>186.17        | 186.17           | 63.07                       | 07/2019<br>07/2019    | 07/2019     | 0(O)<br>0(R)                               | 0/0                         |
| 346   | TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,                                                                                   | 01/2016          | 10,598.98<br>-          | 10,598.98        | 3,272.35                    | 07/2020<br>10/2020    | 10/2020     | 3(O)<br>0(R)                               | 21/23                       |
| 347   | TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA ,                                                                                                 | 07/2009          | 421.01<br>-             | 1,078.31         | 963.23                      | 07/2013<br>-          | -           | -                                          | 26/26                       |
| 348   | FGUTPP UNCHAHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH ,                                                                                       | 07/2013          | 3,363.12<br>-           | 3,363.12         | 2,244.00                    | 12/2016<br>-          | -           | -                                          | 28/28                       |
| 349   | TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH ,                                                                                               | 09/2014          | 9,188.98<br>-           | 9,188.98         | 5,433.65                    | 03/2019<br>09/2019    | 09/2019     | 6(O)<br>0(R)                               | 19/32                       |
| 350   | DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH ,                                                                                               | 05/2011          | 195.42<br>294.60        | 294.60           | 221.63                      | 02/2014<br>02/2018    | 03/2019     | 61(O)<br>13(R)                             | 7/8                         |
| 351   | MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture                                                                                | 04/2012          | 9,750.89<br>-           | 9,750.89         | 8,798.00                    | 12/2016<br>-          | 08/2019     | 32(O)<br>-                                 | 33/34                       |
| 352   | TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND ,                                                                                          | 07/2006          | 1,657.00<br>2,978.86    | 4,401.90         | 2,692.27                    | 02/2016<br>12/2020    | 05/2021     | 63(O)<br>5(R)                              | 16/30                       |
| 353   | TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,                                                                                               | 11/2006          | 2,978.48<br>-           | 3,846.30         | 3,775.64                    | 03/2013<br>12/2020    | 12/2020     | 93(O)<br>0(R)                              | 6/15                        |
| 354   | VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,                                                                                  | 08/2008          | 2,491.58<br>-           | 4,105.30         | 1,592.11                    | 06/2013<br>-          | 12/2021     | 102(O)<br>-                                | 9/13                        |
| 355   | LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,                                                                             | 07/2012          | 1,527.00<br>-           | 1,801.07         | 151.63                      | 08/2017<br>-          | -           | -                                          | 0/15                        |
| 356   | NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,                                                                                                              | 10/2017          | 648.33<br>-             | 648.33           | 148.40                      | 12/2021<br>-          | 12/2021     | 0(O)<br>-                                  | 1/32                        |
| 357   | RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,                                                                                                     | 09/2014          | 1,381.84<br>-           | 1,381.84         | 384.28                      | 09/2019<br>02/2022    | 02/2022     | 29(O)<br>0(R)                              | 5/9                         |
| 358   | EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL ,                                                                                       | 04/2016          | 454.11<br>454.11        | 454.11           | 249.92                      | 04/2018<br>01/2020    | 01/2020     | 21(O)<br>0(R)                              | 0/0                         |
|       | <b>Total</b>                                                                                                                                                  |                  | 2,96,370.25<br>-        | 3,59,705.13      | 2,36,102.37                 |                       |             |                                            | 764/993                     |
|       |                                                                                                                                                               |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <b>HEAVY INDUSTRY</b>                                                                                                                                         |                  |                         |                  |                             |                       |             |                                            |                             |
| 359   | LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]JGCAR,DELHI , Central Sector Projects                     | 08/2016          | 1,554.00<br>-           | 1,554.00         | 161.86                      | 09/2019<br>-          | 09/2019     | 0(O)<br>-                                  | 0/0                         |
| 360   | NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE ,                                                          | 04/2011          | 1,718.00<br>3,727.30    | 3,827.30         | 2,933.23                    | 09/2011<br>06/2019    | 06/2019     | 93(O)<br>0(R)                              | 2/25                        |
|       | <b>Total</b>                                                                                                                                                  |                  | 3,272.00<br>-           | 5,381.30         | 3,095.09                    |                       |             |                                            | 2/25                        |
|       |                                                                                                                                                               |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <b>HEALTH AND FAMILY WELFARE</b>                                                                                                                              |                  |                         |                  |                             |                       |             |                                            |                             |
| 361   | RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS-MNAGLAGIRI GUNTUR ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects                           | 08/2017          | 272.19<br>-             | 272.19           | 104.84                      | 03/2019<br>-          | 03/2019     | 0(O)<br>-                                  | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                    |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|--------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                            | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                  | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 362   | HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH , Central Sector Projects                     | 03/2018          | 601.02 -                | 601.02           | 79.63                       | - -                   | 02/2020     | - -                                        | 0/0                         |
| 363   | LGBRIMH-TEZPUR ASSAM - [N21000007]HSCC,ASSAM ,                                                                     | 07/2012          | 175.57 -                | 175.57           | 113.50                      | 12/2014 -             | -           | -                                          | 0/0                         |
| 364   | ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI ASSAM - [N21000027]HITES,ASSAM ,                                | 05/2017          | 875.00 -                | 875.00           | 174.00                      | 05/2021 -             | 05/2021     | 0(O) -                                     | 0/0                         |
| 365   | LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,                                                            | 02/2013          | 414.11 -                | 513.89           | 141.00                      | 11/2013 10/2020       | 10/2020     | 83(O) 0(R)                                 | 0/0                         |
| 366   | AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,                                                           | 12/2013          | 204.44 -                | 204.44           | 173.67                      | 05/2017 06/2018       | 07/2019     | 26(O) 13(R)                                | 2/2                         |
| 367   | AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,                                                                         | 08/2014          | 293.65 -                | 293.65           | 273.80                      | 05/2017 06/2018       | 03/2019     | 22(O) 9(R)                                 | 3/5                         |
| 368   | GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI ,                                                            | 12/2017          | 156.56 -                | 156.65           | 49.34                       | - -                   | 02/2020     | - -                                        | 0/0                         |
| 369   | SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA , Central Sector Projects                                   | 01/2018          | 249.01 -                | 249.01           | 38.72                       | - -                   | 05/2020     | - -                                        | 0/0                         |
| 370   | CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,                                     | 09/2014          | 505.58 -                | 523.00           | 491.16                      | 03/2018 -             | -           | -                                          | 1/2                         |
| 371   | RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects  | 08/2017          | 274.19 -                | 274.19           | 114.89                      | 03/2019 -             | 03/2019     | 0(O) -                                     | 0/0                         |
| 372   | HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA , Central Sector Projects                        | 03/2018          | 582.99 -                | 582.99           | 57.09                       | - -                   | 02/2020     | - -                                        | 0/0                         |
| 373   | NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,                                                          | 10/2016          | 363.99 -                | 363.99           | 112.29                      | 05/2018 09/2019       | 08/2019     | 15(O) -1(R)                                | 0/0                         |
| 374   | SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,                                          | 07/2016          | 152.95 -                | 152.95           | 83.11                       | 02/2018 02/2018       | 06/2019     | 16(O) 16(R)                                | 1/1                         |
| 375   | ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA PUNJAB - [N21000026]HITES,PUNJAB ,                              | 07/2016          | 703.00 -                | 703.00           | 272.00                      | 06/2020 -             | 06/2020     | 0(O) -                                     | 0/0                         |
| 376   | HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH , Central Sector Projects             | 03/2018          | 268.84 -                | 268.84           | 66.44                       | - -                   | 04/2020     | - -                                        | 0/0                         |
| 377   | ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH ,                      | 07/2016          | 785.00 -                | 785.00           | 39.35                       | 04/2020 -             | 04/2020     | 0(O) -                                     | 0/0                         |
| 378   | CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL ,                                                           | 08/2016          | 244.00 -                | 244.00           | 238.97                      | 09/2018 -             | 09/2018     | -                                          | 0/0                         |
| 379   | RESIDENTIALCOMPLEX AND OPD BLOCK AIIMS KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL , Central Sector Projects | 08/2017          | 355.15 -                | 355.15           | 112.08                      | 03/2019 -             | 03/2019     | 0(O) -                                     | 0/0                         |
| 380   | HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL , Central Sector Projects                       | 04/2018          | 651.99 -                | 651.99           | 43.81                       | - -                   | 02/2020     | - -                                        | 0/0                         |
|       | Total                                                                                                              |                  | 8,129.23 -              | 8,246.52         | 2,779.69                    |                       |             |                                            | 7/10                        |
|       |                                                                                                                    |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>RAILWAYS</u>                                                                                                    |                  |                         |                  |                             |                       |             |                                            |                             |
| 381   | NANDYAL-YERRAGUNTLA(NL) SCR - [220100192]SCR,ANDHRA PRADESH ,                                                      | 03/1996          | 164.36 -                | 1,050.00         | 999.64                      | 02/2009 -             | -           | -                                          | 0/0                         |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                         |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-----------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                 | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                       | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 382   | KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH ,                        | 12/2001          | 1,045.20                | 2,120.16         | 289.91                      | 03/2009               | 03/2023     | 168(O)                                     | 0/0                         |
| 383   | OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH ,                   | 07/2006          | 732.81                  | 1,850.00         | 1,981.73                    | 03/2008               | 03/2020     | 144(O)                                     | 0/0                         |
| 384   | GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH ,                                 | 04/2011          | 761.37                  | 761.37           | .52                         | -                     | -           | -                                          | 0/0                         |
| 385   | CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH ,                                      | 04/2013          | 829.00                  | 1,599.39         | .94                         | -                     | -           | -                                          | 0/1                         |
| 386   | NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH ,                                | 04/2011          | 2,288.70                | 2,288.70         | 375.28                      | 03/2021               | 03/2022     | 12(O)                                      | 0/1                         |
| 387   | VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH , | 03/2012          | 1,503.71                | 1,503.71         | 1,134.27                    | 03/2020               | 03/2022     | 24(O)                                      | 0/0                         |
| 388   | DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH ,                                    | 04/2015          | 3,873.07                | 3,873.07         | .07                         | -                     | -           | -                                          | 0/0                         |
| 389   | GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH ,                                       | 04/2016          | 3,631.00                | 3,631.00         | 124.49                      | 03/2022               | 03/2023     | 12(O)                                      | 0/0                         |
| 390   | VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH ,                                     | 04/2015          | 3,246.26                | 3,548.67         | 132.79                      | 12/2023               | 12/2023     | 0(O)                                       | 0/0                         |
| 391   | KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH ,                        | 04/2015          | 2,499.71                | 2,499.71         | 183.68                      | 03/2022               | 03/2022     | 0(O)                                       | 0/0                         |
| 392   | MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH ,         | 01/2013          | 387.70                  | 387.70           | 323.91                      | 03/2018               | -           | -                                          | 0/0                         |
| 393   | MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH ,               | 08/2016          | 234.50                  | 235.00           | 2.98                        | 03/2019               | 12/2020     | 21(O)                                      | 0/0                         |
| 394   | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) NEFR - [N22000086]NFR,ASSAM , | 09/2006          | 385.20                  | 1,532.00         | 574.07                      | 03/2019               | 03/2020     | 12(O)                                      | 0/0                         |
| 395   | AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM ,                               | 04/2011          | 314.00                  | 551.00           | 602.54                      | 03/2019               | 03/2019     | 0(O)                                       | 0/0                         |
| 396   | LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM ,                           | 04/2012          | 246.07                  | 398.93           | 328.77                      | 03/2019               | 03/2019     | 0(O)                                       | 0/0                         |
| 397   | BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,                          | 04/2015          | 2,232.32                | 2,182.00         | 235.52                      | 03/2022               | 03/2020     | -24(O)                                     | 0/0                         |
| 398   | DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,                                          | 04/2015          | 870.96                  | 821.00           | 214.95                      | 03/2021               | 03/2021     | 0(O)                                       | 0/0                         |
| 399   | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC) ECR - [220100240]ECR,BIHAR ,                      | 04/1997          | 324.73                  | 1,156.41         | 876.49                      | 03/2012               | 03/2020     | 96(O)                                      | 0/0                         |
| 400   | KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR ,                                   | 09/2001          | 792.46                  | 1,320.00         | 929.63                      | 12/2010               | -           | -                                          | 0/0                         |
| 401   | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,                          | 04/1997          | 162.87                  | 589.15           | 183.72                      | -                     | 03/2022     | -                                          | 0/0                         |
| 402   | HAJIPUR-SUGAULI VIA VAISHALI (NL) ECR - [220100303]ECR,BIHAR ,                          | 04/2003          | 528.65                  | 2,066.77         | 330.82                      | -                     | 03/2023     | -                                          | 0/0                         |
| 403   | KOSI BRIDGE (NL) ECR - [220100304]ECR,BIHAR ,                                           | 04/2002          | 499.41                  | 516.02           | 640.78                      | 03/2020               | 03/2020     | 0(O)                                       | 0/0                         |
| 404   | DANIAWAN-BIHARSARIF (NL) ECR - [220100311]ECR,BIHAR ,                                   | 04/2001          | 406.92                  | 339.00           | 200.00                      | -                     | -           | -                                          | 0/0                         |
| 405   | MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR ,                                 | 04/2003          | 218.19                  | 413.56           | 372.16                      | 06/2018               | 10/2018     | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                 |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                         | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                               | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 406   | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,                      | 04/1996          | 477.88<br>283.95        | 749.00           | 495.40                      | 03/2012<br>-          | 03/2020     | 96(O)<br>-                                 | 0/0                         |
| 407   | NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) NEFR - [N22000087]NFR,BIHAR ,                | 09/2006          | 532.87<br>2,132.03      | 2,145.00         | 930.13                      | 03/2019<br>-          | 03/2020     | 12(O)<br>-                                 | 0/0                         |
| 408   | KISHANGANJ JALALGARH NL NEFR - [N22000101]NFR,BIHAR ,                                           | 04/2008          | 333.76<br>-             | 360.00           | 4.98                        | -<br>-                | 03/2020     | -<br>-                                     | 0/0                         |
| 409   | ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR ,                                                  | 04/2008          | 633.87<br>-             | 2,396.88         | .39                         | -<br>-                | -           | -                                          | 0/0                         |
| 410   | NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,                                                   | 04/2008          | 620.57<br>-             | 2,626.98         | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 411   | GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR ,                                     | 04/2008          | 445.25<br>-             | 2,860.55         | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 412   | BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR ,                                                 | 04/2008          | 326.20<br>-             | 2,995.01         | 1.68                        | -<br>-                | -           | -                                          | 0/0                         |
| 413   | SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR ,                                              | 04/1999          | 325.00<br>-             | 729.92           | 253.10                      | -<br>-                | 03/2021     | -<br>-                                     | 0/0                         |
| 414   | CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR ,                                              | 04/2006          | 378.56<br>-             | 2,614.36         | 111.71                      | -<br>-                | 03/2022     | -<br>-                                     | 0/0                         |
| 415   | DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,                                         | 04/2005          | 205.00<br>-             | 205.00           | 5.21                        | -<br>-                | -           | -                                          | 0/0                         |
| 416   | MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,                                                | 04/2006          | 211.00<br>-             | 926.09           | 4.41                        | -<br>-                | -           | -                                          | 0/0                         |
| 417   | SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,                            | 04/2008          | 678.62<br>-             | 2,393.23         | 17.17                       | -<br>-                | -           | -                                          | 0/0                         |
| 418   | MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,                              | 04/2008          | 228.05<br>-             | 228.05           | 1.52                        | -<br>-                | -           | -                                          | 0/0                         |
| 419   | ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,                                                     | 04/2008          | 1,605.17<br>-           | 1,605.17         | .19                         | -<br>-                | 03/2023     | -<br>-                                     | 0/0                         |
| 420   | KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,                                                | 04/2008          | 192.56<br>-             | 192.56           | .38                         | -<br>-                | -           | -                                          | 0/0                         |
| 421   | MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,                                             | 04/2008          | 281.30<br>-             | 281.30           | .58                         | -<br>-                | -           | -                                          | 0/0                         |
| 422   | SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR , | 04/2004          | 372.14<br>-             | 1,474.47         | 338.44                      | -<br>-                | 03/2021     | -<br>-                                     | 0/0                         |
| 423   | JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,    | 04/2009          | 548.00<br>-             | 785.87           | 40.00                       | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 424   | HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,                                        | 04/2013          | 213.01<br>-             | 367.17           | 13.00                       | -<br>-                | -           | -                                          | 0/0                         |
| 425   | SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,                                                   | 05/2015          | 380.00<br>-             | 380.00           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 426   | KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,                                           | 12/2015          | 1,200.20<br>-           | 1,200.20         | .00                         | 03/2020<br>-          | 10/2021     | 19(O)<br>-                                 | 0/1                         |
| 427   | RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,       | 12/2015          | 1,491.47<br>-           | 1,491.47         | .00                         | 03/2020<br>-          | 10/2021     | 19(O)<br>-                                 | 1/1                         |
| 428   | MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,                                         | 01/1991          | 332.15<br>-             | 559.91           | 538.21                      | 07/2014<br>-          | -           | -                                          | 0/0                         |
| 429   | SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR ,                                | 04/2016          | 744.04<br>-             | 1,215.54         | 1.81                        | 03/2021<br>-          | 03/2022     | 12(O)<br>-                                 | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                              |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                      | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                            | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 430   | MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]JECR,BIHAR ,                                                            | 04/2016          | 731.64 -                | 1,185.73         | .00                         | 03/2021 -             | 03/2022     | 12(O) -                                    | 0/0                         |
| 431   | PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]JECR,BIHAR ,       | 11/2001          | 624.47 -                | 3,550.00         | 97.63                       | 02/2016 -             | 03/2021     | 61(O) -                                    | 0/0                         |
| 432   | RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]JECR,BIHAR ,                                            | 04/1998          | 180.82 -                | 528.26           | 462.75                      | - -                   | 12/2018     | - -                                        | 0/0                         |
| 433   | FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA DANIYAWAN-BIHARSHARIF - [N22000476]JECR,BIHAR , | 04/1991          | 329.39 -                | 566.41           | 759.20                      | - -                   | 12/2021     | - -                                        | 0/0                         |
| 434   | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR) NL RVNL - [220100149]RVNL, CHHATISGARH ,                            | 04/1995          | 631.78 632.00           | 1,195.00         | 624.13                      | 12/2012 -             | 03/2022     | 111(O) -                                   | 0/0                         |
| 435   | SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH ,                                                          | 09/2006          | 383.54 -                | 555.00           | 726.22                      | 03/2010 -             | 12/2019     | 117(O) -                                   | 0/3                         |
| 436   | KIRANDUL - JAGDALPUR DOUBLING - [N22000318]JECOR,CHHATISGARH ,                                                               | 12/2012          | 1,160.00 -              | 1,160.83         | 571.51                      | 03/2020 -             | 03/2020     | 0(O) -                                     | 1/1                         |
| 437   | RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,                                                                | 03/2007          | 1,402.02 -              | 758.09           | 1,001.84                    | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/0                         |
| 438   | MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,                                                    | 05/2014          | 207.00 -                | 207.00           | 153.83                      | 03/2018 -             | -           | -                                          | 0/0                         |
| 439   | KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM - [N22000482]SECR,CHHATISGARH ,                                                     | 04/2011          | 1,471.93 -              | 543.00           | .00                         | 03/2022 -             | 03/2022     | 0(O) -                                     | 0/0                         |
| 440   | CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH ,                                                                   | 04/2008          | 872.00 -                | 1,279.00         | .00                         | 12/2019 -             | 12/2019     | 0(O) -                                     | 0/0                         |
| 441   | JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH ,                                                                 | 04/2015          | 1,973.00 -              | 1,973.00         | 78.00                       | 03/2021 -             | 03/2021     | 0(O) -                                     | 0/0                         |
| 442   | GEVRA ROAD PENDRA ROAD - [N22000488]SECR,CHHATISGARH ,                                                                       | 02/2014          | 2,288.00 -              | 4,919.00         | 67.00                       | 03/2022 -             | 03/2022     | 0(O) -                                     | 0/0                         |
| 443   | KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]SECR,CHHATISGARH ,                                   | 04/2013          | 3,055.00 -              | 3,055.00         | 600.00                      | 09/2018 -             | -           | -                                          | 0/0                         |
| 444   | GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,                                                                         | 04/1999          | 156.65 -                | 197.17           | 56.10                       | - -                   | -           | -                                          | 0/0                         |
| 445   | ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,                                                            | 04/2012          | 295.68 -                | 295.68           | 1.20                        | - -                   | -           | -                                          | 0/0                         |
| 446   | AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,                                                                 | 04/2008          | 829.74 416.86           | 385.60           | 500.42                      | 03/2020 03/2020       | 03/2020     | 0(O) 0(R)                                  | 0/0                         |
| 447   | BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,                                           | 04/2008          | 318.24 -                | 321.62           | 83.53                       | 03/2012 -             | 03/2019     | 84(O) -                                    | 0/0                         |
| 448   | BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,                                 | 04/2006          | 117.36 196.95           | 203.00           | 202.29                      | 03/2011 -             | -           | -                                          | 0/0                         |
| 449   | AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,                                                                             | 04/2012          | 975.62 -                | 975.62           | 518.92                      | 12/2021 -             | 12/2021     | 0(O) -                                     | 0/0                         |
| 450   | DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,                                                                              | 04/2012          | 644.38 -                | 644.38           | 127.98                      | 03/2021 -             | 03/2021     | 0(O) -                                     | 0/0                         |
| 451   | MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,                                                                 | 04/2011          | 844.10 -                | 844.10           | 61.85                       | - 03/2022             | 03/2023     | - 12(R)                                    | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                  |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|----------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                          | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 452   | RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,          | 04/1994          | 320.66<br>1,378.12      | 858.96           | 549.56                      | 03/2019<br>03/2019    | 03/2022     | 36(O)<br>36(R)                             | 0/0                         |
| 453   | PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,                                                                            | 04/2013          | 1,548.66<br>-           | 1,548.66         | 777.72                      | 12/2021<br>-          | 12/2021     | 0(O)<br>-                                  | 0/0                         |
| 454   | SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,                                                                                  | 04/2015          | 1,002.39<br>-           | 1,002.39         | 232.37                      | 03/2021<br>03/2019    | 03/2020     | -12(O)<br>12(R)                            | 0/0                         |
| 455   | MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,                                                                | 10/2013          | 343.00<br>-             | 343.00           | 289.38                      | 03/2019<br>-          | 12/2019     | 9(O)<br>-                                  | 0/0                         |
| 456   | GANDHINAGAR REDEVELOPMENT OF STATION ALOGL WITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT , | 03/2017          | 243.60<br>-             | 243.60           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 457   | VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,   | 03/2012          | 248.26<br>-             | 248.26           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 458   | PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT ,                  | 03/2012          | 153.83<br>-             | 153.83           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 459   | BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT ,        | 02/1991          | 551.51<br>-             | 551.51           | 257.05                      | 03/2019<br>-          | 03/2019     | 0(O)<br>-                                  | 0/0                         |
| 460   | DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT ,                            | 04/2017          | 691.84<br>-             | 691.84           | 15.31                       | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 461   | JIND-SONEPAT (NL) NR - [220100280]NR,HARYANA ,                                                                                   | 01/2004          | 238.56<br>-             | 740.00           | 722.65                      | 03/2012<br>-          | -           | -                                          | 0/0                         |
| 462   | ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,                                                                                     | 04/2012          | 287.00<br>-             | 625.00           | 4.38                        | 12/2011<br>-          | -           | -                                          | 0/0                         |
| 463   | HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA ,                                                                  | 04/2013          | 400.00<br>-             | 400.00           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 464   | MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,                                                                  | 12/2015          | 346.32<br>-             | 300.00           | 272.72                      | 03/2019<br>-          | 03/2019     | 0(O)<br>-                                  | 0/0                         |
| 465   | BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,                                                                  | 04/2008          | 2,966.99<br>-           | 7,000.00         | 221.19                      | 12/2026<br>-          | 12/2026     | 0(O)<br>-                                  | 0/0                         |
| 466   | UDHAMPUR-SRINAGAR-BARAMULLA (NL) NR - [220100133]NR,JAMMU AND KASHMIR ,                                                          | 03/1995          | 2,500.00<br>-           | 27,949.00        | 16,834.42                   | 11/2002<br>-          | 03/2021     | 220(O)<br>-                                | 0/0                         |
| 467   | MANDARHILL-DUMKA-RAMPURHAT (NL) ER - [220100168]ER,JHARKHAND ,                                                                   | 04/1995          | 1,125.89<br>-           | 1,126.36         | 2,012.33                    | 03/2016<br>-          | 03/2020     | 48(O)<br>-                                 | 0/0                         |
| 468   | KODERMA-RANCHI VIA BARKAKANA (NL) ECR - [220100222]ECR,JHARKHAND ,                                                               | 03/1999          | 1,033.07<br>-           | 3,020.94         | .00                         | -<br>-                | 03/2021     | -                                          | 0/0                         |
| 469   | KODERMA-TILAIYA (NL) ECR - [220100305]ECR,JHARKHAND ,                                                                            | 04/2002          | 459.91<br>-             | 459.91           | 221.54                      | -<br>-                | -           | -                                          | 0/0                         |
| 470   | DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND ,                                                            | 04/2010          | 309.44<br>-             | 525.81           | 507.60                      | 12/2015<br>12/2018    | 02/2019     | 38(O)<br>2(R)                              | 0/0                         |
| 471   | MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,                                                             | 04/2012          | 258.20<br>-             | 365.00           | 192.35                      | -<br>12/2018          | 01/2020     | -<br>13(R)                                 | 0/0                         |
| 472   | RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,                                               | 04/2012          | 148.77<br>-             | 377.00           | 155.96                      | 12/2016<br>08/2018    | 09/2019     | 33(O)<br>13(R)                             | 0/0                         |
| 473   | BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,                                                                          | 03/2016          | 1,724.20<br>1,724.20    | 1,724.20         | 175.49                      | 03/2021<br>03/2021    | 12/2021     | 9(O)<br>9(R)                               | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                 |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|---------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                         | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                               | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 474   | GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND ,                                  | 03/2015          | 348.23                  | 348.23           | 104.98                      | 03/2021               | 12/2020     | -3(O)                                      | 0/0                         |
| 475   | HUBLI-ANKOLA(NL) SWR - [220100193]SWR,KARNATAKA ,                               | 04/1997          | 2,315.00                | 2,135.00         | 144.75                      | -                     | 12/2024     | -                                          | 0/0                         |
| 476   | BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,                 | 04/1996          | 1,382.78                | 1,382.78         | 7.35                        | 03/2002               | 03/2024     | 264(O)                                     | 0/0                         |
| 477   | TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,                    | 04/2011          | 1,801.01                | 1,801.01         | 13.67                       | -                     | 12/2023     | -                                          | 0/0                         |
| 478   | MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA ,                    | 04/2007          | 179.65                  | 1,350.91         | 924.08                      | -                     | 12/2023     | -                                          | 0/1                         |
| 479   | BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,                                | 04/2010          | 986.30                  | 986.30           | 287.03                      | 03/2016               | 12/2023     | 93(O)                                      | 0/1                         |
| 480   | CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA , | 04/2013          | 558.00                  | 692.43           | .00                         | -                     | 12/2023     | -                                          | 0/0                         |
| 481   | SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,                                 | 04/2011          | 832.47                  | 832.47           | .94                         | 03/2016               | 03/2024     | 96(O)                                      | 0/0                         |
| 482   | WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,                               | 04/2011          | 348.85                  | 348.85           | .36                         | -                     | 12/2023     | -                                          | 0/0                         |
| 483   | HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,                 | 04/2010          | 2,127.00                | 2,127.00         | 1,042.32                    | 03/2023               | 03/2023     | 0(O)                                       | 0/1                         |
| 484   | TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,                          | 04/2011          | 146.75                  | 167.50           | .34                         | -                     | 12/2023     | -                                          | 0/0                         |
| 485   | GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,                                      | 04/2013          | 2,841.84                | 2,841.84         | 39.98                       | 12/2018               | 12/2024     | 72(O)                                      | 0/0                         |
| 486   | CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,                      | 04/2013          | 327.25                  | 367.77           | .31                         | -                     | 12/2023     | -                                          | 0/0                         |
| 487   | MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,                                | 04/2012          | 279.54                  | 279.54           | 8.80                        | 03/2016               | 12/2023     | 93(O)                                      | 0/0                         |
| 488   | HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,                                   | 03/2015          | 1,156.94                | 1,156.94         | 701.76                      | 03/2020               | 03/2021     | 12(O)                                      | 0/5                         |
| 489   | ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,                                    | 03/2015          | 578.00                  | 578.00           | 458.72                      | 03/2020               | 03/2020     | 0(O)                                       | 0/2                         |
| 490   | KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA ,      | 03/1996          | 644.78                  | 889.52           | 433.71                      | 03/2017               | 03/2020     | 36(O)                                      | 0/0                         |
| 491   | ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,                         | 10/1998          | 1,566.00                | 2,815.62         | 254.53                      | -                     | -           | -                                          | 0/0                         |
| 492   | KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,                                       | 04/2011          | 252.96                  | 252.96           | 8.50                        | -                     | -           | -                                          | 0/0                         |
| 493   | CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA ,                                 | 04/2006          | 191.72                  | 369.83           | 432.50                      | -                     | -           | -                                          | 0/0                         |
| 494   | ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,                                     | 04/2010          | 189.24                  | 189.24           | 6.70                        | -                     | -           | -                                          | 0/0                         |
| 495   | TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,                        | 02/2015          | 1,431.90                | 1,431.90         | 23.84                       | -                     | -           | -                                          | 0/0                         |
| 496   | TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,                           | 02/2015          | 1,000.00                | 828.50           | .08                         | -                     | -           | -                                          | 0/0                         |
| 497   | PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA ,            | 02/2012          | 550.00                  | 550.00           | .00                         | 03/2016               | -           | -                                          | 0/0                         |
| 498   | MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. - [N22000454]SR,KERALA ,          | 02/2005          | 241.00                  | 241.00           | 294.63                      | 03/2014               | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                            |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|--------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                    | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                          | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 499   | RAMGANJMUNDI-BHOPAL (NL) WCR - [220100314]WCR,MADHYA PRADESH ,                             | 04/2001          | 424.60                  | 2,713.09         | 898.83                      | 03/2021               | 03/2021     | 0(O)                                       | 0/0                         |
| 500   | CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,                          | 04/2005          | 383.79                  | 1,101.16         | 194.91                      | -                     | -           | -                                          | 0/0                         |
| 501   | RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,                            | 04/2008          | 3,503.69                | 1,030.29         | 1,081.52                    | 03/2022               | 03/2022     | 0(O)                                       | 0/0                         |
| 502   | KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,                       | 12/2015          | 2,473.40                | 1,763.93         | .00                         | 03/2019               | 10/2021     | 36(R)                                      | 1/1                         |
| 503   | BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,                            | 04/2011          | 1,763.93                | 1,485.85         | 1,038.90                    | 03/2020               | 12/2020     | 19(O)                                      | 0/0                         |
| 504   | KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,                             | 06/2016          | 1,485.85                | 2,478.23         | 112.07                      | 12/2020               | 03/2022     | 0(O)                                       | 0/1                         |
| 505   | KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,                           | 08/2016          | 2,478.23                | 1,260.61         | .00                         | 03/2022               | 03/2022     | 0(O)                                       | 0/1                         |
| 506   | MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,                      | 12/2015          | 582.13                  | 174.00           | 139.38                      | 03/2019               | 08/2019     | 5(O)                                       | 0/0                         |
| 507   | CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH , | 04/2010          | 174.00                  | 1,420.39         | 104.10                      | 02/2019               | 02/2019     | 0(O)                                       | 0/0                         |
| 508   | CHHINDWARA-MANDLA FORT GC - [N22000481]SECR,MADHYA PRADESH ,                               | 03/2011          | 556.54                  | 1,342.46         | 396.00                      | 03/2012               | 03/2020     | 96(O)                                      | 0/0                         |
| 509   | ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH ,                                           | 04/2015          | 1,370.00                | 1,370.00         | 101.00                      | 12/2021               | 12/2021     | 0(O)                                       | 0/0                         |
| 510   | INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH ,                              | 04/2016          | 700.00                  | 700.00           | 11.19                       | 06/2020               | 06/2020     | 0(O)                                       | 0/0                         |
| 511   | AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA ,                                      | 06/1994          | 663.01                  | 858.96           | 716.80                      | 06/1999               | -           | -                                          | 0/0                         |
| 512   | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,          | 03/1996          | 668.34                  | 1,781.98         | 1,337.62                    | 03/2004               | 03/2020     | 192(O)                                     | 0/0                         |
| 513   | AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA ,                             | 02/1997          | 2,271.50                | 3,712.50         | 1,909.57                    | 03/2021               | 03/2021     | 0(O)                                       | 0/0                         |
| 514   | MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,                    | 04/2008          | 2,271.50                | 7,986.04         | 2,423.55                    | 03/2014               | 03/2019     | 60(O)                                      | 0/0                         |
| 515   | RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,                   | 04/2012          | 5,300.00                | 714.10           | 65.20                       | 04/2016               | -           | -                                          | 0/0                         |
| 516   | WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,                                    | 04/2008          | 714.10                  | 3,168.29         | 992.77                      | 03/2023               | 03/2023     | 0(O)                                       | 0/0                         |
| 517   | KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,                                       | 04/2011          | 3,168.29                | 792.89           | 275.17                      | 03/2021               | 03/2021     | 0(O)                                       | 0/0                         |
| 518   | 3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,                            | 04/2011          | 792.89                  | 298.70           | 240.89                      | 03/2019               | 03/2019     | 0(O)                                       | 0/0                         |
| 519   | WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,                                 | 04/2012          | 184.06                  | 540.02           | 168.97                      | 03/2022               | 03/2022     | 0(O)                                       | 0/0                         |
| 520   | INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,                        | 02/2016          | 199.12                  | 9,968.00         | .00                         | 03/2024               | 03/2024     | 0(O)                                       | 0/0                         |
| 521   | PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,                                          | 02/2016          | 2,425.00                | 5,341.68         | .00                         | 03/2024               | 03/2024     | 0(O)                                       | 0/0                         |
| 522   | VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,                              | 02/2016          | 2,750.00                | 3,438.51         | .00                         | 03/2024               | 03/2024     | 0(O)                                       | 0/0                         |
| 523   | WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,                        | 02/2015          | 1,272.19                | 1,272.19         | 162.38                      | 03/2022               | 03/2022     | 0(O)                                       | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                    |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                            | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                  | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 524   | ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,                                                             | 02/2015          | 2,449.91<br>2,449.91    | 2,449.91         | 89.27                       | 03/2023<br>-          | 03/2023     | 0(O)<br>-                                  | 0/0                         |
| 525   | PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,                                                                            | 02/2015          | 3,627.47<br>3,627.47    | 3,627.47         | 332.55                      | 03/2024<br>-          | 03/2024     | 0(O)<br>-                                  | 0/0                         |
| 526   | DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,                                                                              | 02/2016          | 1,876.00<br>2,081.27    | 2,081.27         | 1.27                        | 03/2023<br>-          | 03/2023     | 0(O)<br>-                                  | 0/0                         |
| 527   | MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,                                                                 | 02/2016          | 1,035.16<br>1,035.16    | 1,035.16         | 19.79                       | 03/2022<br>-          | 03/2023     | 12(O)<br>-                                 | 0/0                         |
| 528   | WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,                                                                   | 02/2016          | 637.95<br>637.95        | 637.95           | 28.96                       | 03/2023<br>-          | 03/2023     | 0(O)<br>-                                  | 0/0                         |
| 529   | DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,                | 03/2009          | 713.48<br>-             | 1,750.00         | 1,618.00                    | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 530   | DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,                                                                                | 04/2015          | 723.78<br>-             | 723.78           | .22                         | 12/2025<br>-          | 03/2025     | -9(O)<br>-                                 | 0/0                         |
| 531   | RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,                                                             | 09/2016          | 1,908.51<br>-           | 2,686.63         | .00                         | 03/2023<br>-          | 03/2023     | 0(O)<br>-                                  | 0/0                         |
| 532   | MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,                                                           | 10/2013          | 305.00<br>-             | 305.00           | 253.22                      | 03/2019<br>-          | 03/2019     | 0(O)<br>-                                  | 0/0                         |
| 533   | MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,                             | 03/2010          | 265.88<br>-             | 265.88           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 534   | VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA , | 03/2012          | 217.38<br>-             | 217.38           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 535   | WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA ,                                                              | 06/2018          | 229.00<br>-             | 403.00           | 36.28                       | 12/2021<br>-          | 12/2021     | 0(O)<br>-                                  | 0/0                         |
| 536   | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,                                                                     | 04/2003          | 4,454.17<br>-           | 13,809.00        | 8,304.86                    | 03/2011<br>-          | 03/2020     | 108(O)<br>-                                | 0/0                         |
| 537   | NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]NFR,MEGHALAYA ,                                                                 | 04/2010          | 906.46<br>1,202.33      | 6,000.00         | 259.95                      | 03/2021<br>-          | 03/2021     | 0(O)<br>-                                  | 0/0                         |
| 538   | BHAIRABI SAIRONG NL NEFR - [N22000100]NFR,MIZORAM ,                                                                                | 04/2008          | 2,393.47<br>2,393.48    | 4,968.00         | 2,516.15                    | 03/2014<br>12/2020    | 12/2020     | 81(O)<br>0(R)                              | 0/0                         |
| 539   | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL (NCR) - [220100007]NCR,MULTI STATE ,                                                    | 04/1986          | 158.77<br>274.56        | 634.48           | 629.43                      | 03/1994<br>-          | -           | -                                          | 0/0                         |
| 540   | CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE ,                                                                          | 02/1996          | 240.00<br>-             | 579.37           | 537.30                      | -<br>-                | -           | -                                          | 0/0                         |
| 541   | GONDIA-JABALPUR(GC) (SECR) - [220100186]SECR,MULTI STATE ,                                                                         | 02/1997          | 511.86<br>-             | 1,756.00         | 967.96                      | 04/2020<br>-          | 04/2020     | 0(O)<br>-                                  | 0/0                         |
| 542   | NANGALDAM-TALWARA(NL) NR - [220100188]NR,MULTI STATE ,                                                                             | 03/1981          | 450.00<br>-             | 2,100.00         | 484.14                      | 07/2012<br>-          | -           | -                                          | 0/0                         |
| 543   | MUNEERABAD-MAHABOBNAGAR(NL) SCR - [220100205]SCR,MULTI STATE ,                                                                     | 04/1997          | 1,723.00<br>1.00        | 645.00           | 725.63                      | 03/2000<br>-          | 03/2019     | 228(O)<br>-                                | 0/0                         |
| 544   | LALITPUR-SATNA-REWA-SINGRULI NL (NCR) - [220100232]WCR,MULTI STATE ,                                                               | 09/1998          | 247.66<br>-             | 6,093.31         | 972.82                      | 05/2008<br>-          | 03/2023     | 178(O)<br>-                                | 0/4                         |
| 545   | KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE ,                                                             | 04/1999          | 744.71<br>-             | 1,126.79         | 751.05                      | -<br>-                | -           | -                                          | 1/1                         |
| 546   | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) NR - [220100258]NR,MULTI STATE ,                                                               | 03/2002          | 625.30<br>408.76        | 876.10           | 841.57                      | 06/2007<br>-          | -           | -                                          | 0/0                         |
| 547   | QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE ,                                                      | 03/1998          | 280.00<br>-             | 1,122.00         | 834.87                      | -<br>-                | -           | -                                          | 0/6                         |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                   |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                           | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                 | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 548   | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) NEFR - [220100266]NFR,MULTI STATE ,                                             | 04/2000          | 1,180.19<br>2,531.34    | 3,040.00         | 3,065.47                    | 12/2008<br>-          | 03/2019     | 123(O)<br>-                                | 0/0                         |
| 549   | DEOGHAR - SULTANGANJ (INL) ER - [220100273]ER,MULTI STATE ,                                                                       | 04/2000          | 607.09<br>-             | 607.91           | 634.08                      | 02/2013<br>-          | -           | -                                          | 0/0                         |
| 550   | HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE ,                                                                          | 04/2005          | 230.03<br>-             | 770.08           | 274.67                      | 12/2022<br>-          | 05/2019     | -43(O)<br>-                                | 0/0                         |
| 551   | CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,                                                     | 03/2007          | 243.78<br>-             | 895.00           | 99.33                       | 12/2021<br>-          | 12/2021     | 0(O)<br>-                                  | 0/0                         |
| 552   | CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,                                                                                  | 03/2013          | 295.00<br>-             | 477.31           | 186.71                      | 01/2019<br>-          | 02/2019     | 1(O)<br>-                                  | 0/0                         |
| 553   | CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,                                                                               | 04/2007          | 1,347.26<br>-           | 1,347.26         | 606.41                      | 03/2022<br>03/2019    | 03/2022     | 0(O)<br>36(R)                              | 0/0                         |
| 554   | DAHOD-INDORE VIA SARDARPUR JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,                                                     | 04/2007          | 1,640.04<br>-           | 1,640.04         | 603.75                      | 03/2022<br>03/2019    | 03/2022     | 0(O)<br>36(R)                              | 0/0                         |
| 555   | RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,                                                                 | 04/2011          | 2,082.75<br>-           | 2,878.97         | 183.40                      | -<br>-                | -           | -                                          | 0/1                         |
| 556   | GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,                                                     | 04/2011          | 2,912.96<br>-           | 3,845.60         | 1.92                        | 03/2022<br>-          | 03/2022     | 0(O)<br>-                                  | 0/0                         |
| 557   | DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,      | 04/2010          | 2,030.50<br>-           | 2,030.50         | 10.34                       | -<br>-                | 12/2022     | -                                          | 0/0                         |
| 558   | DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,                                                         | 04/2010          | 651.00<br>-             | 1,009.00         | 7.96                        | 03/2015<br>03/2024    | 03/2024     | 108(O)<br>0(R)                             | 0/0                         |
| 559   | GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE ,                                                                                  | 04/2008          | 415.67<br>-             | 549.75           | 14.62                       | -<br>-                | -           | -                                          | 0/0                         |
| 560   | NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,                                                           | 04/2013          | 1,798.00<br>-           | 1,798.00         | .00                         | 03/2019<br>-          | 03/2019     | 0(O)<br>-                                  | 0/0                         |
| 561   | CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,                                                                  | 04/2008          | 523.52<br>-             | 2,350.00         | 2.27                        | -<br>-                | -           | -                                          | 0/0                         |
| 562   | KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,                                                                           | 04/2007          | 270.14<br>-             | 457.08           | 317.14                      | -<br>-                | -           | -                                          | 0/0                         |
| 563   | NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,                                                            | 04/2010          | 242.22<br>-             | 471.00           | 64.68                       | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 564   | NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,                                                             | 04/2010          | 241.52<br>-             | 394.28           | 148.33                      | -<br>-                | -           | -                                          | 0/0                         |
| 565   | MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,                                                                           | 04/2011          | 414.84<br>-             | 661.00           | 121.37                      | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 566   | NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,  | 04/1999          | 819.23<br>-             | 1,871.00         | 1,082.01                    | -<br>-                | -           | -                                          | 0/0                         |
| 567   | MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,                                                                  | 04/2011          | 120.70<br>-             | 1,800.00         | 112.10                      | 03/2019<br>-          | 03/2019     | 0(O)<br>-                                  | 0/0                         |
| 568   | LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE , | 04/1987          | 406.99<br>-             | 544.72           | 147.26                      | 03/2006<br>-          | -           | -                                          | 0/0                         |
| 569   | SULTANGANJ-KATURIA VIA ASARGANJ TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,                                                  | 04/2007          | 450.00<br>-             | 288.85           | 9.31                        | -<br>-                | -           | -                                          | 0/0                         |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                    |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                            | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                  | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 570   | HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,                                                                     | 04/2010          | 172.03 -                | 260.10           | 10.84                       | -                     | -           | -                                          | 0/0                         |
| 571   | PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,                                                                                    | 04/2013          | 915.98 -                | 915.96           | 319.53                      | 03/2022 -             | 03/2022     | 0(O) -                                     | 0/0                         |
| 572   | BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,                                                                              | 04/2011          | 288.35 -                | 238.36           | 291.43                      | -                     | -           | -                                          | 0/0                         |
| 573   | PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,                                                                                  | 04/2011          | 261.38 -                | 332.14           | 378.90                      | -                     | -           | -                                          | 0/0                         |
| 574   | KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE , | 04/2001          | 923.52 -                | 792.27           | 336.43                      | 03/2016 -             | -           | -                                          | 0/0                         |
| 575   | CHINPAI- SAINTHIA DOUBLING MM FOR PRANTI-SURI CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,                      | 04/2005          | 595.51 -                | 538.37           | 109.04                      | 03/2017 -             | -           | -                                          | 0/0                         |
| 576   | KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,                      | 04/2010          | 174.56 -                | 175.99           | 57.52                       | -                     | -           | -                                          | 0/0                         |
| 577   | SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,                                         | 04/2010          | 277.28 -                | 266.52           | 137.93                      | 03/2016 -             | 03/2020     | 48(O) -                                    | 0/0                         |
| 578   | DANKUNI-CHANDANPUR 4TH LINE 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,    | 04/2010          | 365.17 -                | 296.43           | 134.36                      | 03/2017 -             | -           | -                                          | 0/0                         |
| 579   | HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,                                           | 04/2010          | 157.94 -                | 157.94           | 50.69                       | 11/2018 -             | -           | -                                          | 0/0                         |
| 580   | BARIARPIUR-MANANPURVIA KHARAGPUER LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,                                                  | 04/2007          | 450.55 -                | 250.55           | 19.82                       | -                     | -           | -                                          | 0/0                         |
| 581   | TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,                                                                        | 04/2010          | 365.17 -                | 527.54           | 1.73                        | -                     | -           | -                                          | 0/0                         |
| 582   | HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE ,                                                                                    | 04/2011          | 542.18 -                | 542.18           | 311.90                      | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/0                         |
| 583   | BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,                                                                          | 04/2011          | 175.80 -                | 173.91           | 153.48                      | -                     | -           | -                                          | 0/0                         |
| 584   | PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,                                                    | 04/2011          | 299.60 -                | 299.60           | 1.12                        | 03/2017 -             | -           | -                                          | 0/0                         |
| 585   | NEW ALIPUR TO AKRA MM FOR BUDGE BUDGE-PUJALI NL PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,   | 04/2010          | 494.54 -                | 492.68           | 32.00                       | 03/2005 -             | -           | -                                          | 0/0                         |
| 586   | SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE ,                                 | 04/2000          | 297.47 -                | 299.03           | 53.11                       | -                     | -           | -                                          | 0/0                         |
| 587   | CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE , | 04/2003          | 337.96 -                | 355.44           | 72.84                       | -                     | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                    |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                            | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                  | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 588   | MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]JER,MULTI STATE , | 04/2009          | 499.96 -                | 665.75           | 149.39                      | 02/2012 -             | -           | -                                          | 0/0                         |
| 589   | LILUAH-DANKUNI 3RD LINE MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]JER,MULTI STATE ,                                 | 04/2009          | 257.42 -                | 258.73           | 113.58                      | 03/2014 -             | -           | -                                          | 0/0                         |
| 590   | SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]JER,MULTI STATE ,                                                | 04/2010          | 268.52 -                | 268.52           | 78.81                       | - -                   | -           | -                                          | 0/0                         |
| 591   | HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]JER,MULTI STATE ,        | 04/2011          | 166.89 -                | 166.89           | 246.00                      | - -                   | -           | -                                          | 0/0                         |
| 592   | KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,                                                    | 04/2012          | 1,856.95 -              | 2,200.00         | 227.19                      | 03/2023 -             | 03/2024     | 12(O) -                                    | 0/0                         |
| 593   | BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE ,                                                                                 | 04/2012          | 923.23 -                | 1,787.00         | 2.46                        | - -                   | -           | -                                          | 0/1                         |
| 594   | DELHI-SOHNANUHI-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE ,                                                                | 04/2013          | 1,239.00 -              | 1,239.00         | .00                         | - -                   | -           | -                                          | 0/0                         |
| 595   | DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,                                                                  | 04/2007          | 336.91 -                | 336.91           | 143.18                      | - -                   | -           | -                                          | 0/0                         |
| 596   | SRINIVASA-PURAMADANAPALLI NL - [N22000277]SWR,MULTI STATE ,                                                                        | 04/2013          | 296.00 -                | 466.65           | .00                         | - 12/2023             | 12/2023     | - 0(R)                                     | 0/0                         |
| 597   | RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE ,                                                                                | 04/2007          | 2,062.30 -              | 2,062.20         | 674.76                      | - -                   | 03/2022     | -                                          | 0/2                         |
| 598   | BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,                                                                        | 04/2010          | 704.31 -                | 704.31           | 119.69                      | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/1                         |
| 599   | KADAPA-BANGALORE (NL) KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,                                                       | 04/2008          | 2,132.77 -              | 2,132.77         | 216.07                      | 03/2014 -             | 03/2023     | 108(O) -                                   | 0/1                         |
| 600   | AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE ,                                          | 04/2010          | 338.54 -                | 338.54           | 212.64                      | - -                   | -           | -                                          | 0/0                         |
| 601   | JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE ,                                                                 | 04/2008          | 162.96 -                | 162.96           | 153.31                      | - -                   | -           | -                                          | 0/0                         |
| 602   | YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE ,                                                      | 04/2013          | 876.00 -                | 876.00           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 603   | CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE ,                                                                                  | 04/2007          | 328.14 -                | 1,540.00         | 45.20                       | - -                   | -           | -                                          | 0/0                         |
| 604   | MONIGRAM- NIMTITA - [N22000301]JER,MULTI STATE ,                                                                                   | 04/2012          | 250.93 -                | 259.23           | 208.85                      | - -                   | -           | -                                          | 0/0                         |
| 605   | MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE ,                                                                           | 04/2008          | 466.48 -                | 1,000.00         | .83                         | - 12/2024             | 12/2024     | - 0(R)                                     | 0/0                         |
| 606   | PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,                                                                           | 05/2015          | 600.00 -                | 685.99           | 3.52                        | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/0                         |
| 607   | MIRAJ-LONDA - [N22000327]SWR,MULTI STATE ,                                                                                         | 03/2015          | 1,830.00 1,190.92       | 1,190.92         | 207.68                      | - 03/2021             | 03/2021     | - 0(R)                                     | 0/0                         |
| 608   | YELAHANKA-PENKONDA - [N22000328]SWR,MULTI STATE ,                                                                                  | 05/2015          | 860.43 860.43           | 860.43           | 503.45                      | 03/2020 03/2020       | 03/2020     | 0(O) 0(R)                                  | 0/0                         |
| 609   | HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,                                                                                   | 03/2015          | 1,614.59 1,870.41       | 1,870.41         | 732.88                      | 03/2019 03/2021       | 03/2021     | 24(O) 0(R)                                 | 0/0                         |
| 610   | HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,                                                                                 | 05/2015          | 678.54 -                | 678.54           | .00                         | 03/2019 -             | 03/2020     | 12(O) -                                    | 0/38                        |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                    |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|----------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                            | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                  | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 611   | EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects | 10/2006          | 11,589.00<br>30,357.00  | 28,181.00        | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 612   | KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,                                                    | 04/2015          | 2,063.03<br>-           | 2,063.03         | 368.22                      | 03/2021<br>-          | 03/2021     | 0(O)<br>-                                  | 0/0                         |
| 613   | GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,                                        | 04/2015          | 636.38<br>-             | 636.38           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 614   | MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE ,                         | 12/2015          | 1,08,000.00<br>-        | 1,08,000.00      | 1,057.80                    | 12/2023<br>12/2023    | 12/2023     | 0(O)<br>0(R)                               | 0/0                         |
| 615   | WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE ,                                 | 11/2007          | 16,592.00<br>51,101.00  | 51,101.00        | 22,485.00                   | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 616   | CHANDIGARH-BADDI - [N22000467]JNR,MULTI STATE ,                                                    | 04/2007          | 328.14<br>-             | 1,540.00         | 229.95                      | 03/2023<br>-          | 03/2023     | 0(O)<br>-                                  | 0/0                         |
| 617   | JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]JNR,MULTI STATE ,                                      | 03/2002          | 625.00<br>-             | 845.58           | .00                         | 03/2016<br>-          | -           | -                                          | 0/0                         |
| 618   | NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,         | 04/2006          | 2,326.52<br>2,446.57    | 3,000.00         | 677.37                      | 03/2015<br>10/2021    | 10/2021     | 79(O)<br>0(R)                              | 0/0                         |
| 619   | DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,                                                       | 04/2013          | 4,274.00<br>-           | 4,274.00         | .00                         | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 620   | KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,                                            | 04/1994          | 2,923.13<br>-           | 3,798.80         | 1,123.73                    | 03/2009<br>-          | 06/2021     | 147(O)<br>-                                | 0/0                         |
| 621   | HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,                                                 | 04/1996          | 1,185.64<br>-           | 1,844.47         | 1,406.23                    | 12/2017<br>-          | 03/2020     | 27(O)<br>-                                 | 0/0                         |
| 622   | SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,                                         | 04/1998          | 1,202.70<br>245.00      | 1,202.70         | 698.59                      | 02/2015<br>-          | 12/2021     | 82(O)<br>-                                 | 0/0                         |
| 623   | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,                               | 04/2000          | 133.41<br>207.00        | 385.00           | 377.10                      | 03/2009<br>03/2009    | 02/2019     | 119(O)<br>119(R)                           | 1/1                         |
| 624   | TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,                                            | 04/2005          | 810.78<br>-             | 1,928.07         | 574.98                      | 06/2021<br>-          | 03/2023     | 21(O)<br>-                                 | 0/0                         |
| 625   | CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,                                | 04/2010          | 149.90<br>-             | 230.00           | 54.96                       | 03/2015<br>-          | -           | -                                          | 0/0                         |
| 626   | SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,                                              | 03/2011          | 1,111.99<br>1,539.28    | 1,539.28         | 765.60                      | 02/2019<br>-          | 03/2021     | 25(O)<br>-                                 | 0/0                         |
| 627   | BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,                                             | 03/2013          | 843.04<br>843.04        | 843.04           | 81.26                       | 10/2020<br>-          | 03/2021     | 5(O)<br>-                                  | 0/0                         |
| 628   | SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,                                  | 03/2012          | 155.81<br>-             | 238.03           | 180.78                      | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 629   | JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,                                             | 04/2015          | 1,547.38<br>-           | 1,547.38         | 189.40                      | 03/2022<br>-          | 03/2022     | 0(O)<br>-                                  | 0/0                         |
| 630   | KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,                                        | 04/2015          | 2,361.74<br>-           | 2,361.74         | 81.06                       | 03/2022<br>-          | 03/2022     | 0(O)<br>-                                  | 0/0                         |
| 631   | JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,     | 04/2015          | 701.61<br>-             | 810.02           | 88.04                       | 11/2018<br>-          | 03/2021     | 28(O)<br>-                                 | 0/0                         |
| 632   | BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,                    | 04/2015          | 1,172.92<br>-           | 1,172.92         | 245.16                      | 12/2018<br>-          | 03/2021     | 27(O)<br>-                                 | 0/0                         |
| 633   | ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,                                    | 11/2015          | 969.83<br>-             | 1,151.81         | 389.91                      | 03/2020<br>03/2020    | 06/2020     | 3(O)<br>3(R)                               | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                        |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                      | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 634   | RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA , | 04/1995          | 524.43 -                | 939.00           | 184.10                      | 12/2021<br>12/2024    | 12/2024     | 36(O)<br>0(R)                              | 0/0                         |
| 635   | VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,                                                           | 01/1991          | 2,335.67<br>2,335.67    | 2,335.67         | 316.27                      | 12/2024<br>-          | 12/2024     | 0(O)<br>-                                  | 0/0                         |
| 636   | SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,                                                            | 03/2006          | 948.04 -                | 970.00           | 910.62                      | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 637   | BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,                                                              | 03/2009          | 942.95 -                | 942.95           | 887.88                      | 03/2019<br>-          | 03/2021     | 24(O)<br>-                                 | 0/0                         |
| 638   | EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA ,           | 04/2016          | 5,200.00 -              | 5,200.00         | .00                         | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 639   | MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB ,       | 04/2009          | 396.04 -                | 369.00           | 186.27                      | -<br>-                | -           | -                                          | 0/0                         |
| 640   | QADIAN-BEAS - [N22000295]NR,PUNJAB ,                                                                                   | 04/2011          | 205.22 -                | 205.22           | 3.18                        | -<br>-                | -           | -                                          | 0/0                         |
| 641   | DAUSA-GANGAPUR CITY(NL) NWR - [220100184]NWR,RAJASTHAN ,                                                               | 02/1997          | 410.08<br>780.98        | 795.01           | 458.50                      | 02/2019<br>-          | 02/2019     | 0(O)<br>-                                  | 0/0                         |
| 642   | HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN ,                                              | 04/2008          | 829.74 -                | 1,216.00         | 730.74                      | 03/2015<br>-          | 06/2020     | 63(O)<br>-                                 | 0/0                         |
| 643   | JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN ,                         | 04/2008          | 653.19 -                | 1,116.00         | 820.02                      | 03/2014<br>03/2019    | 03/2019     | 60(O)<br>0(R)                              | 0/0                         |
| 644   | BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,                                                          | 04/2012          | 246.08 -                | 348.55           | 139.09                      | 12/2019<br>-          | 06/2019     | -6(O)<br>-                                 | 0/0                         |
| 645   | THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,                                                                        | 04/2013          | 236.93 -                | 294.90           | 165.26                      | 10/2018<br>-          | 10/2018     | -                                          | 0/0                         |
| 646   | AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,                                                            | 04/2013          | 822.00 -                | 1,099.54         | .00                         | -<br>-                | -           | -                                          | 0/1                         |
| 647   | PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,                                                                             | 04/2013          | 323.00 -                | 432.22           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 648   | MAVLI JUNCTION-BARI SADRI MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,                                | 04/2013          | 420.18<br>295.02        | 420.18           | 89.61                       | 03/2020<br>-          | 12/2019     | -3(O)<br>-                                 | 0/0                         |
| 649   | AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,                                                                          | 04/2011          | 213.39 -                | 244.02           | 217.81                      | 11/2019<br>-          | 11/2019     | 0(O)<br>-                                  | 0/0                         |
| 650   | ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN ,                                                                   | 04/2013          | 242.09 -                | 349.00           | 293.97                      | 02/2019<br>-          | 03/2019     | 1(O)<br>-                                  | 0/0                         |
| 651   | AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,                          | 05/2015          | 873.71 -                | 1,103.04         | 2.32                        | -<br>-                | -           | -                                          | 0/0                         |
| 652   | MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,                                                   | 01/2011          | 493.17 -                | 493.17           | 413.97                      | 03/2018<br>-          | 12/2019     | 21(O)<br>-                                 | 0/0                         |
| 653   | JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN ,                                          | 08/2018          | 808.85 -                | 808.85           | .00                         | 08/2022<br>-          | 08/2022     | 0(O)<br>-                                  | 0/0                         |
| 654   | SEVOK RANGPO NEFR - [N22000102]NFR,SIKKIM ,                                                                            | 04/2008          | 1,339.48 -              | 4,084.69         | 383.92                      | 12/2015<br>-          | 03/2020     | 51(O)<br>-                                 | 0/0                         |
| 655   | KARUR-SALEM(NL) SR - [220100191]SR,TAMIL NADU ,                                                                        | 02/1997          | 155.55 -                | 920.00           | 856.94                      | -<br>-                | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                           |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-----------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                   | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                         | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 656   | EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS MTP - [N22000028]MRTP,TAMIL NADU ,                        | 04/2006          | 495.74<br>495.74        | 734.01           | 445.91                      | 06/2013<br>03/2019    | 03/2019     | 69(O)<br>0(R)                              | 1/4                         |
| 657   | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,             | 09/2007          | 724.69<br>-             | 2,072.50         | 1,169.07                    | 02/2019<br>-          | 02/2019     | 0(O)<br>-                                  | 0/0                         |
| 658   | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU ,                            | 09/2006          | 343.17<br>-             | 1,065.00         | 1,049.68                    | -<br>-                | -           | -                                          | 0/0                         |
| 659   | TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU ,                                        | 09/2006          | 227.40<br>-             | 900.00           | 61.97                       | -<br>-                | -           | -                                          | 0/0                         |
| 660   | TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,                                                        | 09/2006          | 582.83<br>-             | 2,300.00         | 237.73                      | -<br>-                | -           | -                                          | 0/0                         |
| 661   | ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU ,                                                            | 04/2008          | 151.84<br>-             | 1,105.00         | 3.34                        | 02/2019<br>-          | 02/2019     | 0(O)<br>-                                  | 0/0                         |
| 662   | SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU , | 04/2013          | 839.00<br>-             | 1,500.00         | .61                         | -<br>-                | -           | -                                          | 0/0                         |
| 663   | CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU ,                                         | 04/1999          | 198.68<br>-             | 556.64           | 303.72                      | -<br>-                | -           | -                                          | 0/0                         |
| 664   | CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU ,                              | 04/1998          | 271.24<br>-             | 520.00           | 468.18                      | -<br>-                | -           | -                                          | 0/0                         |
| 665   | ERODE-PALANI - [N22000199]SR,TAMIL NADU ,                                                                 | 04/2008          | 288.57<br>-             | 1,140.00         | 1.63                        | -<br>-                | -           | -                                          | 0/0                         |
| 666   | MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,                                                       | 04/2008          | 164.41<br>-             | 450.00           | 83.15                       | -<br>-                | 03/2020     | -<br>-                                     | 0/0                         |
| 667   | OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU ,                        | 10/2013          | 187.26<br>-             | 231.67           | 7.62                        | 04/2014<br>-          | 03/2020     | 71(O)<br>-                                 | 0/0                         |
| 668   | MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION - [N22000439]SR,TAMIL NADU ,                               | 02/1997          | 458.63<br>-             | 458.63           | .92                         | 03/2015<br>-          | -           | -                                          | 0/0                         |
| 669   | TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION - [N22000440]SR,TAMIL NADU ,                               | 02/2000          | 200.84<br>-             | 200.84           | 394.26                      | 03/2014<br>-          | -           | -                                          | 0/0                         |
| 670   | THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU ,                | 02/1996          | 268.87<br>-             | 302.02           | 304.07                      | 03/2005<br>-          | -           | -                                          | 0/0                         |
| 671   | ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU ,                        | 02/1999          | 257.00<br>-             | 257.00           | .00                         | 03/2018<br>-          | 03/2018     | -                                          | 0/0                         |
| 672   | TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU ,                     | 02/2017          | 1,567.00<br>-           | 1,567.00         | .00                         | 03/2024<br>-          | 03/2026     | 24(O)<br>-                                 | 0/0                         |
| 673   | VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]SR,TAMIL NADU ,                               | 02/2005          | 600.00<br>600.00        | 645.54           | 671.00                      | 03/2010<br>-          | -           | -                                          | 0/0                         |
| 674   | MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU ,                                      | 02/2015          | 1,700.00<br>-           | 1,700.00         | .00                         | 03/2022<br>-          | 03/2022     | 0(O)<br>-                                  | 0/0                         |
| 675   | MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANNAL ROAD) (62.05 KM) DOUBLING - [N22000450]SR,TAMIL NADU ,    | 02/2003          | 199.55<br>-             | 330.32           | 2.12                        | 03/2009<br>-          | -           | -                                          | 0/0                         |
| 676   | MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU ,                            | 02/2015          | 760.00<br>-             | 1,182.31         | .00                         | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 677   | MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION - [N22000453]SR,TAMIL NADU ,                       | 02/2006          | 208.00<br>-             | 208.00           | 3.58                        | 03/2012<br>-          | -           | -                                          | 0/0                         |
| 678   | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA ,                                       | 12/1994          | 124.43<br>-             | 1,025.00         | 1,021.82                    | -<br>-                | 03/2017     | -                                          | 0/0                         |
| 679   | MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA ,                                                   | 07/1998          | 458.25<br>-             | 458.26           | 3.69                        | -<br>-                | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                   |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                           | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                 | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 680   | MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,                                                                   | 04/2006          | 1,160.48 -              | 1,160.47         | 111.36                      | 03/2010 -             | 03/2022     | 144(O) -                                   | 0/1                         |
| 681   | MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,                                               | 04/2012          | 632.68 -                | 816.55           | 846.22                      | 03/2016 03/2017       | 12/2020     | 57(O) 45(R)                                | 0/0                         |
| 682   | MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,                                                                                  | 04/2013          | 1,112.00 -              | 2,911.84         | .92                         | - -                   | -           | -                                          | 0/1                         |
| 683   | KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA ,                                                                                | 04/2013          | 723.00 -                | 616.08           | .00                         | - -                   | -           | -                                          | 0/1                         |
| 684   | DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,                           | 03/2015          | 636.38 -                | 636.38           | 169.16                      | 03/2021 -             | 03/2021     | 0(O) -                                     | 3/3                         |
| 685   | SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,                                                                  | 04/2015          | 773.94 -                | 773.94           | 412.07                      | 12/2024 -             | 12/2024     | 0(O) -                                     | 0/0                         |
| 686   | MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA , | 04/2017          | 119.73 185.00           | 184.97           | .00                         | 03/2022 -             | 03/2022     | 0(O) -                                     | 0/0                         |
| 687   | AGARTALA SABROOM NL NEFR - [N22000099]NFR,TRIPURA ,                                                                               | 04/2008          | 1,142.00 3,407.00       | 3,407.00         | 3,112.16                    | 03/2014 12/2019       | 03/2019     | 60(O) -9(R)                                | 0/0                         |
| 688   | CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA - [N22000194]NFR,TRIPURA ,                                                            | 04/1999          | 895.00 984.97           | 1,733.20         | 1,549.55                    | 03/2007 -             | 04/2016     | -                                          | 0/0                         |
| 689   | AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,                                                                                    | 04/2012          | 569.63 -                | 650.00           | .00                         | 03/2020 -             | 10/2022     | 31(O) -                                    | 2/3                         |
| 690   | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH ,                                                       | 04/1999          | 108.00 -                | 432.72           | 446.52                      | 12/2009 -             | -           | -                                          | 0/0                         |
| 691   | ETAWAH-MAINPURI (NL) NCR - [220100318]NCR,UTTAR PRADESH ,                                                                         | 04/1997          | 120.00 -                | 245.39           | 210.67                      | 12/2008 -             | -           | -                                          | 0/0                         |
| 692   | UTRATIA-ZAFRABAD NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH ,                                                               | 04/2006          | 369.90 -                | 1,581.53         | 618.19                      | 03/2010 -             | -           | -                                          | 0/0                         |
| 693   | ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,                                      | 02/2008          | 171.10 -                | 275.08           | 141.55                      | 03/2012 -             | -           | -                                          | 0/0                         |
| 694   | ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,                                                            | 03/2013          | 307.00 -                | 308.00           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 695   | BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH ,                                                                   | 03/2008          | 195.64 -                | 435.00           | 451.80                      | - -                   | 03/2018     | -                                          | 0/0                         |
| 696   | AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH ,                                                           | 03/2012          | 199.75 -                | 270.00           | 263.56                      | 08/2018 -             | 01/2019     | 5(O) -                                     | 0/0                         |
| 697   | KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,                                       | 03/2013          | 643.00 -                | 644.00           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 698   | MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH ,                                                                      | 04/2012          | 377.44 -                | 377.44           | 182.85                      | - -                   | -           | -                                          | 0/0                         |
| 699   | FAIZABAD-LALGANJ VIA AKBARGANJ MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH ,                                          | 04/2013          | 654.00 -                | 654.00           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 700   | UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH ,                                                                                   | 04/2012          | 1,229.00 -              | 380.00           | 4.12                        | - -                   | -           | -                                          | 0/0                         |
| 701   | GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH ,                                                                      | 04/2014          | 182.92 -                | 197.73           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 702   | ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,                                                              | 03/2015          | 1,295.42 -              | 1,295.42         | 99.33                       | 03/2022 -             | 02/2019     | -37(O) -                                   | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                 |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-----------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                         | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                               | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 703   | MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,                                                  | 04/2015          | 668.70<br>668.00        | 668.00           | .00                         | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/6                         |
| 704   | VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,                                        | 04/2015          | 943.60<br>-             | 943.60           | 298.09                      | 03/2022<br>-          | 12/2024     | 33(O)<br>-                                 | 0/0                         |
| 705   | LUCKNOW- PILIBHIT VIA SITAPUR LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,                                    | 04/2011          | 927.01<br>-             | 977.00           | 983.62                      | 03/2019<br>-          | 03/2020     | 12(O)<br>-                                 | 0/0                         |
| 706   | MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,                                                | 04/2015          | 1,765.92<br>-           | 1,765.92         | 335.37                      | 03/2023<br>-          | 12/2024     | 21(O)<br>-                                 | 0/0                         |
| 707   | BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,                                | 03/2012          | 1,183.25<br>-           | 1,183.25         | 1,002.84                    | 12/2020<br>-          | 03/2021     | 3(O)<br>-                                  | 0/0                         |
| 708   | RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH ,                                                     | 08/2015          | 2,436.21<br>-           | 2,436.21         | 291.68                      | 03/2020<br>-          | 03/2021     | 12(O)<br>-                                 | 0/0                         |
| 709   | KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH ,                                            | 08/2015          | 528.57<br>-             | 528.57           | 19.97                       | 03/2019<br>-          | 12/2019     | 9(O)<br>-                                  | 0/0                         |
| 710   | GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]NER,UTTAR PRADESH ,                  | 04/1997          | 233.00<br>-             | 318.42           | 339.23                      | 04/1999<br>-          | -           | -                                          | 0/0                         |
| 711   | INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH ,                                           | 04/2016          | 213.00<br>-             | 213.35           | .55                         | 04/2016<br>-          | 01/2022     | 69(O)<br>-                                 | 0/0                         |
| 712   | BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH ,              | 04/2016          | 1,900.00<br>-           | 1,277.06         | .00                         | 01/2022<br>-          | 01/2022     | 0(O)<br>-                                  | 0/0                         |
| 713   | MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]NER,UTTAR PRADESH ,                                        | 04/1997          | 609.04<br>1,063.00      | 1,807.88         | 1,805.97                    | 04/1999<br>-          | 03/2019     | 239(O)<br>-                                | 0/0                         |
| 714   | NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH ,                                          | 04/2017          | 150.00<br>-             | 150.00           | .00                         | 04/2017<br>-          | 10/2022     | 66(O)<br>-                                 | 0/0                         |
| 715   | PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH ,                                 | 04/2017          | 1,343.00<br>-           | 1,343.00         | .00                         | 01/2018<br>-          | -           | -                                          | 0/0                         |
| 716   | PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH ,                                       | 04/2017          | 622.50<br>427.00        | 426.74           | 40.34                       | 04/2017<br>-          | 10/2022     | 66(O)<br>-                                 | 0/0                         |
| 717   | ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH ,                                                      | 04/2017          | 276.90<br>-             | 276.90           | .00                         | 04/2017<br>-          | 04/2022     | 60(O)<br>-                                 | 0/0                         |
| 718   | BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH ,                                            | 04/2016          | 602.50<br>-             | 714.34           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 719   | AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH ,                                            | 04/2016          | 600.00<br>-             | 366.71           | .46                         | 01/2022<br>-          | 01/2022     | 0(O)<br>-                                  | 0/0                         |
| 720   | SHAHGANJ-BHATNI-PHEPHNA-INDARA MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH , | 04/2016          | 1,177.96<br>-           | 1,028.95         | 1.54                        | 03/2014<br>-          | 04/2021     | 85(O)<br>-                                 | 0/0                         |
| 721   | JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH ,                                   | 03/2018          | 4,329.53<br>-           | 4,329.53         | .00                         | 03/2023<br>-          | 03/2023     | 0(O)<br>-                                  | 0/0                         |
| 722   | JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH ,                                                           | 09/2016          | 2,001.00<br>-           | 2,001.00         | .00                         | 03/2021<br>-          | 03/2021     | 0(O)<br>-                                  | 0/0                         |
| 723   | KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,                                                        | 04/2003          | 142.45<br>-             | 228.40           | .15                         | -<br>-                | -           | -                                          | 0/0                         |
| 724   | HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,                                                                   | 04/2012          | 219.83<br>-             | 346.63           | 38.33                       | -<br>-                | -           | -                                          | 0/0                         |
| 725   | RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,                                                | 04/2011          | 16,216.00<br>-          | 16,216.00        | 861.35                      | 12/2024<br>-          | 03/2026     | 15(O)<br>-                                 | 0/0                         |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                   |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                           | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                 | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 726   | NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL) NEFR - [220100135]NFR, WEST BENGAL ,                           | 04/1983          | 297.32<br>200.34        | 614.00           | 270.27                      | 03/2019<br>-          | 03/2020     | 12(O)<br>-                                 | 0/0                         |
| 727   | HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL ,                                                                  | 04/1974          | 393.46<br>154.30        | 1,026.00         | 182.49                      | 03/2007<br>03/2007    | -           | -                                          | 0/0                         |
| 728   | TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL ,                  | 03/2000          | 1,049.69<br>-           | 3,404.92         | 3,544.30                    | 12/2006<br>-          | -           | -                                          | 0/0                         |
| 729   | TARAKESWAR - BISHNUPUR NEW BG LINE (NL) ER - [220100272]ER, WEST BENGAL ,                                                         | 04/2000          | 1,188.91<br>-           | 1,620.01         | 844.12                      | 03/2019<br>12/2009    | 03/2019     | 0(O)<br>111(R)                             | 0/0                         |
| 730   | BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL ,                                                                               | 04/2007          | 1,106.62<br>-           | 1,092.20         | 620.93                      | 12/2010<br>-          | -           | -                                          | 7/7                         |
| 731   | TAMLUK DIGHA LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL ,                                                                  | 03/1984          | 293.97<br>-             | 749.69           | .00                         | 06/2005<br>-          | -           | -                                          | 0/0                         |
| 732   | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL ,           | 04/2010          | 2,397.72<br>-           | 2,397.72         | 197.20                      | 03/2016<br>-          | -           | -                                          | 0/0                         |
| 733   | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL , | 04/2010          | 2,298.42<br>-           | 2,733.86         | 347.70                      | 03/2014<br>-          | 12/2025     | 141(O)<br>-                                | 0/0                         |
| 734   | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL ,     | 04/2010          | 3,951.98<br>-           | 4,259.48         | 1,685.82                    | 03/2016<br>-          | 03/2025     | 108(O)<br>-                                | 0/0                         |
| 735   | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL ,                 | 04/2010          | 2,913.51<br>4,200.00    | 2,913.50         | 885.48                      | 03/2016<br>-          | 03/2025     | 108(O)<br>-                                | 0/0                         |
| 736   | DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL ,                                                                    | 04/2009          | 259.51<br>-             | 533.59           | 145.79                      | 02/2012<br>-          | -           | -                                          | 0/0                         |
| 737   | GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL ,                                                                          | 04/2009          | 193.08<br>-             | 612.45           | 150.71                      | 12/2011<br>-          | -           | -                                          | 0/0                         |
| 738   | EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL ,                                         | 03/2013          | 4,874.58<br>-           | 4,874.58         | 1,881.65                    | 03/2016<br>-          | -           | -                                          | 0/0                         |
| 739   | BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL ,                                                                              | 04/2010          | 267.37<br>-             | 620.00           | 40.77                       | -<br>03/2025          | 03/2025     | -<br>0(R)                                  | 0/0                         |
| 740   | BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL ,                                                               | 04/2011          | 289.64<br>-             | 760.00           | .13                         | -<br>-                | -           | -                                          | 0/0                         |
| 741   | NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL ,                                                          | 04/2010          | 221.42<br>-             | 380.00           | 101.10                      | -<br>-                | 03/2020     | -<br>-                                     | 0/0                         |
| 742   | CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL ,                                           | 04/2009          | 573.78<br>-             | 268.52           | .67                         | -<br>-                | -           | -                                          | 0/0                         |
| 743   | BAZAR SAU - AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL ,                                                                  | 04/2012          | 255.64<br>-             | 272.20           | 89.78                       | -<br>-                | -           | -                                          | 0/0                         |
| 744   | MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL ,                                                                        | 04/2011          | 276.69<br>-             | 426.00           | .00                         | -<br>03/2030          | 03/2030     | -<br>0(R)                                  | 0/0                         |
| 745   | NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL ,                                  | 04/2016          | 602.27<br>-             | 612.00           | 23.69                       | 12/2021<br>-          | 03/2020     | -21(O)<br>-                                | 0/0                         |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                              |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|----------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                      | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                            | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 746   | TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER, WEST BENGAL ,               | 01/1991          | 1,013.45<br>1,013.45    | 1,428.00         | 484.49                      | 12/2021<br>12/2021    | 12/2021     | 0(O)<br>0(R)                               | 0/0                         |
| 747   | BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL ,                                                    | 04/1998          | 1,027.40<br>1,966.70    | 2,373.00         | 484.85                      | 03/2003<br>03/2030    | 03/2030     | 324(O)<br>0(R)                             | 0/0                         |
|       | Total                                                                                                                                        |                  | 4,85,710.46<br>-        | 6,96,269.31      | 1,66,896.81                 |                       |             |                                            | 18/104                      |
|       |                                                                                                                                              |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                                           |                  |                         |                  |                             |                       |             |                                            |                             |
| 748   | CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 ( - [N24000744]NHIDCL,A & N ISLANDS ,     | 03/2015          | 262.97<br>-             | 262.97           | .00                         | 10/2018<br>-          | -           | -                                          | 0/0                         |
| 749   | 2 LANE WITH HARD SHOLDER REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS ,       | 03/2017          | 409.85<br>-             | 409.85           | .00                         | 12/2017<br>-          | -           | -                                          | 0/4                         |
| 750   | CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS ,     | 03/2015          | 277.17<br>-             | 277.17           | .00                         | 04/2017<br>-          | -           | -                                          | 0/4                         |
| 751   | REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS ,     | 02/2018          | 391.00<br>-             | 391.00           | .00                         | 10/2018<br>-          | -           | -                                          | 0/4                         |
| 752   | REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS ,     | 03/2018          | 234.27<br>-             | 234.27           | .00                         | 10/2018<br>-          | -           | -                                          | 0/4                         |
| 753   | Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MORTH,A & N ISLANDS ,      | 11/2017          | 237.80<br>-             | 238.00           | 29.43                       | 11/2019<br>-          | 11/2019     | 0(O)<br>-                                  | 0/0                         |
| 754   | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MORTH,A & N ISLANDS ,      | 11/2017          | 257.34<br>-             | 238.00           | 41.09                       | 11/2019<br>12/2019    | 11/2019     | 0(O)<br>-1(R)                              | 0/0                         |
| 755   | CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH , PPP (BOT)                                                  | 11/2010          | 1,585.00<br>-           | 1,585.00         | 2,167.31                    | 05/2013<br>-          | 04/2019     | 71(O)<br>-                                 | 0/0                         |
| 756   | TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)                                                                  | 04/2011          | 571.00<br>-             | 571.00           | 582.52                      | 10/2013<br>-          | 12/2018     | 62(O)<br>-                                 | 0/0                         |
| 757   | SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)                                 | 11/2011          | 1,535.00<br>-           | 1,535.00         | 2,993.77                    | 05/2014<br>-          | -           | -                                          | 0/0                         |
| 758   | REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH , EPC | 12/2014          | 201.12<br>201.00        | 201.12           | .00                         | 02/2015<br>-          | -           | -                                          | 0/4                         |
| 759   | REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION ) - [N24000263]PWD,ANDHRA PRADESH ,           | 02/2015          | 241.61<br>-             | 241.61           | 7.71                        | 02/2017<br>-          | -           | -                                          | 0/1                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                              |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|----------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                      | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                            | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 760   | REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH , EPC   | 11/2014          | 297.78<br>330.00        | 330.00           | .00                         | 02/2017<br>-          | -           | -                                          | 0/0                         |
| 761   | REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH ,        | 01/2014          | 361.30<br>-             | 207.40           | 44.08                       | 07/2014<br>-          | -           | -                                          | 0/1                         |
| 762   | REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE-DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH , EPC    | 02/2014          | 258.99<br>-             | 258.99           | 16.54                       | 07/2014<br>-          | -           | -                                          | 0/1                         |
| 763   | REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH , EPC   | 07/2014          | 251.55<br>-             | 251.55           | 7.74                        | 02/2015<br>-          | -           | -                                          | 0/1                         |
| 764   | REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH , EPC   | 03/2015          | 175.03<br>-             | 175.00           | .00                         | -<br>-                | -           | -                                          | 0/1                         |
| 765   | REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH , EPC   | 02/2015          | 266.00<br>-             | 266.00           | .00                         | -<br>-                | -           | -                                          | 0/4                         |
| 766   | REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH , EPC | 07/2015          | 314.43<br>-             | 314.43           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 767   | FOUR LANING OF 5.122 KM OF NH9 ( NEW NH 65) FROM KM 269.900 ( DESIGN CH0.0 ) TO KM 275-622( DESIGN C - [N24000274]PWD,ANDHRA PRADESH ,       | 07/2015          | 333.21<br>333.21        | 333.21           | .00                         | 12/2015<br>-          | -           | -                                          | 0/2                         |
| 768   | REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , EPC    | 01/2014          | 195.45<br>-             | 195.45           | .00                         | 11/2014<br>-          | -           | -                                          | 0/4                         |
| 769   | REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH , EPC      | 02/2014          | 170.21<br>-             | 170.21           | 5.65                        | 11/2014<br>-          | -           | -                                          | 0/4                         |
| 770   | REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH , EPC | 10/2015          | 480.21<br>-             | 480.21           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 771   | REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH , EPC                         | 02/2015          | 224.83<br>-             | 224.83           | .00                         | 05/2015<br>-          | -           | -                                          | 2/4                         |
| 772   | REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH , EPC    | 03/2015          | 309.01<br>-             | 309.01           | .00                         | 09/2015<br>-          | -           | -                                          | 0/4                         |
| 773   | REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH , EPC    | 03/2015          | 271.45<br>-             | 271.45           | .00                         | 10/2015<br>-          | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                           |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                                   | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                                         | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 774   | FOUR LANING OF 5.122 KM OF NH9( NEW NH 65) FROM KM 269.900( DESIGN CH.0.0 ) - [N24000302]PWD,ANDHRA PRADESH ,                                             | 07/2015          | 333.21 -                | 333.21           | .00                         | 12/2015 -             | -           | -                                          | 0/0                         |
| 775   | REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH , EPC                | 02/2014          | 417.61 -                | 417.61           | .00                         | 06/2014 -             | -           | -                                          | 0/2                         |
| 776   | FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC                | 10/2015          | 333.21 -                | 333.21           | .00                         | 11/2015 -             | -           | -                                          | 0/0                         |
| 777   | REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH , EPC                                                                 | 02/2015          | 224.83 -                | 224.83           | .00                         | 04/2015 -             | -           | -                                          | 0/0                         |
| 778   | FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,                                                  | 01/2016          | 1,134.97 -              | 1,134.97         | 28.73                       | 11/2018 -             | 11/2018     | -                                          | 0/0                         |
| 779   | VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,                                                                                         | 09/2014          | 1,684.00 -              | 1,684.00         | 54.13                       | 02/2017 -             | -           | -                                          | 0/0                         |
| 780   | REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH ,                                        | 03/2017          | 648.32 -                | 503.10           | 15.10                       | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/0                         |
| 781   | SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,                                   | 03/2017          | 1,041.62 -              | 1,187.10         | 43.99                       | 03/2020 -             | 05/2020     | 2(O) -                                     | 0/0                         |
| 782   | FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH , Central Sector Projects | 06/2017          | 648.33 -                | 648.33           | 15.89                       | 06/2017 -             | 11/2019     | 29(O) -                                    | 0/0                         |
| 783   | 6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,                   | 12/2017          | 328.67 -                | 328.67           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 784   | SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,                   | 12/2017          | 1,323.15 -              | 1,323.15         | .00                         | - -                   | -           | -                                          | 0/0                         |
| 785   | CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH ,                   | 12/2017          | 357.00 -                | 357.00           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 786   | SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH ,                   | 02/2018          | 1,959.00 -              | 1,959.00         | .00                         | - -                   | -           | -                                          | 0/0                         |
| 787   | FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH ,                    | 03/2018          | 1,532.62 -              | 1,532.62         | .00                         | 03/2021 -             | 03/2021     | 0(O) -                                     | 0/0                         |
| 788   | SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH ,                   | 03/2018          | 1,550.98 -              | 1,550.98         | .00                         | - -                   | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                     |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                             | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                                   | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 789   | REHABILITATION AND UPGRADEMENT OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH ,             | 03/2018          | 565.09 -                | 565.09           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 790   | CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH ,             | 03/2018          | 314.43 -                | 314.43           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 791   | CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH ,             | 03/2018          | 557.30 -                | 557.30           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 792   | TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , ITEM RATE | 12/2011          | 156.63 276.00           | 276.00           | 132.21                      | 02/2012 -             | -           | -                                          | 0/0                         |
| 793   | TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , ITEM RATE | 11/2010          | 305.49 -                | 305.49           | .00                         | 03/2011 -             | -           | -                                          | 0/0                         |
| 794   | TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , ITEM RATE  | 03/2012          | 207.03 -                | 207.03           | .00                         | 05/2012 -             | -           | -                                          | 0/0                         |
| 795   | 2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC    | 03/2015          | 194.11 -                | 194.11           | 30.54                       | 05/2018 -             | -           | -                                          | 1/4                         |
| 796   | 2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , EPC                                | 10/2015          | 179.82 -                | 179.82           | 8.99                        | 01/2019 -             | 01/2019     | 0(0) -                                     | 1/4                         |
| 797   | CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC    | 07/2015          | 197.16 -                | 197.16           | 38.50                       | 10/2018 -             | -           | -                                          | 1/4                         |
| 798   | 2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC                | 03/2015          | 394.00 -                | 394.00           | .00                         | 06/2018 -             | -           | -                                          | 0/3                         |
| 799   | FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH , ITEM RATE  | 01/2011          | 264.16 -                | 264.16           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 800   | TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH , ITEM RATE | 12/2009          | 165.00 -                | 165.00           | .00                         | 09/2010 -             | -           | -                                          | 0/0                         |
| 801   | TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH , ITEM RATE | 12/2009          | 104.00 -                | 201.00           | .00                         | 09/2010 -             | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                              |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|----------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                      | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                            | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 802   | 2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH , EPC                            | 03/2015          | 235.08 -                | 235.08           | 47.81                       | 05/2018 -             | -           | -                                          | 1/4                         |
| 803   | 2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH , | 01/2016          | 183.65 -                | 183.65           | .00                         | 11/2016 -             | -           | -                                          | 0/0                         |
| 804   | FUNDED ) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH , | 01/2016          | 334.22 -                | 334.22           | .00                         | 06/2016 -             | -           | -                                          | 0/4                         |
| 805   | CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD( NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH , | 04/2016          | 245.79 -                | 245.79           | .00                         | -                     | -           | -                                          | 0/0                         |
| 806   | CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH ,  | 04/2016          | 198.00 -                | 198.00           | .00                         | 10/2016 -             | -           | -                                          | 0/4                         |
| 807   | FUNDED ) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH , | 11/2015          | 434.06 -                | 434.06           | .00                         | -                     | -           | -                                          | 0/0                         |
| 808   | CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH ,                                | 12/2016          | 138.93 155.00           | 155.00           | .00                         | 01/2017 -             | 01/2020     | 36(O) -                                    | 0/0                         |
| 809   | CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH ,     | 01/2017          | 1,253.10 -              | 1,253.10         | .00                         | 03/2017 -             | -           | -                                          | 0/0                         |
| 810   | TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH , | 03/2017          | 284.09 -                | 284.09           | .00                         | 04/2017 -             | -           | -                                          | 0/0                         |
| 811   | TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH , | 02/2017          | 195.23 -                | 195.23           | .00                         | 04/2017 -             | -           | -                                          | 0/0                         |
| 812   | TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH , | 02/2017          | 203.36 -                | 203.36           | .00                         | 04/2017 -             | -           | -                                          | 0/0                         |
| 813   | TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH ,  | 01/2017          | 194.66 -                | 194.66           | .00                         | 04/2017 -             | -           | -                                          | 0/0                         |
| 814   | TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH ,  | 02/2017          | 168.32 -                | 168.32           | .00                         | 04/2017 -             | -           | -                                          | 0/0                         |
| 815   | TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,  | 02/2017          | 180.57 -                | 180.57           | .00                         | 04/2017 -             | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                              |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|----------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                      | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                            | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 816   | CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH , | 02/2017          | 216.71 -                | 216.71           | .00                         | 04/2017 -             | -           | -                                          | 0/0                         |
| 817   | CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH , | 02/2017          | 167.28 -                | 167.28           | .00                         | 04/2017 -             | -           | -                                          | 0/0                         |
| 818   | TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,  | 01/2017          | 198.22 -                | 198.22           | .00                         | 04/2017 -             | -           | -                                          | 0/0                         |
| 819   | FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH ,   | 03/2018          | 392.60 -                | 392.60           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 820   | HARANGAJO TO MAIBANG (AS-23) KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,                                                              | 12/2003          | 280.00 -                | 361.00           | 410.32                      | 02/2009 -             | 12/2018     | 118(O) -                                   | 0/0                         |
| 821   | MAIBANG TO LUMDING (AS-25) KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,                                                                 | 12/2003          | 199.81 -                | 385.13           | 209.80                      | 04/2009 -             | 03/2019     | 119(O) -                                   | 0/0                         |
| 822   | MAIBANG TO LUMDING (AS-26) KM.60.500 TO KM.83.400 NH-54 - [240106279]NHAI,ASSAM ,                                                            | 12/2003          | 167.64 -                | 167.64           | 268.94                      | 11/2008 -             | 09/2018     | -                                          | 0/0                         |
| 823   | MAIBANG TO LUMDING (AS-24) KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,                                                                | 12/2003          | 155.04 -                | 280.13           | 195.35                      | 11/2008 -             | -           | -                                          | 0/0                         |
| 824   | SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,                                                                                          | 12/2003          | 245.00 174.34           | 174.34           | 214.88                      | 03/2008 -             | 01/2019     | 130(O) -                                   | 0/0                         |
| 825   | NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,                                                                                            | 12/2003          | 225.00 -                | 225.00           | 312.79                      | 06/2008 -             | 04/2019     | 130(O) -                                   | 0/0                         |
| 826   | NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM ,                                                                                             | 12/2003          | 208.00 -                | 230.00           | 297.81                      | 04/2008 -             | 03/2019     | 131(O) -                                   | 0/0                         |
| 827   | DHARAMTUL TO SONAPUR KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,                                                                            | 12/2003          | 160.00 -                | 167.98           | 198.82                      | 05/2008 -             | 02/2019     | 129(O) -                                   | 0/0                         |
| 828   | HARANGAJO TO MAIBANG NH-54 - [N24000062]NHAI,ASSAM ,                                                                                         | 12/2003          | 196.00 -                | 331.23           | 340.12                      | 07/2009 -             | -           | -                                          | 0/0                         |
| 829   | BRAHMPUTRA BRIDGE NH NO-31 - [N24000063]NHAI,ASSAM ,                                                                                         | 12/2003          | 217.61 -                | 360.84           | 390.19                      | 04/2010 -             | 04/2019     | 108(O) -                                   | 0/0                         |
| 830   | FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC         | 05/2015          | 454.89 -                | 454.89           | 22.74                       | 05/2018 -             | -           | -                                          | 0/4                         |
| 831   | 4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC         | 06/2015          | 437.39 -                | 437.39           | 21.86                       | 06/2018 -             | -           | -                                          | 0/4                         |
| 832   | FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC         | 06/2015          | 463.49 -                | 463.49           | 9.26                        | 06/2018 -             | -           | -                                          | 0/4                         |
| 833   | FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC                              | 06/2016          | 829.00 -                | 829.00           | 59.85                       | 01/2019 -             | 01/2019     | 0(O) -                                     | 0/4                         |
| 834   | FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC                     | 03/2015          | 168.39 -                | 168.39           | 16.84                       | 11/2018 -             | -           | -                                          | 0/4                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                         |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                 | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                       | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 835   | 4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC     | 10/2014          | 588.95 -                | 588.95           | 80.00                       | 11/2018 -             | -           | -                                          | 0/4                         |
| 836   | 2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , EPC                     | 11/2010          | 268.08 -                | 268.08           | .00                         | 05/2017 -             | -           | -                                          | 0/0                         |
| 837   | 2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , ITEM RATE   | 11/2010          | 470.20 -                | 470.20           | .00                         | 02/2011 -             | -           | -                                          | 0/0                         |
| 838   | STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM , ITEM RATE | 05/2011          | 176.22 -                | 176.22           | .00                         | 02/2018 -             | -           | -                                          | 0/0                         |
| 839   | STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM , EPC        | 11/2014          | 218.31 -                | 218.31           | .00                         | 02/2018 -             | -           | -                                          | 0/0                         |
| 840   | 4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC         | 12/2015          | 225.02 -                | 159.20           | .00                         | 12/2018 -             | 12/2018     | 0(O) -                                     | 0/4                         |
| 841   | 4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC                   | 12/2015          | 223.30 -                | 223.30           | .00                         | 06/2018 -             | -           | -                                          | 0/0                         |
| 842   | 4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC                             | 01/1991          | 520.01 -                | 520.01           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 843   | 4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC         | 12/2015          | 289.99 -                | 289.99           | .00                         | 12/2018 -             | 12/2018     | 0(O) -                                     | 0/0                         |
| 844   | 4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC      | 01/2016          | 294.17 -                | 294.17           | .00                         | 01/2016 -             | -           | -                                          | 0/4                         |
| 845   | 4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC      | 01/2016          | 252.00 -                | 252.00           | .00                         | 01/2016 -             | -           | -                                          | 0/4                         |
| 846   | FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM ,        | 03/2015          | 829.00 -                | 829.00           | .00                         | 01/2016 -             | -           | -                                          | 0/0                         |
| 847   | PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)                                                                              | 08/2010          | 671.30 -                | 671.30           | 884.43                      | 02/2013 -             | 06/2019     | 76(O) -                                    | 0/0                         |
| 848   | 2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR , PPP (ANNUITY)                                                                      | 05/2011          | 351.54 -                | 351.54           | 351.23                      | 05/2013 -             | -           | -                                          | 0/0                         |
| 849   | PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)                                                              | 09/2011          | 574.00 -                | 574.00           | 768.62                      | 03/2014 -             | 12/2018     | 57(O) -                                    | 0/0                         |
| 850   | 2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,                                                                             | 10/2011          | 375.09 -                | 375.09           | 494.33                      | 04/2014 -             | -           | -                                          | 0/0                         |
| 851   | 4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)                                                                     | 01/2011          | 575.00 -                | 575.00           | 831.49                      | 07/2013 -             | 06/2019     | 71(O) -                                    | 0/0                         |
| 852   | 2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)                                                            | 05/2011          | 511.54 -                | 511.54           | 564.35                      | 11/2013 -             | 12/2018     | 61(O) -                                    | 0/0                         |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                           |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                   | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                         | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 853   | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , EPC       | 01/1991          | 675.00 -                | 675.00           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 854   | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR , ITEM RATE | 01/1991          | 282.41 -                | 282.41           | 67.52                       | 08/2016 -             | -           | -                                          | 0/0                         |
| 855   | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR , ITEM RATE | 01/1991          | 358.22 -                | 358.22           | 188.71                      | 10/2016 -             | -           | -                                          | 0/0                         |
| 856   | FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,                                                                                 | 08/2015          | 556.07 -                | 556.07           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 857   | FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,                                                                     | 12/2015          | 1,041.10 -              | 1,041.10         | 175.85                      | 04/2019 -             | 04/2019     | 0(O) -                                     | 0/0                         |
| 858   | FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,                                                                               | 08/2015          | 814.04 -                | 814.04           | 261.47                      | - -                   | 01/2020     | - -                                        | 0/0                         |
| 859   | FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,                                                                             | 08/2015          | 322.09 -                | 322.09           | 71.28                       | 04/2018 -             | 04/2020     | 24(O) -                                    | 0/0                         |
| 860   | FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,                                                                                 | 01/1991          | 642.41 -                | 642.41           | 9.45                        | - -                   | 10/2020     | - -                                        | 0/0                         |
| 861   | FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,                                                           | 12/2015          | 1,167.45 -              | 1,167.45         | 33.45                       | - -                   | 12/2019     | - -                                        | 0/0                         |
| 862   | TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,                                                            | 08/2015          | 399.54 -                | 399.54           | 142.41                      | 04/2019 -             | 10/2019     | 6(O) -                                     | 0/0                         |
| 863   | REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR ,                           | 01/1991          | 478.35 -                | 478.35           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 864   | TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,                                                                        | 08/2015          | 854.80 -                | 854.80           | 551.98                      | - -                   | 03/2019     | - -                                        | 0/0                         |
| 865   | TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,                                                           | 08/2015          | 516.13 -                | 516.13           | 400.35                      | 04/2018 -             | 12/2018     | 8(O) -                                     | 0/0                         |
| 866   | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , EPC          | 01/1991          | 154.62 -                | 154.62           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 867   | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC          | 01/1991          | 319.68 -                | 319.68           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 868   | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR ,           | 10/2014          | 377.64 -                | 377.64           | .00                         | 03/2014 -             | -           | -                                          | 0/0                         |
| 869   | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR ,           | 10/2013          | 278.39 -                | 278.39           | .00                         | 08/2014 -             | -           | -                                          | 0/0                         |
| 870   | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR ,           | 01/2013          | 322.01 -                | 322.01           | .00                         | 08/2014 -             | -           | -                                          | 0/0                         |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                   |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                           | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                 | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 871   | ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR ,     | 11/2013          | 683.83 -                | 683.83           | .00                         | 07/2016 -             | -           | -                                          | 0/0                         |
| 872   | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR ,    | 02/2014          | 665.50 -                | 665.50           | .00                         | 07/2016 -             | -           | -                                          | 0/0                         |
| 873   | ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR ,     | 02/2016          | 178.85 -                | 178.85           | .00                         | 05/2016 -             | -           | -                                          | 0/0                         |
| 874   | ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR ,     | 02/2016          | 369.77 -                | 369.77           | .00                         | 06/2016 -             | -           | -                                          | 0/0                         |
| 875   | ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR ,     | 02/2016          | 553.30 -                | 553.30           | .00                         | 05/2016 -             | -           | -                                          | 0/0                         |
| 876   | FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR ,     | 01/2014          | 1,408.85 -              | 1,408.85         | .00                         | 10/2016 -             | -           | -                                          | 0/0                         |
| 877   | STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR ,   | 03/2015          | 206.80 -                | 206.80           | .00                         | 07/2016 -             | -           | -                                          | 0/0                         |
| 878   | CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR ,                    | 08/2015          | 288.24 -                | 288.24           | .00                         | 11/2015 -             | -           | -                                          | 0/0                         |
| 879   | BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,                                                        | 05/2015          | 581.84 -                | 581.84           | 77.43                       | 05/2017 -             | 06/2019     | 25(O) -                                    | 0/0                         |
| 880   | REHABILATION OF 4-LANE 5.575 KM LONG 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR ,     | 08/2016          | 1,742.01 -              | 1,742.01         | .00                         | 12/2016 -             | -           | -                                          | 0/0                         |
| 881   | TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,     | 03/2017          | 672.89 -                | 736.01           | .00                         | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/0                         |
| 882   | CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,    | 03/2017          | 235.48 -                | 227.77           | .00                         | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/0                         |
| 883   | SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects | 08/2017          | 950.64 -                | 950.64           | .00                         | 08/2017 -             | -           | -                                          | 0/0                         |
| 884   | CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,    | 12/2017          | 2,598.00 -              | 2,598.00         | .00                         | -                     | -           | -                                          | 0/0                         |
| 885   | REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,          | 01/2018          | 573.70 -                | 573.70           | .00                         | -                     | -           | -                                          | 0/0                         |
| 886   | SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,                                 | 01/2018          | 895.39 -                | 895.39           | .00                         | -                     | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                            |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|--------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                    | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                          | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 887   | DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR ,             | 03/2018          | 496.20<br>-             | 496.20           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 888   | REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH , EPC             | 10/2014          | 213.47<br>-             | 213.47           | .00                         | 03/2015<br>-          | -           | -                                          | 0/0                         |
| 889   | REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 ( BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH , EPC           | 10/2014          | 298.34<br>-             | 298.34           | .00                         | 03/2015<br>-          | -           | -                                          | 0/0                         |
| 890   | REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH , EPC    | 11/2014          | 262.54<br>-             | 262.54           | .00                         | 03/2015<br>-          | -           | -                                          | 0/0                         |
| 891   | REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC           | 12/2015          | 291.05<br>-             | 291.05           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 892   | CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- [N24000283]PWD,CHHATISGARH , ITEM RATE | 12/2010          | 169.26<br>-             | 169.26           | .00                         | 12/2012<br>-          | -           | -                                          | 0/0                         |
| 893   | REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIGMA SECTION. - [N24000286]PWD,CHHATISGARH , EPC            | 12/2014          | 394.20<br>-             | 394.20           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 894   | REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , EPC     | 11/2015          | 485.44<br>-             | 485.44           | .00                         | 12/2015<br>-          | -           | -                                          | 0/0                         |
| 895   | REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH , EPC  | 03/2015          | 422.34<br>-             | 422.34           | 22.25                       | -<br>-                | -           | -                                          | 0/0                         |
| 896   | FOUR LANING OF SIGMA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,                                                                            | 12/2015          | 596.67<br>-             | 596.67           | 41.87                       | 05/2018<br>-          | 06/2019     | 13(O)<br>-                                 | 0/0                         |
| 897   | FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,                                                                         | 12/2015          | 509.13<br>-             | 509.13           | 7.21                        | 04/2018<br>-          | -           | -                                          | 0/0                         |
| 898   | FOUR / SIX LANING OF RAIPUR - SIGMA ( PKG-1) - [N24000510]NHAI,CHHATISGARH ,                                                               | 12/2015          | 726.67<br>-             | 726.67           | 50.67                       | 04/2018<br>-          | 06/2019     | 14(O)<br>-                                 | 0/0                         |
| 899   | 4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH ,        | 03/2018          | 1,029.96<br>-           | 1,029.96         | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 900   | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-I)_ NEW - [N24000609]NHAI,DELHI ,                                              | 09/2015          | 771.18<br>-             | 7,558.00         | 261.77                      | -<br>-                | -           | -                                          | 0/0                         |
| 901   | FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA , EPC                                | 03/2015          | 297.00<br>-             | 297.00           | 38.33                       | 04/2018<br>-          | -           | -                                          | 0/1                         |
| 902   | CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66 ) FROM KM. 26 /200 ( CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA ,              | 03/2015          | 298.33<br>-             | 298.33           | 16.10                       | -<br>-                | -           | -                                          | 0/4                         |
| 903   | CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA , EPC                | 03/2015          | 184.05<br>-             | 184.05           | 10.72                       | -<br>-                | -           | -                                          | 0/4                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                   |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                           | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                 | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 904   | CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC | 03/2015          | 280.16 -                | 280.16           | 16.06                       | - -                   | -           | -                                          | 0/4                         |
| 905   | CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC  | 10/2015          | 936.40 -                | 936.40           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 906   | WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC | 12/2015          | 773.98 -                | 773.98           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 907   | WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA , EPC | 12/2015          | 819.95 -                | 819.95           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 908   | GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT , PPP (BOT)                                        | 03/2010          | 1,509.10 -              | 3,237.87         | 3,187.21                    | 09/2012 -             | 08/2018     | -                                          | 2/3                         |
| 909   | KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT , PPP (BOT)                                                                       | 01/2011          | 953.88 -                | 953.88           | 976.28                      | 07/2013 -             | 12/2018     | 65(O) -                                    | 0/0                         |
| 910   | AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT , PPP (BOT)                                                              | 01/2013          | 2,125.24 -              | 2,125.24         | 4,659.71                    | 12/2015 -             | -           | -                                          | 0/3                         |
| 911   | VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT ,                                                                               | 03/2014          | 503.16 -                | 503.16           | 346.60                      | 08/2016 -             | -           | -                                          | 0/0                         |
| 912   | FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT , | 05/2016          | 998.18 -                | 998.18           | 199.22                      | - -                   | 08/2019     | - -                                        | 0/0                         |
| 913   | FOUR LANING OF TALAJA – MAHUA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT ,  | 05/2016          | 834.64 -                | 834.64           | 137.94                      | - -                   | 10/2019     | - -                                        | 0/0                         |
| 914   | FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT , | 05/2016          | 723.64 -                | 723.64           | 211.88                      | - -                   | 09/2019     | - -                                        | 0/0                         |
| 915   | FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT , | 05/2016          | 763.08 -                | 763.08           | 137.01                      | - -                   | 08/2019     | - -                                        | 0/0                         |
| 916   | SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT , | 05/2016          | 425.60 -                | 425.60           | .00                         | - -                   | 03/2019     | - -                                        | 0/0                         |
| 917   | CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT ,                                                               | 05/2016          | 364.56 -                | 364.56           | 24.94                       | - -                   | 12/2019     | - -                                        | 0/0                         |
| 918   | 4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT ,                       | 07/2016          | 829.97 -                | 829.97           | 71.29                       | - -                   | 01/2020     | - -                                        | 0/0                         |
| 919   | 2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT ,                                                | 12/2016          | 417.19 -                | 417.19           | 122.81                      | - -                   | 09/2019     | - -                                        | 0/0                         |
| 920   | SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI, GUJARAT ,      | 01/2017          | 1,251.11 -              | 1,251.11         | .00                         | - -                   | -           | -                                          | 0/0                         |
| 921   | 4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT ,                                        | 06/2017          | 1,958.88 -              | 1,958.88         | 364.31                      | 06/2020 -             | 08/2020     | 2(O) -                                     | 0/0                         |
| 922   | JUNAGADH BYPASS - [N24000701]NHAI, GUJARAT , Central Sector Projects                                                              | 10/2017          | 232.49 -                | 232.49           | .00                         | 10/2017 -             | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                   |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                           | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                 | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 923   | SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT ,   | 02/2018          | 1,052.21 -              | 1,052.21         | .00                         | - -                   | -           | -                                          | 0/0                         |
| 924   | CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT ,  | 03/2018          | 2,702.05 -              | 2,702.05         | .00                         | - -                   | -           | -                                          | 0/0                         |
| 925   | CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT ,  | 03/2018          | 1,437.64 -              | 1,437.64         | .00                         | - -                   | -           | -                                          | 0/0                         |
| 926   | CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT ,   | 03/2018          | 1,161.39 -              | 1,161.39         | .00                         | - -                   | -           | -                                          | 0/0                         |
| 927   | DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)                                                             | 04/2007          | 486.00 -                | 486.00           | 470.01                      | 05/2010 -             | 10/2018     | -                                          | 0/0                         |
| 928   | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)                                                 | 05/2009          | 1,108.00 -              | 2,288.00         | 3,953.66                    | 11/2011 -             | 06/2019     | 91(O) -                                    | 0/0                         |
| 929   | ROHTAK-BAWAL - [N24000169]NHAI,HARYANA , PPP (BOT)                                                                                | 05/2011          | 650.00 -                | 650.00           | 832.39                      | 11/2013 -             | -           | -                                          | 0/0                         |
| 930   | FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA ,                                           | 08/2015          | 723.54 -                | 723.54           | 530.94                      | 02/2018 -             | -           | -                                          | 0/0                         |
| 931   | 4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA ,                                                             | 12/2015          | 602.95 -                | 602.95           | 54.89                       | 06/2016 -             | 12/2018     | 30(O) -                                    | 0/0                         |
| 932   | 4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA ,                                                             | 01/2016          | 574.28 -                | 574.28           | 79.56                       | 07/2018 -             | 03/2019     | 8(O) -                                     | 0/0                         |
| 933   | 8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)                                                        | 07/2015          | 2,128.72 -              | 2,128.72         | 1,042.73                    | 04/2019 -             | 04/2019     | 0(O) -                                     | 0/0                         |
| 934   | FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA ,                                           | 11/2015          | 867.66 -                | 867.66           | 502.66                      | 05/2018 -             | -           | -                                          | 0/0                         |
| 935   | CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA ,                                                       | 08/2016          | 248.97 -                | 248.97           | 27.57                       | 05/2019 -             | 08/2019     | 3(O) -                                     | 0/0                         |
| 936   | CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA ,  | 09/2016          | 1,004.67 -              | 1,004.67         | .00                         | 05/2019 -             | 05/2019     | 0(O) -                                     | 0/0                         |
| 937   | 4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA ,   | 03/2017          | 639.79 -                | 552.90           | 46.24                       | 03/2020 -             | 06/2019     | -9(O) -                                    | 0/0                         |
| 938   | CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA ,  | 03/2018          | 1,484.30 -              | 1,484.30         | .00                         | - -                   | -           | -                                          | 0/0                         |
| 939   | REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA ,  | 03/2018          | 275.12 -                | 275.12           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 940   | REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI,HARYANA , | 03/2018          | 307.79 -                | 307.79           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 941   | SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA ,  | 03/2018          | 634.70 -                | 634.70           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 942   | SIX LANING & STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA ,   | 03/2018          | 795.50 -                | 795.50           | .00                         | - -                   | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                           |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                   | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                         | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 943   | REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA ,          | 03/2018          | 198.05 -                | 198.05           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 944   | REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA ,          | 03/2018          | 181.78 -                | 181.78           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 945   | REDESIGNING REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION & STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA ,           | 03/2018          | 551.58 -                | 551.58           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 946   | FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)                          | 11/2013          | 1,916.79 -              | 1,916.79         | 1,948.92                    | 11/2016 -             | 04/2019     | 29(O) -                                    | 0/0                         |
| 947   | FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,                                                                       | 09/2015          | 934.46 -                | 934.46           | 104.98                      | 03/2018 -             | 03/2019     | 12(O) -                                    | 0/0                         |
| 948   | 2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,                                | 02/2016          | 273.20 -                | 273.20           | 48.69                       | 02/2019 -             | 02/2019     | 0(O) -                                     | 0/0                         |
| 949   | TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,                                    | 08/2016          | 1,583.18 -              | 1,583.18         | .00                         | - -                   | 09/2020     | -                                          | 0/0                         |
| 950   | FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH , | 09/2016          | 1,273.71 -              | 1,273.71         | .00                         | - -                   | 07/2020     | -                                          | 0/0                         |
| 951   | FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,                             | 10/2016          | 447.75 -                | 447.75           | 54.46                       | - -                   | 11/2019     | -                                          | 0/0                         |
| 952   | 4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH ,                                                      | 06/2017          | 2,485.93 -              | 2,485.93         | .00                         | 06/2020 -             | 06/2020     | 0(O) -                                     | 0/0                         |
| 953   | FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050 ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH ,  | 03/2018          | 478.74 -                | 478.74           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 954   | QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)                                              | 07/2010          | 1,987.00 -              | 1,987.00         | 2,403.47                    | 07/2015 -             | 03/2019     | 44(O) -                                    | 0/0                         |
| 955   | NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)                                                                       | 05/2011          | 2,159.00 -              | 2,159.00         | 3,986.82                    | 06/2015 -             | -           | -                                          | 0/0                         |
| 956   | JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)                                                    | 07/2010          | 1,813.76 -              | 1,813.76         | 2,393.99                    | 07/2013 -             | -           | -                                          | 0/0                         |
| 957   | SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)                                                                   | 06/2011          | 1,100.70 -              | 1,100.70         | 1,288.68                    | 06/2014 -             | -           | -                                          | 0/0                         |
| 958   | FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,                                                    | 12/2015          | 2,168.66 -              | 2,168.66         | .00                         | 06/2019 -             | 12/2020     | 18(O) -                                    | 0/0                         |
| 959   | FOUR LANING OF UDHAMPUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,                                                   | 12/2015          | 2,136.97 -              | 2,136.97         | 87.69                       | 12/2018 -             | 10/2019     | 10(O) -                                    | 0/0                         |
| 960   | CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR , | 12/2017          | 1,471.75 -              | 1,471.75         | .00                         | - -                   | -           | -                                          | 0/0                         |
| 961   | RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)                                                                       | 12/2012          | 1,479.00 -              | 1,479.00         | 740.26                      | 06/2015 -             | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                         |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                 | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                       | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 962   | 4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND ,                                                      | 02/2016          | 997.15<br>-             | 997.15           | 352.03                      | 03/2019<br>-          | 03/2019     | 0(O)<br>-                                  | 0/0                         |
| 963   | TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND ,       | 07/2016          | 458.03<br>-             | 458.03           | 20.00                       | -<br>-                | 12/2019     | -<br>-                                     | 0/0                         |
| 964   | FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,                                                                     | 08/2016          | 323.72<br>-             | 323.72           | 37.20                       | 08/2018<br>-          | 08/2018     | -                                          | 0/0                         |
| 965   | 4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND ,                                          | 03/2017          | 165.50<br>-             | 172.16           | 20.01                       | 03/2020<br>-          | 06/2019     | -9(O)<br>-                                 | 0/0                         |
| 966   | 4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND ,                                | 03/2017          | 239.68<br>-             | 235.90           | 46.25                       | 03/2020<br>-          | 06/2019     | -9(O)<br>-                                 | 0/0                         |
| 967   | FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,                                                         | 01/2018          | 273.46<br>-             | 273.46           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 968   | SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,                                       | 01/2018          | 1,155.16<br>-           | 1,155.16         | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 969   | 4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND ,      | 03/2018          | 1,005.08<br>-           | 1,005.08         | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 970   | HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,                                                         | 09/2010          | 946.00<br>-             | 946.00           | 818.53                      | 06/2018<br>-          | 03/2019     | 9(O)<br>-                                  | 3/3                         |
| 971   | STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , EPC | 03/2015          | 165.67<br>-             | 165.67           | .00                         | 11/2015<br>-          | -           | -                                          | 0/0                         |
| 972   | STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA , EPC | 03/2015          | 159.12<br>-             | 159.12           | .00                         | 11/2015<br>-          | -           | -                                          | 0/0                         |
| 973   | TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 ( NEW NH NO -50) - [N24000342]NHAI,KARNATAKA ,       | 05/2015          | 709.00<br>-             | 709.00           | 380.95                      | 09/2017<br>-          | 12/2018     | 15(O)<br>-                                 | 0/0                         |
| 974   | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC | 01/1991          | 219.40<br>-             | 219.40           | .00                         | 01/2018<br>-          | -           | -                                          | 0/0                         |
| 975   | 4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)                                               | 05/2014          | 1,655.01<br>-           | 1,655.01         | 1,515.16                    | 08/2016<br>-          | 03/2019     | 31(O)<br>-                                 | 0/0                         |
| 976   | FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)                                                             | 03/2015          | 1,388.00<br>-           | 1,388.00         | 924.40                      | 08/2018<br>-          | 04/2019     | 8(O)<br>-                                  | 0/0                         |
| 977   | 4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,                                            | 03/2016          | 701.40<br>-             | 701.40           | 22.02                       | 03/2019<br>-          | 07/2019     | 4(O)<br>-                                  | 0/0                         |
| 978   | 4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,                                              | 03/2016          | 870.00<br>-             | 870.00           | 9.12                        | 03/2019<br>-          | 11/2020     | 20(O)<br>-                                 | 0/0                         |
| 979   | 4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA ,                                                                             | 05/2014          | 720.69<br>-             | 720.69           | 99.03                       | -<br>-                | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                    |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                            | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                  | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 980   | FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,                             | 08/2016          | 1,664.20<br>-           | 1,664.20         | 313.63                      | 04/2020<br>-          | 04/2020     | 0(O)<br>-                                  | 0/0                         |
| 981   | HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,                                                                   | 08/2016          | 1,167.42<br>-           | 1,167.42         | 192.72                      | 03/2019<br>-          | 03/2019     | 0(O)<br>-                                  | 0/0                         |
| 982   | TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA , | 09/2016          | 950.69<br>-             | 950.69           | 499.54                      | 08/2019<br>-          | 08/2019     | 0(O)<br>-                                  | 0/0                         |
| 983   | SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,   | 03/2017          | 831.58<br>-             | 1,177.00         | 121.00                      | 03/2020<br>-          | 06/2020     | 3(O)<br>-                                  | 0/0                         |
| 984   | SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA , | 03/2017          | 993.16<br>-             | 1,434.00         | 413.53                      | 03/2020<br>-          | 06/2020     | 3(O)<br>-                                  | 0/0                         |
| 985   | 2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA , | 02/2018          | 486.78<br>-             | 486.78           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 986   | SIX-LANING OF BANGALORE – NIDAGATTA SECTION KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA ,  | 02/2018          | 1,995.34<br>-           | 1,995.34         | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 987   | SIX LANING OF NIDAGATTA-MYSORE SECTION KM 74.20 TO KM 135.304 OF NH-275 IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA ,    | 02/2018          | 2,177.80<br>-           | 2,177.80         | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 988   | SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)                                   | 02/2010          | 617.00<br>-             | 617.00           | 943.17                      | 08/2012<br>-          | 03/2019     | 79(O)<br>-                                 | 0/0                         |
| 989   | CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC | 01/2014          | 255.75<br>348.00        | 348.43           | 231.56                      | 09/2017<br>-          | -           | -                                          | 0/0                         |
| 990   | CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA , EPC | 01/2014          | 267.16<br>352.00        | 352.05           | 201.35                      | 11/2017<br>-          | -           | -                                          | 0/0                         |
| 991   | 4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,                                                    | 06/2015          | 845.24<br>-             | 845.24           | 127.87                      | -<br>-                | 04/2019     | -<br>-                                     | 0/0                         |
| 992   | 4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,    | 04/2016          | 804.97<br>-             | 804.97           | 21.80                       | 06/2018<br>-          | 04/2019     | 10(O)<br>-                                 | 0/0                         |
| 993   | 4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects                                             | 09/2017          | 1,124.11<br>-           | 1,124.11         | .00                         | 09/2017<br>-          | 06/2020     | 33(O)<br>-                                 | 0/0                         |
| 994   | 6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA ,    | 02/2018          | 1,424.77<br>-           | 1,424.77         | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 995   | INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)                                                               | 10/2010          | 1,175.00<br>-           | 1,206.10         | 1,342.77                    | 04/2013<br>-          | 11/2018     | -                                          | 0/0                         |
| 996   | INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)                                                                    | 11/2010          | 325.00<br>-             | 325.00           | 469.54                      | 05/2013<br>-          | -           | -                                          | 0/0                         |
| 997   | KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH , EPC                             | 02/2015          | 377.83<br>-             | 377.83           | 57.42                       | 07/2017<br>-          | -           | -                                          | 0/0                         |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                        |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|----------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                      | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 998   | SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)                                                    | 01/2012          | 320.48 -                | 320.48           | 189.49                      | 08/2015 -             | -           | -                                          | 0/0                         |
| 999   | BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC                  | 06/2015          | 390.51 -                | 390.51           | 43.25                       | -                     | -           | -                                          | 0/0                         |
| 1000  | BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH , BOT (TOLL)                                                         | 11/2011          | 704.26 -                | 704.26           | 5.21                        | 05/2015 -             | 01/2020     | 56(O) -                                    | 0/0                         |
| 1001  | BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH , BOT (TOLL)                                            | 03/2013          | 257.80 -                | 257.80           | 59.30                       | 02/2016 -             | -           | -                                          | 0/0                         |
| 1002  | INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC               | 11/2013          | 497.05 -                | 497.05           | .00                         | 05/2017 -             | -           | -                                          | 0/0                         |
| 1003  | SHAH DOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH , EPC | 06/2015          | 532.49 -                | 532.49           | 137.08                      | 05/2017 -             | -           | -                                          | 0/0                         |
| 1004  | BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)                                                    | 08/2015          | 257.80 -                | 257.00           | 12.38                       | -                     | -           | -                                          | 0/0                         |
| 1005  | SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , BOT (TOLL)                                           | 11/2011          | 871.15 -                | 871.15           | 332.25                      | 09/2015 -             | -           | -                                          | 0/0                         |
| 1006  | MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH , EPC                 | 06/2015          | 641.02 -                | 641.02           | 89.88                       | 12/2017 -             | -           | -                                          | 0/0                         |
| 1007  | MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , BOT (TOLL)                                         | 01/2012          | 381.86 -                | 381.86           | 252.03                      | 04/2015 -             | -           | -                                          | 0/0                         |
| 1008  | BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH , BOT (TOLL)                                               | 11/2011          | 670.82 -                | 670.82           | 590.00                      | 02/2015 -             | -           | -                                          | 0/0                         |
| 1009  | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,                                                | 03/2015          | 795.76 -                | 795.76           | 171.72                      | -                     | 03/2019     | -                                          | 0/0                         |
| 1010  | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,                                                 | 03/2015          | 794.30 -                | 794.30           | 152.81                      | -                     | 05/2019     | -                                          | 0/0                         |
| 1011  | JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH ,           | 02/2015          | 327.32 -                | 327.32           | 142.73                      | 05/2017 -             | -           | -                                          | 0/0                         |
| 1012  | JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC                  | 11/2015          | 628.45 -                | 628.45           | 20.74                       | 03/2018 -             | -           | -                                          | 0/0                         |
| 1013  | GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH , EPC                              | 12/2015          | 927.54 -                | 927.54           | 29.17                       | 06/2018 -             | -           | -                                          | 0/0                         |
| 1014  | FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,                                                                 | 03/2015          | 928.83 -                | 928.83           | 202.91                      | -                     | 03/2019     | -                                          | 0/0                         |
| 1015  | FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)                                                           | 05/2013          | 1,055.00 -              | 1,601.77         | 1,393.40                    | 11/2015 -             | 12/2018     | 37(O) -                                    | 0/0                         |
| 1016  | FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH , | 06/2015          | 1,012.90 -              | 1,012.90         | 1,042.73                    | 03/2016 -             | 03/2019     | 36(O) -                                    | 0/0                         |
| 1017  | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,                                                | 03/2015          | 810.22 -                | 810.22           | 121.57                      | -                     | 03/2019     | -                                          | 0/0                         |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                                |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|----------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                                        | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                                              | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1018  | FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)              | 06/2015          | 1,583.79 -              | 1,583.79         | 1,439.18                    | 01/2019 -             | 01/2019     | 0(O) -                                     | 0/0                         |
| 1019  | UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC                                                  | 03/2015          | 511.83 -                | 511.83           | 40.87                       | 08/2017 -             | -           | -                                          | 0/0                         |
| 1020  | BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,                                                         | 08/2016          | 227.49 -                | 227.49           | 15.03                       | 01/2019 -             | 01/2019     | 0(O) -                                     | 0/0                         |
| 1021  | FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects | 10/2017          | 639.97 -                | 639.97           | 58.04                       | 10/2017 -             | 01/2020     | 27(O) -                                    | 0/0                         |
| 1022  | BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects                                        | 09/2017          | 374.40 -                | 374.40           | .00                         | 09/2017 -             | -           | -                                          | 0/0                         |
| 1023  | BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects                                | 09/2017          | 990.61 -                | 990.61           | .00                         | 09/2017 -             | -           | -                                          | 0/0                         |
| 1024  | BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,                         | 12/2017          | 950.27 -                | 950.27           | .00                         | -                     | -           | -                                          | 0/0                         |
| 1025  | FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH ,                        | 01/2018          | 960.24 -                | 960.24           | .00                         | -                     | 08/2020     | -                                          | 0/0                         |
| 1026  | FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH ,                        | 01/2018          | 770.73 -                | 770.73           | .00                         | -                     | -           | -                                          | 0/0                         |
| 1027  | PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)                                                                                                    | 10/2010          | 1,724.55 -              | 1,724.55         | 2,253.40                    | 03/2013 -             | 06/2019     | 75(O) -                                    | 0/0                         |
| 1028  | PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA ,                                                                                                                 | 12/2011          | 942.69 -                | 942.69           | 668.59                      | 06/2014 -             | 06/2019     | 60(O) -                                    | 0/0                         |
| 1029  | WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)                                                      | 05/2013          | 1,348.20 -              | 1,348.20         | 1,792.90                    | 02/2014 -             | 06/2019     | 64(O) -                                    | 2/2                         |
| 1030  | REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA ,                                                                 | 06/2014          | 260.39 -                | 260.39           | 87.43                       | 11/2016 -             | -           | -                                          | 0/2                         |
| 1031  | CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC                               | 03/2015          | 168.30 -                | 168.30           | 13.43                       | -                     | -           | -                                          | 0/4                         |
| 1032  | CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC                         | 08/2014          | 187.79 -                | 187.79           | 57.60                       | 07/2016 -             | -           | -                                          | 0/12                        |
| 1033  | REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC                                                       | 01/2014          | 446.77 -                | 446.77           | 87.62                       | -                     | -           | -                                          | 0/4                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                 |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                         | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                               | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1034  | REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA , EPC                                       | 12/2013          | 220.72 -                | 220.72           | 95.02                       | 11/2016 -             | -           | -                                          | 0/4                         |
| 1035  | WIDENING NH-848 FROM KM 16.000 TO 34.000 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC         | 10/2015          | 289.60 -                | 289.60           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1036  | CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE | 12/2011          | 156.26 227.00           | 156.26           | 65.16                       | - -                   | -           | -                                          | 0/0                         |
| 1037  | CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA , ITEM RATE | 03/2011          | 185.82 292.00           | 185.82           | 205.97                      | - -                   | -           | -                                          | 0/0                         |
| 1038  | REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC       | 01/2015          | 225.81 -                | 225.81           | 6.50                        | - -                   | -           | -                                          | 0/0                         |
| 1039  | 4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)                                                                | 07/2015          | 2,288.18 -              | 2,288.18         | .00                         | 05/2019 -             | 05/2019     | 0(O) -                                     | 0/0                         |
| 1040  | CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270( D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 ( D - [N24000432]NHAI,MAHARASHTRA ,            | 09/2015          | 414.51 -                | 414.00           | 230.34                      | 05/2018 -             | 03/2019     | 10(O) -                                    | 0/0                         |
| 1041  | CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 ( - [N24000435]NHAI,MAHARASHTRA ,              | 10/2015          | 531.13 -                | 531.13           | 163.10                      | 05/2018 -             | 05/2019     | 12(O) -                                    | 0/0                         |
| 1042  | 4 LANING OF FAGNE - MAH-GUJ BORDER ( PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC                                                                 | 07/2015          | 1,885.74 -              | 1,885.74         | 1,622.44                    | 05/2019 -             | 05/2019     | 0(O) -                                     | 0/0                         |
| 1043  | CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 ( OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,                             | 10/2015          | 593.26 -                | 593.26           | 45.11                       | 05/2018 -             | 04/2019     | 11(O) -                                    | 0/0                         |
| 1044  | CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB SERVICE ROADS FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,              | 12/2015          | 649.50 -                | 649.50           | 86.54                       | 03/2019 -             | 03/2019     | 0(O) -                                     | 0/0                         |
| 1045  | 6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,                               | 08/2015          | 505.00 -                | 505.00           | 194.09                      | 05/2018 -             | 04/2019     | 11(O) -                                    | 0/0                         |
| 1046  | 4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)                                                         | 01/2015          | 972.50 -                | 972.50           | 1,484.99                    | 07/2017 -             | 12/2018     | 17(O) -                                    | 0/0                         |
| 1047  | 4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)                                                   | 06/2014          | 923.04 -                | 923.04           | 650.92                      | 11/2016 -             | 06/2019     | 31(O) -                                    | 0/0                         |
| 1048  | NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA ,                                                                                               | 09/2005          | 168.00 -                | 168.00           | 226.24                      | 06/2006 -             | -           | -                                          | 0/0                         |
| 1049  | FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)                                                                   | 07/2015          | 1,871.34 -              | 1,871.34         | 2,304.41                    | 01/2018 -             | 12/2018     | 11(O) -                                    | 0/0                         |
| 1050  | FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,                             | 04/2010          | 1,170.52 -              | 1,170.52         | 2,042.41                    | 06/2012 -             | 12/2018     | 78(O) -                                    | 0/0                         |
| 1051  | REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA ,             | 01/2014          | 292.98 -                | 292.98           | 95.60                       | 11/2014 -             | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                      |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|--------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                              | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                    | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1052  | BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA ,           | 03/2016          | 197.69 -                | 197.69           | .60                         | 07/2018 -             | 07/2018     | -                                          | 0/0                         |
| 1053  | NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,                                                                           | 03/2016          | 546.00 -                | 546.00           | 460.55                      | 07/2019 -             | 07/2019     | 0(O) -                                     | 0/0                         |
| 1054  | NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,                                                                           | 03/2016          | 591.66 -                | 591.66           | 608.89                      | 07/2019 -             | 07/2019     | 0(O) -                                     | 0/0                         |
| 1055  | BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA ,            | 03/2016          | 244.00 -                | 244.00           | .00                         | 07/2018 -             | -           | -                                          | 0/0                         |
| 1056  | 4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA ,               | 03/2016          | 1,142.62 -              | 1,142.62         | .00                         | -                     | -           | -                                          | 0/0                         |
| 1057  | 4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA ,               | 03/2016          | 1,101.58 -              | 1,101.58         | .00                         | -                     | -           | -                                          | 0/0                         |
| 1058  | 4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA ,                                                 | 11/2016          | 1,071.61 -              | 1,071.61         | .00                         | -                     | -           | -                                          | 0/0                         |
| 1059  | 4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA ,                                                    | 11/2016          | 1,064.88 -              | 1,064.88         | .00                         | -                     | -           | -                                          | 0/0                         |
| 1060  | 4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA , | 11/2016          | 400.25 -                | 400.25           | 38.57                       | 03/2019 -             | 09/2019     | 6(O) -                                     | 0/0                         |
| 1061  | 4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA , | 11/2016          | 446.17 -                | 446.17           | 2.42                        | 03/2019 -             | 11/2019     | 8(O) -                                     | 0/0                         |
| 1062  | SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA , | 11/2016          | 290.73 -                | 290.73           | 57.93                       | -                     | 05/2019     | -                                          | 0/0                         |
| 1063  | CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA , | 01/2017          | 244.90 -                | 244.90           | 82.41                       | 05/2019 -             | 05/2019     | 0(O) -                                     | 0/0                         |
| 1064  | FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA ,                                                                | 02/2017          | 904.16 -                | 904.16           | 155.12                      | 02/2020 -             | 05/2020     | 3(O) -                                     | 0/0                         |
| 1065  | CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA , | 03/2017          | 247.02 -                | 157.49           | .00                         | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/0                         |
| 1066  | 4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA ,                                             | 03/2017          | 744.64 -                | 982.00           | .00                         | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/0                         |
| 1067  | 4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA ,                                         | 03/2017          | 1,030.44 -              | 1,065.51         | 355.02                      | 03/2020 -             | 05/2020     | 2(O) -                                     | 0/0                         |
| 1068  | 4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA ,                                          | 03/2017          | 988.34 -                | 1,043.28         | 451.51                      | 03/2020 -             | 08/2020     | 5(O) -                                     | 0/0                         |
| 1069  | 4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA ,                                        | 03/2017          | 1,059.73 -              | 1,071.00         | 152.79                      | 03/2017 -             | 11/2020     | 44(O) -                                    | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                          |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                  | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                        | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1070  | DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA ,         | 03/2017          | 296.19 -                | 254.00           | 97.80                       | 03/2020 -             | 05/2019     | -10(O) -                                   | 0/0                         |
| 1071  | 4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA ,                                            | 03/2017          | 1,098.06 -              | 1,160.64         | 413.75                      | 03/2020 -             | 08/2020     | 5(O) -                                     | 0/0                         |
| 1072  | SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA ,     | 12/2017          | 404.94 -                | 404.94           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1073  | 4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA ,                                               | 01/2018          | 607.00 -                | 607.00           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1074  | 4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA ,                                                  | 01/2018          | 621.00 -                | 621.00           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1075  | CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA , EPC                                          | 03/2018          | 291.53 -                | 291.53           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1076  | CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA , EPC                                           | 03/2018          | 289.21 -                | 289.21           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1077  | CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA ,     | 03/2018          | 1,162.92 -              | 1,162.92         | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1078  | FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA ,     | 03/2018          | 642.13 -                | 642.13           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1079  | JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA , PPP (ANNUITY)                                                                            | 01/2011          | 536.00 -                | 536.00           | 837.81                      | 01/2014 -             | 01/2019     | 60(O) -                                    | 0/0                         |
| 1080  | 2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA , ITEM RATE | 12/2010          | 1,494.48 -              | 1,494.48         | .00                         | 02/2011 -             | -           | -                                          | 0/0                         |
| 1081  | TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,                                       | 12/2015          | 479.20 -                | 479.20           | 14.31                       | 05/2018 -             | 03/2019     | 10(O) -                                    | 0/0                         |
| 1082  | WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA ,     | 04/2017          | 553.51 -                | 553.51           | 159.00                      | - -                   | -           | -                                          | 0/0                         |
| 1083  | WIDENING TO 2 LANE RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE  | 11/2010          | 624.41 -                | 624.41           | .00                         | 03/2011 -             | -           | -                                          | 0/0                         |
| 1084  | CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE | 08/2010          | 193.69 -                | 193.69           | .00                         | 10/2010 -             | -           | -                                          | 0/0                         |
| 1085  | CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE                         | 08/2010          | 195.04 -                | 195.04           | 130.82                      | 10/2010 -             | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                          |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                  | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                        | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1086  | GWALIOR-JHANSI NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)                                                                       | 12/2003          | 604.00 -                | 604.00           | 423.83                      | 12/2009 -             | 08/2020     | 128(O) -                                   | 0/0                         |
| 1087  | SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)                                                      | 02/2009          | 1,693.75 -              | 1,693.75         | 2,675.28                    | 08/2011 -             | -           | -                                          | 2/2                         |
| 1088  | 4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)                                                                   | 02/2011          | 2,498.76 -              | 2,498.76         | 2,525.46                    | 08/2014 -             | -           | -                                          | 0/0                         |
| 1089  | VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)                                                        | 09/2011          | 2,848.00 -              | 2,848.00         | 1,141.90                    | 03/2014 -             | 12/2019     | 69(O) -                                    | 0/0                         |
| 1090  | MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)                                                                         | 09/2011          | 754.00 -                | 754.00           | 1,363.43                    | 03/2013 -             | 12/2019     | 81(O) -                                    | 0/0                         |
| 1091  | DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)                                                            | 10/2012          | 1,928.22 -              | 2,945.00         | 2,970.11                    | 04/2015 -             | -           | -                                          | 0/0                         |
| 1092  | WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE , EPC  | 03/2015          | 789.83 -                | 789.83           | 109.77                      | -                     | -           | -                                          | 0/0                         |
| 1093  | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-III) - [N24000446]NHAI,MULTI STATE ,                                         | 09/2015          | 788.51 -                | 788.51           | 103.37                      | 03/2018 -             | -           | -                                          | 0/0                         |
| 1094  | SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,     | 09/2016          | 1,244.10 -              | 1,244.10         | 85.00                       | - -                   | 02/2020     | - -                                        | 0/0                         |
| 1095  | FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE ,     | 03/2018          | 1,294.47 -              | 1,294.47         | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1096  | FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE ,     | 03/2018          | 998.70 -                | 998.70           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1097  | WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD MON-TAMLU-MERANGKONG ROAD PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE | 12/2010          | 1,296.00 -              | 1,296.00         | .00                         | 02/2011 -             | -           | -                                          | 0/0                         |
| 1098  | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,      | 03/2016          | 373.07 -                | 373.07           | .00                         | 08/2016 -             | 08/2019     | 36(O) -                                    | 0/0                         |
| 1099  | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,      | 03/2016          | 396.52 -                | 396.52           | .00                         | 08/2016 -             | 08/2019     | 36(O) -                                    | 0/0                         |
| 1100  | FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND ,      | 03/2016          | 429.52 -                | 429.52           | .00                         | 08/2016 -             | 08/2019     | 36(O) -                                    | 0/0                         |
| 1101  | CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND ,      | 02/2017          | 507.68 -                | 507.68           | .00                         | 04/2017 -             | -           | -                                          | 0/0                         |
| 1102  | (I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND ,      | 02/2017          | 387.00 -                | 387.00           | .00                         | 09/2018 -             | -           | -                                          | 0/0                         |
| 1103  | (II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND ,       | 03/2018          | 500.09 -                | 500.09           | .00                         | 09/2018 -             | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                     |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                             | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                   | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1104  | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND ,  | 03/2018          | 339.57 -                | 339.57           | .00                         | 09/2018 -             | -           | -                                          | 0/0                         |
| 1105  | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND ,  | 03/2018          | 239.30 -                | 239.30           | .00                         | 09/2018 -             | -           | -                                          | 0/0                         |
| 1106  | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND ,  | 03/2018          | 285.68 -                | 285.68           | .00                         | 09/2018 -             | -           | -                                          | 0/0                         |
| 1107  | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND ,  | 03/2018          | 315.03 -                | 315.03           | .00                         | 09/2018 -             | -           | -                                          | 0/0                         |
| 1108  | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND ,  | 03/2018          | 240.64 -                | 240.64           | .00                         | 09/2018 -             | -           | -                                          | 0/0                         |
| 1109  | CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND , | 03/2018          | 237.72 -                | 237.72           | .00                         | 09/2018 -             | -           | -                                          | 0/0                         |
| 1110  | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND , | 03/2018          | 251.97 -                | 251.97           | .00                         | 09/2018 -             | -           | -                                          | 0/0                         |
| 1111  | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND ,  | 03/2018          | 282.98 -                | 282.98           | .00                         | 09/2018 -             | -           | -                                          | 0/0                         |
| 1112  | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND , | 03/2018          | 215.12 -                | 215.12           | .00                         | 09/2018 -             | -           | -                                          | 0/0                         |
| 1113  | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND , | 03/2018          | 215.79 -                | 215.79           | .00                         | 09/2018 -             | -           | -                                          | 0/0                         |
| 1114  | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND , | 03/2018          | 272.89 -                | 272.89           | .00                         | 09/2018 -             | -           | -                                          | 0/0                         |
| 1115  | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND , | 03/2018          | 323.98 -                | 323.98           | .00                         | 09/2018 -             | -           | -                                          | 0/0                         |
| 1116  | PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)                                                                               | 03/2012          | 1,410.00 -              | 1,410.00         | 1,555.96                    | 09/2014 -             | 03/2019     | 54(O) -                                    | 0/0                         |
| 1117  | SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)                                                  | 12/2011          | 1,047.00 -              | 1,047.00         | 1,613.62                    | 06/2014 -             | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                      |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|--------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                              | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                    | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1118  | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC | 01/1991          | 218.63 -                | 218.63           | 29.27                       | 10/2017 -             | -           | -                                          | 0/0                         |
| 1119  | IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA , EPC                                                                        | 12/2013          | 319.80 -                | 319.80           | .00                         | 10/2016 -             | -           | -                                          | 0/0                         |
| 1120  | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA ,     | 01/1991          | 229.41 -                | 229.41           | 6.65                        | 05/2018 -             | -           | -                                          | 0/0                         |
| 1121  | REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC   | 07/2014          | 342.05 -                | 342.05           | .00                         | 01/2017 -             | -           | -                                          | 0/0                         |
| 1122  | 4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,                                                                         | 07/2015          | 1,282.94 -              | 1,282.94         | .00                         | -                     | 04/2020     | -                                          | 0/0                         |
| 1123  | FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,                                                                    | 12/2015          | 752.28 -                | 752.28           | .00                         | -                     | 11/2019     | -                                          | 0/0                         |
| 1124  | WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA , EPC       | 12/2011          | 159.39 -                | 159.39           | .00                         | 11/2017 -             | -           | -                                          | 0/0                         |
| 1125  | WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC   | 12/2011          | 191.08 -                | 191.08           | .00                         | 08/2015 -             | -           | -                                          | 0/0                         |
| 1126  | JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,                                                                   | 02/2016          | 1,069.65 -              | 1,069.65         | .00                         | -                     | 06/2019     | -                                          | 0/0                         |
| 1127  | DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,      | 09/2016          | 2,510.04 -              | 2,510.04         | .00                         | 08/2019 -             | 08/2019     | 0(0)                                       | 0/0                         |
| 1128  | REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,       | 10/2016          | 1,008.96 -              | 1,008.96         | 32.50                       | -                     | 07/2020     | -                                          | 0/0                         |
| 1129  | WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA ,     | 03/2014          | 191.50 192.00           | 192.00           | .00                         | 05/2016 -             | -           | -                                          | 0/0                         |
| 1130  | WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA ,     | 01/2015          | 326.63 327.00           | 327.00           | .00                         | 04/2018 -             | -           | -                                          | 0/0                         |
| 1131  | WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA ,        | 02/2015          | 239.91 240.00           | 240.00           | .00                         | 10/2017 -             | -           | -                                          | 0/0                         |
| 1132  | WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA ,      | 03/2015          | 226.31 226.00           | 226.00           | .00                         | 10/2017 -             | -           | -                                          | 0/0                         |
| 1133  | IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA ,      | 12/2013          | 319.80 320.00           | 320.00           | .00                         | 05/2016 -             | -           | -                                          | 0/0                         |
| 1134  | REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA ,      | 07/2014          | 342.05 342.00           | 342.00           | .00                         | 01/2017 -             | -           | -                                          | 0/0                         |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                  |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|----------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                          | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1135  | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA , | 08/2013          | 171.96<br>172.00        | 172.00           | .00                         | 06/2016<br>-          | -           | -                                          | 0/0                         |
| 1136  | WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA , | 06/2016          | 157.30<br>157.00        | 157.00           | .00                         | 06/2018<br>-          | -           | -                                          | 0/0                         |
| 1137  | WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA , | 03/2014          | 162.51<br>163.00        | 163.00           | .00                         | 05/2016<br>-          | -           | -                                          | 0/0                         |
| 1138  | REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,   | 03/2017          | 1,288.07<br>-           | 1,420.00         | .00                         | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 1139  | REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects    | 07/2017          | 476.56<br>-             | 476.56           | .00                         | 07/2017<br>-          | 11/2020     | 40(O)<br>-                                 | 0/0                         |
| 1140  | REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,  | 12/2017          | 686.65<br>-             | 686.65           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 1141  | REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,  | 12/2017          | 417.51<br>-             | 417.51           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 1142  | REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA ,  | 01/2018          | 953.09<br>-             | 953.09           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 1143  | REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA ,  | 01/2018          | 668.86<br>-             | 668.86           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 1144  | REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE ( - [N24000733]NHAI,ODISHA ,  | 01/2018          | 633.68<br>-             | 633.68           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 1145  | REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA ,    | 01/2018          | 614.48<br>-             | 614.48           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 1146  | REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,  | 01/2018          | 564.66<br>-             | 564.66           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 1147  | REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,  | 01/2018          | 686.65<br>-             | 686.65           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 1148  | REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA ,  | 01/2018          | 1,522.00<br>-           | 1,522.00         | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 1149  | REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA ,  | 01/2018          | 999.00<br>-             | 999.00           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 1150  | REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) ( - [N24000739]NHAI,ODISHA ,  | 01/2018          | 503.88<br>-             | 503.88           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 1151  | SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA , EPC             | 03/2018          | 806.11<br>-             | 806.11           | .00                         | -<br>-                | -           | -                                          | 0/0                         |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                    |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                            | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                  | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1152  | REHABILITATION AND UPGRADE OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB , EPC     | 03/2015          | 435.90<br>-             | 435.90           | 31.02                       | -<br>-                | -           | -                                          | 0/0                         |
| 1153  | WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB , EPC | 01/2015          | 279.68<br>-             | 279.68           | 25.28                       | -<br>-                | -           | -                                          | 0/0                         |
| 1154  | 4-LANING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB , EPC   | 11/2014          | 463.65<br>546.00        | 463.65           | 280.16                      | -<br>-                | -           | -                                          | 0/0                         |
| 1155  | 4 LANING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB , EPC   | 11/2014          | 573.96<br>605.00        | 605.00           | 209.74                      | -<br>-                | -           | -                                          | 0/0                         |
| 1156  | 4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB , EPC  | 02/2015          | 483.38<br>-             | 483.38           | 65.76                       | -<br>-                | -           | -                                          | 0/0                         |
| 1157  | 4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB , EPC  | 02/2015          | 616.36<br>-             | 616.36           | 68.58                       | -<br>-                | -           | -                                          | 0/0                         |
| 1158  | 4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64( - [N24000374]PWD,PUNJAB , EPC | 02/2015          | 486.74<br>-             | 486.74           | 189.39                      | -<br>-                | -           | -                                          | 0/0                         |
| 1159  | CONST.OF 4 LANES WITH PAVED SHOULDRS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15( - [N24000383]PWD,PUNJAB , EPC  | 03/2015          | 312.79<br>-             | 312.79           | 17.57                       | -<br>-                | -           | -                                          | 0/0                         |
| 1160  | CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOUA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB , EPC  | 07/2014          | 319.80<br>-             | 319.80           | 102.55                      | -<br>-                | -           | -                                          | 0/0                         |
| 1161  | DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC | 12/2015          | 766.36<br>-             | 766.36           | 99.86                       | -<br>-                | -           | -                                          | 0/0                         |
| 1162  | 4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC                                  | 11/2015          | 847.02<br>-             | 847.02           | 299.81                      | -<br>-                | -           | -                                          | 0/0                         |
| 1163  | 4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC                                 | 11/2015          | 889.24<br>-             | 889.24           | 389.64                      | -<br>-                | -           | -                                          | 0/0                         |
| 1164  | DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB , EPC  | 12/2015          | 578.38<br>-             | 578.38           | 128.53                      | -<br>-                | -           | -                                          | 0/0                         |
| 1165  | IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB ,        | 09/2015          | 273.06<br>-             | 273.06           | 28.90                       | -<br>-                | 04/2019     | -<br>-                                     | 0/0                         |
| 1166  | FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,                                                             | 09/2014          | 479.00<br>-             | 479.00           | 453.09                      | -<br>-                | 03/2019     | -                                          | 0/0                         |
| 1167  | FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,                                                                      | 10/2015          | 447.29<br>-             | 447.29           | 31.96                       | 12/2017<br>-          | 04/2019     | 16(O)<br>-                                 | 0/0                         |
| 1168  | WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , EPC | 06/2015          | 892.17<br>-             | 892.17           | 26.92                       | -<br>-                | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                               |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                       | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                             | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1169  | WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB , EPC            | 06/2015          | 899.21 -                | 899.21           | 25.08                       | - -                   | -           | -                                          | 0/0                         |
| 1170  | 4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,                 | 08/2016          | 1,388.34 -              | 1,388.34         | 595.70                      | 09/2019 -             | 09/2019     | 0(O) -                                     | 0/0                         |
| 1171  | 4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,                                                                                 | 08/2016          | 1,169.61 -              | 1,169.61         | 234.38                      | - -                   | 04/2020     | - -                                        | 0/0                         |
| 1172  | CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,               | 03/2017          | 754.54 -                | 756.27           | 30.30                       | 03/2020 -             | 04/2020     | 1(O) -                                     | 0/0                         |
| 1173  | FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB ,                      | 02/2018          | 261.76 -                | 261.76           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1174  | REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB , EPC           | 03/2018          | 199.90 -                | 199.90           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1175  | REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB , EPC           | 03/2018          | 196.05 -                | 196.05           | 21.93                       | - -                   | 01/2020     | - -                                        | 0/0                         |
| 1176  | WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN , EPC       | 10/2014          | 269.22 -                | 269.22           | 33.24                       | 01/2015 -             | -           | -                                          | 0/0                         |
| 1177  | WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN , EPC                        | 10/2014          | 257.09 -                | 257.09           | 14.80                       | 01/2015 -             | -           | -                                          | 0/0                         |
| 1178  | REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN , EPC                                        | 10/2013          | 278.87 -                | 278.87           | .00                         | 05/2014 -             | -           | -                                          | 0/0                         |
| 1179  | REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN , ITEM RATE | 01/1991          | 376.52 -                | 376.52           | .00                         | 04/2014 -             | -           | -                                          | 0/0                         |
| 1180  | WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , EPC       | 02/2015          | 383.40 -                | 383.40           | 224.68                      | 03/2015 -             | 06/2019     | 51(O) -                                    | 0/0                         |
| 1181  | WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN , EPC        | 12/2015          | 621.43 -                | 621.43           | .00                         | 06/2018 -             | -           | -                                          | 0/0                         |
| 1182  | TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN ,                                                             | 09/2014          | 425.19 -                | 425.19           | 274.20                      | 09/2016 -             | 03/2019     | 30(O) -                                    | 0/0                         |
| 1183  | PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN ,                                                    | 09/2015          | 567.51 -                | 567.51           | 53.70                       | 03/2018 -             | 01/2019     | 10(O) -                                    | 0/0                         |
| 1184  | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN ,           | 01/1991          | 269.26 -                | 269.26           | 212.72                      | 10/2016 -             | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                              |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|----------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                      | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                            | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1185  | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN , ITEM RATE | 01/1991          | 208.87 -                | 208.87           | 206.78                      | 05/2016 -             | -           | -                                          | 0/0                         |
| 1186  | 2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN ,                                                                         | 10/2015          | 597.00 -                | 597.00           | 604.80                      | 10/2017 -             | 01/2019     | 15(O) -                                    | 0/0                         |
| 1187  | 2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT) | 11/2012          | 530.07 -                | 530.07           | 556.02                      | 08/2016 -             | 02/2019     | 30(O) -                                    | 0/0                         |
| 1188  | BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)  | 08/2014          | 822.90 -                | 822.90           | 688.00                      | 04/2018 -             | 03/2019     | 11(O) -                                    | 0/0                         |
| 1189  | NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN , BOT (TOLL) | 09/2012          | 511.00 -                | 511.00           | .00                         | 10/2013 -             | -           | -                                          | 0/0                         |
| 1190  | NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN , BOT (TOLL)           | 09/2012          | 511.00 -                | 511.00           | .00                         | 10/2013 -             | -           | -                                          | 0/0                         |
| 1191  | GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN , PPP (BOT)                                                               | 02/2008          | 1,673.70 -              | 1,673.70         | 3,326.93                    | 10/2011<br>09/2017    | 03/2019     | 89(O)<br>18(R)                             | 0/0                         |
| 1192  | TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI,RAJASTHAN ,                                               | 08/2015          | 275.90 -                | 275.90           | 256.10                      | -<br>-                | 03/2019     | -<br>-                                     | 0/0                         |
| 1193  | TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN , PPP (BOT)                                                    | 06/2016          | 637.18 -                | 637.18           | 576.75                      | 06/2019 -             | 09/2019     | 3(O) -                                     | 0/0                         |
| 1194  | FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN , PPP (BOT)  | 06/2016          | 763.23 -                | 763.23           | 154.91                      | 06/2019 -             | 11/2019     | 5(O) -                                     | 0/0                         |
| 1195  | FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN ,                                   | 06/2016          | 649.00 -                | 649.00           | .00                         | 06/2019 -             | 09/2019     | 3(O) -                                     | 0/0                         |
| 1196  | 4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN ,                                                     | 07/2016          | 688.70 -                | 688.70           | 470.78                      | -<br>-                | 11/2019     | -<br>-                                     | 0/0                         |
| 1197  | TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN ,            | 07/2016          | 331.46 -                | 331.46           | 248.53                      | 10/2018 -             | 11/2018     | -                                          | 0/0                         |
| 1198  | 2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN ,                                                                  | 08/2016          | 320.30 -                | 320.30           | 193.54                      | 01/2019 -             | 02/2019     | 1(O) -                                     | 0/0                         |
| 1199  | SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN ,            | 09/2016          | 1,239.82 -              | 1,239.82         | 668.12                      | -<br>-                | 05/2020     | -<br>-                                     | 0/0                         |
| 1200  | SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN ,           | 09/2016          | 1,100.19 -              | 1,100.19         | 650.00                      | -<br>-                | 12/2019     | -<br>-                                     | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                    |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                            | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                  | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1201  | 6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN , | 12/2016          | 1,031.95 -              | 1,031.95         | 367.00                      | - -                   | 08/2020     | - -                                        | 0/0                         |
| 1202  | SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN ,                                             | 04/2017          | 894.00 -                | 894.00           | 15.00                       | 04/2020 -             | 11/2019     | -5(O) -                                    | 0/0                         |
| 1203  | FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects          | 10/2017          | 964.17 -                | 964.17           | .00                         | 10/2017 -             | -           | -                                          | 0/0                         |
| 1204  | FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN ,    | 12/2017          | 1,308.73 -              | 1,308.73         | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1205  | UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN , | 02/2018          | 1,103.88 -              | 1,103.88         | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1206  | CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN , | 02/2018          | 741.86 -                | 741.86           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1207  | CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN ,  | 02/2018          | 716.76 -                | 716.76           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1208  | UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN ,  | 03/2018          | 874.25 -                | 874.25           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1209  | CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN ,  | 03/2018          | 1,158.35 -              | 1,158.35         | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1210  | CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM ,                                          | 04/2013          | 151.59 -                | 151.59           | .00                         | 08/2013 -             | -           | -                                          | 0/0                         |
| 1211  | CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE                             | 04/2013          | 166.27 -                | 166.27           | .00                         | 08/2013 -             | -           | -                                          | 0/0                         |
| 1212  | CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE                                | 01/2013          | 182.28 -                | 182.00           | 24.36                       | 02/2013 -             | -           | -                                          | 0/0                         |
| 1213  | RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects                                           | 04/2017          | 388.00 -                | 447.37           | .00                         | 10/2017 -             | -           | -                                          | 0/0                         |
| 1214  | CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM ,  | 04/2017          | 318.42 -                | 318.42           | 7.50                        | 11/2017 -             | -           | -                                          | 0/0                         |
| 1215  | CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM ,  | 03/2017          | 375.80 -                | 375.80           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1216  | CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM ,  | 11/2017          | 290.05 -                | 290.05           | 18.12                       | 11/2017 -             | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                             |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                                     | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                                           | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1217  | CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM ,                           | 03/2018          | 264.84 -                | 264.84           | .00                         | 06/2018 -             | -           | -                                          | 0/0                         |
| 1218  | SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)                                           | 09/2011          | 1,250.00 -              | 1,250.00         | 1,329.17                    | 12/2013 -             | 12/2018     | 60(O) -                                    | 0/0                         |
| 1219  | DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,                                               | 06/2011          | 600.00 -                | 600.00           | 325.55                      | 06/2013 -             | -           | -                                          | 0/0                         |
| 1220  | TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)                                                             | 05/2010          | 374.00 -                | 374.00           | 237.00                      | 05/2013 -             | 12/2018     | 67(O) -                                    | 0/0                         |
| 1221  | 2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)                                                                 | 09/2011          | 485.00 -                | 485.00           | 406.68                      | 08/2013 -             | 12/2018     | 64(O) -                                    | 0/0                         |
| 1222  | 2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)                                                      | 04/2012          | 624.00 -                | 624.00           | 350.79                      | 04/2014 -             | 12/2019     | 68(O) -                                    | 0/0                         |
| 1223  | CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC                    | 03/2015          | 258.97 -                | 268.92           | .00                         | 08/2015 -             | -           | -                                          | 0/0                         |
| 1224  | REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC                    | 03/2015          | 157.18 162.00           | 162.00           | .00                         | 07/2015 -             | -           | -                                          | 0/0                         |
| 1225  | CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU , EPC                      | 11/2015          | 154.14 -                | 154.14           | .00                         | 08/2015 -             | -           | -                                          | 0/0                         |
| 1226  | FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,                              | 05/2015          | 1,387.11 -              | 1,387.11         | 915.30                      | 11/2017 -             | 05/2019     | 18(O) -                                    | 0/0                         |
| 1227  | TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,                                                                               | 06/2015          | 563.92 -                | 563.92           | 96.48                       | 12/2017 -             | 06/2019     | 18(O) -                                    | 0/0                         |
| 1228  | THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,                                                                                             | 07/2014          | 401.11 -                | 401.11           | 273.89                      | 01/2017 -             | -           | -                                          | 0/0                         |
| 1229  | THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU ,                                                                                     | 11/2014          | 563.92 -                | 563.92           | 186.50                      | 11/2016 -             | -           | -                                          | 0/0                         |
| 1230  | TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)                                                                                                     | 03/2007          | 516.00 -                | 516.00           | 627.42                      | 07/2008 -             | -           | -                                          | 0/0                         |
| 1231  | FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,                         | 02/2016          | 707.82 -                | 707.82           | 208.92                      | 08/2018 -             | 06/2019     | 10(O) -                                    | 0/0                         |
| 1232  | FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,                         | 02/2016          | 641.17 -                | 641.17           | 259.00                      | 07/2018 -             | 04/2019     | 9(O) -                                     | 0/0                         |
| 1233  | FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,                         | 03/2017          | 848.45 -                | 848.45           | 5.00                        | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/0                         |
| 1234  | FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects | 03/2016          | 641.17 -                | 641.17           | 244.33                      | 07/2016 -             | 04/2019     | 33(O) -                                    | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                         |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                 | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                       | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1235  | FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects                                             | 08/2017          | 1,176.37 -              | 1,176.37         | .00                         | 08/2017 -             | -           | -                                          | 0/0                         |
| 1236  | 4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects                                                 | 09/2017          | 244.27 -                | 244.27           | .00                         | 09/2017 -             | -           | -                                          | 0/0                         |
| 1237  | 4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects                                              | 09/2017          | 1,227.87 -              | 1,227.87         | .00                         | 09/2017 -             | -           | -                                          | 0/0                         |
| 1238  | SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,      | 12/2017          | 379.90 -                | 379.90           | .00                         | -                     | -           | -                                          | 0/0                         |
| 1239  | FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU ,                           | 02/2018          | 1,166.26 -              | 1,166.26         | .00                         | -                     | -           | -                                          | 0/0                         |
| 1240  | FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU , EPC  | 03/2018          | 505.35 -                | 505.35           | .00                         | -                     | -           | -                                          | 0/0                         |
| 1241  | FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTIKULAM (7/300) - [N24000827]NHAI,TAMIL NADU , EPC | 03/2018          | 628.71 -                | 628.71           | .00                         | -                     | -           | -                                          | 0/0                         |
| 1242  | TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU ,     | 03/2018          | 633.55 -                | 633.55           | .00                         | -                     | -           | -                                          | 0/0                         |
| 1243  | FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU ,      | 03/2018          | 1,016.92 -              | 1,016.92         | .00                         | -                     | -           | -                                          | 0/0                         |
| 1244  | FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU ,     | 03/2018          | 2,065.96 -              | 2,065.96         | .00                         | -                     | -           | -                                          | 0/0                         |
| 1245  | 4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)                                           | 04/2014          | 1,266.60 -              | 1,544.00         | 1,411.79                    | 09/2016 -             | 06/2019     | 33(O) -                                    | 0/0                         |
| 1246  | REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA , EPC    | 12/2013          | 177.18 -                | 177.18           | 40.51                       | 03/2016 -             | -           | -                                          | 3/4                         |
| 1247  | REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]PWD,TELANGANA , EPC  | 12/2013          | 158.65 -                | 158.65           | 103.50                      | 03/2016 -             | -           | -                                          | 3/4                         |
| 1248  | YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA , EPC      | 12/2013          | 244.08 -                | 244.08           | 38.32                       | 03/2016 -             | -           | -                                          | 1/4                         |
| 1249  | REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA , EPC    | 01/2014          | 340.00 -                | 340.00           | .00                         | 03/2016 -             | -           | -                                          | 0/2                         |
| 1250  | REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC   | 01/2014          | 270.00 -                | 270.00           | 19.84                       | 03/2016 -             | -           | -                                          | 1/4                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                          |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                  | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                        | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1251  | REHABILITATION AND UPGRADE OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA , EPC        | 10/2014          | 244.30 -                | 156.09           | .00                         | 12/2016 -             | -           | -                                          | 0/4                         |
| 1252  | REHABILITATION AND UPGRADE OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA , EPC         | 10/2014          | 295.47 -                | 313.27           | .00                         | 02/2017 -             | -           | -                                          | 0/1                         |
| 1253  | EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , EPC    | 03/2015          | 153.21 -                | 153.21           | .00                         | 01/2017 -             | -           | -                                          | 0/0                         |
| 1254  | CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA ,        | 03/2011          | 218.31 -                | 339.82           | 208.28                      | 12/2015 -             | -           | -                                          | 0/3                         |
| 1255  | FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,                                                                          | 12/2015          | 1,423.96 -              | 1,423.96         | 514.42                      | 11/2018 -             | 07/2019     | 8(O) -                                     | 0/0                         |
| 1256  | FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA ,                                                     | 03/2017          | 4,429.00 -              | 4,429.00         | .00                         | 03/2017 -             | -           | -                                          | 0/0                         |
| 1257  | FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA ,       | 03/2018          | 802.65 -                | 802.65           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1258  | FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA ,        | 03/2018          | 950.63 -                | 950.63           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1259  | FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA ,       | 03/2018          | 857.62 -                | 857.62           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1260  | FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHTRA - [N24000825]NHAI,TELANGANA ,     | 03/2018          | 828.29 -                | 828.29           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1261  | 2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC   | 10/2014          | 369.00 -                | 369.00           | 246.46                      | 03/2018 -             | -           | -                                          | 3/4                         |
| 1262  | IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA , EPC    | 05/2014          | 497.89 -                | 497.89           | 70.47                       | 04/2017 -             | -           | -                                          | 0/4                         |
| 1263  | GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)                                                                      | 02/2011          | 1,141.00 -              | 1,141.00         | 1,948.72                    | 08/2013 -             | -           | -                                          | 0/0                         |
| 1264  | BAREILLY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH , PPP (BOT)                                                                     | 03/2011          | 1,046.00 -              | 1,046.00         | 805.19                      | 09/2013 -             | -           | -                                          | 0/0                         |
| 1265  | 2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)                                                     | 07/2012          | 291.36 -                | 291.36           | 442.51                      | 01/2014 -             | 09/2018     | -                                          | 0/0                         |
| 1266  | ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)                                                                               | 03/2013          | 1,573.00 -              | 1,573.00         | 1,998.25                    | 09/2015 -             | -           | -                                          | 0/0                         |
| 1267  | CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH , EPC | 03/2015          | 629.74 -                | 629.74           | .00                         | - -                   | -           | -                                          | 0/0                         |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                        | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                              | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1268  | CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH , EPC                       | 01/2014          | 282.41 -                | 282.41           | .00                         | 03/2016 -             | -           | -                                          | 0/0                         |
| 1269  | STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH , EPC             | 10/2014          | 227.74 -                | 227.74           | .00                         | 10/2016 -             | -           | -                                          | 0/0                         |
| 1270  | FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH ,                                                                               | 05/2015          | 261.09 -                | 261.09           | 240.96                      | 05/2017 -             | -           | -                                          | 0/0                         |
| 1271  | 2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH ,                                         | 04/2014          | 351.34 -                | 351.34           | 425.99                      | 01/2016 -             | -           | -                                          | 0/0                         |
| 1272  | 2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH ,                                        | 09/2015          | 368.73 -                | 368.73           | 235.41                      | 09/2016 -             | -           | -                                          | 0/0                         |
| 1273  | 2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH ,                                                                   | 06/2014          | 301.04 -                | 301.04           | 194.60                      | 01/2016 -             | -           | -                                          | 0/0                         |
| 1274  | 2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH ,                                                           | 04/2014          | 495.78 -                | 495.78           | 608.73                      | 01/2016 -             | -           | -                                          | 0/0                         |
| 1275  | RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH , EPC                        | 10/2013          | 445.89 -                | 445.89           | .00                         | 03/2017 -             | -           | -                                          | 0/0                         |
| 1276  | 2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH , ITEM RATE | 11/2010          | 305.49 -                | 305.49           | .00                         | 03/2017 -             | -           | -                                          | 0/0                         |
| 1277  | BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH , EPC                                  | 01/2014          | 397.04 -                | 397.04           | .00                         | 10/2016 -             | -           | -                                          | 0/0                         |
| 1278  | ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH , EPC                                              | 06/2015          | 774.57 -                | 774.57           | .00                         | 03/2018 -             | -           | -                                          | 0/0                         |
| 1279  | BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH , EPC              | 10/2013          | 317.76 -                | 317.76           | 15.47                       | 03/2017 -             | -           | -                                          | 0/0                         |
| 1280  | JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH , EPC              | 10/2013          | 283.45 -                | 283.45           | .00                         | 10/2016 -             | -           | -                                          | 0/0                         |
| 1281  | SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH , EPC                                   | 10/2013          | 493.94 -                | 493.94           | .00                         | 03/2017 -             | -           | -                                          | 0/0                         |
| 1282  | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-II) - [N24000450]NHAI,UTTAR PRADESH ,                                              | 09/2015          | 785.78 -                | 785.78           | 839.63                      | 03/2018 -             | -           | -                                          | 0/0                         |
| 1283  | 6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)                                                                   | 07/2015          | 1,657.20 -              | 1,657.20         | 1,945.00                    | 01/2019 -             | 01/2019     | 0(0) -                                     | 0/0                         |
| 1284  | 4-LANING OF GHAGHRA BRIDGE TO VARANSI ( PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,                                                          | 12/2015          | 611.65 -                | 611.65           | 681.34                      | 06/2016 -             | -           | -                                          | 0/0                         |
| 1285  | FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,                                                                | 01/2016          | 815.28 -                | 815.28           | 328.63                      | 06/2018 -             | -           | -                                          | 0/0                         |
| 1286  | FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,                                                                 | 01/2016          | 1,027.53 -              | 1,027.53         | 433.51                      | 06/2018 -             | -           | -                                          | 0/0                         |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                        |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|----------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                      | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1287  | FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,                                                  | 06/2016          | 667.00 -                | 667.00           | 374.97                      | 07/2018 -             | -           | -                                          | 0/0                         |
| 1288  | FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,                                                   | 12/2015          | 667.00 -                | 667.00           | 439.40                      | 06/2018 -             | -           | -                                          | 0/0                         |
| 1289  | WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC                              | 05/2013          | 164.54 -                | 164.54           | .00                         | 08/2015 -             | -           | -                                          | 0/0                         |
| 1290  | WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH , EPC                         | 12/2014          | 207.88 -                | 207.88           | .00                         | -                     | -           | -                                          | 0/0                         |
| 1291  | WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH , EPC                        | 12/2014          | 207.88 -                | 207.88           | .00                         | -                     | -           | -                                          | 0/0                         |
| 1292  | MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH ,                                                                                  | 01/2016          | 683.24 -                | 683.24           | 536.60                      | -                     | -           | -                                          | 0/0                         |
| 1293  | DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH ,                                                       | 01/2016          | 701.12 -                | 701.12           | 842.34                      | 05/2019 -             | 05/2019     | 0(O)                                       | 0/0                         |
| 1294  | DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,                                | 01/2016          | 1,081.57 -              | 1,081.57         | 795.28                      | 06/2019 -             | 06/2019     | 0(O)                                       | 0/0                         |
| 1295  | ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,                                      | 03/2016          | 676.73 -                | 676.73           | 409.11                      | 04/2019 -             | 04/2019     | 0(O)                                       | 0/0                         |
| 1296  | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,     | 03/2016          | 1,404.50 -              | 1,404.50         | 193.08                      | -                     | -           | -                                          | 0/0                         |
| 1297  | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU - [N24000549]NHAI,UTTAR PRADESH , | 03/2016          | 1,396.74 -              | 1,396.74         | 153.06                      | -                     | -           | -                                          | 0/0                         |
| 1298  | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,                 | 03/2016          | 1,587.49 -              | 1,587.49         | 164.42                      | 04/2019 -             | 04/2019     | 0(O)                                       | 0/0                         |
| 1299  | FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH , | 03/2016          | 899.00 -                | 899.00           | 351.90                      | 04/2019 -             | 04/2019     | 0(O)                                       | 0/0                         |
| 1300  | 4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,  | 03/2016          | 1,668.00 -              | 1,668.00         | 322.13                      | -                     | 02/2020     | -                                          | 0/0                         |
| 1301  | 4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,        | 03/2016          | 1,408.00 -              | 1,408.00         | .00                         | -                     | 07/2020     | -                                          | 0/0                         |
| 1302  | 4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,                             | 03/2016          | 1,737.00 -              | 1,737.00         | 50.71                       | -                     | 04/2020     | -                                          | 0/0                         |
| 1303  | 4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,                                       | 08/2016          | 2,016.00 -              | 2,016.00         | 1,663.22                    | 04/2019 -             | 11/2019     | 7(O)                                       | 0/0                         |
| 1304  | CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH , | 12/2016          | 534.55 -                | 534.55           | 258.50                      | -                     | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                        |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|----------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                      | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1305  | CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,  | 01/2017          | 450.68 -                | 450.68           | 328.73                      | - -                   | -           | -                                          | 0/0                         |
| 1306  | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,  | 03/2017          | 1,373.28 -              | 1,373.28         | .00                         | 03/2020 -             | 11/2020     | 8(O) -                                     | 0/0                         |
| 1307  | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH , | 03/2017          | 1,184.71 -              | 1,310.00         | .00                         | 03/2020 -             | 08/2020     | 5(O) -                                     | 0/0                         |
| 1308  | DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH , | 03/2017          | 1,989.00 -              | 1,989.00         | 842.34                      | 03/2020 -             | 05/2020     | 2(O) -                                     | 0/0                         |
| 1309  | 6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH , | 03/2017          | 2,064.99 -              | 2,447.00         | 1,002.09                    | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/0                         |
| 1310  | DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,   | 12/2017          | 1,232.21 -              | 1,232.21         | 637.48                      | - -                   | 05/2020     | - -                                        | 0/0                         |
| 1311  | ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH , | 12/2017          | 207.00 -                | 207.00           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1312  | CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH , | 12/2017          | 305.00 -                | 305.00           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1313  | VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,                                                                           | 01/2018          | 450.77 -                | 450.77           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1314  | FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH ,  | 02/2018          | 670.50 -                | 670.50           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1315  | FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH ,                                 | 03/2018          | 809.07 -                | 809.07           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1316  | FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH ,                             | 03/2018          | 925.40 -                | 925.40           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1317  | CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH , | 03/2018          | 1,117.84 -              | 1,117.84         | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1318  | SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH , | 03/2018          | 2,140.93 -              | 2,140.93         | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1319  | 4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH , | 03/2018          | 1,120.57 -              | 1,120.57         | .00                         | - -                   | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                        |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|----------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                      | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1320  | REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH , | 03/2018          | 1,025.80 -              | 1,025.80         | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1321  | REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH , | 03/2018          | 1,115.28 -              | 1,115.28         | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1322  | CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH , | 02/2018          | 972.77 -                | 972.77           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1323  | HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,                                                                   | 11/2011          | 478.51 -                | 478.00           | 409.17                      | 10/2013 -             | 07/2019     | 69(O) -                                    | 0/0                         |
| 1324  | FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,    | 03/2016          | 720.00 -                | 720.00           | 181.70                      | - -                   | 10/2019     | - -                                        | 0/0                         |
| 1325  | 4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,    | 03/2016          | 1,443.00 -              | 1,443.00         | 122.72                      | - -                   | 02/2020     | - -                                        | 0/0                         |
| 1326  | 4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,                                       | 11/2012          | 605.84 -                | 605.84           | 722.46                      | 07/2018 -             | 07/2018     | -                                          | 0/0                         |
| 1327  | CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND , | 03/2018          | 274.31 -                | 274.31           | .00                         | 05/2018 -             | -           | -                                          | 0/4                         |
| 1328  | 2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND , | 03/2018          | 403.36 -                | 403.36           | .00                         | 06/2018 -             | -           | -                                          | 0/4                         |
| 1329  | 2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYAJNA - [N24000743]NHIDCL,UTTARAKHAND ,  | 03/2018          | 417.24 -                | 417.24           | .00                         | 05/2018 -             | -           | -                                          | 0/4                         |
| 1330  | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MORTH,UTTARAKHAND ,  | 12/2017          | 257.34 -                | 257.34           | .00                         | 12/2019 -             | 12/2019     | 0(O) -                                     | 0/0                         |
| 1331  | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MORTH,UTTARAKHAND ,  | 12/2017          | 200.34 -                | 200.34           | 43.14                       | 12/2019 -             | 12/2019     | 0(O) -                                     | 0/0                         |
| 1332  | WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MORTH,UTTARAKHAND ,  | 12/2017          | 248.22 -                | 248.22           | 57.01                       | 12/2019 -             | 12/2019     | 0(O) -                                     | 0/0                         |
| 1333  | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND ,  | 06/2017          | 282.08 -                | 282.08           | 66.19                       | 06/2019 -             | 06/2019     | 0(O) -                                     | 0/0                         |
| 1334  | RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MORTH,UTTARAKHAND ,  | 11/2017          | 232.81 -                | 232.81           | 48.23                       | 11/2019 -             | 11/2019     | 0(O) -                                     | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                         |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                 | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                       | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1335  | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MORTH,UTTARAKHAND ,  | 11/2017          | 283.51 -                | 284.00           | 94.50                       | 11/2019 -             | 11/2019     | 0(O) -                                     | 0/0                         |
| 1336  | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MORTH,UTTARAKHAND ,   | 11/2017          | 266.52 -                | 266.52           | 95.30                       | 11/2019 -             | 11/2019     | 0(O) -                                     | 0/0                         |
| 1337  | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MORTH,UTTARAKHAND ,      | 02/2018          | 418.88 -                | 418.88           | 92.42                       | 02/2020 -             | 02/2020     | 0(O) -                                     | 0/0                         |
| 1338  | REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND ,   | 02/2018          | 293.68 -                | 293.68           | .26                         | - -                   | -           | -                                          | 0/0                         |
| 1339  | CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MORTH,UTTARAKHAND ,   | 05/2018          | 248.00 -                | 248.00           | .00                         | 05/2020 -             | 05/2020     | 0(O) -                                     | 0/0                         |
| 1340  | REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND ,   | 03/2018          | 460.73 -                | 461.00           | .74                         | - -                   | -           | -                                          | 0/0                         |
| 1341  | 4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)                                                                   | 02/2011          | 1,078.84 -              | 1,078.84         | 2,312.98                    | 08/2013 -             | 06/2019     | 70(O) -                                    | 0/0                         |
| 1342  | 4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)                                                                | 02/2011          | 998.79 -                | 998.79           | 1,825.92                    | 08/2013 -             | 06/2020     | 82(O) -                                    | 0/0                         |
| 1343  | 6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)                                                       | 04/2012          | 1,396.18 -              | 1,396.18         | 2,614.84                    | 09/2014 -             | 05/2019     | 56(O) -                                    | 0/0                         |
| 1344  | KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL , PPP (ANNUITY)                                                                   | 02/2012          | 702.16 -                | 702.16           | 454.81                      | 07/2014 -             | 05/2019     | 58(O) -                                    | 0/0                         |
| 1345  | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH, WEST BENGAL ,  | 01/1991          | 322.00 -                | 322.00           | 56.41                       | 03/2018 -             | -           | -                                          | 0/0                         |
| 1346  | CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL ,                                                                       | 10/2015          | 361.15 -                | 361.15           | .00                         | - -                   | 01/2020     | -                                          | 0/0                         |
| 1347  | 4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI ( KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL ,                             | 12/2015          | 1,083.00 -              | 1,083.00         | 155.25                      | 06/2018 -             | 05/2019     | 11(O) -                                    | 0/0                         |
| 1348  | SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)                                                            | 04/2014          | 1,665.00 -              | 1,665.00         | 1,836.44                    | - -                   | 03/2019     | -                                          | 0/0                         |
| 1349  | CONSTRUCTION OF ROB -FLYOVER AT RANICHAK HALDIA - [N24000553]NHAI, WEST BENGAL ,                                                        | 03/2016          | 229.37 -                | 229.37           | 10.43                       | 11/2018 -             | 04/2019     | 5(O) -                                     | 0/0                         |
| 1350  | FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL ,   | 09/2016          | 767.03 -                | 767.03           | 156.04                      | 08/2018 -             | 09/2019     | 13(O) -                                    | 0/0                         |
| 1351  | CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL, WEST BENGAL , | 03/2017          | 158.65 -                | 158.65           | .00                         | 06/2018 -             | -           | -                                          | 0/0                         |
| 1352  | REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL ,   | 03/2018          | 1,261.98 -              | 1,261.98         | .00                         | - -                   | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                           |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                                   | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                                         | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
|       | Total                                                                                                                                                     |                  | 4,11,159.45             | 4,25,383.97      | 1,48,784.68                 |                       |             |                                            | 26/210                      |
|       |                                                                                                                                                           |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>SHIPPING AND PORTS</u>                                                                                                                                 |                  |                         |                  |                             |                       |             |                                            |                             |
| 1353  | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA , PPP (BOT) | 01/2007          | 366.39<br>669.46        | 669.46           | 413.91                      | 12/2010<br>-          | 12/2018     | 96(O)<br>-                                 | 0/0                         |
| 1354  | JAL MARG VIKAS PROJECT - [N25000072]IWAI,MULTI STATE ,                                                                                                    | 01/2018          | 4,200.00<br>-           | 4,200.00         | .00                         | 03/2023<br>-          | 03/2023     | 0(O)<br>-                                  | 0/0                         |
| 1355  | SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU , Public Private (SPV)                                                              | 06/2005          | 2,427.40<br>-           | 2,427.40         | 831.21                      | 10/2008<br>-          | -           | -                                          | 0/0                         |
| 1356  | ENNORE MANALI EXPRESS WAY F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU , Public Private (SPV)                                     | 10/2002          | 150.00<br>600.00        | 600.00           | 550.78                      | 03/2006<br>03/2016    | 02/2019     | 155(O)<br>35(R)                            | 0/0                         |
| 1357  | CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU , PPP (ANNUITY)                                                        | 02/2015          | 244.50<br>258.33        | 271.56           | 271.56                      | 12/2017<br>03/2018    | -           | -                                          | 1/1                         |
| 1358  | CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU ,                                                                         | 03/2016          | 600.00<br>257.90        | 257.90           | 1.45                        | 12/2017<br>05/2020    | 05/2020     | 29(O)<br>0(R)                              | 0/0                         |
|       | Total                                                                                                                                                     |                  | 7,988.29<br>-           | 8,426.32         | 2,068.91                    |                       |             |                                            | 1/1                         |
|       |                                                                                                                                                           |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>TELECOMMUNICATIONS</u>                                                                                                                                 |                  |                         |                  |                             |                       |             |                                            |                             |
| 1359  | GSM-RF EXPANSION PROJECT MTNL DELHI (3G) - [N26000105]MTNL,DELHI ,                                                                                        | 06/2016          | 418.26<br>-             | 418.26           | 172.30                      | 06/2017<br>-          | -           | -                                          | 0/0                         |
| 1360  | MAHARASHTRA CORE (LOT1) - [N26000108]BSNL,MAHARASHTRA , Central Sector Projects                                                                           | 08/2017          | 167.68<br>-             | 167.68           | 32.44                       | 04/2018<br>02/2019    | 02/2019     | 10(O)<br>0(R)                              | 0/0                         |
| 1361  | MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA , Central Sector Projects                                                                      | 08/2017          | 215.30<br>214.10        | 214.10           | 33.46                       | 05/2018<br>02/2019    | 02/2019     | 9(O)<br>0(R)                               | 0/0                         |
| 1362  | MAHARASHTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA , Central Sector Projects                                                 | 01/2018          | 231.80<br>231.80        | 231.80           | 77.65                       | 10/2018<br>02/2019    | 02/2019     | 4(O)<br>0(R)                               | 0/0                         |
| 1363  | NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE ,                                                                                                       | 03/2012          | 13,334.00<br>-          | 24,664.00        | 8,397.00                    | 07/2015<br>-          | 05/2020     | 58(O)<br>-                                 | 0/0                         |
| 1364  | NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE , Central Sector Projects                              | 09/2014          | 2,111.17<br>-           | 2,011.17         | 253.90                      | 09/2014<br>-          | -           | -                                          | 0/70                        |
|       | Total                                                                                                                                                     |                  | 16,478.21<br>-          | 27,707.01        | 8,966.75                    |                       |             |                                            | 0/70                        |
|       |                                                                                                                                                           |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>URBAN DEVELOPMENT</u>                                                                                                                                  |                  |                         |                  |                             |                       |             |                                            |                             |
| 1365  | CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH ,                        | 07/2014          | 232.00<br>-             | 232.00           | .00                         | -<br>-                | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                      |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|--------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                              | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                    | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1366  | CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH ,                       | 06/2014          | 157.84 -                | 157.84           | 134.62                      | 03/2017 -             | -           | -                                          | 4/5                         |
| 1367  | REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH , | 08/2007          | 246.90 -                | 246.90           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1368  | CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD,ANDHRA PRADESH ,                                             | 01/2018          | 206.58 -                | 206.58           | .02                         | 03/2019 -             | 03/2019     | 0(O) -                                     | 0/7                         |
| 1369  | IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR ,                                                                                 | 10/2005          | 956.00 -                | 956.00           | 651.21                      | 03/2015 -             | 03/2021     | 72(O) -                                    | 0/0                         |
| 1370  | CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR ,                | 02/2016          | 496.18 496.00           | 498.99           | 34.09                       | 06/2017 07/2017       | 06/2020     | 36(O) 35(R)                                | 0/0                         |
| 1371  | DELHI MRTS PHASE-III - [N28000056]MMRC,DELHI ,                                                                                       | 09/2011          | 38,585.00 -             | 38,585.00        | 37,044.70                   | 03/2016 05/2019       | 05/2019     | 38(O) 0(R)                                 | 0/0                         |
| 1372  | ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,            | 10/2013          | 1,219.21 -              | 1,592.00         | 331.12                      | 10/2019 -             | 03/2020     | 5(O) -                                     | 0/7                         |
| 1373  | CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI ,         | 07/2012          | 884.30 -                | 884.30           | 647.07                      | 12/2015 -             | -           | -                                          | 0/0                         |
| 1374  | REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI ,                                                                         | 06/2012          | 4,264.00 -              | 4,439.23         | 3,671.53                    | 11/2019 -             | 11/2019     | 0(O) -                                     | 3/7                         |
| 1375  | CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG NEW DELHI - [N28000087]CPWD,DELHI ,            | 06/2015          | 197.33 -                | 197.33           | 14.25                       | 04/2019 06/2020       | 06/2020     | 14(O) 0(R)                                 | 0/2                         |
| 1376  | REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI ,                                                              | 07/2016          | 2,694.00 -              | 2,694.00         | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1377  | RE-DEVELOPMENT OF GOVT. OF INDIA PRESS MINTO ROAD NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI ,         | 11/2017          | 238.56 -                | 238.56           | 3.36                        | 05/2020 -             | 05/2020     | 0(O) -                                     | 0/0                         |
| 1378  | CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI ,       | 12/2017          | 188.00 -                | 188.00           | 85.71                       | 06/2019 -             | 06/2019     | 0(O) -                                     | 0/0                         |
| 1379  | REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI ,                                                                       | 10/2016          | 422.00 -                | 422.00           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1380  | REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI ,        | 10/2016          | 392.00 -                | 392.00           | .00                         | - -                   | -           | -                                          | 0/0                         |
| 1381  | SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI ,       | 10/2016          | 248.20 -                | 248.20           | 1.21                        | 04/2018 -             | -           | -                                          | 0/0                         |
| 1382  | CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI ,                                   | 10/2017          | 271.90 -                | 271.90           | 4.44                        | 11/2019 -             | 11/2019     | 0(O) -                                     | 0/0                         |
| 1383  | CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR GUJARAT - [N12000106]HSCL,GUJARAT ,                                     | 01/2013          | 175.00 -                | 175.00           | 1.83                        | - -                   | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                    |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                            | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                  | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1384  | DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,                               | 11/2012          | 270.83<br>-             | 270.83           | 163.97                      | 11/2014<br>-          | 02/2019     | 51(O)<br>-                                 | 2/8                         |
| 1385  | CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND ,                        | 12/2007          | 253.92<br>253.92        | 253.92           | 193.97                      | 06/2016<br>-          | -           | -                                          | 0/0                         |
| 1386  | CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI KODERMA HAZARIBAG RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND ,             | 12/2007          | 200.00<br>-             | 200.00           | 131.15                      | 03/2018<br>-          | -           | -                                          | 0/0                         |
| 1387  | CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND ,                                     | 02/2014          | 787.29<br>-             | 787.29           | 285.30                      | 12/2016<br>-          | 12/2018     | 24(O)<br>-                                 | 0/0                         |
| 1388  | CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND ,                                                          | 04/2013          | 170.00<br>-             | 170.00           | 88.91                       | 04/2018<br>-          | -           | -                                          | 0/0                         |
| 1389  | 2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,                                             | 09/2012          | 171.86<br>-             | 171.86           | 41.28                       | 03/2016<br>-          | 04/2020     | 49(O)<br>-                                 | 1/6                         |
| 1390  | CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA ,                                             | 05/2005          | 768.88<br>1,070.97      | 1,113.34         | 1,085.64                    | 02/2014<br>-          | -           | -                                          | 0/0                         |
| 1391  | CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA ,                                  | 07/2011          | 324.87<br>324.87        | 324.87           | 262.93                      | 12/2015<br>-          | -           | -                                          | 0/0                         |
| 1392  | BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA ,                                                                 | 02/2014          | 26,405.14<br>-          | 26,405.14        | 499.85                      | 02/2019<br>-          | 03/2020     | 13(O)<br>-                                 | 0/0                         |
| 1393  | RESIDENTIAL QUATERS FOR HAL BANGLORE - [N28000103]CPWD,KARNATAKA ,                                                                 | 12/2016          | 246.31<br>-             | 246.31           | 34.88                       | 02/2020<br>09/2020    | 09/2020     | 7(O)<br>0(R)                               | 0/0                         |
| 1394  | CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,                                                   | 01/2010          | 165.23<br>-             | 165.23           | 58.85                       | 10/2012<br>-          | 03/2019     | 77(O)<br>-                                 | 1/6                         |
| 1395  | KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA ,                                                                                | 07/2012          | 5,181.79<br>-           | 5,181.79         | .00                         | 07/2017<br>-          | 12/2019     | 29(O)<br>-                                 | 0/0                         |
| 1396  | C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]CPWD,KERALA ,    | 09/2017          | 150.29<br>-             | 150.29           | 2.58                        | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 2/7                         |
| 1397  | NAGPUR METRO RAIL - [N28000085]NMRL,MAHARASHTRA ,                                                                                  | 08/2014          | 8,680.00<br>8,680.00    | 8,680.00         | 4,787.71                    | 03/2018<br>12/2019    | 12/2019     | 21(O)<br>0(R)                              | 0/0                         |
| 1398  | MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRL,MAHARASHTRA ,                                                          | 07/2013          | 23,136.00<br>-          | 23,136.00        | .00                         | 01/2015<br>-          | 05/2020     | 64(O)<br>-                                 | 0/0                         |
| 1399  | CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY POWAI MUMBAI - [N28000117]CPWD,MAHARASHTRA ,                                      | 01/2018          | 223.37<br>-             | 223.37           | 4.00                        | 07/2020<br>09/2018    | 09/2020     | 2(O)<br>24(R)                              | 1/14                        |
| 1400  | PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA ,                                                                  | 12/2016          | 11,420.00<br>-          | 11,420.00        | 1,938.17                    | 11/2021<br>-          | 11/2021     | 0(O)<br>-                                  | 0/0                         |
| 1401  | NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects                                        | 02/2014          | 216.69<br>-             | 216.69           | 52.00                       | 03/2015<br>-          | 11/2019     | 56(O)<br>-                                 | 0/10                        |
| 1402  | CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA , | 04/2014          | 151.33<br>-             | 151.33           | 7.15                        | 09/2017<br>-          | 12/2018     | 15(O)<br>-                                 | 0/0                         |
| 1403  | CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR PUNJAB - [N28000088]CPWD,PUNJAB ,                         | 02/2014          | 388.00<br>-             | 388.00           | 395.14                      | 05/2017<br>02/2019    | 03/2019     | 22(O)<br>1(R)                              | 8/12                        |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                              |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|--------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                                      | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                                            | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1404  | CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR PUNJAB - [N28000102]CPWD,PUNJAB ,                                                             | 08/2016          | 294.00 -                | 294.00           | 134.64                      | 04/2019<br>06/2019    | 09/2019     | 5(O)<br>3(R)                               | 4/8                         |
| 1405  | CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR PUNJAB - [N28000120]CPWD,PUNJAB ,                                                              | 01/2018          | 430.00 -                | 430.00           | 25.56                       | 09/2018<br>-          | 09/2018     | -                                          | 0/5                         |
| 1406  | CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN ,                           | 05/2015          | 189.00 -                | 189.00           | .00                         | 03/2017<br>-          | -           | -                                          | 0/0                         |
| 1407  | DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN ,                                         | 12/2016          | 549.31 -                | 540.42           | 215.67                      | 07/2019<br>-          | 10/2019     | 3(O)<br>-                                  | 0/0                         |
| 1408  | STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU ,                                                                                 | 04/2014          | 332.72 -                | 342.00           | 321.13                      | 09/2016<br>-          | -           | -                                          | 0/0                         |
| 1409  | CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,                                                                                              | 02/2009          | 14,600.00 -             | 19,058.00        | 16,352.77                   | 12/2015<br>-          | -           | -                                          | 12/24                       |
| 1410  | C/O OF 152 NOS TYPE-II 304 NOS TYPE-III 76 NOS TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU ,                             | 12/2015          | 209.00 -                | 209.00           | 52.00                       | 10/2019<br>-          | 10/2019     | 0(O)<br>-                                  | 0/6                         |
| 1411  | CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,                                                                                          | 06/2016          | 3,770.00 -              | 3,770.00         | .00                         | 03/2018<br>-          | -           | -                                          | 0/0                         |
| 1412  | CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU ,                                                                          | 11/2017          | 348.77 -                | 348.77           | .00                         | -<br>-                | -           | -                                          | 0/0                         |
| 1413  | ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA ,                                        | 10/2016          | 209.84 -                | 209.84           | 12.71                       | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/5                         |
| 1414  | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA ,                                                                   | 03/2007          | 149.73<br>173.00        | 175.94           | 178.65                      | 12/2015<br>-          | -           | -                                          | 0/0                         |
| 1415  | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA ,                                                                  | 12/2007          | 202.61<br>227.00        | 227.00           | 199.95                      | 12/2016<br>-          | -           | -                                          | 0/0                         |
| 1416  | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA ,                                                                | 10/2011          | 175.49<br>206.71        | 206.71           | 141.28                      | 12/2016<br>-          | -           | -                                          | 0/0                         |
| 1417  | LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH ,                                                                                        | 01/2016          | 6,928.00<br>6,928.00    | 6,928.00         | 2,536.77                    | 03/2019<br>-          | 03/2019     | 0(O)<br>-                                  | 0/0                         |
| 1418  | CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH ,                                                                        | 11/2017          | 171.72 -                | 171.72           | .00                         | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 1419  | CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND ,                          | 12/2008          | 114.26<br>266.00        | 266.00           | .00                         | 12/2013<br>-          | 10/2019     | 70(O)<br>-                                 | 0/0                         |
| 1420  | CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL , Central Sector Projects | 08/2012          | 185.37 -                | 185.37           | 178.30                      | 03/2016<br>-          | -           | -                                          | 0/0                         |
| 1421  | CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL ,                                               | 02/2014          | 156.57 -                | 156.57           | 146.40                      | 08/2016<br>-          | 03/2019     | 31(O)<br>-                                 | 9/16                        |



**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                         |                  |                         |                  |                             | Date of Commissioning |             | (December 2018)                            |                             |
|-------|-------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                 | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                       | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1422  | NSG AT KOLKATA - [N28000104]CPWD, WEST BENGAL , Central Sector Projects | 10/2014          | 162.88<br>-             | 162.88           | 96.48                       | 04/2018<br>-          | 07/2019     | 15(O)<br>-                                 | 3/6                         |
|       | Total                                                                   |                  | 1,60,566.07<br>-        | 1,66,153.31      | 73,250.95                   |                       |             |                                            | 50/161                      |
|       |                                                                         |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>DEFENCE PRODUCTION</u>                                               |                  |                         |                  |                             |                       |             |                                            |                             |
| 1423  | CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL, GOA ,                      | 12/2016          | 167.69<br>168.00        | 170.37           | 103.91                      | 05/2018<br>01/2019    | 01/2019     | 8(O)<br>0(R)                               | 6/10                        |
| 1424  | CONSTRUCTION WORKS PHASE 3B - [N39000002]GSL, GOA ,                     | 12/2016          | 285.95<br>286.00        | 291.29           | 56.87                       | 08/2020<br>-          | 08/2020     | 0(O)<br>-                                  | 5/8                         |
|       | Total                                                                   |                  | 453.64<br>-             | 461.66           | 160.78                      |                       |             |                                            | 11/18                       |
|       |                                                                         |                  |                         |                  |                             |                       |             |                                            |                             |
|       | Grand Total                                                             |                  | 18,17,469.76            | 21,33,649.81     | 8,06,997.78                 |                       |             |                                            | 2330/4505                   |


## Summary of projects in the Flash Report for the month of December, 2018

### Project Implementation - Current Status:

|                                                                                     |      |
|-------------------------------------------------------------------------------------|------|
| Number of Projects in Previous Month                                                | 1443 |
| Number of Projects completed/dropped/frozen in Current Month                        | 22   |
| Number of Projects elevated to the status of Major project during the current month | 1    |
| Number of Projects Added in Current Month                                           | 4    |
| Number of Projects in Current Month                                                 | 1424 |

### Brief Analysis

**Project Status with respect to Original Schedule:** Out of 1424 projects, 26 projects are ahead of schedule, 328 projects are on schedule 384 projects are delayed. 607 projects do not have fixed dates of commissioning. 79 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

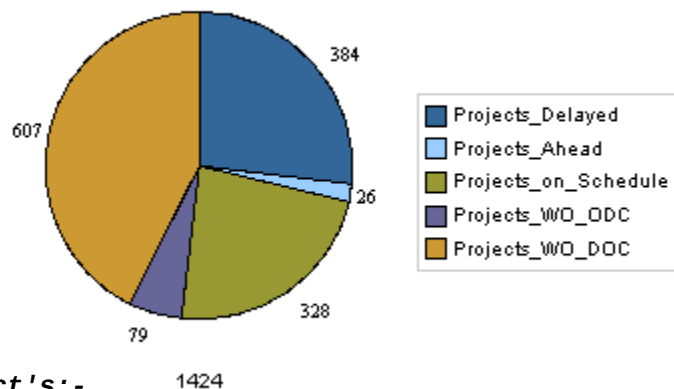


Total No Of Project's:-

### Investment Scenario

**Total original cost of implementation of 1424 projects when sanctioned, was of the order of Rs. 1817469.76 crore but this was subsequently revised to Rs. 2133649.81 crore implying a cost overrun of 17.4%. The expenditure incurred on these projects till December, 2018 is Rs. 806997.78 crore, which is 37.8% of the anticipated cost of the projects.**

Figures are in Rs. Crore

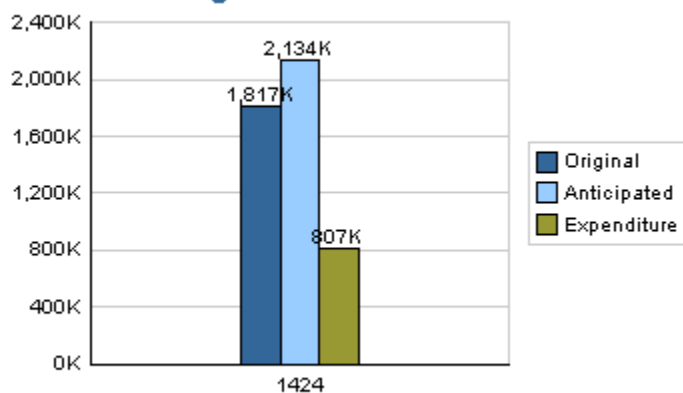

## Sector wise current status of projects on the Flash Report


### ATOMIC ENERGY

#### Current Status:

|                            |   |
|----------------------------|---|
| Number of Projects         | 4 |
| Number of Projects Delayed | 4 |

#### Brief Analysis

**Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.**

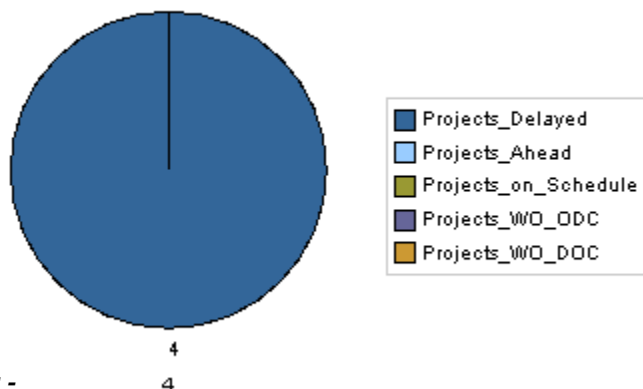


Total No Of Project's:-

#### Investment Scenario

**Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 74849 crore implying a cost overrun of 11.5%. The expenditure incurred on these projects till December, 2018 is Rs. 40488.52 crore, which is 54.1% of the anticipated cost of the projects.**

Figures are in Rs. Crore

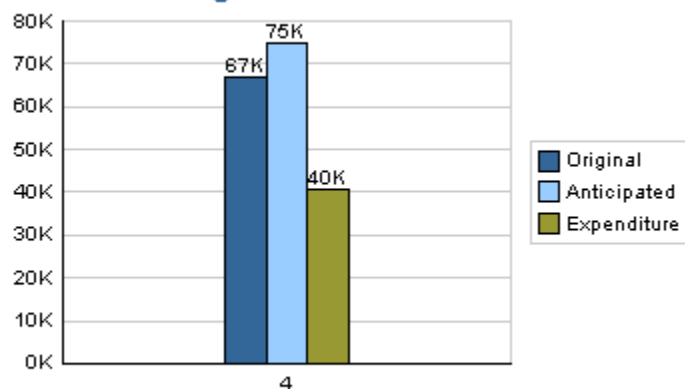

## Sector wise current status of projects on the Flash Report


### CIVIL AVIATION

#### Current Status:

|                            |   |
|----------------------------|---|
| Number of Projects         | 1 |
| Number of Projects Delayed | 1 |

#### Brief Analysis

**Project Status with respect to Original Schedule: Out of 1 project, 1 project is delayed.**

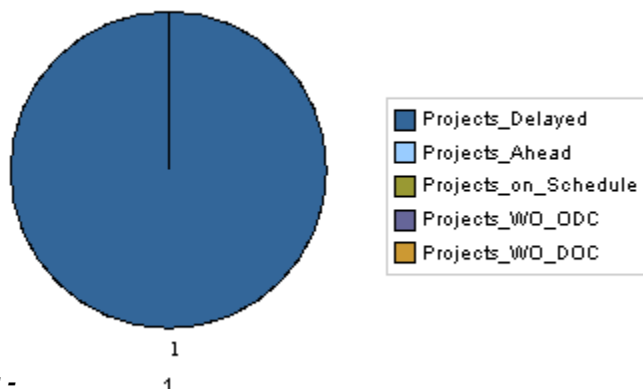


Total No Of Project's:-

#### Investment Scenario

**Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 314.61 crore but this was subsequently anticipated to Rs. 441.33 crore implying a cost overrun of 40.3%. The expenditure incurred on these projects till December, 2018 is Rs. 85.79 crore, which is 19.4% of the anticipated cost of the projects.**

Figures are in Rs. Crore

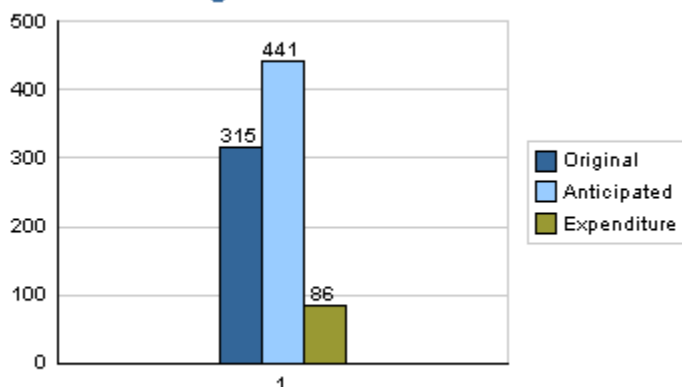

## Sector wise current status of projects on the Flash Report


### COAL

#### Current Status:

|                                                  |    |
|--------------------------------------------------|----|
| Number of Projects                               | 97 |
| Number of Projects On Schedule                   | 49 |
| Number of Projects Delayed                       | 36 |
| Number of Projects Ahead                         | 1  |
| Number of Projects Without Date Of Commissioning | 11 |

#### Brief Analysis

**Project Status with respect to Original Schedule:** Out of 97 projects, 1 project is ahead of schedule, 49 projects are on schedule 36 projects are delayed. 11 projects do not have fixed dates of commissioning.

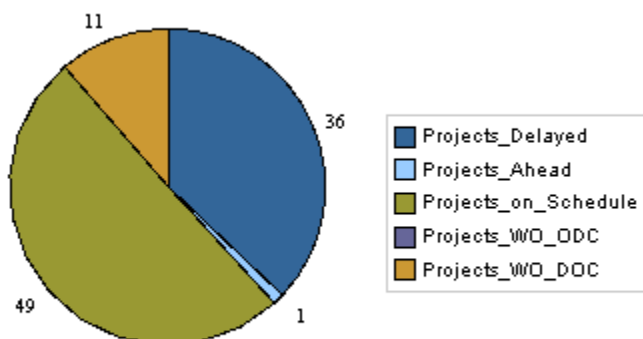


Total No Of Project's:-

97

#### Investment Scenario

**Total original cost of implementation of 97 projects when sanctioned, was of the order of Rs. 96954.88 crore but this was subsequently anticipated to Rs. 96426.38 cr The expenditure incurred on these projects till December, 2018 is Rs. 28901.32 crore, which is 30% of the anticipated cost of the projects.**

Figures are in Rs. Crore

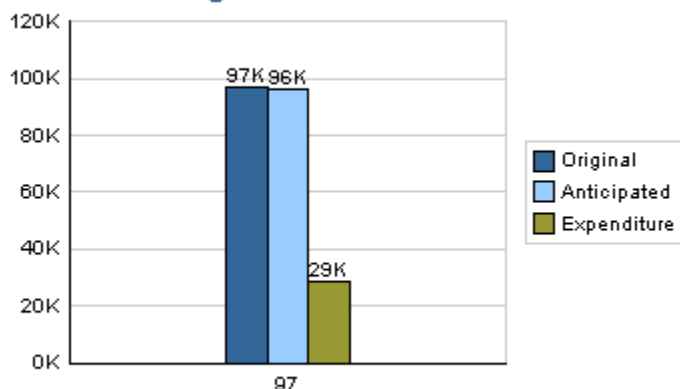

## Sector wise current status of projects on the Flash Report


### FERTILISERS

#### Current Status:

|                                |   |
|--------------------------------|---|
| Number of Projects             | 6 |
| Number of Projects On Schedule | 4 |
| Number of Projects Delayed     | 2 |

#### Brief Analysis

**Project Status with respect to Original Schedule: Out of 6 projects, 4 projects are on schedule 2 projects are delayed.**

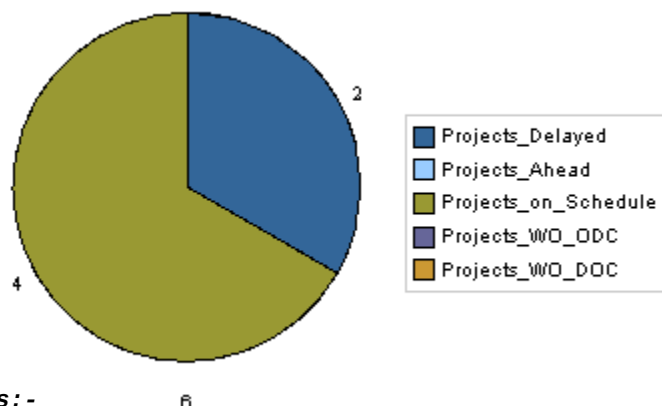


Total No Of Project's:-

6

#### Investment Scenario

**Total original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 1781.92 crore but this was subsequently anticipated to Rs. 1793.57 crore implying a cost overrun of .7%. The expenditure incurred on these projects till December, 2018 is Rs. 690.15 crore, which is 38.5% of the anticipated cost of the projects.**

Figures are in Rs. Crore

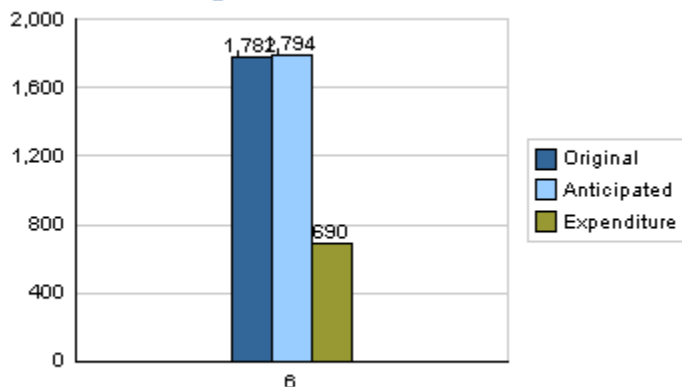

## Sector wise current status of projects on the Flash Report


### MINES

#### Current Status:

|                                |   |
|--------------------------------|---|
| Number of Projects             | 5 |
| Number of Projects On Schedule | 5 |

#### Brief Analysis

**Project Status with respect to Original Schedule: Out of 5 projects, 5 projects are on schedule**




Total No Of Project's:-

#### Investment Scenario

**Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 7078.62 crore but this was subsequently anticipated to Rs. 7078.62 crore. The expenditure incurred on these projects till December, 2018 is Rs. 556.5 crore, which is 7.9% of the anticipated cost of the projects.**

Figures are in Rs. Crore

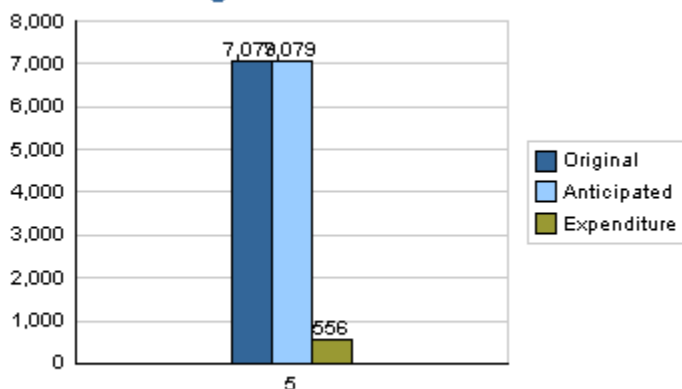

## Sector wise current status of projects on the Flash Report

### STEEL


#### Current Status:

|                                |    |
|--------------------------------|----|
| Number of Projects             | 13 |
| Number of Projects On Schedule | 1  |
| Number of Projects Delayed     | 9  |

|                                                  |   |
|--------------------------------------------------|---|
| Number of Projects Without Date Of Commissioning | 3 |
|--------------------------------------------------|---|

#### Brief Analysis

**Project Status with respect to Original Schedule: Out of 13 projects, 1 project is on schedule 9 projects are delayed. 3 projects do not have fixed dates of commissioning.**

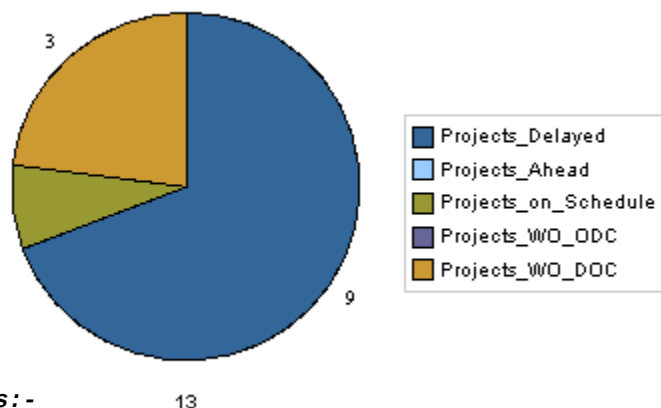


Total No Of Project's:-

13

#### Investment Scenario

**Total original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 32529.65 crore but this was subsequently anticipated to Rs. 32317.05 cr The expenditure incurred on these projects till December, 2018 is Rs. 21213.14 crore, which is 65.6% of the anticipated cost of the projects.**

Figures are in Rs. Crore

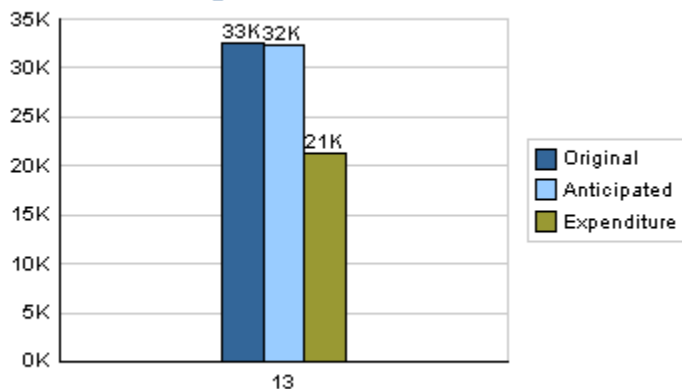



## Sector wise current status of projects on the Flash Report


### PETROLEUM

#### Current Status:

|                                                  |     |
|--------------------------------------------------|-----|
| Number of Projects                               | 137 |
| Number of Projects On Schedule                   | 82  |
| Number of Projects Delayed                       | 33  |
| Number of Projects Ahead                         | 10  |
| Number of Projects Without Date Of Commissioning | 12  |

#### Brief Analysis

Project Status with respect to Original Schedule: Out of 137 projects, 10 projects are ahead of schedule, 82 projects are on schedule 33 projects are delayed. 12 projects do not have fixed dates of commissioning.

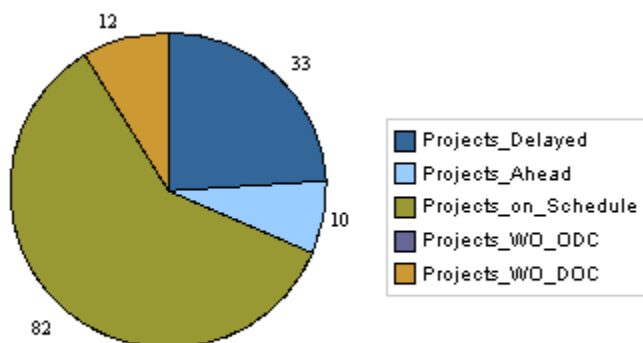


Total No Of Project's:-

137

#### Investment Scenario

Total original cost of implementation of 137 projects when sanctioned, was of the order of Rs. 221562.48 crore but this was subsequently anticipated to Rs. 223009.33 crore implying a cost overrun of .7%. The expenditure incurred on these projects till December, 2018 is Rs. 72956.33 crore, which is 32.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

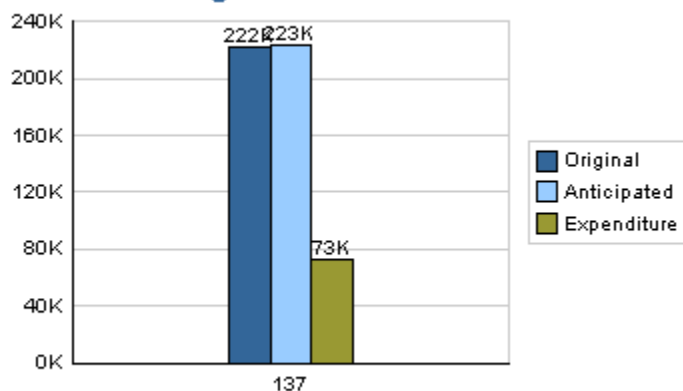

## Sector wise current status of projects on the Flash Report


### POWER

#### Current Status:

|                                                  |    |
|--------------------------------------------------|----|
| Number of Projects                               | 95 |
| Number of Projects On Schedule                   | 27 |
| Number of Projects Delayed                       | 56 |
| Number of Projects Ahead                         | 1  |
| Number of Projects Without Date Of Commissioning | 11 |

#### Brief Analysis

**Project Status with respect to Original Schedule:** Out of 95 projects, 1 project is ahead of schedule, 27 projects are on schedule 56 projects are delayed. 11 projects do not have fixed dates of commissioning.

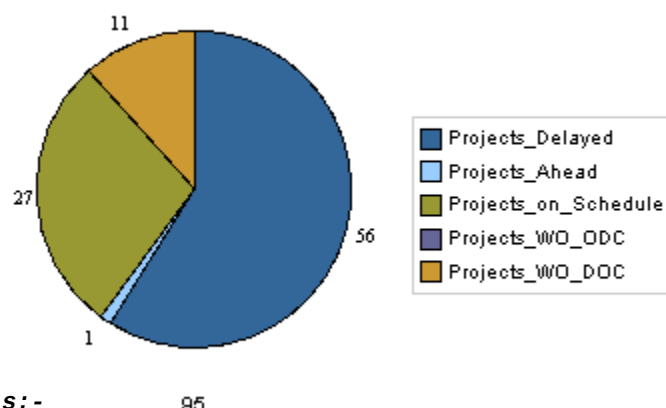


Total No Of Project's:-

#### Investment Scenario

**Total original cost of implementation of 95 projects when sanctioned, was of the order of Rs. 296370.25 crore but this was subsequently anticipated to Rs. 359705.13 crore implying a cost overrun of 21.4%. The expenditure incurred on these projects till December, 2018 is Rs. 236102.37 crore, which is 65.6% of the anticipated cost of the projects.**

Figures are in Rs. Crore

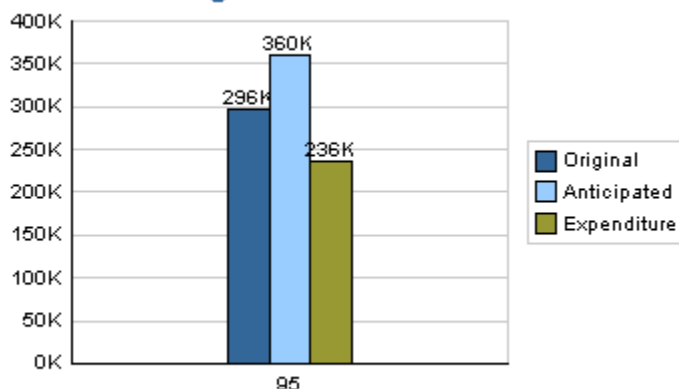

## Sector wise current status of projects on the Flash Report


### HEAVY INDUSTRY

#### Current Status:

|                                |   |
|--------------------------------|---|
| Number of Projects             | 2 |
| Number of Projects On Schedule | 1 |
| Number of Projects Delayed     | 1 |

#### Brief Analysis

**Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project is delayed.**

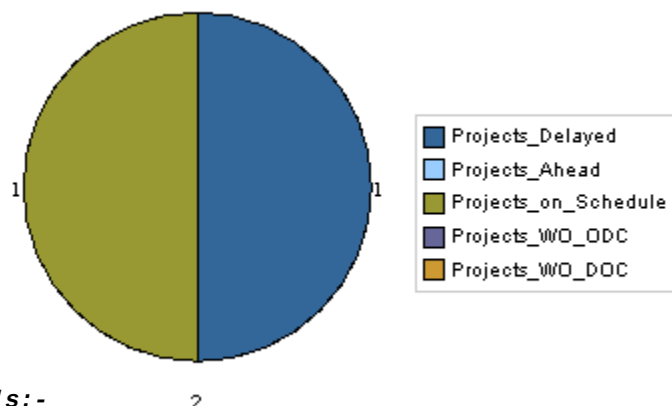


Total No Of Project's:-

2

#### Investment Scenario

**Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 3272 crore but this was subsequently anticipated to Rs. 5381.3 crore implying a cost overrun of 64.5%. The expenditure incurred on these projects till December, 2018 is Rs. 3095.09 crore, which is 57.5% of the anticipated cost of the projects.**

Figures are in Rs. Crore

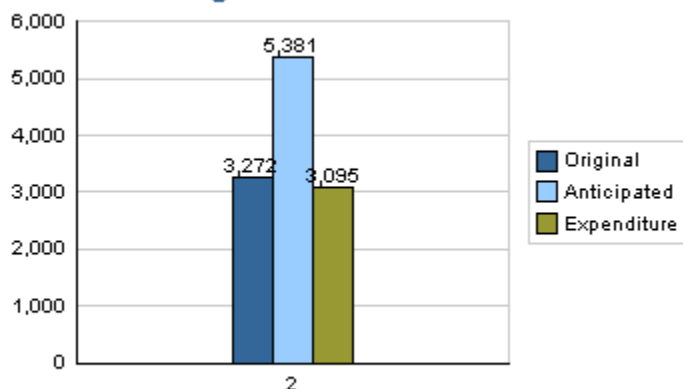

## Sector wise current status of projects on the Flash Report


### HEALTH AND FAMILY WELFARE

#### Current Status:

|                                                           |    |
|-----------------------------------------------------------|----|
| Number of Projects                                        | 20 |
| Number of Projects On Schedule                            | 6  |
| Number of Projects Delayed                                | 5  |
| Number of Projects Without Original Date of Commissioning | 6  |
| Number of Projects Without Date Of Commissioning          | 3  |

#### Brief Analysis

**Project Status with respect to Original Schedule:** Out of 20 projects, 6 projects are on schedule 5 projects are delayed. 3 projects do not have fixed dates of commissioning. 6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

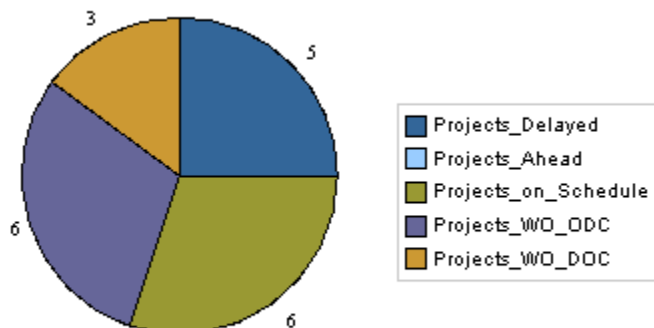


Total No Of Project's:-

20

#### Investment Scenario

**Total original cost of implementation of 20 projects when sanctioned,** was of the order of Rs. 8129.23 crore but this was subsequently anticipated to Rs. 8246.52 crore implying a cost overrun of 1.4%. The expenditure incurred on these projects till December, 2018 is Rs. 2779.69 crore, which is 33.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

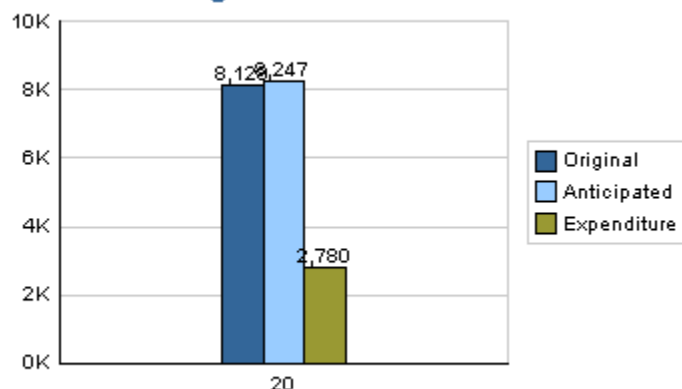

## Sector wise current status of projects on the Flash Report


### RAILWAYS

#### Current Status:

|                                                           |     |
|-----------------------------------------------------------|-----|
| Number of Projects                                        | 367 |
| Number of Projects On Schedule                            | 91  |
| Number of Projects Delayed                                | 94  |
| Number of Projects Ahead                                  | 9   |
| Number of Projects Without Original Date of Commissioning | 28  |
| Number of Projects Without Date Of Commissioning          | 145 |

#### Brief Analysis

**Project Status with respect to Original Schedule:** Out of 367 projects, 9 projects are ahead of schedule, 91 projects are on schedule 94 projects are delayed. 145 projects do not have fixed dates of commissioning. 28 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

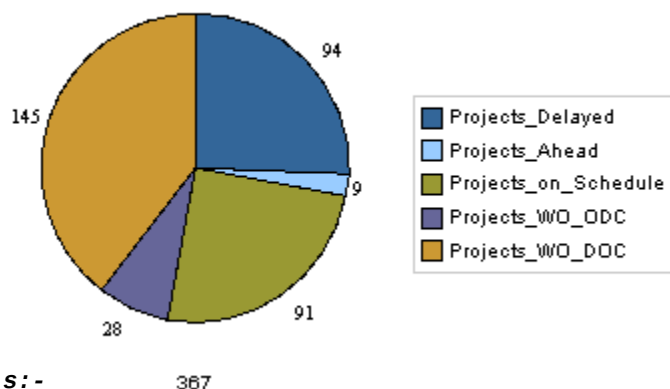


Total No Of Project's:-

#### Investment Scenario

**Total original cost of implementation of 367 projects when sanctioned, was of the order of Rs. 485710.46 crore but this was subsequently anticipated to Rs. 696269.31 crore implying a cost overrun of 43.4%. The expenditure incurred on these projects till December, 2018 is Rs. 166896.81 crore, which is 24% of the anticipated cost of the projects.**

Figures are in Rs. Crore

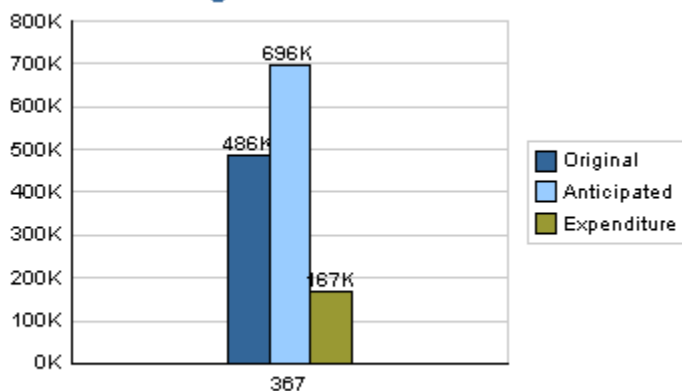

## Sector wise current status of projects on the Flash Report


### ROAD TRANSPORT AND HIGHWAYS

#### Current Status:

|                                                           |     |
|-----------------------------------------------------------|-----|
| Number of Projects                                        | 605 |
| Number of Projects On Schedule                            | 49  |
| Number of Projects Delayed                                | 112 |
| Number of Projects Ahead                                  | 5   |
| Number of Projects Without Original Date of Commissioning | 45  |
| Number of Projects Without Date Of Commissioning          | 394 |

#### Brief Analysis

**Project Status with respect to Original Schedule:** Out of 605 projects, 5 projects are ahead of schedule, 49 projects are on schedule 112 projects are delayed. 394 projects do not have fixed dates of commissioning. 45 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

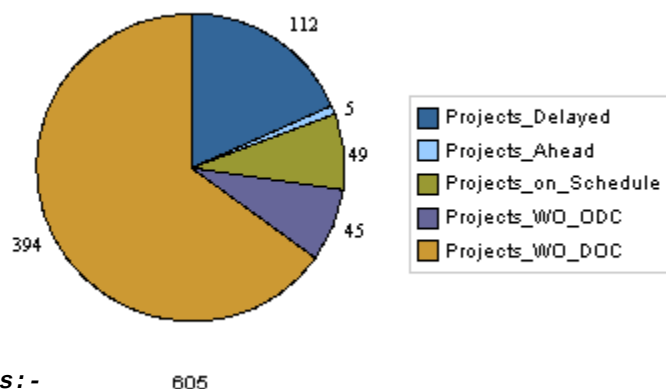


Total No Of Project's:-

605

#### Investment Scenario

**Total original cost of implementation of 605 projects when sanctioned, was of the order of Rs. 411159.45 crore but this was subsequently anticipated to Rs. 425383.97 crore implying a cost overrun of 3.5%. The expenditure incurred on these projects till December, 2018 is Rs. 148784.68 crore, which is 35% of the anticipated cost of the projects.**

Figures are in Rs. Crore

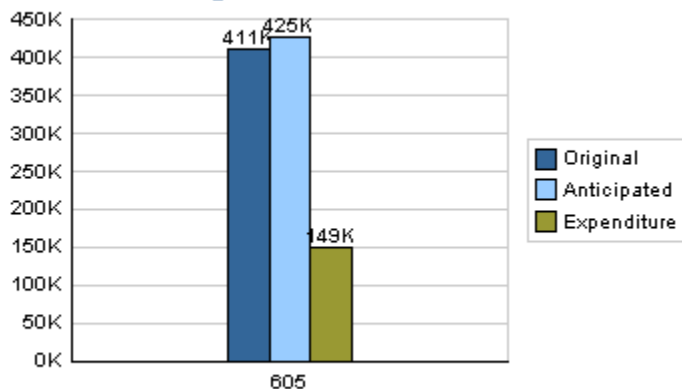

## Sector wise current status of projects on the Flash Report

### SHIPPING AND PORTS


#### Current Status:

|                                |   |
|--------------------------------|---|
| Number of Projects             | 6 |
| Number of Projects On Schedule | 1 |
| Number of Projects Delayed     | 3 |

|                                                  |   |
|--------------------------------------------------|---|
| Number of Projects Without Date Of Commissioning | 2 |
|--------------------------------------------------|---|

#### Brief Analysis

**Project Status with respect to Original Schedule: Out of 6 projects, 1 project is on schedule 3 projects are delayed. 2 projects do not have fixed dates of commissioning.**

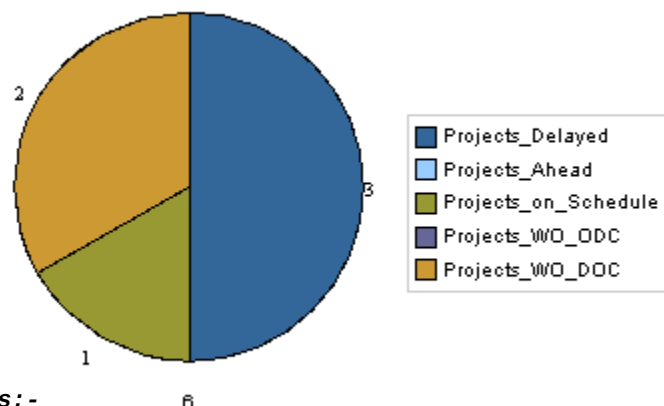


Total No Of Project's:-

#### Investment Scenario

**Total original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 7988.29 crore but this was subsequently anticipated to Rs. 8426.32 crore implying a cost overrun of 5.5%. The expenditure incurred on these projects till December, 2018 is Rs. 2068.91 crore, which is 24.6% of the anticipated cost of the projects.**

Figures are in Rs. Crore

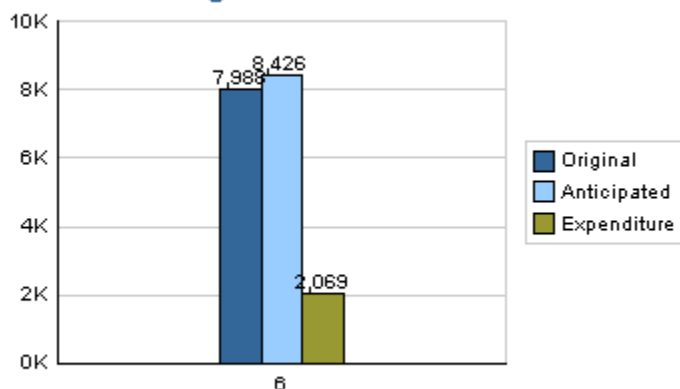

## Sector wise current status of projects on the Flash Report


### TELECOMMUNICATIONS

#### Current Status:

|                                                  |   |
|--------------------------------------------------|---|
| Number of Projects                               | 6 |
| Number of Projects Delayed                       | 4 |
| Number of Projects Without Date Of Commissioning | 2 |

#### Brief Analysis

**Project Status with respect to Original Schedule: Out of 6 projects, 4 projects are delayed. 2 projects do not have fixed dates of commissioning.**

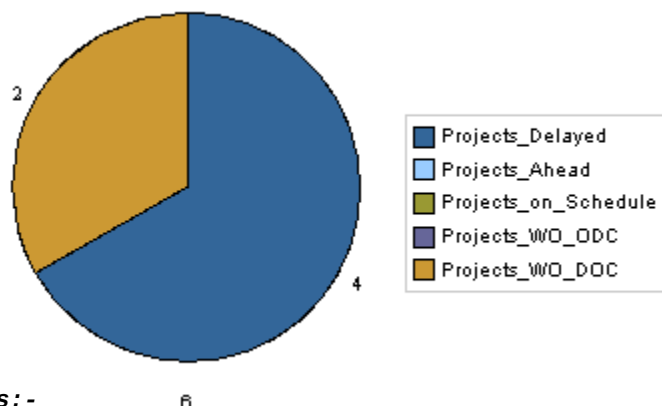


Total No Of Project's:-

6

#### Investment Scenario

**Total original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 16478.21 crore but this was subsequently anticipated to Rs. 27707.01 crore implying a cost overrun of 68.1%. The expenditure incurred on these projects till December, 2018 is Rs. 8966.75 crore, which is 32.4% of the anticipated cost of the projects.**

Figures are in Rs. Crore

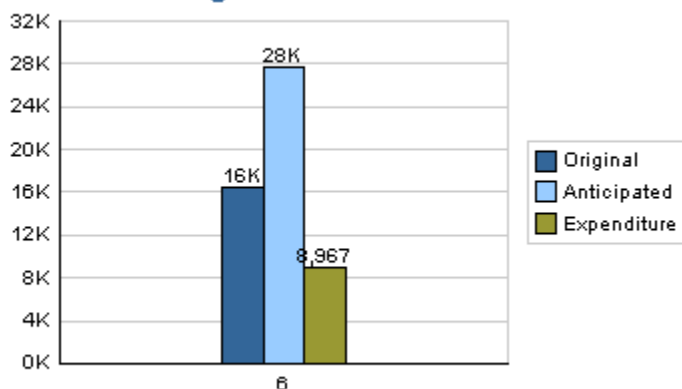



## Sector wise current status of projects on the Flash Report

### URBAN DEVELOPMENT


#### Current Status:

|                                |    |
|--------------------------------|----|
| Number of Projects             | 58 |
| Number of Projects On Schedule | 11 |
| Number of Projects Delayed     | 23 |

Number of Projects Without Date Of Commissioning 24

#### Brief Analysis

**Project Status with respect to Original Schedule:** Out of 58 projects, 11 projects are on schedule 23 projects are delayed. 24 projects do not have fixed dates of commissioning.

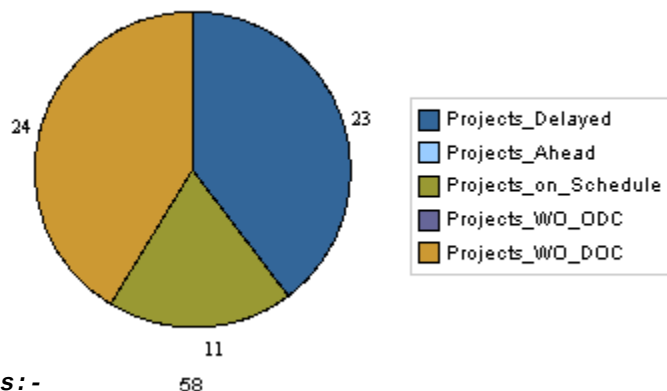


Total No Of Project's:-

#### Investment Scenario

**Total original cost of implementation of 58 projects when sanctioned, was of the order of Rs. 160566.07 crore but this was subsequently anticipated to Rs. 166153.31 crore implying a cost overrun of 3.5%. The expenditure incurred on these projects till December, 2018 is Rs. 73250.95 crore, which is 44.1% of the anticipated cost of the projects.**

Figures are in Rs. Crore

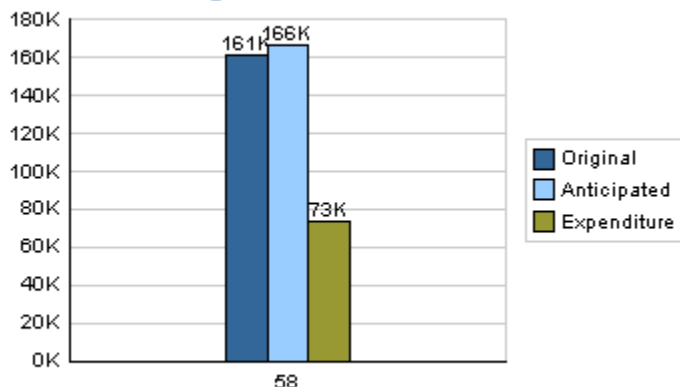

## Sector wise current status of projects on the Flash Report


### DEFENCE PRODUCTION

#### Current Status:

|                                |   |
|--------------------------------|---|
| Number of Projects             | 2 |
| Number of Projects On Schedule | 1 |
| Number of Projects Delayed     | 1 |

#### Brief Analysis

**Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project is delayed.**

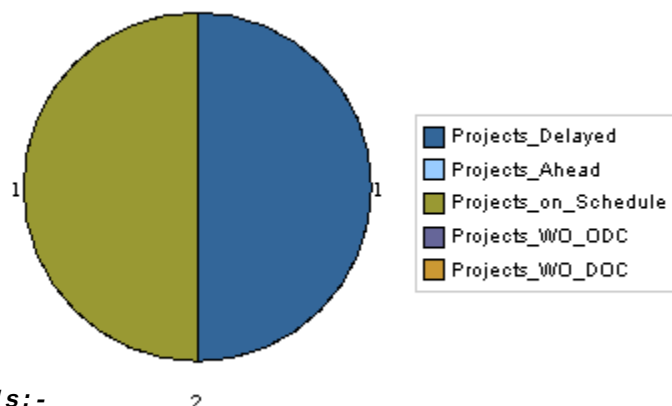


Total No Of Project's:-

#### Investment Scenario

**Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 453.64 crore but this was subsequently anticipated to Rs. 461.66 crore implying a cost overrun of 1.8%. The expenditure incurred on these projects till December, 2018 is Rs. 160.78 crore, which is 34.8% of the anticipated cost of the projects.**

Figures are in Rs. Crore

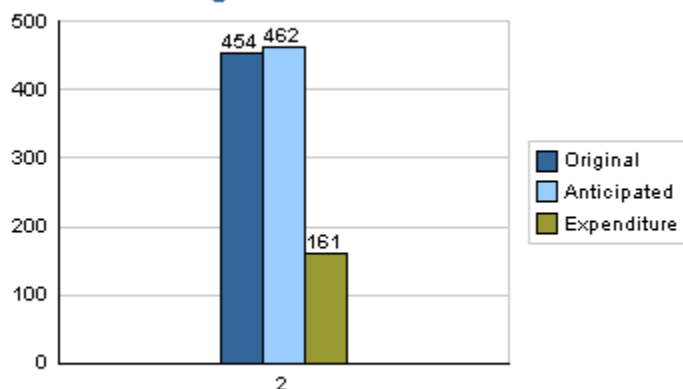

**Annexure - I**

**STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (DECEMBER 2018)**

(All Cost /Expenditure in Rs. crore)

| S.NO         | STATE             | NO OF PROJECTS | COST ORIGINAL       | COST ANTICIPATED    | CUMULATIVE EXPENDITURE |
|--------------|-------------------|----------------|---------------------|---------------------|------------------------|
| 1            | A & N ISLANDS     | 8              | 2,385.01            | 2,492.59            | 156.31                 |
| 2            | ANDHRA PRADESH    | 69             | 1,07,461.29         | 1,11,065.37         | 18,290.61              |
| 3            | ARUNACHAL PRADESH | 31             | 16,421.02           | 33,547.53           | 17,705.53              |
| 4            | ASSAM             | 45             | 27,704.18           | 33,843.2            | 17,232.61              |
| 5            | BIHAR             | 91             | 76,252.26           | 1,11,749.59         | 52,081.46              |
| 6            | CHHATISGARH       | 45             | 78,684.04           | 82,085.57           | 36,635.38              |
| 7            | D & N HAVELI      | 1              | 6,086.08            | 5,842.31            | 4,513.89               |
| 8            | DELHI             | 22             | 55,263.55           | 62,738.78           | 43,355.42              |
| 9            | GOA               | 10             | 4,292.52            | 4,300.54            | 280.71                 |
| 10           | GUJARAT           | 49             | 51,576.03           | 57,377.2            | 29,905.27              |
| 11           | HARYANA           | 29             | 21,083.41           | 22,987.06           | 10,156.74              |
| 12           | HIMACHAL PRADESH  | 13             | 17,058.17           | 26,566.39           | 10,005.89              |
| 13           | JAMMU AND KASHMIR | 10             | 25,238.37           | 51,232.67           | 29,675.16              |
| 14           | JHARKHAND         | 47             | 47,231              | 51,136.74           | 19,993.79              |
| 15           | KARNATAKA         | 46             | 82,156.7            | 87,206.53           | 29,480.11              |
| 16           | KERALA            | 22             | 25,879.48           | 28,054.1            | 6,016.19               |
| 17           | MADHYA PRADESH    | 60             | 67,550.02           | 72,708.48           | 30,869.17              |
| 18           | MAHARASHTRA       | 129            | 1,85,696.8          | 1,97,861.32         | 72,885.03              |
| 19           | MANIPUR           | 2              | 4,670.86            | 14,025.69           | 8,356.86               |
| 20           | MEGHALAYA         | 7              | 4,484.97            | 9,578.51            | 1,390.51               |
| 21           | MIZORAM           | 4              | 3,406.61            | 5,981.14            | 2,646.97               |
| 22           | MULTI STATE       | 163            | 3,45,912.25         | 4,47,775.06         | 1,31,401.37            |
| 23           | NAGALAND          | 21             | 13,711.07           | 14,384.55           | 677.37                 |
| 24           | ODISHA            | 84             | 96,187.7            | 1,01,748.66         | 30,703.42              |
| 25           | PUNJAB            | 33             | 17,042.04           | 17,047.77           | 4,514.7                |
| 26           | RAJASTHAN         | 56             | 46,045.92           | 48,245.1            | 24,810.68              |
| 27           | SIKKIM            | 9              | 3,476.73            | 6,281.03            | 433.9                  |
| 28           | TAMIL NADU        | 76             | 1,19,890.58         | 1,37,033.24         | 62,550.73              |
| 29           | TELANGANA         | 42             | 34,502.53           | 38,040.07           | 10,246.33              |
| 30           | TRIPURA           | 9              | 4,422.36            | 8,345.05            | 6,461.75               |
| 31           | UTTAR PRADESH     | 110            | 1,34,449.08         | 1,35,916.3          | 53,925.79              |
| 32           | UTTARAKHAND       | 28             | 33,689.4            | 39,554.65           | 11,221.07              |
| 33           | WEST BENGAL       | 53             | 57,557.73           | 66,897.02           | 28,417.06              |
| <b>TOTAL</b> |                   | <b>1,424</b>   | <b>18,17,469.76</b> | <b>21,33,649.81</b> | <b>8,06,997.78</b>     |

## LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(DECEMBER 2018)

**ATOMIC ENERGY**

| Sn | Project                                           | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|----|---------------------------------------------------|--------|------------------|--------------------------|-------------------------|-----------------------------|
| 1  | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) | BHAVNI | 09/2003          | 3492                     | -                       | 5687.52                     |

**COAL**

| Sn | Project                                                  | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|----|----------------------------------------------------------|--------|------------------|--------------------------|-------------------------|-----------------------------|
| 2  | NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI | NCL    | 10/2007          | 259.4                    | -                       | 266.38                      |
| 3  | KANIHA OCP, MCL, (10.0 MTY)                              | MCL    | 12/2007          | 457.77                   | -                       | 584.85                      |
| 4  | BALRAM OCP EXTENSION, MCL 8.00 MTY                       | MCL    | 12/2007          | 172.08                   | -                       | 267.19                      |
| 5  | ANANTA OC EXPANSION PH-III (15.0 MTY)                    | MCL    | 08/2008          | 207.28                   | -                       | 235.5                       |
| 6  | JAGANNATHPOR OCP(3.00MTY)                                | SECL   | 09/2008          | 152.43                   | -                       | 178.93                      |
| 7  | RAMAGUNDAM OC-II EXTENSION                               | SCCL   | 12/2009          | 418.97                   | -                       | 477.74                      |
| 8  | AMALGAMATED GONDEGAON GHATROHAN OC                       | WCL    | 02/2016          | 198.68                   | -                       | 254.72                      |

**PETROLEUM**

| Sn | Project                                                             | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|----|---------------------------------------------------------------------|--------|------------------|--------------------------|-------------------------|-----------------------------|
| 9  | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR                        | ISPRL  | 01/2006          | 993                      | -                       | 1549.85                     |
| 10 | FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY | IOCL   | 07/2015          | 822.66                   | -                       | 868.92                      |

**POWER**

| Sn | Project                                                                                              | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|----|------------------------------------------------------------------------------------------------------|--------|------------------|--------------------------|-------------------------|-----------------------------|
| 11 | PARBATI HEP (4X200 MW) (NHPC) II                                                                     | NHPC   | 09/2002          | 3919.59                  | -                       | 7145.69                     |
| 12 | SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)                                                              | NHPC   | 09/2003          | 6285.33                  | -                       | 10421.62                    |
| 13 | KAMENG HYDROELECTRIC PROJECT (NEEPCO)                                                                | NEEPCO | 12/2004          | 2496.9                   | 6179.96                 | 6881.48                     |
| 14 | BARH STPP(3X660MW) NTPC                                                                              | NTPC   | 02/2005          | 8692.97                  | 15095.67                | 15278.98                    |
| 15 | TAPOVAN-VISHNUGAD HEP (4X130MW)                                                                      | NTPC   | 11/2006          | 2978.48                  | -                       | 3775.64                     |
| 16 | TRIPURA GAS BASED POWER PROJECT                                                                      | NEEPCO | 07/2009          | 421.01                   | -                       | 963.23                      |
| 17 | COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L | PGCIL  | 09/2011          | 1940.13                  | -                       | 2529.92                     |
| 18 | KUDGI STPP STAGE 1                                                                                   | NTPC   | 01/2012          | 15166.19                 | -                       | 15364                       |

## LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(DECEMBER 2018)

| Sn              | Project                                                          | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|-----------------|------------------------------------------------------------------|--------|------------------|--------------------------|-------------------------|-----------------------------|
| 19              | BRBCL-NABINAGAR TPP- JV (4X250 MW)                               | NTPC   | 01/2007          | 5353                     | -                       | 7511.72                     |
| 20              | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT | SJVN   | 05/2015          | 436.68                   | -                       | 537.08                      |
| <b>RAILWAYS</b> |                                                                  |        |                  |                          |                         |                             |
| Sn              | Project                                                          | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
| 21              | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)                | NCR    | 04/1986          | 158.77                   | 274.56                  | 629.43                      |
| 22              | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)                           | SCR    | 12/1994          | 124.43                   | -                       | 1021.82                     |
| 23              | AMRAVATI-NARKHER NL(CR)                                          | CR     | 06/1994          | 663.01                   | 668.34                  | 716.8                       |
| 24              | UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR                             | NR     | 03/1995          | 2500                     | -                       | 16834.42                    |
| 25              | CALICUT-MANGALORE (DL) (SR)                                      | SR     | 02/1996          | 240                      | -                       | 537.3                       |
| 26              | MANDARHILL-DUMKA-RAMPURHAT (NL), ER                              | ER     | 04/1995          | 1125.89                  | -                       | 2012.33                     |
| 27              | GONDIA-JABALPUR(GC), (SECR)                                      | SECR   | 02/1997          | 511.86                   | -                       | 967.96                      |
| 28              | NANGALDAM-TALWARA(NL), NR                                        | NR     | 03/1981          | 450                      | -                       | 484.14                      |
| 29              | KARUR-SALEM(NL), SR                                              | SR     | 02/1997          | 155.55                   | -                       | 856.94                      |
| 30              | NANDYAL-YERRAGUNTLA(NL), SCR                                     | SCR    | 03/1996          | 164.36                   | -                       | 999.64                      |
| 31              | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)                           | WCR    | 09/1998          | 247.66                   | -                       | 972.82                      |
| 32              | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR                       | ECR    | 04/1997          | 324.73                   | -                       | 876.49                      |
| 33              | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR                       | NCR    | 04/1999          | 108                      | -                       | 446.52                      |
| 34              | KATIHAR - JOGBANI (GC)(NEFR)                                     | NFR    | 09/2001          | 792.46                   | 724.31                  | 929.63                      |
| 35              | KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)                          | NER    | 04/1999          | 744.71                   | -                       | 751.05                      |
| 36              | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)                            | ECR    | 04/1997          | 162.87                   | -                       | 183.72                      |
| 37              | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR                          | NR     | 03/2002          | 625.3                    | 408.76                  | 841.57                      |
| 38              | QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)                  | SR     | 03/1998          | 280                      | -                       | 834.87                      |
| 39              | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR          | NFR    | 04/2000          | 1180.19                  | 2531.34                 | 3065.47                     |
| 40              | TOLLYGANJ-GARIA WITH EXTENSION TO DUM                            | M RTP  | 03/2000          | 1049.69                  | -                       | 3544.3                      |

## LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(DECEMBER 2018)

| Sn | Project                                                            | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|----|--------------------------------------------------------------------|--------|------------------|--------------------------|-------------------------|-----------------------------|
|    | DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)                          |        |                  |                          |                         |                             |
| 41 | DEOGHAR - SULTANGANJ (INL), ER                                     | ER     | 04/2000          | 607.09                   | -                       | 634.08                      |
| 42 | JIND-SONEPAT (NL),NR                                               | NR     | 01/2004          | 238.56                   | -                       | 722.65                      |
| 43 | HARIDASPUR-PARADEEP(NL)                                            | RVNL   | 04/1996          | 1185.64                  | -                       | 1406.23                     |
| 44 | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)                                | NFR    | 04/2003          | 4454.17                  | -                       | 8304.86                     |
| 45 | KOSI BRIDGE (NL), ECR                                              | ECR    | 04/2002          | 499.41                   | -                       | 640.78                      |
| 46 | RAMGANJMUNDI-BHOPAL (NL),WCR                                       | WCR    | 04/2001          | 424.6                    | -                       | 898.83                      |
| 47 | MAHARAJGANJ-MASRAKH (NL) - NER                                     | NER    | 04/2003          | 218.19                   | -                       | 372.16                      |
| 48 | ETAWAH-MAINPURI (NL),NCR                                           | NCR    | 04/1997          | 120                      | -                       | 210.67                      |
| 49 | HATHUA-BHATNI (N L) (NER)                                          | NER    | 04/2005          | 230.03                   | -                       | 274.67                      |
| 50 | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)                          | RVNL   | 04/2000          | 133.41                   | 207                     | 377.1                       |
| 51 | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR                  | ECR    | 04/1996          | 477.88                   | 283.95                  | 495.4                       |
| 52 | OBULAVARIPALLE-KRISHNAPATNAM(RVNL)                                 | RVNL   | 07/2006          | 732.81                   | -                       | 1981.73                     |
| 53 | SALKA ROAD -ANUPNAGAR LINE DOUBLING                                | RVNL   | 09/2006          | 383.54                   | -                       | 726.22                      |
| 54 | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI    | SR     | 09/2007          | 724.69                   | -                       | 1169.07                     |
| 55 | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE                  | SR     | 09/2006          | 343.17                   | -                       | 1049.68                     |
| 56 | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR    | NFR    | 09/2006          | 385.2                    | -                       | 574.07                      |
| 57 | UTRATIA-ZAFRABAD, NR (LINE DOUBLING)                               | NR     | 04/2006          | 369.9                    | -                       | 618.19                      |
| 58 | BHAIRABI SAIRONG, NL, NEFR                                         | NFR    | 04/2008          | 2393.47                  | 2393.48                 | 2516.15                     |
| 59 | JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)  | NWR    | 04/2008          | 653.19                   | -                       | 820.02                      |
| 60 | BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) | WR     | 04/2006          | 117.36                   | 196.95                  | 202.29                      |
| 61 | BHOJIPUR TANAKPUR VIA PILIBHIT                                     | NER    | 03/2008          | 195.64                   | -                       | 451.8                       |
| 62 | AUNRIHAR MANDUADIH GAZIPUR VARANASI UP                             | NER    | 03/2012          | 199.75                   | -                       | 263.56                      |

## LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(DECEMBER 2018)

| Sn | Project                                                                                           | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|----|---------------------------------------------------------------------------------------------------|--------|------------------|--------------------------|-------------------------|-----------------------------|
| 63 | AJMER-BANGURGRAM                                                                                  | NWR    | 04/2011          | 213.39                   | -                       | 217.81                      |
| 64 | ALWAR-BANDIKUI DOUBLING                                                                           | NWR    | 04/2013          | 242.09                   | -                       | 293.97                      |
| 65 | DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING                                                           | SER    | 04/2010          | 309.44                   | -                       | 507.6                       |
| 66 | CUDDALORE-SALEM VIA VRIDDHACHALAM GC                                                              | SR     | 04/1999          | 198.68                   | -                       | 303.72                      |
| 67 | CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC                                                   | SR     | 04/1998          | 271.24                   | -                       | 468.18                      |
| 68 | KURUPPANTHARA-CHINGAVANAM                                                                         | SR     | 04/2007          | 270.14                   | -                       | 317.14                      |
| 69 | CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA                                                        | NFR    | 04/1999          | 895                      | 984.97                  | 1549.55                     |
| 70 | CHENGANNUR-CHINGAVANAM                                                                            | SR     | 04/2006          | 191.72                   | -                       | 432.5                       |
| 71 | NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI | NFR    | 04/1999          | 819.23                   | -                       | 1082.01                     |
| 72 | AMBARI FALAKATA TO NEW MAYNAGURI                                                                  | NFR    | 04/2011          | 314                      | 486.96                  | 602.54                      |
| 73 | MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD                                             | RVNL   | 04/2012          | 632.68                   | -                       | 846.22                      |
| 74 | BANDEL-BOINCHI 3RD LINE                                                                           | ER     | 04/2011          | 288.35                   | -                       | 291.43                      |
| 75 | PIRPAINTI-BHAGALPUR                                                                               | ER     | 04/2011          | 261.38                   | -                       | 378.9                       |
| 76 | 3RD LINE BETWEEN BHUSAWAL-JALGAON                                                                 | CR     | 04/2011          | 184.06                   | 199.12                  | 240.89                      |
| 77 | HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES      | ER     | 04/2011          | 166.89                   | -                       | 246                         |
| 78 | SAMBALPUR - ANGUL RLY. ELECTRIFICATION                                                            | ECOR   | 03/2012          | 155.81                   | -                       | 180.78                      |
| 79 | RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND                                             | SER    | 04/2012          | 148.77                   | -                       | 155.96                      |
| 80 | MUZAFFARPUR-SITAMARHI NEW LINE                                                                    | ECR    | 01/1991          | 332.15                   | -                       | 538.21                      |
| 81 | LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC                                                       | RVNL   | 04/2011          | 927.01                   | -                       | 983.62                      |
| 82 | DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)               | RVNL   | 03/2009          | 713.48                   | -                       | 1618                        |
| 83 | TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION                                                    | SR     | 02/2000          | 200.84                   | -                       | 394.26                      |
| 84 | THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)                                     | SR     | 02/1996          | 268.87                   | -                       | 304.07                      |
| 85 | VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION                                                    | SR     | 02/2005          | 600                      | 600                     | 671                         |

## LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(DECEMBER 2018)

| Sn                                 | Project                                                                                              | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|------------------------------------|------------------------------------------------------------------------------------------------------|--------|------------------|--------------------------|-------------------------|-----------------------------|
| 86                                 | MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING.                                                        | SR     | 02/2005          | 241                      | -                       | 294.63                      |
| 87                                 | GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW                                        | NER    | 04/1997          | 233                      | -                       | 339.23                      |
| 88                                 | MANDHANA - BRAHMAWART NEW LINE PROJECT.                                                              | NER    | 04/1997          | 609.04                   | 1063                    | 1805.97                     |
| 89                                 | RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR                                              | ECR    | 04/1998          | 180.82                   | -                       | 462.75                      |
| 90                                 | FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, | ECR    | 04/1991          | 329.39                   | -                       | 759.2                       |
| <b>ROAD TRANSPORT AND HIGHWAYS</b> |                                                                                                      |        |                  |                          |                         |                             |
| Sn                                 | Project                                                                                              | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
| 91                                 | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700                                               | NHAI   | 12/2003          | 280                      | -                       | 410.32                      |
| 92                                 | MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000                                                  | NHAI   | 12/2003          | 199.81                   | -                       | 209.8                       |
| 93                                 | MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54                                            | NHAI   | 12/2003          | 167.64                   | -                       | 268.94                      |
| 94                                 | MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450                                                 | NHAI   | 12/2003          | 155.04                   | -                       | 195.35                      |
| 95                                 | NALBARI TO BIJNI (AS-6)                                                                              | NHAI   | 12/2003          | 225                      | -                       | 312.79                      |
| 96                                 | NALBARI T BIJNI (AS-7)                                                                               | NHAI   | 12/2003          | 208                      | -                       | 297.81                      |
| 97                                 | DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)                                                             | NHAI   | 12/2003          | 160                      | -                       | 198.82                      |
| 98                                 | HARANGAJO TO MAIBANG, NH-54                                                                          | NHAI   | 12/2003          | 196                      | -                       | 340.12                      |
| 99                                 | BRAHMPUTRA BRIDGE, NH NO-31                                                                          | NHAI   | 12/2003          | 217.61                   | -                       | 390.19                      |
| 100                                | GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION                                                  | NHAI   | 03/2010          | 1509.1                   | -                       | 3187.21                     |
| 101                                | SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502                                                            | NHAI   | 02/2009          | 1693.75                  | -                       | 2675.28                     |
| 102                                | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)                                                          | NHAI   | 05/2009          | 1108                     | -                       | 3953.66                     |
| 103                                | INDORE-JHABUA-GUJRAT/MP                                                                              | NHAI   | 10/2010          | 1175                     | -                       | 1342.77                     |
| 104                                | CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM                                                       | NHAI   | 11/2010          | 1585                     | -                       | 2167.31                     |
| 105                                | SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM                                          | NHAI   | 02/2010          | 617                      | -                       | 943.17                      |
| 106                                | 4 LANING OF NAGPUR-BETUL                                                                             | NHAI   | 02/2011          | 2498.76                  | -                       | 2525.46                     |
| 107                                | PUNE-SATARA(NH-4)                                                                                    | NHAI   | 10/2010          | 1724.55                  | -                       | 2253.4                      |



## LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(DECEMBER 2018)

| Sn  | Project                                                                  | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|-----|--------------------------------------------------------------------------|--------|------------------|--------------------------|-------------------------|-----------------------------|
| 108 | INDORE-DEWAS(NH-3)                                                       | NHAI   | 11/2010          | 325                      | -                       | 469.54                      |
| 109 | QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00                                 | NHAI   | 07/2010          | 1987                     | -                       | 2403.47                     |
| 110 | NASHRI- CHANANI                                                          | NHAI   | 05/2011          | 2159                     | -                       | 3986.82                     |
| 111 | JAMMU-UDHAMPUR KM.27.5 TO KM.67.00                                       | NHAI   | 07/2010          | 1813.76                  | -                       | 2393.99                     |
| 112 | PATNA-MUZZAFFARPUR                                                       | NHAI   | 08/2010          | 671.3                    | -                       | 884.43                      |
| 113 | ROHTAK-BAWAL                                                             | NHAI   | 05/2011          | 650                      | -                       | 832.39                      |
| 114 | GHAZIABAD-ALIGARH NH-91                                                  | NHAI   | 02/2011          | 1141                     | -                       | 1948.72                     |
| 115 | SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 | NHAI   | 09/2011          | 1250                     | -                       | 1329.17                     |
| 116 | KANDLA - MUNDRA PORT                                                     | NHAI   | 01/2011          | 953.88                   | -                       | 976.28                      |
| 117 | TIRUPATI - TIRUTHANI - CHENNAI                                           | NHAI   | 04/2011          | 571                      | -                       | 582.52                      |
| 118 | JORBAT - BARAPANI                                                        | NHAI   | 01/2011          | 536                      | -                       | 837.81                      |
| 119 | SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547          | NHAI   | 11/2011          | 1535                     | -                       | 2993.77                     |
| 120 | PATNA-BAKTZARPUR KM.181.3 TO KM.231.95                                   | NHAI   | 09/2011          | 574                      | -                       | 768.62                      |
| 121 | 2-LANNING WITH PS MOTIHARI-RAXAUL                                        | NHAI   | 10/2011          | 375.09                   | -                       | 494.33                      |
| 122 | 4-LANNING OF CHAPRA-HAJIPUR                                              | NHAI   | 01/2011          | 575                      | -                       | 831.49                      |
| 123 | 2 LANNING OF MUZAFFARPUR - SONBARSA                                      | NHAI   | 05/2011          | 511.54                   | -                       | 564.35                      |
| 124 | SRINAGAR TO BANIHAL                                                      | NHAI   | 06/2011          | 1100.7                   | -                       | 1288.68                     |
| 125 | PANIKHOLI-RIMOLI                                                         | NHAI   | 03/2012          | 1410                     | -                       | 1555.96                     |
| 126 | MUZZAFFARNAGAR-HARIDWAR                                                  | NHAI   | 09/2011          | 754                      | -                       | 1363.43                     |
| 127 | 4-LANING OF FARAKA-RAIGANJ                                               | NHAI   | 02/2011          | 1078.84                  | -                       | 2312.98                     |
| 128 | 4-LANING OF BRAHAMPUR-FARAKA                                             | NHAI   | 02/2011          | 998.79                   | -                       | 1825.92                     |
| 129 | SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR                            | NHAI   | 12/2011          | 1047                     | -                       | 1613.62                     |

## LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(DECEMBER 2018)

| Sn  | Project                                                                                              | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|-----|------------------------------------------------------------------------------------------------------|--------|------------------|--------------------------|-------------------------|-----------------------------|
| 130 | 6-LANING OF DHANKUNI-KHARAGPUR SECTION                                                               | NHAI   | 04/2012          | 1396.18                  | -                       | 2614.84                     |
| 131 | 2-LANING WITH PS RAIBAREILI TO ALLAHABAD                                                             | NHAI   | 07/2012          | 291.36                   | -                       | 442.51                      |
| 132 | ETAWAH CHAKERI                                                                                       | NHAI   | 03/2013          | 1573                     | -                       | 1998.25                     |
| 133 | AHMEDABAD TO VADODARA SECTION                                                                        | NHAI   | 01/2013          | 2125.24                  | -                       | 4659.71                     |
| 134 | DELHI AGRA APPROVED LENGTH 180.0 KM                                                                  | NHAI   | 10/2012          | 1928.22                  | -                       | 2970.11                     |
| 135 | WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50                                      | NHAI   | 05/2013          | 1348.2                   | -                       | 1792.9                      |
| 136 | FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM)                                   | NHAI   | 11/2013          | 1916.79                  | -                       | 1948.92                     |
| 137 | 4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9                                                | NHAI   | 04/2014          | 1266.6                   | -                       | 1411.79                     |
| 138 | 2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232                                 | NHAI   | 04/2014          | 351.34                   | -                       | 425.99                      |
| 139 | 2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI                                                   | NHAI   | 04/2014          | 495.78                   | -                       | 608.73                      |
| 140 | 2 LANING WITH PS OF GULABPURA - UNIARA                                                               | NHAI   | 10/2015          | 597                      | -                       | 604.8                       |
| 141 | 2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA | NHAI   | 11/2012          | 530.07                   | -                       | 556.02                      |
| 142 | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-II)                                      | NHAI   | 09/2015          | 785.78                   | -                       | 839.63                      |
| 143 | 6 LANING OF AGRA - ETAWAH BYPASS                                                                     | NHAI   | 07/2015          | 1657.2                   | -                       | 1945                        |
| 144 | 4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211                                                        | NHAI   | 01/2015          | 972.5                    | -                       | 1484.99                     |
| 145 | 4-LANING OF GHAGHRA BRIDGE TO VARANSI ( PACKAGE -I)                                                  | NHAI   | 12/2015          | 611.65                   | -                       | 681.34                      |
| 146 | NAGPUR - KONDHALI                                                                                    | NHAI   | 09/2005          | 168                      | -                       | 226.24                      |
| 147 | GURGAON - KOTPUTLI - JAIPUR (SIX LANE)                                                               | NHAI   | 02/2008          | 1673.7                   | -                       | 3326.93                     |
| 148 | FOUR LANING OF GWALIOR-SHIVPURI                                                                      | NHAI   | 05/2013          | 1055                     | -                       | 1393.4                      |
| 149 | FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA  | NHAI   | 06/2015          | 1012.9                   | -                       | 1042.73                     |
| 150 | FOUR LANING OF AURANGABAD - YEDISHI                                                                  | NHAI   | 07/2015          | 1871.34                  | -                       | 2304.41                     |
| 151 | FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS                  | NHAI   | 04/2010          | 1170.52                  | -                       | 2042.41                     |
| 152 | SIX-LANING OF BARWA ADDA-PANAGARH                                                                    | NHAI   | 04/2014          | 1665                     | -                       | 1836.44                     |

## LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(DECEMBER 2018)

| Sn  | Project                                                          | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|-----|------------------------------------------------------------------|--------|------------------|--------------------------|-------------------------|-----------------------------|
| 153 | TRICHY - KARUR                                                   | NHAI   | 03/2007          | 516                      | -                       | 627.42                      |
| 154 | DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM                   | NHAI   | 01/2016          | 701.12                   | -                       | 842.34                      |
| 155 | NAGPUR RING ROAD PACKAGE-2                                       | NHAI   | 03/2016          | 591.66                   | -                       | 608.89                      |
| 156 | 4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 | NHAI   | 11/2012          | 605.84                   | -                       | 722.46                      |

## SHIPPING AND PORTS

| Sn  | Project                                                | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|-----|--------------------------------------------------------|--------|------------------|--------------------------|-------------------------|-----------------------------|
| 157 | CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED | KPL    | 02/2015          | 244.5                    | 258.33                  | 271.56                      |

## URBAN DEVELOPMENT

| Sn  | Project                                                                          | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|-----|----------------------------------------------------------------------------------|--------|------------------|--------------------------|-------------------------|-----------------------------|
| 158 | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V                   | HSCL   | 03/2007          | 149.73                   | 173                     | 178.65                      |
| 159 | CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA                         | HSCL   | 05/2005          | 768.88                   | 1070.97                 | 1085.64                     |
| 160 | CHENNAI METRO RAIL LTD (PHASE 1)                                                 | CMRL   | 02/2009          | 14600                    | -                       | 16352.77                    |
| 161 | CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB | CPWD   | 02/2014          | 388                      | -                       | 395.14                      |

### Details of Projects Ahead of Schedule w.r.t. Original Schedule

| Costing Rs. 150 Crore and above |                                                                                                                    |                               |                                     |                              |                                    | (December 2018)                    |             |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                 |                                                                                                                    |                               |                                     |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                            | Project                                                                                                            | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                               | 2                                                                                                                  | 3                             | 4                                   | 5                            | 6                                  | 7                                  | 8           |
|                                 |                                                                                                                    |                               |                                     |                              |                                    |                                    |             |
|                                 | <u>COAL</u>                                                                                                        |                               |                                     |                              |                                    |                                    |             |
|                                 | <u>South-Eastern Coal Fields Limited</u>                                                                           |                               |                                     |                              |                                    |                                    |             |
| 1                               | BATURA OCP (2.0 MTY)<br>- [N06000049]                                                                              | 8/2015                        | 1,186.64                            | 203.82                       | 103.85                             | 03/2023<br>-                       | 03/2021     |
|                                 | Total                                                                                                              |                               | 1,186.64<br>-                       | 203.82                       | 103.85                             |                                    |             |
|                                 |                                                                                                                    |                               |                                     |                              |                                    |                                    |             |
|                                 | <u>HEALTH AND FAMILY WELFARE</u>                                                                                   |                               |                                     |                              |                                    |                                    |             |
|                                 | <u>Hospital Services Consultancy Corporation Ltd</u>                                                               |                               |                                     |                              |                                    |                                    |             |
| 2                               | NEIGRIHMS SHILLONG MEGHALYA<br>- [N21000013]                                                                       | 10/2016                       | 363.99                              | 363.99                       | 112.29                             | 05/2018<br>09/2019                 | 08/2019     |
|                                 | Total                                                                                                              |                               | 363.99<br>-                         | 363.99                       | 112.29                             |                                    |             |
|                                 |                                                                                                                    |                               |                                     |                              |                                    |                                    |             |
|                                 | <u>PETROLEUM</u>                                                                                                   |                               |                                     |                              |                                    |                                    |             |
|                                 | <u>Gas Authority Of India Limited</u>                                                                              |                               |                                     |                              |                                    |                                    |             |
| 3                               | LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]             | 7/2015                        | 2,881.40<br>-                       | 2,000.00                     | 1,090.43                           | 12/2019<br>12/2020                 | 12/2019     |
|                                 | <u>Hindustan Petroleum Corporation Limited</u>                                                                     |                               |                                     |                              |                                    |                                    |             |
| 4                               | MUMBAI REFINERY EXPANSION PROJECT<br>- [N16000281]                                                                 | 9/2015                        | 4,199.00                            | 4,199.00                     | 194.97                             | 03/2020<br>-                       | 07/2019     |
|                                 | <u>Indian Oil Corporation Limited</u>                                                                              |                               |                                     |                              |                                    |                                    |             |
| 5                               | PARADIP HYDERABAD PIPELINE<br>- [N16000194]                                                                        | 1/2015                        | 2,321.00<br>3,338.00                | 3,338.00                     | 941.59                             | 12/2020<br>-                       | 08/2020     |
| 6                               | RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH<br>- [N16000216]                                             | 1/2016                        | 247.52<br>-                         | 247.52                       | 144.38                             | 02/2019<br>-                       | 01/2019     |
| 7                               | BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL<br>- [N16000252]                                          | 5/2016                        | 664.00<br>-                         | 664.00                       | 455.62                             | 12/2020<br>-                       | 02/2020     |
| 8                               | 30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332] | 3/2018                        | 3,712.00<br>-                       | 3,712.00                     | 6.28                               | 09/2022<br>-                       | 06/2021     |
| 9                               | BRANCH PIPELINE OF PAJPL TO UNA<br>- [N16000250]                                                                   | 2/2016                        | 151.00<br>-                         | 151.00                       | 112.58                             | 09/2019<br>-                       | 02/2019     |
| 10                              | CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP<br>- [N16000226]                                           | 2/2016                        | 356.00<br>-                         | 356.00                       | 205.41                             | 05/2019<br>-                       | 01/2019     |
| 11                              | JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]          | 2/2015                        | 890.00<br>-                         | 887.00                       | 551.16                             | 10/2019<br>-                       | 03/2019     |
|                                 | Total                                                                                                              |                               | 15,421.92<br>-                      | 15,554.52                    | 3,702.42                           |                                    |             |
|                                 |                                                                                                                    |                               |                                     |                              |                                    |                                    |             |
|                                 | <u>POWER</u>                                                                                                       |                               |                                     |                              |                                    |                                    |             |
|                                 | <u>Power Grid Corporation Of India Limited</u>                                                                     |                               |                                     |                              |                                    |                                    |             |

Costing Rs. 150 Crore and above

(December 2018)

|      |                                                                                                                       |                               |                                     |                              |                                    | Date of Commissioning (Month/Year) |             |
|------|-----------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
| S.No | Project                                                                                                               | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1    | 2                                                                                                                     | 3                             | 4                                   | 5                            | 6                                  | 7                                  | 8           |
| 12   | WESTERN REGION STRENGTHENING SCHEME XVII<br>- [N18000246]                                                             | 2/2017                        | 204.12<br>204.12                    | 204.12                       | 102.17                             | 09/2019<br>09/2019                 | 03/2019     |
|      | Total                                                                                                                 |                               | 204.12<br>-                         | 204.12                       | 102.17                             |                                    |             |
|      |                                                                                                                       |                               |                                     |                              |                                    |                                    |             |
|      | <u>RAILWAYS</u>                                                                                                       |                               |                                     |                              |                                    |                                    |             |
|      | <u>East Central Railways</u>                                                                                          |                               |                                     |                              |                                    |                                    |             |
| 13   | GARHWA ROAD-RAMNA<br>- [N22000465]                                                                                    | 3/2015                        | 348.23<br>-                         | 348.23                       | 104.98                             | 03/2021<br>-                       | 12/2020     |
|      | <u>North East Frontier Railway</u>                                                                                    |                               |                                     |                              |                                    |                                    |             |
| 14   | AGARTALA SABROOM, NL, NEFR<br>- [N22000099]                                                                           | 4/2008                        | 1,142.00<br>3,407.00                | 3,407.00                     | 3,112.16                           | 03/2014<br>12/2019                 | 03/2019     |
| 15   | BONGAIGAON-GOALPARA-GUWAHATI (176 KM)<br>- [N22000388]                                                                | 4/2015                        | 2,232.32<br>-                       | 2,182.00                     | 235.52                             | 03/2022<br>-                       | 03/2020     |
| 16   | NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)<br>- [N22000390]                                     | 4/2016                        | 602.27<br>-                         | 612.00                       | 23.69                              | 12/2021<br>-                       | 03/2020     |
|      | <u>North Eastern Railway</u>                                                                                          |                               |                                     |                              |                                    |                                    |             |
| 17   | HATHUA-BHATNI (N L) (NER)<br>- [220100319]                                                                            | 4/2005                        | 230.03<br>-                         | 770.08                       | 274.67                             | 12/2022<br>-                       | 05/2019     |
| 18   | ROSA-SITAPUR CANTT-BURHWAL DOUBLING<br>- [N22000347]                                                                  | 3/2015                        | 1,295.42<br>-                       | 1,295.42                     | 99.33                              | 03/2022<br>-                       | 02/2019     |
|      | <u>North Western Railway</u>                                                                                          |                               |                                     |                              |                                    |                                    |             |
| 19   | BANGURGRAM-GURIYA PATCH DOUBLING<br>- [N22000137]                                                                     | 4/2012                        | 246.08<br>-                         | 348.55                       | 139.09                             | 12/2019<br>-                       | 06/2019     |
| 20   | MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR<br>- [N22000152]                                         | 4/2013                        | 420.18<br>295.02                    | 420.18                       | 89.61                              | 03/2020<br>-                       | 12/2019     |
|      | <u>Rail Vikas Nigam Ltd.</u>                                                                                          |                               |                                     |                              |                                    |                                    |             |
| 21   | DIGHI PORT NEW LINE<br>- [N22000408]                                                                                  | 4/2015                        | 723.78<br>-                         | 723.78                       | .22                                | 12/2025<br>-                       | 03/2025     |
|      | Total                                                                                                                 |                               | 7,240.31<br>-                       | 10,107.24                    | 4,079.27                           |                                    |             |
|      |                                                                                                                       |                               |                                     |                              |                                    |                                    |             |
|      | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                    |                               |                                     |                              |                                    |                                    |             |
|      | <u>Ministry Of Road Transport And Highways</u>                                                                        |                               |                                     |                              |                                    |                                    |             |
| 22   | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S -<br>[N24000821] | 11/2017                       | 257.34<br>-                         | 238.00                       | 41.09                              | 11/2019<br>12/2019                 | 11/2019     |
|      | <u>National Highways Authority Of India</u>                                                                           |                               |                                     |                              |                                    |                                    |             |
| 23   | DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]        | 3/2017                        | 296.19<br>-                         | 254.00                       | 97.80                              | 03/2020<br>-                       | 05/2019     |
| 24   | 4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]     | 3/2017                        | 639.79<br>-                         | 552.90                       | 46.24                              | 03/2020<br>-                       | 06/2019     |
| 25   | 4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]                                        | 3/2017                        | 165.50<br>-                         | 172.16                       | 20.01                              | 03/2020<br>-                       | 06/2019     |
| 26   | 4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]                              | 3/2017                        | 239.68<br>-                         | 235.90                       | 46.25                              | 03/2020<br>-                       | 06/2019     |
| 27   | SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]                                                | 4/2017                        | 894.00                              | 894.00                       | 15.00                              | 04/2020<br>-                       | 11/2019     |

| Costing Rs. 150 Crore and above |             |                               |                                     |                              |                                    | (December 2018)                    |             |
|---------------------------------|-------------|-------------------------------|-------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                 |             |                               |                                     |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                            | Project     | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                               | 2           | 3                             | 4                                   | 5                            | 6                                  | 7                                  | 8           |
|                                 | Total       |                               | 2,492.50                            | 2,346.96                     | 266.39                             |                                    |             |
|                                 |             |                               |                                     |                              |                                    |                                    |             |
|                                 | Grand Total |                               | 26,909.48                           | 28,780.65                    | 8,366.39                           |                                    |             |

## Details of On Schedule Projects w.r.t. Original Schedule

### Annexure - IV

| Costing Rs. 150 Crore and above |                                                                      |                               |                                    |                              |                                    | (December 2018)                    |             |
|---------------------------------|----------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                 |                                                                      |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                            | Project                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                               | 2                                                                    | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
|                                 | <u>COAL</u>                                                          |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>Bharat Coking Coal Limited</u>                                    |                               |                                    |                              |                                    |                                    |             |
| 1                               | NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)<br>- [N06000106]    | 2/2014                        | 555.52<br>-                        | 555.52                       | 5.01                               | 03/2021<br>-                       | 03/2021     |
|                                 | <u>Central Coal Fields Limited</u>                                   |                               |                                    |                              |                                    |                                    |             |
| 2                               | AMRAPALI OC(12MTY)<br>- [N06000103]                                  | 2/2012                        | 858.11<br>-                        | 858.11                       | 184.43                             | 03/2020<br>-                       | 03/2020     |
|                                 | <u>Eastern Coal Fields Limited</u>                                   |                               |                                    |                              |                                    |                                    |             |
| 3                               | JHANJRA COMBINED PR(3.50 MTY)<br>- [N06000020]                       | 11/2015                       | 602.86<br>-                        | 602.86                       | 298.21                             | 03/2022<br>-                       | 03/2022     |
| 4                               | HURA - C OC (3 MTY)<br>- [N06000143]                                 | 10/2015                       | 359.69<br>-                        | 359.69                       | 42.44                              | 03/2022<br>-                       | 03/2022     |
| 5                               | SIDULI MINE (OC AND UG)<br>- [N06000165]                             | 5/2018                        | 535.18<br>-                        | 535.18                       | -                                  | 03/2026<br>-                       | 03/2026     |
|                                 | <u>Mahanadi Coal Fields Limited</u>                                  |                               |                                    |                              |                                    |                                    |             |
| 6                               | GARJANBAHAL OCP<br>- [N06000117]                                     | 11/2014                       | 1,375.38<br>-                      | 1,375.38                     | 424.90                             | 03/2021<br>-                       | 03/2021     |
| 7                               | SIARMAL OCP (40.00MTY)<br>- [N06000113]                              | 5/2014                        | 3,756.36<br>-                      | 3,756.36                     | 689.33                             | 03/2026<br>-                       | 03/2026     |
| 8                               | INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP<br>- [N06000167]            | 5/2018                        | 2,434.75<br>-                      | 2,434.75                     | -                                  | 03/2027<br>-                       | 03/2027     |
|                                 | <u>Neyveli Lignite Corporation</u>                                   |                               |                                    |                              |                                    |                                    |             |
| 9                               | NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW<br>- [N06000152] | 7/2016                        | 17,237.00<br>-                     | 17,237.80                    | 4,026.50                           | 11/2021<br>-                       | 11/2021     |
| 10                              | BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)<br>- [N06000145]            | 3/2015                        | 513.63<br>-                        | 513.63                       | 173.06                             | 12/2019<br>-                       | 12/2019     |
| 11                              | HADLA LIGNITE MINE PROJECT(1.90 MTPA)<br>- [N06000144]               | 3/2015                        | 522.45<br>-                        | 522.45                       | 8.71                               | 09/2019<br>-                       | 09/2019     |
|                                 | <u>Northern Coal Fields Limited</u>                                  |                               |                                    |                              |                                    |                                    |             |
| 12                              | DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)<br>- [N06000162]             | 11/2017                       | 1,255.17<br>-                      | 1,255.17                     | 94.68                              | 03/2022<br>-                       | 03/2022     |
| 13                              | JAYANT EXPANSION OCP 10 TO 20 MTPA<br>- [N06000159]                  | 5/2017                        | 1,783.09<br>-                      | 1,783.09                     | 229.76                             | 03/2021<br>-                       | 03/2021     |
|                                 | <u>Singareni Colliers Company Limited</u>                            |                               |                                    |                              |                                    |                                    |             |
| 14                              | KAKATIYAKHANI OPENCAST III PROJECT PHASE-1<br>- [N06000161]          | 3/2017                        | 413.84<br>-                        | 413.84                       | -                                  | 03/2019<br>-                       | 03/2019     |
| 15                              | KALYANIKHANI 6 INCLINE PROJECT<br>- [N06000147]                      | 12/2015                       | 477.65<br>-                        | 477.65                       | -                                  | 03/2020<br>-                       | 03/2020     |
| 16                              | KAKATIYAKHANI OPENCAST-2 PROJECT<br>- [N06000129]                    | 5/2015                        | 397.09<br>-                        | 442.42                       | 79.96                              | 03/2019<br>-                       | 03/2019     |
|                                 | <u>South-Eastern Coal Fields Limited</u>                             |                               |                                    |                              |                                    |                                    |             |
| 17                              | AMADAND OPENCAST EXPANSION PROJECT<br>- [N06000148]                  | 3/2016                        | 869.44<br>-                        | 869.44                       | 111.89                             | 03/2021<br>-                       | 03/2021     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above |                                                          |                               |                                    |                              |                                    | (December 2018)                    |             |
|---------------------------------|----------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                 |                                                          |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                            | Project                                                  | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                               | 2                                                        | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 18                              | AMGAON OPENCAST PROJECT RCE<br>- [N06000135]             | 7/2015                        | 316.10<br>-                        | 316.10                       | 59.99                              | 03/2020<br>-                       | 03/2020     |
| 19                              | DURGAPUR OPENCAST PROJECT<br>- [N06000136]               | 2/2015                        | 916.24<br>-                        | 916.24                       | 3.81                               | 03/2023<br>-                       | 03/2023     |
| 20                              | JHIRIA WEST OPENCAST PROJECT<br>- [N06000166]            | 11/2018                       | 389.97<br>-                        | 389.97                       | -                                  | 03/2026<br>-                       | 03/2026     |
| 21                              | BATURA HIGHWALL PROJECT<br>- [N06000134]                 | 7/2015                        | 231.92<br>-                        | 231.92                       | -                                  | 03/2022<br>-                       | 03/2022     |
| 22                              | GEVRA EXPANSION OCP (SECL) (35-70) MTY<br>- [060100093]  | 6/2010                        | 11,816.40<br>-                     | 11,816.40                    | 2,848.30                           | 03/2023<br>-                       | 03/2023     |
| 23                              | PELMA OCP(15.00MTY)<br>- [N06000045]                     | 11/2014                       | 1,624.59<br>-                      | 1,624.59                     | 6.13                               | 03/2023<br>-                       | 03/2023     |
| 24                              | BIJARI OC RCE (1.50 MTY)<br>- [N06000111]                | 5/2014                        | 164.49<br>-                        | 164.49                       | 67.20                              | 03/2020<br>-                       | 03/2020     |
| 25                              | CHHAL OC SEAM -III (6.00 MTY)<br>- [N06000104]           | 12/2013                       | 610.63<br>-                        | 610.63                       | 81.27                              | 03/2022<br>-                       | 03/2022     |
| 26                              | MADANNAGAR OPENCAST PROJECT<br>- [N06000140]             | 10/2015                       | 1,875.32<br>-                      | 1,875.32                     | -                                  | 03/2024<br>-                       | 03/2024     |
| 27                              | MAHAMAYA OPENCAST PROJECT<br>- [N06000164]               | 5/2018                        | 410.26<br>-                        | 410.26                       | 9.53                               | 03/2026<br>-                       | 03/2026     |
| 28                              | AMRITDHARA OC PROJECT<br>- [N06000122]                   | 2/2015                        | 481.60<br>-                        | 481.60                       | -                                  | 03/2023<br>-                       | 03/2023     |
| 29                              | KANCHAN OC EXPANSION<br>- [N06000125]                    | 12/2014                       | 371.04<br>-                        | 371.04                       | 41.52                              | 03/2021<br>-                       | 03/2021     |
| 30                              | VIJAY WEST OPENCAST PROJECT<br>- [N06000158]             | 5/2017                        | 976.95<br>-                        | 976.95                       | 75.96                              | 03/2026<br>-                       | 03/2026     |
| 31                              | KUSMUNDA EXPN.OCP(SECL)(15-50)MTY<br>- [N06000008]       | 8/2013                        | 7,612.33<br>-                      | 7,612.33                     | 1,913.96                           | 03/2023<br>-                       | 03/2023     |
| 32                              | MALACHUA OPENCAST PROJECT<br>- [N06000139]               | 10/2015                       | 488.33<br>-                        | 488.33                       | 24.16                              | 03/2023<br>-                       | 03/2023     |
| 33                              | RAJNAGAR OCP RPR (1.70 MTY)<br>- [N06000124]             | 12/2014                       | 357.80<br>-                        | 357.80                       | 113.19                             | 03/2021<br>-                       | 03/2021     |
|                                 | <u>Western Coal Fields Limited</u>                       |                               |                                    |                              |                                    |                                    |             |
| 34                              | BHATADI EXPANSION OC MINE<br>- [N06000150]               | 2/2016                        | 304.52<br>-                        | 304.52                       | 129.39                             | 03/2019<br>-                       | 03/2019     |
| 35                              | AMALGAMATED YEKONA-I YEKONA-II<br>- [N06000132]          | 8/2015                        | 727.28<br>-                        | 727.28                       | 238.43                             | 03/2025<br>-                       | 03/2025     |
| 36                              | DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)<br>- [N06000157]  | 2/2017                        | 328.00<br>-                        | 328.00                       | 90.65                              | 03/2021<br>-                       | 03/2021     |
| 37                              | DINESH OCP<br>- [N06000118]                              | 11/2014                       | 611.16<br>-                        | 611.16                       | 395.73                             | 03/2020<br>-                       | 03/2020     |
| 38                              | KOLAR PIMPRI EXTENSION OC<br>- [N06000160]               | 3/2017                        | 362.73<br>-                        | 362.73                       | 258.23                             | 03/2020<br>-                       | 03/2020     |
| 39                              | NEW MAJRI UG TO OC<br>- [N06000128]                      | 5/2015                        | 295.56<br>-                        | 295.56                       | 88.13                              | 03/2019<br>-                       | 03/2019     |
| 40                              | AMALGAMATED GONDEGAON GHATROHAN OC<br>- [N06000149]      | 2/2016                        | 198.68<br>-                        | 198.68                       | 254.72                             | 03/2019<br>-                       | 03/2019     |
| 41                              | COAL PROJECT NAME JAMUNIA UG (0.84 MTY)<br>- [N06000153] | 7/2016                        | 409.87<br>-                        | 409.87                       | 17.50                              | 03/2022<br>-                       | 03/2022     |



## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above |                                                                                                 |                               |                                    |                              |                                    | (December 2018)                    |             |
|---------------------------------|-------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                 |                                                                                                 |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                            | Project                                                                                         | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                               | 2                                                                                               | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 42                              | BHANEGAON OC<br>- [N06000121]                                                                   | 2/2015                        | 187.94<br>-                        | 409.68                       | 95.83                              | 03/2023<br>02/2017                 | 03/2023     |
| 43                              | AMALGAMATED PAUNI-II III OC MINE<br>- [N06000131]                                               | 6/2015                        | 483.69<br>-                        | 483.69                       | 89.91                              | 03/2021<br>-                       | 03/2021     |
| 44                              | MAKARDHOKRA I OC<br>- [N06000119]                                                               | 9/2014                        | 266.23<br>-                        | 266.23                       | 143.29                             | 03/2021<br>-                       | 03/2021     |
| 45                              | NILJAI EXPANSION (DEEP) OC (3.5 MTY)<br>- [N06000154]                                           | 8/2016                        | 319.76<br>-                        | 319.76                       | 58.04                              | 03/2022<br>-                       | 03/2022     |
| 46                              | MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE<br>- [N06000142]                                      | 11/2015                       | 498.42<br>-                        | 498.42                       | 59.20                              | 03/2020<br>-                       | 03/2020     |
| 47                              | SINGHORI OC MINE<br>- [N06000130]                                                               | 6/2015                        | 205.49<br>-                        | 205.49                       | 105.34                             | 03/2020<br>-                       | 03/2020     |
| 48                              | PENGANGA OCP(REVISED)<br>- [N06000066]                                                          | 9/2014                        | 441.82<br>-                        | 441.82                       | 187.02                             | 03/2020<br>-                       | 03/2020     |
| 49                              | DHANKASA UG (1.00 MTY)<br>- [N06000155]                                                         | 9/2016                        | 458.07<br>-                        | 458.07                       | 16.00                              | 03/2022<br>-                       | 03/2022     |
|                                 | Total                                                                                           |                               | 68,690.40<br>-                     | 68,958.27                    | 13,841.31                          |                                    |             |
|                                 |                                                                                                 |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>DEFENCE PRODUCTION</u>                                                                       |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>Goa Shipyard Limited</u>                                                                     |                               |                                    |                              |                                    |                                    |             |
| 50                              | CONSTRUCTION WORKS PHASE 3B<br>- [N39000002]                                                    | 12/2016                       | 285.95<br>286.00                   | 291.29                       | 56.87                              | 08/2020<br>-                       | 08/2020     |
|                                 | Total                                                                                           |                               | 285.95<br>-                        | 291.29                       | 56.87                              |                                    |             |
|                                 |                                                                                                 |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>FERTILISERS</u>                                                                              |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>National Fertiliser Limited</u>                                                              |                               |                                    |                              |                                    |                                    |             |
| 51                              | GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL<br>- [N08000016]       | 1/2018                        | 239.81<br>-                        | 239.81                       | 32.18                              | 11/2019<br>-                       | 11/2019     |
| 52                              | GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT<br>- [N08000014]      | 1/2018                        | 215.92<br>-                        | 215.92                       | 27.51                              | 11/2019<br>-                       | 11/2019     |
| 53                              | GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA<br>- [N08000015]     | 1/2018                        | 218.83<br>-                        | 218.83                       | 26.47                              | 11/2019<br>-                       | 11/2019     |
|                                 | <u>Rashtriya Chemical &amp; Fertiliser Limited</u>                                              |                               |                                    |                              |                                    |                                    |             |
| 54                              | GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY<br>- [N08000018] | 4/2018                        | 426.72<br>-                        | 426.72                       | 50.89                              | 04/2020<br>-                       | 04/2020     |
|                                 | Total                                                                                           |                               | 1,101.28<br>-                      | 1,101.28                     | 137.05                             |                                    |             |
|                                 |                                                                                                 |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>HEALTH AND FAMILY WELFARE</u>                                                                |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>HII Infra Tech Services Limited</u>                                                          |                               |                                    |                              |                                    |                                    |             |
| 55                              | ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM<br>- [N21000027]                      | 5/2017                        | 875.00<br>-                        | 875.00                       | 174.00                             | 05/2021<br>-                       | 05/2021     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above |                                                                                                                         |                               |                                    |                              |                                    | (December 2018)                    |             |
|---------------------------------|-------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                 |                                                                                                                         |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                            | Project                                                                                                                 | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                               | 2                                                                                                                       | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 56                              | ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB<br>- [N21000026]                                             | 7/2016                        | 703.00<br>-                        | 703.00                       | 272.00                             | 06/2020<br>-                       | 06/2020     |
| 57                              | ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)<br>- [N21000025]                                             | 7/2016                        | 785.00<br>-                        | 785.00                       | 39.35                              | 04/2020<br>-                       | 04/2020     |
|                                 | <u>Hospital Services Consultancy Corporation</u>                                                                        |                               |                                    |                              |                                    |                                    |             |
| 58                              | RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH<br>- [N21000017]                             | 8/2017                        | 272.19<br>-                        | 272.19                       | 104.84                             | 03/2019<br>-                       | 03/2019     |
|                                 | <u>Hospital Services Consultancy Corporation Ltd</u>                                                                    |                               |                                    |                              |                                    |                                    |             |
| 59                              | RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA<br>- [N21000016]                                            | 8/2017                        | 274.19<br>-                        | 274.19                       | 114.89                             | 03/2019<br>-                       | 03/2019     |
| 60                              | RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL<br>- [N21000018]                                          | 8/2017                        | 355.15<br>-                        | 355.15                       | 112.08                             | 03/2019<br>-                       | 03/2019     |
|                                 | Total                                                                                                                   |                               | 3,264.53<br>-                      | 3,264.53                     | 817.16                             |                                    |             |
|                                 |                                                                                                                         |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>HEAVY INDUSTRY</u>                                                                                                   |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>Indira Gandhi Centre For Atomic Research</u>                                                                         |                               |                                    |                              |                                    |                                    |             |
| 61                              | DEVELOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA<br>- [N20000002]             | 8/2016                        | 1,554.00<br>-                      | 1,554.00                     | 161.86                             | 09/2019<br>-                       | 09/2019     |
|                                 | Total                                                                                                                   |                               | 1,554.00<br>-                      | 1,554.00                     | 161.86                             |                                    |             |
|                                 |                                                                                                                         |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>MINES</u>                                                                                                            |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>National Aluminum Company Limited (Nalco)</u>                                                                        |                               |                                    |                              |                                    |                                    |             |
| 62                              | UTKAL D AND E COAL BLOCK<br>- [N10000011]                                                                               | 5/2016                        | 534.00<br>-                        | 534.00                       | 302.60                             | 01/2020<br>01/2020                 | 01/2020     |
| 63                              | 25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU<br>- [N10000014]                                                    | 9/2017                        | 166.62<br>-                        | 166.62                       | 125.00                             | 06/2019<br>06/2019                 | 06/2019     |
| 64                              | CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND 2<br>- [N10000012] | 12/2015                       | 355.00<br>-                        | 355.00                       | 31.92                              | 11/2020<br>-                       | 11/2020     |
| 65                              | SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN<br>- [N10000013]   | 11/2017                       | 483.00<br>-                        | 483.00                       | -                                  | 04/2021<br>04/2021                 | 04/2021     |
| 66                              | 5TH STREAM ALUMINA REFINERY EXPANSION PROJECT<br>- [N10000010]                                                          | 12/2014                       | 5,540.00<br>-                      | 5,540.00                     | 96.98                              | 04/2021<br>04/2021                 | 04/2021     |
|                                 | Total                                                                                                                   |                               | 7,078.62<br>-                      | 7,078.62                     | 556.50                             |                                    |             |
|                                 |                                                                                                                         |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>PETROLEUM</u>                                                                                                        |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>Bharat Petroleum Corporation Limited</u>                                                                             |                               |                                    |                              |                                    |                                    |             |
| 67                              | MMPL PIPELINE REROUTING PROJECT<br>- [N16000261]                                                                        | 4/2013                        | 449.58<br>-                        | 449.58                       | 118.17                             | 12/2019<br>-                       | 12/2019     |
| 68                              | PUNE POL STORAGE DEPOT<br>- [N16000313]                                                                                 | 8/2016                        | 282.64<br>-                        | 282.64                       | 63.91                              | 08/2020<br>-                       | 08/2020     |
| 69                              | KOCHI SALEM LPG PIPELINE PROJECT<br>- [N16000314]                                                                       | 12/2015                       | 1,112.00<br>-                      | 1,112.00                     | 108.79                             | 06/2019<br>-                       | 06/2019     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above |                                                                                                           |                               |                                    |                              |                                    | (December 2018)                    |             |
|---------------------------------|-----------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                 |                                                                                                           |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                            | Project                                                                                                   | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                               | 2                                                                                                         | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 70                              | 2G ETHANOL BIO REFINERY AT BARGARH<br>- [N16000341]                                                       | 8/2017                        | 750.00<br>-                        | 750.00                       | 24.43                              | 12/2020<br>-                       | 12/2020     |
| 71                              | INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY<br>- [N16000260] | 2/2016                        | 554.00<br>-                        | 554.00                       | 158.76                             | 02/2020<br>-                       | 02/2020     |
|                                 | <u>Chennai Petroleum Corporation Limited</u>                                                              |                               |                                    |                              |                                    |                                    |             |
| 72                              | BS-VI PROJECTS<br>- [N16000295]                                                                           | 9/2017                        | 1,858.00<br>-                      | 1,858.00                     | 620.25                             | 12/2019<br>-                       | 12/2019     |
| 73                              | RE-LIQUIFIED NATURAL GAS<br>- [N16000301]                                                                 | 8/2017                        | 421.00<br>-                        | 421.00                       | 19.68                              | 08/2020<br>-                       | 08/2020     |
|                                 | <u>Gas Authority Of India Limited</u>                                                                     |                               |                                    |                              |                                    |                                    |             |
| 74                              | CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI<br>- [N16000329]                                              | 10/2017                       | 226.45<br>-                        | 226.45                       | 25.11                              | 10/2022<br>-                       | 10/2022     |
| 75                              | CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI<br>- [N16000288]                                             | 4/2017                        | 287.49<br>-                        | 287.49                       | 102.07                             | 04/2022<br>-                       | 04/2022     |
| 76                              | CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR<br>- [N16000289]                                         | 7/2017                        | 243.53<br>-                        | 243.53                       | 35.47                              | 07/2022<br>-                       | 07/2022     |
| 77                              | GAIL GAS LTD BENGALURU CGD PROJECT<br>- [N16000210]                                                       | 2/2015                        | 749.00<br>-                        | 749.00                       | 733.62                             | 02/2020<br>-                       | 02/2020     |
| 78                              | CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR<br>- [N16000330]                                          | 10/2017                       | 221.45<br>-                        | 221.45                       | 23.92                              | 10/2022<br>-                       | 10/2022     |
| 79                              | DHAMRA-ANGUL PIPELINE PROJECT<br>- [N16000272]                                                            | 3/2017                        | 1,933.00<br>-                      | 1,933.00                     | 814.01                             | 12/2020<br>-                       | 12/2020     |
| 80                              | CITY GAS DISTRIBUTION (CGD) NETWORK PATNA<br>- [N16000327]                                                | 10/2017                       | 359.25<br>-                        | 359.25                       | 38.05                              | 10/2022<br>-                       | 10/2022     |
| 81                              | DURGAPUR-HALDIA PIPELINE PROJECT<br>- [N16000275]                                                         | 3/2017                        | 1,740.00<br>-                      | 1,740.00                     | 22.96                              | 12/2020<br>-                       | 12/2020     |
| 82                              | BOKARO-ANGUL PIPELINE PROJECT<br>- [N16000274]                                                            | 3/2017                        | 3,437.00<br>-                      | 3,437.00                     | 1,006.30                           | 12/2020<br>-                       | 12/2020     |
| 83                              | CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK<br>- [N16000328]                                             | 7/2017                        | 181.20<br>-                        | 181.20                       | 15.72                              | 07/2022<br>-                       | 07/2022     |
| 84                              | BARAUNI-GUWAHATI PIPELINE<br>- [N16000334]                                                                | 6/2018                        | 3,308.00<br>-                      | 3,308.00                     | 2.63                               | 12/2021<br>-                       | 12/2021     |
| 85                              | DOBHI-DURGAPUR PIPELINE PROJECT<br>- [N16000273]                                                          | 3/2017                        | 2,433.00<br>-                      | 2,433.00                     | 956.29                             | 12/2020<br>-                       | 12/2020     |
| 86                              | LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT<br>- [N16000271] | 7/2015                        | 2,881.40<br>-                      | 2,000.00                     | 1,090.43                           | 12/2019<br>12/2020                 | 12/2019     |
|                                 | <u>Hindustan Petroleum Corporation Limited</u>                                                            |                               |                                    |                              |                                    |                                    |             |
| 87                              | RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA)<br>- [N16000242]              | 11/2016                       | 230.00<br>-                        | 230.00                       | 114.14                             | 02/2019<br>-                       | 02/2019     |
| 88                              | CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA<br>- [N16000312]             | 11/2017                       | 255.00<br>-                        | 255.00                       | 15.68                              | 11/2020<br>-                       | 11/2020     |
| 89                              | 120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE<br>- [N16000316]                                          | 6/2017                        | 161.50<br>-                        | 161.50                       | 17.78                              | 06/2020<br>-                       | 06/2020     |
| 90                              | VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT<br>- [N16000237]                      | 9/2016                        | 407.00<br>-                        | 407.00                       | 262.64                             | 09/2019<br>-                       | 09/2019     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above |                                                                                                                         |                               |                                    |                              |                                    | (December 2018)                    |             |
|---------------------------------|-------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                 |                                                                                                                         |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                            | Project                                                                                                                 | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                               | 2                                                                                                                       | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 91                              | MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION<br>- [N16000238]                                       | 9/2016                        | 1,879.00<br>-                      | 1,879.00                     | 1,015.35                           | 06/2020<br>-                       | 06/2020     |
| 92                              | EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]      | 9/2017                        | 2,677.00<br>-                      | 2,677.00                     | 49.88                              | 03/2021<br>-                       | 03/2021     |
| 93                              | 180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA<br>- [N16000315]                                         | 6/2017                        | 249.26<br>-                        | 249.26                       | 58.33                              | 06/2020<br>-                       | 06/2020     |
| 94                              | VISAKH REFINERY MODERNISATION PROJECT<br>- [N16000235]                                                                  | 7/2016                        | 20,928.00<br>-                     | 20,928.00                    | 2,757.64                           | 07/2020<br>-                       | 07/2020     |
| 95                              | CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]       | 12/2016                       | 300.00<br>-                        | 300.00                       | -                                  | 04/2021<br>-                       | 04/2021     |
|                                 | <u>Indian Oil Corporation Limited</u>                                                                                   |                               |                                    |                              |                                    |                                    |             |
| 96                              | BS-VI PROJECT AT PANIPAT REFINERY<br>- [N16000325]                                                                      | 12/2017                       | 3,529.00<br>-                      | 3,529.00                     | 952.69                             | 07/2019<br>-                       | 07/2019     |
| 97                              | AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]      | 3/2018                        | 676.00<br>-                        | 676.00                       | 4.83                               | 12/2021<br>-                       | 12/2021     |
| 98                              | CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE<br>- [N16000326]           | 10/2017                       | 906.00<br>-                        | 906.00                       | 13.52                              | 02/2020<br>-                       | 02/2020     |
| 99                              | HALDIA BARAUNI PRODUCT PIPELINE<br>- [N16000251]                                                                        | 4/2016                        | 1,021.00<br>-                      | 1,021.00                     | 4.45                               | 12/2020<br>-                       | 12/2020     |
| 100                             | INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY<br>- [N16000337]                                                      | 7/2018                        | 189.00<br>-                        | 189.00                       | 4.04                               | 01/2021<br>-                       | 01/2021     |
| 101                             | CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR<br>- [N16000344]                                             | 4/2018                        | 522.00<br>-                        | 522.00                       | 2.56                               | 03/2021<br>-                       | 03/2021     |
| 102                             | INDMAX PROJECT AT BONGAIGAON REFINERY<br>- [N16000243]                                                                  | 2/2016                        | 2,582.00<br>-                      | 2,582.00                     | 1,281.75                           | 11/2019<br>-                       | 11/2019     |
| 103                             | DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY<br>- [N16000324]              | 12/2017                       | 199.36<br>-                        | 199.36                       | -                                  | 10/2020<br>-                       | 10/2020     |
| 104                             | REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM<br>- [N16000270]                                                      | 7/2014                        | 247.00<br>-                        | 247.00                       | -                                  | 03/2021<br>-                       | 03/2021     |
| 105                             | ENNORE-TRICHY-MADURAI LPG PIPELINE<br>- [N16000162]                                                                     | 5/2013                        | 711.00<br>-                        | 711.00                       | 11.12                              | 06/2020<br>-                       | 06/2020     |
| 106                             | REVAMPING OF FACILITIES AT VIZAG TERMINAL<br>- [N16000343]                                                              | 4/2018                        | 355.00<br>-                        | 355.00                       | -                                  | 04/2022<br>-                       | 04/2022     |
| 107                             | BS-VI PROJECT AT BONGAIGAON REFINERY<br>- [N16000320]                                                                   | 5/2018                        | 1,222.00<br>-                      | 1,222.00                     | 287.90                             | 09/2019<br>-                       | 09/2019     |
| 108                             | ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE<br>- [N16000276] | 5/2016                        | 261.00<br>-                        | 261.00                       | 8.48                               | 01/2021<br>-                       | 01/2021     |
| 109                             | CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP<br>- [N16000302]                                                         | 8/2017                        | 384.58<br>-                        | 384.58                       | 41.38                              | 04/2021<br>-                       | 04/2021     |
| 110                             | CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY<br>- [N16000309]                  | 8/2017                        | 1,342.00<br>-                      | 1,342.00                     | 3.90                               | 08/2020<br>-                       | 08/2020     |
| 111                             | BS-VI PROJECT AT MATHURA REFINERY<br>- [N16000306]                                                                      | 1/2018                        | 666.64<br>-                        | 666.64                       | 223.54                             | 09/2019<br>-                       | 09/2019     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above |                                                                                                                 |                               |                                    |                              |                                    | (December 2018)                    |             |
|---------------------------------|-----------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                 |                                                                                                                 |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                            | Project                                                                                                         | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                               | 2                                                                                                               | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 112                             | INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]  | 8/2017                        | 255.40 -                           | 255.40                       | 0.06                               | 08/2020 -                          | 08/2020     |
| 113                             | INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]                                | 5/2016                        | 429.00 -                           | 429.00                       | 291.90                             | 01/2019 -                          | 01/2019     |
| 114                             | KHARAGPUR LPG BOTTLING PLANT - [N16000300]                                                                      | 4/2017                        | 163.02 -                           | 163.02                       | 32.69                              | 04/2020 -                          | 04/2020     |
| 115                             | BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]                                                                 | 3/2018                        | 3,380.00 -                         | 3,380.00                     | 1,246.09                           | 09/2019 -                          | 09/2019     |
| 116                             | DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]  | 6/2016                        | 423.00 -                           | 423.00                       | 217.07                             | 08/2019 -                          | 08/2019     |
| 117                             | LPG BP PROJECT MOTIHARI - [N16000317]                                                                           | 5/2018                        | 206.50 -                           | 206.50                       | -                                  | 03/2021 -                          | 03/2021     |
| 118                             | NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]                                                      | 8/2018                        | 1,636.00 -                         | 1,636.00                     | 128.78                             | 08/2020 -                          | 08/2020     |
| 119                             | CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]                             | 4/2018                        | 206.63 -                           | 206.63                       | 0.52                               | 02/2020 -                          | 02/2020     |
| 120                             | PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]                                                                | 10/2018                       | 1,297.50 -                         | 1,297.50                     | -                                  | 10/2021 -                          | 10/2021     |
| 121                             | BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]                                                                | 8/2018                        | 557.00 -                           | 557.00                       | 71.41                              | 02/2020 -                          | 02/2020     |
| 122                             | CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]                                        | 8/2017                        | 315.00 -                           | 315.00                       | 2.87                               | 12/2021 -                          | 12/2021     |
| 123                             | BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]                                                        | 5/2018                        | 2,934.40 -                         | 2,934.40                     | 843.32                             | 09/2019 -                          | 09/2019     |
| 124                             | SITARGANJ LPG PROJECT - [N16000282]                                                                             | 2/2017                        | 160.10 -                           | 160.10                       | 27.35                              | 02/2020 -                          | 02/2020     |
| 125                             | LPG BP PROJECT KHORDHA - [N16000283]                                                                            | 12/2016                       | 161.59 -                           | 161.59                       | 33.93                              | 12/2019 -                          | 12/2019     |
| 126                             | INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]           | 9/2016                        | 208.35 -                           | 208.35                       | 67.71                              | 07/2020 -                          | 07/2020     |
| 127                             | AUGMENTATION OF CTMPL - [N16000286]                                                                             | 12/2016                       | 228.00 -                           | 228.00                       | 1.84                               | 06/2020 -                          | 06/2020     |
| 128                             | ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]           | 1/2015                        | 342.00 -                           | 342.00                       | -                                  | 03/2021 -                          | 03/2021     |
| 129                             | MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]                                                                      | 9/2015                        | 324.00 -                           | 324.00                       | 96.21                              | 06/2020 -                          | 06/2020     |
| 130                             | AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193] | 1/2015                        | 1,823.00 -                         | 1,823.00                     | 579.41                             | 12/2020 -                          | 12/2020     |
| 131                             | KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]                                                                | 5/2016                        | 1,945.00 -                         | 1,945.00                     | 514.20                             | 08/2021 -                          | 08/2021     |
| 132                             | ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]                                                                | 4/2018                        | 4,807.08 -                         | 4,807.08                     | 24.09                              | 07/2021 -                          | 07/2021     |
|                                 | <u>Mangalore Refinery And Petrochemicals Limited</u>                                                            |                               |                                    |                              |                                    |                                    |             |
| 133                             | RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]                                                  | 10/2015                       | 135.00 171.00                      | 170.70                       | 124.25                             | 03/2019 -                          | 03/2019     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above |                                                                                                                    |                               |                                    |                              |                                    | (December 2018)                    |             |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                 |                                                                                                                    |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                            | Project                                                                                                            | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                               | 2                                                                                                                  | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 134                             | CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU<br>- [N16000255]                                | 5/2015                        | 224.00<br>207.00                   | 207.25                       | 99.99                              | 04/2019<br>-                       | 04/2019     |
| 135                             | SEA WATER DESALINATION PLANT<br>- [N16000319]                                                                      | 11/2017                       | 581.00<br>-                        | 581.00                       | -                                  | 03/2020<br>-                       | 03/2020     |
| 136                             | BSVI UPGADATION<br>- [N16000257]                                                                                   | 9/2016                        | 1,810.00<br>1,810.00               | 1,810.00                     | 130.79                             | 12/2019<br>-                       | 12/2019     |
|                                 | <u>Oil &amp; Natural Gas Corporation Limited</u>                                                                   |                               |                                    |                              |                                    |                                    |             |
| 137                             | GAMJI REDEVELOPMENT PROJECT<br>- [N16000202]                                                                       | 5/2015                        | 1,671.22<br>-                      | 567.22                       | 449.95                             | 11/2019<br>-                       | 11/2019     |
| 138                             | PIPELINE NETWORK PROJECT GELEKI, ASSAM<br>- [N16000278]                                                            | 7/2016                        | 249.85<br>250.00                   | 244.70                       | 101.71                             | 05/2020<br>05/2020                 | 05/2020     |
| 139                             | PIPELINE REPLACEMENT PROJECT-V (OFFSHORE)<br>- [N16000335]                                                         | 4/2018                        | 766.37<br>-                        | 766.37                       | -                                  | 12/2019<br>-                       | 12/2019     |
| 140                             | DEVELOPMENT OF B-147 FIELD<br>- [N16000292]                                                                        | 2/2017                        | 546.15<br>-                        | 546.15                       | 226.78                             | 11/2019<br>11/2019                 | 11/2019     |
| 141                             | DEVELOPMENT OF BSE-11 BLOCK<br>- [N16000293]                                                                       | 2/2017                        | 511.30<br>-                        | 511.30                       | 197.90                             | 11/2019<br>11/2019                 | 11/2019     |
| 142                             | 4TH PHASE DEVELOPMENT OF NBP FIELD<br>- [N16000294]                                                                | 2/2017                        | 968.61<br>-                        | 968.61                       | 601.19                             | 11/2019<br>11/2019                 | 11/2019     |
| 143                             | NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY<br>- [N16000290]                                          | 1/2017                        | 474.15<br>-                        | 474.15                       | 299.26                             | 05/2019<br>05/2019                 | 05/2019     |
| 144                             | DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)<br>- [N16000297]                                  | 2/2017                        | 4,006.83<br>-                      | 4,006.83                     | 1,651.58                           | 05/2021<br>05/2021                 | 05/2021     |
| 145                             | REDEVELOPMENT OF SANTHAL FIELD<br>- [N16000279]                                                                    | 2/2017                        | 1,162.56<br>-                      | 1,162.56                     | 294.16                             | 03/2026<br>03/2026                 | 03/2026     |
|                                 | <u>Oil India Limited</u>                                                                                           |                               |                                    |                              |                                    |                                    |             |
| 146                             | AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II<br>- [N16000259]                            | 9/2016                        | 571.66<br>-                        | 571.66                       | 42.33                              | 12/2019<br>-                       | 12/2019     |
| 147                             | DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331] | 1/2018                        | 543.91<br>-                        | 543.91                       | 1.65                               | 02/2020<br>-                       | 02/2020     |
| 148                             | PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)<br>- [N16000258]                                               | 5/2016                        | 406.00<br>-                        | 406.00                       | 23.61                              | 10/2020<br>-                       | 10/2020     |
|                                 | Total                                                                                                              |                               | 1,01,759.51<br>-                   | 99,787.91                    | 21,536.77                          |                                    |             |
|                                 |                                                                                                                    |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>POWER</u>                                                                                                       |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>National Thermal Power Corporation</u>                                                                          |                               |                                    |                              |                                    |                                    |             |
| 149                             | TALAIPALLI COAL MINING PROJECT<br>- [N18000266]                                                                    | 9/2015                        | 3,004.00<br>-                      | 3,004.00                     | 1,293.72                           | 11/2019<br>-                       | 11/2019     |
| 150                             | KHARGONE STPP STAGE I (1320 MW)<br>- [N18000205]                                                                   | 3/2015                        | 9,870.51<br>-                      | 11,148.86                    | 6,693.90                           | 09/2019<br>-                       | 09/2019     |
|                                 | <u>Power Grid Corporation Of India Limited</u>                                                                     |                               |                                    |                              |                                    |                                    |             |
| 151                             | WESTERN REGION STRENGTHENING SCHEME XVIII<br>- [N18000241]                                                         | 2/2017                        | 195.05<br>-                        | 195.05                       | 92.00                              | 02/2020<br>02/2020                 | 02/2020     |
| 152                             | ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS<br>- [N18000222]                                              | 4/2016                        | 790.13<br>-                        | 790.30                       | 524.14                             | 06/2019<br>06/2019                 | 06/2019     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above |                                                                                                                     |                               |                                    |                              |                                    | (December 2018)                    |             |
|---------------------------------|---------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                 |                                                                                                                     |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                            | Project                                                                                                             | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                               | 2                                                                                                                   | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 153                             | SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]                                                | 3/2017                        | 337.75 -                           | 337.75                       | 26.00                              | 06/2019<br>06/2019                 | 06/2019     |
| 154                             | SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]                             | 12/2017                       | 193.14 -                           | 193.14                       | 4.00                               | 06/2019<br>06/2019                 | 06/2019     |
| 155                             | S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]  | 3/2017                        | 283.72 -                           | 283.72                       | 109.75                             | 11/2019<br>11/2019                 | 11/2019     |
| 156                             | GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]                                       | 5/2016                        | 3,519.59 -                         | 3,519.59                     | 2,073.40                           | 05/2019<br>05/2019                 | 05/2019     |
| 157                             | PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]  | 3/2017                        | 162.31 -                           | 162.31                       | 86.70                              | 03/2019<br>03/2019                 | 03/2019     |
| 158                             | SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]                 | 10/2016                       | 608.24 -                           | 608.24                       | 376.20                             | 04/2019<br>04/2019                 | 04/2019     |
| 159                             | SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]                                                    | 3/2017                        | 379.95 -                           | 379.95                       | 22.22                              | 12/2019<br>12/2019                 | 12/2019     |
| 160                             | ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]  | 2/2017                        | 322.30 -                           | 322.30                       | 119.48                             | 02/2019<br>02/2019                 | 02/2019     |
| 161                             | HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]  | 8/2017                        | 1,931.39 -                         | 1,931.39                     | 592.69                             | 02/2020<br>02/2020                 | 02/2020     |
| 162                             | TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262] | 5/2017                        | 186.17 -                           | 186.17                       | 63.07                              | 07/2019<br>07/2019                 | 07/2019     |
| 163                             | STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]                                                  | 12/2015                       | 3,654.00 -                         | 3,654.00                     | 2,873.42                           | 04/2019<br>-                       | 04/2019     |
| 164                             | EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]                                                             | 3/2017                        | 3,500.00<br>3,500.00               | 3,500.00                     | 690.00                             | 07/2020<br>-                       | 07/2020     |
| 165                             | PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]                                      | 8/2016                        | 431.89 -                           | 431.89                       | 213.66                             | 02/2019<br>02/2019                 | 02/2019     |
| 166                             | INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]            | 3/2017                        | 251.60 -                           | 251.60                       | 112.11                             | 06/2019<br>06/2019                 | 06/2019     |
| 167                             | EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]                                                                | 11/2017                       | 358.83 -                           | 358.83                       | -                                  | 05/2020<br>05/2020                 | 05/2020     |
| 168                             | SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]                                                              | 9/2016                        | 562.25 -                           | 562.25                       | 103.00                             | 03/2019<br>03/2019                 | 03/2019     |
| 169                             | EASTERN REGION STRENGTHENING SCHEME XVII( PART B) - [N18000244]                                                     | 2/2017                        | 235.53 -                           | 235.53                       | 42.49                              | 06/2019<br>06/2019                 | 06/2019     |
| 170                             | HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]  | 2/2017                        | 5,070.13 -                         | 5,070.13                     | 1,044.71                           | 04/2020<br>04/2020                 | 04/2020     |
| 171                             | PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]         | 4/2016                        | 844.64 -                           | 844.64                       | 303.70                             | 04/2019<br>-                       | 04/2019     |
| 172                             | HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]  | 5/2016                        | 14,733.37 -                        | 14,733.37                    | 5,084.05                           | 11/2019<br>11/2019                 | 11/2019     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above |                                                                                                                                                             |                               |                                    |                              |                                    | (December 2018)                    |             |
|---------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                 |                                                                                                                                                             |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                            | Project                                                                                                                                                     | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                               | 2                                                                                                                                                           | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 173                             | POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230<br><u>Satluj Jal Vidyut Nigam Limited</u> | 7/2016                        | 333.17<br>-                        | 333.17                       | 257.53                             | 03/2019<br>03/2019                 | 03/2019     |
| 174                             | NAITWAR MORI HEP - [N18000265<br><u>Thdc India Limited</u>                                                                                                  | 10/2017                       | 648.33<br>-                        | 648.33                       | 148.40                             | 12/2021<br>-                       | 12/2021     |
| 175                             | AMELIA COAL MINE - [N18000252                                                                                                                               | 1/2017                        | 2,104.21<br>-                      | 2,104.21                     | 66.05                              | 09/2020<br>-                       | 09/2020     |
|                                 | Total                                                                                                                                                       |                               | 54,512.20<br>-                     | 55,790.72                    | 23,016.39                          |                                    |             |
|                                 |                                                                                                                                                             |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>RAILWAYS</u>                                                                                                                                             |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>Central Railways</u>                                                                                                                                     |                               |                                    |                              |                                    |                                    |             |
| 176                             | KALYAN-KASARA 3RD LINE - [N22000233                                                                                                                         | 4/2011                        | 792.89<br>-                        | 792.89                       | 275.17                             | 03/2021<br>-                       | 03/2021     |
| 177                             | WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250                                                                                                                   | 4/2012                        | 540.02<br>-                        | 540.02                       | 168.97                             | 03/2022<br>-                       | 03/2022     |
| 178                             | PUNE-NASIK (265 KM) - [N22000354                                                                                                                            | 2/2016                        | 2,425.00<br>-                      | 5,341.68                     | -                                  | 03/2024<br>-                       | 03/2024     |
| 179                             | DAUND - MANMAD (236 KM) - [N22000360                                                                                                                        | 2/2016                        | 1,876.00<br>-                      | 2,081.27                     | 1.27                               | 03/2023<br>-                       | 03/2023     |
| 180                             | WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356                                                                                                          | 2/2015                        | 1,272.19<br>-                      | 1,272.19                     | 162.38                             | 03/2022<br>-                       | 03/2022     |
| 181                             | WARDHA-NANDED MAHARASHTRA - [N22000231                                                                                                                      | 4/2008                        | 3,168.29<br>-                      | 3,168.29                     | 992.77                             | 03/2023<br>-                       | 03/2023     |
| 182                             | INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353                                                                                                          | 2/2016                        | 9,968.00<br>-                      | 8,857.98                     | -                                  | 03/2024<br>-                       | 03/2024     |
| 183                             | VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355                                                                                                                | 2/2016                        | 2,750.00<br>-                      | 3,438.51                     | -                                  | 03/2024<br>-                       | 03/2024     |
| 184                             | AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181                                                                                                                | 2/1997                        | 2,271.50<br>-                      | 3,712.50                     | 1,909.57                           | 03/2021<br>-                       | 03/2021     |
| 185                             | PUNE-MIRAJ-LONDA (467 KM) - [N22000359                                                                                                                      | 2/2015                        | 3,627.47<br>3,627.00               | 3,627.47                     | 332.55                             | 03/2024<br>-                       | 03/2024     |
| 186                             | WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362                                                                                                             | 2/2016                        | 637.95<br>-                        | 637.95                       | 28.96                              | 03/2023<br>-                       | 03/2023     |
| 187                             | ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358                                                                                                       | 2/2015                        | 2,449.91<br>-                      | 2,449.91                     | 89.27                              | 03/2023<br>-                       | 03/2023     |
| 188                             | 3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247                                                                                                              | 4/2011                        | 184.06<br>-                        | 298.70                       | 240.89                             | 03/2019<br>-                       | 03/2019     |
|                                 | <u>Container Corporation Of India</u>                                                                                                                       |                               |                                    |                              |                                    |                                    |             |
| 189                             | MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426                                                                                                            | 12/2015                       | 346.32<br>-                        | 300.00                       | 272.72                             | 03/2019<br>-                       | 03/2019     |
| 190                             | MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422                                                                                                       | 10/2013                       | 305.00<br>-                        | 305.00                       | 253.22                             | 03/2019<br>-                       | 03/2019     |
|                                 | <u>Dedicated Freight Corridor Corporation Of India Ltd</u>                                                                                                  |                               |                                    |                              |                                    |                                    |             |
| 191                             | WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464                                                                                                             | 11/2007                       | 16,592.00<br>51,101.00             | 51,101.00                    | 22,485.00                          | 03/2020<br>-                       | 03/2020     |



## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above |                                                                                                  |                               |                                    |                              |                                    | (December 2018)                    |             |
|---------------------------------|--------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                 |                                                                                                  |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                            | Project                                                                                          | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                               | 2                                                                                                | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
|                                 | <u>East Central Railways</u>                                                                     |                               |                                    |                              |                                    |                                    |             |
| 192                             | KOSI BRIDGE (NL), ECR<br>- [220100304]                                                           | 4/2002                        | 499.41<br>-                        | 516.02                       | 640.78                             | 03/2020<br>-                       | 03/2020     |
| 193                             | JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC<br>- [N22000181]             | 4/2009                        | 548.00<br>-                        | 785.87                       | 40.00                              | 03/2020<br>-                       | 03/2020     |
|                                 | <u>East Coast Railway</u>                                                                        |                               |                                    |                              |                                    |                                    |             |
| 194                             | EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL<br>[N22000418] | 4/2016                        | 5,200.00<br>-                      | 5,200.00                     | -                                  | 03/2020<br>-                       | 03/2020     |
| 195                             | KOTTAVALSA - KORAPUT DOUBLING<br>- [N22000377]                                                   | 4/2015                        | 2,499.71<br>-                      | 2,499.71                     | 183.68                             | 03/2022<br>-                       | 03/2022     |
| 196                             | KIRANDUL - JAGDALPUR DOUBLING<br>- [N22000318]                                                   | 12/2012                       | 1,160.00<br>-                      | 1,160.83                     | 571.51                             | 03/2020<br>-                       | 03/2020     |
| 197                             | KORAPUT - SINGAPUR ROAD DOUBLING<br>- [N22000379]                                                | 4/2015                        | 2,361.74<br>-                      | 2,361.74                     | 81.06                              | 03/2022<br>-                       | 03/2022     |
| 198                             | SAMBALPUR - ANGUL RLY. ELECTRIFICATION<br>- [N22000319]                                          | 3/2012                        | 155.81<br>-                        | 238.03                       | 180.78                             | 03/2020<br>-                       | 03/2020     |
| 199                             | JAGDALPUR-KORAPUT DOUBLING<br>- [N22000376]                                                      | 4/2015                        | 1,547.38<br>-                      | 1,547.38                     | 189.40                             | 03/2022<br>-                       | 03/2022     |
|                                 | <u>Eastern Railways</u>                                                                          |                               |                                    |                              |                                    |                                    |             |
| 200                             | TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER<br>- [220100272]                                     | 4/2000                        | 1,188.91<br>-                      | 1,620.01                     | 844.12                             | 03/2019<br>12/2009                 | 03/2019     |
| 201                             | PIRPAINTI-JASIDIH<br>- [N22000219]                                                               | 4/2013                        | 915.98<br>-                        | 915.96                       | 319.53                             | 03/2022<br>-                       | 03/2022     |
| 202                             | HANSDIHA-GODDA NL<br>- [N22000236]                                                               | 4/2011                        | 542.18<br>-                        | 542.18                       | 311.90                             | 03/2020<br>-                       | 03/2020     |
|                                 | <u>North Central Railway</u>                                                                     |                               |                                    |                              |                                    |                                    |             |
| 203                             | MATHURA-PLWAL 4TH LINE (80KM)<br>- [N22000372]                                                   | 4/2015                        | 668.70<br>668.00                   | 668.00                       | -                                  | 03/2020<br>-                       | 03/2020     |
| 204                             | GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)<br>- [N22000148]                                  | 4/2011                        | 2,912.96<br>-                      | 3,845.60                     | 1.92                               | 03/2022<br>-                       | 03/2022     |
| 205                             | JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING<br>- [N22000495]                                    | 3/2018                        | 4,329.53<br>-                      | 4,329.53                     | -                                  | 03/2023<br>-                       | 03/2023     |
| 206                             | JHANSI BINA DOUBLING<br>- [N22000496]                                                            | 9/2016                        | 2,001.00<br>-                      | 2,001.00                     | -                                  | 03/2021<br>-                       | 03/2021     |
|                                 | <u>North East Frontier Railway</u>                                                               |                               |                                    |                              |                                    |                                    |             |
| 207                             | DIGARU-HOJAI (102 KM)<br>- [N22000389]                                                           | 4/2015                        | 870.96<br>-                        | 821.00                       | 214.95                             | 03/2021<br>-                       | 03/2021     |
| 208                             | MURKONGSELEK-PASIGHAT NL<br>- [N22000208]                                                        | 4/2011                        | 414.84<br>-                        | 661.00                       | 121.37                             | 03/2020<br>-                       | 03/2020     |
| 209                             | LUMDING-HOJAI PATCH DOUBLING PROJECT<br>- [N22000211]                                            | 4/2012                        | 246.07<br>-                        | 398.93                       | 328.77                             | 03/2019<br>-                       | 03/2019     |
| 210                             | NEW BG LINE FROM BALURGHAT TO HILLY NFR<br>- [N22000206]                                         | 4/2010                        | 242.22<br>-                        | 471.00                       | 64.68                              | 03/2020<br>-                       | 03/2020     |
| 211                             | NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING<br>- [N22000183]                                        | 4/2013                        | 1,798.00<br>-                      | 1,798.00                     | -                                  | 03/2019<br>-                       | 03/2019     |
| 212                             | DIMAPUR-TIZIT NL<br>- [N22000196]                                                                | 4/2013                        | 4,274.00<br>-                      | 4,274.00                     | -                                  | 03/2020<br>-                       | 03/2020     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above |                                                                                                      |                               |                                    |                              |                                    | (December 2018)                    |             |
|---------------------------------|------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                 |                                                                                                      |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                            | Project                                                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                               | 2                                                                                                    | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 213                             | NEW BG LINE FROM BYRNIHAT TO SHILLONG<br>- [N22000205]                                               | 4/2010                        | 906.46<br>-                        | 6,000.00                     | 259.95                             | 03/2021<br>-                       | 03/2021     |
| 214                             | AMBARI FALAKATA TO NEW MAYNAGURI<br>- [N22000210]                                                    | 4/2011                        | 314.00<br>-                        | 551.00                       | 602.54                             | 03/2019<br>-                       | 03/2019     |
|                                 | <u>North Eastern Railway</u>                                                                         |                               |                                    |                              |                                    |                                    |             |
| 215                             | CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP<br>- [N22000131]                                      | 3/2007                        | 243.78<br>-                        | 895.00                       | 99.33                              | 12/2021<br>-                       | 12/2021     |
| 216                             | BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.<br>- [N22000457]                   | 4/2016                        | 1,900.00<br>-                      | 1,277.06                     | -                                  | 01/2022<br>-                       | 01/2022     |
| 217                             | AUNRIHAR - JAUNPUR PATCH DOUBLING .<br>- [N22000469]                                                 | 4/2016                        | 600.00<br>-                        | 366.71                       | 0.46                               | 01/2022<br>-                       | 01/2022     |
|                                 | <u>North Western Railway</u>                                                                         |                               |                                    |                              |                                    |                                    |             |
| 218                             | AJMER-BANGURGRAM<br>- [N22000155]                                                                    | 4/2011                        | 213.39<br>-                        | 244.02                       | 217.81                             | 11/2019<br>-                       | 11/2019     |
| 219                             | JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)<br>- [N22000466]                                    | 8/2018                        | 808.85<br>-                        | 808.85                       | -                                  | 08/2022<br>-                       | 08/2022     |
| 220                             | PHULERA - DIGANA DOUBLING<br>- [N22000326]                                                           | 5/2015                        | 600.00<br>-                        | 685.99                       | 3.52                               | 03/2020<br>-                       | 03/2020     |
| 221                             | DAUSA-GANGAPUR CITY(NL),NWR<br>- [220100184]                                                         | 2/1997                        | 410.08<br>-                        | 795.01                       | 458.50                             | 02/2019<br>-                       | 02/2019     |
|                                 | <u>Northern Railway</u>                                                                              |                               |                                    |                              |                                    |                                    |             |
| 222                             | CHANDIGARH-BADDI<br>- [N22000467]                                                                    | 4/2007                        | 328.14<br>-                        | 1,540.00                     | 229.95                             | 03/2023<br>-                       | 03/2023     |
|                                 | <u>National High Speed Rail Corporation Limited</u>                                                  |                               |                                    |                              |                                    |                                    |             |
| 223                             | MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT<br>- [N22000463]                                            | 12/2015                       | 1,08,000.00<br>-                   | 1,08,000.00                  | 1,057.80                           | 12/2023<br>12/2023                 | 12/2023     |
|                                 | <u>Rail India Technical And Economic Service</u>                                                     |                               |                                    |                              |                                    |                                    |             |
| 224                             | DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY<br>- [N22000394]            | 3/2015                        | 636.38<br>-                        | 636.38                       | 169.16                             | 03/2021<br>-                       | 03/2021     |
|                                 | <u>Rail Vikas Nigam Ltd.</u>                                                                         |                               |                                    |                              |                                    |                                    |             |
| 225                             | HOSPET-HUBLI-LONDA-VASCODAGAMA DL<br>- [N22000297]                                                   | 4/2010                        | 2,127.00<br>-                      | 2,127.00                     | 1,042.32                           | 03/2023<br>-                       | 03/2023     |
| 226                             | PALANPUR-SAMAKHAYALI (DL)<br>- [N22000144]                                                           | 4/2013                        | 1,548.66<br>-                      | 1,548.66                     | 777.72                             | 12/2021<br>-                       | 12/2021     |
| 227                             | VIZIANAGARAM - SAMABALPUR 3RD LINE<br>- [N22000409]                                                  | 1/1991                        | 2,335.67<br>-                      | 2,335.67                     | 316.27                             | 12/2024<br>-                       | 12/2024     |
| 228                             | RAIPUR - TITLAGARH - DOUBLING<br>- [N22000411]                                                       | 3/2007                        | 1,402.02<br>-                      | 758.09                       | 1,001.84                           | 03/2020<br>-                       | 03/2020     |
| 229                             | BHANUPALI-BILASPUR BERI NL<br>- [N22000273]                                                          | 4/2008                        | 2,966.99<br>-                      | 7,000.00                     | 221.19                             | 12/2026<br>-                       | 12/2026     |
| 230                             | VIJAYAWADA-GUDUR<br>- [N22000369]                                                                    | 4/2015                        | 3,246.26<br>-                      | 3,548.67                     | 132.79                             | 12/2023<br>-                       | 12/2023     |
| 231                             | DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)<br>- [N22000407] | 3/2009                        | 713.48<br>-                        | 1,750.00                     | 1,618.00                           | 03/2020<br>-                       | 03/2020     |
| 232                             | DHASA-JETALSAR (GC)<br>- [N22000141]                                                                 | 4/2012                        | 644.38<br>-                        | 644.38                       | 127.98                             | 03/2021<br>-                       | 03/2021     |
| 233                             | SAMBALPUR - TITLAGARH - DOUBLING<br>- [N22000410]                                                    | 3/2006                        | 948.04<br>-                        | 970.00                       | 910.62                             | 03/2020<br>-                       | 03/2020     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above |                                                                                                                    |                               |                                    |                              |                                    | (December 2018)                    |             |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                 |                                                                                                                    |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                            | Project                                                                                                            | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                               | 2                                                                                                                  | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 234                             | AHMEDABAD-BOTAD (GC)<br>- [N22000140]                                                                              | 4/2012                        | 975.62<br>-                        | 975.62                       | 518.92                             | 12/2021<br>-                       | 12/2021     |
| 235                             | SECUNDERABAD-MAHABUBNAGAR DOUBLING<br>- [N22000403]                                                                | 4/2015                        | 773.94<br>-                        | 773.94                       | 412.07                             | 12/2024<br>-                       | 12/2024     |
| 236                             | BINA - KOTA DOUBLING WITH RE<br>- [N22000414]                                                                      | 4/2011                        | 1,485.85<br>-                      | 1,485.85                     | 1,038.90                           | 12/2020<br>-                       | 12/2020     |
|                                 | <u>South Central Railway</u>                                                                                       |                               |                                    |                              |                                    |                                    |             |
| 237                             | KAZIPET-BALHRSHA<br>- [N22000367]                                                                                  | 4/2015                        | 2,063.03<br>-                      | 2,063.03                     | 368.22                             | 03/2021<br>-                       | 03/2021     |
| 238                             | MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432] | 4/2017                        | 119.73<br>185.00                   | 184.97                       | -                                  | 03/2022<br>-                       | 03/2022     |
| 239                             | BHADRACHALAM ROAD-SATTUPALLI<br>- [N22000287]                                                                      | 4/2010                        | 704.31<br>-                        | 704.31                       | 119.69                             | 03/2020<br>-                       | 03/2020     |
|                                 | <u>South East Central Railway</u>                                                                                  |                               |                                    |                              |                                    |                                    |             |
| 240                             | WADSA-GADHCHIROLI NEW LINE (52.36 KM)<br>- [N22000480]                                                             | 6/2018                        | 229.00<br>-                        | 403.00                       | 36.28                              | 12/2021<br>-                       | 12/2021     |
| 241                             | ANUPPUR-KATNI<br>- [N22000485]                                                                                     | 4/2015                        | 1,370.00<br>-                      | 1,370.00                     | 101.00                             | 12/2021<br>-                       | 12/2021     |
| 242                             | JHARSUGUDA-BILASPUR 4TH LINE<br>- [N22000484]                                                                      | 4/2015                        | 1,973.00<br>-                      | 1,973.00                     | 78.00                              | 03/2021<br>-                       | 03/2021     |
| 243                             | CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT<br>- [N22000438]                                           | 4/2010                        | 585.93<br>-                        | 1,420.39                     | 104.10                             | 02/2019<br>-                       | 02/2019     |
| 244                             | CHAMPA-JHARSUGUDA 3RD LINE<br>- [N22000483]                                                                        | 4/2008                        | 872.00<br>-                        | 1,279.00                     | -                                  | 12/2019<br>-                       | 12/2019     |
| 245                             | GONDIA-JABALPUR(GC),(SECR)<br>- [220100186]                                                                        | 2/1997                        | 511.86<br>-                        | 1,756.00                     | 967.96                             | 04/2020<br>-                       | 04/2020     |
| 246                             | RAJNANDGAON - NAGPUR - 3RD LINE (SECR)<br>- [N22000420]                                                            | 9/2016                        | 1,908.51<br>-                      | 2,686.63                     | -                                  | 03/2023<br>-                       | 03/2023     |
| 247                             | GEVRA ROAD PENDRA ROAD<br>- [N22000488]                                                                            | 2/2014                        | 2,288.00<br>-                      | 4,919.00                     | 67.00                              | 03/2022<br>-                       | 03/2022     |
| 248                             | KENDRI-DHARTARI INCLUDING ABHANPUR-RAJIM<br>- [N22000482]                                                          | 4/2011                        | 1,471.93<br>-                      | 543.00                       | -                                  | 03/2022<br>-                       | 03/2022     |
|                                 | <u>South Eastern Railway</u>                                                                                       |                               |                                    |                              |                                    |                                    |             |
| 249                             | TAMLUK DIGHA 88.9 KM WITH MM DESHPURAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]      | 1/1991                        | 1,013.45<br>-                      | 1,428.00                     | 484.49                             | 12/2021<br>12/2021                 | 12/2021     |
|                                 | <u>South Western Railway</u>                                                                                       |                               |                                    |                              |                                    |                                    |             |
| 250                             | ARSIKERE-TUMKUR<br>- [N22000332]                                                                                   | 3/2015                        | 578.00<br>-                        | 578.00                       | 458.72                             | 03/2020<br>03/2020                 | 03/2020     |
| 251                             | YELAHANKA-PENUKONDA<br>- [N22000328]                                                                               | 5/2015                        | 860.43<br>-                        | 860.43                       | 503.45                             | 03/2020<br>03/2020                 | 03/2020     |
|                                 | <u>Southern Railway</u>                                                                                            |                               |                                    |                              |                                    |                                    |             |
| 252                             | MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING<br>- [N22000451]                                                 | 2/2015                        | 760.00<br>-                        | 1,182.31                     | -                                  | 03/2020<br>-                       | 03/2020     |
| 253                             | MADURAI-TUTICORIN VIA ARUPPUKOTTAI<br>- [N22000215]                                                                | 4/2011                        | 120.70<br>-                        | 1,800.00                     | 112.10                             | 03/2019<br>-                       | 03/2019     |
| 254                             | ATTIPPATTU PUTTUR<br>- [N22000184]                                                                                 | 4/2008                        | 151.84<br>-                        | 1,105.00                     | 3.34                               | 02/2019<br>-                       | 02/2019     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above |                                                                                                                    |                               |                                    |                              |                                    | (December 2018)                    |             |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                 |                                                                                                                    |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                            | Project                                                                                                            | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                               | 2                                                                                                                  | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 255                             | MANIYACHI - NAGERCOIL (102 KM) DOUBLING<br>- [N22000449]                                                           | 2/2015                        | 1,700.00<br>-                      | 1,700.00                     | -                                  | 03/2022<br>-                       | 03/2022     |
| 256                             | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI<br>- [N22000079]                                  | 9/2007                        | 724.69<br>-                        | 2,072.50                     | 1,169.07                           | 02/2019<br>-                       | 02/2019     |
|                                 | <u>West Central Railway</u>                                                                                        |                               |                                    |                              |                                    |                                    |             |
| 257                             | KATNI GRADE SEPARATOR/BYE PASS<br>- [N22000416]                                                                    | 8/2016                        | 582.13<br>-                        | 1,260.61                     | -                                  | 03/2022<br>-                       | 03/2022     |
| 258                             | RAMGANJMUUNDI-BHOPAL (NL),WCR<br>- [220100314]                                                                     | 4/2001                        | 424.60<br>-                        | 2,713.09                     | 898.83                             | 03/2021<br>-                       | 03/2021     |
| 259                             | KATNI-BINA 3RD LINE (263 KM)<br>- [N22000415]                                                                      | 6/2016                        | 2,478.23<br>-                      | 2,478.23                     | 112.07                             | 03/2022<br>-                       | 03/2022     |
|                                 | <u>Western Railway</u>                                                                                             |                               |                                    |                              |                                    |                                    |             |
| 260                             | INDORE-DEWAS-UJJAIN (80 KMS)<br>- [N22000493]                                                                      | 4/2016                        | 700.00<br>-                        | 700.00                       | 11.19                              | 06/2020<br>-                       | 06/2020     |
| 261                             | DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM<br>- [N22000494]                       | 4/2017                        | 691.84<br>-                        | 691.84                       | 15.31                              | 03/2020<br>-                       | 03/2020     |
| 262                             | BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION<br>- [N22000487]   | 2/1991                        | 551.51<br>-                        | 551.51                       | 257.05                             | 03/2019<br>-                       | 03/2019     |
| 263                             | AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)<br>- [N22000121]                                                                | 4/2008                        | 829.74<br>-                        | 385.60                       | 500.42                             | 03/2020<br>03/2020                 | 03/2020     |
| 264                             | RATLAM-MHOW-KHANDWA-AKOLA (GC)<br>- [N22000120]                                                                    | 4/2008                        | 3,503.69<br>-                      | 1,030.29                     | 1,081.52                           | 03/2022<br>03/2019                 | 03/2022     |
| 265                             | CHOTTAUDEPUR-DHAR(NL)<br>- [N22000138]                                                                             | 4/2007                        | 1,347.26<br>-                      | 1,347.26                     | 606.41                             | 03/2022<br>03/2019                 | 03/2022     |
| 266                             | DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)<br>- [N22000139]                                                  | 4/2007                        | 1,640.04<br>-                      | 1,640.04                     | 603.75                             | 03/2022<br>03/2019                 | 03/2022     |
|                                 | Total                                                                                                              |                               | 2,50,468.44<br>-                   | 3,13,126.09                  | 51,184.80                          |                                    |             |
|                                 |                                                                                                                    |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                 |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>Ministry Of Road Transport And Highways</u>                                                                     |                               |                                    |                              |                                    |                                    |             |
| 267                             | RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777] | 11/2017                       | 283.51<br>-                        | 284.00                       | 94.50                              | 11/2019<br>-                       | 11/2019     |
| 268                             | RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776] | 11/2017                       | 232.81<br>-                        | 232.81                       | 48.23                              | 11/2019<br>-                       | 11/2019     |
| 269                             | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821] | 11/2017                       | 257.34<br>-                        | 238.00                       | 41.09                              | 11/2019<br>12/2019                 | 11/2019     |
| 270                             | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772] | 12/2017                       | 257.34<br>-                        | 257.34                       | -                                  | 12/2019<br>-                       | 12/2019     |
| 271                             | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773] | 12/2017                       | 200.34<br>-                        | 200.34                       | 43.14                              | 12/2019<br>-                       | 12/2019     |
| 272                             | Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820] | 11/2017                       | 237.80<br>-                        | 238.00                       | 29.43                              | 11/2019<br>-                       | 11/2019     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above |                                                                                                                   |                               |                                    |                              |                                    | (December 2018)                    |             |
|---------------------------------|-------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                 |                                                                                                                   |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                            | Project                                                                                                           | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                               | 2                                                                                                                 | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 273                             | CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781 | 5/2018                        | 248.00 -                           | 248.00                       | -                                  | 05/2020 -                          | 05/2020     |
| 274                             | WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774 | 12/2017                       | 248.22 -                           | 248.22                       | 57.01                              | 12/2019 -                          | 12/2019     |
| 275                             | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778 | 11/2017                       | 266.52 -                           | 266.52                       | 95.30                              | 11/2019 -                          | 11/2019     |
| 276                             | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775 | 6/2017                        | 282.08 -                           | 282.08                       | 66.19                              | 06/2019 -                          | 06/2019     |
| 277                             | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779    | 2/2018                        | 418.88 -                           | 418.88                       | 92.42                              | 02/2020 -                          | 02/2020     |
|                                 | <u>National Highways And Infrastructure Development Corporation Ltd.</u>                                          |                               |                                    |                              |                                    |                                    |             |
| 278                             | 4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429      | 12/2015                       | 225.02 -                           | 159.20                       | -                                  | 12/2018 -                          | 12/2018     |
| 279                             | 2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325                             | 10/2015                       | 179.82 -                           | 179.82                       | 8.99                               | 01/2019 -                          | 01/2019     |
| 280                             | FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321                      | 6/2016                        | 829.00 -                           | 829.00                       | 59.85                              | 01/2019 -                          | 01/2019     |
| 281                             | 4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438      | 12/2015                       | 289.99 -                           | 289.99                       | -                                  | 12/2018 -                          | 12/2018     |
|                                 | <u>National Highways Authority Of India</u>                                                                       |                               |                                    |                              |                                    |                                    |             |
| 282                             | TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665  | 3/2017                        | 672.89 -                           | 736.01                       | -                                  | 03/2020 -                          | 03/2020     |
| 283                             | FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807  | 3/2018                        | 1,532.62 -                         | 1,532.62                     | -                                  | 03/2021 -                          | 03/2021     |
| 284                             | 4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600   | 8/2016                        | 1,388.34 -                         | 1,388.34                     | 595.70                             | 09/2019 -                          | 09/2019     |
| 285                             | 6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672 | 3/2017                        | 2,064.99 -                         | 2,447.00                     | 1,002.09                           | 03/2020 -                          | 03/2020     |
| 286                             | DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619 | 9/2016                        | 2,510.04 -                         | 2,510.04                     | -                                  | 08/2019 -                          | 08/2019     |
| 287                             | REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667                      | 3/2017                        | 648.32 -                           | 503.10                       | 15.10                              | 03/2020 -                          | 03/2020     |
| 288                             | CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625 | 9/2016                        | 1,004.67 -                         | 1,004.67                     | -                                  | 05/2019 -                          | 05/2019     |
| 289                             | 4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548                                                 | 2/2016                        | 997.15 -                           | 997.15                       | 352.03                             | 03/2019 -                          | 03/2019     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above |                                                                                                                   |                               |                                    |                              |                                    | (December 2018)                    |             |
|---------------------------------|-------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                 |                                                                                                                   |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                            | Project                                                                                                           | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                               | 2                                                                                                                 | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 290                             | FOUR LANNING OF VIKRAVANDI-SETHIAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652   | 3/2017                        | 848.45 -                           | 848.45                       | 5.00                               | 03/2020 -                          | 03/2020     |
| 291                             | TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622 | 9/2016                        | 950.69 -                           | 950.69                       | 499.54                             | 08/2019 -                          | 08/2019     |
| 292                             | 4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656                                             | 3/2017                        | 744.64 -                           | 982.00                       | -                                  | 03/2020 -                          | 03/2020     |
| 293                             | DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541                                | 1/2016                        | 1,081.57 -                         | 1,081.57                     | 795.28                             | 06/2019 -                          | 06/2019     |
| 294                             | 4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692                                                      | 6/2017                        | 2,485.93 -                         | 2,485.93                     | -                                  | 06/2020 -                          | 06/2020     |
| 295                             | BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605                                  | 8/2016                        | 227.49 -                           | 227.49                       | 15.03                              | 01/2019 -                          | 01/2019     |
| 296                             | 4 LANING OF FAGNE - MAH-GUJ BORDER ( PKG-3) - [N24000439                                                          | 7/2015                        | 1,885.74 -                         | 1,885.74                     | 1,622.44                           | 05/2019 -                          | 05/2019     |
| 297                             | 4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425                                                               | 7/2015                        | 2,288.18 -                         | 2,288.18                     | -                                  | 05/2019 -                          | 05/2019     |
| 298                             | 8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449                                                                 | 7/2015                        | 2,128.72 -                         | 2,128.72                     | 1,042.73                           | 04/2019 -                          | 04/2019     |
| 299                             | 6 LANING OF AGRA - ETAWAH BYPASS - [N24000452                                                                     | 7/2015                        | 1,657.20 -                         | 1,657.20                     | 1,945.00                           | 01/2019 -                          | 01/2019     |
| 300                             | FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505 | 6/2015                        | 1,583.79 -                         | 1,583.79                     | 1,439.18                           | 01/2019 -                          | 01/2019     |
| 301                             | CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650 | 1/2017                        | 244.90 -                           | 244.90                       | 82.41                              | 05/2019 -                          | 05/2019     |
| 302                             | FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556 | 3/2016                        | 899.00 -                           | 899.00                       | 351.90                             | 04/2019 -                          | 04/2019     |
| 303                             | FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602                             | 8/2016                        | 1,664.20 -                         | 1,664.20                     | 313.63                             | 04/2020 -                          | 04/2020     |
| 304                             | CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442 | 12/2015                       | 649.50 -                           | 649.50                       | 86.54                              | 03/2019 -                          | 03/2019     |
| 305                             | NAGPUR RING ROAD PACKAGE-2 - [N24000560                                                                           | 3/2016                        | 591.66 -                           | 591.66                       | 608.89                             | 07/2019 -                          | 07/2019     |
| 306                             | DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540                                                       | 1/2016                        | 701.12 -                           | 701.12                       | 842.34                             | 05/2019 -                          | 05/2019     |
| 307                             | NAGPUR RING ROAD PACKAGE-1 - [N24000558                                                                           | 3/2016                        | 546.00 -                           | 546.00                       | 460.55                             | 07/2019 -                          | 07/2019     |
| 308                             | HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603                                                                   | 8/2016                        | 1,167.42 -                         | 1,167.42                     | 192.72                             | 03/2019 -                          | 03/2019     |
| 309                             | CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666 | 3/2017                        | 235.48 -                           | 227.77                       | -                                  | 03/2020 -                          | 03/2020     |
| 310                             | ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544                                      | 3/2016                        | 676.73 -                           | 676.73                       | 409.11                             | 04/2019 -                          | 04/2019     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above |                                                                                                                    |                               |                                    |                              |                                    | (December 2018)                    |             |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                 |                                                                                                                    |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                            | Project                                                                                                            | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                               | 2                                                                                                                  | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 311                             | REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]  | 3/2017                        | 1,288.07 -                         | 1,420.00                     | -                                  | 03/2020 -                          | 03/2020     |
| 312                             | CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655] | 3/2017                        | 247.02 -                           | 157.49                       | -                                  | 03/2020 -                          | 03/2020     |
| 313                             | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]                 | 3/2016                        | 1,587.49 -                         | 1,587.49                     | 164.42                             | 04/2019 -                          | 04/2019     |
| 314                             | 2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]                                | 2/2016                        | 273.20 -                           | 273.20                       | 48.69                              | 02/2019 -                          | 02/2019     |
| 315                             | FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]                                                          | 12/2015                       | 1,041.10 -                         | 1,041.10                     | 175.85                             | 04/2019 -                          | 04/2019     |
|                                 | Total                                                                                                              |                               | 42,970.98 -                        | 43,458.47                    | 13,702.32                          |                                    |             |
|                                 |                                                                                                                    |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>SHIPPING AND PORTS</u>                                                                                          |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>Inland Waterways Authority Of India</u>                                                                         |                               |                                    |                              |                                    |                                    |             |
| 316                             | JAL MARG VIKAS PROJECT - [N25000072]                                                                               | 1/2018                        | 4,200.00 -                         | 4,200.00                     | -                                  | 03/2023 -                          | 03/2023     |
|                                 | Total                                                                                                              |                               | 4,200.00 -                         | 4,200.00                     | .00                                |                                    |             |
|                                 |                                                                                                                    |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>STEEL</u>                                                                                                       |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>National Mineral Development Corporation (Nmhc)</u>                                                             |                               |                                    |                              |                                    |                                    |             |
| 317                             | 2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]                                                                      | 11/2015                       | 818.00 -                           | 818.00                       | 31.60                              | 06/2020 -                          | 06/2020     |
|                                 | Total                                                                                                              |                               | 818.00 -                           | 818.00                       | 31.60                              |                                    |             |
|                                 |                                                                                                                    |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>URBAN DEVELOPMENT</u>                                                                                           |                               |                                    |                              |                                    |                                    |             |
|                                 | <u>Central Public Works Department</u>                                                                             |                               |                                    |                              |                                    |                                    |             |
| 318                             | CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]                                                  | 11/2017                       | 171.72 -                           | 171.72                       | -                                  | 03/2020 -                          | 03/2020     |
| 319                             | RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106] | 11/2017                       | 238.56 -                           | 238.56                       | 3.36                               | 05/2020 -                          | 05/2020     |
| 320                             | C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112] | 9/2017                        | 150.29 -                           | 150.29                       | 2.58                               | 03/2020 -                          | 03/2020     |
| 321                             | CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107] | 12/2017                       | 188.00 -                           | 188.00                       | 85.71                              | 06/2019 -                          | 06/2019     |
| 322                             | CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]                             | 10/2017                       | 271.90 -                           | 271.90                       | 4.44                               | 11/2019 -                          | 11/2019     |
| 323                             | ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]              | 10/2016                       | 209.84 -                           | 209.84                       | 12.71                              | 03/2020 -                          | 03/2020     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above |                                                                                                                        |                               |                                    |                              |                                    | (December 2018)                    |             |
|---------------------------------|------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                 |                                                                                                                        |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                            | Project                                                                                                                | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                               | 2                                                                                                                      | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 324                             | CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP<br>- [N28000108]                                                 | 1/2018                        | 206.58<br>-                        | 206.58                       | 0.02                               | 03/2019<br>-                       | 03/2019     |
| 325                             | C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI -<br>[N28000089] | 12/2015                       | 209.00<br>-                        | 209.00                       | 52.00                              | 10/2019<br>-                       | 10/2019     |
|                                 | <u>Lucknow Metro Rail Corporation Limited</u>                                                                          |                               |                                    |                              |                                    |                                    |             |
| 326                             | LUCKNOW METRO RAIL CORPORATION LTD<br>- [N28000094]                                                                    | 1/2016                        | 6,928.00<br>6,928.00               | 6,928.00                     | 2,536.77                           | 03/2019<br>-                       | 03/2019     |
|                                 | <u>Maharashtra Metro Rail Corporation Ltd.</u>                                                                         |                               |                                    |                              |                                    |                                    |             |
| 327                             | PUNE METRO RAIL PROJECT (PHASE 1)<br>- [N28000121]                                                                     | 12/2016                       | 11,420.00<br>-                     | 11,420.00                    | 1,938.17                           | 11/2021<br>-                       | 11/2021     |
|                                 | <u>National Building Construction Corporation Ltd</u>                                                                  |                               |                                    |                              |                                    |                                    |             |
| 328                             | REDEVELOPMENT OF EAST KIDWAI NAGAR<br>- [N28000080]                                                                    | 6/2012                        | 4,264.00<br>-                      | 4,439.23                     | 3,671.53                           | 11/2019<br>-                       | 11/2019     |
|                                 | Total                                                                                                                  |                               | 24,257.89<br>-                     | 24,433.12                    | 8,307.29                           |                                    |             |
|                                 |                                                                                                                        |                               |                                    |                              |                                    |                                    |             |
|                                 | Grand Total                                                                                                            |                               | 5,60,961.80                        | 6,23,862.30                  | 1,33,349.92                        |                                    |             |



## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

### Annexure - V

| (December 2018) |                                                                                           |                                  |                                      |                                |                                       |             |                   |
|-----------------|-------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                 |                                                                                           |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No            | Project                                                                                   | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1               | 2                                                                                         | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
|                 |                                                                                           |                                  |                                      |                                |                                       |             |                   |
|                 | <u>ATOMIC ENERGY</u>                                                                      |                                  |                                      |                                |                                       |             |                   |
|                 | <u>Bhavini Limited</u>                                                                    |                                  |                                      |                                |                                       |             |                   |
| 1               | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)<br>- [020100044]                        | 09/2003                          | 3,492.00<br>-                        | 6,100.00                       | 09/2010<br>-                          | 03/2019     | 74.69             |
|                 | <u>Nuclear Power Corporation Of India Limited</u>                                         |                                  |                                      |                                |                                       |             |                   |
| 2               | KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4<br>- [N02000010]                                  | 10/2009                          | 11,459.00<br>-                       | 16,580.00                      | 12/2015<br>-                          | 06/2020     | 44.69             |
|                 | Total                                                                                     |                                  | 14,951.00<br>-                       | 22,680.00                      |                                       |             |                   |
|                 |                                                                                           |                                  |                                      |                                |                                       |             |                   |
|                 | <u>CIVIL AVIATION</u>                                                                     |                                  |                                      |                                |                                       |             |                   |
|                 | <u>Airport Authority Of India Limited</u>                                                 |                                  |                                      |                                |                                       |             |                   |
| 3               | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR<br>[N04000073] | 10/2013                          | 314.61<br>-                          | 441.33                         | 09/2018<br>-                          | 06/2020     | 40.28             |
|                 | Total                                                                                     |                                  | 314.61<br>-                          | 441.33                         |                                       |             |                   |
|                 |                                                                                           |                                  |                                      |                                |                                       |             |                   |
|                 | <u>COAL</u>                                                                               |                                  |                                      |                                |                                       |             |                   |
|                 | <u>Neyveli Lignite Corporation</u>                                                        |                                  |                                      |                                |                                       |             |                   |
| 4               | NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW<br>- [N06000152]                      | 07/2016                          | 17,237.00<br>-                       | 17,237.80                      | 11/2021<br>-                          | 11/2021     | .00               |
|                 | <u>Northern Coal Fields Limited</u>                                                       |                                  |                                      |                                |                                       |             |                   |
| 5               | NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI<br>- [N06000033]                 | 10/2007                          | 259.40<br>-                          | 486.57                         | 03/2012<br>-                          | -           | 87.58             |
|                 | <u>Singareni Colliers Company Limited</u>                                                 |                                  |                                      |                                |                                       |             |                   |
| 6               | RAMAGUNDAM OC-II EXTENSION<br>- [N06000078]                                               | 12/2009                          | 418.97<br>-                          | 489.62                         | 03/2012<br>-                          | 03/2023     | 16.86             |
| 7               | SHANTIKHANI LONGWALL PROJ-SCCL<br>- [N06000017]                                           | 10/2006                          | 249.03<br>-                          | 448.86                         | 03/2012<br>-                          | 03/2024     | 80.24             |
| 8               | KAKATIYAKHANI OPENCAST-2 PROJECT<br>- [N06000129]                                         | 05/2015                          | 397.09<br>-                          | 442.42                         | 03/2019<br>-                          | 03/2019     | 11.42             |
| 9               | RCE OF INDARAM OCP(1.20 MTPA)<br>- [N06000093]                                            | 07/2011                          | 162.76<br>-                          | 349.28                         | 03/2015<br>-                          | 03/2021     | 114.60            |
|                 | <u>South-Eastern Coal Fields Limited</u>                                                  |                                  |                                      |                                |                                       |             |                   |
| 10              | JAGANNATHPORA OCP(3.00MTY)<br>- [N06000075]                                               | 09/2008                          | 152.43<br>-                          | 459.49                         | 03/2015<br>-                          | 03/2020     | 201.44            |
|                 | <u>Western Coal Fields Limited</u>                                                        |                                  |                                      |                                |                                       |             |                   |
| 11              | KAMPTEE DEEP OC MINE<br>- [N06000141]                                                     | 11/2015                          | 277.65<br>-                          | 313.34                         | 03/2021<br>-                          | 03/2024     | 12.85             |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (December 2018) |                                                                                       |                                  |                                      |                                |                                       |             |                   |
|-----------------|---------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                 |                                                                                       |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No            | Project                                                                               | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1               | 2                                                                                     | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 12              | BHANEGAON OC<br>- [N06000121                                                          | 02/2015                          | 187.94<br>-                          | 409.68                         | 03/2023<br>-                          | 03/2023     | 117.98            |
| 13              | ADASA UG TO OC<br>- [N06000133                                                        | 08/2015                          | 288.90<br>-                          | 333.43                         | 03/2023<br>-                          | 03/2024     | 15.41             |
|                 | Total                                                                                 |                                  | 19,631.17<br>-                       | 20,970.49                      |                                       |             |                   |
|                 |                                                                                       |                                  |                                      |                                |                                       |             |                   |
|                 | <u>DEFENCE PRODUCTION</u>                                                             |                                  |                                      |                                |                                       |             |                   |
|                 | <u>Goa Shipyard Limited</u>                                                           |                                  |                                      |                                |                                       |             |                   |
| 14              | CONSTRUCTION WORKS PHASE 4<br>- [N39000001                                            | 12/2016                          | 167.69<br>168.00                     | 170.37                         | 05/2018<br>-                          | 01/2019     | 1.60              |
| 15              | CONSTRUCTION WORKS PHASE 3B<br>- [N39000002                                           | 12/2016                          | 285.95<br>286.00                     | 291.29                         | 08/2020<br>-                          | 08/2020     | 1.87              |
|                 | Total                                                                                 |                                  | 453.64<br>-                          | 461.66                         |                                       |             |                   |
|                 |                                                                                       |                                  |                                      |                                |                                       |             |                   |
|                 | <u>FERTILISERS</u>                                                                    |                                  |                                      |                                |                                       |             |                   |
|                 | <u>Rashtriya Chemical &amp; Fertiliser Limited</u>                                    |                                  |                                      |                                |                                       |             |                   |
| 16              | NEW SEWAGE TREATMENT PLANT PACKAGE, RCF<br>TROMBAY - [N08000009                       | 10/2014                          | 197.79<br>-                          | 209.44                         | 11/2016<br>-                          | 04/2019     | 5.89              |
|                 | Total                                                                                 |                                  | 197.79<br>-                          | 209.44                         |                                       |             |                   |
|                 |                                                                                       |                                  |                                      |                                |                                       |             |                   |
|                 | <u>HEALTH AND FAMILY WELFARE</u>                                                      |                                  |                                      |                                |                                       |             |                   |
|                 | <u>Hospital Services Consultancy Corporation Ltd</u>                                  |                                  |                                      |                                |                                       |             |                   |
| 17              | LHMC NEW DELHI-RE-DEVELOPMENT<br>- [N21000003                                         | 02/2013                          | 414.11<br>-                          | 513.89                         | 11/2013<br>-                          | 10/2020     | 24.10             |
| 18              | CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI<br>JHAJJAR - [N21000011                    | 09/2014                          | 505.58<br>-                          | 523.00                         | 03/2018<br>-                          | -           | 3.45              |
| 19              | GERIATRICS BLOCK- AIIMS DLEHI<br>- [N21000019                                         | 12/2017                          | 156.56<br>-                          | 156.65                         | -<br>-                                | 02/2020     | .06               |
|                 | Total                                                                                 |                                  | 1,076.25<br>-                        | 1,193.54                       |                                       |             |                   |
|                 |                                                                                       |                                  |                                      |                                |                                       |             |                   |
|                 | <u>HEAVY INDUSTRY</u>                                                                 |                                  |                                      |                                |                                       |             |                   |
|                 | <u>Natrip Implementation Society</u>                                                  |                                  |                                      |                                |                                       |             |                   |
| 20              | NATIONAL AUTOMOTIVE TESTING AND RD<br>INFRASTRUCTURE PROJECT (NATRIP)<br>- [N20000001 | 04/2011                          | 1,718.00<br>-                        | 3,827.30                       | 09/2011<br>-                          | 06/2019     | 122.78            |
|                 | Total                                                                                 |                                  | 1,718.00<br>-                        | 3,827.30                       |                                       |             |                   |
|                 |                                                                                       |                                  |                                      |                                |                                       |             |                   |
|                 | <u>PETROLEUM</u>                                                                      |                                  |                                      |                                |                                       |             |                   |
|                 | <u>Bharat Petroleum Corporation Limited</u>                                           |                                  |                                      |                                |                                       |             |                   |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (December 2018) |                                                                                                         |                                  |                                      |                                |                                       |             |                   |
|-----------------|---------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                 |                                                                                                         |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No            | Project                                                                                                 | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1               | 2                                                                                                       | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 21              | PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY<br>- [N16000227]                    | 11/2014                          | 4,588.29<br>-                        | 5,245.96                       | 08/2018<br>-                          | 11/2019     | 14.33             |
|                 | <u>Hindustan Petroleum Corporation Limited</u>                                                          |                                  |                                      |                                |                                       |             |                   |
| 22              | URAN CHAKAN SHIKRAPUR LPG PIPELINE<br>- [N16000155]                                                     | 12/2009                          | 309.81<br>-                          | 723.40                         | 10/2014<br>-                          | 02/2019     | 133.50            |
| 23              | 50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II<br>- [N16000209]                                       | 11/2011                          | 310.00<br>-                          | 370.00                         | 03/2013<br>-                          | -           | 19.35             |
|                 | <u>Indian Oil Corporation Limited</u>                                                                   |                                  |                                      |                                |                                       |             |                   |
| 24              | LPG TERMINAL AT KOCHI<br>- [N16000171]                                                                  | 10/2015                          | 607.06<br>-                          | 714.25                         | 10/2017<br>-                          | 03/2019     | 17.66             |
| 25              | DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY<br>- [N16000175]                        | 03/2014                          | 3,076.00<br>-                        | 4,190.00                       | 09/2017<br>-                          | 03/2019     | 36.22             |
| 26              | PARADIP HYDERABAD PIPELINE<br>- [N16000194]                                                             | 01/2015                          | 2,321.00<br>-                        | 3,338.00                       | 12/2020<br>-                          | 08/2020     | 43.82             |
|                 | <u>Indian Strategic Petroleum Reserves Ltd</u>                                                          |                                  |                                      |                                |                                       |             |                   |
| 27              | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR<br>- [N16000169]                                           | 01/2006                          | 993.00<br>-                          | 1,693.00                       | 01/2012<br>-                          | -           | 70.49             |
|                 | <u>Mangalore Refinery And Petrochemicals Limited</u>                                                    |                                  |                                      |                                |                                       |             |                   |
| 28              | RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE<br>- [N16000256]                                       | 10/2015                          | 135.00<br>171.00                     | 170.70                         | 03/2019<br>-                          | 03/2019     | 26.44             |
|                 | <u>Oil &amp; Natural Gas Corporation Limited</u>                                                        |                                  |                                      |                                |                                       |             |                   |
| 29              | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)<br>[N16000127]                   | 06/2010                          | 202.94<br>-                          | 330.35                         | 01/2014<br>-                          | 11/2019     | 62.78             |
| 30              | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)<br>[N16000128]                  | 03/2011                          | 861.79<br>-                          | 1,577.15                       | 05/2013<br>-                          | 03/2019     | 83.01             |
| 31              | INTEGRATED DEVELOPMENT OF B-127 FIELDS<br>- [N16000131]                                                 | 12/2011                          | 2,059.63<br>-                        | 2,665.65                       | 03/2015<br>-                          | 12/2019     | 29.42             |
| 32              | LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS<br>[N16000213]                         | 12/2015                          | 3,190.69<br>-                        | 3,247.19                       | 04/2018<br>-                          | 05/2019     | 1.77              |
| 33              | DEVELOPMENT PLAN OF CBM - BOKARO BLOCK<br>- [N16000239]                                                 | 12/2015                          | 658.62<br>-                          | 910.23                         | 03/2023<br>-                          | 03/2022     | 38.20             |
|                 | <u>Oil India Limited</u>                                                                                |                                  |                                      |                                |                                       |             |                   |
| 34              | SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN<br>- [N16000167] | 07/2011                          | 352.56<br>-                          | 438.84                         | 03/2017<br>-                          | 06/2019     | 24.47             |
| 35              | UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE<br>- [N18000148] | 09/2012                          | 871.35<br>-                          | 1,200.00                       | 03/2015<br>-                          | -           | 37.72             |
|                 | <b>Total</b>                                                                                            |                                  | 20,537.74<br>-                       | 26,814.72                      |                                       |             |                   |
|                 |                                                                                                         |                                  |                                      |                                |                                       |             |                   |
|                 | <u>POWER</u>                                                                                            |                                  |                                      |                                |                                       |             |                   |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (December 2018) |                                                                             |                                  |                                      |                                |                                       |             |                   |
|-----------------|-----------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                 |                                                                             |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No            | Project                                                                     | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1               | 2                                                                           | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
|                 | <u>National Hydro-Electric Power Corporation</u>                            |                                  |                                      |                                |                                       |             |                   |
| 36              | PARBATI HEP (4X200 MW) (NHPC) II<br>- [N180100210]                          | 09/2002                          | 3,919.59<br>-                        | 9,394.80                       | 09/2009<br>-                          | 12/2021     | 139.69            |
| 37              | SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)<br>- [N180100221]                   | 09/2003                          | 6,285.33<br>-                        | 19,496.34                      | 09/2010<br>-                          | -           | 210.19            |
|                 | <u>National Thermal Power Corporation</u>                                   |                                  |                                      |                                |                                       |             |                   |
| 38              | GADARWARA SUPER THERMAL POWER PROJECT<br>STAGE-I - [N18000151]              | 03/2013                          | 11,638.55<br>-                       | 12,865.92                      | 09/2017<br>-                          | 06/2019     | 10.55             |
| 39              | TAPOVAN-VISHNUGAD HEP (4X130MW)<br>- [N18000014]                            | 11/2006                          | 2,978.48<br>-                        | 3,846.30                       | 03/2013<br>-                          | 12/2020     | 29.14             |
| 40              | BONGAIGAON THERMAL POWER PROJECT<br>- [N18000041]                           | 01/2008                          | 4,375.35<br>-                        | 8,150.00                       | 09/2011<br>-                          | 01/2019     | 86.27             |
| 41              | DARLIPALLI STPP STAGE-I (2X800 MW)<br>- [N18000176]                         | 02/2014                          | 12,532.44<br>-                       | 13,740.53                      | 08/2018<br>-                          | 06/2019     | 9.64              |
| 42              | NORTH KARANPURA STPP (3X660 MW)<br>- [N18000177]                            | 02/2014                          | 14,366.58<br>-                       | 15,164.05                      | 02/2019<br>-                          | 10/2020     | 5.55              |
| 43              | BRBCL-NABINAGAR TPP- JV (4X250 MW)<br>- [N18000190]                         | 01/2007                          | 5,353.00<br>-                        | 7,998.00                       | 05/2014<br>-                          | 05/2019     | 49.41             |
| 44              | NPGCPL-NABINAGAR STPP - JV (3X660 MW)<br>- [N18000192]                      | 01/2013                          | 12,964.60<br>-                       | 13,731.26                      | 01/2018<br>-                          | 05/2020     | 5.91              |
| 45              | BARH STPP(3X660MW) NTPC<br>- [N180100242]                                   | 02/2005                          | 8,692.97<br>-                        | 15,095.67                      | 01/2011<br>-                          | 04/2021     | 73.65             |
| 46              | KUDGI STPP STAGE 1<br>- [N18000131]                                         | 01/2012                          | 15,166.19<br>-                       | 16,934.65                      | 01/2017<br>-                          | -           | 11.66             |
| 47              | LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X<br>800 MW) - [N18000140]      | 12/2012                          | 11,846.00<br>-                       | 12,739.82                      | 06/2017<br>-                          | 06/2019     | 7.55              |
| 48              | LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT<br>3X57 MW - [N18000142]          | 07/2012                          | 1,527.00<br>-                        | 1,801.07                       | 08/2017<br>-                          | -           | 17.95             |
| 49              | KHARGONE STPP STAGE I (1320 MW)<br>- [N18000205]                            | 03/2015                          | 9,870.51<br>-                        | 11,148.86                      | 09/2019<br>-                          | 09/2019     | 12.95             |
| 50              | PAKRI BARWADIH COAL MINING PROJECT<br>- [N18000225]                         | 10/2004                          | 4,237.96<br>4,238.00                 | 4,552.00                       | 10/2017<br>-                          | -           | 7.41              |
|                 | <u>North East Electric Power Corporation</u>                                |                                  |                                      |                                |                                       |             |                   |
| 51              | KAMENG HYDROELECTRIC PROJECT (NEEPCO)<br>- [N180100239]                     | 12/2004                          | 2,496.90<br>-                        | 6,179.96                       | 12/2009<br>06/2016                    | 03/2019     | 147.51            |
| 52              | TRIPURA GAS BASED POWER PROJECT<br>- [N18000071]                            | 07/2009                          | 421.01<br>-                          | 1,078.31                       | 07/2013<br>-                          | -           | 156.12            |
|                 | <u>Power Grid Corporation Of India Limited</u>                              |                                  |                                      |                                |                                       |             |                   |
| 53              | WESTERN REGION STRENGTHENING SCHEME-V<br>- [N18000035]                      | 12/2007                          | 477.69<br>-                          | 738.48                         | 09/2010<br>-                          | 02/2019     | 54.59             |
| 54              | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA<br>POWER PROJECT - [N18000061] | 10/2008                          | 4,824.12<br>-                        | 5,071.94                       | 10/2012<br>-                          | 06/2019     | 5.14              |
| 55              | NORTH- EAST NORTH WESTERN INTERCONNECTOR I<br>PROJECT - [N18000066]         | 02/2009                          | 11,130.19<br>-                       | 13,762.80                      | 08/2013<br>-                          | 03/2022     | 23.65             |
| 56              | EASTERN REGION STRENGTHENING SCHEME-V<br>- [N18000155]                      | 10/2013                          | 1,364.52<br>-                        | 1,891.41                       | 04/2016<br>-                          | 02/2019     | 38.61             |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (December 2018) |                                                                                                                    |                                  |                                      |                                |                                       |             |                   |
|-----------------|--------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                 |                                                                                                                    |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No            | Project                                                                                                            | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1               | 2                                                                                                                  | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 57              | EASTERN REGION STRENGTHENING SCHEME-XII<br>- [N18000164]                                                           | 05/2014                          | 522.29<br>-                          | 550.18                         | 11/2016<br>-                          | 06/2019     | 5.34              |
| 58              | AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B<br>- [N18000165]                                          | 03/2014                          | 155.57<br>-                          | 206.42                         | 03/2016<br>-                          | 02/2019     | 32.69             |
| 59              | EASTERN REGION STRENGTHENING SCHEME -IX<br>- [N18000171]                                                           | 02/2014                          | 196.58<br>-                          | 225.28                         | 02/2016<br>-                          | 03/2019     | 14.60             |
| 60              | TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP<br>- [N18000180]                                              | 01/2015                          | 268.80<br>-                          | 340.88                         | 03/2018<br>-                          | 02/2019     | 26.82             |
| 61              | SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII<br>- [N18000182]                                                   | 01/2015                          | 203.28<br>-                          | 260.03                         | 07/2017<br>-                          | 06/2019     | 27.92             |
| 62              | COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103] | 09/2011                          | 1,940.13<br>-                        | 2,702.65                       | 09/2014<br>-                          | -           | 39.30             |
| 63              | SYSTEM STRENGTHENING XIII OF SR GRID<br>- [N18000109]                                                              | 10/2011                          | 487.49<br>-                          | 639.46                         | 06/2014<br>-                          | 03/2019     | 31.17             |
| 64              | SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV<br>- [N18000115]                                                     | 12/2011                          | 297.33<br>-                          | 534.02                         | 08/2014<br>-                          | 02/2019     | 79.61             |
| 65              | KUNADANKULAM APP TRANS SYSTEM (PGCIL)<br>- [180100258]                                                             | 05/2005                          | 1,779.29<br>-                        | 2,187.32                       | 11/2008<br>-                          | 03/2019     | 22.93             |
| 66              | COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]    | 03/2013                          | 2,514.88<br>-                        | 3,190.27                       | 12/2015<br>-                          | -           | 26.86             |
| 67              | TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT<br>- [N18000215]        | 01/2014                          | 1,788.41<br>-                        | 2,333.71                       | 09/2017<br>-                          | 11/2018     | 30.49             |
| 68              | ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS<br>- [N18000222]                                              | 04/2016                          | 790.13<br>-                          | 790.30                         | 06/2019<br>-                          | 06/2019     | .02               |
| 69              | COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P<br>- [N18000249]     | 12/2014                          | 4,754.42<br>-                        | 9,141.97                       | 12/2018<br>-                          | 12/2019     | 92.28             |
| 70              | NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES<br>- [N18000250]                | 12/2014                          | 5,111.33<br>-                        | 6,652.57                       | 12/2018<br>-                          | 12/2019     | 30.15             |
| 71              | 400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV)<br>- [N18000270]                                          | 08/2008                          | 771.00<br>-                          | 1,624.00                       | 02/2013<br>-                          | 12/2018     | 110.64            |
|                 | <u>Satluj Jal Vidyut Nigam Limited</u>                                                                             |                                  |                                      |                                |                                       |             |                   |
| 72              | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT<br>- [N18000194]                                  | 05/2015                          | 436.68<br>-                          | 602.44                         | 12/2016<br>-                          | 03/2019     | 37.96             |
|                 | <u>Thdc India Limited</u>                                                                                          |                                  |                                      |                                |                                       |             |                   |
| 73              | DHUKWAN SMALL HYDRO PROJECT<br>- [N18000189]                                                                       | 05/2011                          | 195.42<br>-                          | 294.60                         | 02/2014<br>-                          | 03/2019     | 50.75             |
| 74              | VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT<br>- [N18000042]                                                        | 08/2008                          | 2,491.58<br>-                        | 4,105.30                       | 06/2013<br>-                          | 12/2021     | 64.77             |
| 75              | TEHRI PUMPED STORAGE PLANT(1000MW)<br>- [N18000010]                                                                | 07/2006                          | 1,657.00<br>-                        | 4,401.90                       | 02/2016<br>-                          | 05/2021     | 165.65            |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (December 2018) |                                                                   |                                  |                                      |                                |                                       |             |                   |
|-----------------|-------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                 |                                                                   |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No            | Project                                                           | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated<br>Cost (Rs.crore) | Original/<br>Revised                  | Anticipated | Cost Overruns (%) |
| 1               | 2                                                                 | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
|                 | Total                                                             |                                  | 1,72,830.59                          | 2,36,165.47                    |                                       |             |                   |
|                 |                                                                   |                                  |                                      |                                |                                       |             |                   |
|                 | <u>RAILWAYS</u>                                                   |                                  |                                      |                                |                                       |             |                   |
|                 | <u>Central Railways</u>                                           |                                  |                                      |                                |                                       |             |                   |
| 76              | 3RD LINE BETWEEN BHUSAVAL-JALGAON<br>- [N22000247                 | 04/2011                          | 184.06                               | 298.70                         | 03/2019                               | 03/2019     | 62.28             |
| 77              | AHMEDNAGAR-PARLI VAIJNATH(NL) CR<br>- [220100181                  | 02/1997                          | 2,271.50                             | 3,712.50                       | 03/2021                               | 03/2021     | 63.44             |
| 78              | AMRAVATI-NARKHER NL(CR)<br>- [220100118                           | 06/1994                          | 663.01<br>175.30                     | 858.96                         | 06/1999                               | -           | 29.55             |
| 79              | PUNE-NASIK (265 KM)<br>- [N22000354                               | 02/2016                          | 2,425.00                             | 5,341.68                       | 03/2024                               | 03/2024     | 120.28            |
| 80              | VAIBHAVWADI -KOLHAPUR (107 KM)<br>- [N22000355                    | 02/2016                          | 2,750.00                             | 3,438.51                       | 03/2024                               | 03/2024     | 25.04             |
| 81              | DAUND - MANMAD (236 KM)<br>- [N22000360                           | 02/2016                          | 1,876.00                             | 2,081.27                       | 03/2023                               | 03/2023     | 10.94             |
|                 | <u>Container Corporation Of India</u>                             |                                  |                                      |                                |                                       |             |                   |
| 82              | MULTI MODAL LOGISTICS PARK AT KAKINADA<br>- [N22000431            | 08/2016                          | 234.50                               | 235.00                         | 03/2019                               | 12/2020     | .21               |
|                 | <u>Dedicated Freight Corridor Corporation Of India Ltd</u>        |                                  |                                      |                                |                                       |             |                   |
| 83              | EASTERN DEDICATED FREIGHT CORRIDOR PROJECT<br>- [N22000346        | 10/2006                          | 11,589.00<br>30,357.00               | 28,181.00                      | -                                     | -           | 143.17            |
| 84              | WESTERN DEDICATED FREIGHT CORRIDOR<br>- [N22000464                | 11/2007                          | 16,592.00<br>51,101.00               | 51,101.00                      | 03/2020                               | 03/2020     | 207.99            |
|                 | <u>East Central Railways</u>                                      |                                  |                                      |                                |                                       |             |                   |
| 85              | KODERMA-RANCHI VIA BARKAKANA (NL), ECR<br>- [220100222            | 03/1999                          | 1,033.07                             | 3,020.94                       | -                                     | 03/2021     | 192.42            |
| 86              | HAIJIPUR-SUGAULI VIA VAISHALI (NL), ECR<br>- [220100303           | 04/2003                          | 528.65                               | 2,066.77                       | -                                     | 03/2023     | 290.95            |
| 87              | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN<br>ECR - [N22000002 | 04/1996                          | 477.88<br>283.95                     | 749.00                         | 03/2012                               | 03/2020     | 56.73             |
| 88              | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR<br>- [220100240        | 04/1997                          | 324.73                               | 1,156.41                       | 03/2012                               | 03/2020     | 256.11            |
| 89              | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)<br>- [220100257             | 04/1997                          | 162.87                               | 589.15                         | -                                     | 03/2022     | 261.73            |
| 90              | KOSI BRIDGE (NL), ECR<br>- [220100304                             | 04/2002                          | 499.41                               | 516.02                         | 03/2020                               | 03/2020     | 3.33              |
| 91              | NAWADA-LAXMIPUR (NL)<br>- [N22000167                              | 04/2008                          | 620.57                               | 2,626.98                       | -                                     | -           | 323.32            |
| 92              | MOTIHARI-SITAMARHI (NL)<br>- [N22000174                           | 04/2006                          | 211.00                               | 926.09                         | -                                     | -           | 338.91            |
| 93              | SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)<br>- [N22000175       | 04/2008                          | 678.62                               | 2,393.23                       | -                                     | -           | 252.66            |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (December 2018)           |                                                                                                                    |                                  |                                      |                                |                                       |             |                   |
|---------------------------|--------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                           |                                                                                                                    |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No                      | Project                                                                                                            | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1                         | 2                                                                                                                  | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 94                        | SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]                               | 04/2004                          | 372.14 -                             | 1,474.47                       | -                                     | 03/2021     | 296.21            |
| 95                        | JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]                                  | 04/2009                          | 548.00 -                             | 785.87                         | 03/2020 -                             | 03/2020     | 43.41             |
| 96                        | HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]                                                                      | 04/2013                          | 213.01 -                             | 367.17                         | -                                     | -           | 72.37             |
| 97                        | MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]                                                                       | 01/1991                          | 332.15 -                             | 559.91                         | 07/2014 -                             | -           | 68.57             |
| 98                        | SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]                                                              | 04/2016                          | 744.04 -                             | 1,215.54                       | 03/2021 -                             | 03/2022     | 63.37             |
| 99                        | MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]                                                              | 04/2016                          | 731.64 -                             | 1,185.73                       | 03/2021 -                             | 03/2022     | 62.06             |
| 100                       | PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]         | 11/2001                          | 624.47 -                             | 3,550.00                       | 02/2016 -                             | 03/2021     | 468.48            |
| 101                       | RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]                                              | 04/1998                          | 180.82 -                             | 528.26                         | -                                     | -           | 192.15            |
| 102                       | FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476] | 04/1991                          | 329.39 -                             | 566.41                         | -                                     | 12/2021     | 71.96             |
| <u>East Coast Railway</u> |                                                                                                                    |                                  |                                      |                                |                                       |             |                   |
| 103                       | TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]                                                                         | 04/2005                          | 810.78 -                             | 1,928.07                       | 06/2021 -                             | 03/2023     | 137.80            |
| 104                       | KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]                                                                         | 04/1994                          | 2,923.13 -                           | 3,798.80                       | 03/2009 -                             | 06/2021     | 29.96             |
| 105                       | SAMBALPUR-TALCHER DOUBLING - [N22000315]                                                                           | 03/2011                          | 1,111.99 -                           | 1,539.28                       | 02/2019 -                             | 03/2021     | 38.43             |
| 106                       | KIRANDUL - JAGDALPUR DOUBLING - [N22000318]                                                                        | 12/2012                          | 1,160.00 -                           | 1,160.83                       | 03/2020 -                             | 03/2020     | .07               |
| 107                       | SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]                                                               | 03/2012                          | 155.81 -                             | 238.03                         | 03/2020 -                             | 03/2020     | 52.77             |
| 108                       | GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]                                                                    | 04/2008                          | 445.25 -                             | 2,860.55                       | -                                     | -           | 542.46            |
| 109                       | GAYA-CHATRA (NL) - [N22000169]                                                                                     | 04/2008                          | 415.67 -                             | 549.75                         | -                                     | -           | 32.26             |
| 110                       | BIHTA-AURANGABAD (NL) - [N22000170]                                                                                | 04/2008                          | 326.20 -                             | 2,995.01                       | -                                     | -           | 818.15            |
| 111                       | SAKRI-HASANPUR ROAD (NL) - [N22000171]                                                                             | 04/1999                          | 325.00 -                             | 729.92                         | -                                     | 03/2021     | 124.59            |
| 112                       | CHHAPRA-MUZAFFARPUR (NL) - [N22000172]                                                                             | 04/2006                          | 378.56 -                             | 2,614.36                       | -                                     | 03/2022     | 590.61            |
| 113                       | JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]                                  | 04/2015                          | 701.61 -                             | 810.02                         | 11/2018 -                             | 03/2021     | 15.45             |
| <u>Eastern Railways</u>   |                                                                                                                    |                                  |                                      |                                |                                       |             |                   |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (December 2018)                              |                                                                                                                          |                                  |                                      |                                |                                       |             |                   |
|----------------------------------------------|--------------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                                              |                                                                                                                          |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No                                         | Project                                                                                                                  | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1                                            | 2                                                                                                                        | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 114                                          | TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER<br>- [220100272                                                              | 04/2000                          | 1,188.91<br>-                        | 1,620.01                       | 03/2019<br>12/2009                    | -           | 36.26             |
| 115                                          | DEOGHAR - SULTANGANJ (INL), ER<br>- [220100273                                                                           | 04/2000                          | 607.09<br>-                          | 607.91                         | 02/2013<br>-                          | -           | .14               |
| 116                                          | DAKSHIN-BARASAL-LAKSHMIKANTAPUR<br>- [N22000116                                                                          | 04/2009                          | 259.51<br>-                          | 533.59                         | 02/2012<br>-                          | -           | 105.61            |
| 117                                          | TARAKESHWAR-MAGRA NEW BG LINE<br>- [N22000235                                                                            | 04/2010                          | 365.17<br>-                          | 527.54                         | -<br>-                                | -           | 44.46             |
| 118                                          | SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-<br>MINAKHAN VIA GHATAKPUR NL<br>[N22000241                                   | 04/2000                          | 297.47<br>-                          | 299.03                         | -<br>-                                | -           | .52               |
| 119                                          | CHANDPARA-BANGAON DOUBLING WITH EXENSION TO<br>CHANDBAZAR AND NEW MM FOR BONGAON-<br>PORAMAHESHTALA AND CHA - [N22000242 | 04/2003                          | 337.96<br>-                          | 355.44                         | -<br>-                                | -           | 5.17              |
| 120                                          | MAGRAHAT-DIAMOND HARBOUR WITH MM<br>SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND<br>HATBOUR - BAHRAHAT-KULPI NL - [N22000243   | 04/2009                          | 499.96<br>-                          | 665.75                         | 02/2012<br>-                          | -           | 33.16             |
| 121                                          | LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-<br>JONGALPARA-FURFURA SHARIF NL<br>[N22000244                                   | 04/2009                          | 257.42<br>-                          | 258.73                         | 03/2014<br>-                          | -           | .51               |
| 122                                          | MONIGRAM- NIMTITA<br>- [N22000301                                                                                        | 04/2012                          | 250.93<br>-                          | 259.23                         | -<br>-                                | -           | 3.31              |
| 123                                          | BAZAR SAU -AZIMGANJ JN. DOUBLING<br>- [N22000302                                                                         | 04/2012                          | 255.64<br>-                          | 272.20                         | -<br>-                                | -           | 6.48              |
| 124                                          | MANDARHILL-DUMKA-RAMPURHAT (NL),ER<br>- [220100168                                                                       | 04/1995                          | 1,125.89<br>-                        | 1,126.36                       | 03/2016<br>-                          | 03/2020     | .04               |
| 125                                          | GHUTIASHARIF-CANNING (ER)<br>- [N22000117                                                                                | 04/2009                          | 193.08<br>-                          | 612.45                         | 12/2011<br>-                          | -           | 217.20            |
| 126                                          | LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM<br>FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-<br>BUDAKHALI AND CHANDRANAG - [N22000216 | 04/1987                          | 406.99<br>-                          | 544.72                         | 03/2006<br>-                          | -           | 33.84             |
| 127                                          | HANSNABAD-HINGALGANJ NEW BG LINE<br>- [N22000218                                                                         | 04/2010                          | 172.03<br>-                          | 260.10                         | -<br>-                                | -           | 51.19             |
| 128                                          | PIRPAINTI-BHAGALPUR<br>- [N22000222                                                                                      | 04/2011                          | 261.38<br>-                          | 332.14                         | -<br>-                                | -           | 27.07             |
| 129                                          | KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW<br>MM FOR RANAGHAT-DUTTAPHULIA NEW LINE<br>- [N22000227                       | 04/2010                          | 174.56<br>-                          | 175.99                         | -<br>-                                | -           | .82               |
| <u>Metropolitan Rapid Transport Projects</u> |                                                                                                                          |                                  |                                      |                                |                                       |             |                   |
| 130                                          | TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-<br>NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)<br>- [220100268                      | 03/2000                          | 1,049.69<br>-                        | 3,404.92                       | 12/2006<br>-                          | -           | 224.37            |
| 131                                          | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE<br>LINE(MTP)<br>- [220100164                                                     | 03/1996                          | 495.44<br>-                          | 1,781.98                       | 03/2004<br>-                          | 03/2020     | 259.68            |
| 132                                          | EXTENSION OF MRTS FROM VELACHERY TO STN.<br>THOMAS, MTP<br>- [N22000028                                                  | 04/2006                          | 495.74<br>-                          | 734.01                         | 06/2013<br>-                          | 03/2019     | 48.06             |
| 133                                          | MUMBAI URBAN TRANSPORT PROJECT PHASE-II<br>- [N22000092                                                                  | 04/2008                          | 5,300.00<br>-                        | 7,986.04                       | 03/2014<br>-                          | 03/2019     | 50.68             |



## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (December 2018) |                                                                                       |                               |                                   |                             |                                    |             |                   |
|-----------------|---------------------------------------------------------------------------------------|-------------------------------|-----------------------------------|-----------------------------|------------------------------------|-------------|-------------------|
|                 |                                                                                       |                               |                                   |                             | Date of Commissioning (Month/Year) |             |                   |
| S.No            | Project                                                                               | Date of Approval (Month/Year) | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised                  | Anticipated | Cost Overruns (%) |
| 1               | 2                                                                                     | 3                             | 4                                 | 5                           | 6                                  | 7           | 8                 |
|                 | <u>North Central Railway</u>                                                          |                               |                                   |                             |                                    |             |                   |
| 134             | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)<br>- [220100007                     | 04/1986                       | 158.77<br>274.56                  | 634.48                      | 03/1994<br>-                       | -           | 299.62            |
| 135             | ETAWAH-MAINPURI (NL),NCR<br>- [220100318                                              | 04/1997                       | 120.00<br>-                       | 245.39                      | 12/2008<br>-                       | -           | 104.49            |
| 136             | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR<br>- [220100243                            | 04/1999                       | 108.00<br>-                       | 432.72                      | 12/2009<br>-                       | -           | 300.67            |
| 137             | GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)<br>- [N22000148                        | 04/2011                       | 2,912.96<br>-                     | 3,845.60                    | 03/2022<br>-                       | 03/2022     | 32.02             |
|                 | <u>North East Frontier Railway</u>                                                    |                               |                                   |                             |                                    |             |                   |
| 138             | NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR<br>[220100135 | 04/1983                       | 297.32<br>-                       | 614.00                      | 03/2019<br>-                       | 03/2020     | 106.51            |
| 139             | KATIHAR - JOGBANI (GC)(NEFR)<br>- [220100247                                          | 09/2001                       | 792.46<br>-                       | 1,320.00                    | 12/2010<br>-                       | -           | 66.57             |
| 140             | BHAIRABI SAIRONG, NL, NEFR<br>- [N22000100                                            | 04/2008                       | 2,393.47<br>-                     | 4,968.00                    | 03/2014<br>-                       | 12/2020     | 107.56            |
| 141             | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR<br>- [220100266                | 04/2000                       | 1,180.19<br>-                     | 3,040.00                    | 12/2008<br>-                       | 03/2019     | 157.59            |
| 142             | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)<br>- [220100288                                   | 04/2003                       | 4,454.17<br>-                     | 13,809.00                   | 03/2011<br>-                       | 03/2020     | 210.02            |
| 143             | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR<br>- [N22000086       | 09/2006                       | 385.20<br>-                       | 1,532.00                    | 03/2019<br>-                       | 03/2020     | 297.72            |
| 144             | NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR<br>[N22000087                | 09/2006                       | 532.87<br>-                       | 2,145.00                    | 03/2019<br>-                       | 03/2020     | 302.54            |
| 145             | NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)<br>[N22000124          | 04/2006                       | 2,326.52<br>-                     | 3,000.00                    | 03/2015<br>-                       | 10/2021     | 28.95             |
| 146             | AGARTALA SABROOM, NL, NEFR<br>- [N22000099                                            | 04/2008                       | 1,142.00<br>-                     | 3,407.00                    | 03/2014<br>-                       | 03/2019     | 198.34            |
| 147             | KISHANGANJ JALALGARH, NL, NEFR<br>- [N22000101                                        | 04/2008                       | 333.76<br>-                       | 360.00                      | -<br>-                             | 03/2020     | 7.86              |
| 148             | SEVOK RANGPO, NEFR<br>- [N22000102                                                    | 04/2008                       | 1,339.48<br>-                     | 4,084.69                    | 12/2015<br>-                       | 03/2020     | 204.95            |
| 149             | NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR<br>- [N22000193                              | 04/2010                       | 221.42<br>-                       | 380.00                      | -<br>-                             | 03/2020     | 71.62             |
| 150             | CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA<br>- [N22000194                            | 04/1999                       | 895.00<br>-                       | 1,733.20                    | 03/2007<br>-                       | 04/2016     | 93.65             |
| 151             | AGARTALA-AKHAURA NL<br>- [N22000195                                                   | 04/2012                       | 569.63<br>-                       | 650.00                      | 03/2020<br>-                       | 10/2022     | 14.11             |
| 152             | NEW BG LINE FROM BYRNIHAT TO SHILLONG<br>- [N22000205                                 | 04/2010                       | 906.46<br>-                       | 6,000.00                    | 03/2021<br>-                       | 03/2021     | 561.92            |
| 153             | NEW BG LINE FROM BALURGHAT TO HILLY NFR<br>- [N22000206                               | 04/2010                       | 242.22<br>-                       | 471.00                      | 03/2020<br>-                       | 03/2020     | 94.45             |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (December 2018)              |                                                                                                                       |                                  |                                      |                                |                                       |             |                   |
|------------------------------|-----------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                              |                                                                                                                       |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No                         | Project                                                                                                               | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1                            | 2                                                                                                                     | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 154                          | NEW BG LINE FROM JAGBANI TO BIRATNAGAR<br>- [N22000207]                                                               | 04/2010                          | 241.52<br>-                          | 394.28                         | -<br>-                                | -           | 63.25             |
| 155                          | MURKONGSELEK-PASIGHAT NL<br>- [N22000208]                                                                             | 04/2011                          | 414.84<br>-                          | 661.00                         | 03/2020<br>-                          | 03/2020     | 59.34             |
| 156                          | NEW JALPAIGURI SILIGURI NEW BONGAIGAON<br>INCLUDING BR LINE AND MM CHALSA NAXAL<br>RAJABHATKHOWA JAINTI - [N22000209] | 04/1999                          | 819.23<br>-                          | 1,871.00                       | -<br>-                                | -           | 128.39            |
| 157                          | AMBARI FALAKATA TO NEW MAYNAGURI<br>- [N22000210]                                                                     | 04/2011                          | 314.00<br>-                          | 551.00                         | 03/2019<br>-                          | 03/2019     | 75.48             |
| 158                          | LUMDING-HOJAI PATCH DOUBLING PROJECT<br>- [N22000211]                                                                 | 04/2012                          | 246.07<br>-                          | 398.93                         | 03/2019<br>-                          | 03/2019     | 62.12             |
| 159                          | NEW MAYNAGURI-GUMANIHAT-DOUBLING OF<br>REMAINING PORTION (51.65 KM)<br>[N22000390]                                    | 04/2016                          | 602.27<br>-                          | 612.00                         | 12/2021<br>-                          | 03/2020     | 1.62              |
| <u>North Eastern Railway</u> |                                                                                                                       |                                  |                                      |                                |                                       |             |                   |
| 160                          | MAHARAJGANJ-MASRAKH (NL) - NER<br>- [220100316]                                                                       | 04/2003                          | 218.19<br>-                          | 413.56                         | 06/2018<br>-                          | 10/2018     | 89.54             |
| 161                          | KICHHA-KHATIMA (NL) - NER<br>- [220100317]                                                                            | 04/2003                          | 142.45<br>-                          | 228.40                         | -<br>-                                | -           | 60.34             |
| 162                          | HATHUA-BHATNI (N L) (NER)<br>- [220100319]                                                                            | 04/2005                          | 230.03<br>-                          | 770.08                         | 12/2022<br>-                          | 05/2019     | 234.77            |
| 163                          | KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)<br>- [220100256]                                                              | 04/1999                          | 744.71<br>-                          | 1,126.79                       | -<br>-                                | -           | 51.31             |
| 164                          | GHAZIPUR - AUNRIHAR (40 KM)<br>- [N22000321]                                                                          | 04/2014                          | 182.92<br>-                          | 197.73                         | -<br>-                                | -           | 8.10              |
| 165                          | ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP<br>- [N22000130]                                                               | 03/2013                          | 307.00<br>-                          | 308.00                         | -<br>-                                | -           | .33               |
| 166                          | CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ<br>UP - [N22000131]                                                       | 03/2007                          | 243.78<br>-                          | 895.00                         | 12/2021<br>-                          | 12/2021     | 267.13            |
| 167                          | BHOJIPUR TANAKPUR VIA PILIBHIT<br>- [N22000132]                                                                       | 03/2008                          | 195.64<br>-                          | 435.00                         | -<br>-                                | 03/2018     | 122.35            |
| 168                          | AUNRIHAR MANDUADIH GAZIPUR VARANASI UP<br>- [N22000133]                                                               | 03/2012                          | 199.75<br>-                          | 270.00                         | 08/2018<br>-                          | 01/2019     | 35.17             |
| 169                          | CHHAPRA-BALLIA UP<br>- [N22000134]                                                                                    | 03/2013                          | 295.00<br>-                          | 477.31                         | 01/2019<br>-                          | 02/2019     | 61.80             |
| 170                          | KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI<br>NAUGARH UP - [N22000136]                                           | 03/2013                          | 643.00<br>-                          | 644.00                         | -<br>-                                | -           | .16               |
| 171                          | GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-<br>SITAPUR-LUCKNOW - [N22000455]                                       | 04/1997                          | 233.00<br>-                          | 318.42                         | 04/1999<br>-                          | -           | 36.66             |
| 172                          | INDARA - DOHRIGHAT GAUGE CONVERSION.<br>- [N22000456]                                                                 | 04/2016                          | 213.00<br>-                          | 213.35                         | 04/2016<br>-                          | 01/2022     | .16               |
| 173                          | MANDHANA - BRAHMAWART NEW LINE PROJECT.<br>- [N22000458]                                                              | 04/1997                          | 609.04<br>1,063.00                   | 1,807.88                       | 04/1999<br>-                          | 03/2019     | 196.84            |
| 174                          | BURHWAL - GONDA - 3RD RUNNING LINE.<br>- [N22000468]                                                                  | 04/2016                          | 602.50<br>-                          | 714.34                         | -<br>-                                | -           | 18.56             |
| <u>North Western Railway</u> |                                                                                                                       |                                  |                                      |                                |                                       |             |                   |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (December 2018)         |                                                                                    |                                  |                                      |                                |                                       |             |                   |
|-------------------------|------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                         |                                                                                    |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No                    | Project                                                                            | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1                       | 2                                                                                  | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 175                     | JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)<br>- [N22000113] | 04/2008                          | 653.19<br>-                          | 1,116.00                       | 03/2014<br>-                          | 03/2019     | 70.85             |
| 176                     | DAUSA-GANGAPUR CITY(NL),NWR<br>- [220100184]                                       | 02/1997                          | 410.08<br>-                          | 795.01                         | 02/2019<br>-                          | 02/2019     | 93.87             |
| 177                     | PHULERA - DIGANA DOUBLING<br>- [N22000326]                                         | 05/2015                          | 600.00<br>-                          | 685.99                         | 03/2020<br>-                          | 03/2020     | 14.33             |
| 178                     | AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL<br>- [N22000330]  | 05/2015                          | 873.71<br>-                          | 1,103.04                       | -<br>-                                | -           | 26.25             |
| 179                     | HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)<br>- [N22000112]                      | 04/2008                          | 829.74<br>-                          | 1,216.00                       | 03/2015<br>-                          | 06/2020     | 46.55             |
| 180                     | BANGURGRAM-GURIYA PATCH DOUBLING<br>- [N22000137]                                  | 04/2012                          | 246.08<br>-                          | 348.55                         | 12/2019<br>-                          | 06/2019     | 41.64             |
| 181                     | RATLAM-DUNGARPUR VIA BANSWARA (NL)<br>- [N22000147]                                | 04/2011                          | 2,082.75<br>-                        | 2,878.97                       | -<br>-                                | -           | 38.23             |
| 182                     | THIYAT HAMIRA-SANU<br>- [N22000149]                                                | 04/2013                          | 236.93<br>-                          | 294.90                         | 10/2018<br>-                          | 10/2018     | 24.47             |
| 183                     | AJMER-KOTA (NASIRABAD-JAUNDRI)<br>- [N22000150]                                    | 04/2013                          | 822.00<br>-                          | 1,099.54                       | -<br>-                                | -           | 33.76             |
| 184                     | PUSHKAR-MERTA<br>- [N22000151]                                                     | 04/2013                          | 323.00<br>-                          | 432.22                         | -<br>-                                | -           | 33.81             |
| 185                     | AJMER-BANGURGRAM<br>- [N22000155]                                                  | 04/2011                          | 213.39<br>-                          | 244.02                         | 11/2019<br>-                          | 11/2019     | 14.35             |
| 186                     | ALWAR-BANDIKUI DOUBLING<br>- [N22000157]                                           | 04/2013                          | 242.09<br>-                          | 349.00                         | 02/2019<br>-                          | 03/2019     | 44.16             |
| <b>Northern Railway</b> |                                                                                    |                                  |                                      |                                |                                       |             |                   |
| 187                     | JIND-SONEPAT (NL),NR<br>- [220100280]                                              | 01/2004                          | 238.56<br>-                          | 740.00                         | 03/2012<br>-                          | -           | 210.19            |
| 188                     | GRADE SEPERATOR AT DAYABASTI<br>- [N22000269]                                      | 04/1999                          | 156.65<br>-                          | 197.17                         | -<br>-                                | -           | 25.87             |
| 189                     | ROHTAK-MEHAM HANSI<br>- [N22000272]                                                | 04/2012                          | 287.00<br>-                          | 625.00                         | 12/2011<br>-                          | -           | 117.77            |
| 190                     | HARIDWAR-LAKSAR<br>- [N22000289]                                                   | 04/2012                          | 219.83<br>-                          | 346.63                         | -<br>-                                | -           | 57.68             |
| 191                     | CHANDIGARH-BADDI NL<br>- [N22000296]                                               | 04/2007                          | 328.14<br>-                          | 1,540.00                       | -<br>-                                | -           | 369.31            |
| 192                     | NANGALDAM-TALWARA(NL),NR<br>- [220100188]                                          | 03/1981                          | 450.00<br>-                          | 2,100.00                       | 07/2012<br>-                          | -           | 366.67            |
| 193                     | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR<br>- [220100133]                               | 03/1995                          | 2,500.00<br>-                        | 27,949.00                      | 11/2002<br>-                          | 03/2021     | 1,017.96          |
| 194                     | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR<br>- [220100258]                            | 03/2002                          | 625.30<br>408.76                     | 876.10                         | 06/2007<br>-                          | -           | 40.11             |
| 195                     | UTRATIA-ZAFRABAD, NR (LINE DOUBLING)<br>- [N22000088]                              | 04/2006                          | 369.90<br>-                          | 1,581.53                       | 03/2010<br>-                          | -           | 327.56            |
| 196                     | CHANDIGARH-BADDI<br>- [N22000467]                                                  | 04/2007                          | 328.14<br>-                          | 1,540.00                       | 03/2023<br>-                          | 03/2023     | 369.31            |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (December 2018) |                                                                                                                  |                                  |                                      |                                |                                       |             |                   |
|-----------------|------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                 |                                                                                                                  |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No            | Project                                                                                                          | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1               | 2                                                                                                                | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 197             | JALANDHAR-PATHANKOT-JAMMU TAWI<br>- [N22000492<br><u>Rail Vikas Nigam Ltd.</u>                                   | 03/2002                          | 625.00<br>-                          | 845.58                         | 03/2016<br>-                          | -           | 35.29             |
| 198             | HARIDASPUR-PARADEEP(NL)<br>- [220100285                                                                          | 04/1996                          | 1,185.64<br>-                        | 1,844.47                       | 12/2017<br>-                          | 03/2020     | 55.57             |
| 199             | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)<br>- [220100327                                                        | 04/2000                          | 133.41<br>207.00                     | 385.00                         | 03/2009<br>03/2009                    | 02/2019     | 188.58            |
| 200             | OBULAVARIPALLE-KRISHNAPATNAM(RVNL)<br>- [N22000049                                                               | 07/2006                          | 732.81<br>-                          | 1,850.00                       | 03/2008<br>-                          | 03/2020     | 152.45            |
| 201             | BHANUPALI-BILASPUR BERI NL<br>- [N22000273                                                                       | 04/2008                          | 2,966.99<br>-                        | 7,000.00                       | 12/2026<br>-                          | 12/2026     | 135.93            |
| 202             | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL<br>- [220100149                                 | 04/1995                          | 631.78<br>-                          | 1,195.00                       | 12/2012<br>-                          | 03/2022     | 89.15             |
| 203             | SALKA ROAD -ANUPNAGAR LINE DOUBLING<br>- [N22000075                                                              | 09/2006                          | 383.54<br>-                          | 555.00                         | 03/2010<br>-                          | 12/2019     | 44.70             |
| 204             | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)<br>- [N22000110     | 04/2010                          | 3,951.98<br>-                        | 4,259.48                       | 03/2016<br>-                          | 03/2025     | 7.78              |
| 205             | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)<br>- [N22000109 | 04/2010                          | 2,298.42<br>-                        | 2,733.86                       | 03/2014<br>-                          | 12/2025     | 18.95             |
| 206             | MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD<br>- [N22000213                                            | 04/2012                          | 632.68<br>-                          | 816.55                         | 03/2016<br>-                          | 12/2020     | 29.06             |
| 207             | VIJAYAWADA-GUDUR<br>- [N22000369                                                                                 | 04/2015                          | 3,246.26<br>-                        | 3,548.67                       | 12/2023<br>-                          | 12/2023     | 9.32              |
| 208             | LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC<br>- [N22000404                                                      | 04/2011                          | 927.01<br>-                          | 977.00                         | 03/2019<br>-                          | 03/2020     | 5.39              |
| 209             | DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)<br>- [N22000407              | 03/2009                          | 713.48<br>-                          | 1,750.00                       | 03/2020<br>-                          | 03/2020     | 145.28            |
| 210             | SAMBALPUR - TITLAGARH - DOUBLING<br>- [N22000410<br><u>Railway Electrification</u>                               | 03/2006                          | 948.04<br>-                          | 970.00                         | 03/2020<br>-                          | 03/2020     | 2.32              |
| 211             | ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT<br>- [N22000094<br><u>South Central Railway</u>     | 02/2008                          | 171.10<br>-                          | 275.08                         | 03/2012<br>-                          | -           | 60.77             |
| 212             | KOTPALI-NARASAPUR (NL) (SCR)<br>- [220100265                                                                     | 12/2001                          | 1,045.20<br>-                        | 2,120.16                       | 03/2009<br>-                          | 03/2023     | 102.85            |
| 213             | MANUGURU-RAMAGUNDAM<br>- [N22000259                                                                              | 04/2013                          | 1,112.00<br>-                        | 2,911.84                       | -<br>-                                | -           | 161.86            |
| 214             | KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION<br>- [N22000261                                                 | 04/2012                          | 1,856.95<br>-                        | 2,200.00                       | 03/2023<br>-                          | 03/2024     | 18.47             |
| 215             | BHADRACHALAM-KOVVUR<br>- [N22000264                                                                              | 04/2012                          | 923.23<br>-                          | 1,787.00                       | -<br>-                                | -           | 93.56             |
| 216             | CUMBUM-PRODDATUR<br>- [N22000282                                                                                 | 04/2013                          | 829.00<br>-                          | 1,599.39                       | -<br>-                                | -           | 92.93             |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (December 2018) |                                                                                                                           |                                  |                                      |                                |                                       |             |                   |
|-----------------|---------------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                 |                                                                                                                           |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No            | Project                                                                                                                   | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1               | 2                                                                                                                         | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 217             | NANDYAL-YERRAGUNTALA(NL),SCR<br>- [220100192]                                                                             | 03/1996                          | 164.36<br>-                          | 1,050.00                       | 02/2009<br>-                          | -           | 538.84            |
| 218             | MACHERLA-NALGONDA(NL)(SCR)<br>- [220100220]                                                                               | 07/1998                          | 458.25<br>-                          | 458.26                         | -<br>-                                | -           | .00               |
| 219             | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)<br>- [220100106]                                                                   | 12/1994                          | 124.43<br>-                          | 1,025.00                       | -<br>-                                | -           | 723.76            |
| 220             | MANMAD-PARBHANI-NANDED-SECUNDERABAD-<br>GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION<br>AVOIDANCE SYSTEM (958 K - [N22000432] | 04/2017                          | 119.73<br>185.00                     | 184.97                         | 03/2022<br>-                          | 03/2022     | 54.49             |
|                 | <u>South East Central Railway</u>                                                                                         |                                  |                                      |                                |                                       |             |                   |
| 221             | CHHINDWARA - NAGPUR (GC)(SECR)<br>- [220100324]                                                                           | 04/2005                          | 383.79<br>-                          | 1,101.16                       | -<br>-                                | -           | 186.92            |
| 222             | GONDIA-JABALPUR(GC),(SECR)<br>- [220100186]                                                                               | 02/1997                          | 511.86<br>-                          | 1,756.00                       | 04/2020<br>-                          | 04/2020     | 243.06            |
| 223             | RAJNANDGAON - NAGPUR - 3RD LINE (SECR)<br>- [N22000420]                                                                   | 09/2016                          | 1,908.51<br>-                        | 2,686.63                       | 03/2023<br>-                          | 03/2023     | 40.77             |
| 224             | CHHINDWARA NAINPUR MANDLA FORT GAUGE<br>CONVERSION PROJECT<br>[N22000438]                                                 | 04/2010                          | 585.93<br>-                          | 1,420.39                       | 02/2019<br>-                          | 02/2019     | 142.42            |
| 225             | WADSA-GADHCHIROLI NEW LINE (52.36 KM)<br>- [N22000480]                                                                    | 06/2018                          | 229.00<br>-                          | 403.00                         | 12/2021<br>-                          | 12/2021     | 75.98             |
| 226             | CHHINDWARA-MANDLA FORT GC<br>- [N22000481]                                                                                | 03/2011                          | 556.54<br>-                          | 1,342.46                       | 03/2012<br>-                          | 03/2020     | 141.22            |
| 227             | CHAMPA-JHARSUGUDA 3RD LINE<br>- [N22000483]                                                                               | 04/2008                          | 872.00<br>-                          | 1,279.00                       | 12/2019<br>-                          | 12/2019     | 46.67             |
| 228             | GEVRA ROAD PENDRA ROAD<br>- [N22000488]                                                                                   | 02/2014                          | 2,288.00<br>-                        | 4,919.00                       | 03/2022<br>-                          | 03/2022     | 114.99            |
|                 | <u>South Eastern Railway</u>                                                                                              |                                  |                                      |                                |                                       |             |                   |
| 229             | MM FROM BURAMARA-CHAKULIA<br>- [N22000305]                                                                                | 04/2008                          | 466.48<br>-                          | 1,000.00                       | -<br>-                                | 12/2024     | 114.37            |
| 230             | MM FROM PANSKURA-GHATAL NL<br>- [N22000309]                                                                               | 04/2011                          | 276.69<br>-                          | 426.00                         | -<br>-                                | 03/2030     | 53.96             |
| 231             | HOWRAH-AMTA-CHAMPADANGA NL (SER)<br>- [220100208]                                                                         | 04/1974                          | 393.46<br>154.30                     | 1,026.00                       | 03/2007<br>03/2007                    | -           | 160.76            |
| 232             | TAMLUK DIGHA,LINE DOUBLING (SER)<br>- [N22000097]                                                                         | 03/1984                          | 293.97<br>-                          | 749.69                         | 06/2005<br>-                          | -           | 155.02            |
| 233             | RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM)<br>JHARKHAND<br>- [N22000323]                                                 | 04/2012                          | 148.77<br>-                          | 377.00                         | 12/2016<br>-                          | 09/2019     | 153.41            |
| 234             | BOWAICHANDI-ARAMBAGH<br>- [N22000159]                                                                                     | 04/2010                          | 267.37<br>-                          | 620.00                         | -<br>-                                | 03/2025     | 131.89            |
| 235             | DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA<br>- [N22000160]                                                               | 04/2010                          | 651.00<br>-                          | 1,009.00                       | 03/2015<br>-                          | 03/2024     | 54.99             |
| 236             | BHADUTOLA-JHARGRAM VIA LALGARH (NL)<br>- [N22000161]                                                                      | 04/2011                          | 289.64<br>-                          | 760.00                         | -<br>-                                | -           | 162.39            |
| 237             | CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION<br>- [N22000162]                                                                | 04/2010                          | 149.90<br>-                          | 230.00                         | 03/2015<br>-                          | -           | 53.44             |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (December 2018)              |                                                                                                                    |                               |                                   |                             |                                    |             |                   |
|------------------------------|--------------------------------------------------------------------------------------------------------------------|-------------------------------|-----------------------------------|-----------------------------|------------------------------------|-------------|-------------------|
|                              |                                                                                                                    |                               |                                   |                             | Date of Commissioning (Month/Year) |             |                   |
| S.No                         | Project                                                                                                            | Date of Approval (Month/Year) | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised                  | Anticipated | Cost Overruns (%) |
| 1                            | 2                                                                                                                  | 3                             | 4                                 | 5                           | 6                                  | 7           | 8                 |
| 238                          | DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING<br>- [N22000164]                                                           | 04/2010                       | 309.44<br>-                       | 525.81                      | 12/2015<br>-                       | 02/2019     | 69.92             |
| 239                          | MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING<br>- [N22000165]                                                           | 04/2012                       | 258.20<br>-                       | 365.00                      | -<br>-                             | 01/2020     | 41.36             |
| 240                          | ARA-BHABHUA ROAD (NL)<br>- [N22000166]                                                                             | 04/2008                       | 633.87<br>-                       | 2,396.88                    | -<br>-                             | -           | 278.13            |
| 241                          | ROURKELA JHARSUGUDA THIRD LINE 101 KM<br>- [N22000395]                                                             | 11/2015                       | 969.83<br>-                       | 1,151.81                    | 03/2020<br>-                       | 06/2020     | 18.76             |
| 242                          | TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN<br>NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM<br>NADAKUMAR BOLAI - [N22000397] | 01/1991                       | 1,013.45<br>-                     | 1,428.00                    | 12/2021<br>-                       | 12/2021     | 40.90             |
| 243                          | RUPSA BANGRIPOSI 90 KM WITH MM FOR<br>UPGRADATION FROM RUPSA BURAMARA AND<br>EXTENSION OF LINE FRO - [N22000398]   | 04/1995                       | 524.43<br>-                       | 939.00                      | 12/2021<br>-                       | 12/2024     | 79.05             |
| 244                          | BANKURA DAMODAR VALLEY RLY LINE 96 KM GC<br>WITH 6MMS FOR NL - [N22000402]                                         | 04/1998                       | 1,027.40<br>-                     | 2,373.00                    | 03/2003<br>-                       | 03/2030     | 130.97            |
| <u>South Western Railway</u> |                                                                                                                    |                               |                                   |                             |                                    |             |                   |
| 245                          | MUNIRABAD (GINGERA) -RAICHUR NL<br>- [N22000257]                                                                   | 04/2007                       | 179.65<br>-                       | 1,350.91                    | -<br>-                             | 12/2023     | 651.97            |
| 246                          | CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI<br>NILAYAM NL - [N22000276]                                                | 04/2013                       | 558.00<br>-                       | 692.43                      | -<br>-                             | 12/2023     | 24.09             |
| 247                          | SRINIVASA-PURA-MADANAPALLI NL<br>- [N22000277]                                                                     | 04/2013                       | 296.00<br>-                       | 466.65                      | -<br>-                             | 12/2023     | 57.65             |
| 248                          | TORANAGALLU-RANJITPURA DL<br>- [N22000298]                                                                         | 04/2011                       | 146.75<br>-                       | 167.50                      | -<br>-                             | 12/2023     | 14.14             |
| 249                          | CHIKBALLA-PUR-GOWRIBIDANUR NL<br>- [N22000300]                                                                     | 04/2013                       | 327.25<br>-                       | 367.77                      | -<br>-                             | 12/2023     | 12.38             |
| 250                          | HOTGI-KUDGI-GADAG<br>- [N22000333]                                                                                 | 03/2015                       | 1,614.59<br>-                     | 1,870.41                    | 03/2019<br>-                       | 03/2021     | 15.84             |
| 251                          | KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)<br>- [N22000486]                                                     | 03/1996                       | 644.78<br>-                       | 889.52                      | 03/2017<br>-                       | 03/2020     | 37.96             |
| <u>Southern Railway</u>      |                                                                                                                    |                               |                                   |                             |                                    |             |                   |
| 252                          | CALICUT-MANGALORE (DL) (SR)<br>- [220100151]                                                                       | 02/1996                       | 240.00<br>-                       | 579.37                      | -<br>-                             | -           | 141.40            |
| 253                          | KARUR-SALEM(NL),SR<br>- [220100191]                                                                                | 02/1997                       | 155.55<br>-                       | 920.00                      | -<br>-                             | -           | 491.45            |
| 254                          | QUILON-TIRUNELVELI-TENKASI-<br>VIRUDHUNAGAR(SR)(GC)<br>[220100263]                                                 | 03/1998                       | 280.00<br>-                       | 1,122.00                    | -<br>-                             | -           | 300.71            |
| 255                          | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU<br>'POND'-AGASTIYAMPALLI<br>[N22000079]                                   | 09/2007                       | 724.69<br>-                       | 2,072.50                    | 02/2019<br>-                       | 02/2019     | 185.98            |
| 256                          | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND<br>COIMBATORE - [N22000080]                                                 | 09/2006                       | 343.17<br>-                       | 1,065.00                    | -<br>-                             | -           | 210.34            |
| 257                          | TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)<br>- [N22000084]                                                             | 09/2006                       | 227.40<br>-                       | 900.00                      | -<br>-                             | -           | 295.78            |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (December 2018)             |                                                                                                  |                                  |                                      |                                |                                       |             |                   |
|-----------------------------|--------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                             |                                                                                                  |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No                        | Project                                                                                          | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated<br>Cost (Rs.crore) | Original/<br>Revised                  | Anticipated | Cost Overruns (%) |
| 1                           | 2                                                                                                | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 258                         | TIDIVANAM-NAGARI (NL)<br>- [N22000085]                                                           | 09/2006                          | 582.83<br>-                          | 2,300.00                       | -<br>-                                | -           | 294.63            |
| 259                         | ANGAMALI-SABARIMALA (N.L.)(SR)<br>- [220100252]                                                  | 10/1998                          | 1,566.00<br>-                        | 2,815.62                       | -<br>-                                | -           | 79.80             |
| 260                         | ATTIPPATTU PUTTUR<br>- [N22000184]                                                               | 04/2008                          | 151.84<br>-                          | 1,105.00                       | 02/2019<br>-                          | 02/2019     | 627.74            |
| 261                         | CHENNAI-CUDDALORE VIA MAMALLAPURAM<br>- [N22000185]                                              | 04/2008                          | 523.52<br>-                          | 2,350.00                       | -<br>-                                | -           | 348.88            |
| 262                         | SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO<br>IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR<br>- [N22000186] | 04/2013                          | 839.00<br>-                          | 1,500.00                       | -<br>-                                | -           | 78.78             |
| 263                         | CUDDALORE-SALEM VIA VRIDDHACHALAM GC<br>- [N22000187]                                            | 04/1999                          | 198.68<br>-                          | 556.64                         | -<br>-                                | -           | 180.17            |
| 264                         | CHENNAI BEACH-TAMBARAM-CHENGALPATTU<br>SUBURBAN GC<br>[N22000188]                                | 04/1998                          | 271.24<br>-                          | 520.00                         | -<br>-                                | -           | 91.71             |
| 265                         | KURUPPANTHARA-CHINGAVANAM<br>- [N22000190]                                                       | 04/2007                          | 270.14<br>-                          | 457.08                         | -<br>-                                | -           | 69.20             |
| 266                         | ERODE-PALANI<br>- [N22000199]                                                                    | 04/2008                          | 288.57<br>-                          | 1,140.00                       | -<br>-                                | -           | 295.05            |
| 267                         | MADURAI-BODINAYAKKANUR<br>- [N22000201]                                                          | 04/2008                          | 164.41<br>-                          | 450.00                         | -<br>-                                | 03/2020     | 173.71            |
| 268                         | CHENGANNUR-CHINGAVANAM<br>- [N22000203]                                                          | 04/2006                          | 191.72<br>-                          | 369.83                         | -<br>-                                | -           | 92.90             |
| 269                         | MADURAI-TUTICORIN VIA ARUPPUKOTTAI<br>- [N22000215]                                              | 04/2011                          | 120.70<br>-                          | 1,800.00                       | 03/2019<br>-                          | 03/2019     | 1,391.30          |
| 270                         | OMALUR-METTURDAM- DOUBLINGWITH<br>ELCTRIFICATION 28.93KM<br>[N22000373]                          | 10/2013                          | 187.26<br>-                          | 231.67                         | 04/2014<br>-                          | 03/2020     | 23.72             |
| 271                         | THIRUMAILA - VELACHERY : MASS RAPID TRANSIT<br>SYSTEM (PHASE II)<br>- [N22000441]                | 02/1996                          | 268.87<br>-                          | 302.02                         | 03/2005<br>-                          | -           | 12.33             |
| 272                         | VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION<br>- [N22000446]                                  | 02/2005                          | 600.00<br>600.00                     | 645.54                         | 03/2010<br>-                          | -           | 7.59              |
| 273                         | MADURAI-DINDIGUL (INCL. AMBADUTURAI-<br>KODAIKANNAL ROAD) (62.05 KM) DOUBLING<br>- [N22000450]   | 02/2003                          | 199.55<br>-                          | 330.32                         | 03/2009<br>-                          | -           | 65.53             |
| 274                         | MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING<br>- [N22000451]                               | 02/2015                          | 760.00<br>-                          | 1,182.31                       | 03/2020<br>-                          | 03/2020     | 55.57             |
| <u>West Central Railway</u> |                                                                                                  |                                  |                                      |                                |                                       |             |                   |
| 275                         | RAMGANJMUUNDI-BHOPAL (NL),WCR<br>- [220100314]                                                   | 04/2001                          | 424.60<br>-                          | 2,713.09                       | 03/2021<br>-                          | 03/2021     | 538.98            |
| 276                         | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)<br>- [220100232]                                          | 09/1998                          | 247.66<br>-                          | 6,093.31                       | 05/2008<br>-                          | 03/2023     | 2,360.35          |
| 277                         | KATNI GRADE SEPARATOR/BYE PASS<br>- [N22000416]                                                  | 08/2016                          | 582.13<br>-                          | 1,260.61                       | 03/2022<br>-                          | 03/2022     | 116.55            |
| <u>Western Railway</u>      |                                                                                                  |                                  |                                      |                                |                                       |             |                   |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (December 2018) |                                                                                                                    |                                  |                                      |                                |                                       |             |                   |
|-----------------|--------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                 |                                                                                                                    |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No            | Project                                                                                                            | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1               | 2                                                                                                                  | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 278             | BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]                                   | 04/2006                          | 117.36<br>196.95                     | 203.00                         | 03/2011<br>-                          | -           | 72.97             |
| 279             | BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]                                             | 04/2008                          | 318.24<br>-                          | 321.62                         | 03/2012<br>-                          | 03/2019     | 1.06              |
| 280             | RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]        | 04/1994                          | 320.66<br>-                          | 858.96                         | 03/2019<br>-                          | 03/2022     | 167.87            |
|                 | Total                                                                                                              |                                  | 1,68,116.34<br>-                     | 3,89,745.97                    |                                       |             |                   |
|                 |                                                                                                                    |                                  |                                      |                                |                                       |             |                   |
|                 | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                 |                                  |                                      |                                |                                       |             |                   |
|                 | <u>Ministry Of Road Transport And Highways</u>                                                                     |                                  |                                      |                                |                                       |             |                   |
| 281             | CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316] | 03/2015                          | 258.97<br>-                          | 268.92                         | 08/2015<br>-                          | -           | 3.84              |
| 282             | REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317] | 03/2015                          | 157.18<br>162.00                     | 162.00                         | 07/2015<br>-                          | -           | 3.07              |
| 283             | WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639] | 03/2014                          | 191.50<br>192.00                     | 192.00                         | 05/2016<br>-                          | -           | .26               |
| 284             | WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]  | 01/2015                          | 326.63<br>327.00                     | 327.00                         | 04/2018<br>-                          | -           | .11               |
| 285             | WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]    | 02/2015                          | 239.91<br>240.00                     | 240.00                         | 10/2017<br>-                          | -           | .04               |
| 286             | IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]  | 12/2013                          | 319.80<br>320.00                     | 320.00                         | 05/2016<br>-                          | -           | .06               |
| 287             | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645] | 08/2013                          | 171.96<br>172.00                     | 172.00                         | 06/2016<br>-                          | -           | .02               |
| 288             | WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647] | 03/2014                          | 162.51<br>163.00                     | 163.00                         | 05/2016<br>-                          | -           | .30               |
| 289             | RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777] | 11/2017                          | 283.51<br>-                          | 284.00                         | 11/2019<br>-                          | 11/2019     | .17               |
| 290             | REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782] | 03/2018                          | 460.73<br>-                          | 461.00                         | -<br>-                                | -           | .06               |
| 291             | Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820] | 11/2017                          | 237.80<br>-                          | 238.00                         | 11/2019<br>-                          | 11/2019     | .08               |
|                 | <u>National Highways And Infrastructure Development Corporation Ltd.</u>                                           |                                  |                                      |                                |                                       |             |                   |



## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (December 2018) |                                                                                                                    |                               |                                   |                             |                                    |             |                   |
|-----------------|--------------------------------------------------------------------------------------------------------------------|-------------------------------|-----------------------------------|-----------------------------|------------------------------------|-------------|-------------------|
|                 |                                                                                                                    |                               |                                   |                             | Date of Commissioning (Month/Year) |             |                   |
| S.No            | Project                                                                                                            | Date of Approval (Month/Year) | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised                  | Anticipated | Cost Overruns (%) |
| 1               | 2                                                                                                                  | 3                             | 4                                 | 5                           | 6                                  | 7           | 8                 |
| 292             | CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]                                | 12/2016                       | 138.93<br>155.00                  | 155.00                      | 01/2017<br>-                       | 01/2020     | 11.57             |
| 293             | RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]                                                                  | 04/2017                       | 388.00<br>-                       | 447.37                      | 10/2017<br>-                       | -           | 15.30             |
|                 | <u>National Highways Authority Of India</u>                                                                        |                               |                                   |                             |                                    |             |                   |
| 294             | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]                                               | 12/2003                       | 280.00<br>-                       | 361.00                      | 02/2009<br>-                       | 12/2018     | 28.93             |
| 295             | MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]                                                  | 12/2003                       | 199.81<br>-                       | 385.13                      | 04/2009<br>-                       | 03/2019     | 92.75             |
| 296             | MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]                                                 | 12/2003                       | 155.04<br>-                       | 280.13                      | 11/2008<br>-                       | -           | 80.68             |
| 297             | DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]                                                             | 12/2003                       | 160.00<br>-                       | 167.98                      | 05/2008<br>-                       | 02/2019     | 4.99              |
| 298             | HARANGAJO TO MAIBANG, NH-54 - [N24000062]                                                                          | 12/2003                       | 196.00<br>-                       | 331.23                      | 07/2009<br>-                       | -           | 68.99             |
| 299             | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]                                                          | 05/2009                       | 1,108.00<br>-                     | 2,288.00                    | 11/2011<br>-                       | 06/2019     | 106.50            |
| 300             | BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]                                                                          | 12/2003                       | 217.61<br>-                       | 360.84                      | 04/2010<br>-                       | 04/2019     | 65.82             |
| 301             | NALBARI T BIJNI (AS-7) - [N24000048]                                                                               | 12/2003                       | 208.00<br>-                       | 230.00                      | 04/2008<br>-                       | 03/2019     | 10.58             |
| 302             | 4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]                                                | 04/2014                       | 1,266.60<br>-                     | 1,544.00                    | 09/2016<br>-                       | 06/2019     | 21.90             |
| 303             | GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]                                                  | 03/2010                       | 1,509.10<br>-                     | 3,237.87                    | 09/2012<br>-                       | 08/2018     | 114.56            |
| 304             | INDORE-JHABUA-GUJRAT/MP - [N24000136]                                                                              | 10/2010                       | 1,175.00<br>-                     | 1,206.10                    | 04/2013<br>-                       | 11/2018     | 2.65              |
| 305             | DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]                                                                  | 10/2012                       | 1,928.22<br>-                     | 2,945.00                    | 04/2015<br>-                       | -           | 52.73             |
| 306             | FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]                                                                      | 05/2013                       | 1,055.00<br>-                     | 1,601.77                    | 11/2015<br>-                       | 12/2018     | 51.83             |
| 307             | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-I)_NEW - [N24000609]                                   | 09/2015                       | 771.18<br>-                       | 7,558.00                    | -<br>-                             | -           | 880.06            |
| 308             | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654] | 03/2017                       | 1,184.71<br>-                     | 1,310.00                    | 03/2020<br>-                       | 08/2020     | 10.58             |
| 309             | 4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]                                             | 03/2017                       | 744.64<br>-                       | 982.00                      | 03/2020<br>-                       | 03/2020     | 31.88             |
| 310             | 4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]                                         | 03/2017                       | 1,030.44<br>-                     | 1,065.51                    | 03/2020<br>-                       | 05/2020     | 3.40              |
| 311             | 4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]                                          | 03/2017                       | 988.34<br>-                       | 1,043.28                    | 03/2020<br>-                       | 08/2020     | 5.56              |
| 312             | 4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]                                        | 03/2017                       | 1,059.73<br>-                     | 1,071.00                    | 03/2017<br>-                       | 11/2020     | 1.06              |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (December 2018) |                                                                                                                   |                                  |                                      |                                   |                                       |             |                      |
|-----------------|-------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|-----------------------------------|---------------------------------------|-------------|----------------------|
|                 |                                                                                                                   |                                  |                                      |                                   | Date of Commissioning<br>(Month/Year) |             |                      |
| S.No            | Project                                                                                                           | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated<br>Cost<br>(Rs.crore) | Original/<br>Revised                  | Anticipated | Cost Overruns<br>(%) |
| 1               | 2                                                                                                                 | 3                                | 4                                    | 5                                 | 6                                     | 7           | 8                    |
| 313             | 4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661                                        | 03/2017                          | 1,098.06<br>-                        | 1,160.64                          | 03/2020<br>-                          | 08/2020     | 5.70                 |
| 314             | CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662 | 03/2017                          | 754.54<br>-                          | 756.27                            | 03/2020<br>-                          | 04/2020     | .23                  |
| 315             | TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665  | 03/2017                          | 672.89<br>-                          | 736.01                            | 03/2020<br>-                          | 03/2020     | 9.38                 |
| 316             | SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668                 | 03/2017                          | 1,041.62<br>-                        | 1,187.10                          | 03/2020<br>-                          | 05/2020     | 13.97                |
| 317             | 4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669                                     | 03/2017                          | 165.50<br>-                          | 172.16                            | 03/2020<br>-                          | 06/2019     | 4.02                 |
| 318             | REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671  | 03/2017                          | 1,288.07<br>-                        | 1,420.00                          | 03/2020<br>-                          | 03/2020     | 10.24                |
| 319             | 6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672 | 03/2017                          | 2,064.99<br>-                        | 2,447.00                          | 03/2020<br>-                          | 03/2020     | 18.50                |
| 320             | SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674   | 03/2017                          | 831.58<br>-                          | 1,177.00                          | 03/2020<br>-                          | 06/2020     | 41.54                |
| 321             | SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675 | 03/2017                          | 993.16<br>-                          | 1,434.00                          | 03/2020<br>-                          | 06/2020     | 44.39                |
|                 | <u>Public Works Dept Of State</u>                                                                                 |                                  |                                      |                                   |                                       |             |                      |
| 322             | 4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292  | 11/2014                          | 573.96<br>605.00                     | 605.00                            | -<br>-                                | -           | 5.41                 |
| 323             | TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307 | 12/2011                          | 156.63<br>276.00                     | 276.00                            | 02/2012<br>-                          | -           | 76.21                |
| 324             | REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247  | 10/2014                          | 295.47<br>-                          | 313.27                            | 02/2017<br>-                          | -           | 6.02                 |
| 325             | CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249 | 03/2011                          | 218.31<br>-                          | 339.82                            | 12/2015<br>-                          | -           | 55.66                |
| 326             | CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260 | 01/2014                          | 255.75<br>348.00                     | 348.43                            | 09/2017<br>-                          | -           | 36.24                |
| 327             | CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261 | 01/2014                          | 267.16<br>352.00                     | 352.05                            | 11/2017<br>-                          | -           | 31.78                |
| 328             | REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265 | 11/2014                          | 297.78<br>330.00                     | 330.00                            | 02/2017<br>-                          | -           | 10.82                |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (December 2018) |                                                                                                                   |                                  |                                      |                                |                                       |             |                   |
|-----------------|-------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                 |                                                                                                                   |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No            | Project                                                                                                           | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1               | 2                                                                                                                 | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 329             | TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420 | 12/2009                          | 104.00<br>-                          | 201.00                         | 09/2010<br>-                          | -           | 93.27             |
|                 | Total                                                                                                             |                                  | 29,654.32<br>-                       | 44,654.88                      |                                       |             |                   |
|                 |                                                                                                                   |                                  |                                      |                                |                                       |             |                   |
|                 | <u>SHIPPING AND PORTS</u>                                                                                         |                                  |                                      |                                |                                       |             |                   |
|                 | <u>Kamarajar Port Limited</u>                                                                                     |                                  |                                      |                                |                                       |             |                   |
| 330             | CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066                                               | 02/2015                          | 244.50<br>258.00                     | 271.56                         | 12/2017<br>-                          | -           | 11.07             |
|                 | <u>Mumbai Port Trust</u>                                                                                          |                                  |                                      |                                |                                       |             |                   |
| 331             | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063 | 01/2007                          | 366.39<br>-                          | 669.46                         | 12/2010<br>-                          | -           | 82.72             |
|                 | <u>Port Trust</u>                                                                                                 |                                  |                                      |                                |                                       |             |                   |
| 332             | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035                                          | 10/2002                          | 150.00<br>-                          | 600.00                         | 03/2006<br>-                          | 02/2019     | 300.00            |
|                 | Total                                                                                                             |                                  | 760.89<br>-                          | 1,541.02                       |                                       |             |                   |
|                 |                                                                                                                   |                                  |                                      |                                |                                       |             |                   |
|                 | <u>STEEL</u>                                                                                                      |                                  |                                      |                                |                                       |             |                   |
|                 | <u>Rastriya Ispat Nigam Limited</u>                                                                               |                                  |                                      |                                |                                       |             |                   |
| 333             | REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091                                                               | 12/2009                          | 343.00<br>-                          | 488.40                         | 10/2016<br>-                          | -           | 42.39             |
|                 | Total                                                                                                             |                                  | 343.00<br>-                          | 488.40                         |                                       |             |                   |
|                 |                                                                                                                   |                                  |                                      |                                |                                       |             |                   |
|                 | <u>TELECOMMUNICATIONS</u>                                                                                         |                                  |                                      |                                |                                       |             |                   |
|                 | <u>Department Of Telecommunication</u>                                                                            |                                  |                                      |                                |                                       |             |                   |
| 334             | NETWORK FOR SPECTRUM - [N26000101                                                                                 | 03/2012                          | 13,334.00<br>-                       | 24,664.00                      | 07/2015<br>-                          | 05/2020     | 84.97             |
|                 | Total                                                                                                             |                                  | 13,334.00<br>-                       | 24,664.00                      |                                       |             |                   |
|                 |                                                                                                                   |                                  |                                      |                                |                                       |             |                   |
|                 | <u>URBAN DEVELOPMENT</u>                                                                                          |                                  |                                      |                                |                                       |             |                   |
|                 | <u>Central Public Works Department</u>                                                                            |                                  |                                      |                                |                                       |             |                   |
| 335             | STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060                                                        | 04/2014                          | 332.72<br>-                          | 342.00                         | 09/2016<br>-                          | -           | 2.79              |
| 336             | ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071      | 10/2013                          | 1,219.21<br>-                        | 1,592.00                       | 10/2019<br>-                          | 03/2020     | 30.58             |
| 337             | CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100          | 02/2016                          | 496.18<br>496.00                     | 498.99                         | 06/2017<br>-                          | 06/2020     | .57               |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (December 2018) |                                                                                                                   |                                  |                                      |                                |                                       |             |                      |
|-----------------|-------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|----------------------|
|                 |                                                                                                                   |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                      |
| S.No            | Project                                                                                                           | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/<br>Revised                  | Anticipated | Cost Overruns<br>(%) |
| 1               | 2                                                                                                                 | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                    |
| 338             | CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101] | 12/2008                          | 114.26<br>266.00                     | 266.00                         | 12/2013<br>-                          | 10/2019     | 132.80               |
|                 | <u>Chennai Metro Rail Ltd</u>                                                                                     |                                  |                                      |                                |                                       |             |                      |
| 339             | CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]                                                                    | 02/2009                          | 14,600.00<br>-                       | 19,058.00                      | 12/2015<br>-                          | -           | 30.53                |
|                 | <u>Hindustan Steelwork Construction Limited</u>                                                                   |                                  |                                      |                                |                                       |             |                      |
| 340             | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]                                     | 12/2007                          | 202.61<br>227.00                     | 227.00                         | 12/2016<br>-                          | -           | 12.04                |
| 341             | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]                                   | 10/2011                          | 175.49<br>206.71                     | 206.71                         | 12/2016<br>-                          | -           | 17.79                |
| 342             | CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]                                            | 05/2005                          | 768.88<br>1,070.97                   | 1,113.34                       | 02/2014<br>-                          | -           | 44.80                |
| 343             | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]                                      | 03/2007                          | 149.73<br>173.00                     | 175.94                         | 12/2015<br>-                          | -           | 17.50                |
|                 | <u>National Building Construction Corporation Ltd</u>                                                             |                                  |                                      |                                |                                       |             |                      |
| 344             | REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]                                                                  | 06/2012                          | 4,264.00<br>-                        | 4,439.23                       | 11/2019<br>-                          | 11/2019     | 4.11                 |
|                 | Total                                                                                                             |                                  | 22,323.08<br>-                       | 27,919.21                      |                                       |             |                      |
|                 |                                                                                                                   |                                  |                                      |                                |                                       |             |                      |
|                 | Grand Total                                                                                                       |                                  | 4,66,242.42                          | 8,01,777.43                    |                                       |             |                      |

## Details of Delayed Projects w.r.t. Original Schedule

### Annexure - VI

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                            |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                            |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies) |
| S.No                                            | Project                                                                                                    | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                  |
| 1                                               | 2                                                                                                          | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
|                                                 | <u>ATOMIC ENERGY</u>                                                                                       |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                                 | <u>Bhavini Limited</u>                                                                                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 1                                               | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU                          | 09/2003                       | 3,492.00 -                         | 6,100.00                     | 5,687.52                           | 09/2010 -                          | 03/2019     | 102                   | 74.68            |                                                                  |
|                                                 | <u>Nuclear Power Corporation Of India Limited</u>                                                          |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 2                                               | KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT                                        | 10/2009                       | 11,459.00<br>16,580.00             | 16,580.00                    | 12,848.00                          | 12/2015<br>11/2016                 | 06/2020     | 54                    | 44.69            |                                                                  |
| 3                                               | RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN                          | 10/2009                       | 12,320.00 -                        | 12,320.00                    | 10,138.00                          | 12/2016<br>03/2017                 | 12/2020     | 48                    | 0                |                                                                  |
| 4                                               | KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL, TAMIL NADU                               | 03/2013                       | 39,849.00 -                        | 39,849.00                    | 11,815.00                          | 11/2020 -                          | 11/2023     | 36                    | 0                |                                                                  |
|                                                 | Total                                                                                                      |                               | 67,120.00 -                        | 74,849.00                    | 40,488.52                          |                                    |             |                       |                  |                                                                  |
|                                                 | <u>CIVIL AVIATION</u>                                                                                      |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                                 | <u>Airport Authority Of India Limited</u>                                                                  |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 5                                               | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, A & N ISLANDS | 10/2013                       | 314.61 -                           | 441.33                       | 85.79                              | 09/2018 -                          | 06/2020     | 21                    | 40.28            |                                                                  |
|                                                 | Total                                                                                                      |                               | 314.61 -                           | 441.33                       | 85.79                              |                                    |             |                       |                  |                                                                  |
|                                                 | <u>COAL</u>                                                                                                |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                                 | <u>Bharat Coking Coal Limited</u>                                                                          |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 6                                               | MOONIDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND                                                           | 08/2011                       | 1,230.27 -                         | 1,230.27                     | 326.22                             | 04/2015 -                          | 04/2019     | 48                    | 0                |                                                                  |
|                                                 | <u>Central Coal Fields Limited</u>                                                                         |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 7                                               | NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND                                                    | 12/2007                       | 179.87 -                           | 179.87                       | 174.69                             | 03/2012 -                          | 03/2019     | 84                    | 0                |                                                                  |
| 8                                               | TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND                                                            | 08/2008                       | 264.68 -                           | 264.68                       | 178.37                             | 03/2012 -                          | 03/2019     | 84                    | 0                |                                                                  |
| 9                                               | RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL, JHARKHAND                                                     | 12/2009                       | 510.85 -                           | 510.85                       | 340.29                             | 03/2016 -                          | 03/2019     | 36                    | 0                |                                                                  |
| 10                                              | KARMA OCP (1.0 MTY) - [N06000088]CCL, JHARKHAND                                                            | 06/2009                       | 162.46 -                           | 162.46                       | 89.21                              | 03/2014 -                          | 03/2019     | 60                    | 0                |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                                                                   |
|-------------------------------------------------|-----------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| S.No                                            | Project                                                                                             | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Date of Commissioning (Month/Year) |             | Time Overrun (Months) | Cost Overrun (%) | Reasons for Delay (As Reported by Project Implementing Agencies)                                                                                                  |
|                                                 |                                                                                                     |                               |                                    |                              |                                    | Original / Revised                 | Anticipated |                       |                  |                                                                                                                                                                   |
| 1                                               | 2                                                                                                   | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                                                                                                                                |
| 11                                              | CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND                                                | 08/2007                       | 163.51 -                           | 163.51                       | 103.41                             | 03/2011 -                          | 03/2020     | 108                   | 0                |                                                                                                                                                                   |
| 12                                              | MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND                                                   | 08/2008                       | 706.40 -                           | 706.40                       | 185.62                             | 07/2012 -                          | 03/2021     | 104                   | 0                |                                                                                                                                                                   |
|                                                 | <u>Eastern Coal Fields Limited</u>                                                                  |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                                                                   |
| 13                                              | SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL                                   | 08/2012                       | 1,055.05 -                         | 1,055.05                     | 383.30                             | 03/2018 -                          | 03/2020     | 24                    | 0                | 1. Rehabilitation of PAFs- Progress of R&R activity delayed due to disputes among villagers for selection of rehab. site and resistance by villagers in shifting. |
|                                                 | <u>Mahanadi Coal Fields Limited</u>                                                                 |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                                                                   |
| 14                                              | BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL, ODISHA                                           | 12/2007                       | 490.10 -                           | 490.10                       | 413.37                             | 03/2017 -                          | 03/2020     | 36                    | 0                |                                                                                                                                                                   |
| 15                                              | KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA                                                | 12/2007                       | 457.77 -                           | 457.77                       | 584.85                             | 03/2013 -                          | 03/2020     | 84                    | 0                |                                                                                                                                                                   |
| 16                                              | BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA                                         | 12/2007                       | 172.08 -                           | 172.08                       | 267.19                             | 03/2010 -                          | 03/2020     | 120                   | 0                |                                                                                                                                                                   |
| 17                                              | HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA                                         | 11/2008                       | 479.53 -                           | 479.53                       | 336.08                             | 03/2013 -                          | 03/2020     | 84                    | 0                |                                                                                                                                                                   |
| 18                                              | KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL, ODISHA                                                  | 06/2014                       | 289.03 -                           | 289.03                       | 28.56                              | 03/2018 -                          | 03/2020     | 24                    | 0                |                                                                                                                                                                   |
| 19                                              | ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA                                      | 08/2008                       | 207.28 -                           | 207.28                       | 235.50                             | 03/2012 -                          | 03/2021     | 108                   | 0                |                                                                                                                                                                   |
| 20                                              | JAGANNATH RE-ORGANISATION OC. (6.00 MTY) - [N06000114]MCL, ODISHA                                   | 05/2014                       | 337.66 -                           | 337.66                       | 65.58                              | 03/2019 -                          | 03/2021     | 24                    | 0                |                                                                                                                                                                   |
| 21                                              | BASUNDHARA (WEST) OC EXTN (7.00 MTY) - [N06000112]MCL, ODISHA                                       | 05/2014                       | 479.15 -                           | 479.15                       | 120.51                             | 03/2019 -                          | 03/2024     | 60                    | 0                |                                                                                                                                                                   |
|                                                 | <u>Neyveli Lignite Corporation</u>                                                                  |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                                                                   |
| 22                                              | NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC, TAMIL NADU                           | 06/2011                       | 5,907.11 -                         | 5,907.11                     | 5,828.01                           | 12/2015<br>12/2018                 | 03/2019     | 39                    | 0                |                                                                                                                                                                   |
| 23                                              | EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU        | 04/2013                       | 1,458.17<br>709.06                 | 709.06                       | 399.03                             | 06/2015<br>09/2019                 | 09/2019     | 51                    | -51.37           |                                                                                                                                                                   |
|                                                 | <u>Northern Coal Fields Limited</u>                                                                 |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                                                                   |
| 24                                              | KHADIA EXPANSION OPENCAST PROJECT (4 TO 10 MTPA, 6MTPA INCREMENTAL) - [N06000091]NCL, UTTAR PRADESH | 06/2011                       | 1,131.28 -                         | 1,131.28                     | 711.45                             | 03/2018 -                          | 03/2019     | 12                    | 0                |                                                                                                                                                                   |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                        |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                        |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  |                                                                  |
| S.No                                            | Project                                                                | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) | Reasons for Delay (As Reported by Project Implementing Agencies) |
| 1                                               | 2                                                                      | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
|                                                 | <u>Singareni Colliers Company Limited</u>                              |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 25                                              | RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA                           | 03/2010                       | 209.78 -                           | 209.78                       | 154.21                             | 03/2015 -                          | 03/2019     | 48                    | 0                |                                                                  |
| 26                                              | RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL, TELANGANA | 06/2012                       | 365.01 -                           | 365.01                       | 204.26                             | 06/2015 -                          | 03/2019     | 45                    | 0                |                                                                  |
| 27                                              | RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA                | 11/2012                       | 430.45 -                           | 415.37                       | 160.45                             | 03/2016 -                          | 03/2019     | 36                    | -3.5             |                                                                  |
| 28                                              | KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL, TELANGANA                | 10/2015                       | 426.79 -                           | 426.79                       | -                                  | 03/2018 -                          | 03/2019     | 12                    | 0                |                                                                  |
| 29                                              | KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA             | 07/2012                       | 417.33 -                           | 384.32                       | 146.45                             | 07/2016 -                          | 03/2020     | 44                    | -7.91            |                                                                  |
| 30                                              | KISTARAM OCP - [N06000089]SCCL, TELANGANA                              | 11/2010                       | 242.29 -                           | 164.04                       | 12.69                              | 03/2015 -                          | 03/2021     | 72                    | -32.3            |                                                                  |
| 31                                              | RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA             | 07/2011                       | 162.76 -                           | 349.28                       | 1.31                               | 03/2015 -                          | 03/2021     | 72                    | 114.6            |                                                                  |
| 32                                              | JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA                | 07/2011                       | 447.06 -                           | 437.51                       | 353.61                             | 03/2015 -                          | 03/2021     | 72                    | -2.14            |                                                                  |
| 33                                              | RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA                | 12/2009                       | 418.97 -                           | 489.62                       | 477.74                             | 03/2012 -                          | 03/2023     | 132                   | 16.86            |                                                                  |
| 34                                              | SHANTIKHANI LONGWALL PROJ- SCCL - [N06000017]SCCL, TELANGANA           | 10/2006                       | 249.03 -                           | 448.86                       | 186.91                             | 03/2012 -                          | 03/2024     | 144                   | 80.24            |                                                                  |
|                                                 | <u>South-Eastern Coal Fields Limited</u>                               |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 35                                              | AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL, CHHATISGARH  | 11/2009                       | 198.59 -                           | 198.59                       | 169.50                             | 03/2016 -                          | 03/2019     | 36                    | 0                |                                                                  |
| 36                                              | BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH         | 04/2012                       | 258.56 -                           | 258.56                       | 167.63                             | 03/2016 -                          | 03/2019     | 36                    | 0                |                                                                  |
| 37                                              | JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL, CHHATISGARH               | 09/2008                       | 152.43 -                           | 459.49                       | 178.93                             | 03/2015 -                          | 03/2020     | 60                    | 201.44           |                                                                  |
| 38                                              | KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH           | 07/2008                       | 178.44 -                           | 178.44                       | 5.16                               | 03/2014 -                          | 03/2020     | 72                    | 0                |                                                                  |
| 39                                              | MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH         | 12/2009                       | 321.50 -                           | 321.50                       | 202.68                             | 03/2014 -                          | 03/2020     | 72                    | 0                |                                                                  |
|                                                 | <u>Western Coal Fields Limited</u>                                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 40                                              | ADASA UG TO OC - [N06000133]WCL, MAHARASHTRA                           | 08/2015                       | 288.90 333.43                      | 333.43                       | .02                                | 03/2023 03/2024                    | 03/2024     | 12                    | 15.41            |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|-----------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                     |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies) |
| S.No                                            | Project                                                                                             | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                  |
| 1                                               | 2                                                                                                   | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 41                                              | KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA                                                   | 11/2015                       | 277.65<br>313.34                   | 313.34                       | 6.12                               | 03/2021<br>09/2018                 | 03/2024     | 36                    | 12.85            |                                                                  |
|                                                 | Total                                                                                               |                               | 20,727.79<br>-                     | 20,687.07                    | 13,198.91                          |                                    |             |                       |                  |                                                                  |
|                                                 |                                                                                                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                                 | <u>FERTILISERS</u>                                                                                  |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                                 | <u>Rashtriya Chemical &amp; Fertiliser Limited</u>                                                  |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 42                                              | GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N0800010]RCF,MAHARASHTRA | 02/2016                       | 482.85<br>482.85                   | 482.85                       | 413.00                             | 12/2017<br>01/2019                 | 01/2019     | 13                    | 0                |                                                                  |
| 43                                              | NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA                        | 10/2014                       | 197.79<br>209.44                   | 209.44                       | 140.10                             | 11/2016<br>04/2019                 | 04/2019     | 29                    | 5.89             |                                                                  |
|                                                 | Total                                                                                               |                               | 680.64<br>-                        | 692.29                       | 553.10                             |                                    |             |                       |                  |                                                                  |
|                                                 |                                                                                                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                                 | <u>STEEL</u>                                                                                        |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                                 | <u>National Mineral Development Corporation (NmDC)</u>                                              |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 44                                              | NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH                                           | 01/2010                       | 15,525.00<br>-                     | 15,525.00                    | 14,566.77                          | 05/2015<br>06/2019                 | 06/2019     | 49                    | 0                |                                                                  |
|                                                 | <u>Rastriya Ispat Nigam Limited</u>                                                                 |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 45                                              | ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH                         | 07/2015                       | 465.85<br>-                        | 465.85                       | 276.25                             | 07/2018<br>-                       | 01/2019     | 6                     | 0                | No                                                               |
| 46                                              | CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH                                              | 08/2015                       | 320.66<br>-                        | 320.66                       | 125.36                             | 08/2018<br>-                       | 02/2019     | 6                     | 0                | No                                                               |
| 47                                              | FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH                                                  | 04/2014                       | 1,682.85<br>-                      | 1,682.85                     | 852.10                             | 09/2018<br>-                       | 03/2019     | 6                     | 0                | No                                                               |
| 48                                              | COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH                                                | 12/2011                       | 2,858.00<br>-                      | 2,500.00                     | 1,053.76                           | 12/2017<br>-                       | 09/2019     | 21                    | -12.53           | No                                                               |
|                                                 | <u>Steel Authority Of India Limited (SAIL)</u>                                                      |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 49                                              | INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA                                  | 04/2015                       | 3,127.30<br>-                      | 3,127.30                     | 2,527.38                           | 04/2018<br>-                       | 05/2019     | 13                    | 0                |                                                                  |



## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                 |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|-------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                 |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies) |
| S.No                                            | Project                                                                                         | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                  |
| 1                                               | 2                                                                                               | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 50                                              | MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND      | 05/2015                       | 1,154.18 -                         | 1,154.18                     | 862.45                             | 12/2017 -                          | 06/2019     | 18                    | 0                |                                                                  |
| 51                                              | NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND                              | 03/2015                       | 1,034.01 -                         | 1,034.01                     | 367.64                             | 10/2017 -                          | 06/2020     | 32                    | 0                |                                                                  |
| 52                                              | REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND                         | 11/2016                       | 262.87 -                           | 262.87                       | 77.06                              | 06/2019 -                          | 06/2020     | 12                    | 0                |                                                                  |
|                                                 | Total                                                                                           |                               | 26,430.72 -                        | 26,072.72                    | 20,708.77                          |                                    |             |                       |                  |                                                                  |
|                                                 |                                                                                                 |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                                 | <u>PETROLEUM</u>                                                                                |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                                 | <u>Bharat Petroleum Corporation Limited</u>                                                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 53                                              | HALDIA LPG IMPORT FACILITY - [N16000223]BPCL, WEST BENGAL                                       | 03/2015                       | 694.00 1,097.54                    | 694.00                       | 530.79                             | 10/2018 06/2019                    | 06/2019     | 8                     | 0                |                                                                  |
| 54                                              | PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA    | 11/2014                       | 4,588.29 5,245.96                  | 5,245.96                     | 2,543.09                           | 08/2018 11/2019                    | 11/2019     | 15                    | 14.33            |                                                                  |
| 55                                              | MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA | 02/2016                       | 3,313.00 3,288.96                  | 3,288.96                     | 404.03                             | 02/2020 10/2020                    | 10/2020     | 8                     | -73              |                                                                  |
|                                                 | <u>Gas Authority Of India Limited</u>                                                           |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 56                                              | PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE                           | 03/2015                       | 3,957.00 3,561.00                  | 3,397.00                     | 2,382.96                           | 12/2018 -                          | 03/2019     | 3                     | -14.15           |                                                                  |
| 57                                              | AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]GAIL,UTTAR PRADESH                                | 07/2015                       | 1,427.94 -                         | 800.00                       | 603.92                             | 12/2018 -                          | 03/2019     | 3                     | -43.98           |                                                                  |
| 58                                              | CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT                          | 04/2016                       | 327.78 -                           | 200.00                       | 116.19                             | 04/2018 -                          | 03/2019     | 11                    | -38.98           |                                                                  |
| 59                                              | KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE             | 06/2009                       | 2,915.00 3,030.00                  | 2,915.00                     | 2,009.30                           | 12/2012 02/2019                    | 06/2019     | 78                    | 0                |                                                                  |
|                                                 | <u>Hindustan Petroleum Corporation Limited</u>                                                  |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 60                                              | URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE                                | 12/2009                       | 309.81 723.40                      | 723.40                       | 586.10                             | 10/2014 02/2019                    | 02/2019     | 52                    | 133.5            |                                                                  |
|                                                 | <u>Indian Oil Corporation Limited</u>                                                           |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                                                     |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies) |
| S.No                                            | Project                                                                                                                             | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                  |
| 1                                               | 2                                                                                                                                   | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 61                                              | POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA                                                                    | 03/2014                       | 3,150.00 -                         | 3,150.00                     | 2,494.51                           | 09/2017<br>12/2018                 | 12/2018     | 15                    | 0                |                                                                  |
| 62                                              | LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA                                                                                      | 10/2015                       | 607.06 -                           | 714.25                       | 352.32                             | 10/2017 -                          | 03/2019     | 17                    | 17.66            |                                                                  |
| 63                                              | DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL                                       | 03/2014                       | 3,076.00<br>4,190.00               | 4,190.00                     | 3,224.62                           | 09/2017<br>06/2018                 | 03/2019     | 18                    | 36.22            |                                                                  |
| 64                                              | FUEL QUALITY UPGRADATION (DHD/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR                                          | 07/2015                       | 822.66 -                           | 822.66                       | 868.92                             | 11/2018 -                          | 03/2019     | 4                     | 0                |                                                                  |
| 65                                              | PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE                                                                           | 01/2015                       | 690.00 -                           | 690.00                       | 191.48                             | 07/2018<br>10/2020                 | 10/2020     | 27                    | 0                |                                                                  |
| 66                                              | PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH | 08/2017                       | 236.00 -                           | 236.00                       | 11.66                              | 06/2020 -                          | 10/2020     | 4                     | 0                |                                                                  |
| 67                                              | ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU                     | 05/2016                       | 4,497.00 -                         | 4,497.00                     | 349.40                             | 12/2018 -                          | 12/2020     | 24                    | 0                |                                                                  |
| 68                                              | ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA     | 05/2016                       | 212.00 -                           | 212.00                       | 14.11                              | 01/2021 -                          | 04/2021     | 3                     | 0                |                                                                  |
| 69                                              | CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH                           | 08/2018                       | 466.00 -                           | 466.00                       | 1.53                               | 04/2021 -                          | 07/2021     | 3                     | 0                |                                                                  |
| 70                                              | CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU                                               | 12/2017                       | 466.43 -                           | 466.43                       | 1.18                               | 10/2020 -                          | 08/2021     | 10                    | 0                |                                                                  |
| 71                                              | ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA   | 05/2016                       | 348.00 -                           | 348.00                       | 9.20                               | 01/2021 -                          | 10/2021     | 9                     | 0                |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                               |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                                               |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies) |
| S.No                                            | Project                                                                                                                       | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                  |
| 1                                               | 2                                                                                                                             | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 72                                              | REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]OCL,UTTAR PRADESH            | 08/2017                       | 318.80 -                           | 318.80                       | 13.93                              | 08/2021 -                          | 11/2021     | 3                     | 0                |                                                                  |
|                                                 | <u>Oil &amp; Natural Gas Corporation Limited</u>                                                                              |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 73                                              | FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH                                  | 04/2017                       | 420.76 207.80                      | 207.80                       | 32.71                              | 09/2018 02/2019                    | 02/2019     | 5                     | -50.61           |                                                                  |
| 74                                              | ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM                                                                     | 03/2009                       | 2,465.15 -                         | 2,378.86                     | 2,107.69                           | 03/2013 03/2019                    | 03/2019     | 72                    | -3.5             |                                                                  |
| 75                                              | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA                         | 03/2011                       | 861.79 1,577.15                    | 1,577.15                     | 1,195.62                           | 05/2013 03/2019                    | 03/2019     | 70                    | 83.01            |                                                                  |
| 76                                              | Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU                                      | 11/2015                       | 390.52 390.52                      | 390.52                       | 174.22                             | 03/2019 -                          | 04/2019     | 1                     | 0                |                                                                  |
| 77                                              | LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA                                | 12/2015                       | 3,190.69 -                         | 3,247.19                     | 2,110.87                           | 04/2018 05/2019                    | 05/2019     | 13                    | 1.77             |                                                                  |
| 78                                              | DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI                                                                      | 08/2014                       | 6,086.08 5,842.31                  | 5,842.31                     | 4,513.89                           | 05/2019 10/2019                    | 10/2019     | 5                     | -4.01            |                                                                  |
| 79                                              | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM                                | 06/2010                       | 202.94 341.70                      | 330.35                       | 81.98                              | 01/2014 11/2019                    | 11/2019     | 70                    | 62.78            |                                                                  |
| 80                                              | INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA                                                          | 12/2011                       | 2,059.63 2,665.65                  | 2,665.65                     | 1,842.42                           | 03/2015 12/2019                    | 12/2019     | 57                    | 29.42            |                                                                  |
| 81                                              | ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA | 01/2015                       | 4,619.94 4,619.94                  | 4,619.94                     | 3,951.60                           | 12/2017 03/2020                    | 03/2020     | 27                    | 0                |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|---------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                                     |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies) |
| S.No                                            | Project                                                                                                             | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                  |
| 1                                               | 2                                                                                                                   | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 82                                              | NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA                   | 08/2015                       | 2,818.88 -                         | 2,818.88                     | 1,724.53                           | 03/2019<br>05/2020                 | 05/2020     | 14                    | 0                |                                                                  |
| 83                                              | KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH                                         | 03/2016                       | 34,012.00 -                        | 34,012.00                    | 1,647.21                           | 06/2020<br>08/2021                 | 08/2021     | 14                    | 0                |                                                                  |
|                                                 | <u>Oil India Limited</u>                                                                                            |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 84                                              | SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE | 07/2011                       | 352.56 -                           | 438.84                       | 196.39                             | 03/2017<br>06/2019                 | 06/2019     | 27                    | 24.47            |                                                                  |
| 85                                              | CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM                                           | 07/2011                       | 350.00 -                           | 350.00                       | 2.06                               | 01/2019<br>-                       | 09/2019     | 8                     | 0                |                                                                  |
|                                                 | Total                                                                                                               |                               | 90,253.71 -                        | 92,254.95                    | 36,290.43                          |                                    |             |                       |                  |                                                                  |
|                                                 |                                                                                                                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                                 | <u>POWER</u>                                                                                                        |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                                 | <u>Chenab Valley Power Projects [P] Limited</u>                                                                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 86                                              | PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR                                    | 10/2014                       | 8,112.12 -                         | 8,112.12                     | 982.71                             | 04/2020<br>-                       | 10/2023     | 42                    | 0                |                                                                  |
|                                                 | <u>National Hydro-Electric Power Corporation</u>                                                                    |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 87                                              | PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH                                                 | 09/2002                       | 3,919.59 -                         | 9,394.80                     | 7,145.69                           | 09/2009<br>-                       | 12/2021     | 147                   | 139.69           |                                                                  |
|                                                 | <u>National Thermal Power Corporation</u>                                                                           |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 88                                              | BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM                                                            | 01/2008                       | 4,375.35<br>8,150.00               | 8,150.00                     | 7,220.84                           | 09/2011<br>06/2018                 | 01/2019     | 88                    | 86.27            |                                                                  |
| 89                                              | SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA                                                                          | 03/2012                       | 9,395.18 -                         | 9,395.18                     | 9,026.43                           | 11/2016<br>03/2019                 | 03/2019     | 28                    | 0                |                                                                  |
| 90                                              | BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR                                                          | 01/2007                       | 5,353.00 -                         | 7,998.00                     | 7,511.72                           | 05/2014<br>-                       | 05/2019     | 60                    | 49.41            |                                                                  |
| 91                                              | LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH                                 | 12/2012                       | 11,846.00 -                        | 12,739.82                    | 10,831.46                          | 06/2017<br>06/2019                 | 06/2019     | 24                    | 7.55             |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                         |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                         |
|-------------------------------------------------|-----------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|-----------------------------------------------------------------------------------------|
|                                                 |                                                                                         |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  |                                                                                         |
| S.No                                            | Project                                                                                 | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) | Reasons for Delay (As Reported by Project Implementing Agencies)                        |
| 1                                               | 2                                                                                       | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                                                      |
| 92                                              | GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH          | 03/2013                       | 11,638.55 -                        | 12,865.92                    | 10,375.32                          | 09/2017<br>06/2019                 | 06/2019     | 21                    | 10.55            |                                                                                         |
| 93                                              | DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA                             | 02/2014                       | 12,532.44 -                        | 13,740.53                    | 8,441.41                           | 08/2018<br>06/2019                 | 06/2019     | 10                    | 9.64             |                                                                                         |
| 94                                              | MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH                          | 04/2012                       | 9,750.89 -                         | 9,750.89                     | 8,798.00                           | 12/2016 -                          | 08/2019     | 32                    | 0                |                                                                                         |
| 95                                              | TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH                           | 09/2014                       | 9,188.98 -                         | 9,188.98                     | 5,433.65                           | 03/2019<br>09/2019                 | 09/2019     | 6                     | 0                |                                                                                         |
| 96                                              | NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR                           | 01/2013                       | 12,964.60 -                        | 13,731.26                    | 12,593.00                          | 01/2018 -                          | 05/2020     | 28                    | 5.91             |                                                                                         |
| 97                                              | NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND                             | 02/2014                       | 14,366.58 -                        | 15,164.05                    | 7,916.41                           | 02/2019<br>10/2020                 | 10/2020     | 20                    | 5.55             |                                                                                         |
| 98                                              | TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA               | 01/2016                       | 10,598.98 -                        | 10,598.98                    | 3,272.35                           | 07/2020<br>10/2020                 | 10/2020     | 3                     | 0                |                                                                                         |
| 99                                              | TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND                           | 11/2006                       | 2,978.48 -                         | 3,846.30                     | 3,775.64                           | 03/2013<br>12/2020                 | 12/2020     | 93                    | 29.14            |                                                                                         |
| 100                                             | BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR                                         | 02/2005                       | 8,692.97<br>15,095.67              | 15,095.67                    | 15,278.98                          | 01/2011<br>04/2021                 | 04/2021     | 123                   | 73.65            |                                                                                         |
| 101                                             | RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL                                 | 09/2014                       | 1,381.84 -                         | 1,381.84                     | 384.28                             | 09/2019<br>02/2022                 | 02/2022     | 29                    | 0                |                                                                                         |
|                                                 | <u>North East Electric Power Corporation</u>                                            |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                         |
| 102                                             | KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH             | 12/2004                       | 2,496.90<br>6,179.96               | 6,179.96                     | 6,881.48                           | 12/2009<br>03/2019                 | 03/2019     | 111                   | 147.51           |                                                                                         |
|                                                 | <u>Power Grid Corporation Of India Limited</u>                                          |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                         |
| 103                                             | 400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270]PGCIL,MULTI STATE | 08/2008                       | 771.00<br>1,624.00                 | 1,624.00                     | 1,577.20                           | 02/2013<br>07/2018                 | 12/2018     | 70                    | 110.64           |                                                                                         |
| 104                                             | TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN  | 07/2015                       | 307.18<br>307.18                   | 307.18                       | 210.91                             | 11/2017<br>10/2018                 | 01/2019     | 14                    | 0                | Generation project delayed (now ant. by Mar'20). Working permission received in Jun'18. |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                   |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                                                                                                                                                                                                        |
|-------------------------------------------------|---------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
|                                                 |                                                                                                   |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  |                                                                                                                                                                                                                                                                                                        |
| S.No                                            | Project                                                                                           | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) | Reasons for Delay (As Reported by Project Implementing Agencies)                                                                                                                                                                                                                                       |
| 1                                               | 2                                                                                                 | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                                                                                                                                                                                                                                                                     |
| 105                                             | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH          | 01/2016                       | 305.04<br>305.04                   | 305.04                       | 229.91                             | 03/2017<br>09/2018                 | 01/2019     | 22                    | 0                |                                                                                                                                                                                                                                                                                                        |
| 106                                             | WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA                              | 12/2007                       | 477.69<br>738.48                   | 738.48                       | 686.26                             | 09/2010<br>12/2018                 | 02/2019     | 101                   | 54.59            |                                                                                                                                                                                                                                                                                                        |
| 107                                             | SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE                      | 12/2011                       | 297.33<br>534.02                   | 534.02                       | 441.08                             | 08/2014<br>09/2018                 | 02/2019     | 54                    | 79.61            |                                                                                                                                                                                                                                                                                                        |
| 108                                             | EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE                              | 10/2013                       | 1,364.52<br>1,891.41               | 1,891.41                     | 1,216.98                           | 04/2016<br>12/2018                 | 02/2019     | 34                    | 38.61            | Severe ROW problem at Rajarhat area due to protest by political groups. Work in Rajarhat was on hold since Jan'17. Work of TL resumed in Jun'18 & substation resumed in Aug'18 after intervention from State and Distt. Admn. Presently, works of TL at 2 loc. in Distt. Pargana 24 South are held up. |
| 109                                             | AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE           | 03/2014                       | 155.57<br>206.42                   | 206.42                       | 145.82                             | 03/2016<br>09/2018                 | 02/2019     | 35                    | 32.69            | Downstream line by State Govt. at Hamirpur delayed.                                                                                                                                                                                                                                                    |
| 110                                             | TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE               | 01/2015                       | 268.80<br>340.88                   | 340.88                       | 241.30                             | 03/2018<br>09/2018                 | 02/2019     | 11                    | 26.82            |                                                                                                                                                                                                                                                                                                        |
| 111                                             | GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE     | 04/2015                       | 3,705.61<br>3,705.61               | 3,705.61                     | 2,549.30                           | 04/2018<br>09/2018                 | 02/2019     | 10                    | 0                |                                                                                                                                                                                                                                                                                                        |
| 112                                             | EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE                             | 05/2016                       | 766.21<br>766.21                   | 766.21                       | 454.34                             | 11/2018<br>11/2018                 | 02/2019     | 3                     | 0                |                                                                                                                                                                                                                                                                                                        |
| 113                                             | TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT | 07/2016                       | 300.94<br>300.94                   | 300.94                       | 219.36                             | 12/2018<br>12/2018                 | 02/2019     | 2                     | 0                |                                                                                                                                                                                                                                                                                                        |
| 114                                             | WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE                            | 07/2016                       | 150.99<br>150.99                   | 150.99                       | 95.16                              | 07/2018<br>07/2018                 | 02/2019     | 7                     | 0                | Completion delayed due to non-availability of downstream system by MPPTCL.                                                                                                                                                                                                                             |
| 115                                             | KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU                               | 05/2005                       | 1,779.29<br>2,187.32               | 2,187.32                     | 2,092.52                           | 11/2008<br>09/2018                 | 03/2019     | 124                   | 22.93            |                                                                                                                                                                                                                                                                                                        |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                   |
|-------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|-----------------------------------------------------------------------------------|
|                                                 |                                                                                                                                     |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  |                                                                                   |
| S.No                                            | Project                                                                                                                             | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) | Reasons for Delay (As Reported by Project Implementing Agencies)                  |
| 1                                               | 2                                                                                                                                   | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                                                |
| 116                                             | SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE                                                                 | 10/2011                       | 487.49<br>639.46                   | 639.46                       | 509.60                             | 06/2014<br>12/2018                 | 03/2019     | 57                    | 31.17            |                                                                                   |
| 117                                             | UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE                                                  | 01/2014                       | 374.63<br>374.63                   | 374.63                       | 187.24                             | 04/2016<br>12/2017                 | 03/2019     | 35                    | 0                |                                                                                   |
| 118                                             | NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE                                                    | 02/2014                       | 539.82<br>539.82                   | 539.82                       | 423.73                             | 06/2016<br>09/2018                 | 03/2019     | 33                    | 0                |                                                                                   |
| 119                                             | EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE                                                              | 02/2014                       | 196.58<br>225.28                   | 225.28                       | 151.02                             | 02/2016<br>09/2018                 | 03/2019     | 37                    | 14.6             |                                                                                   |
| 120                                             | ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE | 03/2015                       | 197.40<br>197.40                   | 197.40                       | 74.71                              | 03/2018<br>-                       | 03/2019     | 12                    | 0                |                                                                                   |
| 121                                             | TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN                                                 | 07/2016                       | 1,429.38<br>1,429.38               | 1,429.38                     | 849.56                             | 01/2019<br>01/2019                 | 03/2019     | 2                     | 0                | Progress affected due to delay in forest clearance, awaited. ROW also being faced |
| 122                                             | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE                                           | 10/2008                       | 4,824.12<br>5,071.94               | 5,071.94                     | 4,545.57                           | 10/2012<br>12/2018                 | 06/2019     | 80                    | 5.14             |                                                                                   |
| 123                                             | EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE                                                              | 05/2014                       | 522.29<br>55,018.00                | 550.18                       | 445.93                             | 11/2016<br>06/2019                 | 06/2019     | 31                    | 5.34             |                                                                                   |
| 124                                             | TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE            | 06/2014                       | 5,151.37<br>5,151.37               | 5,151.37                     | 2,892.80                           | 03/2018<br>03/2019                 | 06/2019     | 15                    | 0                |                                                                                   |
| 125                                             | SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE                                                      | 01/2015                       | 203.28<br>260.03                   | 260.03                       | 187.06                             | 07/2017<br>06/2019                 | 06/2019     | 23                    | 27.92            |                                                                                   |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                                  |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                     |
|-------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
|                                                 |                                                                                                                                  |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies)                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    |
| S.No                                            | Project                                                                                                                          | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                     |
| 1                                               | 2                                                                                                                                | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  |
| 126                                             | CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI                     | 03/2015                       | 1,394.52<br>1,394.52               | 1,394.52                     | 260.99                             | 05/2017<br>06/2019                 | 06/2019     | 25                    | 0                | Implementation affected due to delayed land acquisition (land handed over for Dwarka-I S/s in Aug'16 & Rajghat in Dec'16). Rajghat sub station annulled. Additional bays at Maharanibagh in place of Rajghat S/stn. However, only 400KV line bays are being made at Maharanibagh. Award placed in Jan'18. Forest proposal under DPTA & FCA submitted. Approval & tree cutting permission awaited. During meeting convened by MOUD in Nov'18, it has been decided to re-route the line (LILo at Dwarka-I) through Golf course to reduce forest area. |
| 127                                             | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE | 10/2016                       | 408.46<br>408.46                   | 408.46                       | 184.94                             | 01/2019<br>01/2019                 | 06/2019     | 5                     | 0                |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                     |
| 128                                             | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT               | 05/2017                       | 175.64<br>175.64                   | 175.64                       | 73.94                              | 09/2018<br>09/2018                 | 06/2019     | 9                     | 0                | Completion matching with Banaskantha (Radhanesda) S/stn. (Sch. by Jun'19). Gen. delayed (ant. by Dec'19).                                                                                                                                                                                                                                                                                                                                                                                                                                           |
| 129                                             | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA     | 05/2017                       | 445.89<br>445.89                   | 445.89                       | 220.56                             | 02/2019<br>02/2019                 | 06/2019     | 4                     | 0                |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                     |
| 130                                             | TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE                                | 01/2015                       | 871.62<br>871.62                   | 871.62                       | 432.72                             | 10/2017<br>09/2019                 | 09/2019     | 23                    | 0                |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                     |



## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                                                                                                                                                                                                                                                                                                                           |
|-------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
|                                                 |                                                                                                                                     |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  |                                                                                                                                                                                                                                                                                                                                                                                                                           |
| S.No                                            | Project                                                                                                                             | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) | Reasons for Delay (As Reported by Project Implementing Agencies)                                                                                                                                                                                                                                                                                                                                                          |
| 1                                               | 2                                                                                                                                   | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                                                                                                                                                                                                                                                                                                                                                                                        |
| 131                                             | TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE | 03/2016                       | 808.63<br>808.63                   | 808.63                       | 348.56                             | 01/2018<br>03/2019                 | 09/2019     | 20                    | 0                | Implementation affected due to forest (Tiger reserve) clearance. Line passing through buffer zone of Tiger reserve area. Wildlife proposal cleared in NBWL. Stage-I issued on 18.10.18. Demand note for all 3 divisions (except tree cutting & demarcation works) obtained. Payment completed. Gen. Project ant. by Jan/ Feb'19. Alternate arrangements made for evacuation (contingency through Punatsangchu ATS, ready) |
| 132                                             | COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE        | 12/2014                       | 4,754.42<br>4,754.42               | 9,141.97                     | 993.85                             | 12/2018<br>12/2018                 | 12/2019     | 12                    | 92.28            |                                                                                                                                                                                                                                                                                                                                                                                                                           |
| 133                                             | NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE                   | 12/2014                       | 5,111.33<br>5,111.33               | 6,652.57                     | 922.25                             | 12/2018<br>12/2018                 | 12/2019     | 12                    | 30.15            |                                                                                                                                                                                                                                                                                                                                                                                                                           |
| 134                                             | EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL                                                               | 04/2016                       | 454.11<br>454.11                   | 454.11                       | 249.92                             | 04/2018<br>01/2020                 | 01/2020     | 21                    | 0                |                                                                                                                                                                                                                                                                                                                                                                                                                           |
| 135                                             | 400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE                          | 09/2017                       | 198.49<br>198.49                   | 198.49                       | 15.70                              | 09/2019<br>02/2020                 | 02/2020     | 5                     | 0                |                                                                                                                                                                                                                                                                                                                                                                                                                           |
| 136                                             | NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE                                                   | 02/2009                       | 11,130.19<br>13,762.80             | 13,762.80                    | 12,723.70                          | 08/2013<br>03/2022                 | 03/2022     | 103                   | 23.65            |                                                                                                                                                                                                                                                                                                                                                                                                                           |
|                                                 | <u>Satluj Jal Vidyut Nigam Limited</u>                                                                                              |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                                                                                                                                                                                                                                                                                                                           |
| 137                                             | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR                                            | 05/2015                       | 436.68<br>-                        | 602.44                       | 537.08                             | 12/2016<br>-                       | 03/2019     | 27                    | 37.96            |                                                                                                                                                                                                                                                                                                                                                                                                                           |
| 138                                             | WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT                                             | 11/2016                       | 330.00<br>-                        | 330.00                       | 310.99                             | 11/2017<br>-                       | 03/2019     | 16                    | 0                |                                                                                                                                                                                                                                                                                                                                                                                                                           |
|                                                 | <u>Thdc India Limited</u>                                                                                                           |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                                                                                                                                                                                                                                                                                                                           |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                   |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                                                                                                                                                                                         |
|-------------------------------------------------|---------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
|                                                 |                                                                                                   |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  |                                                                                                                                                                                                                                                                                         |
| S.No                                            | Project                                                                                           | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) | Reasons for Delay (As Reported by Project Implementing Agencies)                                                                                                                                                                                                                        |
| 1                                               | 2                                                                                                 | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                                                                                                                                                                                                                                                      |
| 139                                             | DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH                                     | 05/2011                       | 195.42<br>294.60                   | 294.60                       | 221.63                             | 02/2014<br>02/2018                 | 03/2019     | 61                    | 50.75            | IIInd stage forest clearance of 1.39 Ha. land for compensatory afforestation in lieu of 1.39 Ha. forest land for power evacuation is pending.                                                                                                                                           |
| 140                                             | TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND                                | 07/2006                       | 1,657.00<br>2,978.86               | 4,401.90                     | 2,692.27                           | 02/2016<br>12/2020                 | 05/2021     | 63                    | 165.65           | Decision on renewal of 3.0 Ha land and compensatory afforestation of identified 10 Ha. land is to be expedited.                                                                                                                                                                         |
| 141                                             | VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND                        | 08/2008                       | 2,491.58<br>-                      | 4,105.30                     | 1,592.11                           | 06/2013<br>-                       | 12/2021     | 102                   | 64.77            | Post Award: 1. There were frequent hindrances by local villagers since mobilization of works since Jan 2014. Local hindrances have minimized in VPHEP with the strong intervention of MoP and support of District Administration. Regular support of Distt. Administration is required. |
|                                                 | Total                                                                                             |                               | 1,95,032.96<br>-                   | 2,38,881.23                  | 1,68,077.94                        |                                    |             |                       |                  |                                                                                                                                                                                                                                                                                         |
|                                                 |                                                                                                   |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                                                                                                                                                                                         |
|                                                 | <u>HEAVY INDUSTRY</u>                                                                             |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                                                                                                                                                                                         |
|                                                 | <u>Natrip Implementation Society</u>                                                              |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                                                                                                                                                                                         |
| 142                                             | NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]NATIS,MULTI STATE | 04/2011                       | 1,718.00<br>3,727.30               | 3,827.30                     | 2,933.23                           | 09/2011<br>06/2019                 | 06/2019     | 93                    | 122.78           |                                                                                                                                                                                                                                                                                         |
|                                                 | Total                                                                                             |                               | 1,718.00<br>-                      | 3,827.30                     | 2,933.23                           |                                    |             |                       |                  |                                                                                                                                                                                                                                                                                         |
|                                                 |                                                                                                   |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                                                                                                                                                                                         |
|                                                 | <u>HEALTH AND FAMILY WELFARE</u>                                                                  |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                                                                                                                                                                                         |
|                                                 | <u>Hospital Services Consultancy Corporation Ltd</u>                                              |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                                                                                                                                                                                         |
| 143                                             | AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI                                                          | 08/2014                       | 293.65<br>-                        | 293.65                       | 273.80                             | 05/2017<br>06/2018                 | 03/2019     | 22                    | 0                |                                                                                                                                                                                                                                                                                         |
| 144                                             | SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB                           | 07/2016                       | 152.95<br>-                        | 152.95                       | 83.11                              | 02/2018<br>02/2018                 | 06/2019     | 16                    | 0                |                                                                                                                                                                                                                                                                                         |
| 145                                             | AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI                                            | 12/2013                       | 204.44<br>-                        | 204.44                       | 173.67                             | 05/2017<br>06/2018                 | 07/2019     | 26                    | 0                |                                                                                                                                                                                                                                                                                         |
| 146                                             | LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI                                             | 02/2013                       | 414.11<br>-                        | 513.89                       | 141.00                             | 11/2013<br>10/2020                 | 10/2020     | 83                    | 24.1             |                                                                                                                                                                                                                                                                                         |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|---------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                                     |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies) |
| S.No                                            | Project                                                                                                             | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                  |
| 1                                               | 2                                                                                                                   | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 147                                             | NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA                                                             | 10/2016                       | 363.99 -                           | 363.99                       | 112.29                             | 05/2018<br>09/2019                 | 08/2019     | 15                    | 0                |                                                                  |
|                                                 | Total                                                                                                               |                               | 1,429.14 -                         | 1,528.92                     | 783.87                             |                                    |             |                       |                  |                                                                  |
|                                                 | <u>RAILWAYS</u>                                                                                                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                                 | <u>Central Railways</u>                                                                                             |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 148                                             | MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA                                                    | 02/2016                       | 1,035.16<br>1,035.16               | 1,035.16                     | 19.79                              | 03/2022 -                          | 03/2023     | 12                    | 0                |                                                                  |
|                                                 | <u>Container Corporation Of India</u>                                                                               |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 149                                             | MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH                                                 | 12/2015                       | 174.00 -                           | 174.00                       | 139.38                             | 03/2019 -                          | 08/2019     | 5                     | 0                |                                                                  |
| 150                                             | MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN                                                  | 01/2011                       | 493.17 -                           | 493.17                       | 413.97                             | 03/2018 -                          | 12/2019     | 21                    | 0                |                                                                  |
| 151                                             | MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT                                                     | 10/2013                       | 343.00 -                           | 343.00                       | 289.38                             | 03/2019 -                          | 12/2019     | 9                     | 0                |                                                                  |
| 152                                             | MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH                                             | 08/2016                       | 234.50 -                           | 235.00                       | 2.98                               | 03/2019 -                          | 12/2020     | 21                    | .21              |                                                                  |
|                                                 | <u>East Central Railways</u>                                                                                        |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 153                                             | KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH                                                  | 08/2015                       | 528.57 -                           | 528.57                       | 19.97                              | 03/2019 -                          | 12/2019     | 9                     | 0                |                                                                  |
| 154                                             | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR                                                    | 04/1997                       | 324.73 -                           | 1,156.41                     | 876.49                             | 03/2012 -                          | 03/2020     | 96                    | 256.11           |                                                                  |
| 155                                             | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR                                            | 04/1996                       | 477.88<br>283.95                   | 749.00                       | 495.40                             | 03/2012 -                          | 03/2020     | 96                    | 56.73            |                                                                  |
| 156                                             | HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE                                                                    | 05/2015                       | 678.54 -                           | 678.54                       | -                                  | 03/2019 -                          | 03/2020     | 12                    | 0                |                                                                  |
| 157                                             | RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH                                                           | 08/2015                       | 2,436.21 -                         | 2,436.21                     | 291.68                             | 03/2020 -                          | 03/2021     | 12                    | 0                |                                                                  |
| 158                                             | PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]ECR,BIHAR | 11/2001                       | 624.47 -                           | 3,550.00                     | 97.63                              | 02/2016 -                          | 03/2021     | 61                    | 468.48           |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                              |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                         |
|-------------------------------------------------|----------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|-------------------------------------------------------------------------------------------------------------------------|
|                                                 |                                                                                              |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies)                                                        |
| S.No                                            | Project                                                                                      | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                                                                         |
| 1                                               | 2                                                                                            | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                                                                                      |
| 159                                             | KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR                                          | 12/2015                       | 1,200.20 -                         | 1,200.20                     | -                                  | 03/2020 -                          | 10/2021     | 19                    | 0                |                                                                                                                         |
| 160                                             | RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR      | 12/2015                       | 1,491.47 -                         | 1,491.47                     | -                                  | 03/2020 -                          | 10/2021     | 19                    | 0                |                                                                                                                         |
| 161                                             | SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR                                | 04/2016                       | 744.04 -                           | 1,215.54                     | 1.81                               | 03/2021 -                          | 03/2022     | 12                    | 63.37            |                                                                                                                         |
| 162                                             | MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR                                | 04/2016                       | 731.64 -                           | 1,185.73                     | -                                  | 03/2021 -                          | 03/2022     | 12                    | 62.06            |                                                                                                                         |
|                                                 | <u>East Coast Railway</u>                                                                    |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                         |
| 163                                             | SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA                                          | 03/2011                       | 1,111.99<br>1,539.28               | 1,539.28                     | 765.60                             | 02/2019 -                          | 03/2021     | 25                    | 38.43            |                                                                                                                         |
| 164                                             | BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA                                         | 03/2013                       | 843.04<br>843.04                   | 843.04                       | 81.26                              | 10/2020 -                          | 03/2021     | 5                     | 0                |                                                                                                                         |
| 165                                             | JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA | 04/2015                       | 701.61 -                           | 810.02                       | 88.04                              | 11/2018 -                          | 03/2021     | 28                    | 15.45            |                                                                                                                         |
| 166                                             | BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA                | 04/2015                       | 1,172.92 -                         | 1,172.92                     | 245.16                             | 12/2018 -                          | 03/2021     | 27                    | 0                |                                                                                                                         |
| 167                                             | KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA                                        | 04/1994                       | 2,923.13 -                         | 3,798.80                     | 1,123.73                           | 03/2009 -                          | 06/2021     | 147                   | 29.96            |                                                                                                                         |
| 168                                             | TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA                                        | 04/2005                       | 810.78 -                           | 1,928.07                     | 574.98                             | 06/2021 -                          | 03/2023     | 21                    | 137.8            |                                                                                                                         |
|                                                 | <u>Eastern Railways</u>                                                                      |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                         |
| 169                                             | MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND                                 | 04/1995                       | 1,125.89 -                         | 1,126.36                     | 2,012.33                           | 03/2016 -                          | 03/2020     | 48                    | .04              | Acquisition by State Govt. is awaited.                                                                                  |
| 170                                             | SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE     | 04/2010                       | 277.28 -                           | 266.52                       | 137.93                             | 03/2016 -                          | 03/2020     | 48                    | -3.88            | For Bira - Chakla (11.50) New line- The work will start after acquisition and handing over of land by State Government. |
|                                                 | <u>Metropolitan Rapid Transport Projects</u>                                                 |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                         |
| 171                                             | EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU            | 04/2006                       | 495.74<br>495.74                   | 734.01                       | 445.91                             | 06/2013<br>03/2019                 | 03/2019     | 69                    | 48.06            |                                                                                                                         |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                        |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|--------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                        |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies) |
| S.No                                            | Project                                                                                                | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                  |
| 1                                               | 2                                                                                                      | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 172                                             | MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA                                 | 04/2008                       | 5,300.00 -                         | 7,986.04                     | 2,423.55                           | 03/2014 -                          | 03/2019     | 60                    | 50.68            |                                                                  |
| 173                                             | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA                       | 03/1996                       | 495.44<br>1,781.98                 | 1,781.98                     | 1,337.62                           | 03/2004 -                          | 03/2020     | 192                   | 259.68           |                                                                  |
|                                                 | <u>North East Frontier Railway</u>                                                                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 174                                             | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE                  | 04/2000                       | 1,180.19<br>2,531.34               | 3,040.00                     | 3,065.47                           | 12/2008 -                          | 03/2019     | 123                   | 157.59           |                                                                  |
| 175                                             | AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA                                                   | 04/2008                       | 1,142.00<br>3,407.00               | 3,407.00                     | 3,112.16                           | 03/2014<br>12/2019                 | 03/2019     | 60                    | 198.34           |                                                                  |
| 176                                             | NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL | 04/1983                       | 297.32<br>200.34                   | 614.00                       | 270.27                             | 03/2019 -                          | 03/2020     | 12                    | 106.51           |                                                                  |
| 177                                             | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR                                          | 04/2003                       | 4,454.17 -                         | 13,809.00                    | 8,304.86                           | 03/2011 -                          | 03/2020     | 108                   | 210.02           |                                                                  |
| 178                                             | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM                | 09/2006                       | 385.20 -                           | 1,532.00                     | 574.07                             | 03/2019 -                          | 03/2020     | 12                    | 297.72           |                                                                  |
| 179                                             | NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR                       | 09/2006                       | 532.87<br>2,132.03                 | 2,145.00                     | 930.13                             | 03/2019 -                          | 03/2020     | 12                    | 302.54           |                                                                  |
| 180                                             | SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM                                                            | 04/2008                       | 1,339.48 -                         | 4,084.69                     | 383.92                             | 12/2015 -                          | 03/2020     | 51                    | 204.95           |                                                                  |
| 181                                             | BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM                                                   | 04/2008                       | 2,393.47<br>2,393.48               | 4,968.00                     | 2,516.15                           | 03/2014<br>12/2020                 | 12/2020     | 81                    | 107.56           |                                                                  |
| 182                                             | NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND              | 04/2006                       | 2,326.52<br>2,446.57               | 3,000.00                     | 677.37                             | 03/2015<br>10/2021                 | 10/2021     | 79                    | 28.95            |                                                                  |
| 183                                             | AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA                                                          | 04/2012                       | 569.63 -                           | 650.00                       | -                                  | 03/2020 -                          | 10/2022     | 31                    | 14.11            |                                                                  |
|                                                 | <u>North Eastern Railway</u>                                                                           |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 184                                             | AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER, UTTAR PRADESH                                 | 03/2012                       | 199.75 -                           | 270.00                       | 263.56                             | 08/2018 -                          | 01/2019     | 5                     | 35.17            |                                                                  |
| 185                                             | CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE                                                        | 03/2013                       | 295.00 -                           | 477.31                       | 186.71                             | 01/2019 -                          | 02/2019     | 1                     | 61.8             |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|----------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                                |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies) |
| S.No                                            | Project                                                                                                        | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                  |
| 1                                               | 2                                                                                                              | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 186                                             | MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]NER,UTTAR PRADESH                                         | 04/1997                       | 609.04<br>1,063.00                 | 1,807.88                     | 1,805.97                           | 04/1999<br>-                       | 03/2019     | 239                   | 196.84           |                                                                  |
| 187                                             | SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH | 04/2016                       | 1,177.96<br>-                      | 1,028.95                     | 1.54                               | 03/2014<br>-                       | 04/2021     | 85                    | -12.65           |                                                                  |
| 188                                             | INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH                                            | 04/2016                       | 213.00<br>-                        | 213.35                       | .55                                | 04/2016<br>-                       | 01/2022     | 69                    | .16              |                                                                  |
| 189                                             | ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH                                                       | 04/2017                       | 276.90<br>-                        | 276.90                       | -                                  | 04/2017<br>-                       | 04/2022     | 60                    | 0                |                                                                  |
| 190                                             | NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH                                           | 04/2017                       | 150.00<br>-                        | 150.00                       | -                                  | 04/2017<br>-                       | 10/2022     | 66                    | 0                |                                                                  |
| 191                                             | PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH                                        | 04/2017                       | 622.50<br>427.00                   | 426.74                       | 40.34                              | 04/2017<br>-                       | 10/2022     | 66                    | -31.45           |                                                                  |
|                                                 | <u>North Western Railway</u>                                                                                   |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 192                                             | JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN                   | 04/2008                       | 653.19<br>-                        | 1,116.00                     | 820.02                             | 03/2014<br>03/2019                 | 03/2019     | 60                    | 70.85            |                                                                  |
| 193                                             | ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN                                                             | 04/2013                       | 242.09<br>-                        | 349.00                       | 293.97                             | 02/2019<br>-                       | 03/2019     | 1                     | 44.16            |                                                                  |
| 194                                             | HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN                                        | 04/2008                       | 829.74<br>-                        | 1,216.00                     | 730.74                             | 03/2015<br>-                       | 06/2020     | 63                    | 46.55            |                                                                  |
|                                                 | <u>Northern Railway</u>                                                                                        |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 195                                             | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR                                          | 03/1995                       | 2,500.00<br>-                      | 27,949.00                    | 16,834.42                          | 11/2002<br>-                       | 03/2021     | 220                   | 1017.96          |                                                                  |
|                                                 | <u>Rail Vikas Nigam Ltd.</u>                                                                                   |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 196                                             | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA                                             | 04/2000                       | 133.41<br>207.00                   | 385.00                       | 377.10                             | 03/2009<br>03/2009                 | 02/2019     | 119                   | 188.58           |                                                                  |
| 197                                             | SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH                                              | 09/2006                       | 383.54<br>-                        | 555.00                       | 726.22                             | 03/2010<br>-                       | 12/2019     | 117                   | 44.7             |                                                                  |
| 198                                             | HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA                                                               | 04/1996                       | 1,185.64<br>-                      | 1,844.47                     | 1,406.23                           | 12/2017<br>-                       | 03/2020     | 27                    | 55.57            |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                            |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                                            |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  |                                                                  |
| S.No                                            | Project                                                                                                                    | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) | Reasons for Delay (As Reported by Project Implementing Agencies) |
| 1                                               | 2                                                                                                                          | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 199                                             | OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH                                                        | 07/2006                       | 732.81 -                           | 1,850.00                     | 1,981.73                           | 03/2008 -                          | 03/2020     | 144                   | 152.45           |                                                                  |
| 200                                             | LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH                                                | 04/2011                       | 927.01 -                           | 977.00                       | 983.62                             | 03/2019 -                          | 03/2020     | 12                    | 5.39             |                                                                  |
| 201                                             | MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA                                          | 04/2012                       | 632.68 -                           | 816.55                       | 846.22                             | 03/2016<br>03/2017                 | 12/2020     | 57                    | 29.06            |                                                                  |
| 202                                             | BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA                                                                    | 03/2009                       | 942.95 -                           | 942.95                       | 887.88                             | 03/2019 -                          | 03/2021     | 24                    | 0                |                                                                  |
| 203                                             | BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH                                             | 03/2012                       | 1,183.25 -                         | 1,183.25                     | 1,002.84                           | 12/2020 -                          | 03/2021     | 3                     | 0                |                                                                  |
| 204                                             | SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA                                                                   | 04/1998                       | 1,202.70<br>245.00                 | 1,202.70                     | 698.59                             | 02/2015 -                          | 12/2021     | 82                    | 0                |                                                                  |
| 205                                             | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH                             | 04/1995                       | 631.78<br>632.00                   | 1,195.00                     | 624.13                             | 12/2012 -                          | 03/2022     | 111                   | 89.15            |                                                                  |
| 206                                             | VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH                                      | 03/2012                       | 1,503.71 -                         | 1,503.71                     | 1,134.27                           | 03/2020 -                          | 03/2022     | 24                    | 0                |                                                                  |
| 207                                             | VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH                                                     | 04/2015                       | 943.60 -                           | 943.60                       | 298.09                             | 03/2022 -                          | 12/2024     | 33                    | 0                |                                                                  |
| 208                                             | MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH                                                             | 04/2015                       | 1,765.92 -                         | 1,765.92                     | 335.37                             | 03/2023 -                          | 12/2024     | 21                    | 0                |                                                                  |
| 209                                             | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL | 04/2010                       | 3,951.98 -                         | 4,259.48                     | 1,685.82                           | 03/2016 -                          | 03/2025     | 108                   | 7.78             |                                                                  |
| 210                                             | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL             | 04/2010                       | 2,913.51<br>4,200.00               | 2,913.50                     | 885.48                             | 03/2016 -                          | 03/2025     | 108                   | 0                |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                                 |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                                                 |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  |                                                                  |
| S.No                                            | Project                                                                                                                         | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) | Reasons for Delay (As Reported by Project Implementing Agencies) |
| 1                                               | 2                                                                                                                               | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 211                                             | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL | 04/2010                       | 2,298.42 -                         | 2,733.86                     | 347.70                             | 03/2014 -                          | 12/2025     | 141                   | 18.95            |                                                                  |
| 212                                             | RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL, UTTARAKHAND                                                                 | 04/2011                       | 16,216.00 -                        | 16,216.00                    | 861.35                             | 12/2024 -                          | 03/2026     | 15                    | 0                |                                                                  |
|                                                 | <u>South Central Railway</u>                                                                                                    |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 213                                             | MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE                                                                  | 04/1997                       | 1,723.00 1.00                      | 645.00                       | 725.63                             | 03/2000 -                          | 03/2019     | 228                   | -62.57           |                                                                  |
| 214                                             | MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, TELANGANA                                                                  | 04/2006                       | 1,160.48 -                         | 1,160.47                     | 111.36                             | 03/2010 -                          | 03/2022     | 144                   | 0                |                                                                  |
| 215                                             | NADIKUDE-SRI KALAHASTI - [N22000286]SCR, ANDHRA PRADESH                                                                         | 04/2011                       | 2,288.70 -                         | 2,288.70                     | 375.28                             | 03/2021 -                          | 03/2022     | 12                    | 0                |                                                                  |
| 216                                             | KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH                                                                 | 12/2001                       | 1,045.20 -                         | 2,120.16                     | 289.91                             | 03/2009 -                          | 03/2023     | 168                   | 102.85           |                                                                  |
| 217                                             | KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR, MULTI STATE                                                    | 04/2008                       | 2,132.77 -                         | 2,132.77                     | 216.07                             | 03/2014 -                          | 03/2023     | 108                   | 0                |                                                                  |
| 218                                             | GUNTUR-GUNTAKAL - [N22000368]SCR, ANDHRA PRADESH                                                                                | 04/2016                       | 3,631.00 -                         | 3,631.00                     | 124.49                             | 03/2022 -                          | 03/2023     | 12                    | 0                |                                                                  |
| 219                                             | KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR, MULTI STATE                                                  | 04/2012                       | 1,856.95 -                         | 2,200.00                     | 227.19                             | 03/2023 -                          | 03/2024     | 12                    | 18.47            |                                                                  |
|                                                 | <u>South East Central Railway</u>                                                                                               |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 220                                             | CHHINDWARA-MANDLA FORT GC - [N22000481]SECR, MADHYA PRADESH                                                                     | 03/2011                       | 556.54 -                           | 1,342.46                     | 396.00                             | 03/2012 -                          | 03/2020     | 96                    | 141.22           |                                                                  |
|                                                 | <u>South Eastern Railway</u>                                                                                                    |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 221                                             | DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND                                                             | 04/2010                       | 309.44 -                           | 525.81                       | 507.60                             | 12/2015 12/2018                    | 02/2019     | 38                    | 69.92            |                                                                  |
| 222                                             | RAJKHARSWAN-CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND                                                | 04/2012                       | 148.77 -                           | 377.00                       | 155.96                             | 12/2016 08/2018                    | 09/2019     | 33                    | 153.41           |                                                                  |
| 223                                             | ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER, ODISHA                                                                  | 11/2015                       | 969.83 -                           | 1,151.81                     | 389.91                             | 03/2020 03/2020                    | 06/2020     | 3                     | 18.76            |                                                                  |



## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                  |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                                  |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  |                                                                  |
| S.No                                            | Project                                                                                                          | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) | Reasons for Delay (As Reported by Project Implementing Agencies) |
| 1                                               | 2                                                                                                                | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 224                                             | BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND                                                            | 03/2016                       | 1,724.20<br>1,724.20               | 1,724.20                     | 175.49                             | 03/2021<br>03/2021                 | 12/2021     | 9                     | 0                |                                                                  |
| 225                                             | DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE                                          | 04/2010                       | 651.00<br>-                        | 1,009.00                     | 7.96                               | 03/2015<br>03/2024                 | 03/2024     | 108                   | 54.99            |                                                                  |
| 226                                             | RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADE FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA | 04/1995                       | 524.43<br>-                        | 939.00                       | 184.10                             | 12/2021<br>12/2024                 | 12/2024     | 36                    | 79.05            |                                                                  |
| 227                                             | BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL                           | 04/1998                       | 1,027.40<br>1,966.70               | 2,373.00                     | 484.85                             | 03/2003<br>03/2030                 | 03/2030     | 324                   | 130.97           |                                                                  |
|                                                 | <u>South Western Railway</u>                                                                                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 228                                             | KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA                                         | 03/1996                       | 644.78<br>889.52                   | 889.52                       | 433.71                             | 03/2017<br>-                       | 03/2020     | 36                    | 37.96            |                                                                  |
| 229                                             | HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA                                                                      | 03/2015                       | 1,156.94<br>1,156.94               | 1,156.94                     | 701.76                             | 03/2020<br>03/2020                 | 03/2021     | 12                    | 0                |                                                                  |
| 230                                             | HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE                                                                   | 03/2015                       | 1,614.59<br>1,870.41               | 1,870.41                     | 732.88                             | 03/2019<br>03/2021                 | 03/2021     | 24                    | 15.84            |                                                                  |
| 231                                             | BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA                                                                   | 04/2010                       | 986.30<br>986.30                   | 986.30                       | 287.03                             | 03/2016<br>12/2023                 | 12/2023     | 93                    | 0                |                                                                  |
| 232                                             | MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA                                                                   | 04/2012                       | 279.54<br>279.54                   | 279.54                       | 8.80                               | 03/2016<br>12/2023                 | 12/2023     | 93                    | 0                |                                                                  |
| 233                                             | BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA                                                    | 04/1996                       | 1,382.78<br>1,382.78               | 1,382.78                     | 7.35                               | 03/2002<br>03/2024                 | 03/2024     | 264                   | 0                |                                                                  |
| 234                                             | SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA                                                                    | 04/2011                       | 832.47<br>-                        | 832.47                       | .94                                | 03/2016<br>03/2024                 | 03/2024     | 96                    | 0                |                                                                  |
| 235                                             | GADAG-WADI NL - [N22000299]SWR,KARNATAKA                                                                         | 04/2013                       | 2,841.84<br>2,841.84               | 2,841.84                     | 39.98                              | 12/2018<br>12/2024                 | 12/2024     | 72                    | 0                |                                                                  |
|                                                 | <u>Southern Railway</u>                                                                                          |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 236                                             | OMALUR-METTURDAM-DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU                                  | 10/2013                       | 187.26<br>-                        | 231.67                       | 7.62                               | 04/2014<br>-                       | 03/2020     | 71                    | 23.72            |                                                                  |
| 237                                             | TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU                              | 02/2017                       | 1,567.00<br>-                      | 1,567.00                     | -                                  | 03/2024<br>-                       | 03/2026     | 24                    | 0                |                                                                  |
|                                                 | <u>West Central Railway</u>                                                                                      |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 238                                             | KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH                                               | 12/2015                       | 1,763.93<br>-                      | 1,763.93                     | -                                  | 03/2020<br>-                       | 10/2021     | 19                    | 0                |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                                   |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                                                   |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  |                                                                  |
| S.No                                            | Project                                                                                                                           | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) | Reasons for Delay (As Reported by Project Implementing Agencies) |
| 1                                               | 2                                                                                                                                 | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 239                                             | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE                                                               | 09/1998                       | 247.66 -                           | 6,093.31                     | 972.82                             | 05/2008 -                          | 03/2023     | 178                   | 2360.35          |                                                                  |
|                                                 | <u>Western Railway</u>                                                                                                            |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 240                                             | BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT                                                  | 04/2008                       | 318.24 -                           | 321.62                       | 83.53                              | 03/2012 -                          | 03/2019     | 84                    | 1.06             |                                                                  |
| 241                                             | RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT             | 04/1994                       | 320.66<br>1,378.12                 | 858.96                       | 549.56                             | 03/2019<br>03/2019                 | 03/2022     | 36                    | 167.87           |                                                                  |
|                                                 | Total                                                                                                                             |                               | 1,20,608.03 -                      | 1,96,974.52                  | 75,977.23                          |                                    |             |                       |                  |                                                                  |
|                                                 |                                                                                                                                   |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                                 | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                                |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                                 | <u>Ministry Of Road Transport And Highways</u>                                                                                    |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 242                                             | WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN | 02/2015                       | 383.40 -                           | 383.40                       | 224.68                             | 03/2015 -                          | 06/2019     | 51                    | 0                |                                                                  |
|                                                 | <u>National Highways And Infrastructure Development Corporation Ltd.</u>                                                          |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 243                                             | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND | 03/2016                       | 373.07 -                           | 373.07                       | -                                  | 08/2016 -                          | 08/2019     | 36                    | 0                |                                                                  |
| 244                                             | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND | 03/2016                       | 396.52 -                           | 396.52                       | -                                  | 08/2016 -                          | 08/2019     | 36                    | 0                |                                                                  |
| 245                                             | FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND | 03/2016                       | 429.52 -                           | 429.52                       | -                                  | 08/2016 -                          | 08/2019     | 36                    | 0                |                                                                  |
| 246                                             | CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH                       | 12/2016                       | 138.93<br>155.00                   | 155.00                       | -                                  | 01/2017 -                          | 01/2020     | 36                    | 11.57            |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                                 |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                                                 |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies) |
| S.No                                            | Project                                                                                                                         | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                  |
| 1                                               | 2                                                                                                                               | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
|                                                 | <u>National Highways Authority Of India</u>                                                                                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 247                                             | 2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU                                          | 04/2012                       | 624.00 -                           | 624.00                       | 350.79                             | 04/2014 -                          | 12/2019     | 68                    | 0                |                                                                  |
| 248                                             | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM                                                  | 12/2003                       | 280.00 -                           | 361.00                       | 410.32                             | 02/2009 -                          | 12/2018     | 118                   | 28.93            |                                                                  |
| 249                                             | SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU                            | 09/2011                       | 1,250.00 -                         | 1,250.00                     | 1,329.17                           | 12/2013 -                          | 12/2018     | 60                    | 0                |                                                                  |
| 250                                             | KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT                                                                                  | 01/2011                       | 953.88 -                           | 953.88                       | 976.28                             | 07/2013 -                          | 12/2018     | 65                    | 0                |                                                                  |
| 251                                             | TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU                                                 | 05/2010                       | 374.00 -                           | 374.00                       | 237.00                             | 05/2013 -                          | 12/2018     | 67                    | 0                |                                                                  |
| 252                                             | 2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU                                                     | 09/2011                       | 485.00 -                           | 485.00                       | 406.68                             | 08/2013 -                          | 12/2018     | 64                    | 0                |                                                                  |
| 253                                             | TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH                                                                 | 04/2011                       | 571.00 -                           | 571.00                       | 582.52                             | 10/2013 -                          | 12/2018     | 62                    | 0                |                                                                  |
| 254                                             | PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR                                                                  | 09/2011                       | 574.00 -                           | 574.00                       | 768.62                             | 03/2014 -                          | 12/2018     | 57                    | 0                |                                                                  |
| 255                                             | 2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR                                                                     | 05/2011                       | 511.54 -                           | 511.54                       | 564.35                             | 11/2013 -                          | 12/2018     | 61                    | 0                |                                                                  |
| 256                                             | TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 ( NEW NH NO -50) - [N24000342]NHAI,KARNATAKA | 05/2015                       | 709.00 -                           | 709.00                       | 380.95                             | 09/2017 -                          | 12/2018     | 15                    | 0                |                                                                  |
| 257                                             | 4 LANING OF AMBALA - KAITHAL - PACKAGE - 1 - [N24000443]NHAI,HARYANA                                                            | 12/2015                       | 602.95 -                           | 602.95                       | 54.89                              | 06/2016 -                          | 12/2018     | 30                    | 0                |                                                                  |
| 258                                             | 4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA                                                     | 01/2015                       | 972.50 -                           | 972.50                       | 1,484.99                           | 07/2017 -                          | 12/2018     | 17                    | 0                |                                                                  |
| 259                                             | FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH                                                                | 05/2013                       | 1,055.00 -                         | 1,601.77                     | 1,393.40                           | 11/2015 -                          | 12/2018     | 37                    | 51.83            |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                                  |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                                                  |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies) |
| S.No                                            | Project                                                                                                                          | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                  |
| 1                                               | 2                                                                                                                                | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 260                                             | FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA                                                                | 07/2015                       | 1,871.34 -                         | 1,871.34                     | 2,304.41                           | 01/2018 -                          | 12/2018     | 11                    | 0                |                                                                  |
| 261                                             | FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA                | 04/2010                       | 1,170.52 -                         | 1,170.52                     | 2,042.41                           | 06/2012 -                          | 12/2018     | 78                    | 0                |                                                                  |
| 262                                             | TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR                                                    | 08/2015                       | 516.13 -                           | 516.13                       | 400.35                             | 04/2018 -                          | 12/2018     | 8                     | 0                |                                                                  |
| 263                                             | SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM                                                                                | 12/2003                       | 245.00<br>174.34                   | 174.34                       | 214.88                             | 03/2008 -                          | 01/2019     | 130                   | -28.84           |                                                                  |
| 264                                             | JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA                                                                                    | 01/2011                       | 536.00 -                           | 536.00                       | 837.81                             | 01/2014 -                          | 01/2019     | 60                    | 0                |                                                                  |
| 265                                             | PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN                                         | 09/2015                       | 567.51 -                           | 567.51                       | 53.70                              | 03/2018 -                          | 01/2019     | 10                    | 0                |                                                                  |
| 266                                             | 2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN                                                               | 10/2015                       | 597.00 -                           | 597.00                       | 604.80                             | 10/2017 -                          | 01/2019     | 15                    | 0                |                                                                  |
| 267                                             | DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM                                                                  | 12/2003                       | 160.00 -                           | 167.98                       | 198.82                             | 05/2008 -                          | 02/2019     | 129                   | 4.99             |                                                                  |
| 268                                             | 2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN | 11/2012                       | 530.07 -                           | 530.07                       | 556.02                             | 08/2016 -                          | 02/2019     | 30                    | 0                |                                                                  |
| 269                                             | 2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN                                                        | 08/2016                       | 320.30 -                           | 320.30                       | 193.54                             | 01/2019 -                          | 02/2019     | 1                     | 0                |                                                                  |
| 270                                             | MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM                                                      | 12/2003                       | 199.81 -                           | 385.13                       | 209.80                             | 04/2009 -                          | 03/2019     | 119                   | 92.75            |                                                                  |
| 271                                             | NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM                                                                                   | 12/2003                       | 208.00 -                           | 230.00                       | 297.81                             | 04/2008 -                          | 03/2019     | 131                   | 10.58            |                                                                  |
| 272                                             | HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA                                                    | 09/2010                       | 946.00 -                           | 946.00                       | 818.53                             | 06/2018 -                          | 03/2019     | 9                     | 0                |                                                                  |
| 273                                             | SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA                                             | 02/2010                       | 617.00 -                           | 617.00                       | 943.17                             | 08/2012 -                          | 03/2019     | 79                    | 0                |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                                      |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                                                      |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies) |
| S.No                                            | Project                                                                                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                  |
| 1                                               | 2                                                                                                                                    | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 274                                             | QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR                                                         | 07/2010                       | 1,987.00 -                         | 1,987.00                     | 2,403.47                           | 07/2015 -                          | 03/2019     | 44                    | 0                |                                                                  |
| 275                                             | PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA                                                                                            | 03/2012                       | 1,410.00 -                         | 1,410.00                     | 1,555.96                           | 09/2014 -                          | 03/2019     | 54                    | 0                |                                                                  |
| 276                                             | TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN                                                      | 09/2014                       | 425.19 -                           | 425.19                       | 274.20                             | 09/2016 -                          | 03/2019     | 30                    | 0                |                                                                  |
| 277                                             | CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270( D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 ( D - [N24000432]NHAI,MAHARASHTRA   | 09/2015                       | 414.51 -                           | 414.00                       | 230.34                             | 05/2018 -                          | 03/2019     | 10                    | -12              |                                                                  |
| 278                                             | BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN      | 08/2014                       | 822.90 -                           | 822.90                       | 688.00                             | 04/2018 -                          | 03/2019     | 11                    | 0                |                                                                  |
| 279                                             | 4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA                                                                  | 01/2016                       | 574.28 -                           | 574.28                       | 79.56                              | 07/2018 -                          | 03/2019     | 8                     | 0                |                                                                  |
| 280                                             | 4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA                                                        | 05/2014                       | 1,655.01 -                         | 1,655.01                     | 1,515.16                           | 08/2016 -                          | 03/2019     | 31                    | 0                |                                                                  |
| 281                                             | GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN                                                                   | 02/2008                       | 1,673.70 -                         | 1,673.70                     | 3,326.93                           | 10/2011<br>09/2017                 | 03/2019     | 89                    | 0                |                                                                  |
| 282                                             | FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH                                                                   | 09/2015                       | 934.46 -                           | 934.46                       | 104.98                             | 03/2018 -                          | 03/2019     | 12                    | 0                |                                                                  |
| 283                                             | FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH | 06/2015                       | 1,012.90 -                         | 1,012.90                     | 1,042.73                           | 03/2016 -                          | 03/2019     | 36                    | 0                |                                                                  |
| 284                                             | TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA                                     | 12/2015                       | 479.20 -                           | 479.20                       | 14.31                              | 05/2018 -                          | 03/2019     | 10                    | 0                |                                                                  |
| 285                                             | NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM                                                                                      | 12/2003                       | 225.00 -                           | 225.00                       | 312.79                             | 06/2008 -                          | 04/2019     | 130                   | 0                |                                                                  |
| 286                                             | BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM                                                                                   | 12/2003                       | 217.61 -                           | 360.84                       | 390.19                             | 04/2010 -                          | 04/2019     | 108                   | 65.82            |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                                   |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                                                   |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies) |
| S.No                                            | Project                                                                                                                           | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                  |
| 1                                               | 2                                                                                                                                 | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 287                                             | CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH                                                   | 11/2010                       | 1,585.00 -                         | 1,585.00                     | 2,167.31                           | 05/2013 -                          | 04/2019     | 71                    | 0                |                                                                  |
| 288                                             | FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH                              | 11/2013                       | 1,916.79 -                         | 1,916.79                     | 1,948.92                           | 11/2016 -                          | 04/2019     | 29                    | 0                |                                                                  |
| 289                                             | CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 ( OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA                 | 10/2015                       | 593.26 -                           | 593.26                       | 45.11                              | 05/2018 -                          | 04/2019     | 11                    | 0                |                                                                  |
| 290                                             | 6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA                  | 08/2015                       | 505.00 -                           | 505.00                       | 194.09                             | 05/2018 -                          | 04/2019     | 11                    | 0                |                                                                  |
| 291                                             | FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA                                                                   | 03/2015                       | 1,388.00 -                         | 1,388.00                     | 924.40                             | 08/2018 -                          | 04/2019     | 8                     | 0                |                                                                  |
| 292                                             | FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB                                                                       | 10/2015                       | 447.29 -                           | 447.29                       | 31.96                              | 12/2017 -                          | 04/2019     | 16                    | 0                |                                                                  |
| 293                                             | CONSTRUCTION OF ROB – FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL                                                   | 03/2016                       | 229.37 -                           | 229.37                       | 10.43                              | 11/2018 -                          | 04/2019     | 5                     | 0                |                                                                  |
| 294                                             | FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU | 02/2016                       | 641.17 -                           | 641.17                       | 259.00                             | 07/2018 -                          | 04/2019     | 9                     | 0                |                                                                  |
| 295                                             | 4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA     | 04/2016                       | 804.97 -                           | 804.97                       | 21.80                              | 06/2018 -                          | 04/2019     | 10                    | 0                |                                                                  |
| 296                                             | FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU | 03/2016                       | 641.17 -                           | 641.17                       | 244.33                             | 07/2016 -                          | 04/2019     | 33                    | 0                |                                                                  |
| 297                                             | 6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL                                                              | 04/2012                       | 1,396.18 -                         | 1,396.18                     | 2,614.84                           | 09/2014 -                          | 05/2019     | 56                    | 0                |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                                   |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                                                   |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies) |
| S.No                                            | Project                                                                                                                           | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                  |
| 1                                               | 2                                                                                                                                 | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 298                                             | KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL                                                                             | 02/2012                       | 702.16 -                           | 702.16                       | 454.81                             | 07/2014 -                          | 05/2019     | 58                    | 0                |                                                                  |
| 299                                             | FOUR LANE OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANE WITH PS KM 81 TO KM 120 - [N24000349]NHAI, TAMIL NADU         | 05/2015                       | 1,387.11 -                         | 1,387.11                     | 915.30                             | 11/2017 -                          | 05/2019     | 18                    | 0                |                                                                  |
| 300                                             | CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (-) [N24000435]NHAI, MAHARASHTRA | 10/2015                       | 531.13 -                           | 531.13                       | 163.10                             | 05/2018 -                          | 05/2019     | 12                    | 0                |                                                                  |
| 301                                             | 4 LANE OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL                            | 12/2015                       | 1,083.00 -                         | 1,083.00                     | 155.25                             | 06/2018 -                          | 05/2019     | 11                    | 0                |                                                                  |
| 302                                             | PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA                                                           | 05/2009                       | 1,108.00 -                         | 2,288.00                     | 3,953.66                           | 11/2011 -                          | 06/2019     | 91                    | 106.5            |                                                                  |
| 303                                             | PUNE-SATARA (NH-4) - [N24000156]NHAI, MAHARASHTRA                                                                                 | 10/2010                       | 1,724.55 -                         | 1,724.55                     | 2,253.40                           | 03/2013 -                          | 06/2019     | 75                    | 0                |                                                                  |
| 304                                             | PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR                                                                                       | 08/2010                       | 671.30 -                           | 671.30                       | 884.43                             | 02/2013 -                          | 06/2019     | 76                    | 0                |                                                                  |
| 305                                             | 4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR                                                                              | 01/2011                       | 575.00 -                           | 575.00                       | 831.49                             | 07/2013 -                          | 06/2019     | 71                    | 0                |                                                                  |
| 306                                             | 4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL                                                                         | 02/2011                       | 1,078.84 -                         | 1,078.84                     | 2,312.98                           | 08/2013 -                          | 06/2019     | 70                    | 0                |                                                                  |
| 307                                             | PANVEL-INDAPUR - [N24000216]NHAI, MAHARASHTRA                                                                                     | 12/2011                       | 942.69 -                           | 942.69                       | 668.59                             | 06/2014 -                          | 06/2019     | 60                    | 0                |                                                                  |
| 308                                             | WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA                                    | 05/2013                       | 1,348.20 -                         | 1,348.20                     | 1,792.90                           | 02/2014 -                          | 06/2019     | 64                    | 0                |                                                                  |
| 309                                             | 4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA                                                | 04/2014                       | 1,266.60 -                         | 1,544.00                     | 1,411.79                           | 09/2016 -                          | 06/2019     | 33                    | 21.9             |                                                                  |
| 310                                             | TWO LANE WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU                                                        | 06/2015                       | 563.92 -                           | 563.92                       | 96.48                              | 12/2017 -                          | 06/2019     | 18                    | 0                |                                                                  |
| 311                                             | 4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA                                                | 06/2014                       | 923.04 -                           | 923.04                       | 650.92                             | 11/2016 -                          | 06/2019     | 31                    | 0                |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                                      |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                                                      |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies) |
| S.No                                            | Project                                                                                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                  |
| 1                                               | 2                                                                                                                                    | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 312                                             | FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI, CHHATISGARH                                                                       | 12/2015                       | 596.67 -                           | 596.67                       | 41.87                              | 05/2018 -                          | 06/2019     | 13                    | 0                |                                                                  |
| 313                                             | FOUR / SIX LANING OF RAIPUR - SIMGA ( PKG-1) - [N24000510]NHAI, CHHATISGARH                                                          | 12/2015                       | 726.67 -                           | 726.67                       | 50.67                              | 04/2018 -                          | 06/2019     | 14                    | 0                |                                                                  |
| 314                                             | FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI, TAMIL NADU   | 02/2016                       | 707.82 -                           | 707.82                       | 208.92                             | 08/2018 -                          | 06/2019     | 10                    | 0                |                                                                  |
| 315                                             | BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI, BIHAR                                                             | 05/2015                       | 581.84 -                           | 581.84                       | 77.43                              | 05/2017 -                          | 06/2019     | 25                    | 0                |                                                                  |
| 316                                             | HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI, UTTARAKHAND                                                                  | 11/2011                       | 478.51 -                           | 478.00                       | 409.17                             | 10/2013 -                          | 07/2019     | 69                    | -11              |                                                                  |
| 317                                             | FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI, TELANGANA                                                                       | 12/2015                       | 1,423.96 -                         | 1,423.96                     | 514.42                             | 11/2018 -                          | 07/2019     | 8                     | 0                |                                                                  |
| 318                                             | 4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI, KARNATAKA                                          | 03/2016                       | 701.40 -                           | 701.40                       | 22.02                              | 03/2019 -                          | 07/2019     | 4                     | 0                |                                                                  |
| 319                                             | CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI, HARYANA                                                           | 08/2016                       | 248.97 -                           | 248.97                       | 27.57                              | 05/2019 -                          | 08/2019     | 3                     | 0                |                                                                  |
| 320                                             | TWO LANNING WITH PAVED SHOULDER OF SALASAR- NAGPUR - [N24000586]NHAI, RAJASTHAN                                                      | 06/2016                       | 637.18 -                           | 637.18                       | 576.75                             | 06/2019 -                          | 09/2019     | 3                     | 0                |                                                                  |
| 321                                             | FOUR LANNING OF BAR-BILARA- JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN                          | 06/2016                       | 649.00 -                           | 649.00                       | -                                  | 06/2019 -                          | 09/2019     | 3                     | 0                |                                                                  |
| 322                                             | FOUR LANNING OF CHICHRA- KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL | 09/2016                       | 767.03 -                           | 767.03                       | 156.04                             | 08/2018 -                          | 09/2019     | 13                    | 0                |                                                                  |
| 323                                             | 4-LANNING OF RAIPUR- KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI, MAHARASHTRA | 11/2016                       | 400.25 -                           | 400.25                       | 38.57                              | 03/2019 -                          | 09/2019     | 6                     | 0                |                                                                  |
| 324                                             | FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI, JAMMU AND KASHMIR                                               | 12/2015                       | 2,136.97 -                         | 2,136.97                     | 87.69                              | 12/2018 -                          | 10/2019     | 10                    | 0                |                                                                  |



## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                                      |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                                                      |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies) |
| S.No                                            | Project                                                                                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                  |
| 1                                               | 2                                                                                                                                    | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 325                                             | TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR                                                         | 08/2015                       | 399.54 -                           | 399.54                       | 142.41                             | 04/2019 -                          | 10/2019     | 6                     | 0                |                                                                  |
| 326                                             | FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN      | 06/2016                       | 763.23 -                           | 763.23                       | 154.91                             | 06/2019 -                          | 11/2019     | 5                     | 0                |                                                                  |
| 327                                             | 4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH                                       | 08/2016                       | 2,016.00 -                         | 2,016.00                     | 1,663.22                           | 04/2019 -                          | 11/2019     | 7                     | 0                |                                                                  |
| 328                                             | 4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA   | 11/2016                       | 446.17 -                           | 446.17                       | 2.42                               | 03/2019 -                          | 11/2019     | 8                     | 0                |                                                                  |
| 329                                             | FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH      | 06/2017                       | 648.33 -                           | 648.33                       | 15.89                              | 06/2017 -                          | 11/2019     | 29                    | 0                |                                                                  |
| 330                                             | VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE                                                                | 09/2011                       | 2,848.00 -                         | 2,848.00                     | 1,141.90                           | 03/2014 -                          | 12/2019     | 69                    | 0                |                                                                  |
| 331                                             | MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE                                                                                 | 09/2011                       | 754.00 -                           | 754.00                       | 1,363.43                           | 03/2013 -                          | 12/2019     | 81                    | 0                |                                                                  |
| 332                                             | FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH | 10/2017                       | 639.97 -                           | 639.97                       | 58.04                              | 10/2017 -                          | 01/2020     | 27                    | 0                |                                                                  |
| 333                                             | FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR                                                                          | 08/2015                       | 322.09 -                           | 322.09                       | 71.28                              | 04/2018 -                          | 04/2020     | 24                    | 0                |                                                                  |
| 334                                             | CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB        | 03/2017                       | 754.54 -                           | 756.27                       | 30.30                              | 03/2020 -                          | 04/2020     | 1                     | .23              |                                                                  |
| 335                                             | FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA                                                                  | 02/2017                       | 904.16 -                           | 904.16                       | 155.12                             | 02/2020 -                          | 05/2020     | 3                     | 0                |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                                      |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                                                      |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies) |
| S.No                                            | Project                                                                                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                  |
| 1                                               | 2                                                                                                                                    | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 336                                             | 4-LANNING OF WARDHA-BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA                                            | 03/2017                       | 1,030.44 -                         | 1,065.51                     | 355.02                             | 03/2020 -                          | 05/2020     | 2                     | 3.4              |                                                                  |
| 337                                             | DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH | 03/2017                       | 1,989.00 -                         | 1,989.00                     | 842.34                             | 03/2020 -                          | 05/2020     | 2                     | 0                |                                                                  |
| 338                                             | SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH                | 03/2017                       | 1,041.62 -                         | 1,187.10                     | 43.99                              | 03/2020 -                          | 05/2020     | 2                     | 13.97            |                                                                  |
| 339                                             | 4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL                                                                         | 02/2011                       | 998.79 -                           | 998.79                       | 1,825.92                           | 08/2013 -                          | 06/2020     | 82                    | 0                |                                                                  |
| 340                                             | SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA       | 03/2017                       | 831.58 -                           | 1,177.00                     | 121.00                             | 03/2020 -                          | 06/2020     | 3                     | 41.54            |                                                                  |
| 341                                             | SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA     | 03/2017                       | 993.16 -                           | 1,434.00                     | 413.53                             | 03/2020 -                          | 06/2020     | 3                     | 44.39            |                                                                  |
| 342                                             | 4-LANNING OF THALSERRY - MAHE BYPASS - [N24000704]NHAI,KERALA                                                                        | 09/2017                       | 1,124.11 -                         | 1,124.11                     | -                                  | 09/2017 -                          | 06/2020     | 33                    | 0                |                                                                  |
| 343                                             | GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE                                                                                  | 12/2003                       | 604.00 -                           | 604.00                       | 423.83                             | 12/2009 -                          | 08/2020     | 128                   | 0                |                                                                  |
| 344                                             | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH | 03/2017                       | 1,184.71 -                         | 1,310.00                     | -                                  | 03/2020 -                          | 08/2020     | 5                     | 10.58            |                                                                  |
| 345                                             | 4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA                                            | 03/2017                       | 988.34 -                           | 1,043.28                     | 451.51                             | 03/2020 -                          | 08/2020     | 5                     | 5.56             |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above |                                                                                                                                     |                               |                                    |                              |                                    | (December 2018)                    |             |                       |                  |                                                                  |
|---------------------------------|-------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                 |                                                                                                                                     |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies) |
| S.No                            | Project                                                                                                                             | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                  |
| 1                               | 2                                                                                                                                   | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 346                             | 4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA                                         | 03/2017                       | 1,098.06                           | 1,160.64                     | 413.75                             | 03/2020                            | 08/2020     | 5                     | 5.7              |                                                                  |
| 347                             | 4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT                                            | 06/2017                       | 1,958.88                           | 1,958.88                     | 364.31                             | 06/2020                            | 08/2020     | 2                     | 0                |                                                                  |
| 348                             | 4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA                                            | 03/2016                       | 870.00                             | 870.00                       | 9.12                               | 03/2019                            | 11/2020     | 20                    | 0                |                                                                  |
| 349                             | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH | 03/2017                       | 1,373.28                           | 1,373.28                     | -                                  | 03/2020                            | 11/2020     | 8                     | 0                |                                                                  |
| 350                             | 4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA                                         | 03/2017                       | 1,059.73                           | 1,071.00                     | 152.79                             | 03/2017                            | 11/2020     | 44                    | 1.06             |                                                                  |
| 351                             | REHABILITATION AND UPGRADE OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI, ODISHA                                     | 07/2017                       | 476.56                             | 476.56                       | -                                  | 07/2017                            | 11/2020     | 40                    | 0                |                                                                  |
| 352                             | FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR                                                | 12/2015                       | 2,168.66                           | 2,168.66                     | -                                  | 06/2019                            | 12/2020     | 18                    | 0                |                                                                  |
|                                 | <u>National Highways Development Project</u>                                                                                        |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 353                             | BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH                                                                   | 11/2011                       | 704.26                             | 704.26                       | 5.21                               | 05/2015                            | 01/2020     | 56                    | 0                |                                                                  |
|                                 | Total                                                                                                                               |                               | 96,101.97                          | 99,712.68                    | 68,218.96                          |                                    |             |                       |                  |                                                                  |
|                                 |                                                                                                                                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                 | <u>SHIPPING AND PORTS</u>                                                                                                           |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                 | <u>Kamarajar Port Limited</u>                                                                                                       |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 354                             | CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU                                                     | 03/2016                       | 600.00                             | 257.90                       | 1.45                               | 12/2017                            | 05/2020     | 29                    | -57.02           |                                                                  |
|                                 | <u>Mumbai Port Trust</u>                                                                                                            |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                                               |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                                                               |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  |                                                                  |
| S.No                                            | Project                                                                                                                                       | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) | Reasons for Delay (As Reported by Project Implementing Agencies) |
| 1                                               | 2                                                                                                                                             | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 355                                             | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA | 01/2007                       | 366.39<br>669.46                   | 669.46                       | 413.91                             | 12/2010<br>-                       | 12/2018     | 96                    | 82.72            | Nil                                                              |
|                                                 | <u>Port Trust</u>                                                                                                                             |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 356                                             | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU                                                | 10/2002                       | 150.00<br>600.00                   | 600.00                       | 550.78                             | 03/2006<br>03/2016                 | 02/2019     | 155                   | 300              |                                                                  |
|                                                 | Total                                                                                                                                         |                               | 1,116.39<br>-                      | 1,527.36                     | 966.14                             |                                    |             |                       |                  |                                                                  |
|                                                 |                                                                                                                                               |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                                 | <u>TELECOMMUNICATIONS</u>                                                                                                                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                                 | <u>Bharat Sanchar Nigam Limited</u>                                                                                                           |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 357                                             | MAHARASHTRA CORE (LOT1) - [N26000108]BSNL,MAHARASHTRA                                                                                         | 08/2017                       | 167.68<br>-                        | 167.68                       | 32.44                              | 04/2018<br>02/2019                 | 02/2019     | 10                    | 0                |                                                                  |
| 358                                             | MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA                                                                                    | 08/2017                       | 215.30<br>214.10                   | 214.10                       | 33.46                              | 05/2018<br>02/2019                 | 02/2019     | 9                     | -56              |                                                                  |
| 359                                             | MAHARASHTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA                                                               | 01/2018                       | 231.80<br>231.80                   | 231.80                       | 77.65                              | 10/2018<br>02/2019                 | 02/2019     | 4                     | 0                |                                                                  |
|                                                 | <u>Department Of Telecommunication</u>                                                                                                        |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 360                                             | NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE                                                                                             | 03/2012                       | 13,334.00<br>-                     | 24,664.00                    | 8,397.00                           | 07/2015<br>-                       | 05/2020     | 58                    | 84.97            |                                                                  |
|                                                 | Total                                                                                                                                         |                               | 13,948.78<br>-                     | 25,277.58                    | 8,540.55                           |                                    |             |                       |                  |                                                                  |
|                                                 |                                                                                                                                               |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                                 | <u>URBAN DEVELOPMENT</u>                                                                                                                      |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                                 | <u>Bangalore Metro Rail Corporation Limited</u>                                                                                               |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 361                                             | BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA                                                                             | 02/2014                       | 26,405.14<br>-                     | 26,405.14                    | 499.85                             | 02/2019<br>-                       | 03/2020     | 13                    | 0                |                                                                  |
|                                                 | <u>Central Public Works Department</u>                                                                                                        |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 362                                             | DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH                                            | 11/2012                       | 270.83<br>-                        | 270.83                       | 163.97                             | 11/2014<br>-                       | 02/2019     | 51                    | 0                |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                                    |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                                                    |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies) |
| S.No                                            | Project                                                                                                                            | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                  |
| 1                                               | 2                                                                                                                                  | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 363                                             | CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL                      | 02/2014                       | 156.57 -                           | 156.57                       | 146.40                             | 08/2016 -                          | 03/2019     | 31                    | 0                |                                                                  |
| 364                                             | CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD, KERALA                                                    | 01/2010                       | 165.23 -                           | 165.23                       | 58.85                              | 10/2012 -                          | 03/2019     | 77                    | 0                |                                                                  |
| 365                                             | CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD, PUNJAB                         | 02/2014                       | 388.00 -                           | 388.00                       | 395.14                             | 05/2017 02/2019                    | 03/2019     | 22                    | 0                |                                                                  |
| 366                                             | NSG AT KOLKATA - [N28000104]CPWD, WEST BENGAL                                                                                      | 10/2014                       | 162.88 -                           | 162.88                       | 96.48                              | 04/2018 -                          | 07/2019     | 15                    | 0                |                                                                  |
| 367                                             | CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD, PUNJAB                                   | 08/2016                       | 294.00 -                           | 294.00                       | 134.64                             | 04/2019 06/2019                    | 09/2019     | 5                     | 0                |                                                                  |
| 368                                             | CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD, UTTARAKHAND | 12/2008                       | 114.26 266.00                      | 266.00                       | -                                  | 12/2013 -                          | 10/2019     | 70                    | 132.8            |                                                                  |
| 369                                             | DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD, RAJASTHAN               | 12/2016                       | 549.31 -                           | 540.42                       | 215.67                             | 07/2019 -                          | 10/2019     | 3                     | -1.62            |                                                                  |
| 370                                             | NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD, MANIPUR                                                                 | 02/2014                       | 216.69 -                           | 216.69                       | 52.00                              | 03/2015 -                          | 11/2019     | 56                    | 0                |                                                                  |
| 371                                             | ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD, DELHI           | 10/2013                       | 1,219.21 -                         | 1,592.00                     | 331.12                             | 10/2019 -                          | 03/2020     | 5                     | 30.58            |                                                                  |
| 372                                             | 2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD, JHARKHAND                                              | 09/2012                       | 171.86 -                           | 171.86                       | 41.28                              | 03/2016 -                          | 04/2020     | 49                    | 0                |                                                                  |
| 373                                             | CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD, DELHI          | 06/2015                       | 197.33 -                           | 197.33                       | 14.25                              | 04/2019 06/2020                    | 06/2020     | 14                    | 0                |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                                    |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                                                    |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies) |
| S.No                                            | Project                                                                                                                            | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                  |
| 1                                               | 2                                                                                                                                  | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 374                                             | CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR                | 02/2016                       | 496.18<br>496.00                   | 498.99                       | 34.09                              | 06/2017<br>07/2017                 | 06/2020     | 36                    | .57              |                                                                  |
| 375                                             | RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103]CPWD,KARNATAKA                                                                  | 12/2016                       | 246.31<br>-                        | 246.31                       | 34.88                              | 02/2020<br>09/2020                 | 09/2020     | 7                     | 0                |                                                                  |
| 376                                             | CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA                                      | 01/2018                       | 223.37<br>-                        | 223.37                       | 4.00                               | 07/2020<br>09/2018                 | 09/2020     | 2                     | 0                |                                                                  |
|                                                 | <u>Hindustan Steelwork Construction Limited</u>                                                                                    |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 377                                             | CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL, MEGHALAYA | 04/2014                       | 151.33<br>-                        | 151.33                       | 7.15                               | 09/2017<br>-                       | 12/2018     | 15                    | 0                |                                                                  |
| 378                                             | CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL, JHARKHAND                                      | 02/2014                       | 787.29<br>-                        | 787.29                       | 285.30                             | 12/2016<br>-                       | 12/2018     | 24                    | 0                |                                                                  |
| 379                                             | IRRIGATION WORK OF BAGMATI - [N12000108]HSCL, BIHAR                                                                                | 10/2005                       | 956.00<br>-                        | 956.00                       | 651.21                             | 03/2015<br>-                       | 03/2021     | 72                    | 0                |                                                                  |
|                                                 | <u>Kochi Metro Rail Corporation Ltd</u>                                                                                            |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 380                                             | KOCHI METRO RAIL PROJECT - [N28000081]KMRCL, KERALA                                                                                | 07/2012                       | 5,181.79<br>-                      | 5,181.79                     | -                                  | 07/2017<br>-                       | 12/2019     | 29                    | 0                |                                                                  |
|                                                 | <u>Maharashtra Metro Rail Corporation Ltd.</u>                                                                                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 381                                             | DELHI MRTS PHASE-III - [N28000056]MMRC, DELHI                                                                                      | 09/2011                       | 38,585.00<br>-                     | 38,585.00                    | 37,044.70                          | 03/2016<br>05/2019                 | 05/2019     | 38                    | 0                |                                                                  |
|                                                 | <u>Mumbai Metro Rail Corporation Ltd</u>                                                                                           |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 382                                             | MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA                                                          | 07/2013                       | 23,136.00<br>-                     | 23,136.00                    | -                                  | 01/2015<br>-                       | 05/2020     | 64                    | 0                |                                                                  |
|                                                 | <u>Nagpur Metro Rail Corporation Ltd</u>                                                                                           |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 383                                             | NAGPUR METRO RAIL - [N28000085]NMRCL, MAHARASHTRA                                                                                  | 08/2014                       | 8,680.00<br>8,680.00               | 8,680.00                     | 4,787.71                           | 03/2018<br>12/2019                 | 12/2019     | 21                    | 0                |                                                                  |
|                                                 | Total                                                                                                                              |                               | 1,08,754.58<br>-                   | 1,09,273.03                  | 44,998.69                          |                                    |             |                       |                  |                                                                  |
|                                                 |                                                                                                                                    |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                                 | <u>DEFENCE PRODUCTION</u>                                                                                                          |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs. 150 Crore and above (December 2018) |                                                 |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|-------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                 |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  |                                                                  |
| S.No                                            | Project                                         | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) | Reasons for Delay (As Reported by Project Implementing Agencies) |
| 1                                               | 2                                               | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
|                                                 | <u>Goa Shipyard Limited</u>                     |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 384                                             | CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL,GOA | 12/2016                       | 167.69<br>168.00                   | 170.37                       | 103.91                             | 05/2018<br>01/2019                 | 01/2019     | 8                     | 1.6              |                                                                  |
|                                                 | Total                                           |                               | 167.69<br>-                        | 170.37                       | 103.91                             |                                    |             |                       |                  |                                                                  |
|                                                 |                                                 |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|                                                 | Grand Total                                     |                               | 7,44,405.01                        | 8,92,170.35                  | 4,81,926.04                        |                                    |             |                       |                  |                                                                  |

# Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

| (December 2018) |                                                                                             |                               |                                     |                             |                                    |             |                   |                     |
|-----------------|---------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|-----------------------------|------------------------------------|-------------|-------------------|---------------------|
|                 |                                                                                             |                               |                                     |                             | Date of Commissioning (Month/Year) |             |                   |                     |
| Sl.No           | Project                                                                                     | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised                 | Anticipated | Cost Overruns (%) | T.O.R.s (in months) |
| 1               | 2                                                                                           | 3                             | 4                                   | 5                           | 6                                  | 7           | 8                 | 9                   |
|                 |                                                                                             |                               |                                     |                             |                                    |             |                   |                     |
|                 | <u>ATOMIC ENERGY</u>                                                                        |                               |                                     |                             |                                    |             |                   |                     |
|                 | <u>Bhavini Limited</u>                                                                      |                               |                                     |                             |                                    |             |                   |                     |
| 1               | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)<br>- [020100044]                          | 09/2003                       | 3,492.00<br>-                       | 6,100.00                    | 09/2010<br>-                       | 03/2019     | 74.69             | 102                 |
|                 | <u>Nuclear Power Corporation Of India Limited</u>                                           |                               |                                     |                             |                                    |             |                   |                     |
| 2               | KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4<br>- [N02000010]                                    | 10/2009                       | 11,459.00<br>-                      | 16,580.00                   | 12/2015<br>-                       | 06/2020     | 44.69             | 54                  |
|                 | Total                                                                                       |                               | 14,951.00<br>-                      | 22,680.00                   |                                    |             |                   |                     |
|                 |                                                                                             |                               |                                     |                             |                                    |             |                   |                     |
|                 | <u>CIVIL AVIATION</u>                                                                       |                               |                                     |                             |                                    |             |                   |                     |
|                 | <u>Airport Authority Of India Limited</u>                                                   |                               |                                     |                             |                                    |             |                   |                     |
| 3               | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR<br>- [N04000073] | 10/2013                       | 314.61<br>-                         | 441.33                      | 09/2018<br>-                       | 06/2020     | 40.28             | 21                  |
|                 | Total                                                                                       |                               | 314.61<br>-                         | 441.33                      |                                    |             |                   |                     |
|                 |                                                                                             |                               |                                     |                             |                                    |             |                   |                     |
|                 | <u>COAL</u>                                                                                 |                               |                                     |                             |                                    |             |                   |                     |
|                 | <u>Singareni Colliers Company Limited</u>                                                   |                               |                                     |                             |                                    |             |                   |                     |
| 4               | RCE OF INDARAM OCP(1.20 MTPA)<br>- [N06000093]                                              | 07/2011                       | 162.76<br>-                         | 349.28                      | 03/2015<br>-                       | 03/2021     | 114.60            | 72                  |
| 5               | SHANTIKHANI LONGWALL PROJ-SCCL<br>- [N06000017]                                             | 10/2006                       | 249.03<br>-                         | 448.86                      | 03/2012<br>-                       | 03/2024     | 80.24             | 144                 |
| 6               | RAMAGUNDAM OC-II EXTENSION<br>- [N06000078]                                                 | 12/2009                       | 418.97<br>-                         | 489.62                      | 03/2012<br>-                       | 03/2023     | 16.86             | 132                 |
|                 | <u>South-Eastern Coal Fields Limited</u>                                                    |                               |                                     |                             |                                    |             |                   |                     |
| 7               | JAGANNATHPOR OCP(3.00MTY)<br>- [N06000075]                                                  | 09/2008                       | 152.43<br>-                         | 459.49                      | 03/2015<br>-                       | 03/2020     | 201.44            | 60                  |
|                 | <u>Western Coal Fields Limited</u>                                                          |                               |                                     |                             |                                    |             |                   |                     |
| 8               | KAMPTEE DEEP OC MINE<br>- [N06000141]                                                       | 11/2015                       | 277.65<br>-                         | 313.34                      | 03/2021<br>-                       | 03/2024     | 12.85             | 36                  |
| 9               | ADASA UG TO OC<br>- [N06000133]                                                             | 08/2015                       | 288.90<br>-                         | 333.43                      | 03/2023<br>-                       | 03/2024     | 15.41             | 12                  |
|                 | Total                                                                                       |                               | 1,549.74<br>-                       | 2,394.02                    |                                    |             |                   |                     |
|                 |                                                                                             |                               |                                     |                             |                                    |             |                   |                     |
|                 | <u>DEFENCE PRODUCTION</u>                                                                   |                               |                                     |                             |                                    |             |                   |                     |
|                 | <u>Goa Shipyard Limited</u>                                                                 |                               |                                     |                             |                                    |             |                   |                     |
| 10              | CONSTRUCTION WORKS PHASE 4<br>- [N39000001]                                                 | 12/2016                       | 167.69<br>168.00                    | 170.37                      | 05/2018<br>-                       | 01/2019     | 1.60              | 8                   |



## Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2018)

|       |                                                                                      |                               |                                     |                             | Date of Commissioning (Month/Year) |             |                   |                     |
|-------|--------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|-----------------------------|------------------------------------|-------------|-------------------|---------------------|
| Sl.No | Project                                                                              | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised                 | Anticipated | Cost Overruns (%) | T.O.R.s (in months) |
| 1     | 2                                                                                    | 3                             | 4                                   | 5                           | 6                                  | 7           | 8                 | 9                   |
|       | Total                                                                                |                               | 167.69 -                            | 170.37                      |                                    |             |                   |                     |
|       |                                                                                      |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>FERTILISERS</u>                                                                   |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>Rashtriya Chemical &amp; Fertiliser Limited</u>                                   |                               |                                     |                             |                                    |             |                   |                     |
| 11    | NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]                        | 10/2014                       | 197.79 -                            | 209.44                      | 11/2016 -                          | 04/2019     | 5.89              | 29                  |
|       | Total                                                                                |                               | 197.79 -                            | 209.44                      |                                    |             |                   |                     |
|       |                                                                                      |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>HEALTH AND FAMILY WELFARE</u>                                                     |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>Hospital Services Consultancy Corporation Ltd</u>                                 |                               |                                     |                             |                                    |             |                   |                     |
| 12    | LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]                                          | 02/2013                       | 414.11 -                            | 513.89                      | 11/2013 -                          | 10/2020     | 24.10             | 83                  |
|       | Total                                                                                |                               | 414.11 -                            | 513.89                      |                                    |             |                   |                     |
|       |                                                                                      |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>HEAVY INDUSTRY</u>                                                                |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>Natip Implementation Society</u>                                                  |                               |                                     |                             |                                    |             |                   |                     |
| 13    | NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATIP) - [N20000001]      | 04/2011                       | 1,718.00 -                          | 3,827.30                    | 09/2011 -                          | 06/2019     | 122.78            | 93                  |
|       | Total                                                                                |                               | 1,718.00 -                          | 3,827.30                    |                                    |             |                   |                     |
|       |                                                                                      |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>PETROLEUM</u>                                                                     |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>Bharat Petroleum Corporation Limited</u>                                          |                               |                                     |                             |                                    |             |                   |                     |
| 14    | PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]    | 11/2014                       | 4,588.29 -                          | 5,245.96                    | 08/2018 -                          | 11/2019     | 14.33             | 15                  |
|       | <u>Hindustan Petroleum Corporation Limited</u>                                       |                               |                                     |                             |                                    |             |                   |                     |
| 15    | URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]                                     | 12/2009                       | 309.81 -                            | 723.40                      | 10/2014 -                          | 02/2019     | 133.50            | 52                  |
|       | <u>Indian Oil Corporation Limited</u>                                                |                               |                                     |                             |                                    |             |                   |                     |
| 16    | LPG TERMINAL AT KOCHI - [N16000171]                                                  | 10/2015                       | 607.06 -                            | 714.25                      | 10/2017 -                          | 03/2019     | 17.66             | 17                  |
| 17    | DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]        | 03/2014                       | 3,076.00 -                          | 4,190.00                    | 09/2017 -                          | 03/2019     | 36.22             | 18                  |
|       | <u>Oil &amp; Natural Gas Corporation Limited</u>                                     |                               |                                     |                             |                                    |             |                   |                     |
| 18    | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127] | 06/2010                       | 202.94 -                            | 330.35                      | 01/2014 -                          | 11/2019     | 62.78             | 70                  |

## Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2018)

|       |                                                                                                        |                               |                                     |                             | Date of Commissioning (Month/Year) |             |                   |                     |
|-------|--------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|-----------------------------|------------------------------------|-------------|-------------------|---------------------|
| Sl.No | Project                                                                                                | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised                 | Anticipated | Cost Overruns (%) | T.O.R.s (in months) |
| 1     | 2                                                                                                      | 3                             | 4                                   | 5                           | 6                                  | 7           | 8                 | 9                   |
| 19    | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)<br>- [N16000128                | 03/2011                       | 861.79<br>-                         | 1,577.15                    | 05/2013<br>-                       | 03/2019     | 83.01             | 70                  |
| 20    | INTEGRATED DEVELOPMENT OF B-127 FIELDS<br>- [N16000131                                                 | 12/2011                       | 2,059.63<br>-                       | 2,665.65                    | 03/2015<br>-                       | 12/2019     | 29.42             | 57                  |
| 21    | LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS<br>- [N16000213                       | 12/2015                       | 3,190.69<br>-                       | 3,247.19                    | 04/2018<br>-                       | 05/2019     | 1.77              | 13                  |
|       | <u>Oil India Limited</u>                                                                               |                               |                                     |                             |                                    |             |                   |                     |
| 22    | SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN<br>- [N16000167 | 07/2011                       | 352.56<br>-                         | 438.84                      | 03/2017<br>-                       | 06/2019     | 24.47             | 27                  |
|       | Total                                                                                                  |                               | 15,248.77<br>-                      | 19,132.79                   |                                    |             |                   |                     |
|       |                                                                                                        |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>POWER</u>                                                                                           |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>National Hydro-Electric Power Corporation</u>                                                       |                               |                                     |                             |                                    |             |                   |                     |
| 23    | PARBATI HEP (4X200 MW) (NHPC) II<br>- [180100210                                                       | 09/2002                       | 3,919.59<br>-                       | 9,394.80                    | 09/2009<br>-                       | 12/2021     | 139.69            | 147                 |
|       | <u>National Thermal Power Corporation</u>                                                              |                               |                                     |                             |                                    |             |                   |                     |
| 24    | TAPOVAN-VISHNUGAD HEP (4X130MW)<br>- [N18000014                                                        | 11/2006                       | 2,978.48<br>-                       | 3,846.30                    | 03/2013<br>-                       | 12/2020     | 29.14             | 93                  |
| 25    | BRBCL-NABINAGAR TPP- JV (4X250 MW)<br>- [N18000190                                                     | 01/2007                       | 5,353.00<br>-                       | 7,998.00                    | 05/2014<br>-                       | 05/2019     | 49.41             | 60                  |
| 26    | BONGAIGAON THERMAL POWER PROJECT<br>- [N18000041                                                       | 01/2008                       | 4,375.35<br>-                       | 8,150.00                    | 09/2011<br>-                       | 01/2019     | 86.27             | 88                  |
| 27    | LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)<br>- [N18000140                                  | 12/2012                       | 11,846.00<br>-                      | 12,739.82                   | 06/2017<br>-                       | 06/2019     | 7.55              | 24                  |
| 28    | GADARWARA SUPER THERMAL POWER PROJECT STAGE-I<br>- [N18000151                                          | 03/2013                       | 11,638.55<br>-                      | 12,865.92                   | 09/2017<br>-                       | 06/2019     | 10.55             | 21                  |
| 29    | NPGCPL-NABINAGAR STPP - JV (3X660 MW)<br>- [N18000192                                                  | 01/2013                       | 12,964.60<br>-                      | 13,731.26                   | 01/2018<br>-                       | 05/2020     | 5.91              | 28                  |
| 30    | DARLIPALLI STPP STAGE-I (2X800 MW)<br>- [N18000176                                                     | 02/2014                       | 12,532.44<br>-                      | 13,740.53                   | 08/2018<br>-                       | 06/2019     | 9.64              | 10                  |
| 31    | BARH STPP(3X660MW) NTPC<br>- [180100242                                                                | 02/2005                       | 8,692.97<br>-                       | 15,095.67                   | 01/2011<br>-                       | 04/2021     | 73.65             | 123                 |
| 32    | NORTH KARANPURA STPP (3X660 MW)<br>- [N18000177                                                        | 02/2014                       | 14,366.58<br>-                      | 15,164.05                   | 02/2019<br>-                       | 10/2020     | 5.55              | 20                  |
|       | <u>North East Electric Power Corporation</u>                                                           |                               |                                     |                             |                                    |             |                   |                     |
| 33    | KAMENG HYDROELECTRIC PROJECT (NEEPCO)<br>- [180100239                                                  | 12/2004                       | 2,496.90<br>-                       | 6,179.96                    | 12/2009<br>06/2016                 | 03/2019     | 147.51            | 111                 |
|       | <u>Power Grid Corporation Of India Limited</u>                                                         |                               |                                     |                             |                                    |             |                   |                     |
| 34    | AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B<br>- [N18000165                               | 03/2014                       | 155.57<br>-                         | 206.42                      | 03/2016<br>-                       | 02/2019     | 32.69             | 35                  |

## Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2018)

|       |                                                                                                                     |                               |                                     |                             | Date of Commissioning (Month/Year) |             |                   |                     |
|-------|---------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|-----------------------------|------------------------------------|-------------|-------------------|---------------------|
| Sl.No | Project                                                                                                             | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised                 | Anticipated | Cost Overruns (%) | T.O.R.s (in months) |
| 1     | 2                                                                                                                   | 3                             | 4                                   | 5                           | 6                                  | 7           | 8                 | 9                   |
| 35    | EASTERN REGION STRENGTHENING SCHEME -IX<br>- [N18000171                                                             | 02/2014                       | 196.58<br>-                         | 225.28                      | 02/2016<br>-                       | 03/2019     | 14.60             | 37                  |
| 36    | SYSTEM STRENGTHENING IN SOUTHERN REGION -<br>XXIII<br>- [N18000182                                                  | 01/2015                       | 203.28<br>-                         | 260.03                      | 07/2017<br>-                       | 06/2019     | 27.92             | 23                  |
| 37    | TRANSMISSION SYSTEM ASSOCIATED WITH<br>KISHENGANAGA HEP<br>[N18000180                                               | 01/2015                       | 268.80<br>-                         | 340.88                      | 03/2018<br>-                       | 02/2019     | 26.82             | 11                  |
| 38    | SYSTEM STRENGTHENING OF SOUTHERN REGION -<br>XIV<br>- [N18000115                                                    | 12/2011                       | 297.33<br>-                         | 534.02                      | 08/2014<br>-                       | 02/2019     | 79.61             | 54                  |
| 39    | EASTERN REGION STRENGTHENING SCHEME-XII<br>- [N18000164                                                             | 05/2014                       | 522.29<br>-                         | 550.18                      | 11/2016<br>-                       | 06/2019     | 5.34              | 31                  |
| 40    | SYSTEM STRENGTHENING XIII OF SR GRID<br>- [N18000109                                                                | 10/2011                       | 487.49<br>-                         | 639.46                      | 06/2014<br>-                       | 03/2019     | 31.17             | 57                  |
| 41    | WESTERN REGION STRENGTHENING SCHEME-V<br>- [N18000035                                                               | 12/2007                       | 477.69<br>-                         | 738.48                      | 09/2010<br>-                       | 02/2019     | 54.59             | 101                 |
| 42    | 400KV D/C TEESTA III - KISHANGANJ TRANSMISSION<br>LINE (JV)<br>- [N18000270                                         | 08/2008                       | 771.00<br>-                         | 1,624.00                    | 02/2013<br>-                       | 12/2018     | 110.64            | 70                  |
| 43    | EASTERN REGION STRENGTHENING SCHEME-V<br>- [N18000155                                                               | 10/2013                       | 1,364.52<br>-                       | 1,891.41                    | 04/2016<br>-                       | 02/2019     | 38.61             | 34                  |
| 44    | KUNADANKULAM APP TRANS SYSTEM (PGCIL)<br>- [180100258                                                               | 05/2005                       | 1,779.29<br>-                       | 2,187.32                    | 11/2008<br>-                       | 03/2019     | 22.93             | 124                 |
| 45    | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA<br>MEGA POWER PROJECT<br>[N18000061                                         | 10/2008                       | 4,824.12<br>-                       | 5,071.94                    | 10/2012<br>-                       | 06/2019     | 5.14              | 80                  |
| 46    | NORTH EASTERN REGION POWER SYSTEM<br>IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6)<br>STATES<br>- [N18000250            | 12/2014                       | 5,111.33<br>-                       | 6,652.57                    | 12/2018<br>-                       | 12/2019     | 30.15             | 12                  |
| 47    | COMPREHENSIVE SCHEME FOR THE<br>STRENGTHENING OF THE TRANSMISSION AND<br>DISTRIBUTION SYSTEM IN A P<br>- [N18000249 | 12/2014                       | 4,754.42<br>-                       | 9,141.97                    | 12/2018<br>-                       | 12/2019     | 92.28             | 12                  |
| 48    | NORTH- EAST NORTH WESTERN<br>INTERCONNECTOR I PROJECT<br>- [N18000066                                               | 02/2009                       | 11,130.19<br>-                      | 13,762.80                   | 08/2013<br>-                       | 03/2022     | 23.65             | 103                 |
|       | <u>Satluj Jal Vidyut Nigam Limited</u>                                                                              |                               |                                     |                             |                                    |             |                   |                     |
| 49    | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW<br>BUXAR THERMAL POWER PLANT<br>- [N18000194                                 | 05/2015                       | 436.68<br>-                         | 602.44                      | 12/2016<br>-                       | 03/2019     | 37.96             | 27                  |
|       | <u>Thdc India Limited</u>                                                                                           |                               |                                     |                             |                                    |             |                   |                     |
| 50    | DHUKWAN SMALL HYDRO PROJECT<br>- [N18000189                                                                         | 05/2011                       | 195.42<br>-                         | 294.60                      | 02/2014<br>-                       | 03/2019     | 50.75             | 61                  |
| 51    | VISHNUGAD PIPALKOTI HYDRO ELECTRIC<br>PROJECT<br>[N18000042                                                         | 08/2008                       | 2,491.58<br>-                       | 4,105.30                    | 06/2013<br>-                       | 12/2021     | 64.77             | 102                 |
| 52    | TEHRI PUMPED STORAGE PLANT(1000MW)<br>- [N18000010                                                                  | 07/2006                       | 1,657.00<br>-                       | 4,401.90                    | 02/2016<br>-                       | 05/2021     | 165.65            | 63                  |
|       | Total                                                                                                               |                               | 1,28,289.04<br>-                    | 1,72,137.31                 |                                    |             |                   |                     |
|       |                                                                                                                     |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>RAILWAYS</u>                                                                                                     |                               |                                     |                             |                                    |             |                   |                     |

## Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2018)

|       |                                                                                                            |                               |                                     |                             | Date of Commissioning (Month/Year) |             |                   |                     |
|-------|------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|-----------------------------|------------------------------------|-------------|-------------------|---------------------|
| Sl.No | Project                                                                                                    | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised                 | Anticipated | Cost Overruns (%) | T.O.R.s (in months) |
| 1     | 2                                                                                                          | 3                             | 4                                   | 5                           | 6                                  | 7           | 8                 | 9                   |
|       | <u>Container Corporation Of India</u>                                                                      |                               |                                     |                             |                                    |             |                   |                     |
| 53    | MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]                                                       | 08/2016                       | 234.50 -                            | 235.00                      | 03/2019 -                          | 12/2020     | .21               | 21                  |
|       | <u>East Central Railways</u>                                                                               |                               |                                     |                             |                                    |             |                   |                     |
| 54    | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]                                            | 04/1996                       | 477.88<br>283.95                    | 749.00                      | 03/2012 -                          | 03/2020     | 56.73             | 96                  |
| 55    | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]                                                   | 04/1997                       | 324.73 -                            | 1,156.41                    | 03/2012 -                          | 03/2020     | 256.11            | 96                  |
| 56    | MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]                                                      | 04/2016                       | 731.64 -                            | 1,185.73                    | 03/2021 -                          | 03/2022     | 62.06             | 12                  |
| 57    | SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]                                                      | 04/2016                       | 744.04 -                            | 1,215.54                    | 03/2021 -                          | 03/2022     | 63.37             | 12                  |
| 58    | PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474] | 11/2001                       | 624.47 -                            | 3,550.00                    | 02/2016 -                          | 03/2021     | 468.48            | 61                  |
|       | <u>East Coast Railway</u>                                                                                  |                               |                                     |                             |                                    |             |                   |                     |
| 59    | JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]                          | 04/2015                       | 701.61 -                            | 810.02                      | 11/2018 -                          | 03/2021     | 15.45             | 28                  |
| 60    | SAMBALPUR-TALCHER DOUBLING - [N22000315]                                                                   | 03/2011                       | 1,111.99 -                          | 1,539.28                    | 02/2019 -                          | 03/2021     | 38.43             | 25                  |
| 61    | TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]                                                                 | 04/2005                       | 810.78 -                            | 1,928.07                    | 06/2021 -                          | 03/2023     | 137.80            | 21                  |
| 62    | KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]                                                                 | 04/1994                       | 2,923.13 -                          | 3,798.80                    | 03/2009 -                          | 06/2021     | 29.96             | 147                 |
|       | <u>Eastern Railways</u>                                                                                    |                               |                                     |                             |                                    |             |                   |                     |
| 63    | MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]                                                           | 04/1995                       | 1,125.89 -                          | 1,126.36                    | 03/2016 -                          | 03/2020     | .04               | 48                  |
|       | <u>Metropolitan Rapid Transport Projects</u>                                                               |                               |                                     |                             |                                    |             |                   |                     |
| 64    | EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]                                         | 04/2006                       | 495.74 -                            | 734.01                      | 06/2013 -                          | 03/2019     | 48.06             | 69                  |
| 65    | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]                                            | 03/1996                       | 495.44 -                            | 1,781.98                    | 03/2004 -                          | 03/2020     | 259.68            | 192                 |
| 66    | MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]                                                      | 04/2008                       | 5,300.00 -                          | 7,986.04                    | 03/2014 -                          | 03/2019     | 50.68             | 60                  |
|       | <u>North East Frontier Railway</u>                                                                         |                               |                                     |                             |                                    |             |                   |                     |
| 67    | NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]                      | 04/1983                       | 297.32 -                            | 614.00                      | 03/2019 -                          | 03/2020     | 106.51            | 12                  |
| 68    | AGARTALA-AKHAURA NL - [N22000195]                                                                          | 04/2012                       | 569.63 -                            | 650.00                      | 03/2020 -                          | 10/2022     | 14.11             | 31                  |
| 69    | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]                              | 09/2006                       | 385.20 -                            | 1,532.00                    | 03/2019 -                          | 03/2020     | 297.72            | 12                  |

## Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2018)

|       |                                                                                  |                               |                                     |                             | Date of Commissioning (Month/Year) |             |                   |                     |
|-------|----------------------------------------------------------------------------------|-------------------------------|-------------------------------------|-----------------------------|------------------------------------|-------------|-------------------|---------------------|
| Sl.No | Project                                                                          | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised                 | Anticipated | Cost Overruns (%) | T.O.R.s (in months) |
| 1     | 2                                                                                | 3                             | 4                                   | 5                           | 6                                  | 7           | 8                 | 9                   |
| 70    | NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR<br>[N22000087]          | 09/2006                       | 532.87<br>-                         | 2,145.00                    | 03/2019<br>-                       | 03/2020     | 302.54            | 12                  |
| 71    | NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)<br>[N22000124]    | 04/2006                       | 2,326.52<br>-                       | 3,000.00                    | 03/2015<br>-                       | 10/2021     | 28.95             | 79                  |
| 72    | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR<br>- [220100266]          | 04/2000                       | 1,180.19<br>-                       | 3,040.00                    | 12/2008<br>-                       | 03/2019     | 157.59            | 123                 |
| 73    | AGARTALA SABROOM, NL, NEFR<br>- [N22000099]                                      | 04/2008                       | 1,142.00<br>-                       | 3,407.00                    | 03/2014<br>-                       | 03/2019     | 198.34            | 60                  |
| 74    | SEVOK RANGPO, NEFR<br>- [N22000102]                                              | 04/2008                       | 1,339.48<br>-                       | 4,084.69                    | 12/2015<br>-                       | 03/2020     | 204.95            | 51                  |
| 75    | BHAIRABI SAIRONG, NL, NEFR<br>- [N22000100]                                      | 04/2008                       | 2,393.47<br>-                       | 4,968.00                    | 03/2014<br>-                       | 12/2020     | 107.56            | 81                  |
| 76    | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)<br>- [220100288]                             | 04/2003                       | 4,454.17<br>-                       | 13,809.00                   | 03/2011<br>-                       | 03/2020     | 210.02            | 108                 |
|       | <u>North Eastern Railway</u>                                                     |                               |                                     |                             |                                    |             |                   |                     |
| 77    | INDARA - DOHRIGHAT GAUGE CONVERSION.<br>- [N22000456]                            | 04/2016                       | 213.00<br>-                         | 213.35                      | 04/2016<br>-                       | 01/2022     | .16               | 69                  |
| 78    | AUNRIHAR MANDUADIH GAZIPUR VARANASI UP<br>- [N22000133]                          | 03/2012                       | 199.75<br>-                         | 270.00                      | 08/2018<br>-                       | 01/2019     | 35.17             | 5                   |
| 79    | CHHAPRA-BALLIA UP<br>- [N22000134]                                               | 03/2013                       | 295.00<br>-                         | 477.31                      | 01/2019<br>-                       | 02/2019     | 61.80             | 1                   |
| 80    | MANDHANA - BRAHMAWART NEW LINE PROJECT.<br>- [N22000458]                         | 04/1997                       | 609.04<br>1,063.00                  | 1,807.88                    | 04/1999<br>-                       | 03/2019     | 196.84            | 239                 |
|       | <u>North Western Railway</u>                                                     |                               |                                     |                             |                                    |             |                   |                     |
| 81    | ALWAR-BANDIKUI DOUBLING<br>- [N22000157]                                         | 04/2013                       | 242.09<br>-                         | 349.00                      | 02/2019<br>-                       | 03/2019     | 44.16             | 1                   |
| 82    | JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR)<br>[N22000113] | 04/2008                       | 653.19<br>-                         | 1,116.00                    | 03/2014<br>-                       | 03/2019     | 70.85             | 60                  |
| 83    | HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)<br>- [N22000112]                    | 04/2008                       | 829.74<br>-                         | 1,216.00                    | 03/2015<br>-                       | 06/2020     | 46.55             | 63                  |
|       | <u>Northern Railway</u>                                                          |                               |                                     |                             |                                    |             |                   |                     |
| 84    | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR<br>- [220100133]                             | 03/1995                       | 2,500.00<br>-                       | 27,949.00                   | 11/2002<br>-                       | 03/2021     | 1,017.96          | 220                 |
|       | <u>Rail Vikas Nigam Ltd.</u>                                                     |                               |                                     |                             |                                    |             |                   |                     |
| 85    | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)<br>- [220100327]                       | 04/2000                       | 133.41<br>207.00                    | 385.00                      | 03/2009<br>03/2009                 | 02/2019     | 188.58            | 119                 |
| 86    | SALKA ROAD -ANUPNAGAR LINE DOUBLING<br>- [N22000075]                             | 09/2006                       | 383.54<br>-                         | 555.00                      | 03/2010<br>-                       | 12/2019     | 44.70             | 117                 |
| 87    | MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD<br>[N22000213]             | 04/2012                       | 632.68<br>-                         | 816.55                      | 03/2016<br>-                       | 12/2020     | 29.06             | 57                  |
| 88    | LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC<br>- [N22000404]                     | 04/2011                       | 927.01<br>-                         | 977.00                      | 03/2019<br>-                       | 03/2020     | 5.39              | 12                  |

## Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2018)

|       |                                                                                                               |                               |                                     |                             | Date of Commissioning (Month/Year) |             |                   |                     |
|-------|---------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|-----------------------------|------------------------------------|-------------|-------------------|---------------------|
| Sl.No | Project                                                                                                       | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised                 | Anticipated | Cost Overruns (%) | T.O.R.s (in months) |
| 1     | 2                                                                                                             | 3                             | 4                                   | 5                           | 6                                  | 7           | 8                 | 9                   |
| 89    | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149                                 | 04/1995                       | 631.78 -                            | 1,195.00                    | 12/2012 -                          | 03/2022     | 89.15             | 111                 |
| 90    | HARIDASPUR-PARADEEP(NL) - [220100285                                                                          | 04/1996                       | 1,185.64 -                          | 1,844.47                    | 12/2017 -                          | 03/2020     | 55.57             | 27                  |
| 91    | OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049                                                               | 07/2006                       | 732.81 -                            | 1,850.00                    | 03/2008 -                          | 03/2020     | 152.45            | 144                 |
| 92    | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109 | 04/2010                       | 2,298.42 -                          | 2,733.86                    | 03/2014 -                          | 12/2025     | 18.95             | 141                 |
| 93    | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110     | 04/2010                       | 3,951.98 -                          | 4,259.48                    | 03/2016 -                          | 03/2025     | 7.78              | 108                 |
|       | <u>South Central Railway</u>                                                                                  |                               |                                     |                             |                                    |             |                   |                     |
| 94    | KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265                                                                   | 12/2001                       | 1,045.20 -                          | 2,120.16                    | 03/2009 -                          | 03/2023     | 102.85            | 168                 |
| 95    | KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261                                                 | 04/2012                       | 1,856.95 -                          | 2,200.00                    | 03/2023 -                          | 03/2024     | 18.47             | 12                  |
|       | <u>South East Central Railway</u>                                                                             |                               |                                     |                             |                                    |             |                   |                     |
| 96    | CHHINDWARA-MANDLA FORT GC - [N22000481                                                                        | 03/2011                       | 556.54 -                            | 1,342.46                    | 03/2012 -                          | 03/2020     | 141.22            | 96                  |
|       | <u>South Eastern Railway</u>                                                                                  |                               |                                     |                             |                                    |             |                   |                     |
| 97    | RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323                                            | 04/2012                       | 148.77 -                            | 377.00                      | 12/2016 -                          | 09/2019     | 153.41            | 33                  |
| 98    | DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164                                                          | 04/2010                       | 309.44 -                            | 525.81                      | 12/2015 -                          | 02/2019     | 69.92             | 38                  |
| 99    | RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADE FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398         | 04/1995                       | 524.43 -                            | 939.00                      | 12/2021 -                          | 12/2024     | 79.05             | 36                  |
| 100   | DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160                                                       | 04/2010                       | 651.00 -                            | 1,009.00                    | 03/2015 -                          | 03/2024     | 54.99             | 108                 |
| 101   | ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395                                                            | 11/2015                       | 969.83 -                            | 1,151.81                    | 03/2020 -                          | 06/2020     | 18.76             | 3                   |
| 102   | BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402                                        | 04/1998                       | 1,027.40 -                          | 2,373.00                    | 03/2003 -                          | 03/2030     | 130.97            | 324                 |
|       | <u>South Western Railway</u>                                                                                  |                               |                                     |                             |                                    |             |                   |                     |
| 103   | KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486                                                    | 03/1996                       | 644.78 -                            | 889.52                      | 03/2017 -                          | 03/2020     | 37.96             | 36                  |
| 104   | HOTGI-KUDGI-GADAG - [N22000333                                                                                | 03/2015                       | 1,614.59 -                          | 1,870.41                    | 03/2019 -                          | 03/2021     | 15.84             | 24                  |
|       | <u>Southern Railway</u>                                                                                       |                               |                                     |                             |                                    |             |                   |                     |
| 105   | OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373                                            | 10/2013                       | 187.26 -                            | 231.67                      | 04/2014 -                          | 03/2020     | 23.72             | 71                  |
|       | <u>West Central Railway</u>                                                                                   |                               |                                     |                             |                                    |             |                   |                     |

## Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2018)

|       |                                                                                                                    |                               |                                     |                             | Date of Commissioning (Month/Year) |             |                   |                     |
|-------|--------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|-----------------------------|------------------------------------|-------------|-------------------|---------------------|
| Sl.No | Project                                                                                                            | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised                 | Anticipated | Cost Overruns (%) | T.O.R.s (in months) |
| 1     | 2                                                                                                                  | 3                             | 4                                   | 5                           | 6                                  | 7           | 8                 | 9                   |
| 106   | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]                                                               | 09/1998                       | 247.66 -                            | 6,093.31                    | 05/2008 -                          | 03/2023     | 2,360.35          | 178                 |
|       | <u>Western Railway</u>                                                                                             |                               |                                     |                             |                                    |             |                   |                     |
| 107   | BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]                                             | 04/2008                       | 318.24 -                            | 321.62                      | 03/2012 -                          | 03/2019     | 1.06              | 84                  |
| 108   | RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]        | 04/1994                       | 320.66 -                            | 858.96                      | 03/2019 -                          | 03/2022     | 167.87            | 36                  |
|       | Total                                                                                                              |                               | 57,564.52 -                         | 1,35,364.56                 |                                    |             |                   |                     |
|       |                                                                                                                    |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                 |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>National Highways And Infrastructure Development Corporation Ltd.</u>                                           |                               |                                     |                             |                                    |             |                   |                     |
| 109   | CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]                                | 12/2016                       | 138.93 155.00                       | 155.00                      | 01/2017 -                          | 01/2020     | 11.57             | 36                  |
|       | <u>National Highways Authority Of India</u>                                                                        |                               |                                     |                             |                                    |             |                   |                     |
| 110   | DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]                                                              | 12/2003                       | 160.00 -                            | 167.98                      | 05/2008 -                          | 02/2019     | 4.99              | 129                 |
| 111   | NALBARI T BIJNI (AS-7) - [N24000048]                                                                               | 12/2003                       | 208.00 -                            | 230.00                      | 04/2008 -                          | 03/2019     | 10.58             | 131                 |
| 112   | BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]                                                                           | 12/2003                       | 217.61 -                            | 360.84                      | 04/2010 -                          | 04/2019     | 65.82             | 108                 |
| 113   | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]                                               | 12/2003                       | 280.00 -                            | 361.00                      | 02/2009 -                          | 12/2018     | 28.93             | 118                 |
| 114   | MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]                                                  | 12/2003                       | 199.81 -                            | 385.13                      | 04/2009 -                          | 03/2019     | 92.75             | 119                 |
| 115   | CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662] | 03/2017                       | 754.54 -                            | 756.27                      | 03/2020 -                          | 04/2020     | .23               | 1                   |
| 116   | 4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]                                          | 03/2017                       | 988.34 -                            | 1,043.28                    | 03/2020 -                          | 08/2020     | 5.56              | 5                   |
| 117   | 4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]                                         | 03/2017                       | 1,030.44 -                          | 1,065.51                    | 03/2020 -                          | 05/2020     | 3.40              | 2                   |
| 118   | 4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]                                        | 03/2017                       | 1,059.73 -                          | 1,071.00                    | 03/2017 -                          | 11/2020     | 1.06              | 44                  |
| 119   | 4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]                                        | 03/2017                       | 1,098.06 -                          | 1,160.64                    | 03/2020 -                          | 08/2020     | 5.70              | 5                   |
| 120   | SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]   | 03/2017                       | 831.58 -                            | 1,177.00                    | 03/2020 -                          | 06/2020     | 41.54             | 3                   |

## Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2018)

|       |                                                                                                                   |                               |                                     |                             | Date of Commissioning (Month/Year) |             |                   |                     |
|-------|-------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|-----------------------------|------------------------------------|-------------|-------------------|---------------------|
| Sl.No | Project                                                                                                           | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised                 | Anticipated | Cost Overruns (%) | T.O.R.s (in months) |
| 1     | 2                                                                                                                 | 3                             | 4                                   | 5                           | 6                                  | 7           | 8                 | 9                   |
| 121   | SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668                 | 03/2017                       | 1,041.62 -                          | 1,187.10                    | 03/2020 -                          | 05/2020     | 13.97             | 2                   |
| 122   | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654 | 03/2017                       | 1,184.71 -                          | 1,310.00                    | 03/2020 -                          | 08/2020     | 10.58             | 5                   |
| 123   | SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675 | 03/2017                       | 993.16 -                            | 1,434.00                    | 03/2020 -                          | 06/2020     | 44.39             | 3                   |
| 124   | 4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233                                                | 04/2014                       | 1,266.60 -                          | 1,544.00                    | 09/2016 -                          | 06/2019     | 21.90             | 33                  |
| 125   | FOUR LANING OF GWALIOR-SHIVPURI - [N24000494                                                                      | 05/2013                       | 1,055.00 -                          | 1,601.77                    | 11/2015 -                          | 12/2018     | 51.83             | 37                  |
| 126   | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133                                                          | 05/2009                       | 1,108.00 -                          | 2,288.00                    | 11/2011 -                          | 06/2019     | 106.50            | 91                  |
|       | Total                                                                                                             |                               | 13,616.13 -                         | 17,298.52                   |                                    |             |                   |                     |
|       |                                                                                                                   |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>SHIPPING AND PORTS</u>                                                                                         |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>Mumbai Port Trust</u>                                                                                          |                               |                                     |                             |                                    |             |                   |                     |
| 127   | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063 | 01/2007                       | 366.39 -                            | 669.46                      | 12/2010 -                          | -           | 82.72             | 96                  |
|       | <u>Port Trust</u>                                                                                                 |                               |                                     |                             |                                    |             |                   |                     |
| 128   | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035                                          | 10/2002                       | 150.00 -                            | 600.00                      | 03/2006 -                          | 02/2019     | 300.00            | 155                 |
|       | Total                                                                                                             |                               | 516.39 -                            | 1,269.46                    |                                    |             |                   |                     |
|       |                                                                                                                   |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>TELECOMMUNICATIONS</u>                                                                                         |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>Department Of Telecommunication</u>                                                                            |                               |                                     |                             |                                    |             |                   |                     |
| 129   | NETWORK FOR SPECTRUM - [N26000101                                                                                 | 03/2012                       | 13,334.00 -                         | 24,664.00                   | 07/2015 -                          | 05/2020     | 84.97             | 58                  |
|       | Total                                                                                                             |                               | 13,334.00 -                         | 24,664.00                   |                                    |             |                   |                     |
|       |                                                                                                                   |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>URBAN DEVELOPMENT</u>                                                                                          |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>Central Public Works Department</u>                                                                            |                               |                                     |                             |                                    |             |                   |                     |
| 130   | CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101  | 12/2008                       | 114.26<br>266.00                    | 266.00                      | 12/2013 -                          | 10/2019     | 132.80            | 70                  |
| 131   | CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100          | 02/2016                       | 496.18<br>496.00                    | 498.99                      | 06/2017 -                          | 06/2020     | .57               | 36                  |



## Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2018)

|       |                                                                                                              |                                  |                                        |                                | Date of Commissioning<br>(Month/Year) |             |                   |                     |
|-------|--------------------------------------------------------------------------------------------------------------|----------------------------------|----------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|---------------------|
| Sl.No | Project                                                                                                      | Date of Approval<br>(Month/Year) | Original / Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs.crore) | Original / Revised                    | Anticipated | Cost Overruns (%) | T.O.R.s (in months) |
| 1     | 2                                                                                                            | 3                                | 4                                      | 5                              | 6                                     | 7           | 8                 | 9                   |
| 132   | ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071 | 10/2013                          | 1,219.21 -                             | 1,592.00                       | 10/2019 -                             | 03/2020     | 30.58             | 5                   |
|       | Total                                                                                                        |                                  | 1,829.65 -                             | 2,356.99                       |                                       |             |                   |                     |
|       |                                                                                                              |                                  |                                        |                                |                                       |             |                   |                     |
|       | Grand Total                                                                                                  |                                  | 2,49,711.44                            | 4,02,459.98                    |                                       |             |                   |                     |

## Details of Projects Without Date of Commissioning

### Annexure - VIII

| Costing Rs. 150 Crore and above |                                                                                                     |                               |                                     | (December 2018)                    |             |
|---------------------------------|-----------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
|                                 |                                                                                                     |                               |                                     | Date of Commissioning (Month/Year) |             |
| Sl.No                           | Project                                                                                             | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1                               | 2                                                                                                   | 3                             | 4                                   | 5                                  | 6           |
|                                 | <u>COAL</u>                                                                                         |                               |                                     |                                    |             |
|                                 | <u>Bharat Coking Coal Limited</u>                                                                   |                               |                                     |                                    |             |
| 1                               | MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND                                                   | 08/2010                       | 289.45 -                            | 05/2014 -                          | 04/2018     |
| 2                               | PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND                                                   | 10/2012                       | 269.82 -                            | 04/2014 -                          | 04/2018     |
| 3                               | MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND                                           | 02/2011                       | 339.88 -                            | 04/2014 -                          | 10/2018     |
| 4                               | KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND                                                        | 08/2011                       | 988.35 -                            | 04/2017 -                          | -           |
|                                 | <u>Eastern Coal Fields Limited</u>                                                                  |                               |                                     |                                    |             |
| 5                               | RANIGANJ MASTER PLAN - [N06000163]ECL, WEST BENGAL                                                  | 08/2009                       | 2,661.73 -                          | 08/2019 -                          | -           |
|                                 | <u>Mahanadi Coal Fields Limited</u>                                                                 |                               |                                     |                                    |             |
| 6                               | KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA                                        | 01/2005                       | 302.96 -                            | 03/2010 -                          | 03/2018     |
|                                 | <u>Northern Coal Fields Limited</u>                                                                 |                               |                                     |                                    |             |
| 7                               | NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]INCL,MADHYA PRADESH           | 10/2007                       | 259.40 -                            | 03/2012 -                          | -           |
|                                 | <u>Singareni Colliers Company Limited</u>                                                           |                               |                                     |                                    |             |
| 8                               | KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA                                                      | 12/2008                       | 453.63 -                            | 12/2012 -                          | -           |
| 9                               | MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA                                      | 03/2010                       | 181.19 -                            | 03/2012 -                          | -           |
|                                 | <u>South-Eastern Coal Fields Limited</u>                                                            |                               |                                     |                                    |             |
| 10                              | AMERA OC RCE - [N06000123]SECL, CHHATISGARH                                                         | 02/2015                       | 335.97 -                            | 03/2018 -                          | 03/2018     |
|                                 | <u>Western Coal Fields Limited</u>                                                                  |                               |                                     |                                    |             |
| 11                              | GOKUL - [N06000120]WCL, MAHARASHTRA                                                                 | 11/2014                       | 267.67 -                            | 03/2018 -                          | 03/2018     |
|                                 | Total                                                                                               |                               | 6,350.05 -                          |                                    |             |
|                                 | <u>STEEL</u>                                                                                        |                               |                                     |                                    |             |
|                                 | <u>Raastriya Ispat Nigam Limited</u>                                                                |                               |                                     |                                    |             |
| 12                              | REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL, ANDHRA PRADESH                            | 12/2009                       | 343.00 -                            | 10/2016 -                          | -           |
|                                 | <u>Steel Authority Of India Limited (SAIL)</u>                                                      |                               |                                     |                                    |             |
| 13                              | DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL, CHHATISGARH | 04/2014                       | 188.93 -                            | 04/2015 -                          | -           |

## Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December  
2018)

|       |                                                                                                                       |                               |                                     | Date of Commissioning (Month/Year) |             |
|-------|-----------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
| Sl.No | Project                                                                                                               | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1     | 2                                                                                                                     | 3                             | 4                                   | 5                                  | 6           |
| 14    | EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND | 02/2014                       | 4,749.00<br>-                       | 09/2017<br>-                       | -           |
|       | Total                                                                                                                 |                               | 5,280.93<br>-                       |                                    |             |
|       |                                                                                                                       |                               |                                     |                                    |             |
|       | <u>PETROLEUM</u>                                                                                                      |                               |                                     |                                    |             |
|       | <u>Bharat Petroleum Corporation Limited</u>                                                                           |                               |                                     |                                    |             |
| 15    | IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU                                                          | 11/2012                       | 678.00<br>-                         | 02/2017<br>-                       | -           |
|       | <u>Chennai Petroleum Corporation Limited</u>                                                                          |                               |                                     |                                    |             |
| 16    | RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU                                                                | 03/2013                       | 3,110.36<br>-                       | 11/2015<br>-                       | -           |
|       | <u>Hindustan Petroleum Corporation Limited</u>                                                                        |                               |                                     |                                    |             |
| 17    | 50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN                                          | 11/2011                       | 310.00<br>-                         | 03/2013<br>-                       | -           |
|       | <u>Indian Oil Corporation Limited</u>                                                                                 |                               |                                     |                                    |             |
| 18    | PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE                                                         | 08/2009                       | 1,793.00<br>-                       | 12/2016<br>-                       | -           |
| 19    | RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND                           | 04/2011                       | 191.96<br>-                         | 05/2015<br>-                       | -           |
| 20    | REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL,GUJARAT                                                           | 10/2014                       | 279.00<br>-                         | 08/2018<br>-                       | -           |
| 21    | LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN                                                                    | 03/2018                       | 229.80<br>-                         | -<br>-                             | -           |
| 22    | AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]IOCL,GUJARAT          | 03/2018                       | 588.20<br>-                         | -<br>-                             | -           |
|       | <u>Indian Strategic Petroleum Reserves Ltd</u>                                                                        |                               |                                     |                                    |             |
| 23    | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR,KARNATAKA                                              | 01/2006                       | 993.00<br>-                         | 01/2012<br>-                       | -           |
|       | <u>Oil &amp; Natural Gas Corporation Limited</u>                                                                      |                               |                                     |                                    |             |
| 24    | CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE                                         | 06/2007                       | 736.65<br>-                         | 09/2011<br>-                       | -           |
|       | <u>Oil India Limited</u>                                                                                              |                               |                                     |                                    |             |
| 25    | 50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE                                                           | 11/2015                       | 500.00<br>-                         | 06/2017<br>-                       | -           |
| 26    | UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM         | 09/2012                       | 871.35<br>-                         | 03/2015<br>-                       | -           |
|       | Total                                                                                                                 |                               | 10,281.32<br>-                      |                                    |             |
|       |                                                                                                                       |                               |                                     |                                    |             |
|       | <u>POWER</u>                                                                                                          |                               |                                     |                                    |             |
|       | <u>National Hydro-Electric Power Corporation</u>                                                                      |                               |                                     |                                    |             |
| 27    | SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH                                           | 09/2003                       | 6,285.33<br>-                       | 09/2010<br>-                       | -           |
|       | <u>National Thermal Power Corporation</u>                                                                             |                               |                                     |                                    |             |

## Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2018)

|       |                                                                                                                                    |                               |                                     | Date of Commissioning (Month/Year) |             |
|-------|------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
| Sl.No | Project                                                                                                                            | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1     | 2                                                                                                                                  | 3                             | 4                                   | 5                                  | 6           |
| 28    | PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND                                                                     | 10/2004                       | 4,237.96<br>4,238.00                | 10/2017<br>-                       | 12/2016     |
| 29    | KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA                                                                                     | 01/2012                       | 15,166.19<br>-                      | 01/2017<br>-                       | -           |
| 30    | MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA                                                                                   | 03/2012                       | 7,921.47<br>-                       | 09/2016<br>-                       | -           |
| 31    | LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND                                                    | 07/2012                       | 1,527.00<br>-                       | 08/2017<br>-                       | -           |
| 32    | FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH                                                               | 07/2013                       | 3,363.12<br>-                       | 12/2016<br>-                       | -           |
|       | <u>North East Electric Power Corporation</u>                                                                                       |                               |                                     |                                    |             |
| 33    | TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA                                                                        | 07/2009                       | 421.01<br>-                         | 07/2013<br>-                       | -           |
|       | <u>Power Grid Corporation Of India Limited</u>                                                                                     |                               |                                     |                                    |             |
| 34    | TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR    | 01/2014                       | 1,788.41<br>1,788.41                | 09/2017<br>09/2017                 | 11/2018     |
| 35    | COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU | 09/2011                       | 1,940.13<br>-                       | 09/2014<br>-                       | -           |
| 36    | COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE   | 03/2013                       | 2,514.88<br>-                       | 12/2015<br>-                       | -           |
| 37    | SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE                                                        | 01/2016                       | 1,455.47<br>-                       | 07/2018<br>-                       | -           |
|       | Total                                                                                                                              |                               | 46,620.97<br>-                      |                                    |             |
|       |                                                                                                                                    |                               |                                     |                                    |             |
|       | <u>HEALTH AND FAMILY WELFARE</u>                                                                                                   |                               |                                     |                                    |             |
|       | <u>Hospital Services Consultancy Corporation Ltd</u>                                                                               |                               |                                     |                                    |             |
| 38    | CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL                                                                             | 08/2016                       | 244.00<br>-                         | 09/2018<br>-                       | 09/2018     |
| 39    | LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM                                                                                      | 07/2012                       | 175.57<br>-                         | 12/2014<br>-                       | -           |
| 40    | CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA                                                       | 09/2014                       | 505.58<br>-                         | 03/2018<br>-                       | -           |
|       | Total                                                                                                                              |                               | 925.15<br>-                         |                                    |             |
|       |                                                                                                                                    |                               |                                     |                                    |             |
|       | <u>RAILWAYS</u>                                                                                                                    |                               |                                     |                                    |             |
|       | <u>Central Railways</u>                                                                                                            |                               |                                     |                                    |             |
| 41    | AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA                                                                                | 06/1994                       | 663.01<br>668.34                    | 06/1999<br>-                       | -           |
|       | <u>Container Corporation Of India</u>                                                                                              |                               |                                     |                                    |             |
| 42    | MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH                                                      | 01/2013                       | 387.70<br>-                         | 03/2018<br>-                       | -           |
| 43    | MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH                                                            | 05/2014                       | 207.00<br>-                         | 03/2018<br>-                       | -           |

## Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December  
2018)

|       |                                                                                                                                  |                               |                                     | Date of Commissioning (Month/Year) |             |
|-------|----------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
| Sl.No | Project                                                                                                                          | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1     | 2                                                                                                                                | 3                             | 4                                   | 5                                  | 6           |
|       | <u>Dedicated Freight Corridor Corporation Of India Ltd</u>                                                                       |                               |                                     |                                    |             |
| 44    | EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE                                                         | 10/2006                       | 11,589.00<br>30,357.00              | -<br>-                             | -           |
|       | <u>East Central Railways</u>                                                                                                     |                               |                                     |                                    |             |
| 45    | KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND                                                                             | 04/2002                       | 459.91<br>-                         | -<br>-                             | -           |
| 46    | DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR                                                                             | 04/2001                       | 406.92<br>-                         | -<br>-                             | -           |
| 47    | NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR                                                                                      | 04/2008                       | 620.57<br>-                         | -<br>-                             | -           |
| 48    | DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR                                                                            | 04/2005                       | 205.00<br>-                         | -<br>-                             | -           |
| 49    | MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR                                                                                   | 04/2006                       | 211.00<br>-                         | -<br>-                             | -           |
| 50    | SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR                                                               | 04/2008                       | 678.62<br>-                         | -<br>-                             | -           |
| 51    | MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR                                                                 | 04/2008                       | 228.05<br>-                         | -<br>-                             | -           |
| 52    | KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR                                                                                   | 04/2008                       | 192.56<br>-                         | -<br>-                             | -           |
| 53    | MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR                                                                                | 04/2008                       | 281.30<br>-                         | -<br>-                             | -           |
| 54    | HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR                                                                           | 04/2013                       | 213.01<br>-                         | -<br>-                             | -           |
| 55    | SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR                                                                                      | 05/2015                       | 380.00<br>-                         | -<br>-                             | -           |
| 56    | MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR                                                                            | 01/1991                       | 332.15<br>-                         | 07/2014<br>-                       | -           |
|       | <u>East Coast Railway</u>                                                                                                        |                               |                                     |                                    |             |
| 57    | GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR                                                                        | 04/2008                       | 445.25<br>-                         | -<br>-                             | -           |
| 58    | GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE                                                                                   | 04/2008                       | 415.67<br>-                         | -<br>-                             | -           |
| 59    | BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR                                                                                    | 04/2008                       | 326.20<br>-                         | -<br>-                             | -           |
|       | <u>Eastern Railways</u>                                                                                                          |                               |                                     |                                    |             |
| 60    | DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE                                                                       | 04/2000                       | 607.09<br>-                         | 02/2013<br>-                       | -           |
| 61    | BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL                                                                                 | 04/2007                       | 1,106.62<br>-                       | 12/2010<br>-                       | -           |
| 62    | DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL                                                                      | 04/2009                       | 259.51<br>-                         | 02/2012<br>-                       | -           |
| 63    | GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL                                                                            | 04/2009                       | 193.08<br>-                         | 12/2011<br>-                       | -           |
| 64    | LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE | 04/1987                       | 406.99<br>-                         | 03/2006<br>-                       | -           |
| 65    | SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE                                                  | 04/2007                       | 450.00<br>-                         | -<br>-                             | -           |

## Details of Projects Without Date of Commissioning

| Costing Rs. 150 Crore and above |                                                                                                                                  |                               |                                     |                                    | (December 2018) |
|---------------------------------|----------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-----------------|
|                                 |                                                                                                                                  |                               |                                     | Date of Commissioning (Month/Year) |                 |
| Sl.No                           | Project                                                                                                                          | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated     |
| 1                               | 2                                                                                                                                | 3                             | 4                                   | 5                                  | 6               |
| 66                              | HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE                                                                     | 04/2010                       | 172.03<br>-                         | -<br>-                             | -               |
| 67                              | BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE                                                                              | 04/2011                       | 288.35<br>-                         | -<br>-                             | -               |
| 68                              | PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE                                                                                  | 04/2011                       | 261.38<br>-                         | -<br>-                             | -               |
| 69                              | KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE | 04/2001                       | 923.52<br>-                         | 03/2016<br>-                       | -               |
| 70                              | CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE                     | 04/2005                       | 595.51<br>-                         | 03/2017<br>-                       | -               |
| 71                              | KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE                      | 04/2010                       | 174.56<br>-                         | -<br>-                             | -               |
| 72                              | DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE   | 04/2010                       | 365.17<br>-                         | 03/2017<br>-                       | -               |
| 73                              | HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE                                           | 04/2010                       | 157.94<br>-                         | 11/2018<br>-                       | -               |
| 74                              | BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE                                                 | 04/2007                       | 450.55<br>-                         | -<br>-                             | -               |
| 75                              | TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE                                                                        | 04/2010                       | 365.17<br>-                         | -<br>-                             | -               |
| 76                              | BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE                                                                          | 04/2011                       | 175.80<br>-                         | -<br>-                             | -               |
| 77                              | PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE                                                    | 04/2011                       | 299.60<br>-                         | 03/2017<br>-                       | -               |
| 78                              | NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE | 04/2010                       | 494.54<br>-                         | 03/2005<br>-                       | -               |
| 79                              | SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE                                 | 04/2000                       | 297.47<br>-                         | -<br>-                             | -               |
| 80                              | CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESTALA AND CHA - [N22000242]ER,MULTI STATE  | 04/2003                       | 337.96<br>-                         | -<br>-                             | -               |
| 81                              | MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE   | 04/2009                       | 499.96<br>-                         | 02/2012<br>-                       | -               |
| 82                              | LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE                                 | 04/2009                       | 257.42<br>-                         | 03/2014<br>-                       | -               |
| 83                              | SANTOSHAPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE                                                 | 04/2010                       | 268.52<br>-                         | -<br>-                             | -               |
| 84                              | HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE         | 04/2011                       | 166.89<br>-                         | -<br>-                             | -               |
| 85                              | MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE                                                                                    | 04/2012                       | 250.93<br>-                         | -<br>-                             | -               |
| 86                              | BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL                                                                    | 04/2012                       | 255.64<br>-                         | -<br>-                             | -               |

## Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2018)

|       |                                                                                                                                 |                               |                                     | Date of Commissioning (Month/Year) |             |
|-------|---------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
| Sl.No | Project                                                                                                                         | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1     | 2                                                                                                                               | 3                             | 4                                   | 5                                  | 6           |
|       | <u>Kochi Metro Rail Corporation Ltd</u>                                                                                         |                               |                                     |                                    |             |
| 87    | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRL, WEST BENGAL            | 04/2010                       | 2,397.72 -                          | 03/2016 -                          | -           |
|       | <u>Metropolitan Rapid Transport Projects</u>                                                                                    |                               |                                     |                                    |             |
| 88    | TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL                  | 03/2000                       | 1,049.69 -                          | 12/2006 -                          | -           |
| 89    | EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL                                         | 03/2013                       | 4,874.58 -                          | 03/2016 -                          | -           |
| 90    | CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL                                           | 04/2009                       | 573.78 -                            | - -                                | -           |
| 91    | RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA                                                         | 04/2012                       | 714.10 -                            | 04/2016 -                          | -           |
|       | <u>North Central Railway</u>                                                                                                    |                               |                                     |                                    |             |
| 92    | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR, MULTI STATE                                                 | 04/1986                       | 158.77 274.56                       | 03/1994 -                          | -           |
| 93    | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, UTTAR PRADESH                                                      | 04/1999                       | 108.00 -                            | 12/2009 -                          | -           |
| 94    | ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH                                                                       | 04/1997                       | 120.00 -                            | 12/2008 -                          | -           |
|       | <u>North East Frontier Railway</u>                                                                                              |                               |                                     |                                    |             |
| 95    | CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA                                                            | 04/1999                       | 895.00 984.97                       | 03/2007 -                          | 04/2016     |
| 96    | KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR                                                                           | 09/2001                       | 792.46 724.31                       | 12/2010 -                          | -           |
| 97    | NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE                                                            | 04/2010                       | 241.52 -                            | - -                                | -           |
| 98    | NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE | 04/1999                       | 819.23 -                            | - -                                | -           |
|       | <u>North Eastern Railway</u>                                                                                                    |                               |                                     |                                    |             |
| 99    | BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH                                                                  | 03/2008                       | 195.64 -                            | - -                                | 03/2018     |
| 100   | MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR                                                                          | 04/2003                       | 218.19 -                            | 06/2018 -                          | 10/2018     |
| 101   | KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]NER, MULTI STATE                                                           | 04/1999                       | 744.71 -                            | - -                                | -           |
| 102   | KICHHA-KHATIMA (NL) - NER - [220100317]NER, UTTARAKHAND                                                                         | 04/2003                       | 142.45 -                            | - -                                | -           |
| 103   | ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130]NER, UTTAR PRADESH                                                          | 03/2013                       | 307.00 -                            | - -                                | -           |
| 104   | KAPILVASTU-BASTI VIA BANSI SIDHARTH NAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH                                      | 03/2013                       | 643.00 -                            | - -                                | -           |
| 105   | GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER, UTTAR PRADESH                                                                     | 04/2014                       | 182.92 -                            | - -                                | -           |
| 106   | GONDA - BAHRAICH (60 KMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]NER, UTTAR PRADESH                                    | 04/1997                       | 233.00 -                            | 04/1999 -                          | -           |

## Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December  
2018)

|       |                                                                                                                |                               |                                     | Date of Commissioning (Month/Year) |             |
|-------|----------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
| Sl.No | Project                                                                                                        | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1     | 2                                                                                                              | 3                             | 4                                   | 5                                  | 6           |
| 107   | PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH                                  | 04/2017                       | 1,343.00<br>-                       | 01/2018<br>-                       | -           |
| 108   | BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH                                             | 04/2016                       | 602.50<br>-                         | -<br>-                             | -           |
|       | <u>North Western Railway</u>                                                                                   |                               |                                     |                                    |             |
| 109   | THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN                                                                  | 04/2013                       | 236.93<br>-                         | 10/2018<br>-                       | 10/2018     |
| 110   | RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE                                                | 04/2011                       | 2,082.75<br>-                       | -<br>-                             | -           |
| 111   | AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN                                                      | 04/2013                       | 822.00<br>-                         | -<br>-                             | -           |
| 112   | PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN                                                                       | 04/2013                       | 323.00<br>-                         | -<br>-                             | -           |
| 113   | AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN                    | 05/2015                       | 873.71<br>-                         | -<br>-                             | -           |
|       | <u>Northern Railway</u>                                                                                        |                               |                                     |                                    |             |
| 114   | NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE                                                           | 03/1981                       | 450.00<br>-                         | 07/2012<br>-                       | -           |
| 115   | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE                                             | 03/2002                       | 625.30<br>408.76                    | 06/2007<br>-                       | -           |
| 116   | JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA                                                                   | 01/2004                       | 238.56<br>-                         | 03/2012<br>-                       | -           |
| 117   | UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH                                             | 04/2006                       | 369.90<br>-                         | 03/2010<br>-                       | -           |
| 118   | MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH                                                     | 04/2012                       | 377.44<br>-                         | -<br>-                             | -           |
| 119   | MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB | 04/2009                       | 396.04<br>-                         | -<br>-                             | -           |
| 120   | GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI                                                             | 04/1999                       | 156.65<br>-                         | -<br>-                             | -           |
| 121   | FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH                        | 04/2013                       | 654.00<br>-                         | -<br>-                             | -           |
| 122   | DELHI-SOHNANUHIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE                                                 | 04/2013                       | 1,239.00<br>-                       | -<br>-                             | -           |
| 123   | ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA                                                                     | 04/2012                       | 287.00<br>-                         | 12/2011<br>-                       | -           |
| 124   | DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE                                                | 04/2007                       | 336.91<br>-                         | -<br>-                             | -           |
| 125   | ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI                                                | 04/2012                       | 295.68<br>-                         | -<br>-                             | -           |
| 126   | HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND                                                                    | 04/2012                       | 219.83<br>-                         | -<br>-                             | -           |
| 127   | AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE                        | 04/2010                       | 338.54<br>-                         | -<br>-                             | -           |
| 128   | JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE                                               | 04/2008                       | 162.96<br>-                         | -<br>-                             | -           |
| 129   | HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA                                                  | 04/2013                       | 400.00<br>-                         | -<br>-                             | -           |



## Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2018)

|       |                                                                                            |                               |                                     | Date of Commissioning (Month/Year) |             |
|-------|--------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
| Sl.No | Project                                                                                    | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1     | 2                                                                                          | 3                             | 4                                   | 5                                  | 6           |
| 130   | YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE                | 04/2013                       | 876.00<br>-                         | -<br>-                             | -           |
| 131   | UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH                                             | 04/2012                       | 1,229.00<br>-                       | -<br>-                             | -           |
| 132   | QADIAN-BEAS - [N22000295]NR,PUNJAB                                                         | 04/2011                       | 205.22<br>-                         | -<br>-                             | -           |
| 133   | CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE                                            | 04/2007                       | 328.14<br>-                         | -<br>-                             | -           |
| 134   | JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE                                 | 03/2002                       | 625.00<br>-                         | 03/2016<br>-                       | -           |
|       | <u>Rail India Technical And Economic Service</u>                                           |                               |                                     |                                    |             |
| 135   | GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE                                  | 04/2015                       | 636.38<br>-                         | -<br>-                             | -           |
|       | <u>Railway Electrification</u>                                                             |                               |                                     |                                    |             |
| 136   | ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH | 02/2008                       | 171.10<br>-                         | 03/2012<br>-                       | -           |
|       | <u>South Central Railway</u>                                                               |                               |                                     |                                    |             |
| 137   | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA                          | 12/1994                       | 124.43<br>-                         | -<br>-                             | 03/2017     |
| 138   | NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH                                | 03/1996                       | 164.36<br>-                         | 02/2009<br>-                       | -           |
| 139   | MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA                                      | 07/1998                       | 458.25<br>-                         | -<br>-                             | -           |
| 140   | MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA                                             | 04/2013                       | 1,112.00<br>-                       | -<br>-                             | -           |
| 141   | BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE                                           | 04/2012                       | 923.23<br>-                         | -<br>-                             | -           |
| 142   | GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH                                      | 04/2011                       | 761.37<br>-                         | -<br>-                             | -           |
| 143   | CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH                                           | 04/2013                       | 829.00<br>-                         | -<br>-                             | -           |
| 144   | KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA                                           | 04/2013                       | 723.00<br>-                         | -<br>-                             | -           |
| 145   | DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH                                         | 04/2015                       | 3,873.07<br>-                       | -<br>-                             | -           |
|       | <u>South East Central Railway</u>                                                          |                               |                                     |                                    |             |
| 146   | CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH                            | 04/2005                       | 383.79<br>-                         | -<br>-                             | -           |
| 147   | KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]SECR,CHHATISGARH   | 04/2013                       | 3,055.00<br>-                       | 09/2018<br>-                       | -           |
|       | <u>South Eastern Railway</u>                                                               |                               |                                     |                                    |             |
| 148   | HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL                              | 04/1974                       | 393.46<br>154.30                    | 03/2007<br>03/2007                 | -           |
| 149   | TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL                              | 03/1984                       | 293.97<br>-                         | 06/2005<br>-                       | -           |
| 150   | BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL                           | 04/2011                       | 289.64<br>-                         | -<br>-                             | -           |

## Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December  
2018)

|       |                                                                                                         |                               |                                     | Date of Commissioning (Month/Year) |             |
|-------|---------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
| Sl.No | Project                                                                                                 | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1     | 2                                                                                                       | 3                             | 4                                   | 5                                  | 6           |
| 151   | CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SR,ODISHA                                        | 04/2010                       | 149.90<br>-                         | 03/2015<br>-                       | -           |
| 152   | ARA-BHABHUA ROAD (NL) - [N22000166]SR,BIHAR                                                             | 04/2008                       | 633.87<br>-                         | -<br>-                             | -           |
|       | <u>Southern Railway</u>                                                                                 |                               |                                     |                                    |             |
| 153   | ATTIPATTU - KORUKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU                         | 02/1999                       | 257.00<br>-                         | 03/2018<br>-                       | 03/2018     |
| 154   | CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE                                                 | 02/1996                       | 240.00<br>-                         | -<br>-                             | -           |
| 155   | KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU                                                           | 02/1997                       | 155.55<br>-                         | -<br>-                             | -           |
| 156   | ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA                                                   | 10/1998                       | 1,566.00<br>-                       | -<br>-                             | -           |
| 157   | QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE                             | 03/1998                       | 280.00<br>-                         | -<br>-                             | -           |
| 158   | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU                            | 09/2006                       | 343.17<br>-                         | -<br>-                             | -           |
| 159   | TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU                                        | 09/2006                       | 227.40<br>-                         | -<br>-                             | -           |
| 160   | TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU                                                        | 09/2006                       | 582.83<br>-                         | -<br>-                             | -           |
| 161   | CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE                                          | 04/2008                       | 523.52<br>-                         | -<br>-                             | -           |
| 162   | SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU | 04/2013                       | 839.00<br>-                         | -<br>-                             | -           |
| 163   | CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU                                         | 04/1999                       | 198.68<br>-                         | -<br>-                             | -           |
| 164   | CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU                              | 04/1998                       | 271.24<br>-                         | -<br>-                             | -           |
| 165   | KURUPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE                                                    | 04/2007                       | 270.14<br>-                         | -<br>-                             | -           |
| 166   | KUMBALAM-TURAVUR - [N22000191]SR,KERALA                                                                 | 04/2011                       | 252.96<br>-                         | -<br>-                             | -           |
| 167   | ERODE-PALANI - [N22000199]SR,TAMIL NADU                                                                 | 04/2008                       | 288.57<br>-                         | -<br>-                             | -           |
| 168   | CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA                                                           | 04/2006                       | 191.72<br>-                         | -<br>-                             | -           |
| 169   | ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA                                                               | 04/2010                       | 189.24<br>-                         | -<br>-                             | -           |
| 170   | TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA                                                  | 02/2015                       | 1,431.90<br>-                       | -<br>-                             | -           |
| 171   | TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA                                                     | 02/2015                       | 1,000.00<br>-                       | -<br>-                             | -           |
| 172   | MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION - [N22000439]SR,TAMIL NADU                               | 02/1997                       | 458.63<br>-                         | 03/2015<br>-                       | -           |
| 173   | TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION - [N22000440]SR,TAMIL NADU                               | 02/2000                       | 200.84<br>-                         | 03/2014<br>-                       | -           |

## Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December  
2018)

|       |                                                                                                                                        |                               |                                     | Date of Commissioning (Month/Year) |             |
|-------|----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
| Sl.No | Project                                                                                                                                | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1     | 2                                                                                                                                      | 3                             | 4                                   | 5                                  | 6           |
| 174   | THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU                                               | 02/1996                       | 268.87<br>-                         | 03/2005<br>-                       | -           |
| 175   | PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA                                                                     | 02/2012                       | 550.00<br>-                         | 03/2016<br>-                       | -           |
| 176   | VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]SR,TAMIL NADU                                                              | 02/2005                       | 600.00<br>600.00                    | 03/2010<br>-                       | -           |
| 177   | MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANAL ROAD) (62.05 KM) DOUBLING - [N22000450]SR,TAMIL NADU                                    | 02/2003                       | 199.55<br>-                         | 03/2009<br>-                       | -           |
| 178   | MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. - [N22000453]SR,TAMIL NADU                                                     | 02/2006                       | 208.00<br>-                         | 03/2012<br>-                       | -           |
| 179   | MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. - [N22000454]SR,KERALA                                                                   | 02/2005                       | 241.00<br>-                         | 03/2014<br>-                       | -           |
|       | <u>Western Railway</u>                                                                                                                 |                               |                                     |                                    |             |
| 180   | BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT                                             | 04/2006                       | 117.36<br>196.95                    | 03/2011<br>-                       | -           |
| 181   | GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT           | 03/2017                       | 243.60<br>-                         | -<br>-                             | -           |
| 182   | MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA                                   | 03/2010                       | 265.88<br>-                         | -<br>-                             | -           |
| 183   | VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA       | 03/2012                       | 217.38<br>-                         | -<br>-                             | -           |
| 184   | VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT           | 03/2012                       | 248.26<br>-                         | -<br>-                             | -           |
| 185   | PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT                          | 03/2012                       | 153.83<br>-                         | -<br>-                             | -           |
|       | <b>Total</b>                                                                                                                           |                               | 87,889.88<br>-                      |                                    |             |
|       |                                                                                                                                        |                               |                                     |                                    |             |
|       | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                                     |                               |                                     |                                    |             |
|       | <u>Dept Of Road Transport &amp; Highways</u>                                                                                           |                               |                                     |                                    |             |
| 186   | CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66 ) FROM KM. 26 /200 ( CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA            | 03/2015                       | 298.33<br>-                         | -<br>-                             | -           |
| 187   | CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA                  | 03/2015                       | 184.05<br>-                         | -<br>-                             | -           |
| 188   | CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA            | 03/2015                       | 280.16<br>-                         | -<br>-                             | -           |
| 189   | REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH | 12/2014                       | 201.12<br>201.00                    | 02/2015<br>-                       | -           |
|       | <u>Ministry Of Road Transport And Highways</u>                                                                                         |                               |                                     |                                    |             |
| 190   | REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH | 07/2015                       | 314.43<br>-                         | -<br>-                             | -           |

## Details of Projects Without Date of Commissioning

| Costing Rs. 150 Crore and above |                                                                                                                                        |                               |                                     |                                    | (December 2018) |
|---------------------------------|----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-----------------|
|                                 |                                                                                                                                        |                               |                                     | Date of Commissioning (Month/Year) |                 |
| Sl.No                           | Project                                                                                                                                | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated     |
| 1                               | 2                                                                                                                                      | 3                             | 4                                   | 5                                  | 6               |
| 191                             | WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA     | 10/2015                       | 289.60<br>-                         | -<br>-                             | -               |
| 192                             | CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA    | 12/2011                       | 156.26<br>227.00                    | -<br>-                             | -               |
| 193                             | CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA    | 03/2011                       | 185.82<br>292.00                    | -<br>-                             | -               |
| 194                             | REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH    | 03/2015                       | 422.34<br>-                         | -<br>-                             | -               |
| 195                             | REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH | 10/2015                       | 480.21<br>-                         | -<br>-                             | -               |
| 196                             | WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN      | 10/2014                       | 269.22<br>-                         | 01/2015<br>-                       | -               |
| 197                             | WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN                       | 10/2014                       | 257.09<br>-                         | 01/2015<br>-                       | -               |
| 198                             | REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN                                       | 10/2013                       | 278.87<br>-                         | 05/2014<br>-                       | -               |
| 199                             | REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN      | 01/1991                       | 376.52<br>-                         | 04/2014<br>-                       | -               |
| 200                             | CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU     | 03/2015                       | 258.97<br>-                         | 08/2015<br>-                       | -               |
| 201                             | REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU     | 03/2015                       | 157.18<br>162.00                    | 07/2015<br>-                       | -               |
| 202                             | CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU      | 11/2015                       | 154.14<br>-                         | 08/2015<br>-                       | -               |
| 203                             | CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH     | 03/2015                       | 629.74<br>-                         | -<br>-                             | -               |
| 204                             | CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH                     | 01/2014                       | 282.41<br>-                         | 03/2016<br>-                       | -               |
| 205                             | REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA    | 01/2015                       | 225.81<br>-                         | -<br>-                             | -               |
| 206                             | WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN       | 12/2015                       | 621.43<br>-                         | 06/2018<br>-                       | -               |
| 207                             | STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA      | 03/2015                       | 165.67<br>-                         | 11/2015<br>-                       | -               |

## Details of Projects Without Date of Commissioning

| Costing Rs. 150 Crore and above |                                                                                                                                     |                               |                                     |                                    | (December 2018) |
|---------------------------------|-------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-----------------|
|                                 |                                                                                                                                     |                               |                                     | Date of Commissioning (Month/Year) |                 |
| Sl.No                           | Project                                                                                                                             | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated     |
| 1                               | 2                                                                                                                                   | 3                             | 4                                   | 5                                  | 6               |
| 208                             | STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA   | 03/2015                       | 159.12<br>-                         | 11/2015<br>-                       | -               |
| 209                             | STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH        | 10/2014                       | 227.74<br>-                         | 10/2016<br>-                       | -               |
| 210                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN   | 01/1991                       | 269.26<br>-                         | 10/2016<br>-                       | -               |
| 211                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA   | 01/1991                       | 219.40<br>-                         | 01/2018<br>-                       | -               |
| 212                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA      | 01/1991                       | 218.63<br>-                         | 10/2017<br>-                       | -               |
| 213                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR       | 01/1991                       | 675.00<br>-                         | -<br>-                             | -               |
| 214                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL | 01/1991                       | 322.00<br>-                         | 03/2018<br>-                       | -               |
| 215                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR       | 01/1991                       | 282.41<br>-                         | 08/2016<br>-                       | -               |
| 216                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR       | 01/1991                       | 358.22<br>-                         | 10/2016<br>-                       | -               |
| 217                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARALI - [N24000406]MORTH,RAJASTHAN     | 01/1991                       | 208.87<br>-                         | 05/2016<br>-                       | -               |
| 218                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA      | 01/1991                       | 229.41<br>-                         | 05/2018<br>-                       | -               |
| 219                             | CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA          | 10/2015                       | 936.40<br>-                         | -<br>-                             | -               |
| 220                             | WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH                                 | 05/2013                       | 164.54<br>-                         | 08/2015<br>-                       | -               |
| 221                             | WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH                            | 12/2014                       | 207.88<br>-                         | -<br>-                             | -               |
| 222                             | WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA         | 12/2015                       | 773.98<br>-                         | -<br>-                             | -               |
| 223                             | WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA         | 12/2015                       | 819.95<br>-                         | -<br>-                             | -               |
| 224                             | REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR                       | 01/1991                       | 478.35<br>-                         | -<br>-                             | -               |
| 225                             | WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH                           | 12/2014                       | 207.88<br>-                         | -<br>-                             | -               |

## Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2018)

|       |                                                                                                                                |                               |                                     | Date of Commissioning (Month/Year) |             |
|-------|--------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
| Sl.No | Project                                                                                                                        | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1     | 2                                                                                                                              | 3                             | 4                                   | 5                                  | 6           |
| 226   | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR  | 10/2014                       | 377.64<br>-                         | 03/2014<br>-                       | -           |
| 227   | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR  | 10/2013                       | 278.39<br>-                         | 08/2014<br>-                       | -           |
| 228   | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR  | 01/2013                       | 322.01<br>-                         | 08/2014<br>-                       | -           |
| 229   | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR  | 11/2013                       | 683.83<br>-                         | 07/2016<br>-                       | -           |
| 230   | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR   | 02/2014                       | 665.50<br>-                         | 07/2016<br>-                       | -           |
| 231   | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR  | 02/2016                       | 178.85<br>-                         | 05/2016<br>-                       | -           |
| 232   | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR  | 02/2016                       | 369.77<br>-                         | 06/2016<br>-                       | -           |
| 233   | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR  | 02/2016                       | 553.30<br>-                         | 05/2016<br>-                       | -           |
| 234   | FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR    | 01/2014                       | 1,408.85<br>-                       | 10/2016<br>-                       | -           |
| 235   | STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV - [N24000580]MORTH,BIHAR | 03/2015                       | 206.80<br>-                         | 07/2016<br>-                       | -           |
| 236   | CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR                   | 08/2015                       | 288.24<br>-                         | 11/2015<br>-                       | -           |
| 237   | REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR  | 08/2016                       | 1,742.01<br>-                       | 12/2016<br>-                       | -           |
| 238   | WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA | 03/2014                       | 191.50<br>192.00                    | 05/2016<br>-                       | -           |
| 239   | WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA | 01/2015                       | 326.63<br>327.00                    | 04/2018<br>-                       | -           |
| 240   | WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA    | 02/2015                       | 239.91<br>240.00                    | 10/2017<br>-                       | -           |
| 241   | WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA  | 03/2015                       | 226.31<br>226.00                    | 10/2017<br>-                       | -           |
| 242   | IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA  | 12/2013                       | 319.80<br>320.00                    | 05/2016<br>-                       | -           |

## Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December  
2018)

|       |                                                                                                                                            |                               |                                     | Date of Commissioning (Month/Year) |             |
|-------|--------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
| Sl.No | Project                                                                                                                                    | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1     | 2                                                                                                                                          | 3                             | 4                                   | 5                                  | 6           |
| 243   | REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA              | 07/2014                       | 342.05<br>342.00                    | 01/2017<br>-                       | -           |
| 244   | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA             | 08/2013                       | 171.96<br>172.00                    | 06/2016<br>-                       | -           |
| 245   | WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA             | 06/2016                       | 157.30<br>157.00                    | 06/2018<br>-                       | -           |
| 246   | WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA             | 03/2014                       | 162.51<br>163.00                    | 05/2016<br>-                       | -           |
| 247   | REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND        | 02/2018                       | 293.68<br>-                         | -<br>-                             | -           |
| 248   | REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND        | 03/2018                       | 460.73<br>-                         | -<br>-                             | -           |
|       | <u>National Highways And Infrastructure Development Corporation Ltd.</u>                                                                   |                               |                                     |                                    |             |
| 249   | FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM             | 05/2015                       | 454.89<br>-                         | 05/2018<br>-                       | -           |
| 250   | 4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM             | 06/2015                       | 437.39<br>-                         | 06/2018<br>-                       | -           |
| 251   | FOUR LANING OF JHANJI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM              | 06/2015                       | 463.49<br>-                         | 06/2018<br>-                       | -           |
| 252   | FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM                         | 03/2015                       | 168.39<br>-                         | 11/2018<br>-                       | -           |
| 253   | 4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM              | 10/2014                       | 588.95<br>-                         | 11/2018<br>-                       | -           |
| 254   | 2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH | 03/2015                       | 194.11<br>-                         | 05/2018<br>-                       | -           |
| 255   | CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH | 07/2015                       | 197.16<br>-                         | 10/2018<br>-                       | -           |
| 256   | 2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH             | 03/2015                       | 394.00<br>-                         | 06/2018<br>-                       | -           |
| 257   | 2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA           | 10/2014                       | 369.00<br>-                         | 03/2018<br>-                       | -           |
| 258   | IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA            | 05/2014                       | 497.89<br>-                         | 04/2017<br>-                       | -           |
| 259   | 2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH                                | 03/2015                       | 235.08<br>-                         | 05/2018<br>-                       | -           |



## Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2018)

|       |                                                                                                                                            |                               |                                     |                    | Date of Commissioning (Month/Year) |
|-------|--------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|--------------------|------------------------------------|
| Sl.No | Project                                                                                                                                    | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised | Anticipated                        |
| 1     | 2                                                                                                                                          | 3                             | 4                                   | 5                  | 6                                  |
| 260   | 4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM                            | 12/2015                       | 223.30<br>-                         | 06/2018<br>-       | -                                  |
| 261   | 4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM                                      | 01/1991                       | 520.01<br>-                         | -<br>-             | -                                  |
| 262   | 4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM               | 01/2016                       | 294.17<br>-                         | 01/2016<br>-       | -                                  |
| 263   | 4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM               | 01/2016                       | 252.00<br>-                         | 01/2016<br>-       | -                                  |
| 264   | 2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH | 01/2016                       | 183.65<br>-                         | 11/2016<br>-       | -                                  |
| 265   | FUNDED ) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH | 01/2016                       | 334.22<br>-                         | 06/2016<br>-       | -                                  |
| 266   | CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD( NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH | 04/2016                       | 245.79<br>-                         | -<br>-             | -                                  |
| 267   | CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH  | 04/2016                       | 198.00<br>-                         | 10/2016<br>-       | -                                  |
| 268   | FUNDED ) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH | 11/2015                       | 434.06<br>-                         | -<br>-             | -                                  |
| 269   | CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH     | 01/2017                       | 1,253.10<br>-                       | 03/2017<br>-       | -                                  |
| 270   | TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH | 03/2017                       | 284.09<br>-                         | 04/2017<br>-       | -                                  |
| 271   | TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH | 02/2017                       | 195.23<br>-                         | 04/2017<br>-       | -                                  |
| 272   | TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH | 02/2017                       | 203.36<br>-                         | 04/2017<br>-       | -                                  |
| 273   | TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH  | 01/2017                       | 194.66<br>-                         | 04/2017<br>-       | -                                  |
| 274   | TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH  | 02/2017                       | 168.32<br>-                         | 04/2017<br>-       | -                                  |
| 275   | TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH  | 02/2017                       | 180.57<br>-                         | 04/2017<br>-       | -                                  |
| 276   | CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH | 02/2017                       | 216.71<br>-                         | 04/2017<br>-       | -                                  |
| 277   | CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH | 02/2017                       | 167.28<br>-                         | 04/2017<br>-       | -                                  |



## Details of Projects Without Date of Commissioning

| Costing Rs. 150 Crore and above |                                                                                                                                           |                               |                                     |                                    | (December 2018) |
|---------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-----------------|
|                                 |                                                                                                                                           |                               |                                     | Date of Commissioning (Month/Year) |                 |
| Sl.No                           | Project                                                                                                                                   | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated     |
| 1                               | 2                                                                                                                                         | 3                             | 4                                   | 5                                  | 6               |
| 278                             | CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND         | 02/2017                       | 507.68<br>-                         | 04/2017<br>-                       | -               |
| 279                             | TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH | 01/2017                       | 198.22<br>-                         | 04/2017<br>-                       | -               |
| 280                             | RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM                                                                            | 04/2017                       | 388.00<br>-                         | 10/2017<br>-                       | -               |
| 281                             | CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND      | 03/2018                       | 274.31<br>-                         | 05/2018<br>-                       | -               |
| 282                             | 2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND      | 03/2018                       | 403.36<br>-                         | 06/2018<br>-                       | -               |
| 283                             | 2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND       | 03/2018                       | 417.24<br>-                         | 05/2018<br>-                       | -               |
| 284                             | CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS     | 03/2015                       | 262.97<br>-                         | 10/2018<br>-                       | -               |
| 285                             | 2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS    | 03/2017                       | 409.85<br>-                         | 12/2017<br>-                       | -               |
| 286                             | CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS    | 03/2015                       | 277.17<br>-                         | 04/2017<br>-                       | -               |
| 287                             | REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS    | 02/2018                       | 391.00<br>-                         | 10/2018<br>-                       | -               |
| 288                             | REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS    | 03/2018                       | 234.27<br>-                         | 10/2018<br>-                       | -               |
| 289                             | (I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND         | 02/2017                       | 387.00<br>-                         | 09/2018<br>-                       | -               |
| 290                             | (II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND          | 03/2018                       | 500.09<br>-                         | 09/2018<br>-                       | -               |
| 291                             | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND          | 03/2018                       | 339.57<br>-                         | 09/2018<br>-                       | -               |
| 292                             | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND          | 03/2018                       | 239.30<br>-                         | 09/2018<br>-                       | -               |
| 293                             | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND          | 03/2018                       | 285.68<br>-                         | 09/2018<br>-                       | -               |
| 294                             | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND          | 03/2018                       | 315.03<br>-                         | 09/2018<br>-                       | -               |

## Details of Projects Without Date of Commissioning

| Costing Rs. 150 Crore and above             |                                                                                                                                       |                               |                                     |                                    | (December 2018) |
|---------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-----------------|
|                                             |                                                                                                                                       |                               |                                     | Date of Commissioning (Month/Year) |                 |
| Sl.No                                       | Project                                                                                                                               | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated     |
| 1                                           | 2                                                                                                                                     | 3                             | 4                                   | 5                                  | 6               |
| 295                                         | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND      | 03/2018                       | 240.64 -                            | 09/2018 -                          | -               |
| 296                                         | CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND     | 03/2018                       | 237.72 -                            | 09/2018 -                          | -               |
| 297                                         | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND     | 03/2018                       | 251.97 -                            | 09/2018 -                          | -               |
| 298                                         | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND      | 03/2018                       | 282.98 -                            | 09/2018 -                          | -               |
| 299                                         | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND     | 03/2018                       | 215.12 -                            | 09/2018 -                          | -               |
| 300                                         | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND     | 03/2018                       | 215.79 -                            | 09/2018 -                          | -               |
| 301                                         | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND     | 03/2018                       | 272.89 -                            | 09/2018 -                          | -               |
| 302                                         | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND     | 03/2018                       | 323.98 -                            | 09/2018 -                          | -               |
| 303                                         | CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM       | 04/2017                       | 318.42 -                            | 11/2017 -                          | -               |
| 304                                         | CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM       | 03/2017                       | 375.80 -                            | - -                                | -               |
| 305                                         | CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM       | 11/2017                       | 290.05 -                            | 11/2017 -                          | -               |
| 306                                         | CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM       | 03/2018                       | 264.84 -                            | 06/2018 -                          | -               |
| 307                                         | CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA- NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL | 03/2017                       | 158.65 -                            | 06/2018 -                          | -               |
| 308                                         | WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA    | 04/2017                       | 553.51 -                            | - -                                | -               |
| 309                                         | FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM        | 03/2015                       | 829.00 -                            | 01/2016 -                          | -               |
| <u>National Highways Authority Of India</u> |                                                                                                                                       |                               |                                     |                                    |                 |
| 310                                         | BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA              | 03/2016                       | 197.69 -                            | 07/2018 -                          | 07/2018         |
| 311                                         | FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND                                                                     | 08/2016                       | 323.72 -                            | 08/2018 -                          | 08/2018         |

## Details of Projects Without Date of Commissioning

| Costing Rs. 150 Crore and above |                                                                                                                                 |                               |                                     |                                    | (December 2018) |
|---------------------------------|---------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-----------------|
|                                 |                                                                                                                                 |                               |                                     | Date of Commissioning (Month/Year) |                 |
| Sl.No                           | Project                                                                                                                         | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated     |
| 1                               | 2                                                                                                                               | 3                             | 4                                   | 5                                  | 6               |
| 312                             | FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHILIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH                         | 01/2016                       | 1,134.97 -                          | 11/2018 -                          | 11/2018         |
| 313                             | 4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND                                  | 11/2012                       | 605.84 -                            | 07/2018 -                          | 07/2018         |
| 314                             | GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT                                                   | 03/2010                       | 1,509.10 -                          | 09/2012 -                          | 08/2018         |
| 315                             | MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM                                               | 12/2003                       | 167.64 -                            | 11/2008 -                          | 09/2018         |
| 316                             | 2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH                                                        | 07/2012                       | 291.36 -                            | 01/2014 -                          | 09/2018         |
| 317                             | DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA                                                                       | 04/2007                       | 486.00 -                            | 05/2010 -                          | 10/2018         |
| 318                             | INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH                                                                        | 10/2010                       | 1,175.00 -                          | 04/2013 -                          | 11/2018         |
| 319                             | TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN | 07/2016                       | 331.46 -                            | 10/2018 -                          | 11/2018         |
| 320                             | MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM                                                    | 12/2003                       | 155.04 -                            | 11/2008 -                          | -               |
| 321                             | HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM                                                                             | 12/2003                       | 196.00 -                            | 07/2009 -                          | -               |
| 322                             | SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE                                                         | 02/2009                       | 1,693.75 -                          | 08/2011 -                          | -               |
| 323                             | 4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE                                                                          | 02/2011                       | 2,498.76 -                          | 08/2014 -                          | -               |
| 324                             | INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH                                                                             | 11/2010                       | 325.00 -                            | 05/2013 -                          | -               |
| 325                             | NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR                                                                             | 05/2011                       | 2,159.00 -                          | 06/2015 -                          | -               |
| 326                             | JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR                                                          | 07/2010                       | 1,813.76 -                          | 07/2013 -                          | -               |
| 327                             | 2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR                                                                              | 05/2011                       | 351.54 -                            | 05/2013 -                          | -               |
| 328                             | ROHTAK-BAWAL - [N24000169]NHAI,HARYANA                                                                                          | 05/2011                       | 650.00 -                            | 11/2013 -                          | -               |
| 329                             | GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH                                                                         | 02/2011                       | 1,141.00 -                          | 08/2013 -                          | -               |
| 330                             | DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU                      | 06/2011                       | 600.00 -                            | 06/2013 -                          | -               |
| 331                             | SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH                                | 11/2011                       | 1,535.00 -                          | 05/2014 -                          | -               |
| 332                             | 2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR                                                                       | 10/2011                       | 375.09 -                            | 04/2014 -                          | -               |
| 333                             | SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR                                                                         | 06/2011                       | 1,100.70 -                          | 06/2014 -                          | -               |
| 334                             | BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH                                                                         | 03/2011                       | 1,046.00 -                          | 09/2013 -                          | -               |
| 335                             | SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA                                                          | 12/2011                       | 1,047.00 -                          | 06/2014 -                          | -               |

## Details of Projects Without Date of Commissioning

| Costing Rs. 150 Crore and above |                                                                                                       |                               |                                     |                                    | (December 2018) |
|---------------------------------|-------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-----------------|
|                                 |                                                                                                       |                               |                                     | Date of Commissioning (Month/Year) |                 |
| Sl.No                           | Project                                                                                               | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated     |
| 1                               | 2                                                                                                     | 3                             | 4                                   | 5                                  | 6               |
| 336                             | RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND                                                   | 12/2012                       | 1,479.00<br>-                       | 06/2015<br>-                       | -               |
| 337                             | ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH                                                        | 03/2013                       | 1,573.00<br>-                       | 09/2015<br>-                       | -               |
| 338                             | AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT                                               | 01/2013                       | 2,125.24<br>-                       | 12/2015<br>-                       | -               |
| 339                             | DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE                                     | 10/2012                       | 1,928.22<br>-                       | 04/2015<br>-                       | -               |
| 340                             | FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA                 | 08/2015                       | 723.54<br>-                         | 02/2018<br>-                       | -               |
| 341                             | FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH                                        | 05/2015                       | 261.09<br>-                         | 05/2017<br>-                       | -               |
| 342                             | THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU                                         | 07/2014                       | 401.11<br>-                         | 01/2017<br>-                       | -               |
| 343                             | 2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH  | 04/2014                       | 351.34<br>-                         | 01/2016<br>-                       | -               |
| 344                             | VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT                                                      | 03/2014                       | 503.16<br>-                         | 08/2016<br>-                       | -               |
| 345                             | 2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH | 09/2015                       | 368.73<br>-                         | 09/2016<br>-                       | -               |
| 346                             | 2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH                            | 06/2014                       | 301.04<br>-                         | 01/2016<br>-                       | -               |
| 347                             | 2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH                     | 04/2014                       | 495.78<br>-                         | 01/2016<br>-                       | -               |
| 348                             | THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU                                 | 11/2014                       | 563.92<br>-                         | 11/2016<br>-                       | -               |
| 349                             | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-III) - [N24000446]NHAI,MULTI STATE        | 09/2015                       | 788.51<br>-                         | 03/2018<br>-                       | -               |
| 350                             | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-II) - [N24000450]NHAI,UTTAR PRADESH       | 09/2015                       | 785.78<br>-                         | 03/2018<br>-                       | -               |
| 351                             | 4-LANING OF GHAGHRA BRIDGE TO VARANASI ( PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH                  | 12/2015                       | 611.65<br>-                         | 06/2016<br>-                       | -               |
| 352                             | NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA                                                       | 09/2005                       | 168.00<br>-                         | 06/2006<br>-                       | -               |
| 353                             | FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR                                               | 08/2015                       | 556.07<br>-                         | -<br>-                             | -               |
| 354                             | FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH                         | 01/2016                       | 815.28<br>-                         | 06/2018<br>-                       | -               |
| 355                             | FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA                 | 11/2015                       | 867.66<br>-                         | 05/2018<br>-                       | -               |
| 356                             | FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH                          | 01/2016                       | 1,027.53<br>-                       | 06/2018<br>-                       | -               |
| 357                             | FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH                   | 06/2016                       | 667.00<br>-                         | 07/2018<br>-                       | -               |
| 358                             | FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH                    | 12/2015                       | 667.00<br>-                         | 06/2018<br>-                       | -               |
| 359                             | FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH                                      | 12/2015                       | 509.13<br>-                         | 04/2018<br>-                       | -               |

## Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December  
2018)

|       |                                                                                                                                          |                               |                                     | Date of Commissioning (Month/Year) |             |
|-------|------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
| Sl.No | Project                                                                                                                                  | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1     | 2                                                                                                                                        | 3                             | 4                                   | 5                                  | 6           |
| 360   | TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU                                                                                              | 03/2007                       | 516.00<br>-                         | 07/2008<br>-                       | -           |
| 361   | MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH                                                                                      | 01/2016                       | 683.24<br>-                         | -<br>-                             | -           |
| 362   | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH         | 03/2016                       | 1,404.50<br>-                       | -<br>-                             | -           |
| 363   | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH | 03/2016                       | 1,396.74<br>-                       | -<br>-                             | -           |
| 364   | BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA                  | 03/2016                       | 244.00<br>-                         | 07/2018<br>-                       | -           |
| 365   | 4-LANNING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA                                                                               | 05/2014                       | 720.69<br>-                         | -<br>-                             | -           |
| 366   | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-I)_NEW - [N24000609]NHAI,DELHI                                               | 09/2015                       | 771.18<br>-                         | -<br>-                             | -           |
| 367   | 4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA                                                       | 11/2016                       | 1,071.61<br>-                       | -<br>-                             | -           |
| 368   | 4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA                                                          | 11/2016                       | 1,064.88<br>-                       | -<br>-                             | -           |
| 369   | VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH                                                                          | 09/2014                       | 1,684.00<br>-                       | 02/2017<br>-                       | -           |
| 370   | CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH     | 12/2016                       | 534.55<br>-                         | -<br>-                             | -           |
| 371   | CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH      | 01/2017                       | 450.68<br>-                         | -<br>-                             | -           |
| 372   | SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT                | 01/2017                       | 1,251.11<br>-                       | -<br>-                             | -           |
| 373   | SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR                                  | 08/2017                       | 950.64<br>-                         | 08/2017<br>-                       | -           |
| 374   | FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU                                                                        | 08/2017                       | 1,176.37<br>-                       | 08/2017<br>-                       | -           |
| 375   | JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT                                                                                                | 10/2017                       | 232.49<br>-                         | 10/2017<br>-                       | -           |
| 376   | FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN                                          | 10/2017                       | 964.17<br>-                         | 10/2017<br>-                       | -           |
| 377   | BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH                                            | 09/2017                       | 374.40<br>-                         | 09/2017<br>-                       | -           |
| 378   | BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH                                    | 09/2017                       | 990.61<br>-                         | 09/2017<br>-                       | -           |
| 379   | 4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU                                                                            | 09/2017                       | 244.27<br>-                         | 09/2017<br>-                       | -           |
| 380   | 4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU                                                                         | 09/2017                       | 1,227.87<br>-                       | 09/2017<br>-                       | -           |
| 381   | BALANCE WORK FOR FOUR LANNING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH    | 12/2017                       | 950.27<br>-                         | -<br>-                             | -           |

## Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December  
2018)

|       |                                                                                                                                          |                               |                                     | Date of Commissioning (Month/Year) |             |
|-------|------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
| Sl.No | Project                                                                                                                                  | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1     | 2                                                                                                                                        | 3                             | 4                                   | 5                                  | 6           |
| 382   | SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI, TAMIL NADU        | 12/2017                       | 379.90<br>-                         | -<br>-                             | -           |
| 383   | FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTIO - [N24000711]NHAI, RAJASTHAN          | 12/2017                       | 1,308.73<br>-                       | -<br>-                             | -           |
| 384   | SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI, MAHARASHTRA      | 12/2017                       | 404.94<br>-                         | -<br>-                             | -           |
| 385   | CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI, BIHAR            | 12/2017                       | 2,598.00<br>-                       | -<br>-                             | -           |
| 386   | REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI, ODISHA           | 12/2017                       | 686.65<br>-                         | -<br>-                             | -           |
| 387   | REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI, ODISHA           | 12/2017                       | 417.51<br>-                         | -<br>-                             | -           |
| 388   | CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI, JAMMU AND KASHMIR | 12/2017                       | 1,471.75<br>-                       | -<br>-                             | -           |
| 389   | 6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI, ANDHRA PRADESH   | 12/2017                       | 328.67<br>-                         | -<br>-                             | -           |
| 390   | SIX LANING OF NARASANNAPETA - RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI, ANDHRA PRADESH   | 12/2017                       | 1,323.15<br>-                       | -<br>-                             | -           |
| 391   | CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI, ANDHRA PRADESH   | 12/2017                       | 357.00<br>-                         | -<br>-                             | -           |
| 392   | ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI, UTTAR PRADESH    | 12/2017                       | 207.00<br>-                         | -<br>-                             | -           |
| 393   | CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI, UTTAR PRADESH    | 12/2017                       | 305.00<br>-                         | -<br>-                             | -           |
| 394   | REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI, BIHAR                  | 01/2018                       | 573.70<br>-                         | -<br>-                             | -           |
| 395   | SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI, BIHAR                                         | 01/2018                       | 895.39<br>-                         | -<br>-                             | -           |
| 396   | FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI, JHARKHAND                                                           | 01/2018                       | 273.46<br>-                         | -<br>-                             | -           |
| 397   | SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI, JHARKHAND                                         | 01/2018                       | 1,155.16<br>-                       | -<br>-                             | -           |
| 398   | FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI, MADHYA PRADESH   | 01/2018                       | 770.73<br>-                         | -<br>-                             | -           |
| 399   | 4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI, MAHARASHTRA                                                | 01/2018                       | 607.00<br>-                         | -<br>-                             | -           |
| 400   | 4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI, MAHARASHTRA                                                   | 01/2018                       | 621.00<br>-                         | -<br>-                             | -           |

## Details of Projects Without Date of Commissioning

| Costing Rs. 150 Crore and above |                                                                                                                                      |                               |                                     |                                    | (December 2018) |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-----------------|
|                                 |                                                                                                                                      |                               |                                     | Date of Commissioning (Month/Year) |                 |
| Sl.No                           | Project                                                                                                                              | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated     |
| 1                               | 2                                                                                                                                    | 3                             | 4                                   | 5                                  | 6               |
| 401                             | REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI, ODISHA       | 01/2018                       | 953.09<br>-                         | -<br>-                             | -               |
| 402                             | REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI, ODISHA       | 01/2018                       | 668.86<br>-                         | -<br>-                             | -               |
| 403                             | REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE ( - [N24000733]NHAI, ODISHA       | 01/2018                       | 633.68<br>-                         | -<br>-                             | -               |
| 404                             | REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI, ODISHA         | 01/2018                       | 614.48<br>-                         | -<br>-                             | -               |
| 405                             | REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI, ODISHA       | 01/2018                       | 564.66<br>-                         | -<br>-                             | -               |
| 406                             | REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI, ODISHA       | 01/2018                       | 686.65<br>-                         | -<br>-                             | -               |
| 407                             | REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI, ODISHA       | 01/2018                       | 1,522.00<br>-                       | -<br>-                             | -               |
| 408                             | REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI, ODISHA       | 01/2018                       | 999.00<br>-                         | -<br>-                             | -               |
| 409                             | REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) ( - [N24000739]NHAI, ODISHA       | 01/2018                       | 503.88<br>-                         | -<br>-                             | -               |
| 410                             | VARANASI RING ROAD PKG - I - [N24000740]NHAI, UTTAR PRADESH                                                                          | 01/2018                       | 450.77<br>-                         | -<br>-                             | -               |
| 411                             | FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI, TELANGANA                                                  | 03/2017                       | 4,429.00<br>-                       | 03/2017<br>-                       | -               |
| 412                             | 2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI, KARNATAKA    | 02/2018                       | 486.78<br>-                         | -<br>-                             | -               |
| 413                             | 6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI, KERALA       | 02/2018                       | 1,424.77<br>-                       | -<br>-                             | -               |
| 414                             | FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI, TAMIL NADU                         | 02/2018                       | 1,166.26<br>-                       | -<br>-                             | -               |
| 415                             | FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI, UTTAR PRADESH | 02/2018                       | 670.50<br>-                         | -<br>-                             | -               |
| 416                             | SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI, KARNATAKA    | 02/2018                       | 1,995.34<br>-                       | -<br>-                             | -               |
| 417                             | SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI, KARNATAKA     | 02/2018                       | 2,177.80<br>-                       | -<br>-                             | -               |
| 418                             | REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL  | 03/2018                       | 1,261.98<br>-                       | -<br>-                             | -               |



## Details of Projects Without Date of Commissioning

| Costing Rs. 150 Crore and above |                                                                                                                                          |                               |                                     |                                    | (December 2018) |
|---------------------------------|------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-----------------|
|                                 |                                                                                                                                          |                               |                                     | Date of Commissioning (Month/Year) |                 |
| Sl.No                           | Project                                                                                                                                  | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated     |
| 1                               | 2                                                                                                                                        | 3                             | 4                                   | 5                                  | 6               |
| 419                             | FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB                  | 02/2018                       | 261.76<br>-                         | -<br>-                             | -               |
| 420                             | FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH                                     | 03/2018                       | 809.07<br>-                         | -<br>-                             | -               |
| 421                             | FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH                                 | 03/2018                       | 925.40<br>-                         | -<br>-                             | -               |
| 422                             | UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN         | 02/2018                       | 1,103.88<br>-                       | -<br>-                             | -               |
| 423                             | CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN         | 02/2018                       | 741.86<br>-                         | -<br>-                             | -               |
| 424                             | CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH     | 03/2018                       | 1,117.84<br>-                       | -<br>-                             | -               |
| 425                             | CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN          | 02/2018                       | 716.76<br>-                         | -<br>-                             | -               |
| 426                             | SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH     | 03/2018                       | 2,140.93<br>-                       | -<br>-                             | -               |
| 427                             | SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH    | 02/2018                       | 1,959.00<br>-                       | -<br>-                             | -               |
| 428                             | 4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH     | 03/2018                       | 1,120.57<br>-                       | -<br>-                             | -               |
| 429                             | SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT            | 02/2018                       | 1,052.21<br>-                       | -<br>-                             | -               |
| 430                             | REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH     | 03/2018                       | 1,025.80<br>-                       | -<br>-                             | -               |
| 431                             | REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH     | 03/2018                       | 1,115.28<br>-                       | -<br>-                             | -               |
| 432                             | FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA         | 03/2018                       | 802.65<br>-                         | -<br>-                             | -               |
| 433                             | CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH     | 02/2018                       | 972.77<br>-                         | -<br>-                             | -               |
| 434                             | FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH | 03/2018                       | 392.60<br>-                         | -<br>-                             | -               |
| 435                             | SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH    | 03/2018                       | 1,550.98<br>-                       | -<br>-                             | -               |
| 436                             | REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH    | 03/2018                       | 565.09<br>-                         | -<br>-                             | -               |



## Details of Projects Without Date of Commissioning

| Costing Rs. 150 Crore and above |                                                                                                                                       |                               |                                     |                                    | (December 2018) |
|---------------------------------|---------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-----------------|
|                                 |                                                                                                                                       |                               |                                     | Date of Commissioning (Month/Year) |                 |
| Sl.No                           | Project                                                                                                                               | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated     |
| 1                               | 2                                                                                                                                     | 3                             | 4                                   | 5                                  | 6               |
| 437                             | CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH | 03/2018                       | 314.43<br>-                         | -<br>-                             | -               |
| 438                             | CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH | 03/2018                       | 557.30<br>-                         | -<br>-                             | -               |
| 439                             | DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR          | 03/2018                       | 496.20<br>-                         | -<br>-                             | -               |
| 440                             | 4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH     | 03/2018                       | 1,029.96<br>-                       | -<br>-                             | -               |
| 441                             | CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT        | 03/2018                       | 2,702.05<br>-                       | -<br>-                             | -               |
| 442                             | FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA       | 03/2018                       | 950.63<br>-                         | -<br>-                             | -               |
| 443                             | FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA      | 03/2018                       | 857.62<br>-                         | -<br>-                             | -               |
| 444                             | FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA      | 03/2018                       | 828.29<br>-                         | -<br>-                             | -               |
| 445                             | FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU      | 03/2018                       | 505.35<br>-                         | -<br>-                             | -               |
| 446                             | FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827]NHAI,TAMIL NADU     | 03/2018                       | 628.71<br>-                         | -<br>-                             | -               |
| 447                             | TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU     | 03/2018                       | 633.55<br>-                         | -<br>-                             | -               |
| 448                             | FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU      | 03/2018                       | 1,016.92<br>-                       | -<br>-                             | -               |
| 449                             | FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU     | 03/2018                       | 2,065.96<br>-                       | -<br>-                             | -               |
| 450                             | FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE    | 03/2018                       | 1,294.47<br>-                       | -<br>-                             | -               |
| 451                             | FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE    | 03/2018                       | 998.70<br>-                         | -<br>-                             | -               |
| 452                             | CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT        | 03/2018                       | 1,437.64<br>-                       | -<br>-                             | -               |
| 453                             | CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT         | 03/2018                       | 1,161.39<br>-                       | -<br>-                             | -               |

## Details of Projects Without Date of Commissioning

| Costing Rs. 150 Crore and above |                                                                                                                                         |                               |                                     |                                    | (December 2018) |
|---------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-----------------|
|                                 |                                                                                                                                         |                               |                                     | Date of Commissioning (Month/Year) |                 |
| Sl.No                           | Project                                                                                                                                 | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated     |
| 1                               | 2                                                                                                                                       | 3                             | 4                                   | 5                                  | 6               |
| 454                             | CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA          | 03/2018                       | 1,484.30<br>-                       | -<br>-                             | -               |
| 455                             | REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA          | 03/2018                       | 275.12<br>-                         | -<br>-                             | -               |
| 456                             | REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTING - [N24000837]NHAI,HARYANA       | 03/2018                       | 307.79<br>-                         | -<br>-                             | -               |
| 457                             | UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN         | 03/2018                       | 874.25<br>-                         | -<br>-                             | -               |
| 458                             | SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA          | 03/2018                       | 634.70<br>-                         | -<br>-                             | -               |
| 459                             | CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN         | 03/2018                       | 1,158.35<br>-                       | -<br>-                             | -               |
| 460                             | SIX LANING & STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA           | 03/2018                       | 795.50<br>-                         | -<br>-                             | -               |
| 461                             | REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB           | 03/2018                       | 199.90<br>-                         | -<br>-                             | -               |
| 462                             | SIX LANING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA                           | 03/2018                       | 806.11<br>-                         | -<br>-                             | -               |
| 463                             | REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA          | 03/2018                       | 198.05<br>-                         | -<br>-                             | -               |
| 464                             | CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA                                               | 03/2018                       | 291.53<br>-                         | -<br>-                             | -               |
| 465                             | REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA          | 03/2018                       | 181.78<br>-                         | -<br>-                             | -               |
| 466                             | CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA                                                | 03/2018                       | 289.21<br>-                         | -<br>-                             | -               |
| 467                             | REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION & STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA          | 03/2018                       | 551.58<br>-                         | -<br>-                             | -               |
| 468                             | CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA     | 03/2018                       | 1,162.92<br>-                       | -<br>-                             | -               |
| 469                             | FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH | 03/2018                       | 478.74<br>-                         | -<br>-                             | -               |
| 470                             | FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA      | 03/2018                       | 642.13<br>-                         | -<br>-                             | -               |
| 471                             | 4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND        | 03/2018                       | 1,005.08<br>-                       | -<br>-                             | -               |

## Details of Projects Without Date of Commissioning

| Costing Rs. 150 Crore and above |                                                                                                                                |                               |                                     |                                    | (December 2018) |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-----------------|
|                                 |                                                                                                                                |                               |                                     | Date of Commissioning (Month/Year) |                 |
| Sl.No                           | Project                                                                                                                        | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated     |
| 1                               | 2                                                                                                                              | 3                             | 4                                   | 5                                  | 6               |
|                                 | <u>National Highways Development Project</u>                                                                                   |                               |                                     |                                    |                 |
| 472                             | REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA                                   | 06/2014                       | 260.39<br>-                         | 11/2016<br>-                       | -               |
| 473                             | FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA                          | 03/2015                       | 297.00<br>-                         | 04/2018<br>-                       | -               |
| 474                             | CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA     | 03/2015                       | 168.30<br>-                         | -<br>-                             | -               |
| 475                             | REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA                             | 01/2014                       | 446.77<br>-                         | -<br>-                             | -               |
| 476                             | REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA                            | 12/2013                       | 220.72<br>-                         | 11/2016<br>-                       | -               |
| 477                             | KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH                               | 02/2015                       | 377.83<br>-                         | 07/2017<br>-                       | -               |
| 478                             | RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH              | 10/2013                       | 445.89<br>-                         | 03/2017<br>-                       | -               |
| 479                             | BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH                        | 01/2014                       | 397.04<br>-                         | 10/2016<br>-                       | -               |
| 480                             | BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH                | 06/2015                       | 390.51<br>-                         | -<br>-                             | -               |
| 481                             | BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH                                                 | 03/2013                       | 257.80<br>-                         | 02/2016<br>-                       | -               |
| 482                             | INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH             | 11/2013                       | 497.05<br>-                         | 05/2017<br>-                       | -               |
| 483                             | ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH                                    | 06/2015                       | 774.57<br>-                         | 03/2018<br>-                       | -               |
| 484                             | SHAHDL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH | 06/2015                       | 532.49<br>-                         | 05/2017<br>-                       | -               |
| 485                             | BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH                                                         | 08/2015                       | 257.80<br>-                         | -<br>-                             | -               |
| 486                             | BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH    | 10/2013                       | 317.76<br>-                         | 03/2017<br>-                       | -               |
| 487                             | JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH    | 10/2013                       | 283.45<br>-                         | 10/2016<br>-                       | -               |
| 488                             | MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH               | 06/2015                       | 641.02<br>-                         | 12/2017<br>-                       | -               |
| 489                             | MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH                                              | 01/2012                       | 381.86<br>-                         | 04/2015<br>-                       | -               |
| 490                             | SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH                         | 10/2013                       | 493.94<br>-                         | 03/2017<br>-                       | -               |
| 491                             | BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH                                                    | 11/2011                       | 670.82<br>-                         | 02/2015<br>-                       | -               |

## Details of Projects Without Date of Commissioning

| Costing Rs. 150 Crore and above |                                                                                                                                      |                               |                                     |                                    | (December 2018) |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-----------------|
|                                 |                                                                                                                                      |                               |                                     | Date of Commissioning (Month/Year) |                 |
| Sl.No                           | Project                                                                                                                              | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated     |
| 1                               | 2                                                                                                                                    | 3                             | 4                                   | 5                                  | 6               |
| 492                             | JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH           | 02/2015                       | 327.32<br>-                         | 05/2017<br>-                       | -               |
| 493                             | JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH                      | 11/2015                       | 628.45<br>-                         | 03/2018<br>-                       | -               |
| 494                             | GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH                                  | 12/2015                       | 927.54<br>-                         | 06/2018<br>-                       | -               |
|                                 | <u>Public Works Dept Of State</u>                                                                                                    |                               |                                     |                                    |                 |
| 495                             | REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA       | 12/2013                       | 177.18<br>-                         | 03/2016<br>-                       | -               |
| 496                             | REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPPLY SECTIO - [N24000242]PWD,TELANGANA      | 12/2013                       | 158.65<br>-                         | 03/2016<br>-                       | -               |
| 497                             | YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH - 222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA        | 12/2013                       | 244.08<br>-                         | 03/2016<br>-                       | -               |
| 498                             | REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA       | 01/2014                       | 340.00<br>-                         | 03/2016<br>-                       | -               |
| 499                             | REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA      | 01/2014                       | 270.00<br>-                         | 03/2016<br>-                       | -               |
| 500                             | REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA      | 10/2014                       | 244.30<br>-                         | 12/2016<br>-                       | -               |
| 501                             | REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA       | 10/2014                       | 295.47<br>-                         | 02/2017<br>-                       | -               |
| 502                             | EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA      | 03/2015                       | 153.21<br>-                         | 01/2017<br>-                       | -               |
| 503                             | CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA      | 03/2011                       | 218.31<br>-                         | 12/2015<br>-                       | -               |
| 504                             | CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA    | 08/2014                       | 187.79<br>-                         | 07/2016<br>-                       | -               |
| 505                             | CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA         | 01/2014                       | 255.75<br>348.00                    | 09/2017<br>-                       | -               |
| 506                             | CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA         | 01/2014                       | 267.16<br>352.00                    | 11/2017<br>-                       | -               |
| 507                             | REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH      | 02/2015                       | 241.61<br>-                         | 02/2017<br>-                       | -               |
| 508                             | REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH | 11/2014                       | 297.78<br>330.00                    | 02/2017<br>-                       | -               |

## Details of Projects Without Date of Commissioning

| Costing Rs. 150 Crore and above |                                                                                                                                      |                               |                                     |                                    | (December 2018) |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-----------------|
|                                 |                                                                                                                                      |                               |                                     | Date of Commissioning (Month/Year) |                 |
| Sl.No                           | Project                                                                                                                              | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated     |
| 1                               | 2                                                                                                                                    | 3                             | 4                                   | 5                                  | 6               |
| 509                             | REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH  | 01/2014                       | 361.30<br>-                         | 07/2014<br>-                       | -               |
| 510                             | REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH | 02/2014                       | 258.99<br>-                         | 07/2014<br>-                       | -               |
| 511                             | REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH | 07/2014                       | 251.55<br>-                         | 02/2015<br>-                       | -               |
| 512                             | REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH | 03/2015                       | 175.03<br>-                         | -<br>-                             | -               |
| 513                             | REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH | 02/2015                       | 266.00<br>-                         | -<br>-                             | -               |
| 514                             | FOUR LANING OF 5.122 KM OF NH9 ( NEW NH 65) FROM KM 269.900 ( DESIGN CH0.0 ) TO KM 275-622( DESIGN C - [N24000274]PWD,ANDHRA PRADESH | 07/2015                       | 333.21<br>333.21                    | 12/2015<br>-                       | -               |
| 515                             | REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH             | 10/2014                       | 213.47<br>-                         | 03/2015<br>-                       | -               |
| 516                             | REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 ( BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH           | 10/2014                       | 298.34<br>-                         | 03/2015<br>-                       | -               |
| 517                             | REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH    | 11/2014                       | 262.54<br>-                         | 03/2015<br>-                       | -               |
| 518                             | REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH           | 12/2015                       | 291.05<br>-                         | -<br>-                             | -               |
| 519                             | REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH  | 01/2014                       | 195.45<br>-                         | 11/2014<br>-                       | -               |
| 520                             | CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH    | 12/2010                       | 169.26<br>-                         | 12/2012<br>-                       | -               |
| 521                             | REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH    | 02/2014                       | 170.21<br>-                         | 11/2014<br>-                       | -               |
| 522                             | REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH            | 12/2014                       | 394.20<br>-                         | -<br>-                             | -               |
| 523                             | REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH     | 11/2015                       | 485.44<br>-                         | 12/2015<br>-                       | -               |
| 524                             | REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB         | 03/2015                       | 435.90<br>-                         | -<br>-                             | -               |
| 525                             | WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB         | 01/2015                       | 279.68<br>-                         | -<br>-                             | -               |

## Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December  
2018)

|       |                                                                                                                                         |                               |                                     | Date of Commissioning (Month/Year) |             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
| Sl.No | Project                                                                                                                                 | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1     | 2                                                                                                                                       | 3                             | 4                                   | 5                                  | 6           |
| 526   | 4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB             | 11/2014                       | 463.65<br>546.00                    | -<br>-                             | -           |
| 527   | 4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB             | 11/2014                       | 573.96<br>605.00                    | -<br>-                             | -           |
| 528   | REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH                          | 02/2015                       | 224.83<br>-                         | 05/2015<br>-                       | -           |
| 529   | REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOU - [N24000300]PWD,ANDHRA PRADESH    | 03/2015                       | 309.01<br>-                         | 09/2015<br>-                       | -           |
| 530   | REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH    | 03/2015                       | 271.45<br>-                         | 10/2015<br>-                       | -           |
| 531   | FOUR LANING OF 5.122 KM OF NH9( NEW NH 65) FROM KM 269.900( DESIGN CH0.0 ) - [N24000302]PWD,ANDHRA PRADESH                              | 07/2015                       | 333.21<br>-                         | 12/2015<br>-                       | -           |
| 532   | REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH    | 02/2014                       | 417.61<br>-                         | 06/2014<br>-                       | -           |
| 533   | WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM            | 11/2010                       | 624.41<br>-                         | 03/2011<br>-                       | -           |
| 534   | TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH | 12/2011                       | 156.63<br>276.00                    | 02/2012<br>-                       | -           |
| 535   | CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM            | 08/2010                       | 193.69<br>-                         | 10/2010<br>-                       | -           |
| 536   | TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH | 11/2010                       | 305.49<br>-                         | 03/2011<br>-                       | -           |
| 537   | TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH  | 03/2012                       | 207.03<br>-                         | 05/2012<br>-                       | -           |
| 538   | CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM                                                 | 04/2013                       | 151.59<br>-                         | 08/2013<br>-                       | -           |
| 539   | CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM                                              | 04/2013                       | 166.27<br>-                         | 08/2013<br>-                       | -           |
| 540   | CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM                                                 | 01/2013                       | 182.28<br>-                         | 02/2013<br>-                       | -           |
| 541   | WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND          | 12/2010                       | 1,296.00<br>-                       | 02/2011<br>-                       | -           |
| 542   | 4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB             | 02/2015                       | 483.38<br>-                         | -<br>-                             | -           |
| 543   | 4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB             | 02/2015                       | 616.36<br>-                         | -<br>-                             | -           |
| 544   | 2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH      | 11/2010                       | 305.49<br>-                         | 03/2017<br>-                       | -           |

## Details of Projects Without Date of Commissioning

| Costing Rs. 150 Crore and above |                                                                                                                                        |                               |                                     |                                    | (December 2018) |
|---------------------------------|----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-----------------|
|                                 |                                                                                                                                        |                               |                                     | Date of Commissioning (Month/Year) |                 |
| Sl.No                           | Project                                                                                                                                | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated     |
| 1                               | 2                                                                                                                                      | 3                             | 4                                   | 5                                  | 6               |
| 545                             | 4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64( - [N24000374]PWD,PUNJAB           | 02/2015                       | 486.74<br>-                         | -<br>-                             | -               |
| 546                             | SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH                                                                 | 01/2012                       | 320.48<br>-                         | 08/2015<br>-                       | -               |
| 547                             | CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15( - [N24000383]PWD,PUNJAB           | 03/2015                       | 312.79<br>-                         | -<br>-                             | -               |
| 548                             | CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOLA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB            | 07/2014                       | 319.80<br>-                         | -<br>-                             | -               |
| 549                             | DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB           | 12/2015                       | 766.36<br>-                         | -<br>-                             | -               |
| 550                             | FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH | 01/2011                       | 264.16<br>-                         | -<br>-                             | -               |
| 551                             | 4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB                                            | 11/2015                       | 847.02<br>-                         | -<br>-                             | -               |
| 552                             | 2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA           | 12/2010                       | 1,494.48<br>-                       | 02/2011<br>-                       | -               |
| 553                             | 4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB                                           | 11/2015                       | 889.24<br>-                         | -<br>-                             | -               |
| 554                             | 2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM                          | 11/2010                       | 268.08<br>-                         | 05/2017<br>-                       | -               |
| 555                             | 2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM              | 11/2010                       | 470.20<br>-                         | 02/2011<br>-                       | -               |
| 556                             | SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH                                                        | 11/2011                       | 871.15<br>-                         | 09/2015<br>-                       | -               |
| 557                             | DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB            | 12/2015                       | 578.38<br>-                         | -<br>-                             | -               |
| 558                             | WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE      | 03/2015                       | 789.83<br>-                         | -<br>-                             | -               |
| 559                             | FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH   | 10/2015                       | 333.21<br>-                         | 11/2015<br>-                       | -               |
| 560                             | STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM            | 05/2011                       | 176.22<br>-                         | 02/2018<br>-                       | -               |
| 561                             | STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM             | 11/2014                       | 218.31<br>-                         | 02/2018<br>-                       | -               |
| 562                             | IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA                                                                                | 12/2013                       | 319.80<br>-                         | 10/2016<br>-                       | -               |
| 563                             | CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM                                   | 08/2010                       | 195.04<br>-                         | 10/2010<br>-                       | -               |



## Details of Projects Without Date of Commissioning

| Costing Rs. 150 Crore and above |                                                                                                                                         |                               |                                     |                                    | (December 2018) |
|---------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-----------------|
|                                 |                                                                                                                                         |                               |                                     | Date of Commissioning (Month/Year) |                 |
| Sl.No                           | Project                                                                                                                                 | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated     |
| 1                               | 2                                                                                                                                       | 3                             | 4                                   | 5                                  | 6               |
| 564                             | REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH                                                     | 02/2015                       | 224.83<br>-                         | 04/2015<br>-                       | -               |
| 565                             | REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA            | 07/2014                       | 342.05<br>-                         | 01/2017<br>-                       | -               |
| 566                             | TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH | 12/2009                       | 165.00<br>-                         | 09/2010<br>-                       | -               |
| 567                             | TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH | 12/2009                       | 104.00<br>-                         | 09/2010<br>-                       | -               |
| 568                             | NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN         | 09/2012                       | 511.00<br>-                         | 10/2013<br>-                       | -               |
| 569                             | NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN                   | 09/2012                       | 511.00<br>-                         | 10/2013<br>-                       | -               |
| 570                             | UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH                                 | 03/2015                       | 511.83<br>-                         | 08/2017<br>-                       | -               |
| 571                             | WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA                | 12/2011                       | 159.39<br>-                         | 11/2017<br>-                       | -               |
| 572                             | WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB            | 06/2015                       | 892.17<br>-                         | -<br>-                             | -               |
| 573                             | WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB            | 06/2015                       | 899.21<br>-                         | -<br>-                             | -               |
| 574                             | WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA            | 12/2011                       | 191.08<br>-                         | 08/2015<br>-                       | -               |
| 575                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIK 40 - [N24000530]PWD,BIHAR               | 01/1991                       | 154.62<br>-                         | -<br>-                             | -               |
| 576                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR              | 01/1991                       | 319.68<br>-                         | -<br>-                             | -               |
| 577                             | REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA       | 01/2014                       | 292.98<br>-                         | 11/2014<br>-                       | -               |
| 578                             | 4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA                    | 03/2016                       | 1,142.62<br>-                       | -<br>-                             | -               |
| 579                             | 4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA                    | 03/2016                       | 1,101.58<br>-                       | -<br>-                             | -               |
|                                 | Total                                                                                                                                   |                               | 2,29,781.22<br>-                    |                                    |                 |
|                                 |                                                                                                                                         |                               |                                     |                                    |                 |
|                                 | SHIPPING AND PORTS                                                                                                                      |                               |                                     |                                    |                 |
|                                 | Kamarajar Port Limited                                                                                                                  |                               |                                     |                                    |                 |



## Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(December 2018)

|       |                                                                                                                              |                               |                                     | Date of Commissioning (Month/Year) |             |
|-------|------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
| Sl.No | Project                                                                                                                      | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1     | 2                                                                                                                            | 3                             | 4                                   | 5                                  | 6           |
| 580   | CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU                                           | 02/2015                       | 244.50<br>258.33                    | 12/2017<br>03/2018                 | -           |
|       | <u>Port Trust</u>                                                                                                            |                               |                                     |                                    |             |
| 581   | SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU                                                        | 06/2005                       | 2,427.40<br>-                       | 10/2008<br>-                       | -           |
|       | Total                                                                                                                        |                               | 2,671.90<br>-                       |                                    |             |
|       |                                                                                                                              |                               |                                     |                                    |             |
|       | <u>TELECOMMUNICATIONS</u>                                                                                                    |                               |                                     |                                    |             |
|       | <u>Indian Telephone Industry</u>                                                                                             |                               |                                     |                                    |             |
| 582   | NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE                           | 09/2014                       | 2,111.17<br>-                       | 09/2014<br>-                       | -           |
|       | <u>Mahanagar Telephone Nigam Limited</u>                                                                                     |                               |                                     |                                    |             |
| 583   | GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI                                                            | 06/2016                       | 418.26<br>-                         | 06/2017<br>-                       | -           |
|       | Total                                                                                                                        |                               | 2,529.43<br>-                       |                                    |             |
|       |                                                                                                                              |                               |                                     |                                    |             |
|       | <u>URBAN DEVELOPMENT</u>                                                                                                     |                               |                                     |                                    |             |
|       | <u>Central Public Works Department</u>                                                                                       |                               |                                     |                                    |             |
| 584   | CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD,PUNJAB                               | 01/2018                       | 430.00<br>-                         | 09/2018<br>-                       | 09/2018     |
| 585   | STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU                                                   | 04/2014                       | 332.72<br>-                         | 09/2016<br>-                       | -           |
| 586   | CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH                 | 06/2014                       | 157.84<br>-                         | 03/2017<br>-                       | -           |
| 587   | CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI   | 07/2012                       | 884.30<br>-                         | 12/2015<br>-                       | -           |
| 588   | CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU                                            | 11/2017                       | 348.77<br>-                         | -<br>-                             | -           |
| 589   | REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI                                                                 | 10/2016                       | 422.00<br>-                         | -<br>-                             | -           |
| 590   | REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI | 10/2016                       | 392.00<br>-                         | -<br>-                             | -           |
| 591   | SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI | 10/2016                       | 248.20<br>-                         | 04/2018<br>-                       | -           |
|       | <u>Chennai Metro Rail Ltd</u>                                                                                                |                               |                                     |                                    |             |
| 592   | CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU                                                                | 02/2009                       | 14,600.00<br>-                      | 12/2015<br>-                       | -           |
| 593   | CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU                                                            | 06/2016                       | 3,770.00<br>-                       | 03/2018<br>-                       | -           |
|       | <u>Hindustan Steelwork Construction Limited</u>                                                                              |                               |                                     |                                    |             |
| 594   | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA                                     | 03/2007                       | 149.73<br>173.00                    | 12/2015<br>-                       | -           |

## Details of Projects Without Date of Commissioning

| Costing Rs. 150 Crore and above                         |                                                                                                                                    |                               |                                     |                                    | (December 2018) |
|---------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-----------------|
|                                                         |                                                                                                                                    |                               |                                     | Date of Commissioning (Month/Year) |                 |
| Sl.No                                                   | Project                                                                                                                            | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated     |
| 1                                                       | 2                                                                                                                                  | 3                             | 4                                   | 5                                  | 6               |
| 595                                                     | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA                                          | 12/2007                       | 202.61<br>227.00                    | 12/2016<br>-                       | -               |
| 596                                                     | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA                                        | 10/2011                       | 175.49<br>206.71                    | 12/2016<br>-                       | -               |
| 597                                                     | CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA                                               | 05/2005                       | 768.88<br>1,070.97                  | 02/2014<br>-                       | -               |
| 598                                                     | CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA                                    | 07/2011                       | 324.87<br>324.87                    | 12/2015<br>-                       | -               |
| 599                                                     | CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH  | 07/2014                       | 232.00<br>-                         | -<br>-                             | -               |
| 600                                                     | CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT                                    | 01/2013                       | 175.00<br>-                         | -<br>-                             | -               |
| 601                                                     | CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN   | 05/2015                       | 189.00<br>-                         | 03/2017<br>-                       | -               |
| 602                                                     | CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND                           | 12/2007                       | 253.92<br>253.92                    | 06/2016<br>-                       | -               |
| 603                                                     | CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND            | 12/2007                       | 200.00<br>-                         | 03/2018<br>-                       | -               |
| 604                                                     | CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND                                                            | 04/2013                       | 170.00<br>-                         | 04/2018<br>-                       | -               |
| 605                                                     | CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL | 08/2012                       | 185.37<br>-                         | 03/2016<br>-                       | -               |
| <u>Jawahar Lal Nehru National Urban Renewal Mission</u> |                                                                                                                                    |                               |                                     |                                    |                 |
| 606                                                     | REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH | 08/2007                       | 246.90<br>-                         | -<br>-                             | -               |
| <u>National Building Construcion Corporation Ltd</u>    |                                                                                                                                    |                               |                                     |                                    |                 |
| 607                                                     | REDEVELOPMENT OF GPRA COLONY AT NAUJOJI NAGAR - [N28000105]NBCC,DELHI                                                              | 07/2016                       | 2,694.00<br>-                       | -<br>-                             | -               |
| Total                                                   |                                                                                                                                    |                               | 27,553.60<br>-                      |                                    |                 |
|                                                         |                                                                                                                                    |                               |                                     |                                    |                 |
| Grand Total                                             |                                                                                                                                    |                               | 4,19,884.45                         |                                    |                 |

## Details of Projects Without Original Date of Commissioning

### Annexure - IX

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                              |                               |                                    |                              |                                    |                                    |             |                                   |                            |
|-------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------------------|----------------------------|
|                                                 |                                                                                                                              |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                                   |                            |
| Sl.No                                           | Project                                                                                                                      | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
| 1                                               | 2                                                                                                                            | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                                 | 10                         |
|                                                 | <u>HEALTH AND FAMILY WELFARE</u>                                                                                             |                               |                                    |                              |                                    |                                    |             |                                   |                            |
|                                                 | <u>Hospital Services Consultancy Corporation</u>                                                                             |                               |                                    |                              |                                    |                                    |             |                                   |                            |
| 1                                               | HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH                                                        | 03/2018                       | 601.02                             | 601.02                       | 79.63                              | -                                  | 02/2020     | -                                 | 0/0                        |
| 2                                               | HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA                                                           | 03/2018                       | 582.99                             | 582.99                       | 57.09                              | -                                  | 02/2020     | -                                 | 0/0                        |
| 3                                               | HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL                                                          | 04/2018                       | 651.99                             | 651.99                       | 43.81                              | -                                  | 02/2020     | -                                 | 0/0                        |
| 4                                               | HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC, UTTAR PRADESH                                                | 03/2018                       | 268.84                             | 268.84                       | 66.44                              | -                                  | 04/2020     | -                                 | 0/0                        |
| 5                                               | SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC, GOA                                                                      | 01/2018                       | 249.01                             | 249.01                       | 38.72                              | -                                  | 05/2020     | -                                 | 0/0                        |
|                                                 | <u>Hospital Services Consultancy Corporation Ltd</u>                                                                         |                               |                                    |                              |                                    |                                    |             |                                   |                            |
| 6                                               | GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC, DELHI                                                                       | 12/2017                       | 156.56                             | 156.65                       | 49.34                              | -                                  | 02/2020     | -                                 | 0/0                        |
|                                                 | <b>Total</b>                                                                                                                 |                               | 2,510.41                           | 2,510.50                     | 335.03                             |                                    |             |                                   | 0/0                        |
|                                                 | <u>RAILWAYS</u>                                                                                                              |                               |                                    |                              |                                    |                                    |             |                                   |                            |
|                                                 | <u>East Central Railways</u>                                                                                                 |                               |                                    |                              |                                    |                                    |             |                                   |                            |
| 7                                               | RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR, BIHAR                                              | 04/1998                       | 180.82                             | 528.26                       | 462.75                             | -                                  | 12/2018     | -                                 | 0/0                        |
| 8                                               | KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND                                                           | 03/1999                       | 1,033.07                           | 3,020.94                     | -                                  | -                                  | 03/2021     | -                                 | 0/0                        |
| 9                                               | SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR, BIHAR                               | 04/2004                       | 372.14                             | 1,474.47                     | 338.44                             | -                                  | 03/2021     | -                                 | 0/0                        |
| 10                                              | FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR, BIHAR | 04/1991                       | 329.39                             | 566.41                       | 759.20                             | -                                  | 12/2021     | -                                 | 0/0                        |
| 11                                              | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR, BIHAR                                                                | 04/1997                       | 162.87                             | 589.15                       | 183.72                             | -                                  | 03/2022     | -                                 | 0/0                        |
| 12                                              | HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, BIHAR                                                               | 04/2003                       | 528.65                             | 2,066.77                     | 330.82                             | -                                  | 03/2023     | -                                 | 0/0                        |
| 13                                              | ARARIA-SUPAUL (NL) - [N22000177]ECR, BIHAR                                                                                   | 04/2008                       | 1,605.17                           | 1,605.17                     | .19                                | -                                  | 03/2023     | -                                 | 0/0                        |
|                                                 | <u>East Coast Railway</u>                                                                                                    |                               |                                    |                              |                                    |                                    |             |                                   |                            |
| 14                                              | SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR, BIHAR                                                                             | 04/1999                       | 325.00                             | 729.92                       | 253.10                             | -                                  | 03/2021     | -                                 | 0/0                        |

## Details of Projects Without Original Date of Commissioning

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                             |                               |                                    |                              |                                    |                                    |             |                                   |                            |
|-------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------------------|----------------------------|
|                                                 |                                                                                                                             |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                                   |                            |
| Sl.No                                           | Project                                                                                                                     | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
| 1                                               | 2                                                                                                                           | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                                 | 10                         |
| 15                                              | CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR                                                                            | 04/2006                       | 378.56 -                           | 2,614.36                     | 111.71                             | - -                                | 03/2022     | -                                 | 0/0                        |
|                                                 | <u>North Central Railway</u>                                                                                                |                               |                                    |                              |                                    |                                    |             |                                   |                            |
| 16                                              | DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE | 04/2010                       | 2,030.50 -                         | 2,030.50                     | 10.34                              | - -                                | 12/2022     | -                                 | 0/0                        |
|                                                 | <u>North East Frontier Railway</u>                                                                                          |                               |                                    |                              |                                    |                                    |             |                                   |                            |
| 17                                              | KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR                                                                       | 04/2008                       | 333.76 -                           | 360.00                       | 4.98                               | - -                                | 03/2020     | -                                 | 0/0                        |
| 18                                              | NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL                                                      | 04/2010                       | 221.42 -                           | 380.00                       | 101.10                             | - -                                | 03/2020     | -                                 | 0/0                        |
|                                                 | <u>Rail Vikas Nigam Ltd.</u>                                                                                                |                               |                                    |                              |                                    |                                    |             |                                   |                            |
| 19                                              | RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE                                                                           | 04/2007                       | 2,062.30 -                         | 2,062.20                     | 674.76                             | - -                                | 03/2022     | -                                 | 0/2                        |
|                                                 | <u>South Eastern Railway</u>                                                                                                |                               |                                    |                              |                                    |                                    |             |                                   |                            |
| 20                                              | MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND                                                          | 04/2012                       | 258.20 -                           | 365.00                       | 192.35                             | - 12/2018                          | 01/2020     | 13(R3)                            | 0/0                        |
| 21                                              | MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE                                                                      | 04/2008                       | 466.48 -                           | 1,000.00                     | .83                                | - 12/2024                          | 12/2024     | 0(R3)                             | 0/0                        |
| 22                                              | BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL                                                                          | 04/2010                       | 267.37 -                           | 620.00                       | 40.77                              | - 03/2025                          | 03/2025     | 0(R3)                             | 0/0                        |
| 23                                              | MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL                                                                    | 04/2011                       | 276.69 -                           | 426.00                       | -                                  | - 03/2030                          | 03/2030     | 0(R3)                             | 0/0                        |
|                                                 | <u>South Western Railway</u>                                                                                                |                               |                                    |                              |                                    |                                    |             |                                   |                            |
| 24                                              | MIRAJ-LONDA - [N22000327]SWR,MULTI STATE                                                                                    | 03/2015                       | 1,830.00 1,190.92                  | 1,190.92                     | 207.68                             | - 03/2021                          | 03/2021     | 0(R3)                             | 0/0                        |
| 25                                              | TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA                                                                  | 04/2011                       | 1,801.01 -                         | 1,801.01                     | 13.67                              | - 12/2023                          | 12/2023     | 0(R3)                             | 0/0                        |
| 26                                              | MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA                                                                  | 04/2007                       | 179.65 1,350.91                    | 1,350.91                     | 924.08                             | - -                                | 12/2023     | -                                 | 0/1                        |
| 27                                              | CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA                                               | 04/2013                       | 558.00 692.43                      | 692.43                       | -                                  | - 12/2023                          | 12/2023     | 0(R3)                             | 0/0                        |
| 28                                              | SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE                                                                  | 04/2013                       | 296.00 -                           | 466.65                       | -                                  | - 12/2023                          | 12/2023     | 0(R3)                             | 0/0                        |
| 29                                              | WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA                                                                             | 04/2011                       | 348.85 -                           | 348.85                       | .36                                | - 12/2023                          | 12/2023     | 0(R3)                             | 0/0                        |
| 30                                              | TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA                                                                        | 04/2011                       | 146.75 167.50                      | 167.50                       | .34                                | - 12/2023                          | 12/2023     | 0(R3)                             | 0/0                        |
| 31                                              | CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA                                                                    | 04/2013                       | 327.25 367.77                      | 367.77                       | .31                                | - 12/2023                          | 12/2023     | 0(R3)                             | 0/0                        |
| 32                                              | HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA                                                                             | 04/1997                       | 2,315.00 -                         | 2,135.00                     | 144.75                             | - 12/2024                          | 12/2024     | 0(R3)                             | 0/0                        |
|                                                 | <u>Southern Railway</u>                                                                                                     |                               |                                    |                              |                                    |                                    |             |                                   |                            |

## Details of Projects Without Original Date of Commissioning

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                                    |                               |                                    |                              |                                    |                                    |             |                                   |                            |
|-------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------------------|----------------------------|
|                                                 |                                                                                                                                    |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                                   |                            |
| Sl.No                                           | Project                                                                                                                            | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
| 1                                               | 2                                                                                                                                  | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                                 | 10                         |
| 33                                              | MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU                                                                                  | 04/2008                       | 164.41 -                           | 450.00                       | 83.15                              | - -                                | 03/2020     | -                                 | 0/0                        |
|                                                 | <u>Western Railway</u>                                                                                                             |                               |                                    |                              |                                    |                                    |             |                                   |                            |
| 34                                              | MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT                                                                         | 04/2011                       | 844.10 -                           | 844.10                       | 61.85                              | - 03/2022                          | 03/2023     | 12(R3)                            | 0/0                        |
|                                                 | Total                                                                                                                              |                               | 19,643.41 -                        | 30,254.29                    | 4,901.25                           |                                    |             |                                   | 0/3                        |
|                                                 |                                                                                                                                    |                               |                                    |                              |                                    |                                    |             |                                   |                            |
|                                                 | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                                 |                               |                                    |                              |                                    |                                    |             |                                   |                            |
|                                                 | <u>National Highways Authority Of India</u>                                                                                        |                               |                                    |                              |                                    |                                    |             |                                   |                            |
| 35                                              | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH                                              | 03/2015                       | 795.76 -                           | 795.76                       | 171.72                             | - -                                | 03/2019     | -                                 | 0/0                        |
| 36                                              | FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB                                                               | 09/2014                       | 479.00 -                           | 479.00                       | 453.09                             | - -                                | 03/2019     | -                                 | 0/0                        |
| 37                                              | FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH                                                               | 03/2015                       | 928.83 -                           | 928.83                       | 202.91                             | - -                                | 03/2019     | -                                 | 0/0                        |
| 38                                              | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH                                              | 03/2015                       | 810.22 -                           | 810.22                       | 121.57                             | - -                                | 03/2019     | -                                 | 0/0                        |
| 39                                              | SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL                                                                    | 04/2014                       | 1,665.00 -                         | 1,665.00                     | 1,836.44                           | - -                                | 03/2019     | -                                 | 0/0                        |
| 40                                              | TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN                                        | 08/2015                       | 275.90 -                           | 275.90                       | 256.10                             | - -                                | 03/2019     | -                                 | 0/0                        |
| 41                                              | TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI,BIHAR                                                                  | 08/2015                       | 854.80 -                           | 854.80                       | 551.98                             | - -                                | 03/2019     | -                                 | 0/0                        |
| 42                                              | SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT     | 05/2016                       | 425.60 -                           | 425.60                       | -                                  | - -                                | 03/2019     | -                                 | 0/0                        |
| 43                                              | 4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA                                                      | 06/2015                       | 845.24 -                           | 845.24                       | 127.87                             | - -                                | 04/2019     | -                                 | 0/0                        |
| 44                                              | IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB          | 09/2015                       | 273.06 -                           | 273.06                       | 28.90                              | - -                                | 04/2019     | -                                 | 0/0                        |
| 45                                              | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH                                               | 03/2015                       | 794.30 -                           | 794.30                       | 152.81                             | - -                                | 05/2019     | -                                 | 0/0                        |
| 46                                              | SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA | 11/2016                       | 290.73 -                           | 290.73                       | 57.93                              | - -                                | 05/2019     | -                                 | 0/0                        |
| 47                                              | JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA                                                                   | 02/2016                       | 1,069.65 -                         | 1,069.65                     | -                                  | - -                                | 06/2019     | -                                 | 0/0                        |

## Details of Projects Without Original Date of Commissioning

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                                 |                               |                                    |                              |                                    |                                    |             |                                   |                            |
|-------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------------------|----------------------------|
|                                                 |                                                                                                                                 |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                                   |                            |
| Sl.No                                           | Project                                                                                                                         | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
| 1                                               | 2                                                                                                                               | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                                 | 10                         |
| 48                                              | FOUR LANE OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT   | 05/2016                       | 998.18 -                           | 998.18                       | 199.22                             | - -                                | 08/2019     | -                                 | 0/0                        |
| 49                                              | FOUR LANE OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT   | 05/2016                       | 763.08 -                           | 763.08                       | 137.01                             | - -                                | 08/2019     | -                                 | 0/0                        |
| 50                                              | FOUR LANE OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT   | 05/2016                       | 723.64 -                           | 723.64                       | 211.88                             | - -                                | 09/2019     | -                                 | 0/0                        |
| 51                                              | 2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT                                                | 12/2016                       | 417.19 -                           | 417.19                       | 122.81                             | - -                                | 09/2019     | -                                 | 0/0                        |
| 52                                              | FOUR LANE OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI, UTTARAKHAND | 03/2016                       | 720.00 -                           | 720.00                       | 181.70                             | - -                                | 10/2019     | -                                 | 0/0                        |
| 53                                              | FOUR LANE OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT   | 05/2016                       | 834.64 -                           | 834.64                       | 137.94                             | - -                                | 10/2019     | -                                 | 0/0                        |
| 54                                              | FOUR LANE WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI, ODISHA                                                                 | 12/2015                       | 752.28 -                           | 752.28                       | -                                  | - -                                | 11/2019     | -                                 | 0/0                        |
| 55                                              | 4/2 LANE WITH PS DAUSA-LALSOT-KAUNTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN                                           | 07/2016                       | 688.70 -                           | 688.70                       | 470.78                             | - -                                | 11/2019     | -                                 | 0/0                        |
| 56                                              | FOUR LANE OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI, HIMACHAL PRADESH                       | 10/2016                       | 447.75 -                           | 447.75                       | 54.46                              | - -                                | 11/2019     | -                                 | 0/0                        |
| 57                                              | FOUR LANE OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR                                                    | 12/2015                       | 1,167.45 -                         | 1,167.45                     | 33.45                              | - -                                | 12/2019     | -                                 | 0/0                        |
| 58                                              | CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT                                                               | 05/2016                       | 364.56 -                           | 364.56                       | 24.94                              | - -                                | 12/2019     | -                                 | 0/0                        |
| 59                                              | TWO/FOUR LANE WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI, JHARKHAND   | 07/2016                       | 458.03 -                           | 458.03                       | 20.00                              | - -                                | 12/2019     | -                                 | 0/0                        |
| 60                                              | SIX LANE OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI, RAJASTHAN  | 09/2016                       | 1,100.19 -                         | 1,100.19                     | 650.00                             | - -                                | 12/2019     | -                                 | 0/0                        |
| 61                                              | CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL                                                                 | 10/2015                       | 361.15 -                           | 361.15                       | -                                  | - -                                | 01/2020     | -                                 | 0/0                        |
| 62                                              | FOUR LANE OF KOILWAR TO BHOJPUR - [N24000482]NHAI, BIHAR                                                                        | 08/2015                       | 814.04 -                           | 814.04                       | 261.47                             | - -                                | 01/2020     | -                                 | 0/0                        |
| 63                                              | 4-LANE OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT                          | 07/2016                       | 829.97 -                           | 829.97                       | 71.29                              | - -                                | 01/2020     | -                                 | 0/0                        |

## Details of Projects Without Original Date of Commissioning

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                                                         |                               |                                    |                              |                                    |                                    |             |                                   |                            |
|-------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------------------|----------------------------|
|                                                 |                                                                                                                                         |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                                   |                            |
| Sl.No                                           | Project                                                                                                                                 | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
| 1                                               | 2                                                                                                                                       | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                                 | 10                         |
| 64                                              | REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB           | 03/2018                       | 196.05<br>-                        | 196.05                       | 21.93                              | -<br>-                             | 01/2020     | -                                 | 0/0                        |
| 65                                              | 4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND       | 03/2016                       | 1,443.00<br>-                      | 1,443.00                     | 122.72                             | -<br>-                             | 02/2020     | -                                 | 0/0                        |
| 66                                              | 4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 ( - [N24000563]NHAI,UTTAR PRADESH     | 03/2016                       | 1,668.00<br>-                      | 1,668.00                     | 322.13                             | -<br>-                             | 02/2020     | -                                 | 0/0                        |
| 67                                              | SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE      | 09/2016                       | 1,244.10<br>-                      | 1,244.10                     | 85.00                              | -<br>-                             | 02/2020     | -                                 | 0/0                        |
| 68                                              | 4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA                                                                              | 07/2015                       | 1,282.94<br>-                      | 1,282.94                     | -                                  | -<br>-                             | 04/2020     | -                                 | 0/0                        |
| 69                                              | 4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH                                | 03/2016                       | 1,737.00<br>-                      | 1,737.00                     | 50.71                              | -<br>-                             | 04/2020     | -                                 | 0/0                        |
| 70                                              | 4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB                                                                             | 08/2016                       | 1,169.61<br>-                      | 1,169.61                     | 234.38                             | -<br>-                             | 04/2020     | -                                 | 0/0                        |
| 71                                              | SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 ( - [N24000621]NHAI,RAJASTHAN        | 09/2016                       | 1,239.82<br>-                      | 1,239.82                     | 668.12                             | -<br>-                             | 05/2020     | -                                 | 0/0                        |
| 72                                              | DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH      | 12/2017                       | 1,232.21<br>-                      | 1,232.21                     | 637.48                             | -<br>-                             | 05/2020     | -                                 | 0/0                        |
| 73                                              | 4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH           | 03/2016                       | 1,408.00<br>-                      | 1,408.00                     | -                                  | -<br>-                             | 07/2020     | -                                 | 0/0                        |
| 74                                              | FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH | 09/2016                       | 1,273.71<br>-                      | 1,273.71                     | -                                  | -<br>-                             | 07/2020     | -                                 | 0/0                        |
| 75                                              | REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA           | 10/2016                       | 1,008.96<br>-                      | 1,008.96                     | 32.50                              | -<br>-                             | 07/2020     | -                                 | 0/0                        |
| 76                                              | 6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASTHAN(PACKAGE - - [N24000636]NHAI,RAJASTHAN        | 12/2016                       | 1,031.95<br>-                      | 1,031.95                     | 367.00                             | -<br>-                             | 08/2020     | -                                 | 0/0                        |
| 77                                              | FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH   | 01/2018                       | 960.24<br>-                        | 960.24                       | -                                  | -<br>-                             | 08/2020     | -                                 | 0/0                        |

### Details of Projects Without Original Date of Commissioning

| Costing Rs. 150 Crore and above (December 2018) |                                                                                                      |                               |                                    |                              |                                    |                                    |             |                                   |                            |
|-------------------------------------------------|------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------------------|----------------------------|
|                                                 |                                                                                                      |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                                   |                            |
| Sl.No                                           | Project                                                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
| 1                                               | 2                                                                                                    | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                                 | 10                         |
| 78                                              | TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH | 08/2016                       | 1,583.18<br>-                      | 1,583.18                     | -                                  | -<br>-                             | 09/2020     | -                                 | 0/0                        |
| 79                                              | FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR                                              | 01/1991                       | 642.41<br>-                        | 642.41                       | 9.45                               | -<br>-                             | 10/2020     | -                                 | 0/0                        |
|                                                 | Total                                                                                                |                               | 40,070.12<br>-                     | 40,070.12                    | 9,089.69                           |                                    |             |                                   | 0/0                        |
|                                                 |                                                                                                      |                               |                                    |                              |                                    |                                    |             |                                   |                            |
|                                                 | Grand Total                                                                                          |                               | 62,223.94                          | 72,834.91                    | 14,325.97                          |                                    |             |                                   | 0/3                        |



## Details of Projects Without Milestones w.r.t. Original Schedule

**Annexure - X**

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                       |                               |                                    |                                    |         |                            |
|-------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|---------|----------------------------|
| Sl.No                                           | Project                                                                                                               | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |         | Milestones Achieved/ Total |
| 1                                               | 2                                                                                                                     | 3                             | 4                                  | 5                                  | 6       | 7                          |
|                                                 | <u>CIVIL AVIATION</u>                                                                                                 |                               |                                    |                                    |         |                            |
|                                                 | <u>Airport Authority Of India Limited</u>                                                                             |                               |                                    |                                    |         |                            |
| 1                                               | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS             | 10/2013                       | 314.61 -                           | 09/2018 -                          | 06/2020 | 0/0                        |
|                                                 | <u>COAL</u>                                                                                                           |                               |                                    |                                    |         |                            |
|                                                 | <u>Mahanadi Coal Fields Limited</u>                                                                                   |                               |                                    |                                    |         |                            |
| 2                                               | INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]MCL,ODISHA                                                      | 05/2018                       | 2,434.75 -                         | 03/2027 -                          | 03/2027 | 0/0                        |
|                                                 | <u>Neyveli Lignite Corporation</u>                                                                                    |                               |                                    |                                    |         |                            |
| 3                                               | HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN                                                      | 03/2015                       | 522.45 -                           | 09/2019 -                          | 09/2019 | 0/0                        |
| 4                                               | BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN                                                   | 03/2015                       | 513.63 -                           | 12/2019 -                          | 12/2019 | 0/0                        |
| 5                                               | NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH                                    | 07/2016                       | 17,237.00 -                        | 11/2021 -                          | 11/2021 | 0/0                        |
|                                                 | <u>South-Eastern Coal Fields Limited</u>                                                                              |                               |                                    |                                    |         |                            |
| 6                                               | MAHAMAYA OPENCAST PROJECT - [N06000164]SECL,CHHATISGARH                                                               | 05/2018                       | 410.26 -                           | 03/2026 -                          | 03/2026 | 0/0                        |
| 7                                               | JHIRIA WEST OPENCAST PROJECT - [N06000166]SECL,CHHATISGARH                                                            | 11/2018                       | 389.97 -                           | 03/2026 -                          | 03/2026 | 0/0                        |
|                                                 | <u>Western Coal Fields Limited</u>                                                                                    |                               |                                    |                                    |         |                            |
| 8                                               | KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA                                                                | 03/2017                       | 362.73 -                           | 03/2020 -                          | 03/2020 | 0/0                        |
| 9                                               | COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH                                               | 07/2016                       | 409.87 -                           | 03/2022 -                          | 03/2022 | 0/0                        |
|                                                 | <u>STEEL</u>                                                                                                          |                               |                                    |                                    |         |                            |
|                                                 | <u>Steel Authority Of India Limited (Sail)</u>                                                                        |                               |                                    |                                    |         |                            |
| 10                                              | EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND | 02/2014                       | 4,749.00 -                         | 09/2017 -                          | -       | 0/0                        |
|                                                 | <u>PETROLEUM</u>                                                                                                      |                               |                                    |                                    |         |                            |
|                                                 | <u>Bharat Petroleum Corporation Limited</u>                                                                           |                               |                                    |                                    |         |                            |
| 11                                              | KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA                                                             | 12/2015                       | 1,112.00 -                         | 06/2019 -                          | 06/2019 | 0/0                        |
| 12                                              | MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA                                                         | 04/2013                       | 449.58 -                           | 12/2019 -                          | 12/2019 | 0/0                        |
| 13                                              | IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU                                                          | 11/2012                       | 678.00 -                           | 02/2017 -                          | -       | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                       |                               |                                    |                                    |         |                            |
|-------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|---------|----------------------------|
| SI.No                                           | Project                                                                                                                               | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |         | Milestones Achieved/ Total |
| 1                                               | 2                                                                                                                                     | 3                             | 4                                  | 5                                  | 6       | 7                          |
|                                                 | <u>Chennai Petroleum Corporation Limited</u>                                                                                          |                               |                                    |                                    |         |                            |
| 14                                              | BS-VI PROJECTS - [N16000295]CPCL, TAMIL NADU                                                                                          | 09/2017                       | 1,858.00<br>-                      | 12/2019<br>-                       | 12/2019 | 0/0                        |
| 15                                              | RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL, TAMIL NADU                                                                                | 08/2017                       | 421.00<br>-                        | 08/2020<br>-                       | 08/2020 | 0/0                        |
|                                                 | <u>Gas Authority Of India Limited</u>                                                                                                 |                               |                                    |                                    |         |                            |
| 16                                              | GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL, KARNATAKA                                                                       | 02/2015                       | 749.00<br>-                        | 02/2020<br>-                       | 02/2020 | 0/0                        |
| 17                                              | BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL, MULTI STATE                                                                              | 06/2018                       | 3,308.00<br>-                      | 12/2021<br>-                       | 12/2021 | 0/0                        |
| 18                                              | CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL, ODISHA                                                            | 07/2017                       | 243.53<br>243.53                   | 07/2022<br>-                       | 07/2022 | 0/0                        |
| 19                                              | CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]GAIL, ODISHA                                                                | 07/2017                       | 181.20<br>-                        | 07/2022<br>-                       | 07/2022 | 0/0                        |
| 20                                              | CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL, BIHAR                                                                    | 10/2017                       | 359.25<br>-                        | 10/2022<br>-                       | 10/2022 | 0/0                        |
| 21                                              | CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]GAIL, JHARKHAND                                                          | 10/2017                       | 221.45<br>-                        | 10/2022<br>-                       | 10/2022 | 0/0                        |
|                                                 | <u>Hindustan Petroleum Corporation Limited</u>                                                                                        |                               |                                    |                                    |         |                            |
| 22                                              | MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL, MAHARASHTRA                                                                      | 09/2015                       | 4,199.00<br>-                      | 03/2020<br>-                       | 07/2019 | 0/0                        |
| 23                                              | 180 TMTPA NEW LPG PLANT AT PATALGANGA (DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL, MAHARASHTRA                                       | 06/2017                       | 249.26<br>-                        | 06/2020<br>-                       | 06/2020 | 0/0                        |
| 24                                              | 120 TMTPA NEW LPG PLANT AT BARHI JHARKHAND STATE - [N16000316]HPCL, JHARKHAND                                                         | 06/2017                       | 161.50<br>-                        | 06/2020<br>-                       | 06/2020 | 0/0                        |
| 25                                              | CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR-CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL, CHHATTISGARH    | 12/2016                       | 300.00<br>-                        | 04/2021<br>-                       | 04/2021 | 0/0                        |
|                                                 | <u>Indian Oil Corporation Limited</u>                                                                                                 |                               |                                    |                                    |         |                            |
| 26                                              | CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL, HARYANA                                      | 04/2018                       | 206.63<br>-                        | 02/2020<br>-                       | 02/2020 | 0/0                        |
| 27                                              | CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL, GUJARAT               | 10/2017                       | 906.00<br>-                        | 02/2020<br>-                       | 02/2020 | 0/0                        |
| 28                                              | BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL, ASSAM                                                                           | 08/2018                       | 557.00<br>-                        | 02/2020<br>-                       | 02/2020 | 0/0                        |
| 29                                              | ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU                                                                      | 05/2013                       | 711.00<br>-                        | 06/2020<br>-                       | 06/2020 | 0/0                        |
| 30                                              | INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL, GUJARAT                    | 09/2016                       | 208.35<br>-                        | 07/2020<br>-                       | 07/2020 | 0/0                        |
| 31                                              | INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL, UTTAR PRADESH     | 08/2017                       | 255.40<br>-                        | 08/2020<br>-                       | 08/2020 | 0/0                        |
| 32                                              | NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL, HARYANA                                                               | 08/2018                       | 1,636.00<br>-                      | 08/2020<br>-                       | 08/2020 | 0/0                        |
| 33                                              | PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND - [N16000304]IOCL, MADHYA PRADESH | 08/2017                       | 236.00<br>-                        | 06/2020<br>-                       | 10/2020 | 0/0                        |
| 34                                              | DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL, BIHAR                    | 12/2017                       | 199.36<br>-                        | 10/2020<br>-                       | 10/2020 | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018)      |                                                                                                                                       |                               |                                    |                                    |             |                            |
|------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                                | Project                                                                                                                               | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                      |                                                                                                                                       |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                                    | 2                                                                                                                                     | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 35                                                   | HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL, WEST BENGAL                                                                        | 04/2016                       | 1,021.00<br>-                      | 12/2020<br>-                       | 12/2020     | 0/0                        |
| 36                                                   | ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL, MAHARASHTRA | 05/2016                       | 261.00<br>-                        | 01/2021<br>-                       | 01/2021     | 0/0                        |
| 37                                                   | INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL, BIHAR                                                            | 07/2018                       | 189.00<br>-                        | 01/2021<br>-                       | 01/2021     | 0/0                        |
| 38                                                   | ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL, ANDHRA PRADESH             | 01/2015                       | 342.00<br>-                        | 03/2021<br>-                       | 03/2021     | 0/0                        |
| 39                                                   | REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL, ANDHRA PRADESH                                                   | 07/2014                       | 247.00<br>-                        | 03/2021<br>-                       | 03/2021     | 0/0                        |
| 40                                                   | CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL, BIHAR                                                   | 04/2018                       | 522.00<br>-                        | 03/2021<br>-                       | 03/2021     | 0/0                        |
| 41                                                   | ADDITIONAL FACILITIES AT MANMAD FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL, MAHARASHTRA     | 05/2016                       | 212.00<br>-                        | 01/2021<br>-                       | 04/2021     | 0/0                        |
| 42                                                   | CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL, ANDHRA PRADESH                                                      | 08/2017                       | 384.58<br>-                        | 04/2021<br>-                       | 04/2021     | 0/0                        |
| 43                                                   | ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL, ODISHA                                                                          | 04/2018                       | 4,807.08<br>-                      | 07/2021<br>-                       | 07/2021     | 0/0                        |
| 44                                                   | CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL, ANDHRA PRADESH                            | 08/2018                       | 466.00<br>-                        | 04/2021<br>-                       | 07/2021     | 0/0                        |
| 45                                                   | CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL, TAMIL NADU                                                | 12/2017                       | 466.43<br>-                        | 10/2020<br>-                       | 08/2021     | 0/0                        |
| 46                                                   | ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL, MAHARASHTRA    | 05/2016                       | 348.00<br>-                        | 01/2021<br>-                       | 10/2021     | 0/0                        |
| 47                                                   | PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL, ODISHA                                                                          | 10/2018                       | 1,297.50<br>-                      | 10/2021<br>-                       | 10/2021     | 0/0                        |
| 48                                                   | REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL, UTTAR PRADESH                  | 08/2017                       | 318.80<br>-                        | 08/2021<br>-                       | 11/2021     | 0/0                        |
| 49                                                   | REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL, ANDHRA PRADESH                                                           | 04/2018                       | 355.00<br>-                        | 04/2022<br>-                       | 04/2022     | 0/0                        |
| 50                                                   | REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL, GUJARAT                                                                          | 10/2014                       | 279.00<br>-                        | 08/2018<br>-                       | -           | 0/0                        |
| <u>Indian Strategic Petroleum Reserves Ltd</u>       |                                                                                                                                       |                               |                                    |                                    |             |                            |
| 51                                                   | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR, KARNATAKA                                                             | 01/2006                       | 993.00<br>-                        | 01/2012<br>-                       | -           | 0/0                        |
| <u>Mangalore Refinery And Petrochemicals Limited</u> |                                                                                                                                       |                               |                                    |                                    |             |                            |
| 52                                                   | SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN, KARNATAKA                                                                  | 11/2017                       | 581.00<br>-                        | 03/2020<br>-                       | 03/2020     | 0/0                        |
| <u>Oil India Limited</u>                             |                                                                                                                                       |                               |                                    |                                    |             |                            |
| 53                                                   | CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL, ASSAM                                                            | 07/2011                       | 350.00<br>-                        | 01/2019<br>-                       | 09/2019     | 0/0                        |
| 54                                                   | 50MW WIND ENERGY POWER PROJECT - [N16000298]OIL, MULTI STATE                                                                          | 11/2015                       | 500.00<br>-                        | 06/2017<br>-                       | -           | 0/0                        |
| <u>POWER</u>                                         |                                                                                                                                       |                               |                                    |                                    |             |                            |
| <u>Chenab Valley Power Projects [P] Limited</u>      |                                                                                                                                       |                               |                                    |                                    |             |                            |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                      |                               |                                    |                    |             |                            |
|-------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|--------------------|-------------|----------------------------|
| SI.No                                           | Project                                                                                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Original / Revised | Anticipated | Milestones Achieved/ Total |
| 1                                               | 2                                                                                                                                    | 3                             | 4                                  | 5                  | 6           | 7                          |
| 55                                              | PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR<br><u>National Hydro-Electric Power Corporation</u> | 10/2014                       | 8,112.12<br>-                      | 04/2020<br>-       | 10/2023     | 0/0                        |
| 56                                              | SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH<br><u>National Thermal Power Corporation</u>             | 09/2003                       | 6,285.33<br>-                      | 09/2010<br>-       | -           | 0/0                        |
| 57                                              | PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND                                                                       | 10/2004                       | 4,237.96<br>4,238.00               | 10/2017<br>-       | 12/2016     | 0/0                        |
| 58                                              | TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH<br><u>Power Grid Corporation Of India Limited</u>                       | 09/2015                       | 3,004.00<br>-                      | 11/2019<br>-       | 11/2019     | 0/0                        |
| 59                                              | TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS-KARGIL-KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR       | 01/2014                       | 1,788.41<br>1,788.41               | 09/2017<br>09/2017 | 11/2018     | 0/0                        |
| 60                                              | 400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270]PGCIL,MULTI STATE                                              | 08/2008                       | 771.00<br>1,624.00                 | 02/2013<br>07/2018 | 12/2018     | 0/0                        |
| 61                                              | TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN                                               | 07/2015                       | 307.18<br>307.18                   | 11/2017<br>10/2018 | 01/2019     | 0/0                        |
| 62                                              | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH                                             | 01/2016                       | 305.04<br>305.04                   | 03/2017<br>09/2018 | 01/2019     | 0/0                        |
| 63                                              | EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE                                                                | 05/2016                       | 766.21<br>766.21                   | 11/2018<br>11/2018 | 02/2019     | 0/0                        |
| 64                                              | TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT                                    | 07/2016                       | 300.94<br>300.94                   | 12/2018<br>12/2018 | 02/2019     | 0/0                        |
| 65                                              | WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE                                                               | 07/2016                       | 150.99<br>150.99                   | 07/2018<br>07/2018 | 02/2019     | 0/0                        |
| 66                                              | PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL,MULTI STATE                                      | 08/2016                       | 431.89<br>431.89                   | 02/2019<br>02/2019 | 02/2019     | 0/0                        |
| 67                                              | ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE  | 02/2017                       | 322.30<br>322.30                   | 02/2019<br>02/2019 | 02/2019     | 0/0                        |
| 68                                              | UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE                                                   | 01/2014                       | 374.63<br>374.63                   | 04/2016<br>12/2017 | 03/2019     | 0/0                        |
| 69                                              | ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE  | 03/2015                       | 197.40<br>197.40                   | 03/2018<br>-       | 03/2019     | 0/0                        |
| 70                                              | TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN                                                  | 07/2016                       | 1,429.38<br>1,429.38               | 01/2019<br>01/2019 | 03/2019     | 0/0                        |
| 71                                              | POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL,MULTI STATE  | 07/2016                       | 333.17<br>333.17                   | 03/2019<br>03/2019 | 03/2019     | 0/0                        |
| 72                                              | SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE                                                              | 09/2016                       | 562.25<br>562.25                   | 03/2019<br>03/2019 | 03/2019     | 0/0                        |
| 73                                              | PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]PGCIL,MULTI STATE  | 03/2017                       | 162.31<br>162.31                   | 03/2019<br>03/2019 | 03/2019     | 0/0                        |
| 74                                              | WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL,MULTI STATE                                                              | 02/2017                       | 204.12<br>204.12                   | 09/2019<br>09/2019 | 03/2019     | 0/0                        |
| 75                                              | PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA              | 04/2016                       | 844.64<br>-                        | 04/2019<br>-       | 04/2019     | 0/0                        |
| 76                                              | SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE                 | 10/2016                       | 608.24<br>608.24                   | 04/2019<br>04/2019 | 04/2019     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                     |                               |                                    |                                    |             |                            |
|-------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                             | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                     |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                   | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 77                                              | STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE                                                 | 12/2015                       | 3,654.00<br>-                      | 04/2019<br>-                       | 04/2019     | 0/0                        |
| 78                                              | GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE                                      | 05/2016                       | 3,519.59<br>3,519.59               | 05/2019<br>05/2019                 | 05/2019     | 0/0                        |
| 79                                              | ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR                                                       | 04/2016                       | 790.13<br>790.30                   | 06/2019<br>06/2019                 | 06/2019     | 0/0                        |
| 80                                              | INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE           | 03/2017                       | 251.60<br>251.60                   | 06/2019<br>06/2019                 | 06/2019     | 0/0                        |
| 81                                              | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE    | 10/2016                       | 408.46<br>408.46                   | 01/2019<br>01/2019                 | 06/2019     | 0/0                        |
| 82                                              | EASTERN REGION STRENGTHENING SCHEME XVII( PART B) - [N18000244]PGCIL,MULTI STATE                                                    | 02/2017                       | 235.53<br>235.53                   | 06/2019<br>06/2019                 | 06/2019     | 0/0                        |
| 83                                              | SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE                                               | 03/2017                       | 337.75<br>337.75                   | 06/2019<br>06/2019                 | 06/2019     | 0/0                        |
| 84                                              | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT                  | 05/2017                       | 175.64<br>175.64                   | 09/2018<br>09/2018                 | 06/2019     | 0/0                        |
| 85                                              | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA        | 05/2017                       | 445.89<br>445.89                   | 02/2019<br>02/2019                 | 06/2019     | 0/0                        |
| 86                                              | SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT                                | 12/2017                       | 193.14<br>193.14                   | 06/2019<br>06/2019                 | 06/2019     | 0/0                        |
| 87                                              | TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU | 05/2017                       | 186.17<br>186.17                   | 07/2019<br>07/2019                 | 07/2019     | 0/0                        |
| 88                                              | TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE | 03/2016                       | 808.63<br>808.63                   | 01/2018<br>03/2019                 | 09/2019     | 0/0                        |
| 89                                              | HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE | 05/2016                       | 14,733.37<br>14,733.37             | 11/2019<br>11/2019                 | 11/2019     | 0/0                        |
| 90                                              | S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE | 03/2017                       | 283.72<br>283.72                   | 11/2019<br>11/2019                 | 11/2019     | 0/0                        |
| 91                                              | SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE                                                   | 03/2017                       | 379.95<br>379.95                   | 12/2019<br>12/2019                 | 12/2019     | 0/0                        |
| 92                                              | COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE        | 12/2014                       | 4,754.42<br>4,754.42               | 12/2018<br>12/2018                 | 12/2019     | 0/0                        |
| 93                                              | NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE                   | 12/2014                       | 5,111.33<br>5,111.33               | 12/2018<br>12/2018                 | 12/2019     | 0/0                        |
| 94                                              | EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL                                                               | 04/2016                       | 454.11<br>454.11                   | 04/2018<br>01/2020                 | 01/2020     | 0/0                        |
| 95                                              | WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE                                                            | 02/2017                       | 195.05<br>195.05                   | 02/2020<br>02/2020                 | 02/2020     | 0/0                        |
| 96                                              | HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE | 08/2017                       | 1,931.39<br>1,931.39               | 02/2020<br>02/2020                 | 02/2020     | 0/0                        |
| 97                                              | 400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE                          | 09/2017                       | 198.49<br>198.49                   | 09/2019<br>02/2020                 | 02/2020     | 0/0                        |
| 98                                              | HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE | 02/2017                       | 5,070.13<br>5,070.13               | 04/2020<br>04/2020                 | 04/2020     | 0/0                        |
| 99                                              | EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE                                                               | 11/2017                       | 358.83<br>358.83                   | 05/2020<br>05/2020                 | 05/2020     | 0/0                        |
| 100                                             | EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE                                                            | 03/2017                       | 3,500.00<br>3,500.00               | 07/2020<br>-                       | 07/2020     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                 |                               |                                    |                                    |             |                            |
|-------------------------------------------------|-----------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                         | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                 |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                               | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 101                                             | SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE                                     | 01/2016                       | 1,455.47 -                         | 07/2018 -                          | -           | 0/0                        |
|                                                 | <u>HEAVY INDUSTRY</u>                                                                                           |                               |                                    |                                    |             |                            |
|                                                 | <u>Indira Gandhi Centre For Atomic Research</u>                                                                 |                               |                                    |                                    |             |                            |
| 102                                             | LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]IGCAR,DELHI | 08/2016                       | 1,554.00 -                         | 09/2019 -                          | 09/2019     | 0/0                        |
|                                                 | <u>HEALTH AND FAMILY WELFARE</u>                                                                                |                               |                                    |                                    |             |                            |
|                                                 | <u>HII Infra Tech Services Limited</u>                                                                          |                               |                                    |                                    |             |                            |
| 103                                             | ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH                     | 07/2016                       | 785.00 -                           | 04/2020 -                          | 04/2020     | 0/0                        |
| 104                                             | ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB                            | 07/2016                       | 703.00 -                           | 06/2020 -                          | 06/2020     | 0/0                        |
| 105                                             | ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM                              | 05/2017                       | 875.00 -                           | 05/2021 -                          | 05/2021     | 0/0                        |
|                                                 | <u>Hospital Services Consultancy Corporation</u>                                                                |                               |                                    |                                    |             |                            |
| 106                                             | RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH     | 08/2017                       | 272.19 -                           | 03/2019 -                          | 03/2019     | 0/0                        |
| 107                                             | HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH                                            | 03/2018                       | 601.02 -                           | -                                  | 02/2020     | 0/0                        |
| 108                                             | HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA                                               | 03/2018                       | 582.99 -                           | -                                  | 02/2020     | 0/0                        |
| 109                                             | HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL                                              | 04/2018                       | 651.99 -                           | -                                  | 02/2020     | 0/0                        |
| 110                                             | HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH                                    | 03/2018                       | 268.84 -                           | -                                  | 04/2020     | 0/0                        |
| 111                                             | SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA                                                          | 01/2018                       | 249.01 -                           | -                                  | 05/2020     | 0/0                        |
|                                                 | <u>Hospital Services Consultancy Corporation Ltd</u>                                                            |                               |                                    |                                    |             |                            |
| 112                                             | CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL                                                          | 08/2016                       | 244.00 -                           | 09/2018 -                          | 09/2018     | 0/0                        |
| 113                                             | RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA - [N21000016]HSCC,MAHARASHTRA                      | 08/2017                       | 274.19 -                           | 03/2019 -                          | 03/2019     | 0/0                        |
| 114                                             | RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL                     | 08/2017                       | 355.15 -                           | 03/2019 -                          | 03/2019     | 0/0                        |
| 115                                             | GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI                                                           | 12/2017                       | 156.56 -                           | -                                  | 02/2020     | 0/0                        |
| 116                                             | LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI                                                           | 02/2013                       | 414.11 -                           | 11/2013 10/2020                    | 10/2020     | 0/0                        |
| 117                                             | LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM                                                                   | 07/2012                       | 175.57 -                           | 12/2014 -                          | -           | 0/0                        |
| 118                                             | NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA                                                         | 10/2016                       | 363.99 -                           | 05/2018 09/2019                    | 08/2019     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                               |                               |                                    |                                    |         |                            |
|-------------------------------------------------|-------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|---------|----------------------------|
| Sl.No                                           | Project                                                                       | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |         | Milestones Achieved/ Total |
| 1                                               | 2                                                                             | 3                             | 4                                  | 5                                  | 6       | 7                          |
|                                                 | <u>RAILWAYS</u>                                                               |                               |                                    |                                    |         |                            |
|                                                 | <u>Central Railways</u>                                                       |                               |                                    |                                    |         |                            |
| 119                                             | 3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA                 | 04/2011                       | 184.06<br>199.12                   | 03/2019<br>-                       | 03/2019 | 0/0                        |
| 120                                             | AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA                  | 02/1997                       | 2,271.50<br>2,271.50               | 03/2021<br>-                       | 03/2021 | 0/0                        |
| 121                                             | KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA                            | 04/2011                       | 792.89<br>792.89                   | 03/2021<br>-                       | 03/2021 | 0/0                        |
| 122                                             | WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA                      | 04/2012                       | 540.02<br>540.02                   | 03/2022<br>-                       | 03/2022 | 0/0                        |
| 123                                             | WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA             | 02/2015                       | 1,272.19<br>1,272.19               | 03/2022<br>-                       | 03/2022 | 0/0                        |
| 124                                             | WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA                         | 04/2008                       | 3,168.29<br>3,168.29               | 03/2023<br>-                       | 03/2023 | 0/0                        |
| 125                                             | ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA          | 02/2015                       | 2,449.91<br>2,449.91               | 03/2023<br>-                       | 03/2023 | 0/0                        |
| 126                                             | DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA                           | 02/2016                       | 1,876.00<br>2,081.27               | 03/2023<br>-                       | 03/2023 | 0/0                        |
| 127                                             | MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA              | 02/2016                       | 1,035.16<br>1,035.16               | 03/2022<br>-                       | 03/2023 | 0/0                        |
| 128                                             | WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA                | 02/2016                       | 637.95<br>637.95                   | 03/2023<br>-                       | 03/2023 | 0/0                        |
| 129                                             | INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA             | 02/2016                       | 9,968.00<br>-                      | 03/2024<br>-                       | 03/2024 | 0/0                        |
| 130                                             | PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA                               | 02/2016                       | 2,425.00<br>-                      | 03/2024<br>-                       | 03/2024 | 0/0                        |
| 131                                             | VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA                   | 02/2016                       | 2,750.00<br>-                      | 03/2024<br>-                       | 03/2024 | 0/0                        |
| 132                                             | PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA                         | 02/2015                       | 3,627.47<br>3,627.47               | 03/2024<br>-                       | 03/2024 | 0/0                        |
| 133                                             | AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA                           | 06/1994                       | 663.01<br>668.34                   | 06/1999<br>-                       | -       | 0/0                        |
|                                                 | <u>Container Corporation Of India</u>                                         |                               |                                    |                                    |         |                            |
| 134                                             | MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA        | 10/2013                       | 305.00<br>-                        | 03/2019<br>-                       | 03/2019 | 0/0                        |
| 135                                             | MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA                 | 12/2015                       | 346.32<br>-                        | 03/2019<br>-                       | 03/2019 | 0/0                        |
| 136                                             | MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH           | 12/2015                       | 174.00<br>-                        | 03/2019<br>-                       | 08/2019 | 0/0                        |
| 137                                             | MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN            | 01/2011                       | 493.17<br>-                        | 03/2018<br>-                       | 12/2019 | 0/0                        |
| 138                                             | MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT               | 10/2013                       | 343.00<br>-                        | 03/2019<br>-                       | 12/2019 | 0/0                        |
| 139                                             | MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH       | 08/2016                       | 234.50<br>-                        | 03/2019<br>-                       | 12/2020 | 0/0                        |
| 140                                             | MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH | 01/2013                       | 387.70<br>-                        | 03/2018<br>-                       | -       | 0/0                        |



## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                        |                               |                                    |                                    |             |                            |
|-------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                                | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                        |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                      | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 141                                             | MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI, CHHATISGARH<br><u>Dedicated Freight Corridor Corporation Of India Ltd</u> | 05/2014                       | 207.00<br>-                        | 03/2018<br>-                       | -           | 0/0                        |
| 142                                             | WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC, MULTI STATE                                                                      | 11/2007                       | 16,592.00<br>51,101.00             | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 143                                             | EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC, MULTI STATE<br><u>East Central Railways</u>                              | 10/2006                       | 11,589.00<br>30,357.00             | -<br>-                             | -           | 0/0                        |
| 144                                             | RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR, BIHAR                                                        | 04/1998                       | 180.82<br>-                        | -<br>-                             | 12/2018     | 0/0                        |
| 145                                             | KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH                                                                    | 08/2015                       | 528.57<br>-                        | 03/2019<br>-                       | 12/2019     | 0/0                        |
| 146                                             | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR, BIHAR                                                                     | 04/1997                       | 324.73<br>-                        | 03/2012<br>-                       | 03/2020     | 0/0                        |
| 147                                             | KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR                                                                                          | 04/2002                       | 499.41<br>-                        | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 148                                             | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR                                                              | 04/1996                       | 477.88<br>283.95                   | 03/2012<br>-                       | 03/2020     | 0/0                        |
| 149                                             | JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR, BIHAR                                           | 04/2009                       | 548.00<br>-                        | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 150                                             | GARHWA ROAD-RAMNA - [N22000465]ECR, JHARKHAND                                                                                          | 03/2015                       | 348.23<br>-                        | 03/2021<br>-                       | 12/2020     | 0/0                        |
| 151                                             | KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND                                                                     | 03/1999                       | 1,033.07<br>-                      | -<br>-                             | 03/2021     | 0/0                        |
| 152                                             | SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR, BIHAR                                         | 04/2004                       | 372.14<br>-                        | -<br>-                             | 03/2021     | 0/0                        |
| 153                                             | RAMNA - SINGRAULI DOUBLING - [N22000417]ECR, UTTAR PRADESH                                                                             | 08/2015                       | 2,436.21<br>-                      | 03/2020<br>-                       | 03/2021     | 0/0                        |
| 154                                             | PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]ECR, BIHAR                   | 11/2001                       | 624.47<br>-                        | 02/2016<br>-                       | 03/2021     | 0/0                        |
| 155                                             | FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR, BIHAR           | 04/1991                       | 329.39<br>-                        | -<br>-                             | 12/2021     | 0/0                        |
| 156                                             | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR, BIHAR                                                                          | 04/1997                       | 162.87<br>-                        | -<br>-                             | 03/2022     | 0/0                        |
| 157                                             | SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR, BIHAR                                                                         | 04/2016                       | 744.04<br>-                        | 03/2021<br>-                       | 03/2022     | 0/0                        |
| 158                                             | MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR, BIHAR                                                                         | 04/2016                       | 731.64<br>-                        | 03/2021<br>-                       | 03/2022     | 0/0                        |
| 159                                             | HAJIPUR-SAGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, BIHAR                                                                         | 04/2003                       | 528.65<br>-                        | -<br>-                             | 03/2023     | 0/0                        |
| 160                                             | ARARIA-SUPAUL (NL) - [N22000177]ECR, BIHAR                                                                                             | 04/2008                       | 1,605.17<br>-                      | -<br>-                             | 03/2023     | 0/0                        |
| 161                                             | KODERMA-TILAIYA (NL), ECR - [220100305]ECR, JHARKHAND                                                                                  | 04/2002                       | 459.91<br>-                        | -<br>-                             | -           | 0/0                        |
| 162                                             | DANIYAWAN-BIHARSARIF (NL), ECR - [220100311]ECR, BIHAR                                                                                 | 04/2001                       | 406.92<br>-                        | -<br>-                             | -           | 0/0                        |



## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                            |                               |                                    |                                    |             |                            |
|-------------------------------------------------|------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                    | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                            |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                          | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 163                                             | NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR                                                                | 04/2008                       | 620.57<br>-                        | -<br>-                             | -           | 0/0                        |
| 164                                             | DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR                                                      | 04/2005                       | 205.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 165                                             | MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR                                                             | 04/2006                       | 211.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 166                                             | SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR                                         | 04/2008                       | 678.62<br>-                        | -<br>-                             | -           | 0/0                        |
| 167                                             | MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR                                           | 04/2008                       | 228.05<br>-                        | -<br>-                             | -           | 0/0                        |
| 168                                             | KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR                                                             | 04/2008                       | 192.56<br>-                        | -<br>-                             | -           | 0/0                        |
| 169                                             | MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR                                                          | 04/2008                       | 281.30<br>-                        | -<br>-                             | -           | 0/0                        |
| 170                                             | HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR                                                     | 04/2013                       | 213.01<br>-                        | -<br>-                             | -           | 0/0                        |
| 171                                             | SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR                                                                | 05/2015                       | 380.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 172                                             | MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR                                                      | 01/1991                       | 332.15<br>-                        | 07/2014<br>-                       | -           | 0/0                        |
| <u>East Coast Railway</u>                       |                                                                                                            |                               |                                    |                                    |             |                            |
| 173                                             | SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA                                            | 03/2012                       | 155.81<br>-                        | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 174                                             | EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA | 04/2016                       | 5,200.00<br>-                      | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 175                                             | SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR                                                           | 04/1999                       | 325.00<br>-                        | -<br>-                             | 03/2021     | 0/0                        |
| 176                                             | SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA                                                        | 03/2011                       | 1,111.99<br>1,539.28               | 02/2019<br>-                       | 03/2021     | 0/0                        |
| 177                                             | BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA                                                       | 03/2013                       | 843.04<br>843.04                   | 10/2020<br>-                       | 03/2021     | 0/0                        |
| 178                                             | JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA               | 04/2015                       | 701.61<br>-                        | 11/2018<br>-                       | 03/2021     | 0/0                        |
| 179                                             | BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA                              | 04/2015                       | 1,172.92<br>-                      | 12/2018<br>-                       | 03/2021     | 0/0                        |
| 180                                             | KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA                                                      | 04/1994                       | 2,923.13<br>-                      | 03/2009<br>-                       | 06/2021     | 0/0                        |
| 181                                             | CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR                                                           | 04/2006                       | 378.56<br>-                        | -<br>-                             | 03/2022     | 0/0                        |
| 182                                             | JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA                                                        | 04/2015                       | 1,547.38<br>-                      | 03/2022<br>-                       | 03/2022     | 0/0                        |
| 183                                             | KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH                                             | 04/2015                       | 2,499.71<br>-                      | 03/2022<br>-                       | 03/2022     | 0/0                        |
| 184                                             | KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA                                                  | 04/2015                       | 2,361.74<br>-                      | 03/2022<br>-                       | 03/2022     | 0/0                        |
| 185                                             | TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA                                                      | 04/2005                       | 810.78<br>-                        | 06/2021<br>-                       | 03/2023     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                  |                               |                                    |                                    |             |                            |
|-------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                          | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                  |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 186                                             | GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR                                                                        | 04/2008                       | 445.25<br>-                        | -<br>-                             | -           | 0/0                        |
| 187                                             | GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE                                                                                   | 04/2008                       | 415.67<br>-                        | -<br>-                             | -           | 0/0                        |
| 188                                             | BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR                                                                                    | 04/2008                       | 326.20<br>-                        | -<br>-                             | -           | 0/0                        |
| <u>Eastern Railways</u>                         |                                                                                                                                  |                               |                                    |                                    |             |                            |
| 189                                             | MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND                                                                     | 04/1995                       | 1,125.89<br>-                      | 03/2016<br>-                       | 03/2020     | 0/0                        |
| 190                                             | SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE                                         | 04/2010                       | 277.28<br>-                        | 03/2016<br>-                       | 03/2020     | 0/0                        |
| 191                                             | HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE                                                                                    | 04/2011                       | 542.18<br>-                        | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 192                                             | PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE                                                                                    | 04/2013                       | 915.98<br>-                        | 03/2022<br>-                       | 03/2022     | 0/0                        |
| 193                                             | DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE                                                                       | 04/2000                       | 607.09<br>-                        | 02/2013<br>-                       | -           | 0/0                        |
| 194                                             | DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL                                                                     | 04/2009                       | 259.51<br>-                        | 02/2012<br>-                       | -           | 0/0                        |
| 195                                             | GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL                                                                           | 04/2009                       | 193.08<br>-                        | 12/2011<br>-                       | -           | 0/0                        |
| 196                                             | LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE | 04/1987                       | 406.99<br>-                        | 03/2006<br>-                       | -           | 0/0                        |
| 197                                             | SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE                                                  | 04/2007                       | 450.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 198                                             | HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE                                                                     | 04/2010                       | 172.03<br>-                        | -<br>-                             | -           | 0/0                        |
| 199                                             | BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE                                                                              | 04/2011                       | 288.35<br>-                        | -<br>-                             | -           | 0/0                        |
| 200                                             | PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE                                                                                  | 04/2011                       | 261.38<br>-                        | -<br>-                             | -           | 0/0                        |
| 201                                             | KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE | 04/2001                       | 923.52<br>-                        | 03/2016<br>-                       | -           | 0/0                        |
| 202                                             | CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE                     | 04/2005                       | 595.51<br>-                        | 03/2017<br>-                       | -           | 0/0                        |
| 203                                             | KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE                      | 04/2010                       | 174.56<br>-                        | -<br>-                             | -           | 0/0                        |
| 204                                             | DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE   | 04/2010                       | 365.17<br>-                        | 03/2017<br>-                       | -           | 0/0                        |
| 205                                             | HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE                                           | 04/2010                       | 157.94<br>-                        | 11/2018<br>-                       | -           | 0/0                        |
| 206                                             | BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE                                                 | 04/2007                       | 450.55<br>-                        | -<br>-                             | -           | 0/0                        |
| 207                                             | TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE                                                                        | 04/2010                       | 365.17<br>-                        | -<br>-                             | -           | 0/0                        |
| 208                                             | BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE                                                                          | 04/2011                       | 175.80<br>-                        | -<br>-                             | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                   |                               |                                    |                                    |             |                            |
|-------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                           | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                   |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                 | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 209                                             | PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE                                                     | 04/2011                       | 299.60<br>-                        | 03/2017<br>-                       | -           | 0/0                        |
| 210                                             | NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE  | 04/2010                       | 494.54<br>-                        | 03/2005<br>-                       | -           | 0/0                        |
| 211                                             | SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE                                  | 04/2000                       | 297.47<br>-                        | -<br>-                             | -           | 0/0                        |
| 212                                             | CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE | 04/2003                       | 337.96<br>-                        | -<br>-                             | -           | 0/0                        |
| 213                                             | MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE   | 04/2009                       | 499.96<br>-                        | 02/2012<br>-                       | -           | 0/0                        |
| 214                                             | LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE                                  | 04/2009                       | 257.42<br>-                        | 03/2014<br>-                       | -           | 0/0                        |
| 215                                             | SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE                                                 | 04/2010                       | 268.52<br>-                        | -<br>-                             | -           | 0/0                        |
| 216                                             | HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE          | 04/2011                       | 166.89<br>-                        | -<br>-                             | -           | 0/0                        |
| 217                                             | MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE                                                                                     | 04/2012                       | 250.93<br>-                        | -<br>-                             | -           | 0/0                        |
| 218                                             | BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL                                                                      | 04/2012                       | 255.64<br>-                        | -<br>-                             | -           | 0/0                        |
| 219                                             | TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL                                                           | 04/2000                       | 1,188.91<br>-                      | 03/2019<br>12/2009                 | 03/2019     | 0/0                        |
| <u>Kochi Metro Rail Corporation Ltd</u>         |                                                                                                                                   |                               |                                    |                                    |             |                            |
| 220                                             | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL,WEST BENGAL              | 04/2010                       | 2,397.72<br>-                      | 03/2016<br>-                       | -           | 0/0                        |
| <u>Metropolitan Rapid Transport Projects</u>    |                                                                                                                                   |                               |                                    |                                    |             |                            |
| 221                                             | MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA                                                             | 04/2008                       | 5,300.00<br>-                      | 03/2014<br>-                       | 03/2019     | 0/0                        |
| 222                                             | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA                                                   | 03/1996                       | 495.44<br>1,781.98                 | 03/2004<br>-                       | 03/2020     | 0/0                        |
| 223                                             | TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL                     | 03/2000                       | 1,049.69<br>-                      | 12/2006<br>-                       | -           | 0/0                        |
| 224                                             | EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL                                            | 03/2013                       | 4,874.58<br>-                      | 03/2016<br>-                       | -           | 0/0                        |
| 225                                             | CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHUPUR - [N22000212]MRTP,WEST BENGAL                                              | 04/2009                       | 573.78<br>-                        | -<br>-                             | -           | 0/0                        |
| 226                                             | RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA                                                            | 04/2012                       | 714.10<br>-                        | 04/2016<br>-                       | -           | 0/0                        |
| <u>North Central Railway</u>                    |                                                                                                                                   |                               |                                    |                                    |             |                            |
| 227                                             | JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH                                                                               | 09/2016                       | 2,001.00<br>-                      | 03/2021<br>-                       | 03/2021     | 0/0                        |
| 228                                             | GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE                                                       | 04/2011                       | 2,912.96<br>-                      | 03/2022<br>-                       | 03/2022     | 0/0                        |
| 229                                             | DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE        | 04/2010                       | 2,030.50<br>-                      | -<br>-                             | 12/2022     | 0/0                        |
| 230                                             | JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH                                                       | 03/2018                       | 4,329.53<br>-                      | 03/2023<br>-                       | 03/2023     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                      |                               |                                    |                                    |             |                            |
|-------------------------------------------------|------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                      |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                    | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 231                                             | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE                       | 04/1986                       | 158.77<br>274.56                   | 03/1994<br>-                       | -           | 0/0                        |
| 232                                             | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH                            | 04/1999                       | 108.00<br>-                        | 12/2009<br>-                       | -           | 0/0                        |
| 233                                             | ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH                                              | 04/1997                       | 120.00<br>-                        | 12/2008<br>-                       | -           | 0/0                        |
| <u>North East Frontier Railway</u>              |                                                                                                      |                               |                                    |                                    |             |                            |
| 234                                             | CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA                                  | 04/1999                       | 895.00<br>984.97                   | 03/2007<br>-                       | 04/2016     | 0/0                        |
| 235                                             | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE                  | 04/2000                       | 1,180.19<br>2,531.34               | 12/2008<br>-                       | 03/2019     | 0/0                        |
| 236                                             | AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA                                                  | 04/2008                       | 1,142.00<br>3,407.00               | 03/2014<br>12/2019                 | 03/2019     | 0/0                        |
| 237                                             | NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE                                | 04/2013                       | 1,798.00<br>-                      | 03/2019<br>-                       | 03/2019     | 0/0                        |
| 238                                             | AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM                                              | 04/2011                       | 314.00<br>486.96                   | 03/2019<br>-                       | 03/2019     | 0/0                        |
| 239                                             | LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM                                          | 04/2012                       | 246.07<br>614.81                   | 03/2019<br>-                       | 03/2019     | 0/0                        |
| 240                                             | NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL | 04/1983                       | 297.32<br>200.34                   | 03/2019<br>-                       | 03/2020     | 0/0                        |
| 241                                             | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR                                         | 04/2003                       | 4,454.17<br>-                      | 03/2011<br>-                       | 03/2020     | 0/0                        |
| 242                                             | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM               | 09/2006                       | 385.20<br>-                        | 03/2019<br>-                       | 03/2020     | 0/0                        |
| 243                                             | NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR                      | 09/2006                       | 532.87<br>2,132.03                 | 03/2019<br>-                       | 03/2020     | 0/0                        |
| 244                                             | KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR                                                | 04/2008                       | 333.76<br>-                        | -<br>-                             | 03/2020     | 0/0                        |
| 245                                             | SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM                                                           | 04/2008                       | 1,339.48<br>-                      | 12/2015<br>-                       | 03/2020     | 0/0                        |
| 246                                             | NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL                                | 04/2010                       | 221.42<br>-                        | -<br>-                             | 03/2020     | 0/0                        |
| 247                                             | DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND                                                           | 04/2013                       | 4,274.00<br>-                      | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 248                                             | NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE                                 | 04/2010                       | 242.22<br>-                        | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 249                                             | MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE                                                | 04/2011                       | 414.84<br>-                        | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 250                                             | BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM                                         | 04/2015                       | 2,232.32<br>-                      | 03/2022<br>-                       | 03/2020     | 0/0                        |
| 251                                             | NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL        | 04/2016                       | 602.27<br>-                        | 12/2021<br>-                       | 03/2020     | 0/0                        |
| 252                                             | BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM                                                  | 04/2008                       | 2,393.47<br>2,393.48               | 03/2014<br>12/2020                 | 12/2020     | 0/0                        |
| 253                                             | NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA                                     | 04/2010                       | 906.46<br>1,202.33                 | 03/2021<br>-                       | 03/2021     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                |                               |                                    |                                    |             |                            |
|-------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                        | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                              | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 254                                             | DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM                                                                                   | 04/2015                       | 870.96<br>-                        | 03/2021<br>-                       | 03/2021     | 0/0                        |
| 255                                             | NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND                                       | 04/2006                       | 2,326.52<br>2,446.57               | 03/2015<br>10/2021                 | 10/2021     | 0/0                        |
| 256                                             | KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR                                                                            | 09/2001                       | 792.46<br>724.31                   | 12/2010<br>-                       | -           | 0/0                        |
| 257                                             | NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE                                                            | 04/2010                       | 241.52<br>-                        | -<br>-                             | -           | 0/0                        |
| 258                                             | NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE | 04/1999                       | 819.23<br>-                        | -<br>-                             | -           | 0/0                        |
|                                                 | <u>North Eastern Railway</u>                                                                                                   |                               |                                    |                                    |             |                            |
| 259                                             | BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH                                                                  | 03/2008                       | 195.64<br>-                        | -<br>-                             | 03/2018     | 0/0                        |
| 260                                             | MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR                                                                          | 04/2003                       | 218.19<br>-                        | 06/2018<br>-                       | 10/2018     | 0/0                        |
| 261                                             | AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH                                                          | 03/2012                       | 199.75<br>-                        | 08/2018<br>-                       | 01/2019     | 0/0                        |
| 262                                             | CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE                                                                                 | 03/2013                       | 295.00<br>-                        | 01/2019<br>-                       | 02/2019     | 0/0                        |
| 263                                             | ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH                                                             | 03/2015                       | 1,295.42<br>-                      | 03/2022<br>-                       | 02/2019     | 0/0                        |
| 264                                             | MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]NER,UTTAR PRADESH                                                         | 04/1997                       | 609.04<br>1,063.00                 | 04/1999<br>-                       | 03/2019     | 0/0                        |
| 265                                             | HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE                                                                         | 04/2005                       | 230.03<br>-                        | 12/2022<br>-                       | 05/2019     | 0/0                        |
| 266                                             | SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH                 | 04/2016                       | 1,177.96<br>-                      | 03/2014<br>-                       | 04/2021     | 0/0                        |
| 267                                             | CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE                                                    | 03/2007                       | 243.78<br>-                        | 12/2021<br>-                       | 12/2021     | 0/0                        |
| 268                                             | INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH                                                            | 04/2016                       | 213.00<br>-                        | 04/2016<br>-                       | 01/2022     | 0/0                        |
| 269                                             | BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH                               | 04/2016                       | 1,900.00<br>-                      | 01/2022<br>-                       | 01/2022     | 0/0                        |
| 270                                             | AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH                                                             | 04/2016                       | 600.00<br>-                        | 01/2022<br>-                       | 01/2022     | 0/0                        |
| 271                                             | ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH                                                                       | 04/2017                       | 276.90<br>-                        | 04/2017<br>-                       | 04/2022     | 0/0                        |
| 272                                             | NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH                                                           | 04/2017                       | 150.00<br>-                        | 04/2017<br>-                       | 10/2022     | 0/0                        |
| 273                                             | PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH                                                        | 04/2017                       | 622.50<br>427.00                   | 04/2017<br>-                       | 10/2022     | 0/0                        |
| 274                                             | KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND                                                                         | 04/2003                       | 142.45<br>-                        | -<br>-                             | -           | 0/0                        |
| 275                                             | ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH                                                           | 03/2013                       | 307.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 276                                             | KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH                                      | 03/2013                       | 643.00<br>-                        | -<br>-                             | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                              |                               |                                    |                                    |             |                            |
|-------------------------------------------------|----------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                      | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                              |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                            | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 277                                             | GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH                                   | 04/2014                       | 182.92<br>-                        | -<br>-                             | -           | 0/0                        |
| 278                                             | GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]NER,UTTAR PRADESH | 04/1997                       | 233.00<br>-                        | 04/1999<br>-                       | -           | 0/0                        |
| 279                                             | PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH                | 04/2017                       | 1,343.00<br>-                      | 01/2018<br>-                       | -           | 0/0                        |
| 280                                             | BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH                           | 04/2016                       | 602.50<br>-                        | -<br>-                             | -           | 0/0                        |
|                                                 | <u>North Western Railway</u>                                                                 |                               |                                    |                                    |             |                            |
| 281                                             | THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN                                                | 04/2013                       | 236.93<br>-                        | 10/2018<br>-                       | 10/2018     | 0/0                        |
| 282                                             | DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN                                       | 02/1997                       | 410.08<br>780.98                   | 02/2019<br>-                       | 02/2019     | 0/0                        |
| 283                                             | JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN | 04/2008                       | 653.19<br>-                        | 03/2014<br>03/2019                 | 03/2019     | 0/0                        |
| 284                                             | ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN                                           | 04/2013                       | 242.09<br>-                        | 02/2019<br>-                       | 03/2019     | 0/0                        |
| 285                                             | BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN                                  | 04/2012                       | 246.08<br>-                        | 12/2019<br>-                       | 06/2019     | 0/0                        |
| 286                                             | AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN                                                  | 04/2011                       | 213.39<br>-                        | 11/2019<br>-                       | 11/2019     | 0/0                        |
| 287                                             | MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN       | 04/2013                       | 420.18<br>295.02                   | 03/2020<br>-                       | 12/2019     | 0/0                        |
| 288                                             | PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE                                       | 05/2015                       | 600.00<br>-                        | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 289                                             | HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN                      | 04/2008                       | 829.74<br>-                        | 03/2015<br>-                       | 06/2020     | 0/0                        |
| 290                                             | JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN                  | 08/2018                       | 808.85<br>-                        | 08/2022<br>-                       | 08/2022     | 0/0                        |
| 291                                             | PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN                                                     | 04/2013                       | 323.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 292                                             | AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN  | 05/2015                       | 873.71<br>-                        | -<br>-                             | -           | 0/0                        |
|                                                 | <u>Northern Railway</u>                                                                      |                               |                                    |                                    |             |                            |
| 293                                             | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR                        | 03/1995                       | 2,500.00<br>-                      | 11/2002<br>-                       | 03/2021     | 0/0                        |
| 294                                             | CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE                                                 | 04/2007                       | 328.14<br>-                        | 03/2023<br>-                       | 03/2023     | 0/0                        |
| 295                                             | NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE                                         | 03/1981                       | 450.00<br>-                        | 07/2012<br>-                       | -           | 0/0                        |
| 296                                             | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE                           | 03/2002                       | 625.30<br>408.76                   | 06/2007<br>-                       | -           | 0/0                        |
| 297                                             | JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA                                                 | 01/2004                       | 238.56<br>-                        | 03/2012<br>-                       | -           | 0/0                        |
| 298                                             | UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH                           | 04/2006                       | 369.90<br>-                        | 03/2010<br>-                       | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                               |                               |                                    |                                    |             |                            |
|-------------------------------------------------|---------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                       | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                               |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                             | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 299                                             | MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH                                                    | 04/2012                       | 377.44<br>-                        | -<br>-                             | -           | 0/0                        |
| 300                                             | MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB | 04/2009                       | 396.04<br>-                        | -<br>-                             | -           | 0/0                        |
| 301                                             | GRADE SEPARATOR AT DAYABASTI - [N22000269]NR,DELHI                                                            | 04/1999                       | 156.65<br>-                        | -<br>-                             | -           | 0/0                        |
| 302                                             | FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH                       | 04/2013                       | 654.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 303                                             | DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE                                             | 04/2013                       | 1,239.00<br>-                      | -<br>-                             | -           | 0/0                        |
| 304                                             | ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA                                                                    | 04/2012                       | 287.00<br>-                        | 12/2011<br>-                       | -           | 0/0                        |
| 305                                             | DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE                                               | 04/2007                       | 336.91<br>-                        | -<br>-                             | -           | 0/0                        |
| 306                                             | ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI                                               | 04/2012                       | 295.68<br>-                        | -<br>-                             | -           | 0/0                        |
| 307                                             | HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND                                                                   | 04/2012                       | 219.83<br>-                        | -<br>-                             | -           | 0/0                        |
| 308                                             | AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE                       | 04/2010                       | 338.54<br>-                        | -<br>-                             | -           | 0/0                        |
| 309                                             | JAKHAL-MANSAB DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE                                             | 04/2008                       | 162.96<br>-                        | -<br>-                             | -           | 0/0                        |
| 310                                             | HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA                                                 | 04/2013                       | 400.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 311                                             | YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE                                   | 04/2013                       | 876.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 312                                             | UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH                                                                 | 04/2012                       | 1,229.00<br>-                      | -<br>-                             | -           | 0/0                        |
| 313                                             | QADIAN-BEAS - [N22000295]NR,PUNJAB                                                                            | 04/2011                       | 205.22<br>-                        | -<br>-                             | -           | 0/0                        |
| 314                                             | CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE                                                               | 04/2007                       | 328.14<br>-                        | -<br>-                             | -           | 0/0                        |
| 315                                             | JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE                                                    | 03/2002                       | 625.00<br>-                        | 03/2016<br>-                       | -           | 0/0                        |
|                                                 | <u>National High Speed Rail Corporation Limited</u>                                                           |                               |                                    |                                    |             |                            |
| 316                                             | MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE                                      | 12/2015                       | 1,08,000.00<br>-                   | 12/2023<br>12/2023                 | 12/2023     | 0/0                        |
|                                                 | <u>Rail India Technical And Economic Service</u>                                                              |                               |                                    |                                    |             |                            |
| 317                                             | GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE                                                     | 04/2015                       | 636.38<br>-                        | -<br>-                             | -           | 0/0                        |
|                                                 | <u>Rail Vikas Nigam Ltd.</u>                                                                                  |                               |                                    |                                    |             |                            |
| 318                                             | HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA                                                              | 04/1996                       | 1,185.64<br>-                      | 12/2017<br>-                       | 03/2020     | 0/0                        |
| 319                                             | OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH                                           | 07/2006                       | 732.81<br>-                        | 03/2008<br>-                       | 03/2020     | 0/0                        |
| 320                                             | LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH                                   | 04/2011                       | 927.01<br>-                        | 03/2019<br>-                       | 03/2020     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                |                               |                                    |                                    |             |                            |
|-------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                        | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                              | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 321                                             | DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA             | 03/2009                       | 713.48 -                           | 03/2020 -                          | 03/2020     | 0/0                        |
| 322                                             | SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA                                                                      | 03/2006                       | 948.04 -                           | 03/2020 -                          | 03/2020     | 0/0                        |
| 323                                             | RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH                                                                    | 03/2007                       | 1,402.02 -                         | 03/2020 -                          | 03/2020     | 0/0                        |
| 324                                             | MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA                                              | 04/2012                       | 632.68 -                           | 03/2016 03/2017                    | 12/2020     | 0/0                        |
| 325                                             | BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH                                                                  | 04/2011                       | 1,485.85 -                         | 12/2020 -                          | 12/2020     | 0/0                        |
| 326                                             | DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT                                                                                  | 04/2012                       | 644.38 -                           | 03/2021 -                          | 03/2021     | 0/0                        |
| 327                                             | BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA                                                                        | 03/2009                       | 942.95 -                           | 03/2019 -                          | 03/2021     | 0/0                        |
| 328                                             | BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH                                                 | 03/2012                       | 1,183.25 -                         | 12/2020 -                          | 03/2021     | 0/0                        |
| 329                                             | SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA                                                                       | 04/1998                       | 1,202.70 245.00                    | 02/2015 -                          | 12/2021     | 0/0                        |
| 330                                             | AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT                                                                                 | 04/2012                       | 975.62 -                           | 12/2021 -                          | 12/2021     | 0/0                        |
| 331                                             | PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT                                                                            | 04/2013                       | 1,548.66 -                         | 12/2021 -                          | 12/2021     | 0/0                        |
| 332                                             | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH                                 | 04/1995                       | 631.78 632.00                      | 12/2012 -                          | 03/2022     | 0/0                        |
| 333                                             | VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH                                          | 03/2012                       | 1,503.71 -                         | 03/2020 -                          | 03/2022     | 0/0                        |
| 334                                             | VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH                                                                              | 04/2015                       | 3,246.26 -                         | 12/2023 -                          | 12/2023     | 0/0                        |
| 335                                             | VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH                                                         | 04/2015                       | 943.60 -                           | 03/2022 -                          | 12/2024     | 0/0                        |
| 336                                             | SECUNDERABAD-MAHABUNAGAR DOUBLING - [N22000403]RVNL,TELANGANA                                                                  | 04/2015                       | 773.94 -                           | 12/2024 -                          | 12/2024     | 0/0                        |
| 337                                             | MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH                                                                 | 04/2015                       | 1,765.92 -                         | 03/2023 -                          | 12/2024     | 0/0                        |
| 338                                             | VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA                                                                    | 01/1991                       | 2,335.67 2,335.67                  | 12/2024 -                          | 12/2024     | 0/0                        |
| 339                                             | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL     | 04/2010                       | 3,951.98 -                         | 03/2016 -                          | 03/2025     | 0/0                        |
| 340                                             | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL                 | 04/2010                       | 2,913.51 4,200.00                  | 03/2016 -                          | 03/2025     | 0/0                        |
| 341                                             | DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA                                                                              | 04/2015                       | 723.78 -                           | 12/2025 -                          | 03/2025     | 0/0                        |
| 342                                             | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL | 04/2010                       | 2,298.42 -                         | 03/2014 -                          | 12/2025     | 0/0                        |
| 343                                             | RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND                                                                 | 04/2011                       | 16,216.00 -                        | 12/2024 -                          | 03/2026     | 0/0                        |
| 344                                             | BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH                                                                  | 04/2008                       | 2,966.99 -                         | 12/2026 -                          | 12/2026     | 0/0                        |



## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                 |                               |                                    |                    |             |                            |
|-------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|--------------------|-------------|----------------------------|
| SI.No                                           | Project                                                                                                                         | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Original / Revised | Anticipated | Milestones Achieved/ Total |
| 1                                               | 2                                                                                                                               | 3                             | 4                                  | 5                  | 6           | 7                          |
|                                                 | <u>Railway Electrification</u>                                                                                                  |                               |                                    |                    |             |                            |
| 345                                             | ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH                                      | 02/2008                       | 171.10<br>-                        | 03/2012<br>-       | -           | 0/0                        |
|                                                 | <u>South Central Railway</u>                                                                                                    |                               |                                    |                    |             |                            |
| 346                                             | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA                                                               | 12/1994                       | 124.43<br>-                        | -<br>-             | 03/2017     | 0/0                        |
| 347                                             | MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE                                                                    | 04/1997                       | 1,723.00<br>1.00                   | 03/2000<br>-       | 03/2019     | 0/0                        |
| 348                                             | KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE                                                                                   | 04/2015                       | 2,063.03<br>-                      | 03/2021<br>-       | 03/2021     | 0/0                        |
| 349                                             | MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA | 04/2017                       | 119.73<br>185.00                   | 03/2022<br>-       | 03/2022     | 0/0                        |
| 350                                             | KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH                                                                  | 12/2001                       | 1,045.20<br>-                      | 03/2009<br>-       | 03/2023     | 0/0                        |
| 351                                             | GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH                                                                                 | 04/2016                       | 3,631.00<br>-                      | 03/2022<br>-       | 03/2023     | 0/0                        |
| 352                                             | KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE                                                   | 04/2012                       | 1,856.95<br>-                      | 03/2023<br>-       | 03/2024     | 0/0                        |
| 353                                             | NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH                                                                    | 03/1996                       | 164.36<br>-                        | 02/2009<br>-       | -           | 0/0                        |
| 354                                             | MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA                                                                           | 07/1998                       | 458.25<br>-                        | -<br>-             | -           | 0/0                        |
| 355                                             | GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH                                                                           | 04/2011                       | 761.37<br>-                        | -<br>-             | -           | 0/0                        |
| 356                                             | DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH                                                                              | 04/2015                       | 3,873.07<br>-                      | -<br>-             | -           | 0/0                        |
|                                                 | <u>South East Central Railway</u>                                                                                               |                               |                                    |                    |             |                            |
| 357                                             | CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH                                        | 04/2010                       | 585.93<br>-                        | 02/2019<br>-       | 02/2019     | 0/0                        |
| 358                                             | CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH                                                                        | 04/2008                       | 872.00<br>-                        | 12/2019<br>-       | 12/2019     | 0/0                        |
| 359                                             | CHHINDWARA-MANDLA FORT GC - [N22000481]SECR,MADHYA PRADESH                                                                      | 03/2011                       | 556.54<br>-                        | 03/2012<br>-       | 03/2020     | 0/0                        |
| 360                                             | GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE                                                                        | 02/1997                       | 511.86<br>-                        | 04/2020<br>-       | 04/2020     | 0/0                        |
| 361                                             | JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH                                                                      | 04/2015                       | 1,973.00<br>-                      | 03/2021<br>-       | 03/2021     | 0/0                        |
| 362                                             | WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA                                                             | 06/2018                       | 229.00<br>-                        | 12/2021<br>-       | 12/2021     | 0/0                        |
| 363                                             | ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH                                                                                  | 04/2015                       | 1,370.00<br>-                      | 12/2021<br>-       | 12/2021     | 0/0                        |
| 364                                             | KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM - [N22000482]SECR,CHHATISGARH                                                          | 04/2011                       | 1,471.93<br>-                      | 03/2022<br>-       | 03/2022     | 0/0                        |
| 365                                             | GEVRA ROAD PENDRA ROAD - [N22000488]SECR,CHHATISGARH                                                                            | 02/2014                       | 2,288.00<br>-                      | 03/2022<br>-       | 03/2022     | 0/0                        |
| 366                                             | RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA                                                            | 09/2016                       | 1,908.51<br>-                      | 03/2023<br>-       | 03/2023     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                             |                               |                                    |                    |             |                            |
|-------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|--------------------|-------------|----------------------------|
| SI.No                                           | Project                                                                                                                     | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Original / Revised | Anticipated | Milestones Achieved/ Total |
| 1                                               | 2                                                                                                                           | 3                             | 4                                  | 5                  | 6           | 7                          |
| 367                                             | CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH                                                             | 04/2005                       | 383.79<br>-                        | -<br>-             | -           | 0/0                        |
| 368                                             | KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]SECR,CHHATISGARH                                    | 04/2013                       | 3,055.00<br>-                      | 09/2018<br>-       | -           | 0/0                        |
|                                                 | <u>South Eastern Railway</u>                                                                                                |                               |                                    |                    |             |                            |
| 369                                             | DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND                                                          | 04/2010                       | 309.44<br>-                        | 12/2015<br>12/2018 | 02/2019     | 0/0                        |
| 370                                             | RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND                                            | 04/2012                       | 148.77<br>-                        | 12/2016<br>08/2018 | 09/2019     | 0/0                        |
| 371                                             | MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND                                                          | 04/2012                       | 258.20<br>-                        | -<br>12/2018       | 01/2020     | 0/0                        |
| 372                                             | ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA                                                               | 11/2015                       | 969.83<br>-                        | 03/2020<br>03/2020 | 06/2020     | 0/0                        |
| 373                                             | BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND                                                                       | 03/2016                       | 1,724.20<br>1,724.20               | 03/2021<br>03/2021 | 12/2021     | 0/0                        |
| 374                                             | TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER,WEST BENGAL | 01/1991                       | 1,013.45<br>1,013.45               | 12/2021<br>12/2021 | 12/2021     | 0/0                        |
| 375                                             | DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE                                                     | 04/2010                       | 651.00<br>-                        | 03/2015<br>03/2024 | 03/2024     | 0/0                        |
| 376                                             | MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE                                                                      | 04/2008                       | 466.48<br>-                        | -<br>12/2024       | 12/2024     | 0/0                        |
| 377                                             | RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA        | 04/1995                       | 524.43<br>-                        | 12/2021<br>12/2024 | 12/2024     | 0/0                        |
| 378                                             | BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL                                                                           | 04/2010                       | 267.37<br>-                        | -<br>03/2025       | 03/2025     | 0/0                        |
| 379                                             | MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL                                                                     | 04/2011                       | 276.69<br>-                        | -<br>03/2030       | 03/2030     | 0/0                        |
| 380                                             | BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL                                      | 04/1998                       | 1,027.40<br>1,966.70               | 03/2003<br>03/2030 | 03/2030     | 0/0                        |
| 381                                             | HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL                                                               | 04/1974                       | 393.46<br>154.30                   | 03/2007<br>03/2007 | -           | 0/0                        |
| 382                                             | TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL                                                               | 03/1984                       | 293.97<br>-                        | 06/2005<br>-       | -           | 0/0                        |
| 383                                             | BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL                                                            | 04/2011                       | 289.64<br>-                        | -<br>-             | -           | 0/0                        |
| 384                                             | CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA                                                           | 04/2010                       | 149.90<br>-                        | 03/2015<br>-       | -           | 0/0                        |
| 385                                             | ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR                                                                                | 04/2008                       | 633.87<br>-                        | -<br>-             | -           | 0/0                        |
|                                                 | <u>South Western Railway</u>                                                                                                |                               |                                    |                    |             |                            |
| 386                                             | YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE                                                                            | 05/2015                       | 860.43<br>860.43                   | 03/2020<br>03/2020 | 03/2020     | 0/0                        |
| 387                                             | KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA                                                    | 03/1996                       | 644.78<br>889.52                   | 03/2017<br>-       | 03/2020     | 0/0                        |
| 388                                             | MIRAJ-LONDA - [N22000327]SWR,MULTI STATE                                                                                    | 03/2015                       | 1,830.00<br>1,190.92               | -<br>03/2021       | 03/2021     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                            |                               |                                    |                    |             |                            |
|-------------------------------------------------|--------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|--------------------|-------------|----------------------------|
| SI.No                                           | Project                                                                                    | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Original / Revised | Anticipated | Milestones Achieved/ Total |
| 1                                               | 2                                                                                          | 3                             | 4                                  | 5                  | 6           | 7                          |
| 389                                             | HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE                                             | 03/2015                       | 1,614.59<br>1,870.41               | 03/2019<br>03/2021 | 03/2021     | 0/0                        |
| 390                                             | TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA                                 | 04/2011                       | 1,801.01<br>-                      | -<br>12/2023       | 12/2023     | 0/0                        |
| 391                                             | CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA              | 04/2013                       | 558.00<br>692.43                   | -<br>12/2023       | 12/2023     | 0/0                        |
| 392                                             | SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE                                 | 04/2013                       | 296.00<br>-                        | -<br>12/2023       | 12/2023     | 0/0                        |
| 393                                             | WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA                                            | 04/2011                       | 348.85<br>-                        | -<br>12/2023       | 12/2023     | 0/0                        |
| 394                                             | TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA                                       | 04/2011                       | 146.75<br>167.50                   | -<br>12/2023       | 12/2023     | 0/0                        |
| 395                                             | CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA                                   | 04/2013                       | 327.25<br>367.77                   | -<br>12/2023       | 12/2023     | 0/0                        |
| 396                                             | MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA                                             | 04/2012                       | 279.54<br>279.54                   | 03/2016<br>12/2023 | 12/2023     | 0/0                        |
| 397                                             | BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA                              | 04/1996                       | 1,382.78<br>1,382.78               | 03/2002<br>03/2024 | 03/2024     | 0/0                        |
| 398                                             | SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA                                              | 04/2011                       | 832.47<br>-                        | 03/2016<br>03/2024 | 03/2024     | 0/0                        |
| 399                                             | HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA                                            | 04/1997                       | 2,315.00<br>-                      | -<br>12/2024       | 12/2024     | 0/0                        |
| 400                                             | GADAG-WADI NL - [N22000299]SWR,KARNATAKA                                                   | 04/2013                       | 2,841.84<br>2,841.84               | 12/2018<br>12/2024 | 12/2024     | 0/0                        |
|                                                 | <u>Southern Railway</u>                                                                    |                               |                                    |                    |             |                            |
| 401                                             | ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU           | 02/1999                       | 257.00<br>-                        | 03/2018<br>-       | 03/2018     | 0/0                        |
| 402                                             | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU | 09/2007                       | 724.69<br>-                        | 02/2019<br>-       | 02/2019     | 0/0                        |
| 403                                             | ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU                                               | 04/2008                       | 151.84<br>-                        | 02/2019<br>-       | 02/2019     | 0/0                        |
| 404                                             | MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE                             | 04/2011                       | 120.70<br>-                        | 03/2019<br>-       | 03/2019     | 0/0                        |
| 405                                             | MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU                                          | 04/2008                       | 164.41<br>-                        | -<br>-             | 03/2020     | 0/0                        |
| 406                                             | OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU           | 10/2013                       | 187.26<br>-                        | 04/2014<br>-       | 03/2020     | 0/0                        |
| 407                                             | MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU               | 02/2015                       | 760.00<br>-                        | 03/2020<br>-       | 03/2020     | 0/0                        |
| 408                                             | MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU                         | 02/2015                       | 1,700.00<br>-                      | 03/2022<br>-       | 03/2022     | 0/0                        |
| 409                                             | TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU        | 02/2017                       | 1,567.00<br>-                      | 03/2024<br>-       | 03/2026     | 0/0                        |
| 410                                             | CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE                                    | 02/1996                       | 240.00<br>-                        | -<br>-             | -           | 0/0                        |
| 411                                             | KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU                                              | 02/1997                       | 155.55<br>-                        | -<br>-             | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                         |                               |                                    |                    |             |                            |
|-------------------------------------------------|---------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|--------------------|-------------|----------------------------|
|                                                 |                                                                                                         |                               | Date of Commissioning (Month/Year) |                    |             |                            |
| SI.No                                           | Project                                                                                                 | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Original / Revised | Anticipated | Milestones Achieved/ Total |
| 1                                               | 2                                                                                                       | 3                             | 4                                  | 5                  | 6           | 7                          |
| 412                                             | ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA                                                   | 10/1998                       | 1,566.00<br>-                      | -<br>-             | -           | 0/0                        |
| 413                                             | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU                            | 09/2006                       | 343.17<br>-                        | -<br>-             | -           | 0/0                        |
| 414                                             | TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU                                        | 09/2006                       | 227.40<br>-                        | -<br>-             | -           | 0/0                        |
| 415                                             | TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU                                                        | 09/2006                       | 582.83<br>-                        | -<br>-             | -           | 0/0                        |
| 416                                             | CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE                                          | 04/2008                       | 523.52<br>-                        | -<br>-             | -           | 0/0                        |
| 417                                             | SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU | 04/2013                       | 839.00<br>-                        | -<br>-             | -           | 0/0                        |
| 418                                             | CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU                                         | 04/1999                       | 198.68<br>-                        | -<br>-             | -           | 0/0                        |
| 419                                             | CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU                              | 04/1998                       | 271.24<br>-                        | -<br>-             | -           | 0/0                        |
| 420                                             | KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE                                                   | 04/2007                       | 270.14<br>-                        | -<br>-             | -           | 0/0                        |
| 421                                             | KUMBALAM-TURAVUR - [N22000191]SR,KERALA                                                                 | 04/2011                       | 252.96<br>-                        | -<br>-             | -           | 0/0                        |
| 422                                             | ERODE-PALANI - [N22000199]SR,TAMIL NADU                                                                 | 04/2008                       | 288.57<br>-                        | -<br>-             | -           | 0/0                        |
| 423                                             | CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA                                                           | 04/2006                       | 191.72<br>-                        | -<br>-             | -           | 0/0                        |
| 424                                             | ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA                                                               | 04/2010                       | 189.24<br>-                        | -<br>-             | -           | 0/0                        |
| 425                                             | TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA                                                  | 02/2015                       | 1,431.90<br>-                      | -<br>-             | -           | 0/0                        |
| 426                                             | TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA                                                     | 02/2015                       | 1,000.00<br>-                      | -<br>-             | -           | 0/0                        |
| 427                                             | MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION - [N22000439]SR,TAMIL NADU                               | 02/1997                       | 458.63<br>-                        | 03/2015<br>-       | -           | 0/0                        |
| 428                                             | TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION - [N22000440]SR,TAMIL NADU                               | 02/2000                       | 200.84<br>-                        | 03/2014<br>-       | -           | 0/0                        |
| 429                                             | THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU                | 02/1996                       | 268.87<br>-                        | 03/2005<br>-       | -           | 0/0                        |
| 430                                             | PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA                                      | 02/2012                       | 550.00<br>-                        | 03/2016<br>-       | -           | 0/0                        |
| 431                                             | VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]SR,TAMIL NADU                               | 02/2005                       | 600.00<br>600.00                   | 03/2010<br>-       | -           | 0/0                        |
| 432                                             | MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANAL ROAD) (62.05 KM) DOUBLING - [N22000450]SR,TAMIL NADU     | 02/2003                       | 199.55<br>-                        | 03/2009<br>-       | -           | 0/0                        |
| 433                                             | MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. - [N22000453]SR,TAMIL NADU                      | 02/2006                       | 208.00<br>-                        | 03/2012<br>-       | -           | 0/0                        |
| 434                                             | MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. - [N22000454]SR,KERALA                                    | 02/2005                       | 241.00<br>-                        | 03/2014<br>-       | -           | 0/0                        |
|                                                 | <u>West Central Railway</u>                                                                             |                               |                                    |                    |             |                            |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                     |                               |                                    |                                    |             |                            |
|-------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                             | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                     |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                   | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 435                                             | RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH                                                                       | 04/2001                       | 424.60<br>-                        | 03/2021<br>-                       | 03/2021     | 0/0                        |
|                                                 | <u>Western Railway</u>                                                                                                              |                               |                                    |                                    |             |                            |
| 436                                             | BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT                                                    | 04/2008                       | 318.24<br>-                        | 03/2012<br>-                       | 03/2019     | 0/0                        |
| 437                                             | BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT             | 02/1991                       | 551.51<br>-                        | 03/2019<br>-                       | 03/2019     | 0/0                        |
| 438                                             | AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT                                                                          | 04/2008                       | 829.74<br>416.86                   | 03/2020<br>03/2020                 | 03/2020     | 0/0                        |
| 439                                             | SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT                                                                                       | 04/2015                       | 1,002.39<br>-                      | 03/2021<br>03/2019                 | 03/2020     | 0/0                        |
| 440                                             | DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT                                 | 04/2017                       | 691.84<br>-                        | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 441                                             | INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH                                                                         | 04/2016                       | 700.00<br>-                        | 06/2020<br>-                       | 06/2020     | 0/0                        |
| 442                                             | RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH                                                                       | 04/2008                       | 3,503.69<br>2,473.40               | 03/2022<br>03/2019                 | 03/2022     | 0/0                        |
| 443                                             | CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE                                                                                   | 04/2007                       | 1,347.26<br>-                      | 03/2022<br>03/2019                 | 03/2022     | 0/0                        |
| 444                                             | DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE                                                        | 04/2007                       | 1,640.04<br>-                      | 03/2022<br>03/2019                 | 03/2022     | 0/0                        |
| 445                                             | RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT               | 04/1994                       | 320.66<br>1,378.12                 | 03/2019<br>03/2019                 | 03/2022     | 0/0                        |
| 446                                             | MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT                                                                          | 04/2011                       | 844.10<br>-                        | -<br>03/2022                       | 03/2023     | 0/0                        |
| 447                                             | BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT                                          | 04/2006                       | 117.36<br>196.95                   | 03/2011<br>-                       | -           | 0/0                        |
| 448                                             | GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT        | 03/2017                       | 243.60<br>-                        | -<br>-                             | -           | 0/0                        |
| 449                                             | MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA                                | 03/2010                       | 265.88<br>-                        | -<br>-                             | -           | 0/0                        |
| 450                                             | VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA    | 03/2012                       | 217.38<br>-                        | -<br>-                             | -           | 0/0                        |
| 451                                             | VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT        | 03/2012                       | 248.26<br>-                        | -<br>-                             | -           | 0/0                        |
| 452                                             | PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT                       | 03/2012                       | 153.83<br>-                        | -<br>-                             | -           | 0/0                        |
|                                                 |                                                                                                                                     |                               |                                    |                                    |             |                            |
|                                                 | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                                  |                               |                                    |                                    |             |                            |
|                                                 | <u>Ministry Of Road Transport And Highways</u>                                                                                      |                               |                                    |                                    |             |                            |
| 453                                             | WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN   | 02/2015                       | 383.40<br>-                        | 03/2015<br>-                       | 06/2019     | 0/0                        |
| 454                                             | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND | 06/2017                       | 282.08<br>-                        | 06/2019<br>-                       | 06/2019     | 0/0                        |
| 455                                             | RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2-LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MORTH,UTTARAKHAND  | 11/2017                       | 232.81<br>-                        | 11/2019<br>-                       | 11/2019     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                        |                               |                                    |                    |             |                            |
|-------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|--------------------|-------------|----------------------------|
|                                                 |                                                                                                                                        |                               | Date of Commissioning (Month/Year) |                    |             |                            |
| SI.No                                           | Project                                                                                                                                | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Original / Revised | Anticipated | Milestones Achieved/ Total |
| 1                                               | 2                                                                                                                                      | 3                             | 4                                  | 5                  | 6           | 7                          |
| 456                                             | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MORTH,UTTARAKHAND   | 11/2017                       | 283.51 -                           | 11/2019 -          | 11/2019     | 0/0                        |
| 457                                             | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MORTH,UTTARAKHAND    | 11/2017                       | 266.52 -                           | 11/2019 -          | 11/2019     | 0/0                        |
| 458                                             | Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MORTH,A & N ISLANDS  | 11/2017                       | 237.80 -                           | 11/2019 -          | 11/2019     | 0/0                        |
| 459                                             | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MORTH,A & N ISLANDS  | 11/2017                       | 257.34 -                           | 11/2019 12/2019    | 11/2019     | 0/0                        |
| 460                                             | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MORTH,UTTARAKHAND    | 12/2017                       | 257.34 -                           | 12/2019 -          | 12/2019     | 0/0                        |
| 461                                             | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MORTH,UTTARAKHAND    | 12/2017                       | 200.34 -                           | 12/2019 -          | 12/2019     | 0/0                        |
| 462                                             | WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MORTH,UTTARAKHAND    | 12/2017                       | 248.22 -                           | 12/2019 -          | 12/2019     | 0/0                        |
| 463                                             | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MORTH,UTTARAKHAND       | 02/2018                       | 418.88 -                           | 02/2020 -          | 02/2020     | 0/0                        |
| 464                                             | CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MORTH,UTTARAKHAND    | 05/2018                       | 248.00 -                           | 05/2020 -          | 05/2020     | 0/0                        |
| 465                                             | REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH  | 07/2015                       | 314.43 -                           | - -                | -           | 0/0                        |
| 466                                             | WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA     | 10/2015                       | 289.60 -                           | - -                | -           | 0/0                        |
| 467                                             | CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA    | 12/2011                       | 156.26 227.00                      | - -                | -           | 0/0                        |
| 468                                             | CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA    | 03/2011                       | 185.82 292.00                      | - -                | -           | 0/0                        |
| 469                                             | REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH    | 03/2015                       | 422.34 -                           | - -                | -           | 0/0                        |
| 470                                             | REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH | 10/2015                       | 480.21 -                           | - -                | -           | 0/0                        |
| 471                                             | WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN      | 10/2014                       | 269.22 -                           | 01/2015 -          | -           | 0/0                        |
| 472                                             | WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN                       | 10/2014                       | 257.09 -                           | 01/2015 -          | -           | 0/0                        |
| 473                                             | REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN                                       | 10/2013                       | 278.87 -                           | 05/2014 -          | -           | 0/0                        |
| 474                                             | REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN      | 01/1991                       | 376.52 -                           | 04/2014 -          | -           | 0/0                        |
| 475                                             | CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU     | 03/2015                       | 258.97 -                           | 08/2015 -          | -           | 0/0                        |
| 476                                             | REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU     | 03/2015                       | 157.18 162.00                      | 07/2015 -          | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                     |                               |                                    |                                    |             |                            |
|-------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                             | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                     |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                   | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 477                                             | CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU    | 11/2015                       | 154.14<br>-                        | 08/2015<br>-                       | -           | 0/0                        |
| 478                                             | CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH  | 03/2015                       | 629.74<br>-                        | -<br>-                             | -           | 0/0                        |
| 479                                             | CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH                  | 01/2014                       | 282.41<br>-                        | 03/2016<br>-                       | -           | 0/0                        |
| 480                                             | REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA | 01/2015                       | 225.81<br>-                        | -<br>-                             | -           | 0/0                        |
| 481                                             | WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN    | 12/2015                       | 621.43<br>-                        | 06/2018<br>-                       | -           | 0/0                        |
| 482                                             | STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA   | 03/2015                       | 165.67<br>-                        | 11/2015<br>-                       | -           | 0/0                        |
| 483                                             | STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA   | 03/2015                       | 159.12<br>-                        | 11/2015<br>-                       | -           | 0/0                        |
| 484                                             | STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH        | 10/2014                       | 227.74<br>-                        | 10/2016<br>-                       | -           | 0/0                        |
| 485                                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN   | 01/1991                       | 269.26<br>-                        | 10/2016<br>-                       | -           | 0/0                        |
| 486                                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA   | 01/1991                       | 219.40<br>-                        | 01/2018<br>-                       | -           | 0/0                        |
| 487                                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA      | 01/1991                       | 218.63<br>-                        | 10/2017<br>-                       | -           | 0/0                        |
| 488                                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR       | 01/1991                       | 675.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 489                                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL | 01/1991                       | 322.00<br>-                        | 03/2018<br>-                       | -           | 0/0                        |
| 490                                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR       | 01/1991                       | 282.41<br>-                        | 08/2016<br>-                       | -           | 0/0                        |
| 491                                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR       | 01/1991                       | 358.22<br>-                        | 10/2016<br>-                       | -           | 0/0                        |
| 492                                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARALI - [N24000406]MORTH,RAJASTHAN     | 01/1991                       | 208.87<br>-                        | 05/2016<br>-                       | -           | 0/0                        |
| 493                                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA      | 01/1991                       | 229.41<br>-                        | 05/2018<br>-                       | -           | 0/0                        |
| 494                                             | CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA          | 10/2015                       | 936.40<br>-                        | -<br>-                             | -           | 0/0                        |
| 495                                             | WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH                                 | 05/2013                       | 164.54<br>-                        | 08/2015<br>-                       | -           | 0/0                        |
| 496                                             | WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH                            | 12/2014                       | 207.88<br>-                        | -<br>-                             | -           | 0/0                        |
| 497                                             | WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA         | 12/2015                       | 773.98<br>-                        | -<br>-                             | -           | 0/0                        |
| 498                                             | WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA         | 12/2015                       | 819.95<br>-                        | -<br>-                             | -           | 0/0                        |
| 499                                             | REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR                       | 01/1991                       | 478.35<br>-                        | -<br>-                             | -           | 0/0                        |



## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                     |                               |                                    |                                    |             |                            |
|-------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                             | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                     |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                   | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 500                                             | WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH                           | 12/2014                       | 207.88<br>-                        | -<br>-                             | -           | 0/0                        |
| 501                                             | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR       | 10/2014                       | 377.64<br>-                        | 03/2014<br>-                       | -           | 0/0                        |
| 502                                             | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR       | 10/2013                       | 278.39<br>-                        | 08/2014<br>-                       | -           | 0/0                        |
| 503                                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR       | 01/2013                       | 322.01<br>-                        | 08/2014<br>-                       | -           | 0/0                        |
| 504                                             | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR       | 11/2013                       | 683.83<br>-                        | 07/2016<br>-                       | -           | 0/0                        |
| 505                                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR        | 02/2014                       | 665.50<br>-                        | 07/2016<br>-                       | -           | 0/0                        |
| 506                                             | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR       | 02/2016                       | 178.85<br>-                        | 05/2016<br>-                       | -           | 0/0                        |
| 507                                             | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR       | 02/2016                       | 369.77<br>-                        | 06/2016<br>-                       | -           | 0/0                        |
| 508                                             | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR       | 02/2016                       | 553.30<br>-                        | 05/2016<br>-                       | -           | 0/0                        |
| 509                                             | FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR         | 01/2014                       | 1,408.85<br>-                      | 10/2016<br>-                       | -           | 0/0                        |
| 510                                             | STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV - [N24000580]MORTH,BIHAR      | 03/2015                       | 206.80<br>-                        | 07/2016<br>-                       | -           | 0/0                        |
| 511                                             | CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR                        | 08/2015                       | 288.24<br>-                        | 11/2015<br>-                       | -           | 0/0                        |
| 512                                             | REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR       | 08/2016                       | 1,742.01<br>-                      | 12/2016<br>-                       | -           | 0/0                        |
| 513                                             | WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA      | 03/2014                       | 191.50<br>192.00                   | 05/2016<br>-                       | -           | 0/0                        |
| 514                                             | WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]MORTH,ODISHA       | 01/2015                       | 326.63<br>327.00                   | 04/2018<br>-                       | -           | 0/0                        |
| 515                                             | WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA         | 02/2015                       | 239.91<br>240.00                   | 10/2017<br>-                       | -           | 0/0                        |
| 516                                             | WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA       | 03/2015                       | 226.31<br>226.00                   | 10/2017<br>-                       | -           | 0/0                        |
| 517                                             | IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA       | 12/2013                       | 319.80<br>320.00                   | 05/2016<br>-                       | -           | 0/0                        |
| 518                                             | REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA       | 07/2014                       | 342.05<br>342.00                   | 01/2017<br>-                       | -           | 0/0                        |
| 519                                             | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA      | 08/2013                       | 171.96<br>172.00                   | 06/2016<br>-                       | -           | 0/0                        |
| 520                                             | WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA      | 06/2016                       | 157.30<br>157.00                   | 06/2018<br>-                       | -           | 0/0                        |
| 521                                             | WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA      | 03/2014                       | 162.51<br>163.00                   | 05/2016<br>-                       | -           | 0/0                        |
| 522                                             | REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND | 02/2018                       | 293.68<br>-                        | -<br>-                             | -           | 0/0                        |
| 523                                             | REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND | 03/2018                       | 460.73<br>-                        | -<br>-                             | -           | 0/0                        |



## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                             |                               |                                    |                    |             |                            |
|-------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|--------------------|-------------|----------------------------|
|                                                 |                                                                                                                                             |                               | Date of Commissioning (Month/Year) |                    |             |                            |
| SI.No                                           | Project                                                                                                                                     | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Original / Revised | Anticipated | Milestones Achieved/ Total |
| 1                                               | 2                                                                                                                                           | 3                             | 4                                  | 5                  | 6           | 7                          |
|                                                 | <b>National Highways And Infrastructure Development Corporation Ltd.</b>                                                                    |                               |                                    |                    |             |                            |
| 524                                             | 4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM                   | 12/2015                       | 289.99 -                           | 12/2018 -          | 12/2018     | 0/0                        |
| 525                                             | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND           | 03/2016                       | 373.07 -                           | 08/2016 -          | 08/2019     | 0/0                        |
| 526                                             | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND           | 03/2016                       | 396.52 -                           | 08/2016 -          | 08/2019     | 0/0                        |
| 527                                             | FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND           | 03/2016                       | 429.52 -                           | 08/2016 -          | 08/2019     | 0/0                        |
| 528                                             | CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH                                 | 12/2016                       | 138.93<br>155.00                   | 01/2017 -          | 01/2020     | 0/0                        |
| 529                                             | 4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM                             | 12/2015                       | 223.30 -                           | 06/2018 -          | -           | 0/0                        |
| 530                                             | 4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM                                       | 01/1991                       | 520.01 -                           | - -                | -           | 0/0                        |
| 531                                             | 2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH | 01/2016                       | 183.65 -                           | 11/2016 -          | -           | 0/0                        |
| 532                                             | CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD( NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH  | 04/2016                       | 245.79 -                           | - -                | -           | 0/0                        |
| 533                                             | FUNDED ) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH  | 11/2015                       | 434.06 -                           | - -                | -           | 0/0                        |
| 534                                             | CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH      | 01/2017                       | 1,253.10 -                         | 03/2017 -          | -           | 0/0                        |
| 535                                             | TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH  | 03/2017                       | 284.09 -                           | 04/2017 -          | -           | 0/0                        |
| 536                                             | TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH  | 02/2017                       | 195.23 -                           | 04/2017 -          | -           | 0/0                        |
| 537                                             | TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH  | 02/2017                       | 203.36 -                           | 04/2017 -          | -           | 0/0                        |
| 538                                             | TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH   | 01/2017                       | 194.66 -                           | 04/2017 -          | -           | 0/0                        |
| 539                                             | TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH   | 02/2017                       | 168.32 -                           | 04/2017 -          | -           | 0/0                        |
| 540                                             | TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH   | 02/2017                       | 180.57 -                           | 04/2017 -          | -           | 0/0                        |
| 541                                             | CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH  | 02/2017                       | 216.71 -                           | 04/2017 -          | -           | 0/0                        |
| 542                                             | CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH  | 02/2017                       | 167.28 -                           | 04/2017 -          | -           | 0/0                        |
| 543                                             | CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND           | 02/2017                       | 507.68 -                           | 04/2017 -          | -           | 0/0                        |
| 544                                             | TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH   | 01/2017                       | 198.22 -                           | 04/2017 -          | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                        |                               |                                    |                    |             |                            |
|-------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|--------------------|-------------|----------------------------|
|                                                 |                                                                                                                                        |                               | Date of Commissioning (Month/Year) |                    |             |                            |
| Sl.No                                           | Project                                                                                                                                | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Original / Revised | Anticipated | Milestones Achieved/ Total |
| 1                                               | 2                                                                                                                                      | 3                             | 4                                  | 5                  | 6           | 7                          |
| 545                                             | RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM                                                                         | 04/2017                       | 388.00<br>-                        | 10/2017<br>-       | -           | 0/0                        |
| 546                                             | CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 ( - [N24000744]NHIDCL,A & N ISLANDS | 03/2015                       | 262.97<br>-                        | 10/2018<br>-       | -           | 0/0                        |
| 547                                             | (I) CONSTRUCTION OF FOUR/SIX LANEING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND     | 02/2017                       | 387.00<br>-                        | 09/2018<br>-       | -           | 0/0                        |
| 548                                             | (II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND       | 03/2018                       | 500.09<br>-                        | 09/2018<br>-       | -           | 0/0                        |
| 549                                             | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND       | 03/2018                       | 339.57<br>-                        | 09/2018<br>-       | -           | 0/0                        |
| 550                                             | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND       | 03/2018                       | 239.30<br>-                        | 09/2018<br>-       | -           | 0/0                        |
| 551                                             | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND       | 03/2018                       | 285.68<br>-                        | 09/2018<br>-       | -           | 0/0                        |
| 552                                             | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND       | 03/2018                       | 315.03<br>-                        | 09/2018<br>-       | -           | 0/0                        |
| 553                                             | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND       | 03/2018                       | 240.64<br>-                        | 09/2018<br>-       | -           | 0/0                        |
| 554                                             | CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND      | 03/2018                       | 237.72<br>-                        | 09/2018<br>-       | -           | 0/0                        |
| 555                                             | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND      | 03/2018                       | 251.97<br>-                        | 09/2018<br>-       | -           | 0/0                        |
| 556                                             | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND       | 03/2018                       | 282.98<br>-                        | 09/2018<br>-       | -           | 0/0                        |
| 557                                             | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND      | 03/2018                       | 215.12<br>-                        | 09/2018<br>-       | -           | 0/0                        |
| 558                                             | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND      | 03/2018                       | 215.79<br>-                        | 09/2018<br>-       | -           | 0/0                        |
| 559                                             | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND      | 03/2018                       | 272.89<br>-                        | 09/2018<br>-       | -           | 0/0                        |
| 560                                             | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND      | 03/2018                       | 323.98<br>-                        | 09/2018<br>-       | -           | 0/0                        |
| 561                                             | CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM        | 04/2017                       | 318.42<br>-                        | 11/2017<br>-       | -           | 0/0                        |
| 562                                             | CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM        | 03/2017                       | 375.80<br>-                        | -<br>-             | -           | 0/0                        |
| 563                                             | CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM        | 11/2017                       | 290.05<br>-                        | 11/2017<br>-       | -           | 0/0                        |
| 564                                             | CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM        | 03/2018                       | 264.84<br>-                        | 06/2018<br>-       | -           | 0/0                        |
| 565                                             | CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL   | 03/2017                       | 158.65<br>-                        | 06/2018<br>-       | -           | 0/0                        |
| 566                                             | WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA     | 04/2017                       | 553.51<br>-                        | -<br>-             | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                 |                               |                                    |                                    |             |                            |
|-------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                         | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                 |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                               | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 567                                             | FOUR LANING OF NH-52 FROM END OF BISWANATH CHARALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM   | 03/2015                       | 829.00 -                           | 01/2016 -                          | -           | 0/0                        |
|                                                 | <u>National Highways Authority Of India</u>                                                                                     |                               |                                    |                                    |             |                            |
| 568                                             | BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA         | 03/2016                       | 197.69 -                           | 07/2018 -                          | 07/2018     | 0/0                        |
| 569                                             | FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND                                                               | 08/2016                       | 323.72 -                           | 08/2018 -                          | 08/2018     | 0/0                        |
| 570                                             | FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH                          | 01/2016                       | 1,134.97 -                         | 11/2018 -                          | 11/2018     | 0/0                        |
| 571                                             | 2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU                                          | 04/2012                       | 624.00 -                           | 04/2014 -                          | 12/2019     | 0/0                        |
| 572                                             | 4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND                                  | 11/2012                       | 605.84 -                           | 07/2018 -                          | 07/2018     | 0/0                        |
| 573                                             | MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM                                               | 12/2003                       | 167.64 -                           | 11/2008 -                          | 09/2018     | 0/0                        |
| 574                                             | 2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH                                                        | 07/2012                       | 291.36 -                           | 01/2014 -                          | 09/2018     | 0/0                        |
| 575                                             | DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA                                                                       | 04/2007                       | 486.00 -                           | 05/2010 -                          | 10/2018     | 0/0                        |
| 576                                             | INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH                                                                        | 10/2010                       | 1,175.00 -                         | 04/2013 -                          | 11/2018     | 0/0                        |
| 577                                             | TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN | 07/2016                       | 331.46 -                           | 10/2018 -                          | 11/2018     | 0/0                        |
| 578                                             | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM                                                  | 12/2003                       | 280.00 -                           | 02/2009 -                          | 12/2018     | 0/0                        |
| 579                                             | SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU                           | 09/2011                       | 1,250.00 -                         | 12/2013 -                          | 12/2018     | 0/0                        |
| 580                                             | KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT                                                                                  | 01/2011                       | 953.88 -                           | 07/2013 -                          | 12/2018     | 0/0                        |
| 581                                             | TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU                                                 | 05/2010                       | 374.00 -                           | 05/2013 -                          | 12/2018     | 0/0                        |
| 582                                             | 2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU                                                     | 09/2011                       | 485.00 -                           | 08/2013 -                          | 12/2018     | 0/0                        |
| 583                                             | TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH                                                                 | 04/2011                       | 571.00 -                           | 10/2013 -                          | 12/2018     | 0/0                        |
| 584                                             | PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR                                                                  | 09/2011                       | 574.00 -                           | 03/2014 -                          | 12/2018     | 0/0                        |
| 585                                             | 2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR                                                                     | 05/2011                       | 511.54 -                           | 11/2013 -                          | 12/2018     | 0/0                        |
| 586                                             | TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 ( NEW NH NO -50) - [N24000342]NHAI,KARNATAKA | 05/2015                       | 709.00 -                           | 09/2017 -                          | 12/2018     | 0/0                        |
| 587                                             | 4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA                                                             | 12/2015                       | 602.95 -                           | 06/2016 -                          | 12/2018     | 0/0                        |
| 588                                             | 4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA                                                     | 01/2015                       | 972.50 -                           | 07/2017 -                          | 12/2018     | 0/0                        |
| 589                                             | FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH                                                                | 05/2013                       | 1,055.00 -                         | 11/2015 -                          | 12/2018     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                       |                               |                                    |                    |             |                            |
|-------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|--------------------|-------------|----------------------------|
|                                                 |                                                                                                                                       |                               | Date of Commissioning (Month/Year) |                    |             |                            |
| Sl.No                                           | Project                                                                                                                               | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Original / Revised | Anticipated | Milestones Achieved/ Total |
| 1                                               | 2                                                                                                                                     | 3                             | 4                                  | 5                  | 6           | 7                          |
| 590                                             | FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA                                                                     | 07/2015                       | 1,871.34<br>-                      | 01/2018<br>-       | 12/2018     | 0/0                        |
| 591                                             | FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA                    | 04/2010                       | 1,170.52<br>-                      | 06/2012<br>-       | 12/2018     | 0/0                        |
| 592                                             | TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR                                                         | 08/2015                       | 516.13<br>-                        | 04/2018<br>-       | 12/2018     | 0/0                        |
| 593                                             | SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM                                                                                     | 12/2003                       | 245.00<br>174.34                   | 03/2008<br>-       | 01/2019     | 0/0                        |
| 594                                             | JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA                                                                                         | 01/2011                       | 536.00<br>-                        | 01/2014<br>-       | 01/2019     | 0/0                        |
| 595                                             | PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN                                              | 09/2015                       | 567.51<br>-                        | 03/2018<br>-       | 01/2019     | 0/0                        |
| 596                                             | 2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN                                                                    | 10/2015                       | 597.00<br>-                        | 10/2017<br>-       | 01/2019     | 0/0                        |
| 597                                             | 6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH                                                                      | 07/2015                       | 1,657.20<br>-                      | 01/2019<br>-       | 01/2019     | 0/0                        |
| 598                                             | FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH | 06/2015                       | 1,583.79<br>-                      | 01/2019<br>-       | 01/2019     | 0/0                        |
| 599                                             | BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH                                  | 08/2016                       | 227.49<br>-                        | 01/2019<br>-       | 01/2019     | 0/0                        |
| 600                                             | DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM                                                                       | 12/2003                       | 160.00<br>-                        | 05/2008<br>-       | 02/2019     | 0/0                        |
| 601                                             | 2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN      | 11/2012                       | 530.07<br>-                        | 08/2016<br>-       | 02/2019     | 0/0                        |
| 602                                             | 2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH                              | 02/2016                       | 273.20<br>-                        | 02/2019<br>-       | 02/2019     | 0/0                        |
| 603                                             | 2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN                                                             | 08/2016                       | 320.30<br>-                        | 01/2019<br>-       | 02/2019     | 0/0                        |
| 604                                             | MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM                                                           | 12/2003                       | 199.81<br>-                        | 04/2009<br>-       | 03/2019     | 0/0                        |
| 605                                             | NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM                                                                                        | 12/2003                       | 208.00<br>-                        | 04/2008<br>-       | 03/2019     | 0/0                        |
| 606                                             | SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA                                                  | 02/2010                       | 617.00<br>-                        | 08/2012<br>-       | 03/2019     | 0/0                        |
| 607                                             | QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR                                                          | 07/2010                       | 1,987.00<br>-                      | 07/2015<br>-       | 03/2019     | 0/0                        |
| 608                                             | PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA                                                                                             | 03/2012                       | 1,410.00<br>-                      | 09/2014<br>-       | 03/2019     | 0/0                        |
| 609                                             | TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN                                                       | 09/2014                       | 425.19<br>-                        | 09/2016<br>-       | 03/2019     | 0/0                        |
| 610                                             | CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270 (D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 ( D - [N24000432]NHAI,MAHARASHTRA    | 09/2015                       | 414.51<br>-                        | 05/2018<br>-       | 03/2019     | 0/0                        |
| 611                                             | CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA    | 12/2015                       | 649.50<br>-                        | 03/2019<br>-       | 03/2019     | 0/0                        |
| 612                                             | BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN       | 08/2014                       | 822.90<br>-                        | 04/2018<br>-       | 03/2019     | 0/0                        |
| 613                                             | 4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA                                                                   | 01/2016                       | 574.28<br>-                        | 07/2018<br>-       | 03/2019     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                      |                               |                                    |                                    |             |                            |
|-------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                      |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                    | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 614                                             | 4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA                                                        | 05/2014                       | 1,655.01 -                         | 08/2016 -                          | 03/2019     | 0/0                        |
| 615                                             | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH                                                | 03/2015                       | 795.76 -                           | - -                                | 03/2019     | 0/0                        |
| 616                                             | GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN                                                                   | 02/2008                       | 1,673.70 -                         | 10/2011<br>09/2017                 | 03/2019     | 0/0                        |
| 617                                             | FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH                                                                    | 09/2015                       | 934.46 -                           | 03/2018 -                          | 03/2019     | 0/0                        |
| 618                                             | FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB                                                                 | 09/2014                       | 479.00 -                           | - -                                | 03/2019     | 0/0                        |
| 619                                             | FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH                                                                 | 03/2015                       | 928.83 -                           | - -                                | 03/2019     | 0/0                        |
| 620                                             | FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH | 06/2015                       | 1,012.90 -                         | 03/2016 -                          | 03/2019     | 0/0                        |
| 621                                             | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH                                                | 03/2015                       | 810.22 -                           | - -                                | 03/2019     | 0/0                        |
| 622                                             | SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL                                                                      | 04/2014                       | 1,665.00 -                         | - -                                | 03/2019     | 0/0                        |
| 623                                             | TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA                                     | 12/2015                       | 479.20 -                           | 05/2018 -                          | 03/2019     | 0/0                        |
| 624                                             | TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN                                          | 08/2015                       | 275.90 -                           | - -                                | 03/2019     | 0/0                        |
| 625                                             | TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR                                                                     | 08/2015                       | 854.80 -                           | - -                                | 03/2019     | 0/0                        |
| 626                                             | 4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND                                                     | 02/2016                       | 997.15 -                           | 03/2019 -                          | 03/2019     | 0/0                        |
| 627                                             | SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT       | 05/2016                       | 425.60 -                           | - -                                | 03/2019     | 0/0                        |
| 628                                             | HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA                                                                       | 08/2016                       | 1,167.42 -                         | 03/2019 -                          | 03/2019     | 0/0                        |
| 629                                             | NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM                                                                                      | 12/2003                       | 225.00 -                           | 06/2008 -                          | 04/2019     | 0/0                        |
| 630                                             | BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM                                                                                   | 12/2003                       | 217.61 -                           | 04/2010 -                          | 04/2019     | 0/0                        |
| 631                                             | CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH                                                      | 11/2010                       | 1,585.00 -                         | 05/2013 -                          | 04/2019     | 0/0                        |
| 632                                             | FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH                                 | 11/2013                       | 1,916.79 -                         | 11/2016 -                          | 04/2019     | 0/0                        |
| 633                                             | CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 ( OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA                    | 10/2015                       | 593.26 -                           | 05/2018 -                          | 04/2019     | 0/0                        |
| 634                                             | 8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA                                                                       | 07/2015                       | 2,128.72 -                         | 04/2019 -                          | 04/2019     | 0/0                        |
| 635                                             | 6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA                      | 08/2015                       | 505.00 -                           | 05/2018 -                          | 04/2019     | 0/0                        |
| 636                                             | 4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA                                                        | 06/2015                       | 845.24 -                           | - -                                | 04/2019     | 0/0                        |
| 637                                             | IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB            | 09/2015                       | 273.06 -                           | - -                                | 04/2019     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                      |                               |                                    |                                    |             |                            |
|-------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                      |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                    | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 638                                             | FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR                                                                  | 12/2015                       | 1,041.10<br>-                      | 04/2019<br>-                       | 04/2019     | 0/0                        |
| 639                                             | FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA                                                                      | 03/2015                       | 1,388.00<br>-                      | 08/2018<br>-                       | 04/2019     | 0/0                        |
| 640                                             | FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB                                                                          | 10/2015                       | 447.29<br>-                        | 12/2017<br>-                       | 04/2019     | 0/0                        |
| 641                                             | ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH                                      | 03/2016                       | 676.73<br>-                        | 04/2019<br>-                       | 04/2019     | 0/0                        |
| 642                                             | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH                 | 03/2016                       | 1,587.49<br>-                      | 04/2019<br>-                       | 04/2019     | 0/0                        |
| 643                                             | CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL                                                       | 03/2016                       | 229.37<br>-                        | 11/2018<br>-                       | 04/2019     | 0/0                        |
| 644                                             | FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH | 03/2016                       | 899.00<br>-                        | 04/2019<br>-                       | 04/2019     | 0/0                        |
| 645                                             | FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU    | 02/2016                       | 641.17<br>-                        | 07/2018<br>-                       | 04/2019     | 0/0                        |
| 646                                             | 4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA        | 04/2016                       | 804.97<br>-                        | 06/2018<br>-                       | 04/2019     | 0/0                        |
| 647                                             | FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU    | 03/2016                       | 641.17<br>-                        | 07/2016<br>-                       | 04/2019     | 0/0                        |
| 648                                             | 6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL                                                                 | 04/2012                       | 1,396.18<br>-                      | 09/2014<br>-                       | 05/2019     | 0/0                        |
| 649                                             | KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL                                                                                 | 02/2012                       | 702.16<br>-                        | 07/2014<br>-                       | 05/2019     | 0/0                        |
| 650                                             | FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU         | 05/2015                       | 1,387.11<br>-                      | 11/2017<br>-                       | 05/2019     | 0/0                        |
| 651                                             | 4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA                                                                 | 07/2015                       | 2,288.18<br>-                      | 05/2019<br>-                       | 05/2019     | 0/0                        |
| 652                                             | CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 ( - [N24000435]NHAI,MAHARASHTRA     | 10/2015                       | 531.13<br>-                        | 05/2018<br>-                       | 05/2019     | 0/0                        |
| 653                                             | 4 LANING OF FAGNE - MAH-GUJ BORDER ( PKG-3) - [N24000439]NHAI,MAHARASHTRA                                                            | 07/2015                       | 1,885.74<br>-                      | 05/2019<br>-                       | 05/2019     | 0/0                        |
| 654                                             | 4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI ( KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL                             | 12/2015                       | 1,083.00<br>-                      | 06/2018<br>-                       | 05/2019     | 0/0                        |
| 655                                             | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH                                                 | 03/2015                       | 794.30<br>-                        | -<br>-                             | 05/2019     | 0/0                        |
| 656                                             | DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH                                                       | 01/2016                       | 701.12<br>-                        | 05/2019<br>-                       | 05/2019     | 0/0                        |
| 657                                             | CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA       | 09/2016                       | 1,004.67<br>-                      | 05/2019<br>-                       | 05/2019     | 0/0                        |
| 658                                             | SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA   | 11/2016                       | 290.73<br>-                        | -<br>-                             | 05/2019     | 0/0                        |
| 659                                             | CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA   | 01/2017                       | 244.90<br>-                        | 05/2019<br>-                       | 05/2019     | 0/0                        |
| 660                                             | DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA       | 03/2017                       | 296.19<br>-                        | 03/2020<br>-                       | 05/2019     | 0/0                        |
| 661                                             | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA                                                                | 05/2009                       | 1,108.00<br>-                      | 11/2011<br>-                       | 06/2019     | 0/0                        |



## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                   |                               |                                    |                                    |             |                            |
|-------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                           | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                   |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                 | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 662                                             | PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA                                                                                   | 10/2010                       | 1,724.55<br>-                      | 03/2013<br>-                       | 06/2019     | 0/0                        |
| 663                                             | PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR                                                                                        | 08/2010                       | 671.30<br>-                        | 02/2013<br>-                       | 06/2019     | 0/0                        |
| 664                                             | 4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR                                                                               | 01/2011                       | 575.00<br>-                        | 07/2013<br>-                       | 06/2019     | 0/0                        |
| 665                                             | 4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL                                                                         | 02/2011                       | 1,078.84<br>-                      | 08/2013<br>-                       | 06/2019     | 0/0                        |
| 666                                             | PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA                                                                                      | 12/2011                       | 942.69<br>-                        | 06/2014<br>-                       | 06/2019     | 0/0                        |
| 667                                             | 4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA                                                 | 04/2014                       | 1,266.60<br>-                      | 09/2016<br>-                       | 06/2019     | 0/0                        |
| 668                                             | TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU                                                       | 06/2015                       | 563.92<br>-                        | 12/2017<br>-                       | 06/2019     | 0/0                        |
| 669                                             | 4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA                                                 | 06/2014                       | 923.04<br>-                        | 11/2016<br>-                       | 06/2019     | 0/0                        |
| 670                                             | FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH                                                                     | 12/2015                       | 596.67<br>-                        | 05/2018<br>-                       | 06/2019     | 0/0                        |
| 671                                             | FOUR / SIX LANING OF RAIPUR - SIMGA ( PKG-1) - [N24000510]NHAI,CHHATISGARH                                                        | 12/2015                       | 726.67<br>-                        | 04/2018<br>-                       | 06/2019     | 0/0                        |
| 672                                             | DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH                             | 01/2016                       | 1,081.57<br>-                      | 06/2019<br>-                       | 06/2019     | 0/0                        |
| 673                                             | JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA                                                                  | 02/2016                       | 1,069.65<br>-                      | -<br>-                             | 06/2019     | 0/0                        |
| 674                                             | FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU | 02/2016                       | 707.82<br>-                        | 08/2018<br>-                       | 06/2019     | 0/0                        |
| 675                                             | BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR                                                           | 05/2015                       | 581.84<br>-                        | 05/2017<br>-                       | 06/2019     | 0/0                        |
| 676                                             | 4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA     | 03/2017                       | 639.79<br>-                        | 03/2020<br>-                       | 06/2019     | 0/0                        |
| 677                                             | 4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND                                      | 03/2017                       | 165.50<br>-                        | 03/2020<br>-                       | 06/2019     | 0/0                        |
| 678                                             | 4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND                            | 03/2017                       | 239.68<br>-                        | 03/2020<br>-                       | 06/2019     | 0/0                        |
| 679                                             | HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND                                                                | 11/2011                       | 478.51<br>-                        | 10/2013<br>-                       | 07/2019     | 0/0                        |
| 680                                             | FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA                                                                     | 12/2015                       | 1,423.96<br>-                      | 11/2018<br>-                       | 07/2019     | 0/0                        |
| 681                                             | 4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA                                        | 03/2016                       | 701.40<br>-                        | 03/2019<br>-                       | 07/2019     | 0/0                        |
| 682                                             | NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA                                                                          | 03/2016                       | 546.00<br>-                        | 07/2019<br>-                       | 07/2019     | 0/0                        |
| 683                                             | NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA                                                                          | 03/2016                       | 591.66<br>-                        | 07/2019<br>-                       | 07/2019     | 0/0                        |
| 684                                             | FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT    | 05/2016                       | 998.18<br>-                        | -<br>-                             | 08/2019     | 0/0                        |
| 685                                             | FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT    | 05/2016                       | 763.08<br>-                        | -<br>-                             | 08/2019     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                    |                               |                                    |                    |             |                            |
|-------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|--------------------|-------------|----------------------------|
|                                                 |                                                                                                                                    |                               | Date of Commissioning (Month/Year) |                    |             |                            |
| Sl.No                                           | Project                                                                                                                            | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Original / Revised | Anticipated | Milestones Achieved/ Total |
| 1                                               | 2                                                                                                                                  | 3                             | 4                                  | 5                  | 6           | 7                          |
| 686                                             | CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA                                                          | 08/2016                       | 248.97 -                           | 05/2019 -          | 08/2019     | 0/0                        |
| 687                                             | DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA      | 09/2016                       | 2,510.04 -                         | 08/2019 -          | 08/2019     | 0/0                        |
| 688                                             | TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA   | 09/2016                       | 950.69 -                           | 08/2019 -          | 08/2019     | 0/0                        |
| 689                                             | FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT     | 05/2016                       | 723.64 -                           | - -                | 09/2019     | 0/0                        |
| 690                                             | TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN                                                      | 06/2016                       | 637.18 -                           | 06/2019 -          | 09/2019     | 0/0                        |
| 691                                             | FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN                          | 06/2016                       | 649.00 -                           | 06/2019 -          | 09/2019     | 0/0                        |
| 692                                             | 4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB        | 08/2016                       | 1,388.34 -                         | 09/2019 -          | 09/2019     | 0/0                        |
| 693                                             | FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL | 09/2016                       | 767.03 -                           | 08/2018 -          | 09/2019     | 0/0                        |
| 694                                             | 4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA | 11/2016                       | 400.25 -                           | 03/2019 -          | 09/2019     | 0/0                        |
| 695                                             | 2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT                                                    | 12/2016                       | 417.19 -                           | - -                | 09/2019     | 0/0                        |
| 696                                             | FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR                                              | 12/2015                       | 2,136.97 -                         | 12/2018 -          | 10/2019     | 0/0                        |
| 697                                             | TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR                                                      | 08/2015                       | 399.54 -                           | 04/2019 -          | 10/2019     | 0/0                        |
| 698                                             | FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND  | 03/2016                       | 720.00 -                           | - -                | 10/2019     | 0/0                        |
| 699                                             | FOUR LANING OF TALAJA - MAHUA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT      | 05/2016                       | 834.64 -                           | - -                | 10/2019     | 0/0                        |
| 700                                             | FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA                                                                    | 12/2015                       | 752.28 -                           | - -                | 11/2019     | 0/0                        |
| 701                                             | FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN     | 06/2016                       | 763.23 -                           | 06/2019 -          | 11/2019     | 0/0                        |
| 702                                             | 4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN                                             | 07/2016                       | 688.70 -                           | - -                | 11/2019     | 0/0                        |
| 703                                             | 4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH                                     | 08/2016                       | 2,016.00 -                         | 04/2019 -          | 11/2019     | 0/0                        |
| 704                                             | 4-LANNING OF KODEBAD-DHARTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA | 11/2016                       | 446.17 -                           | 03/2019 -          | 11/2019     | 0/0                        |
| 705                                             | FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH                        | 10/2016                       | 447.75 -                           | - -                | 11/2019     | 0/0                        |
| 706                                             | SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN                                               | 04/2017                       | 894.00 -                           | 04/2020 -          | 11/2019     | 0/0                        |
| 707                                             | FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH    | 06/2017                       | 648.33 -                           | 06/2017 -          | 11/2019     | 0/0                        |
| 708                                             | VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE                                                              | 09/2011                       | 2,848.00 -                         | 03/2014 -          | 12/2019     | 0/0                        |
| 709                                             | MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE                                                                               | 09/2011                       | 754.00 -                           | 03/2013 -          | 12/2019     | 0/0                        |



## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                        |                               |                                    |                                    |             |                            |
|-------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                                | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                        |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                      | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 710                                             | FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR                                                         | 12/2015                       | 1,167.45<br>-                      | -<br>-                             | 12/2019     | 0/0                        |
| 711                                             | CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT                                                                      | 05/2016                       | 364.56<br>-                        | -<br>-                             | 12/2019     | 0/0                        |
| 712                                             | TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS- WEST BENGAL BORDER SECTION OF NH - [N24000594]NHAI, JHARKHAND       | 07/2016                       | 458.03<br>-                        | -<br>-                             | 12/2019     | 0/0                        |
| 713                                             | SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI, RAJASTHAN      | 09/2016                       | 1,100.19<br>-                      | -<br>-                             | 12/2019     | 0/0                        |
| 714                                             | CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL                                                                        | 10/2015                       | 361.15<br>-                        | -<br>-                             | 01/2020     | 0/0                        |
| 715                                             | FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI, BIHAR                                                                             | 08/2015                       | 814.04<br>-                        | -<br>-                             | 01/2020     | 0/0                        |
| 716                                             | 4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT                              | 07/2016                       | 829.97<br>-                        | -<br>-                             | 01/2020     | 0/0                        |
| 717                                             | FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI, MADHYA PRADESH  | 10/2017                       | 639.97<br>-                        | 10/2017<br>-                       | 01/2020     | 0/0                        |
| 718                                             | REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI, PUNJAB         | 03/2018                       | 196.05<br>-                        | -<br>-                             | 01/2020     | 0/0                        |
| 719                                             | 4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI, UTTARAKHAND     | 03/2016                       | 1,443.00<br>-                      | -<br>-                             | 02/2020     | 0/0                        |
| 720                                             | 4-LANNING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 ( - [N24000563]NHAI, UTTAR PRADESH | 03/2016                       | 1,668.00<br>-                      | -<br>-                             | 02/2020     | 0/0                        |
| 721                                             | SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT (APP - [N24000624]NHAI, MULTI STATE   | 09/2016                       | 1,244.10<br>-                      | -<br>-                             | 02/2020     | 0/0                        |
| 722                                             | FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250 (DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI, TAMIL NADU    | 03/2017                       | 848.45<br>-                        | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 723                                             | CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI, MAHARASHTRA    | 03/2017                       | 247.02<br>-                        | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 724                                             | 4-LANNING OF BODHRE-DHULE SECTION (KM 390.000 TO 452.800) - [N24000656]NHAI, MAHARASHTRA                                               | 03/2017                       | 744.64<br>-                        | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 725                                             | TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI, BIHAR           | 03/2017                       | 672.89<br>-                        | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 726                                             | CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI, BIHAR          | 03/2017                       | 235.48<br>-                        | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 727                                             | REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI, ANDHRA PRADESH                      | 03/2017                       | 648.32<br>-                        | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 728                                             | REHABILITATION AND UPGRADATION BY 4-LANNING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI, ODISHA         | 03/2017                       | 1,288.07<br>-                      | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 729                                             | 6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI, UTTAR PRADESH  | 03/2017                       | 2,064.99<br>-                      | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 730                                             | 4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI, ODISHA                                                                            | 07/2015                       | 1,282.94<br>-                      | -<br>-                             | 04/2020     | 0/0                        |
| 731                                             | FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI, BIHAR                                                                           | 08/2015                       | 322.09<br>-                        | 04/2018<br>-                       | 04/2020     | 0/0                        |
| 732                                             | 4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI, UTTAR PRADESH                              | 03/2016                       | 1,737.00<br>-                      | -<br>-                             | 04/2020     | 0/0                        |
| 733                                             | 4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI, PUNJAB                                                                           | 08/2016                       | 1,169.61<br>-                      | -<br>-                             | 04/2020     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                         |                               |                                    |                                    |             |                            |
|-------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                                 | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                         |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                       | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 734                                             | FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA                                    | 08/2016                       | 1,664.20<br>-                      | 04/2020<br>-                       | 04/2020     | 0/0                        |
| 735                                             | CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB           | 03/2017                       | 754.54<br>-                        | 03/2020<br>-                       | 04/2020     | 0/0                        |
| 736                                             | SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 ( - [N24000621]NHAI,RAJASTHAN        | 09/2016                       | 1,239.82<br>-                      | -<br>-                             | 05/2020     | 0/0                        |
| 737                                             | FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA                                                                     | 02/2017                       | 904.16<br>-                        | 02/2020<br>-                       | 05/2020     | 0/0                        |
| 738                                             | 4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA                                              | 03/2017                       | 1,030.44<br>-                      | 03/2020<br>-                       | 05/2020     | 0/0                        |
| 739                                             | DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH    | 03/2017                       | 1,989.00<br>-                      | 03/2020<br>-                       | 05/2020     | 0/0                        |
| 740                                             | SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH                   | 03/2017                       | 1,041.62<br>-                      | 03/2020<br>-                       | 05/2020     | 0/0                        |
| 741                                             | DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH      | 12/2017                       | 1,232.21<br>-                      | -<br>-                             | 05/2020     | 0/0                        |
| 742                                             | 4-LANING OF BRAHAMPURE-FARAKA - [N24000203]NHAI,WEST BENGAL                                                                             | 02/2011                       | 998.79<br>-                        | 08/2013<br>-                       | 06/2020     | 0/0                        |
| 743                                             | SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA          | 03/2017                       | 831.58<br>-                        | 03/2020<br>-                       | 06/2020     | 0/0                        |
| 744                                             | SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA        | 03/2017                       | 993.16<br>-                        | 03/2020<br>-                       | 06/2020     | 0/0                        |
| 745                                             | 4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH                                                      | 06/2017                       | 2,485.93<br>-                      | 06/2020<br>-                       | 06/2020     | 0/0                        |
| 746                                             | 4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA                                                                            | 09/2017                       | 1,124.11<br>-                      | 09/2017<br>-                       | 06/2020     | 0/0                        |
| 747                                             | 4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH           | 03/2016                       | 1,408.00<br>-                      | -<br>-                             | 07/2020     | 0/0                        |
| 748                                             | FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH | 09/2016                       | 1,273.71<br>-                      | -<br>-                             | 07/2020     | 0/0                        |
| 749                                             | REHABILITATION AND UPGRADEATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA          | 10/2016                       | 1,008.96<br>-                      | -<br>-                             | 07/2020     | 0/0                        |
| 750                                             | GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE                                                                                     | 12/2003                       | 604.00<br>-                        | 12/2009<br>-                       | 08/2020     | 0/0                        |
| 751                                             | 6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN        | 12/2016                       | 1,031.95<br>-                      | -<br>-                             | 08/2020     | 0/0                        |
| 752                                             | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH    | 03/2017                       | 1,184.71<br>-                      | 03/2020<br>-                       | 08/2020     | 0/0                        |
| 753                                             | 4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA                                               | 03/2017                       | 988.34<br>-                        | 03/2020<br>-                       | 08/2020     | 0/0                        |
| 754                                             | 4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA                                             | 03/2017                       | 1,098.06<br>-                      | 03/2020<br>-                       | 08/2020     | 0/0                        |
| 755                                             | 4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT                                                 | 06/2017                       | 1,958.88<br>-                      | 06/2020<br>-                       | 08/2020     | 0/0                        |
| 756                                             | FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH   | 01/2018                       | 960.24<br>-                        | -<br>-                             | 08/2020     | 0/0                        |
| 757                                             | TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH                                    | 08/2016                       | 1,583.18<br>-                      | -<br>-                             | 09/2020     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                      |                               |                                    |                                    |             |                            |
|-------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                      |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                    | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 758                                             | FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR                                                                              | 01/1991                       | 642.41<br>-                        | -<br>-                             | 10/2020     | 0/0                        |
| 759                                             | 4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA                                             | 03/2016                       | 870.00<br>-                        | 03/2019<br>-                       | 11/2020     | 0/0                        |
| 760                                             | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH  | 03/2017                       | 1,373.28<br>-                      | 03/2020<br>-                       | 11/2020     | 0/0                        |
| 761                                             | 4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA                                          | 03/2017                       | 1,059.73<br>-                      | 03/2017<br>-                       | 11/2020     | 0/0                        |
| 762                                             | REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA                                  | 07/2017                       | 476.56<br>-                        | 07/2017<br>-                       | 11/2020     | 0/0                        |
| 763                                             | FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR                                                 | 12/2015                       | 2,168.66<br>-                      | 06/2019<br>-                       | 12/2020     | 0/0                        |
| 764                                             | FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH | 03/2018                       | 1,532.62<br>-                      | 03/2021<br>-                       | 03/2021     | 0/0                        |
| 765                                             | MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM                                                         | 12/2003                       | 155.04<br>-                        | 11/2008<br>-                       | -           | 0/0                        |
| 766                                             | HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM                                                                                  | 12/2003                       | 196.00<br>-                        | 07/2009<br>-                       | -           | 0/0                        |
| 767                                             | 4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE                                                                               | 02/2011                       | 2,498.76<br>-                      | 08/2014<br>-                       | -           | 0/0                        |
| 768                                             | INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH                                                                                  | 11/2010                       | 325.00<br>-                        | 05/2013<br>-                       | -           | 0/0                        |
| 769                                             | NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR                                                                                  | 05/2011                       | 2,159.00<br>-                      | 06/2015<br>-                       | -           | 0/0                        |
| 770                                             | JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR                                                               | 07/2010                       | 1,813.76<br>-                      | 07/2013<br>-                       | -           | 0/0                        |
| 771                                             | 2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR                                                                                   | 05/2011                       | 351.54<br>-                        | 05/2013<br>-                       | -           | 0/0                        |
| 772                                             | ROHTAK-BAWAL - [N24000169]NHAI,HARYANA                                                                                               | 05/2011                       | 650.00<br>-                        | 11/2013<br>-                       | -           | 0/0                        |
| 773                                             | GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH                                                                              | 02/2011                       | 1,141.00<br>-                      | 08/2013<br>-                       | -           | 0/0                        |
| 774                                             | DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU                          | 06/2011                       | 600.00<br>-                        | 06/2013<br>-                       | -           | 0/0                        |
| 775                                             | SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH                                     | 11/2011                       | 1,535.00<br>-                      | 05/2014<br>-                       | -           | 0/0                        |
| 776                                             | 2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR                                                                            | 10/2011                       | 375.09<br>-                        | 04/2014<br>-                       | -           | 0/0                        |
| 777                                             | SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR                                                                              | 06/2011                       | 1,100.70<br>-                      | 06/2014<br>-                       | -           | 0/0                        |
| 778                                             | BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH                                                                              | 03/2011                       | 1,046.00<br>-                      | 09/2013<br>-                       | -           | 0/0                        |
| 779                                             | SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA                                                               | 12/2011                       | 1,047.00<br>-                      | 06/2014<br>-                       | -           | 0/0                        |
| 780                                             | RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND                                                                                  | 12/2012                       | 1,479.00<br>-                      | 06/2015<br>-                       | -           | 0/0                        |
| 781                                             | ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH                                                                                       | 03/2013                       | 1,573.00<br>-                      | 09/2015<br>-                       | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                  |                               |                                    |                                    |             |                            |
|-------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                          | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                  |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 782                                             | DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE                                                                | 10/2012                       | 1,928.22<br>-                      | 04/2015<br>-                       | -           | 0/0                        |
| 783                                             | FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA                                            | 08/2015                       | 723.54<br>-                        | 02/2018<br>-                       | -           | 0/0                        |
| 784                                             | FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH                                                                   | 05/2015                       | 261.09<br>-                        | 05/2017<br>-                       | -           | 0/0                        |
| 785                                             | THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU                                                                    | 07/2014                       | 401.11<br>-                        | 01/2017<br>-                       | -           | 0/0                        |
| 786                                             | 2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH                             | 04/2014                       | 351.34<br>-                        | 01/2016<br>-                       | -           | 0/0                        |
| 787                                             | VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT                                                                                 | 03/2014                       | 503.16<br>-                        | 08/2016<br>-                       | -           | 0/0                        |
| 788                                             | 2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH                            | 09/2015                       | 368.73<br>-                        | 09/2016<br>-                       | -           | 0/0                        |
| 789                                             | 2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH                                                       | 06/2014                       | 301.04<br>-                        | 01/2016<br>-                       | -           | 0/0                        |
| 790                                             | 2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH                                                | 04/2014                       | 495.78<br>-                        | 01/2016<br>-                       | -           | 0/0                        |
| 791                                             | THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU                                                            | 11/2014                       | 563.92<br>-                        | 11/2016<br>-                       | -           | 0/0                        |
| 792                                             | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-III) - [N24000446]NHAI,MULTI STATE                                   | 09/2015                       | 788.51<br>-                        | 03/2018<br>-                       | -           | 0/0                        |
| 793                                             | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-II) - [N24000450]NHAI,UTTAR PRADESH                                  | 09/2015                       | 785.78<br>-                        | 03/2018<br>-                       | -           | 0/0                        |
| 794                                             | 4-LANING OF GHAGHRA BRIDGE TO VARANSI ( PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH                                              | 12/2015                       | 611.65<br>-                        | 06/2016<br>-                       | -           | 0/0                        |
| 795                                             | NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA                                                                                  | 09/2005                       | 168.00<br>-                        | 06/2006<br>-                       | -           | 0/0                        |
| 796                                             | FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR                                                                          | 08/2015                       | 556.07<br>-                        | -<br>-                             | -           | 0/0                        |
| 797                                             | FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH                                                    | 01/2016                       | 815.28<br>-                        | 06/2018<br>-                       | -           | 0/0                        |
| 798                                             | FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA                                            | 11/2015                       | 867.66<br>-                        | 05/2018<br>-                       | -           | 0/0                        |
| 799                                             | FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH                                                     | 01/2016                       | 1,027.53<br>-                      | 06/2018<br>-                       | -           | 0/0                        |
| 800                                             | FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH                                              | 06/2016                       | 667.00<br>-                        | 07/2018<br>-                       | -           | 0/0                        |
| 801                                             | FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH                                               | 12/2015                       | 667.00<br>-                        | 06/2018<br>-                       | -           | 0/0                        |
| 802                                             | FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH                                                                 | 12/2015                       | 509.13<br>-                        | 04/2018<br>-                       | -           | 0/0                        |
| 803                                             | TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU                                                                                      | 03/2007                       | 516.00<br>-                        | 07/2008<br>-                       | -           | 0/0                        |
| 804                                             | MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH                                                                              | 01/2016                       | 683.24<br>-                        | -<br>-                             | -           | 0/0                        |
| 805                                             | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH | 03/2016                       | 1,404.50<br>-                      | -<br>-                             | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                       |                               |                                    |                                    |             |                            |
|-------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                               | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                       |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                     | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 806                                             | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH | 03/2016                       | 1,396.74<br>-                      | -<br>-                             | -           | 0/0                        |
| 807                                             | BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA                | 03/2016                       | 244.00<br>-                        | 07/2018<br>-                       | -           | 0/0                        |
| 808                                             | 4-LANNING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA                                                                            | 05/2014                       | 720.69<br>-                        | -<br>-                             | -           | 0/0                        |
| 809                                             | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-I)_NEW - [N24000609]NHAI,DELHI                                            | 09/2015                       | 771.18<br>-                        | -<br>-                             | -           | 0/0                        |
| 810                                             | 4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA                                                    | 11/2016                       | 1,071.61<br>-                      | -<br>-                             | -           | 0/0                        |
| 811                                             | 4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA                                                       | 11/2016                       | 1,064.88<br>-                      | -<br>-                             | -           | 0/0                        |
| 812                                             | VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH                                                                       | 09/2014                       | 1,684.00<br>-                      | 02/2017<br>-                       | -           | 0/0                        |
| 813                                             | CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH  | 12/2016                       | 534.55<br>-                        | -<br>-                             | -           | 0/0                        |
| 814                                             | CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH   | 01/2017                       | 450.68<br>-                        | -<br>-                             | -           | 0/0                        |
| 815                                             | SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT             | 01/2017                       | 1,251.11<br>-                      | -<br>-                             | -           | 0/0                        |
| 816                                             | SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR                               | 08/2017                       | 950.64<br>-                        | 08/2017<br>-                       | -           | 0/0                        |
| 817                                             | FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU                                                                     | 08/2017                       | 1,176.37<br>-                      | 08/2017<br>-                       | -           | 0/0                        |
| 818                                             | JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT                                                                                             | 10/2017                       | 232.49<br>-                        | 10/2017<br>-                       | -           | 0/0                        |
| 819                                             | FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN                                       | 10/2017                       | 964.17<br>-                        | 10/2017<br>-                       | -           | 0/0                        |
| 820                                             | BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH                                         | 09/2017                       | 374.40<br>-                        | 09/2017<br>-                       | -           | 0/0                        |
| 821                                             | BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH                                 | 09/2017                       | 990.61<br>-                        | 09/2017<br>-                       | -           | 0/0                        |
| 822                                             | 4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU                                                                         | 09/2017                       | 244.27<br>-                        | 09/2017<br>-                       | -           | 0/0                        |
| 823                                             | 4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU                                                                      | 09/2017                       | 1,227.87<br>-                      | 09/2017<br>-                       | -           | 0/0                        |
| 824                                             | BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH  | 12/2017                       | 950.27<br>-                        | -<br>-                             | -           | 0/0                        |
| 825                                             | SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU      | 12/2017                       | 379.90<br>-                        | -<br>-                             | -           | 0/0                        |
| 826                                             | FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN       | 12/2017                       | 1,308.73<br>-                      | -<br>-                             | -           | 0/0                        |
| 827                                             | SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA    | 12/2017                       | 404.94<br>-                        | -<br>-                             | -           | 0/0                        |
| 828                                             | CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR          | 12/2017                       | 2,598.00<br>-                      | -<br>-                             | -           | 0/0                        |
| 829                                             | REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA         | 12/2017                       | 686.65<br>-                        | -<br>-                             | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                          |                               |                                    |                                    |             |                            |
|-------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                                  | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                          |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                        | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 830                                             | REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI, ODISHA           | 12/2017                       | 417.51<br>-                        | -<br>-                             | -           | 0/0                        |
| 831                                             | CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI, JAMMU AND KASHMIR | 12/2017                       | 1,471.75<br>-                      | -<br>-                             | -           | 0/0                        |
| 832                                             | 6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI, ANDHRA PRADESH   | 12/2017                       | 328.67<br>-                        | -<br>-                             | -           | 0/0                        |
| 833                                             | SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI, ANDHRA PRADESH   | 12/2017                       | 1,323.15<br>-                      | -<br>-                             | -           | 0/0                        |
| 834                                             | CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI, ANDHRA PRADESH   | 12/2017                       | 357.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 835                                             | ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI, UTTAR PRADESH    | 12/2017                       | 207.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 836                                             | CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI, UTTAR PRADESH    | 12/2017                       | 305.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 837                                             | REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI, BIHAR                  | 01/2018                       | 573.70<br>-                        | -<br>-                             | -           | 0/0                        |
| 838                                             | SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI, BIHAR                                         | 01/2018                       | 895.39<br>-                        | -<br>-                             | -           | 0/0                        |
| 839                                             | FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI, JHARKHAND                                                           | 01/2018                       | 273.46<br>-                        | -<br>-                             | -           | 0/0                        |
| 840                                             | SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI, JHARKHAND                                         | 01/2018                       | 1,155.16<br>-                      | -<br>-                             | -           | 0/0                        |
| 841                                             | FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI, MADHYA PRADESH   | 01/2018                       | 770.73<br>-                        | -<br>-                             | -           | 0/0                        |
| 842                                             | 4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI, MAHARASHTRA                                                | 01/2018                       | 607.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 843                                             | 4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI, MAHARASHTRA                                                   | 01/2018                       | 621.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 844                                             | REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI, ODISHA           | 01/2018                       | 953.09<br>-                        | -<br>-                             | -           | 0/0                        |
| 845                                             | REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI, ODISHA           | 01/2018                       | 668.86<br>-                        | -<br>-                             | -           | 0/0                        |
| 846                                             | REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE ( - [N24000733]NHAI, ODISHA           | 01/2018                       | 633.68<br>-                        | -<br>-                             | -           | 0/0                        |
| 847                                             | REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI, ODISHA             | 01/2018                       | 614.48<br>-                        | -<br>-                             | -           | 0/0                        |
| 848                                             | REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI, ODISHA           | 01/2018                       | 564.66<br>-                        | -<br>-                             | -           | 0/0                        |
| 849                                             | REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI, ODISHA           | 01/2018                       | 686.65<br>-                        | -<br>-                             | -           | 0/0                        |
| 850                                             | REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI, ODISHA           | 01/2018                       | 1,522.00<br>-                      | -<br>-                             | -           | 0/0                        |
| 851                                             | REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI, ODISHA           | 01/2018                       | 999.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 852                                             | REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) ( - [N24000739]NHAI, ODISHA           | 01/2018                       | 503.88<br>-                        | -<br>-                             | -           | 0/0                        |



## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                       |                               |                                    |                                    |             |                            |
|-------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                               | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                       |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                     | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 853                                             | VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH                                                                            | 01/2018                       | 450.77<br>-                        | -<br>-                             | -           | 0/0                        |
| 854                                             | FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA                                                    | 03/2017                       | 4,429.00<br>-                      | 03/2017<br>-                       | -           | 0/0                        |
| 855                                             | 2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA      | 02/2018                       | 486.78<br>-                        | -<br>-                             | -           | 0/0                        |
| 856                                             | 6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA         | 02/2018                       | 1,424.77<br>-                      | -<br>-                             | -           | 0/0                        |
| 857                                             | FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU                           | 02/2018                       | 1,166.26<br>-                      | -<br>-                             | -           | 0/0                        |
| 858                                             | FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH   | 02/2018                       | 670.50<br>-                        | -<br>-                             | -           | 0/0                        |
| 859                                             | SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA      | 02/2018                       | 1,995.34<br>-                      | -<br>-                             | -           | 0/0                        |
| 860                                             | SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA       | 02/2018                       | 2,177.80<br>-                      | -<br>-                             | -           | 0/0                        |
| 861                                             | REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL    | 03/2018                       | 1,261.98<br>-                      | -<br>-                             | -           | 0/0                        |
| 862                                             | FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB               | 02/2018                       | 261.76<br>-                        | -<br>-                             | -           | 0/0                        |
| 863                                             | FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH                                  | 03/2018                       | 809.07<br>-                        | -<br>-                             | -           | 0/0                        |
| 864                                             | FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH                              | 03/2018                       | 925.40<br>-                        | -<br>-                             | -           | 0/0                        |
| 865                                             | UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN      | 02/2018                       | 1,103.88<br>-                      | -<br>-                             | -           | 0/0                        |
| 866                                             | CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN      | 02/2018                       | 741.86<br>-                        | -<br>-                             | -           | 0/0                        |
| 867                                             | CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH  | 03/2018                       | 1,117.84<br>-                      | -<br>-                             | -           | 0/0                        |
| 868                                             | CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN       | 02/2018                       | 716.76<br>-                        | -<br>-                             | -           | 0/0                        |
| 869                                             | SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH  | 03/2018                       | 2,140.93<br>-                      | -<br>-                             | -           | 0/0                        |
| 870                                             | SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH | 02/2018                       | 1,959.00<br>-                      | -<br>-                             | -           | 0/0                        |
| 871                                             | 4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH  | 03/2018                       | 1,120.57<br>-                      | -<br>-                             | -           | 0/0                        |
| 872                                             | SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT         | 02/2018                       | 1,052.21<br>-                      | -<br>-                             | -           | 0/0                        |
| 873                                             | REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH  | 03/2018                       | 1,025.80<br>-                      | -<br>-                             | -           | 0/0                        |
| 874                                             | REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH  | 03/2018                       | 1,115.28<br>-                      | -<br>-                             | -           | 0/0                        |
| 875                                             | FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA      | 03/2018                       | 802.65<br>-                        | -<br>-                             | -           | 0/0                        |
| 876                                             | CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH  | 02/2018                       | 972.77<br>-                        | -<br>-                             | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                          |                               |                                    |                                    |             |                            |
|-------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                                  | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                          |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                        | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 877                                             | FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH | 03/2018                       | 392.60<br>-                        | -<br>-                             | -           | 0/0                        |
| 878                                             | SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH    | 03/2018                       | 1,550.98<br>-                      | -<br>-                             | -           | 0/0                        |
| 879                                             | REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH    | 03/2018                       | 565.09<br>-                        | -<br>-                             | -           | 0/0                        |
| 880                                             | CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH    | 03/2018                       | 314.43<br>-                        | -<br>-                             | -           | 0/0                        |
| 881                                             | CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH    | 03/2018                       | 557.30<br>-                        | -<br>-                             | -           | 0/0                        |
| 882                                             | DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR             | 03/2018                       | 496.20<br>-                        | -<br>-                             | -           | 0/0                        |
| 883                                             | 4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH        | 03/2018                       | 1,029.96<br>-                      | -<br>-                             | -           | 0/0                        |
| 884                                             | CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT           | 03/2018                       | 2,702.05<br>-                      | -<br>-                             | -           | 0/0                        |
| 885                                             | FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA          | 03/2018                       | 950.63<br>-                        | -<br>-                             | -           | 0/0                        |
| 886                                             | FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA         | 03/2018                       | 857.62<br>-                        | -<br>-                             | -           | 0/0                        |
| 887                                             | FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA         | 03/2018                       | 828.29<br>-                        | -<br>-                             | -           | 0/0                        |
| 888                                             | FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU       | 03/2018                       | 505.35<br>-                        | -<br>-                             | -           | 0/0                        |
| 889                                             | FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU      | 03/2018                       | 628.71<br>-                        | -<br>-                             | -           | 0/0                        |
| 890                                             | TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU        | 03/2018                       | 633.55<br>-                        | -<br>-                             | -           | 0/0                        |
| 891                                             | FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU         | 03/2018                       | 1,016.92<br>-                      | -<br>-                             | -           | 0/0                        |
| 892                                             | FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU        | 03/2018                       | 2,065.96<br>-                      | -<br>-                             | -           | 0/0                        |
| 893                                             | FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE       | 03/2018                       | 1,294.47<br>-                      | -<br>-                             | -           | 0/0                        |
| 894                                             | FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE       | 03/2018                       | 998.70<br>-                        | -<br>-                             | -           | 0/0                        |
| 895                                             | CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT           | 03/2018                       | 1,437.64<br>-                      | -<br>-                             | -           | 0/0                        |
| 896                                             | CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT            | 03/2018                       | 1,161.39<br>-                      | -<br>-                             | -           | 0/0                        |
| 897                                             | CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA           | 03/2018                       | 1,484.30<br>-                      | -<br>-                             | -           | 0/0                        |
| 898                                             | REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA           | 03/2018                       | 275.12<br>-                        | -<br>-                             | -           | 0/0                        |
| 899                                             | REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXIST - [N24000837]NHAI,HARYANA           | 03/2018                       | 307.79<br>-                        | -<br>-                             | -           | 0/0                        |
| 900                                             | UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN          | 03/2018                       | 874.25<br>-                        | -<br>-                             | -           | 0/0                        |



## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                         |                               |                                    |                                    |             |                            |
|-------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                                 | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                         |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                       | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 901                                             | SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA          | 03/2018                       | 634.70<br>-                        | -<br>-                             | -           | 0/0                        |
| 902                                             | CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN         | 03/2018                       | 1,158.35<br>-                      | -<br>-                             | -           | 0/0                        |
| 903                                             | SIX LANING & STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA           | 03/2018                       | 795.50<br>-                        | -<br>-                             | -           | 0/0                        |
| 904                                             | REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB           | 03/2018                       | 199.90<br>-                        | -<br>-                             | -           | 0/0                        |
| 905                                             | SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA                          | 03/2018                       | 806.11<br>-                        | -<br>-                             | -           | 0/0                        |
| 906                                             | REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA          | 03/2018                       | 198.05<br>-                        | -<br>-                             | -           | 0/0                        |
| 907                                             | CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA                                               | 03/2018                       | 291.53<br>-                        | -<br>-                             | -           | 0/0                        |
| 908                                             | REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA          | 03/2018                       | 181.78<br>-                        | -<br>-                             | -           | 0/0                        |
| 909                                             | CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA                                                | 03/2018                       | 289.21<br>-                        | -<br>-                             | -           | 0/0                        |
| 910                                             | REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION & STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA          | 03/2018                       | 551.58<br>-                        | -<br>-                             | -           | 0/0                        |
| 911                                             | CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA     | 03/2018                       | 1,162.92<br>-                      | -<br>-                             | -           | 0/0                        |
| 912                                             | FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH | 03/2018                       | 478.74<br>-                        | -<br>-                             | -           | 0/0                        |
| 913                                             | FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA      | 03/2018                       | 642.13<br>-                        | -<br>-                             | -           | 0/0                        |
| 914                                             | 4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND        | 03/2018                       | 1,005.08<br>-                      | -<br>-                             | -           | 0/0                        |
| <b>National Highways Development Project</b>    |                                                                                                                                         |                               |                                    |                                    |             |                            |
| 915                                             | BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH                                                                       | 11/2011                       | 704.26<br>-                        | 05/2015<br>-                       | 01/2020     | 0/0                        |
| 916                                             | KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH                                        | 02/2015                       | 377.83<br>-                        | 07/2017<br>-                       | -           | 0/0                        |
| 917                                             | RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH                       | 10/2013                       | 445.89<br>-                        | 03/2017<br>-                       | -           | 0/0                        |
| 918                                             | BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH                                 | 01/2014                       | 397.04<br>-                        | 10/2016<br>-                       | -           | 0/0                        |
| 919                                             | BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH                         | 06/2015                       | 390.51<br>-                        | -<br>-                             | -           | 0/0                        |
| 920                                             | BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH                                                          | 03/2013                       | 257.80<br>-                        | 02/2016<br>-                       | -           | 0/0                        |
| 921                                             | INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH                      | 11/2013                       | 497.05<br>-                        | 05/2017<br>-                       | -           | 0/0                        |
| 922                                             | ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH                                             | 06/2015                       | 774.57<br>-                        | 03/2018<br>-                       | -           | 0/0                        |
| 923                                             | SHAHDOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH         | 06/2015                       | 532.49<br>-                        | 05/2017<br>-                       | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                      |                               |                                    |                                    |             |                            |
|-------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                      |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                    | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 924                                             | BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH                                                               | 08/2015                       | 257.80<br>-                        | -<br>-                             | -           | 0/0                        |
| 925                                             | BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH          | 10/2013                       | 317.76<br>-                        | 03/2017<br>-                       | -           | 0/0                        |
| 926                                             | JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH          | 10/2013                       | 283.45<br>-                        | 10/2016<br>-                       | -           | 0/0                        |
| 927                                             | MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH                     | 06/2015                       | 641.02<br>-                        | 12/2017<br>-                       | -           | 0/0                        |
| 928                                             | MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH                                                    | 01/2012                       | 381.86<br>-                        | 04/2015<br>-                       | -           | 0/0                        |
| 929                                             | SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH                               | 10/2013                       | 493.94<br>-                        | 03/2017<br>-                       | -           | 0/0                        |
| 930                                             | BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH                                                          | 11/2011                       | 670.82<br>-                        | 02/2015<br>-                       | -           | 0/0                        |
| 931                                             | JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH           | 02/2015                       | 327.32<br>-                        | 05/2017<br>-                       | -           | 0/0                        |
| 932                                             | JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH                      | 11/2015                       | 628.45<br>-                        | 03/2018<br>-                       | -           | 0/0                        |
| 933                                             | GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH                                  | 12/2015                       | 927.54<br>-                        | 06/2018<br>-                       | -           | 0/0                        |
| <u>Public Works Dept Of State</u>               |                                                                                                                                      |                               |                                    |                                    |             |                            |
| 934                                             | EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA      | 03/2015                       | 153.21<br>-                        | 01/2017<br>-                       | -           | 0/0                        |
| 935                                             | CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA         | 01/2014                       | 255.75<br>348.00                   | 09/2017<br>-                       | -           | 0/0                        |
| 936                                             | CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA         | 01/2014                       | 267.16<br>352.00                   | 11/2017<br>-                       | -           | 0/0                        |
| 937                                             | REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH | 11/2014                       | 297.78<br>330.00                   | 02/2017<br>-                       | -           | 0/0                        |
| 938                                             | REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH             | 10/2014                       | 213.47<br>-                        | 03/2015<br>-                       | -           | 0/0                        |
| 939                                             | REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 ( BEDMA-DAHAKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH           | 10/2014                       | 298.34<br>-                        | 03/2015<br>-                       | -           | 0/0                        |
| 940                                             | REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHAKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH    | 11/2014                       | 262.54<br>-                        | 03/2015<br>-                       | -           | 0/0                        |
| 941                                             | REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH           | 12/2015                       | 291.05<br>-                        | -<br>-                             | -           | 0/0                        |
| 942                                             | CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH    | 12/2010                       | 169.26<br>-                        | 12/2012<br>-                       | -           | 0/0                        |
| 943                                             | REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH            | 12/2014                       | 394.20<br>-                        | -<br>-                             | -           | 0/0                        |
| 944                                             | REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH     | 11/2015                       | 485.44<br>-                        | 12/2015<br>-                       | -           | 0/0                        |
| 945                                             | REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB         | 03/2015                       | 435.90<br>-                        | -<br>-                             | -           | 0/0                        |
| 946                                             | WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB         | 01/2015                       | 279.68<br>-                        | -<br>-                             | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                         |                               |                                    |                                    |             |                            |
|-------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                                 | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                         |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                       | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 947                                             | 4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB             | 11/2014                       | 463.65<br>546.00                   | -<br>-                             | -           | 0/0                        |
| 948                                             | 4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB             | 11/2014                       | 573.96<br>605.00                   | -<br>-                             | -           | 0/0                        |
| 949                                             | REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH    | 03/2015                       | 271.45<br>-                        | 10/2015<br>-                       | -           | 0/0                        |
| 950                                             | FOUR LANING OF 5.122 KM OF NH9( NEW NH 65) FROM KM 269.900( DESIGN CH.0.0 ) - [N24000302]PWD,ANDHRA PRADESH                             | 07/2015                       | 333.21<br>-                        | 12/2015<br>-                       | -           | 0/0                        |
| 951                                             | WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM            | 11/2010                       | 624.41<br>-                        | 03/2011<br>-                       | -           | 0/0                        |
| 952                                             | TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH | 12/2011                       | 156.63<br>276.00                   | 02/2012<br>-                       | -           | 0/0                        |
| 953                                             | CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM            | 08/2010                       | 193.69<br>-                        | 10/2010<br>-                       | -           | 0/0                        |
| 954                                             | TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH | 11/2010                       | 305.49<br>-                        | 03/2011<br>-                       | -           | 0/0                        |
| 955                                             | TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH  | 03/2012                       | 207.03<br>-                        | 05/2012<br>-                       | -           | 0/0                        |
| 956                                             | CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM                                                 | 04/2013                       | 151.59<br>-                        | 08/2013<br>-                       | -           | 0/0                        |
| 957                                             | CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM                                              | 04/2013                       | 166.27<br>-                        | 08/2013<br>-                       | -           | 0/0                        |
| 958                                             | CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM                                                 | 01/2013                       | 182.28<br>-                        | 02/2013<br>-                       | -           | 0/0                        |
| 959                                             | WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND          | 12/2010                       | 1,296.00<br>-                      | 02/2011<br>-                       | -           | 0/0                        |
| 960                                             | 4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB             | 02/2015                       | 483.38<br>-                        | -<br>-                             | -           | 0/0                        |
| 961                                             | 4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB             | 02/2015                       | 616.36<br>-                        | -<br>-                             | -           | 0/0                        |
| 962                                             | 2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH     | 11/2010                       | 305.49<br>-                        | 03/2017<br>-                       | -           | 0/0                        |
| 963                                             | 4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64( - [N24000374]PWD,PUNJAB            | 02/2015                       | 486.74<br>-                        | -<br>-                             | -           | 0/0                        |
| 964                                             | SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH                                                                  | 01/2012                       | 320.48<br>-                        | 08/2015<br>-                       | -           | 0/0                        |
| 965                                             | CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15( - [N24000383]PWD,PUNJAB            | 03/2015                       | 312.79<br>-                        | -<br>-                             | -           | 0/0                        |
| 966                                             | CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB            | 07/2014                       | 319.80<br>-                        | -<br>-                             | -           | 0/0                        |
| 967                                             | DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB            | 12/2015                       | 766.36<br>-                        | -<br>-                             | -           | 0/0                        |
| 968                                             | FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH  | 01/2011                       | 264.16<br>-                        | -<br>-                             | -           | 0/0                        |
| 969                                             | 4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB                                             | 11/2015                       | 847.02<br>-                        | -<br>-                             | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                         |                               |                                    |                                    |             |                            |
|-------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                                 | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                         |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                       | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 970                                             | 2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA            | 12/2010                       | 1,494.48<br>-                      | 02/2011<br>-                       | -           | 0/0                        |
| 971                                             | 4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB                                            | 11/2015                       | 889.24<br>-                        | -<br>-                             | -           | 0/0                        |
| 972                                             | 2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM                           | 11/2010                       | 268.08<br>-                        | 05/2017<br>-                       | -           | 0/0                        |
| 973                                             | 2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM               | 11/2010                       | 470.20<br>-                        | 02/2011<br>-                       | -           | 0/0                        |
| 974                                             | SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH                                                         | 11/2011                       | 871.15<br>-                        | 09/2015<br>-                       | -           | 0/0                        |
| 975                                             | DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB             | 12/2015                       | 578.38<br>-                        | -<br>-                             | -           | 0/0                        |
| 976                                             | WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE       | 03/2015                       | 789.83<br>-                        | -<br>-                             | -           | 0/0                        |
| 977                                             | FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH    | 10/2015                       | 333.21<br>-                        | 11/2015<br>-                       | -           | 0/0                        |
| 978                                             | STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM             | 05/2011                       | 176.22<br>-                        | 02/2018<br>-                       | -           | 0/0                        |
| 979                                             | STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM              | 11/2014                       | 218.31<br>-                        | 02/2018<br>-                       | -           | 0/0                        |
| 980                                             | IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA                                                                                 | 12/2013                       | 319.80<br>-                        | 10/2016<br>-                       | -           | 0/0                        |
| 981                                             | CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM                                    | 08/2010                       | 195.04<br>-                        | 10/2010<br>-                       | -           | 0/0                        |
| 982                                             | REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH                                                     | 02/2015                       | 224.83<br>-                        | 04/2015<br>-                       | -           | 0/0                        |
| 983                                             | REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA            | 07/2014                       | 342.05<br>-                        | 01/2017<br>-                       | -           | 0/0                        |
| 984                                             | TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH | 12/2009                       | 165.00<br>-                        | 09/2010<br>-                       | -           | 0/0                        |
| 985                                             | TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH | 12/2009                       | 104.00<br>-                        | 09/2010<br>-                       | -           | 0/0                        |
| 986                                             | NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN         | 09/2012                       | 511.00<br>-                        | 10/2013<br>-                       | -           | 0/0                        |
| 987                                             | NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN                   | 09/2012                       | 511.00<br>-                        | 10/2013<br>-                       | -           | 0/0                        |
| 988                                             | UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH                                 | 03/2015                       | 511.83<br>-                        | 08/2017<br>-                       | -           | 0/0                        |
| 989                                             | WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA                | 12/2011                       | 159.39<br>-                        | 11/2017<br>-                       | -           | 0/0                        |
| 990                                             | WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB            | 06/2015                       | 892.17<br>-                        | -<br>-                             | -           | 0/0                        |
| 991                                             | WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB            | 06/2015                       | 899.21<br>-                        | -<br>-                             | -           | 0/0                        |
| 992                                             | WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA            | 12/2011                       | 191.08<br>-                        | 08/2015<br>-                       | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                               |                               |                                    |                                    |             |                            |
|-------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                                       | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                               |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                             | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 993                                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR                    | 01/1991                       | 154.62<br>-                        | -<br>-                             | -           | 0/0                        |
| 994                                             | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR                    | 01/1991                       | 319.68<br>-                        | -<br>-                             | -           | 0/0                        |
| 995                                             | REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA             | 01/2014                       | 292.98<br>-                        | 11/2014<br>-                       | -           | 0/0                        |
| 996                                             | 4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA                          | 03/2016                       | 1,142.62<br>-                      | -<br>-                             | -           | 0/0                        |
| 997                                             | 4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA                          | 03/2016                       | 1,101.58<br>-                      | -<br>-                             | -           | 0/0                        |
|                                                 |                                                                                                                                               |                               |                                    |                                    |             |                            |
|                                                 | <u>SHIPPING AND PORTS</u>                                                                                                                     |                               |                                    |                                    |             |                            |
|                                                 | <u>Inland Waterways Authority Of India</u>                                                                                                    |                               |                                    |                                    |             |                            |
| 998                                             | JAL MARG VIKAS PROJECT - [N25000072]IWAI,MULTI STATE                                                                                          | 01/2018                       | 4,200.00<br>-                      | 03/2023<br>-                       | 03/2023     | 0/0                        |
|                                                 | <u>Kamarajar Port Limited</u>                                                                                                                 |                               |                                    |                                    |             |                            |
| 999                                             | CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU                                                               | 03/2016                       | 600.00<br>257.90                   | 12/2017<br>05/2020                 | 05/2020     | 0/0                        |
|                                                 | <u>Mumbai Port Trust</u>                                                                                                                      |                               |                                    |                                    |             |                            |
| 1000                                            | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA | 01/2007                       | 366.39<br>669.46                   | 12/2010<br>-                       | 12/2018     | 0/0                        |
|                                                 | <u>Port Trust</u>                                                                                                                             |                               |                                    |                                    |             |                            |
| 1001                                            | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU                                                | 10/2002                       | 150.00<br>600.00                   | 03/2006<br>03/2016                 | 02/2019     | 0/0                        |
| 1002                                            | SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU                                                                         | 06/2005                       | 2,427.40<br>-                      | 10/2008<br>-                       | -           | 0/0                        |
|                                                 |                                                                                                                                               |                               |                                    |                                    |             |                            |
|                                                 | <u>TELECOMMUNICATIONS</u>                                                                                                                     |                               |                                    |                                    |             |                            |
|                                                 | <u>Bharat Sanchar Nigam Limited</u>                                                                                                           |                               |                                    |                                    |             |                            |
| 1003                                            | MAHARASHTRA CORE (LOT1) - [N26000108]BSNL,MAHARASHTRA                                                                                         | 08/2017                       | 167.68<br>-                        | 04/2018<br>02/2019                 | 02/2019     | 0/0                        |
| 1004                                            | MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA                                                                                    | 08/2017                       | 215.30<br>214.10                   | 05/2018<br>02/2019                 | 02/2019     | 0/0                        |
| 1005                                            | MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA                                                                | 01/2018                       | 231.80<br>231.80                   | 10/2018<br>02/2019                 | 02/2019     | 0/0                        |
|                                                 | <u>Department Of Telecommunication</u>                                                                                                        |                               |                                    |                                    |             |                            |
| 1006                                            | NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE                                                                                             | 03/2012                       | 13,334.00<br>-                     | 07/2015<br>-                       | 05/2020     | 0/0                        |
|                                                 | <u>Mahanagar Telephone Nigam Limited</u>                                                                                                      |                               |                                    |                                    |             |                            |
| 1007                                            | GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI                                                                             | 06/2016                       | 418.26<br>-                        | 06/2017<br>-                       | -           | 0/0                        |
|                                                 |                                                                                                                                               |                               |                                    |                                    |             |                            |
|                                                 | <u>URBAN DEVELOPMENT</u>                                                                                                                      |                               |                                    |                                    |             |                            |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                   |                               |                                    |                                    |         |                            |
|-------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|---------|----------------------------|
| SI.No                                           | Project                                                                                                                           | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |         | Milestones Achieved/ Total |
| 1                                               | 2                                                                                                                                 | 3                             | 4                                  | 5                                  | 6       | 7                          |
|                                                 | <b>Bangalore Metro Rail Corporation Limited</b>                                                                                   |                               |                                    |                                    |         |                            |
| 1008                                            | BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA                                                                 | 02/2014                       | 26,405.14 -                        | 02/2019 -                          | 03/2020 | 0/0                        |
|                                                 | <b>Central Public Works Department</b>                                                                                            |                               |                                    |                                    |         |                            |
| 1009                                            | CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI      | 12/2017                       | 188.00 -                           | 06/2019 -                          | 06/2019 | 0/0                        |
| 1010                                            | CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND | 12/2008                       | 114.26 266.00                      | 12/2013 -                          | 10/2019 | 0/0                        |
| 1011                                            | DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN               | 12/2016                       | 549.31 -                           | 07/2019 -                          | 10/2019 | 0/0                        |
| 1012                                            | CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI                                  | 10/2017                       | 271.90 -                           | 11/2019 -                          | 11/2019 | 0/0                        |
| 1013                                            | CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH                                               | 11/2017                       | 171.72 -                           | 03/2020 -                          | 03/2020 | 0/0                        |
| 1014                                            | RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI      | 11/2017                       | 238.56 -                           | 05/2020 -                          | 05/2020 | 0/0                        |
| 1015                                            | CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR               | 02/2016                       | 496.18 496.00                      | 06/2017 07/2017                    | 06/2020 | 0/0                        |
| 1016                                            | RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA                                                                  | 12/2016                       | 246.31 -                           | 02/2020 09/2020                    | 09/2020 | 0/0                        |
| 1017                                            | STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU                                                        | 04/2014                       | 332.72 -                           | 09/2016 -                          | -       | 0/0                        |
| 1018                                            | CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI        | 07/2012                       | 884.30 -                           | 12/2015 -                          | -       | 0/0                        |
| 1019                                            | CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU                                                 | 11/2017                       | 348.77 -                           | - -                                | -       | 0/0                        |
| 1020                                            | REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI                                                                      | 10/2016                       | 422.00 -                           | - -                                | -       | 0/0                        |
| 1021                                            | REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI      | 10/2016                       | 392.00 -                           | - -                                | -       | 0/0                        |
| 1022                                            | SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI      | 10/2016                       | 248.20 -                           | 04/2018 -                          | -       | 0/0                        |
|                                                 | <b>Chennai Metro Rail Ltd</b>                                                                                                     |                               |                                    |                                    |         |                            |
| 1023                                            | CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU                                                                 | 06/2016                       | 3,770.00 -                         | 03/2018 -                          | -       | 0/0                        |
|                                                 | <b>Hindustan Steelwork Construction Limited</b>                                                                                   |                               |                                    |                                    |         |                            |
| 1024                                            | CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA  | 04/2014                       | 151.33 -                           | 09/2017 -                          | 12/2018 | 0/0                        |
| 1025                                            | CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND                                      | 02/2014                       | 787.29 -                           | 12/2016 -                          | 12/2018 | 0/0                        |
| 1026                                            | IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR                                                                                | 10/2005                       | 956.00 -                           | 03/2015 -                          | 03/2021 | 0/0                        |
| 1027                                            | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA                                          | 03/2007                       | 149.73 173.00                      | 12/2015 -                          | -       | 0/0                        |
| 1028                                            | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA                                         | 12/2007                       | 202.61 227.00                      | 12/2016 -                          | -       | 0/0                        |



## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |                                                                                                                                    |                               |                                    |                                    |             |                            |
|-------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                                           | Project                                                                                                                            | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                                 |                                                                                                                                    |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                                               | 2                                                                                                                                  | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 1029                                            | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA                                        | 10/2011                       | 175.49<br>206.71                   | 12/2016<br>-                       | -           | 0/0                        |
| 1030                                            | CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA                                               | 05/2005                       | 768.88<br>1,070.97                 | 02/2014<br>-                       | -           | 0/0                        |
| 1031                                            | CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA                                    | 07/2011                       | 324.87<br>324.87                   | 12/2015<br>-                       | -           | 0/0                        |
| 1032                                            | CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH  | 07/2014                       | 232.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 1033                                            | CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT                                    | 01/2013                       | 175.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 1034                                            | CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN   | 05/2015                       | 189.00<br>-                        | 03/2017<br>-                       | -           | 0/0                        |
| 1035                                            | CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND                           | 12/2007                       | 253.92<br>253.92                   | 06/2016<br>-                       | -           | 0/0                        |
| 1036                                            | CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND            | 12/2007                       | 200.00<br>-                        | 03/2018<br>-                       | -           | 0/0                        |
| 1037                                            | CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND                                                            | 04/2013                       | 170.00<br>-                        | 04/2018<br>-                       | -           | 0/0                        |
| 1038                                            | CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL | 08/2012                       | 185.37<br>-                        | 03/2016<br>-                       | -           | 0/0                        |
|                                                 | <u>Jawahar Lal Nehru National Urban Renewal Mission</u>                                                                            |                               |                                    |                                    |             |                            |
| 1039                                            | REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH | 08/2007                       | 246.90<br>-                        | -<br>-                             | -           | 0/0                        |
|                                                 | <u>Kochi Metro Rail Corporation Ltd</u>                                                                                            |                               |                                    |                                    |             |                            |
| 1040                                            | KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA                                                                                 | 07/2012                       | 5,181.79<br>-                      | 07/2017<br>-                       | 12/2019     | 0/0                        |
|                                                 | <u>Lucknow Metro Rail Corporation Limited</u>                                                                                      |                               |                                    |                                    |             |                            |
| 1041                                            | LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH                                                                | 01/2016                       | 6,928.00<br>6,928.00               | 03/2019<br>-                       | 03/2019     | 0/0                        |
|                                                 | <u>Maharashtra Metro Rail Corporation Ltd.</u>                                                                                     |                               |                                    |                                    |             |                            |
| 1042                                            | DELHI MRTS PHASE-III - [N28000056]MMRC,DELHI                                                                                       | 09/2011                       | 38,585.00<br>-                     | 03/2016<br>05/2019                 | 05/2019     | 0/0                        |
| 1043                                            | PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA                                                                    | 12/2016                       | 11,420.00<br>-                     | 11/2021<br>-                       | 11/2021     | 0/0                        |
|                                                 | <u>Mumbai Metro Rail Corporation Ltd</u>                                                                                           |                               |                                    |                                    |             |                            |
| 1044                                            | MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA                                                           | 07/2013                       | 23,136.00<br>-                     | 01/2015<br>-                       | 05/2020     | 0/0                        |
|                                                 | <u>Nagpur Metro Rail Corporation Ltd</u>                                                                                           |                               |                                    |                                    |             |                            |
| 1045                                            | NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA                                                                                   | 08/2014                       | 8,680.00<br>8,680.00               | 03/2018<br>12/2019                 | 12/2019     | 0/0                        |
|                                                 | <u>National Building Construcion Corporation Ltd</u>                                                                               |                               |                                    |                                    |             |                            |
| 1046                                            | REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI                                                              | 07/2016                       | 2,694.00<br>-                      | -<br>-                             | -           | 0/0                        |
|                                                 | Total                                                                                                                              |                               | 11,47,474.56<br>-                  |                                    |             | 0/0                        |

### Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs. 150 Crore and Above (December 2018) |             |                               |                                    |                                    |             |                            |
|-------------------------------------------------|-------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
|                                                 |             |                               |                                    | Date of Commissioning (Month/Year) |             |                            |
| Sl.No                                           | Project     | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Original / Revised                 | Anticipated | Milestones Achieved/ Total |
| 1                                               | 2           | 3                             | 4                                  | 5                                  | 6           | 7                          |
|                                                 | Grand Total |                               | 11,47,474.56                       |                                    |             | 0/0                        |



## List of Projects Ahead of Schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                                                                                    |                  |                                     |                              |                                         | (December 2018)       |             |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------|------------------|-------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                                                                                    |                  |                                     |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                                                                            | Date of Approval | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated |
| 1                               | 2                                                                                                                  | 3                | 4                                   | 5                            | 6                                       | 7                     | 8           |
|                                 | <u>COAL</u>                                                                                                        |                  |                                     |                              |                                         |                       |             |
|                                 | <u>South-Eastern Coal Fields Limited</u>                                                                           |                  |                                     |                              |                                         |                       |             |
| 1                               | BATURA OCP (2.0 MTY)<br>- [N06000049]                                                                              | 8/2015           | 1,186.64                            | 203.82                       | 103.85                                  | 03/2023<br>-          | 03/2021     |
|                                 | Total                                                                                                              |                  | 1,186.64<br>-                       | 203.82                       | 103.85                                  |                       |             |
|                                 | <u>HEALTH AND FAMILY WELFARE</u>                                                                                   |                  |                                     |                              |                                         |                       |             |
|                                 | <u>Hospital Services Consultancy Corporation Ltd</u>                                                               |                  |                                     |                              |                                         |                       |             |
| 2                               | NEIGRIHMS SHILLONG MEGHALYA<br>- [N21000013]                                                                       | 10/2016          | 363.99                              | 363.99                       | 112.29                                  | 05/2018<br>09/2019    | 08/2019     |
|                                 | Total                                                                                                              |                  | 363.99<br>-                         | 363.99                       | 112.29                                  |                       |             |
|                                 | <u>PETROLEUM</u>                                                                                                   |                  |                                     |                              |                                         |                       |             |
|                                 | <u>Gas Authority Of India Limited</u>                                                                              |                  |                                     |                              |                                         |                       |             |
| 3                               | LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT<br>- [N16000271]          | 7/2015           | 2,881.40<br>-                       | 2,000.00                     | 1,090.43                                | 12/2019<br>12/2020    | 12/2019     |
|                                 | <u>Hindustan Petroleum Corporation Limited</u>                                                                     |                  |                                     |                              |                                         |                       |             |
| 4                               | MUMBAI REFINERY EXPANSION PROJECT<br>- [N16000281]                                                                 | 9/2015           | 4,199.00                            | 4,199.00                     | 194.97                                  | 03/2020<br>-          | 07/2019     |
|                                 | <u>Indian Oil Corporation Limited</u>                                                                              |                  |                                     |                              |                                         |                       |             |
| 5                               | PARADIP HYDERABAD PIPELINE<br>- [N16000194]                                                                        | 1/2015           | 2,321.00<br>3,338.00                | 3,338.00                     | 941.59                                  | 12/2020<br>-          | 08/2020     |
| 6                               | RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH<br>- [N16000216]                                             | 1/2016           | 247.52<br>-                         | 247.52                       | 144.38                                  | 02/2019<br>-          | 01/2019     |
| 7                               | BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL<br>- [N16000252]                                          | 5/2016           | 664.00<br>-                         | 664.00                       | 455.62                                  | 12/2020<br>-          | 02/2020     |
| 8                               | 30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332] | 3/2018           | 3,712.00<br>-                       | 3,712.00                     | 6.28                                    | 09/2022<br>-          | 06/2021     |
| 9                               | BRANCH PIPELINE OF PAJPL TO UNA<br>- [N16000250]                                                                   | 2/2016           | 151.00<br>-                         | 151.00                       | 112.58                                  | 09/2019<br>-          | 02/2019     |
| 10                              | CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP<br>- [N16000226]                                           | 2/2016           | 356.00<br>-                         | 356.00                       | 205.41                                  | 05/2019<br>-          | 01/2019     |
| 11                              | JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE<br>- [N16000195]       | 2/2015           | 890.00<br>-                         | 887.00                       | 551.16                                  | 10/2019<br>-          | 03/2019     |
|                                 | Total                                                                                                              |                  | 15,421.92<br>-                      | 15,554.52                    | 3,702.42                                |                       |             |

Costing Rs. 150 Crore and above

(December 2018)

|       |                                                                                                                   |                  |                                     |                              |                                         | Date of Commissioning |             |
|-------|-------------------------------------------------------------------------------------------------------------------|------------------|-------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
| Sl.No | Project                                                                                                           | Date of Approval | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated |
| 1     | 2                                                                                                                 | 3                | 4                                   | 5                            | 6                                       | 7                     | 8           |
|       | <u>POWER</u>                                                                                                      |                  |                                     |                              |                                         |                       |             |
|       | <u>Power Grid Corporation Of India Limited</u>                                                                    |                  |                                     |                              |                                         |                       |             |
| 12    | WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246                                                             | 2/2017           | 204.12<br>204.12                    | 204.12                       | 102.17                                  | 09/2019<br>09/2019    | 03/2019     |
|       | Total                                                                                                             |                  | 204.12<br>-                         | 204.12                       | 102.17                                  |                       |             |
|       | <u>RAILWAYS</u>                                                                                                   |                  |                                     |                              |                                         |                       |             |
|       | <u>East Central Railways</u>                                                                                      |                  |                                     |                              |                                         |                       |             |
| 13    | GARHWA ROAD-RAMNA - [N22000465                                                                                    | 3/2015           | 348.23<br>-                         | 348.23                       | 104.98                                  | 03/2021<br>-          | 12/2020     |
|       | <u>North East Frontier Railway</u>                                                                                |                  |                                     |                              |                                         |                       |             |
| 14    | AGARTALA SABROOM, NL, NEFR - [N22000099                                                                           | 4/2008           | 1,142.00<br>3,407.00                | 3,407.00                     | 3,112.16                                | 03/2014<br>12/2019    | 03/2019     |
| 15    | BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388                                                                | 4/2015           | 2,232.32<br>-                       | 2,182.00                     | 235.52                                  | 03/2022<br>-          | 03/2020     |
| 16    | NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390                                     | 4/2016           | 602.27<br>-                         | 612.00                       | 23.69                                   | 12/2021<br>-          | 03/2020     |
|       | <u>North Eastern Railway</u>                                                                                      |                  |                                     |                              |                                         |                       |             |
| 17    | HATHUA-BHATNI (N L) (NER) - [220100319                                                                            | 4/2005           | 230.03<br>-                         | 770.08                       | 274.67                                  | 12/2022<br>-          | 05/2019     |
| 18    | ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347                                                                  | 3/2015           | 1,295.42<br>-                       | 1,295.42                     | 99.33                                   | 03/2022<br>-          | 02/2019     |
|       | <u>North Western Railway</u>                                                                                      |                  |                                     |                              |                                         |                       |             |
| 19    | BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137                                                                     | 4/2012           | 246.08<br>-                         | 348.55                       | 139.09                                  | 12/2019<br>-          | 06/2019     |
| 20    | MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR - [N22000152                                           | 4/2013           | 420.18<br>295.02                    | 420.18                       | 89.61                                   | 03/2020<br>-          | 12/2019     |
|       | <u>Rail Vikas Nigam Ltd.</u>                                                                                      |                  |                                     |                              |                                         |                       |             |
| 21    | DIGHI PORT NEW LINE - [N22000408                                                                                  | 4/2015           | 723.78<br>-                         | 723.78                       | 0.22                                    | 12/2025<br>-          | 03/2025     |
|       | Total                                                                                                             |                  | 7,240.31<br>-                       | 10,107.24                    | 4,079.27                                |                       |             |
|       | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                |                  |                                     |                              |                                         |                       |             |
|       | <u>Ministry Of Road Transport And Highways</u>                                                                    |                  |                                     |                              |                                         |                       |             |
| 22    | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821 | 11/2017          | 257.34<br>-                         | 238.00                       | 41.09                                   | 11/2019<br>12/2019    | 11/2019     |
|       | <u>National Highways Authority Of India</u>                                                                       |                  |                                     |                              |                                         |                       |             |
| 23    | DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660     | 3/2017           | 296.19<br>-                         | 254.00                       | 97.80                                   | 03/2020<br>-          | 05/2019     |
| 24    | 4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664  | 3/2017           | 639.79<br>-                         | 552.90                       | 46.24                                   | 03/2020<br>-          | 06/2019     |

Costing Rs. 150 Crore and above

(December 2018)

|       |                                                                                         |                  |                                     |                              |                                         | Date of Commissioning |             |
|-------|-----------------------------------------------------------------------------------------|------------------|-------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
| Sl.No | Project                                                                                 | Date of Approval | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated |
| 1     | 2                                                                                       | 3                | 4                                   | 5                            | 6                                       | 7                     | 8           |
| 25    | 4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669           | 3/2017           | 165.50 -                            | 172.16                       | 20.01                                   | 03/2020 -             | 06/2019     |
| 26    | 4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670 | 3/2017           | 239.68 -                            | 235.90                       | 46.25                                   | 03/2020 -             | 06/2019     |
| 27    | SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691                   | 4/2017           | 894.00                              | 894.00                       | 15.00                                   | 04/2020 -             | 11/2019     |
|       | Total                                                                                   |                  | 2,492.50 -                          | 2,346.96                     | 266.39                                  |                       |             |
|       |                                                                                         |                  |                                     |                              |                                         |                       |             |
|       | Grand Total                                                                             |                  | 26,909.48                           | 28,780.65                    | 8,366.39                                |                       |             |

## List of Projects on schedule w.r.t. Latest Schedule

### Annexure - XII

| Costing Rs. 150 Crore and above |                                                                                  |                  |                                    |                              |                                         | (December 2018)       |             |
|---------------------------------|----------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                                                  |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                                          | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                                                | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
|                                 | <u>COAL</u>                                                                      |                  |                                    |                              |                                         |                       |             |
|                                 | <u>Bharat Coking Coal Limited</u>                                                |                  |                                    |                              |                                         |                       |             |
| 1                               | NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)<br>- [N06000106]                | 2/2014           | 555.52<br>-                        | 555.52                       | 5.01                                    | 03/2021<br>-          | 03/2021     |
|                                 | <u>Central Coal Fields Limited</u>                                               |                  |                                    |                              |                                         |                       |             |
| 2                               | AMRAPALI OC(12MTY)<br>- [N06000103]                                              | 2/2012           | 858.11<br>-                        | 858.11                       | 184.43                                  | 03/2020<br>-          | 03/2020     |
|                                 | <u>Eastern Coal Fields Limited</u>                                               |                  |                                    |                              |                                         |                       |             |
| 3                               | JHANJRA COMBINED PR(3.50 MTY)<br>- [N06000020]                                   | 11/2015          | 602.86<br>-                        | 602.86                       | 298.21                                  | 03/2022<br>-          | 03/2022     |
| 4                               | SIDULI MINE (OC AND UG)<br>- [N06000165]                                         | 5/2018           | 535.18<br>-                        | 535.18                       | -                                       | 03/2026<br>-          | 03/2026     |
| 5                               | HURA - C OC (3 MTY)<br>- [N06000143]                                             | 10/2015          | 359.69<br>-                        | 359.69                       | 42.44                                   | 03/2022<br>-          | 03/2022     |
|                                 | <u>Mahanadi Coal Fields Limited</u>                                              |                  |                                    |                              |                                         |                       |             |
| 6                               | SIARMAL OCP (40.00MTY)<br>- [N06000113]                                          | 5/2014           | 3,756.36<br>-                      | 3,756.36                     | 689.33                                  | 03/2026<br>-          | 03/2026     |
| 7                               | GARJANBAHAL OCP<br>- [N06000117]                                                 | 11/2014          | 1,375.38<br>-                      | 1,375.38                     | 424.90                                  | 03/2021<br>-          | 03/2021     |
| 8                               | INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP<br>- [N06000167]                        | 5/2018           | 2,434.75<br>-                      | 2,434.75                     | -                                       | 03/2027<br>-          | 03/2027     |
|                                 | <u>Neyveli Lignite Corporation</u>                                               |                  |                                    |                              |                                         |                       |             |
| 9                               | EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)<br>- [N06000138] | 4/2013           | 1,458.17<br>-                      | 709.06                       | 399.03                                  | 06/2015<br>09/2019    | 09/2019     |
| 10                              | NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW<br>- [N06000152]             | 7/2016           | 17,237.00<br>-                     | 17,237.80                    | 4,026.50                                | 11/2021<br>-          | 11/2021     |
| 11                              | HADLA LIGNITE MINE PROJECT(1.90 MTPA)<br>- [N06000144]                           | 3/2015           | 522.45<br>-                        | 522.45                       | 8.71                                    | 09/2019<br>-          | 09/2019     |
| 12                              | BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)<br>- [N06000145]                        | 3/2015           | 513.63<br>-                        | 513.63                       | 173.06                                  | 12/2019<br>-          | 12/2019     |
|                                 | <u>Northern Coal Fields Limited</u>                                              |                  |                                    |                              |                                         |                       |             |
| 13                              | JAYANT EXPANSION OCP 10 TO 20 MTPA<br>- [N06000159]                              | 5/2017           | 1,783.09<br>-                      | 1,783.09                     | 229.76                                  | 03/2021<br>-          | 03/2021     |
| 14                              | DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)<br>- [N06000162]                         | 11/2017          | 1,255.17<br>-                      | 1,255.17                     | 94.68                                   | 03/2022<br>-          | 03/2022     |
|                                 | <u>Singareni Colliers Company Limited</u>                                        |                  |                                    |                              |                                         |                       |             |
| 15                              | KAKATIYAKHANI OPENCAST-2 PROJECT<br>- [N06000129]                                | 5/2015           | 397.09<br>-                        | 442.42                       | 79.96                                   | 03/2019<br>-          | 03/2019     |
| 16                              | KAKATIYAKHANI OPENCAST III PROJECT PHASE-1<br>- [N06000161]                      | 3/2017           | 413.84<br>-                        | 413.84                       | -                                       | 03/2019<br>-          | 03/2019     |
| 17                              | KALYANIKHANI 6 INCLINE PROJECT<br>- [N06000147]                                  | 12/2015          | 477.65<br>-                        | 477.65                       | -                                       | 03/2020<br>-          | 03/2020     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                            |                  |                                    |                              |                                         | (December 2018)       |             |
|---------------------------------|------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                            |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                    | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                          | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
|                                 | <u>South-Eastern Coal Fields Limited</u>                   |                  |                                    |                              |                                         |                       |             |
| 18                              | PELMA OCP(15.00MTY)<br>- [N06000045]                       | 11/2014          | 1,624.59<br>-                      | 1,624.59                     | 6.13                                    | 03/2023<br>-          | 03/2023     |
| 19                              | CHHAL OC SEAM -III (6.00 MTY)<br>- [N06000104]             | 12/2013          | 610.63<br>-                        | 610.63                       | 81.27                                   | 03/2022<br>-          | 03/2022     |
| 20                              | BIJARI OC RCE (1.50 MTY)<br>- [N06000111]                  | 5/2014           | 164.49<br>-                        | 164.49                       | 67.20                                   | 03/2020<br>-          | 03/2020     |
| 21                              | JHIRIA WEST OPENCAST PROJECT<br>- [N06000166]              | 11/2018          | 389.97<br>-                        | 389.97                       | -                                       | 03/2026<br>-          | 03/2026     |
| 22                              | MAHAMAYA OPENCAST PROJECT<br>- [N06000164]                 | 5/2018           | 410.26<br>-                        | 410.26                       | 9.53                                    | 03/2026<br>-          | 03/2026     |
| 23                              | VIJAY WEST OPENCAST PROJECT<br>- [N06000158]               | 5/2017           | 976.95<br>-                        | 976.95                       | 75.96                                   | 03/2026<br>-          | 03/2026     |
| 24                              | AMADAND OPENCAST EXPANSION PROJECT<br>- [N06000148]        | 3/2016           | 869.44<br>-                        | 869.44                       | 111.89                                  | 03/2021<br>-          | 03/2021     |
| 25                              | GEVRA EXPANSION OCP (SECL) (35-70) MTY<br>- [060100093]    | 6/2010           | 11,816.40<br>-                     | 11,816.40                    | 2,848.30                                | 03/2023<br>-          | 03/2023     |
| 26                              | KUSMUNDA EXPN.OCP(SECL)(15-50)MTY<br>- [N06000008]         | 8/2013           | 7,612.33<br>-                      | 7,612.33                     | 1,913.96                                | 03/2023<br>-          | 03/2023     |
| 27                              | DURGAPUR OPENCAST PROJECT<br>- [N06000136]                 | 2/2015           | 916.24<br>-                        | 916.24                       | 3.81                                    | 03/2023<br>-          | 03/2023     |
| 28                              | AMGAON OPENCAST PROJECT RCE<br>- [N06000135]               | 7/2015           | 316.10<br>-                        | 316.10                       | 59.99                                   | 03/2020<br>-          | 03/2020     |
| 29                              | BATURA HIGHWALL PROJECT<br>- [N06000134]                   | 7/2015           | 231.92<br>-                        | 231.92                       | -                                       | 03/2022<br>-          | 03/2022     |
| 30                              | KANCHAN OC EXPANSION<br>- [N06000125]                      | 12/2014          | 371.04<br>-                        | 371.04                       | 41.52                                   | 03/2021<br>-          | 03/2021     |
| 31                              | RAJNAGAR OCP RPR (1.70 MTY)<br>- [N06000124]               | 12/2014          | 357.80<br>-                        | 357.80                       | 113.19                                  | 03/2021<br>-          | 03/2021     |
| 32                              | AMRITDHARA OC PROJECT<br>- [N06000122]                     | 2/2015           | 481.60<br>-                        | 481.60                       | -                                       | 03/2023<br>-          | 03/2023     |
| 33                              | MADANNAGAR OPENCAST PROJECT<br>- [N06000140]               | 10/2015          | 1,875.32<br>-                      | 1,875.32                     | -                                       | 03/2024<br>-          | 03/2024     |
| 34                              | MALACHUA OPENCAST PROJECT<br>- [N06000139]                 | 10/2015          | 488.33<br>-                        | 488.33                       | 24.16                                   | 03/2023<br>-          | 03/2023     |
|                                 | <u>Western Coal Fields Limited</u>                         |                  |                                    |                              |                                         |                       |             |
| 35                              | MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE<br>- [N06000142] | 11/2015          | 498.42<br>-                        | 498.42                       | 59.20                                   | 03/2020<br>-          | 03/2020     |
| 36                              | AMALGAMATED PAUNI-II III OC MINE<br>- [N06000131]          | 6/2015           | 483.69<br>-                        | 483.69                       | 89.91                                   | 03/2021<br>-          | 03/2021     |
| 37                              | ADASA UG TO OC<br>- [N06000133]                            | 8/2015           | 288.90<br>-                        | 333.43                       | .02                                     | 03/2023<br>03/2024    | 03/2024     |
| 38                              | KOLAR PIMPRI EXTENSION OC<br>- [N06000160]                 | 3/2017           | 362.73<br>-                        | 362.73                       | 258.23                                  | 03/2020<br>-          | 03/2020     |
| 39                              | DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)<br>- [N06000157]    | 2/2017           | 328.00<br>-                        | 328.00                       | 90.65                                   | 03/2021<br>-          | 03/2021     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                                                                |                  |                                    |                              |                                         | (December 2018)       |             |
|---------------------------------|------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                                                                |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                                                        | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                                                              | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 40                              | DHANKASA UG (1.00 MTY)<br>- [N06000155]                                                        | 9/2016           | 458.07<br>-                        | 458.07                       | 16.00                                   | 03/2022<br>-          | 03/2022     |
| 41                              | NILJAI EXPANSION (DEEP) OC (3.5 MTY)<br>- [N06000154]                                          | 8/2016           | 319.76<br>-                        | 319.76                       | 58.04                                   | 03/2022<br>-          | 03/2022     |
| 42                              | COAL PROJECT NAME JAMUNIA UG (0.84 MTY)<br>- [N06000153]                                       | 7/2016           | 409.87<br>-                        | 409.87                       | 17.50                                   | 03/2022<br>-          | 03/2022     |
| 43                              | BHATADI EXPANSION OC MINE<br>- [N06000150]                                                     | 2/2016           | 304.52<br>-                        | 304.52                       | 129.39                                  | 03/2019<br>-          | 03/2019     |
| 44                              | AMALGAMATED GONDEGAON GHATROHAN OC<br>- [N06000149]                                            | 2/2016           | 198.68<br>-                        | 198.68                       | 254.72                                  | 03/2019<br>-          | 03/2019     |
| 45                              | PENGANGA OCP(REVISED)<br>- [N06000066]                                                         | 9/2014           | 441.82<br>-                        | 441.82                       | 187.02                                  | 03/2020<br>-          | 03/2020     |
| 46                              | AMALGAMATED YEKONA-I YEKONA-II<br>- [N06000132]                                                | 8/2015           | 727.28<br>-                        | 727.28                       | 238.43                                  | 03/2025<br>-          | 03/2025     |
| 47                              | SINGHORI OC MINE<br>- [N06000130]                                                              | 6/2015           | 205.49<br>-                        | 205.49                       | 105.34                                  | 03/2020<br>-          | 03/2020     |
| 48                              | MAKARDHOKRA I OC<br>- [N06000119]                                                              | 9/2014           | 266.23<br>-                        | 266.23                       | 143.29                                  | 03/2021<br>-          | 03/2021     |
| 49                              | DINESH OCP<br>- [N06000118]                                                                    | 11/2014          | 611.16<br>-                        | 611.16                       | 395.73                                  | 03/2020<br>-          | 03/2020     |
| 50                              | NEW MAJRI UG TO OC<br>- [N06000128]                                                            | 5/2015           | 295.56<br>-                        | 295.56                       | 88.13                                   | 03/2019<br>-          | 03/2019     |
|                                 | Total                                                                                          |                  | 70,249.53<br>-                     | 69,591.08                    | 14,144.53                               |                       |             |
|                                 |                                                                                                |                  |                                    |                              |                                         |                       |             |
|                                 | <u>DEFENCE PRODUCTION</u>                                                                      |                  |                                    |                              |                                         |                       |             |
|                                 | <u>Goa Shipyard Limited</u>                                                                    |                  |                                    |                              |                                         |                       |             |
| 51                              | CONSTRUCTION WORKS PHASE 4<br>- [N39000001]                                                    | 12/2016          | 167.69<br>168.00                   | 170.37                       | 103.91                                  | 05/2018<br>01/2019    | 01/2019     |
| 52                              | CONSTRUCTION WORKS PHASE 3B<br>- [N39000002]                                                   | 12/2016          | 285.95<br>286.00                   | 291.29                       | 56.87                                   | 08/2020<br>-          | 08/2020     |
|                                 | Total                                                                                          |                  | 453.64<br>-                        | 461.66                       | 160.78                                  |                       |             |
|                                 |                                                                                                |                  |                                    |                              |                                         |                       |             |
|                                 | <u>FERTILISERS</u>                                                                             |                  |                                    |                              |                                         |                       |             |
|                                 | <u>National Fertiliser Limited</u>                                                             |                  |                                    |                              |                                         |                       |             |
| 53                              | GAS TURBO GENERATOR AND HEAT RECOVERY<br>STEAM GENERATOR PROJECT NFL PANIPAT<br>- [N08000014]  | 1/2018           | 215.92<br>-                        | 215.92                       | 27.51                                   | 11/2019<br>-          | 11/2019     |
| 54                              | GAS TURBO GENERATOR AND HEAT RECOVERY<br>STEAM GENERATOR PROJECT NFL NANGAL<br>- [N08000016]   | 1/2018           | 239.81<br>-                        | 239.81                       | 32.18                                   | 11/2019<br>-          | 11/2019     |
| 55                              | GAS TURBO GENERATOR AND HEAT RECOVERY<br>STEAM GENERATOR PROJECT NFL BATHINDA<br>- [N08000015] | 1/2018           | 218.83<br>-                        | 218.83                       | 26.47                                   | 11/2019<br>-          | 11/2019     |
|                                 | <u>Rashtriya Chemical &amp; Fertiliser Limited</u>                                             |                  |                                    |                              |                                         |                       |             |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                                                                             |                  |                                    |                              |                                         | Date of Commissioning |             |
|---------------------------------|-------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                                                                             |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                                                                     | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                                                                           | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 56                              | NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY<br>- [N08000009]                                            | 10/2014          | 197.79<br>-                        | 209.44                       | 140.10                                  | 11/2016<br>04/2019    | 04/2019     |
| 57                              | GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY<br>- [N08000018]             | 4/2018           | 426.72<br>-                        | 426.72                       | 50.89                                   | 04/2020<br>-          | 04/2020     |
| 58                              | GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL.<br>- [N08000010]                    | 2/2016           | 482.85<br>-                        | 482.85                       | 413.00                                  | 12/2017<br>01/2019    | 01/2019     |
|                                 | Total                                                                                                       |                  | 1,781.92<br>-                      | 1,793.57                     | 690.15                                  |                       |             |
|                                 |                                                                                                             |                  |                                    |                              |                                         |                       |             |
|                                 | <u>HEALTH AND FAMILY WELFARE</u>                                                                            |                  |                                    |                              |                                         |                       |             |
|                                 | <u>HII Infra Tech Services Limited</u>                                                                      |                  |                                    |                              |                                         |                       |             |
| 59                              | ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)<br>- [N21000025]                                 | 7/2016           | 785.00<br>-                        | 785.00                       | 39.35                                   | 04/2020<br>-          | 04/2020     |
| 60                              | ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB<br>- [N21000026]                                 | 7/2016           | 703.00<br>-                        | 703.00                       | 272.00                                  | 06/2020<br>-          | 06/2020     |
| 61                              | ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM<br>- [N21000027]                                  | 5/2017           | 875.00<br>-                        | 875.00                       | 174.00                                  | 05/2021<br>-          | 05/2021     |
|                                 | <u>Hospital Services Consultancy Corporation</u>                                                            |                  |                                    |                              |                                         |                       |             |
| 62                              | RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH<br>- [N21000017]                 | 8/2017           | 272.19<br>-                        | 272.19                       | 104.84                                  | 03/2019<br>-          | 03/2019     |
|                                 | <u>Hospital Services Consultancy Corporation Ltd</u>                                                        |                  |                                    |                              |                                         |                       |             |
| 63                              | LHMC NEW DELHI-RE-DEVELOPMENT<br>- [N21000003]                                                              | 2/2013           | 414.11<br>-                        | 513.89                       | 141.00                                  | 11/2013<br>10/2020    | 10/2020     |
| 64                              | RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARAstra<br>- [N21000016]                                | 8/2017           | 274.19<br>-                        | 274.19                       | 114.89                                  | 03/2019<br>-          | 03/2019     |
| 65                              | RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL<br>- [N21000018]                              | 8/2017           | 355.15<br>-                        | 355.15                       | 112.08                                  | 03/2019<br>-          | 03/2019     |
|                                 | Total                                                                                                       |                  | 3,678.64<br>-                      | 3,778.42                     | 958.16                                  |                       |             |
|                                 |                                                                                                             |                  |                                    |                              |                                         |                       |             |
|                                 | <u>HEAVY INDUSTRY</u>                                                                                       |                  |                                    |                              |                                         |                       |             |
|                                 | <u>Indira Gandhi Centre For Atomic Research</u>                                                             |                  |                                    |                              |                                         |                       |             |
| 66                              | DEVELOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA<br>- [N20000002] | 8/2016           | 1,554.00<br>-                      | 1,554.00                     | 161.86                                  | 09/2019<br>-          | 09/2019     |
|                                 | Total                                                                                                       |                  | 1,554.00<br>-                      | 1,554.00                     | 161.86                                  |                       |             |
|                                 |                                                                                                             |                  |                                    |                              |                                         |                       |             |
|                                 | <u>MINES</u>                                                                                                |                  |                                    |                              |                                         |                       |             |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                                                                                    |                  |                                    |                              |                                         | (December 2018)       |             |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                                                                                    |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                                                                            | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                                                                                  | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
|                                 | <u>National Aluminum Company Limited (Nalco)</u>                                                                   |                  |                                    |                              |                                         |                       |             |
| 67                              | 5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]                                                        | 12/2014          | 5,540.00 -                         | 5,540.00                     | 96.98                                   | 04/2021<br>04/2021    | 04/2021     |
| 68                              | SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013] | 11/2017          | 483.00 -                           | 483.00                       | -                                       | 04/2021<br>04/2021    | 04/2021     |
| 69                              | UTKAL D AND E COAL BLOCK - [N10000011]                                                                             | 5/2016           | 534.00 -                           | 534.00                       | 302.60                                  | 01/2020<br>01/2020    | 01/2020     |
| 70                              | 25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]                                                  | 9/2017           | 166.62 -                           | 166.62                       | 125.00                                  | 06/2019<br>06/2019    | 06/2019     |
| 71                              | CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012] | 12/2015          | 355.00 -                           | 355.00                       | 31.92                                   | 11/2020<br>-          | 11/2020     |
|                                 | Total                                                                                                              |                  | 7,078.62 -                         | 7,078.62                     | 556.50                                  |                       |             |
|                                 |                                                                                                                    |                  |                                    |                              |                                         |                       |             |
|                                 | <u>PETROLEUM</u>                                                                                                   |                  |                                    |                              |                                         |                       |             |
|                                 | <u>Bharat Petroleum Corporation Limited</u>                                                                        |                  |                                    |                              |                                         |                       |             |
| 72                              | HALDIA LPG IMPORT FACILITY - [N16000223]                                                                           | 3/2015           | 694.00 -                           | 694.00                       | 530.79                                  | 10/2018<br>06/2019    | 06/2019     |
| 73                              | 2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]                                                                   | 8/2017           | 750.00 -                           | 750.00                       | 24.43                                   | 12/2020<br>-          | 12/2020     |
| 74                              | KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]                                                                     | 12/2015          | 1,112.00 -                         | 1,112.00                     | 108.79                                  | 06/2019<br>-          | 06/2019     |
| 75                              | PUNE POL STORAGE DEPOT - [N16000313]                                                                               | 8/2016           | 282.64 -                           | 282.64                       | 63.91                                   | 08/2020<br>-          | 08/2020     |
| 76                              | MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]                               | 2/2016           | 3,313.00 -                         | 3,288.96                     | 404.03                                  | 02/2020<br>10/2020    | 10/2020     |
| 77                              | MMPL PIPELINE REROUTING PROJECT - [N16000261]                                                                      | 4/2013           | 449.58 -                           | 449.58                       | 118.17                                  | 12/2019<br>-          | 12/2019     |
| 78                              | INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]             | 2/2016           | 554.00 -                           | 554.00                       | 158.76                                  | 02/2020<br>-          | 02/2020     |
| 79                              | PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]                                  | 11/2014          | 4,588.29 -                         | 5,245.96                     | 2,543.09                                | 08/2018<br>11/2019    | 11/2019     |
|                                 | <u>Chennai Petroleum Corporation Limited</u>                                                                       |                  |                                    |                              |                                         |                       |             |
| 80                              | BS-VI PROJECTS - [N16000295]                                                                                       | 9/2017           | 1,858.00 -                         | 1,858.00                     | 620.25                                  | 12/2019<br>-          | 12/2019     |
| 81                              | RE-LIQUIFIED NATURAL GAS - [N16000301]                                                                             | 8/2017           | 421.00 -                           | 421.00                       | 19.68                                   | 08/2020<br>-          | 08/2020     |
|                                 | <u>Gas Authority Of India Limited</u>                                                                              |                  |                                    |                              |                                         |                       |             |
| 82                              | GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]                                                                   | 2/2015           | 749.00 -                           | 749.00                       | 733.62                                  | 02/2020<br>-          | 02/2020     |
| 83                              | DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]                                                                        | 3/2017           | 1,933.00 -                         | 1,933.00                     | 814.01                                  | 12/2020<br>-          | 12/2020     |



## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                                                                                       |                  |                                    |                              |                                         | (December 2018)       |             |
|---------------------------------|-----------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                                                                                       |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                                                                               | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                                                                                     | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 84                              | BOKARO-ANGUL PIPELINE PROJECT<br>- [N16000274]                                                                        | 3/2017           | 3,437.00<br>-                      | 3,437.00                     | 1,006.30                                | 12/2020<br>-          | 12/2020     |
| 85                              | CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI<br>- [N16000288]                                                         | 4/2017           | 287.49<br>-                        | 287.49                       | 102.07                                  | 04/2022<br>-          | 04/2022     |
| 86                              | BARAUNI-GUWAHATI PIPELINE<br>- [N16000334]                                                                            | 6/2018           | 3,308.00<br>-                      | 3,308.00                     | 2.63                                    | 12/2021<br>-          | 12/2021     |
| 87                              | CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR<br>[N16000330]                                                        | 10/2017          | 221.45<br>-                        | 221.45                       | 23.92                                   | 10/2022<br>-          | 10/2022     |
| 88                              | CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI<br>- [N16000329]                                                          | 10/2017          | 226.45<br>-                        | 226.45                       | 25.11                                   | 10/2022<br>-          | 10/2022     |
| 89                              | CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK<br>- [N16000328]                                                         | 7/2017           | 181.20<br>-                        | 181.20                       | 15.72                                   | 07/2022<br>-          | 07/2022     |
| 90                              | CITY GAS DISTRIBUTION (CGD) NETWORK PATNA<br>- [N16000327]                                                            | 10/2017          | 359.25<br>-                        | 359.25                       | 38.05                                   | 10/2022<br>-          | 10/2022     |
| 91                              | CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR<br>[N16000289]                                                       | 7/2017           | 243.53<br>-                        | 243.53                       | 35.47                                   | 07/2022<br>-          | 07/2022     |
| 92                              | DURGAPUR-HALDIA PIPELINE PROJECT<br>- [N16000275]                                                                     | 3/2017           | 1,740.00<br>-                      | 1,740.00                     | 22.96                                   | 12/2020<br>-          | 12/2020     |
| 93                              | DOBHI-DURGAPUR PIPELINE PROJECT<br>- [N16000273]                                                                      | 3/2017           | 2,433.00<br>-                      | 2,433.00                     | 956.29                                  | 12/2020<br>-          | 12/2020     |
|                                 | <u>Hindustan Petroleum Corporation Limited</u>                                                                        |                  |                                    |                              |                                         |                       |             |
| 94                              | URAN CHAKAN SHIKRAPUR LPG PIPELINE<br>- [N16000155]                                                                   | 12/2009          | 309.81<br>-                        | 723.40                       | 586.10                                  | 10/2014<br>02/2019    | 02/2019     |
| 95                              | EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST -<br>[N16000296] | 9/2017           | 2,677.00<br>-                      | 2,677.00                     | 49.88                                   | 03/2021<br>-          | 03/2021     |
| 96                              | CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA<br>[N16000312]                           | 11/2017          | 255.00<br>-                        | 255.00                       | 15.68                                   | 11/2020<br>-          | 11/2020     |
| 97                              | 120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE<br>- [N16000316]                                                       | 6/2017           | 161.50<br>-                        | 161.50                       | 17.78                                   | 06/2020<br>-          | 06/2020     |
| 98                              | 180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA<br>[N16000315]                                         | 6/2017           | 249.26<br>-                        | 249.26                       | 58.33                                   | 06/2020<br>-          | 06/2020     |
| 99                              | CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH -<br>[N16000311]  | 12/2016          | 300.00<br>-                        | 300.00                       | -                                       | 04/2021<br>-          | 04/2021     |
| 100                             | VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT<br>[N16000237]                                    | 9/2016           | 407.00<br>-                        | 407.00                       | 262.64                                  | 09/2019<br>-          | 09/2019     |
| 101                             | RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA)<br>- [N16000242]                          | 11/2016          | 230.00<br>-                        | 230.00                       | 114.14                                  | 02/2019<br>-          | 02/2019     |
| 102                             | MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION<br>- [N16000238]                                     | 9/2016           | 1,879.00<br>-                      | 1,879.00                     | 1,015.35                                | 06/2020<br>-          | 06/2020     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                                                                                    |                  |                                    |                              |                                         | (December 2018)       |             |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                                                                                    |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                                                                            | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                                                                                  | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 103                             | VISAKH REFINERY MODERNISATION PROJECT<br>- [N16000235]                                                             | 7/2016           | 20,928.00<br>-                     | 20,928.00                    | 2,757.64                                | 07/2020<br>-          | 07/2020     |
|                                 | <u>Indian Oil Corporation Limited</u>                                                                              |                  |                                    |                              |                                         |                       |             |
| 104                             | ENNORE-TRICHY-MADURAI LPG PIPELINE<br>- [N16000162]                                                                | 5/2013           | 711.00<br>-                        | 711.00                       | 11.12                                   | 06/2020<br>-          | 06/2020     |
| 105                             | PARADIP SOMNATHPUR HALDIA PIPELINE<br>- [N16000345]                                                                | 10/2018          | 1,297.50<br>-                      | 1,297.50                     | -                                       | 10/2021<br>-          | 10/2021     |
| 106                             | CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR<br>- [N16000344]                                        | 4/2018           | 522.00<br>-                        | 522.00                       | 2.56                                    | 03/2021<br>-          | 03/2021     |
| 107                             | REVAMPING OF FACILITIES AT VIZAG TERMINAL<br>- [N16000343]                                                         | 4/2018           | 355.00<br>-                        | 355.00                       | -                                       | 04/2022<br>-          | 04/2022     |
| 108                             | NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT<br>- [N16000340]                                                      | 8/2018           | 1,636.00<br>-                      | 1,636.00                     | 128.78                                  | 08/2020<br>-          | 08/2020     |
| 109                             | BS VI PROJECT AT GUWAHATI REFINERY<br>- [N16000339]                                                                | 8/2018           | 557.00<br>-                        | 557.00                       | 71.41                                   | 02/2020<br>-          | 02/2020     |
| 110                             | ETHYLENE GLYCOL PROJECT AT PARADIP<br>- [N16000338]                                                                | 4/2018           | 4,807.08<br>-                      | 4,807.08                     | 24.09                                   | 07/2021<br>-          | 07/2021     |
| 111                             | INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY<br>- [N16000337]                                                 | 7/2018           | 189.00<br>-                        | 189.00                       | 4.04                                    | 01/2021<br>-          | 01/2021     |
| 112                             | BS-VI PROJECT AT BONGAIGAON REFINERY<br>- [N16000320]                                                              | 5/2018           | 1,222.00<br>-                      | 1,222.00                     | 287.90                                  | 09/2019<br>-          | 09/2019     |
| 113                             | LPG BP PROJECT MOTIHARI<br>- [N16000317]                                                                           | 5/2018           | 206.50<br>-                        | 206.50                       | -                                       | 03/2021<br>-          | 03/2021     |
| 114                             | BS-VI PROJECT AT GUJARAT REFINERY<br>- [N16000310]                                                                 | 3/2018           | 3,380.00<br>-                      | 3,380.00                     | 1,246.09                                | 09/2019<br>-          | 09/2019     |
| 115                             | CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY<br>- [N16000309]             | 8/2017           | 1,342.00<br>-                      | 1,342.00                     | 3.90                                    | 08/2020<br>-          | 08/2020     |
| 116                             | CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY<br>- [N16000308]                                        | 8/2017           | 315.00<br>-                        | 315.00                       | 2.87                                    | 12/2021<br>-          | 12/2021     |
| 117                             | BS-VI PROJECT AT MATHURA REFINERY<br>- [N16000306]                                                                 | 1/2018           | 666.64<br>-                        | 666.64                       | 223.54                                  | 09/2019<br>-          | 09/2019     |
| 118                             | CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP<br>- [N16000302]                                                    | 8/2017           | 384.58<br>-                        | 384.58                       | 41.38                                   | 04/2021<br>-          | 04/2021     |
| 119                             | KHARAGPUR LPG BOTTLING PLANT<br>- [N16000300]                                                                      | 4/2017           | 163.02<br>-                        | 163.02                       | 32.69                                   | 04/2020<br>-          | 04/2020     |
| 120                             | ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE<br>- [N16000269]           | 1/2015           | 342.00<br>-                        | 342.00                       | -                                       | 03/2021<br>-          | 03/2021     |
| 121                             | AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333] | 3/2018           | 676.00<br>-                        | 676.00                       | 4.83                                    | 12/2021<br>-          | 12/2021     |
| 122                             | CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE<br>- [N16000326]      | 10/2017          | 906.00<br>-                        | 906.00                       | 13.52                                   | 02/2020<br>-          | 02/2020     |
| 123                             | BS-VI PROJECT AT PANIPAT REFINERY<br>- [N16000325]                                                                 | 12/2017          | 3,529.00<br>-                      | 3,529.00                     | 952.69                                  | 07/2019<br>-          | 07/2019     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                                                                                      |                  |                                    |                              |                                         | (December 2018)       |             |
|---------------------------------|----------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                                                                                      |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                                                                              | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                                                                                    | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 124                             | DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]              | 12/2017          | 199.36 -                           | 199.36                       | -                                       | 10/2020 -             | 10/2020     |
| 125                             | INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]       | 8/2017           | 255.40 -                           | 255.40                       | .06                                     | 08/2020 -             | 08/2020     |
| 126                             | BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]                                                             | 5/2018           | 2,934.40 -                         | 2,934.40                     | 843.32                                  | 09/2019 -             | 09/2019     |
| 127                             | CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]                                  | 4/2018           | 206.63 -                           | 206.63                       | .52                                     | 02/2020 -             | 02/2020     |
| 128                             | MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]                                                                           | 9/2015           | 324.00 -                           | 324.00                       | 96.21                                   | 06/2020 -             | 06/2020     |
| 129                             | HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]                                                                        | 4/2016           | 1,021.00 -                         | 1,021.00                     | 4.45                                    | 12/2020 -             | 12/2020     |
| 130                             | KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]                                                                     | 5/2016           | 1,945.00 -                         | 1,945.00                     | 514.20                                  | 08/2021 -             | 08/2021     |
| 131                             | INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]                                                                  | 2/2016           | 2,582.00 -                         | 2,582.00                     | 1,281.75                                | 11/2019 -             | 11/2019     |
| 132                             | DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]       | 6/2016           | 423.00 -                           | 423.00                       | 217.07                                  | 08/2019 -             | 08/2019     |
| 133                             | PARADIP LPG IMPORT FACILITY - [N16000196]                                                                            | 1/2015           | 690.00 -                           | 690.00                       | 191.48                                  | 07/2018<br>10/2020    | 10/2020     |
| 134                             | AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]      | 1/2015           | 1,823.00 -                         | 1,823.00                     | 579.41                                  | 12/2020 -             | 12/2020     |
| 135                             | POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]                                                                | 3/2014           | 3,150.00 -                         | 3,150.00                     | 2,494.51                                | 09/2017<br>12/2018    | 12/2018     |
| 136                             | AUGMENTATION OF CTMPL - [N16000286]                                                                                  | 12/2016          | 228.00 -                           | 228.00                       | 1.84                                    | 06/2020 -             | 06/2020     |
| 137                             | INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]                | 9/2016           | 208.35 -                           | 208.35                       | 67.71                                   | 07/2020 -             | 07/2020     |
| 138                             | LPG BP PROJECT KHORDHA - [N16000283]                                                                                 | 12/2016          | 161.59 -                           | 161.59                       | 33.93                                   | 12/2019 -             | 12/2019     |
| 139                             | SITARGANJ LPG PROJECT - [N16000282]                                                                                  | 2/2017           | 160.10 -                           | 160.10                       | 27.35                                   | 02/2020 -             | 02/2020     |
| 140                             | INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]                                     | 5/2016           | 429.00 -                           | 429.00                       | 291.90                                  | 01/2019 -             | 01/2019     |
| 141                             | ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276] | 5/2016           | 261.00 -                           | 261.00                       | 8.48                                    | 01/2021 -             | 01/2021     |
| 142                             | REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]                                                      | 7/2014           | 247.00 -                           | 247.00                       | -                                       | 03/2021 -             | 03/2021     |
|                                 | <u>Mangalore Refinery And Petrochemicals Limited</u>                                                                 |                  |                                    |                              |                                         |                       |             |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                                                          |                  |                                    |                              |                                         | (December 2018)       |             |
|---------------------------------|------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                                                          |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                                                  | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                                                        | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 143                             | CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU<br>- [N16000255]      | 5/2015           | 224.00<br>207.00                   | 207.25                       | 99.99                                   | 04/2019<br>-          | 04/2019     |
| 144                             | BSVI UPGRADATION<br>- [N16000257]                                                        | 9/2016           | 1,810.00<br>1,810.00               | 1,810.00                     | 130.79                                  | 12/2019<br>-          | 12/2019     |
| 145                             | SEA WATER DESALINATION PLANT<br>- [N16000319]                                            | 11/2017          | 581.00<br>-                        | 581.00                       | -                                       | 03/2020<br>-          | 03/2020     |
| 146                             | RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE<br>- [N16000256]                        | 10/2015          | 135.00<br>171.00                   | 170.70                       | 124.25                                  | 03/2019<br>-          | 03/2019     |
|                                 | <u>Oil &amp; Natural Gas Corporation Limited</u>                                         |                  |                                    |                              |                                         |                       |             |
| 147                             | ASSAM RENEWAL PROJECT FOR GROUP A<br>- [N16000061]                                       | 3/2009           | 2,465.15<br>-                      | 2,378.86                     | 2,107.69                                | 03/2013<br>03/2019    | 03/2019     |
| 148                             | MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III<br>- [N16000197]                         | 11/2014          | 6,068.80<br>-                      | 5,296.93                     | 4,576.40                                | 04/2019<br>03/2019    | 03/2019     |
| 149                             | DAMAN DEVELOPMENT PROJECT<br>- [N16000198]                                               | 8/2014           | 6,086.08<br>-                      | 5,842.31                     | 4,513.89                                | 05/2019<br>10/2019    | 10/2019     |
| 150                             | NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY<br>- [N16000204]     | 8/2015           | 2,818.88<br>-                      | 2,818.88                     | 1,724.53                                | 03/2019<br>05/2020    | 05/2020     |
| 151                             | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)<br>- [N16000128] | 3/2011           | 861.79<br>-                        | 1,577.15                     | 1,195.62                                | 05/2013<br>03/2019    | 03/2019     |
| 152                             | PIPELINE REPLACEMENT PROJECT-V (OFFSHORE)<br>- [N16000335]                               | 4/2018           | 766.37<br>-                        | 766.37                       | -                                       | 12/2019<br>-          | 12/2019     |
| 153                             | DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)<br>- [N16000297]        | 2/2017           | 4,006.83<br>-                      | 4,006.83                     | 1,651.58                                | 05/2021<br>05/2021    | 05/2021     |
| 154                             | 4TH PHASE DEVELOPMENT OF NBP FIELD<br>- [N16000294]                                      | 2/2017           | 968.61<br>-                        | 968.61                       | 601.19                                  | 11/2019<br>11/2019    | 11/2019     |
| 155                             | DEVELOPMENT OF BSE-11 BLOCK<br>- [N16000293]                                             | 2/2017           | 511.30<br>-                        | 511.30                       | 197.90                                  | 11/2019<br>11/2019    | 11/2019     |
| 156                             | DEVELOPMENT OF B-147 FIELD<br>- [N16000292]                                              | 2/2017           | 546.15<br>-                        | 546.15                       | 226.78                                  | 11/2019<br>11/2019    | 11/2019     |
| 157                             | NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY<br>- [N16000290]                | 1/2017           | 474.15<br>-                        | 474.15                       | 299.26                                  | 05/2019<br>05/2019    | 05/2019     |
| 158                             | FIELD DEVELOPMENT OF NBP BLOCK KG-ONN-2003, NAGAYALANKA-KG<br>- [N16000280]              | 4/2017           | 420.76<br>-                        | 207.80                       | 32.71                                   | 09/2018<br>02/2019    | 02/2019     |
| 159                             | REDEVELOPMENT OF SANTHAL FIELD<br>- [N16000279]                                          | 2/2017           | 1,162.56<br>-                      | 1,162.56                     | 294.16                                  | 03/2026<br>03/2026    | 03/2026     |
| 160                             | PIPELINE NETWORK PROJECT GELEKI, ASSAM<br>- [N16000278]                                  | 7/2016           | 249.85<br>250.00                   | 244.70                       | 101.71                                  | 05/2020<br>05/2020    | 05/2020     |
| 161                             | KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT<br>- [N16000247]                              | 3/2016           | 34,012.00<br>-                     | 34,012.00                    | 1,647.21                                | 06/2020<br>08/2021    | 08/2021     |
| 162                             | DEVELOPMENT PLAN OF CBM - BOKARO BLOCK<br>- [N16000239]                                  | 12/2015          | 658.62<br>-                        | 910.23                       | 109.60                                  | 03/2023<br>03/2022    | 03/2022     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                                                                                       |                  |                                    |                              |                                         | (December 2018)       |             |
|---------------------------------|-----------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                                                                                       |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                                                                               | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                                                                                     | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 163                             | LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS<br>- [N16000213]                                     | 12/2015          | 3,190.69<br>-                      | 3,247.19                     | 2,110.87                                | 04/2018<br>05/2019    | 05/2019     |
| 164                             | ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA<br>- [N16000212]      | 1/2015           | 4,619.94<br>-                      | 4,619.94                     | 3,951.60                                | 12/2017<br>03/2020    | 03/2020     |
| 165                             | INTEGRATED DEVELOPMENT OF B-127 FIELDS<br>- [N16000131]                                                               | 12/2011          | 2,059.63<br>-                      | 2,665.65                     | 1,842.42                                | 03/2015<br>12/2019    | 12/2019     |
| 166                             | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)<br>- [N16000127]                               | 6/2010           | 202.94<br>-                        | 330.35                       | 81.98                                   | 01/2014<br>11/2019    | 11/2019     |
| 167                             | GAMJI REDEVELOPMENT PROJECT<br>- [N16000202]                                                                          | 5/2015           | 1,671.22<br>-                      | 567.22                       | 449.95                                  | 11/2019<br>-          | 11/2019     |
|                                 | <u>Oil India Limited</u>                                                                                              |                  |                                    |                              |                                         |                       |             |
| 168                             | SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN<br>- [N16000167]               | 7/2011           | 352.56<br>-                        | 438.84                       | 196.39                                  | 03/2017<br>06/2019    | 06/2019     |
| 169                             | PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)<br>- [N16000258]                                                  | 5/2016           | 406.00<br>-                        | 406.00                       | 23.61                                   | 10/2020<br>-          | 10/2020     |
| 170                             | DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA<br>- [N16000331] | 1/2018           | 543.91<br>-                        | 543.91                       | 1.65                                    | 02/2020<br>-          | 02/2020     |
| 171                             | AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II<br>- [N16000259]                               | 9/2016           | 571.66<br>-                        | 571.66                       | 42.33                                   | 12/2019<br>-          | 12/2019     |
|                                 | Total                                                                                                                 |                  | 1,75,441.05<br>-                   | 1,75,926.36                  | 51,287.25                               |                       |             |
|                                 |                                                                                                                       |                  |                                    |                              |                                         |                       |             |
|                                 | <u>POWER</u>                                                                                                          |                  |                                    |                              |                                         |                       |             |
|                                 | <u>National Thermal Power Corporation</u>                                                                             |                  |                                    |                              |                                         |                       |             |
| 172                             | GADARWARA SUPER THERMAL POWER PROJECT STAGE-I<br>- [N18000151]                                                        | 3/2013           | 11,638.55<br>-                     | 12,865.92                    | 10,375.32                               | 09/2017<br>06/2019    | 06/2019     |
| 173                             | TAPOVAN-VISHNUGAD HEP (4X130MW)<br>- [N18000014]                                                                      | 11/2006          | 2,978.48<br>-                      | 3,846.30                     | 3,775.64                                | 03/2013<br>12/2020    | 12/2020     |
| 174                             | DARLIPALLI STPP STAGE-I (2X800 MW)<br>- [N18000176]                                                                   | 2/2014           | 12,532.44<br>-                     | 13,740.53                    | 8,441.41                                | 08/2018<br>06/2019    | 06/2019     |
| 175                             | RAMMAM-III HEPP (3X40 MW)<br>- [N18000178]                                                                            | 9/2014           | 1,381.84<br>-                      | 1,381.84                     | 384.28                                  | 09/2019<br>02/2022    | 02/2022     |
| 176                             | NORTH KARANPURA STPP (3X660 MW)<br>- [N18000177]                                                                      | 2/2014           | 14,366.58<br>-                     | 15,164.05                    | 7,916.41                                | 02/2019<br>10/2020    | 10/2020     |
| 177                             | TALAIPALLI COAL MINING PROJECT<br>- [N18000266]                                                                       | 9/2015           | 3,004.00<br>-                      | 3,004.00                     | 1,293.72                                | 11/2019<br>-          | 11/2019     |
| 178                             | TELANGANA SUPER THERMAL POWER PROJECT PHASE I<br>- [N18000212]                                                        | 1/2016           | 10,598.98<br>-                     | 10,598.98                    | 3,272.35                                | 07/2020<br>10/2020    | 10/2020     |
| 179                             | KHARGONE STPP STAGE I (1320 MW)<br>- [N18000205]                                                                      | 3/2015           | 9,870.51<br>-                      | 11,148.86                    | 6,693.90                                | 09/2019<br>-          | 09/2019     |
| 180                             | LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)<br>- [N18000140]                                                | 12/2012          | 11,846.00<br>-                     | 12,739.82                    | 10,831.46                               | 06/2017<br>06/2019    | 06/2019     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                                                                                           |                  |                                    |                              |                                         | (December 2018)       |             |
|---------------------------------|---------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                                                                                           |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                                                                                   | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                                                                                         | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 181                             | SOLAPUR STPP<br>- [N18000133]                                                                                             | 3/2012           | 9,395.18<br>-                      | 9,395.18                     | 9,026.43                                | 11/2016<br>03/2019    | 03/2019     |
| 182                             | BARH STPP(3X660MW) NTPC<br>- [180100242]                                                                                  | 2/2005           | 8,692.97<br>-                      | 15,095.67                    | 15,278.98                               | 01/2011<br>04/2021    | 04/2021     |
| 183                             | TANDA TPP STAGE-II (2X660 MW)<br>- [N18000175]                                                                            | 9/2014           | 9,188.98<br>-                      | 9,188.98                     | 5,433.65                                | 03/2019<br>09/2019    | 09/2019     |
|                                 | <u>North East Electric Power Corporation</u>                                                                              |                  |                                    |                              |                                         |                       |             |
| 184                             | KAMENG HYDROELECTRIC PROJECT (NEEPCO)<br>- [180100239]                                                                    | 12/2004          | 2,496.90<br>-                      | 6,179.96                     | 6,881.48                                | 12/2009<br>03/2019    | 03/2019     |
|                                 | <u>Power Grid Corporation Of India Limited</u>                                                                            |                  |                                    |                              |                                         |                       |             |
| 185                             | NORTH- EAST NORTH WESTERN INTERCONNECTOR I<br>PROJECT<br>- [N18000066]                                                    | 2/2009           | 11,130.19<br>-                     | 13,762.80                    | 12,723.70                               | 08/2013<br>03/2022    | 03/2022     |
| 186                             | S/S WORK ASSOCIATED WITH ADDITIONAL INTER<br>REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN<br>REGION I.E WARO - [N18000238]  | 3/2017           | 283.72<br>-                        | 283.72                       | 109.75                                  | 11/2019<br>11/2019    | 11/2019     |
| 187                             | INSTALLATION OF BUS REACTORS AT CUDDAPAH<br>NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB<br>STATION - [N18000236]            | 3/2017           | 251.60<br>-                        | 251.60                       | 112.11                                  | 06/2019<br>06/2019    | 06/2019     |
| 188                             | SOUTHERN REGION STRENGTHENING SCHEME-XXI<br>- [N18000233]                                                                 | 9/2016           | 562.25<br>-                        | 562.25                       | 103.00                                  | 03/2019<br>03/2019    | 03/2019     |
| 189                             | PROVISION OF STATECOM AT NALAGARH AND<br>LUCKNOW IN NORTHERN REGION<br>- [N18000231]                                      | 8/2016           | 431.89<br>-                        | 431.89                       | 213.66                                  | 02/2019<br>02/2019    | 02/2019     |
| 190                             | POWERGRID WORK ASSOCIATED WITH SYSTEM<br>STRENGTHENING FOR IPP IN CHATTISGARH AND<br>OTHER GEN. PROJECT IN - [N18000230]  | 7/2016           | 333.17<br>-                        | 333.17                       | 257.53                                  | 03/2019<br>03/2019    | 03/2019     |
| 191                             | PG WORKS ASSOCIATED WITH COMMON<br>TRANSMISSION SYSTEM FOR PHASE-II GENERATION<br>PROJECT IN ODISHA - [N18000223]         | 4/2016           | 844.64<br>-                        | 844.64                       | 303.70                                  | 04/2019<br>-          | 04/2019     |
| 192                             | ASSOCIATED TRANSMISSION SYSTEM FOR<br>NABINAGAR-II TIPS<br>[N18000222]                                                    | 4/2016           | 790.13<br>-                        | 790.30                       | 524.14                                  | 06/2019<br>06/2019    | 06/2019     |
| 193                             | HVDC BIPOLE LINK BETWEEN WR (RAIGARH,<br>CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-<br>SCHEME-I: RAIGARH-P - [N18000219] | 5/2016           | 14,733.37<br>-                     | 14,733.37                    | 5,084.05                                | 11/2019<br>11/2019    | 11/2019     |
| 194                             | GREEN ENERGY CORRIDORS - INTER STATE<br>TRANSMISSION SCHEME PART-D<br>- [N18000218]                                       | 5/2016           | 3,519.59<br>-                      | 3,519.59                     | 2,073.40                                | 05/2019<br>05/2019    | 05/2019     |
| 195                             | SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT<br>BANASKANTHA (RADHANESDA) GUJARAT<br>- [N18000269]                              | 12/2017          | 193.14<br>-                        | 193.14                       | 4.00                                    | 06/2019<br>06/2019    | 06/2019     |
| 196                             | EASTERN REGION STRENGTHENING SCHEME XX<br>- [N18000268]                                                                   | 11/2017          | 358.83<br>-                        | 358.83                       | -                                       | 05/2020<br>05/2020    | 05/2020     |
| 197                             | 400 KV D/C BAHARAMPUR (PG) - BHERAMERE<br>(B'DESH) LINE CKT II (INDIA PORTION)<br>[N18000267]                             | 9/2017           | 198.49<br>-                        | 198.49                       | 15.70                                   | 09/2019<br>02/2020    | 02/2020     |
| 198                             | HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH<br>TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING<br>AT PUGALUR EN - [N18000264]  | 8/2017           | 1,931.39<br>-                      | 1,931.39                     | 592.69                                  | 02/2020<br>02/2020    | 02/2020     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                                                                                     |                  |                                    |                              |                                         | Date of Commissioning |             |
|---------------------------------|---------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
| Sl.No                           | Project                                                                                                             | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                                                                                   | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 199                             | TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262] | 5/2017           | 186.17 -                           | 186.17                       | 63.07                                   | 07/2019<br>07/2019    | 07/2019     |
| 200                             | SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]                                                | 3/2017           | 337.75 -                           | 337.75                       | 26.00                                   | 06/2019<br>06/2019    | 06/2019     |
| 201                             | HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]  | 2/2017           | 5,070.13 -                         | 5,070.13                     | 1,044.71                                | 04/2020<br>04/2020    | 04/2020     |
| 202                             | SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]                                                    | 3/2017           | 379.95 -                           | 379.95                       | 22.22                                   | 12/2019<br>12/2019    | 12/2019     |
| 203                             | EASTERN REGION STRENGTHENING SCHEME XVII (PART B) - [N18000244]                                                     | 2/2017           | 235.53 -                           | 235.53                       | 42.49                                   | 06/2019<br>06/2019    | 06/2019     |
| 204                             | PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]  | 3/2017           | 162.31 -                           | 162.31                       | 86.70                                   | 03/2019<br>03/2019    | 03/2019     |
| 205                             | ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]  | 2/2017           | 322.30 -                           | 322.30                       | 119.48                                  | 02/2019<br>02/2019    | 02/2019     |
| 206                             | WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]                                                             | 2/2017           | 195.05 -                           | 195.05                       | 92.00                                   | 02/2020<br>02/2020    | 02/2020     |
| 207                             | SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]                 | 10/2016          | 608.24 -                           | 608.24                       | 376.20                                  | 04/2019<br>04/2019    | 04/2019     |
| 208                             | EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]                                                             | 3/2017           | 3,500.00<br>3,500.00               | 3,500.00                     | 690.00                                  | 07/2020<br>-          | 07/2020     |
| 209                             | STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]                                                  | 12/2015          | 3,654.00 -                         | 3,654.00                     | 2,873.42                                | 04/2019<br>-          | 04/2019     |
| 210                             | EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]                                                               | 5/2014           | 522.29 -                           | 550.18                       | 445.93                                  | 11/2016<br>06/2019    | 06/2019     |
| 211                             | SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]                                                       | 1/2015           | 203.28 -                           | 260.03                       | 187.06                                  | 07/2017<br>06/2019    | 06/2019     |
| 212                             | CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]                   | 3/2015           | 1,394.52 -                         | 1,394.52                     | 260.99                                  | 05/2017<br>06/2019    | 06/2019     |
| 213                             | EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]                                                                | 4/2016           | 454.11 -                           | 454.11                       | 249.92                                  | 04/2018<br>01/2020    | 01/2020     |
| 214                             | TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]                                    | 1/2015           | 871.62 -                           | 871.62                       | 432.72                                  | 10/2017<br>09/2019    | 09/2019     |
|                                 | <u>Satluj Jal Vidyut Nigam Limited</u>                                                                              |                  |                                    |                              |                                         |                       |             |
| 215                             | NAITWAR MORI HEP - [N18000265]                                                                                      | 10/2017          | 648.33 -                           | 648.33                       | 148.40                                  | 12/2021<br>-          | 12/2021     |
|                                 | <u>Thdc India Limited</u>                                                                                           |                  |                                    |                              |                                         |                       |             |
| 216                             | AMELIA COAL MINE - [N18000252]                                                                                      | 1/2017           | 2,104.21 -                         | 2,104.21                     | 66.05                                   | 09/2020<br>-          | 09/2020     |
|                                 | <b>Total</b>                                                                                                        |                  | 1,64,403.60 -                      | 1,83,479.70                  | 1,18,949.82                             |                       |             |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                                                       |                  |                                    |                              |                                         | (December 2018)       |             |
|---------------------------------|---------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                                                       |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                                               | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                                                     | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
|                                 | <u>RAILWAYS</u>                                                                       |                  |                                    |                              |                                         |                       |             |
|                                 | <u>Central Railways</u>                                                               |                  |                                    |                              |                                         |                       |             |
| 217                             | WARDHA-NANDED MAHARASHTRA<br>- [N22000231]                                            | 4/2008           | 3,168.29<br>-                      | 3,168.29                     | 992.77                                  | 03/2023<br>-          | 03/2023     |
| 218                             | KALYAN-KASARA 3RD LINE<br>- [N22000233]                                               | 4/2011           | 792.89<br>-                        | 792.89                       | 275.17                                  | 03/2021<br>-          | 03/2021     |
| 219                             | WARDHA-SEWAGRAM NGP 3RD LINE<br>- [N22000250]                                         | 4/2012           | 540.02<br>-                        | 540.02                       | 168.97                                  | 03/2022<br>-          | 03/2022     |
| 220                             | WARDHA - NAGPUR - 4TH LINE (76 KM)<br>- [N22000362]                                   | 2/2016           | 637.95<br>-                        | 637.95                       | 28.96                                   | 03/2023<br>-          | 03/2023     |
| 221                             | DAUND - MANMAD (236 KM)<br>- [N22000360]                                              | 2/2016           | 1,876.00<br>-                      | 2,081.27                     | 1.27                                    | 03/2023<br>-          | 03/2023     |
| 222                             | PUNE-MIRAJ-LONDA (467 KM)<br>- [N22000359]                                            | 2/2015           | 3,627.47<br>3,627.00               | 3,627.47                     | 332.55                                  | 03/2024<br>-          | 03/2024     |
| 223                             | ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)<br>- [N22000358]                             | 2/2015           | 2,449.91<br>-                      | 2,449.91                     | 89.27                                   | 03/2023<br>-          | 03/2023     |
| 224                             | WARDHA-BALHARSHAH - 3RD LINE (132 KM)<br>- [N22000356]                                | 2/2015           | 1,272.19<br>-                      | 1,272.19                     | 162.38                                  | 03/2022<br>-          | 03/2022     |
| 225                             | VAIBHAVWADI -KOLHAPUR (107 KM)<br>- [N22000355]                                       | 2/2016           | 2,750.00<br>-                      | 3,438.51                     | -                                       | 03/2024<br>-          | 03/2024     |
| 226                             | PUNE-NASIK (265 KM)<br>- [N22000354]                                                  | 2/2016           | 2,425.00<br>-                      | 5,341.68                     | -                                       | 03/2024<br>-          | 03/2024     |
| 227                             | INDORE - MANMAD VIA MALEGAON (368 KM)<br>- [N22000353]                                | 2/2016           | 9,968.00<br>-                      | 8,857.98                     | -                                       | 03/2024<br>-          | 03/2024     |
| 228                             | AHMEDNAGAR-PARLI VAIJNATH(NL) CR<br>- [220100181]                                     | 2/1997           | 2,271.50<br>-                      | 3,712.50                     | 1,909.57                                | 03/2021<br>-          | 03/2021     |
| 229                             | 3RD LINE BETWEEN BHUSAWAL-JALGAON<br>- [N22000247]                                    | 4/2011           | 184.06<br>-                        | 298.70                       | 240.89                                  | 03/2019<br>-          | 03/2019     |
|                                 | <u>Container Corporation Of India</u>                                                 |                  |                                    |                              |                                         |                       |             |
| 230                             | MULTI MODAL LOGISTICS TRANSPORT AT MIHAN<br>- [N22000422]                             | 10/2013          | 305.00<br>-                        | 305.00                       | 253.22                                  | 03/2019<br>-          | 03/2019     |
| 231                             | MULTI MODAL LOGISTICS PARK AT BARHI<br>- [N22000426]                                  | 12/2015          | 346.32<br>-                        | 300.00                       | 272.72                                  | 03/2019<br>-          | 03/2019     |
|                                 | <u>Dedicated Freight Corridor Corporation Of India Ltd</u>                            |                  |                                    |                              |                                         |                       |             |
| 232                             | WESTERN DEDICATED FREIGHT CORRIDOR<br>- [N22000464]                                   | 11/2007          | 16,592.00<br>51,101.00             | 51,101.00                    | 22,485.00                               | 03/2020<br>-          | 03/2020     |
|                                 | <u>East Central Railways</u>                                                          |                  |                                    |                              |                                         |                       |             |
| 233                             | KOSI BRIDGE (NL), ECR<br>- [220100304]                                                | 4/2002           | 499.41<br>-                        | 516.02                       | 640.78                                  | 03/2020<br>-          | 03/2020     |
| 234                             | JAYNAGAR-BIJALPURA INCLUDING EXTENSION<br>BIJALPURA-BARDIBAS(NEPAL) GC<br>[N22000181] | 4/2009           | 548.00<br>-                        | 785.87                       | 40.00                                   | 03/2020<br>-          | 03/2020     |
|                                 | <u>East Coast Railway</u>                                                             |                  |                                    |                              |                                         |                       |             |
| 235                             | KIRANDUL - JAGDALPUR DOUBLING<br>- [N22000318]                                        | 12/2012          | 1,160.00<br>-                      | 1,160.83                     | 571.51                                  | 03/2020<br>-          | 03/2020     |



## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                                                                    |                  |                                    |                              |                                         | (December 2018)       |             |
|---------------------------------|----------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                                                                    |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                                                            | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                                                                  | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 236                             | KOTTAVALSA - KORAPUT DOUBLING<br>- [N22000377]                                                     | 4/2015           | 2,499.71<br>-                      | 2,499.71                     | 183.68                                  | 03/2022<br>-          | 03/2022     |
| 237                             | EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL<br>- [N22000418] | 4/2016           | 5,200.00<br>-                      | 5,200.00                     | -                                       | 03/2020<br>-          | 03/2020     |
| 238                             | KORAPUT - SINGAPUR ROAD DOUBLING<br>- [N22000379]                                                  | 4/2015           | 2,361.74<br>-                      | 2,361.74                     | 81.06                                   | 03/2022<br>-          | 03/2022     |
| 239                             | JAGADALPUR-KORAPUT DOUBLING<br>- [N22000376]                                                       | 4/2015           | 1,547.38<br>-                      | 1,547.38                     | 189.40                                  | 03/2022<br>-          | 03/2022     |
| 240                             | SAMBALPUR - ANGUL RLY. ELECTRIFICATION<br>- [N22000319]                                            | 3/2012           | 155.81<br>-                        | 238.03                       | 180.78                                  | 03/2020<br>-          | 03/2020     |
|                                 | <u>Eastern Railways</u>                                                                            |                  |                                    |                              |                                         |                       |             |
| 241                             | HANSDIHA-GODDA NL<br>- [N22000236]                                                                 | 4/2011           | 542.18<br>-                        | 542.18                       | 311.90                                  | 03/2020<br>-          | 03/2020     |
| 242                             | PIRPAINTI-JASIDIH<br>- [N22000219]                                                                 | 4/2013           | 915.98<br>-                        | 915.96                       | 319.53                                  | 03/2022<br>-          | 03/2022     |
|                                 | <u>Metropolitan Rapid Transport Projects</u>                                                       |                  |                                    |                              |                                         |                       |             |
| 243                             | EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP<br>- [N22000028]                              | 4/2006           | 495.74<br>-                        | 734.01                       | 445.91                                  | 06/2013<br>03/2019    | 03/2019     |
|                                 | <u>North Central Railway</u>                                                                       |                  |                                    |                              |                                         |                       |             |
| 244                             | GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)<br>- [N22000148]                                    | 4/2011           | 2,912.96<br>-                      | 3,845.60                     | 1.92                                    | 03/2022<br>-          | 03/2022     |
| 245                             | MATHURA-PLWAL 4TH LINE (80KM)<br>- [N22000372]                                                     | 4/2015           | 668.70<br>668.00                   | 668.00                       | -                                       | 03/2020<br>-          | 03/2020     |
| 246                             | JHANSI BINA DOUBLING<br>- [N22000496]                                                              | 9/2016           | 2,001.00<br>-                      | 2,001.00                     | -                                       | 03/2021<br>-          | 03/2021     |
| 247                             | JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING<br>- [N22000495]                                      | 3/2018           | 4,329.53<br>-                      | 4,329.53                     | -                                       | 03/2023<br>-          | 03/2023     |
|                                 | <u>North East Frontier Railway</u>                                                                 |                  |                                    |                              |                                         |                       |             |
| 248                             | BHAIRABI SAIRONG, NL, NEFR<br>- [N22000100]                                                        | 4/2008           | 2,393.47<br>-                      | 4,968.00                     | 2,516.15                                | 03/2014<br>12/2020    | 12/2020     |
| 249                             | NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING<br>- [N22000183]                                          | 4/2013           | 1,798.00<br>-                      | 1,798.00                     | -                                       | 03/2019<br>-          | 03/2019     |
| 250                             | NEW BG LINE FROM BYRNIHAT TO SHILLONG<br>- [N22000205]                                             | 4/2010           | 906.46<br>-                        | 6,000.00                     | 259.95                                  | 03/2021<br>-          | 03/2021     |
| 251                             | MURKONGSELEK-PASIGHAT NL<br>- [N22000208]                                                          | 4/2011           | 414.84<br>-                        | 661.00                       | 121.37                                  | 03/2020<br>-          | 03/2020     |
| 252                             | DIGARU-HOJAI (102 KM)<br>- [N22000389]                                                             | 4/2015           | 870.96<br>-                        | 821.00                       | 214.95                                  | 03/2021<br>-          | 03/2021     |
| 253                             | LUMDING-HOJAI PATCH DOUBLING PROJECT<br>- [N22000211]                                              | 4/2012           | 246.07<br>-                        | 398.93                       | 328.77                                  | 03/2019<br>-          | 03/2019     |
| 254                             | AMBARI FALAKATA TO NEW MAYNAGURI<br>- [N22000210]                                                  | 4/2011           | 314.00<br>-                        | 551.00                       | 602.54                                  | 03/2019<br>-          | 03/2019     |
| 255                             | NEW BG LINE FROM BALURGHAT TO HILLY NFR<br>- [N22000206]                                           | 4/2010           | 242.22<br>-                        | 471.00                       | 64.68                                   | 03/2020<br>-          | 03/2020     |
| 256                             | DIMAPUR-TIZIT NL<br>- [N22000196]                                                                  | 4/2013           | 4,274.00<br>-                      | 4,274.00                     | -                                       | 03/2020<br>-          | 03/2020     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                                                        |                  |                                    |                              |                                         | (December 2018)       |             |
|---------------------------------|----------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                                                        |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                                                | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                                                      | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 257                             | NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]           | 4/2006           | 2,326.52 -                         | 3,000.00                     | 677.37                                  | 03/2015<br>10/2021    | 10/2021     |
|                                 | <u>North Eastern Railway</u>                                                           |                  |                                    |                              |                                         |                       |             |
| 258                             | CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]                           | 3/2007           | 243.78 -                           | 895.00                       | 99.33                                   | 12/2021 -             | 12/2021     |
| 259                             | AUNRIHAR - JAUNPUR PATCH DOUBLING - [N22000469]                                        | 4/2016           | 600.00 -                           | 366.71                       | .46                                     | 01/2022 -             | 01/2022     |
| 260                             | BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]        | 4/2016           | 1,900.00 -                         | 1,277.06                     | -                                       | 01/2022 -             | 01/2022     |
|                                 | <u>North Western Railway</u>                                                           |                  |                                    |                              |                                         |                       |             |
| 261                             | JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]        | 4/2008           | 653.19 -                           | 1,116.00                     | 820.02                                  | 03/2014<br>03/2019    | 03/2019     |
| 262                             | JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]                         | 8/2018           | 808.85 -                           | 808.85                       | -                                       | 08/2022 -             | 08/2022     |
| 263                             | AJMER-BANGURGRAM - [N22000155]                                                         | 4/2011           | 213.39 -                           | 244.02                       | 217.81                                  | 11/2019 -             | 11/2019     |
| 264                             | PHULERA - DIGANA DOUBLING - [N22000326]                                                | 5/2015           | 600.00 -                           | 685.99                       | 3.52                                    | 03/2020 -             | 03/2020     |
| 265                             | DAUSA-GANGAPUR CITY(NL),NWR - [220100184]                                              | 2/1997           | 410.08 -                           | 795.01                       | 458.50                                  | 02/2019 -             | 02/2019     |
|                                 | <u>Northern Railway</u>                                                                |                  |                                    |                              |                                         |                       |             |
| 266                             | CHANDIGARH-BADDI - [N22000467]                                                         | 4/2007           | 328.14 -                           | 1,540.00                     | 229.95                                  | 03/2023 -             | 03/2023     |
|                                 | <u>National High Speed Rail Corporation Limited</u>                                    |                  |                                    |                              |                                         |                       |             |
| 267                             | MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]                                 | 12/2015          | 1,08,000.00 -                      | 1,08,000.00                  | 1,057.80                                | 12/2023<br>12/2023    | 12/2023     |
|                                 | <u>Rail India Technical And Economic Service</u>                                       |                  |                                    |                              |                                         |                       |             |
| 268                             | DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394] | 3/2015           | 636.38 -                           | 636.38                       | 169.16                                  | 03/2021 -             | 03/2021     |
|                                 | <u>Rail Vikas Nigam Ltd.</u>                                                           |                  |                                    |                              |                                         |                       |             |
| 269                             | BHANUPALI-BILASPUR BERI NL - [N22000273]                                               | 4/2008           | 2,966.99 -                         | 7,000.00                     | 221.19                                  | 12/2026 -             | 12/2026     |
| 270                             | HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]                                        | 4/2010           | 2,127.00 -                         | 2,127.00                     | 1,042.32                                | 03/2023 -             | 03/2023     |
| 271                             | AHMEDABAD-BOTAD (GC) - [N22000140]                                                     | 4/2012           | 975.62 -                           | 975.62                       | 518.92                                  | 12/2021 -             | 12/2021     |
| 272                             | PALANPUR-SAMAKHAYALI (DL) - [N22000144]                                                | 4/2013           | 1,548.66 -                         | 1,548.66                     | 777.72                                  | 12/2021 -             | 12/2021     |
| 273                             | VIJAYAWADA-GUDUR - [N22000369]                                                         | 4/2015           | 3,246.26 -                         | 3,548.67                     | 132.79                                  | 12/2023 -             | 12/2023     |
| 274                             | BINA - KOTA DOUBLING WITH RE - [N22000414]                                             | 4/2011           | 1,485.85 -                         | 1,485.85                     | 1,038.90                                | 12/2020 -             | 12/2020     |
| 275                             | RAIPUR - TITLAGARH - DOUBLING - [N22000411]                                            | 3/2007           | 1,402.02 -                         | 758.09                       | 1,001.84                                | 03/2020 -             | 03/2020     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                                                                                    |                  |                                    |                              |                                         | (December 2018)       |             |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                                                                                    |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                                                                            | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                                                                                  | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 276                             | SAMBALPUR - TITLAGARH - DOUBLING<br>- [N22000410]                                                                  | 3/2006           | 948.04<br>-                        | 970.00                       | 910.62                                  | 03/2020<br>-          | 03/2020     |
| 277                             | VIZIANAGARAM -SAMABALPUR 3RD LINE<br>- [N22000409]                                                                 | 1/1991           | 2,335.67<br>-                      | 2,335.67                     | 316.27                                  | 12/2024<br>-          | 12/2024     |
| 278                             | DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)<br>- [N22000407]               | 3/2009           | 713.48<br>-                        | 1,750.00                     | 1,618.00                                | 03/2020<br>-          | 03/2020     |
| 279                             | SECUNDERABAD-MAHABUBNAGAR DOUBLING<br>- [N22000403]                                                                | 4/2015           | 773.94<br>-                        | 773.94                       | 412.07                                  | 12/2024<br>-          | 12/2024     |
| 280                             | DHASA-JETALSAR (GC)<br>- [N22000141]                                                                               | 4/2012           | 644.38<br>-                        | 644.38                       | 127.98                                  | 03/2021<br>-          | 03/2021     |
|                                 | <u>South Central Railway</u>                                                                                       |                  |                                    |                              |                                         |                       |             |
| 281                             | BHADRACHALAM ROAD-SATTUPALLI<br>- [N22000287]                                                                      | 4/2010           | 704.31<br>-                        | 704.31                       | 119.69                                  | 03/2020<br>-          | 03/2020     |
| 282                             | MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432] | 4/2017           | 119.73<br>185.00                   | 184.97                       | -                                       | 03/2022<br>-          | 03/2022     |
| 283                             | KAZIPET-BALHRSHA<br>- [N22000367]                                                                                  | 4/2015           | 2,063.03<br>-                      | 2,063.03                     | 368.22                                  | 03/2021<br>-          | 03/2021     |
|                                 | <u>South East Central Railway</u>                                                                                  |                  |                                    |                              |                                         |                       |             |
| 284                             | GONDIA-JABALPUR(GC),(SECR)<br>- [220100186]                                                                        | 2/1997           | 511.86<br>-                        | 1,756.00                     | 967.96                                  | 04/2020<br>-          | 04/2020     |
| 285                             | GEVRA ROAD PENDRA ROAD<br>- [N22000488]                                                                            | 2/2014           | 2,288.00<br>-                      | 4,919.00                     | 67.00                                   | 03/2022<br>-          | 03/2022     |
| 286                             | ANUPPUR-KATNI<br>- [N22000485]                                                                                     | 4/2015           | 1,370.00<br>-                      | 1,370.00                     | 101.00                                  | 12/2021<br>-          | 12/2021     |
| 287                             | JHARSUGUDA-BILASPUR 4TH LINE<br>- [N22000484]                                                                      | 4/2015           | 1,973.00<br>-                      | 1,973.00                     | 78.00                                   | 03/2021<br>-          | 03/2021     |
| 288                             | CHAMPA-JHARSUGUDA 3RD LINE<br>- [N22000483]                                                                        | 4/2008           | 872.00<br>-                        | 1,279.00                     | -                                       | 12/2019<br>-          | 12/2019     |
| 289                             | KENDRI-DHARTARI INCLUDING ABHANPUR-RAJIM<br>- [N22000482]                                                          | 4/2011           | 1,471.93<br>-                      | 543.00                       | -                                       | 03/2022<br>-          | 03/2022     |
| 290                             | WADSA-GADHCHIROLI NEW LINE (52.36 KM)<br>- [N22000480]                                                             | 6/2018           | 229.00<br>-                        | 403.00                       | 36.28                                   | 12/2021<br>-          | 12/2021     |
| 291                             | CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT<br>- [N22000438]                                           | 4/2010           | 585.93<br>-                        | 1,420.39                     | 104.10                                  | 02/2019<br>-          | 02/2019     |
| 292                             | RAJNANDGAON - NAGPUR - 3RD LINE (SECR)<br>- [N22000420]                                                            | 9/2016           | 1,908.51<br>-                      | 2,686.63                     | -                                       | 03/2023<br>-          | 03/2023     |
|                                 | <u>South Eastern Railway</u>                                                                                       |                  |                                    |                              |                                         |                       |             |
| 293                             | MM FROM BURAMARA-CHAKULIA<br>- [N22000305]                                                                         | 4/2008           | 466.48<br>-                        | 1,000.00                     | .83                                     | -<br>12/2024          | 12/2024     |
| 294                             | BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL<br>- [N22000402]                                         | 4/1998           | 1,027.40<br>-                      | 2,373.00                     | 484.85                                  | 03/2003<br>03/2030    | 03/2030     |
| 295                             | RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADEATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]        | 4/1995           | 524.43<br>-                        | 939.00                       | 184.10                                  | 12/2021<br>12/2024    | 12/2024     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                                                                             |                  |                                    |                              |                                         | (December 2018)       |             |
|---------------------------------|-------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                                                                             |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                                                                     | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                                                                           | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 296                             | DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160                                                     | 4/2010           | 651.00 -                           | 1,009.00                     | 7.96                                    | 03/2015<br>03/2024    | 03/2024     |
| 297                             | MM FROM PANSKURA-GHATAL NL - [N22000309                                                                     | 4/2011           | 276.69 -                           | 426.00                       | -                                       | -<br>03/2030          | 03/2030     |
| 298                             | TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397 | 1/1991           | 1,013.45 -                         | 1,428.00                     | 484.49                                  | 12/2021<br>12/2021    | 12/2021     |
| 299                             | BOWAICHANDI-ARAMBAGH - [N22000159                                                                           | 4/2010           | 267.37 -                           | 620.00                       | 40.77                                   | -<br>03/2025          | 03/2025     |
|                                 | <u>South Western Railway</u>                                                                                |                  |                                    |                              |                                         |                       |             |
| 300                             | TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256                                                                | 4/2011           | 1,801.01 -                         | 1,801.01                     | 13.67                                   | -<br>12/2023          | 12/2023     |
| 301                             | HOTGI-KUDGI-GADAG - [N22000333                                                                              | 3/2015           | 1,614.59 -                         | 1,870.41                     | 732.88                                  | 03/2019<br>03/2021    | 03/2021     |
| 302                             | ARSIKERE-TUMKUR - [N22000332                                                                                | 3/2015           | 578.00 -                           | 578.00                       | 458.72                                  | 03/2020<br>03/2020    | 03/2020     |
| 303                             | YELAHANKA-PENUKONDA - [N22000328                                                                            | 5/2015           | 860.43 -                           | 860.43                       | 503.45                                  | 03/2020<br>03/2020    | 03/2020     |
| 304                             | MIRAJ-LONDA - [N22000327                                                                                    | 3/2015           | 1,830.00 -                         | 1,190.92                     | 207.68                                  | -<br>03/2021          | 03/2021     |
| 305                             | BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274                                                             | 4/1996           | 1,382.78 -                         | 1,382.78                     | 7.35                                    | 03/2002<br>03/2024    | 03/2024     |
| 306                             | HUBLI-ANKOLA(NL),SWR - [220100193                                                                           | 4/1997           | 2,315.00 -                         | 2,135.00                     | 144.75                                  | -<br>12/2024          | 12/2024     |
| 307                             | MARIKUPPAM - KUPPAM - [N22000308                                                                            | 4/2012           | 279.54 -                           | 279.54                       | 8.80                                    | 03/2016<br>12/2023    | 12/2023     |
| 308                             | CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300                                                                  | 4/2013           | 327.25 -                           | 367.77                       | .31                                     | -<br>12/2023          | 12/2023     |
| 309                             | GADAG-WADI NL - [N22000299                                                                                  | 4/2013           | 2,841.84 -                         | 2,841.84                     | 39.98                                   | 12/2018<br>12/2024    | 12/2024     |
| 310                             | TORANAGALLU-RANJITPURA DL - [N22000298                                                                      | 4/2011           | 146.75 -                           | 167.50                       | .34                                     | -<br>12/2023          | 12/2023     |
| 311                             | WHITE FIELD-KOLAR NL - [N22000280                                                                           | 4/2011           | 348.85 -                           | 348.85                       | .36                                     | -<br>12/2023          | 12/2023     |
| 312                             | SHIMOGA-HARIHAR NL - [N22000278                                                                             | 4/2011           | 832.47 -                           | 832.47                       | .94                                     | 03/2016<br>03/2024    | 03/2024     |
| 313                             | BAGALKOT-KUDACHI NL - [N22000258                                                                            | 4/2010           | 986.30 -                           | 986.30                       | 287.03                                  | 03/2016<br>12/2023    | 12/2023     |
| 314                             | CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276                                             | 4/2013           | 558.00 -                           | 692.43                       | -                                       | -<br>12/2023          | 12/2023     |
| 315                             | SRINIVASA-PURA-MADANAPALLI NL - [N22000277                                                                  | 4/2013           | 296.00 -                           | 466.65                       | -                                       | -<br>12/2023          | 12/2023     |
|                                 | <u>Southern Railway</u>                                                                                     |                  |                                    |                              |                                         |                       |             |
| 316                             | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079                               | 9/2007           | 724.69 -                           | 2,072.50                     | 1,169.07                                | 02/2019<br>-          | 02/2019     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                                                                                          |                  |                                    |                              |                                         | (December 2018)       |             |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                                                                                          |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                                                                                  | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                                                                                        | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 317                             | MADURAI-TUTICORIN VIA ARUPPUKOTTAI<br>- [N22000215]                                                                      | 4/2011           | 120.70<br>-                        | 1,800.00                     | 112.10                                  | 03/2019<br>-          | 03/2019     |
| 318                             | ATTIPPATTU PUTTUR<br>- [N22000184]                                                                                       | 4/2008           | 151.84<br>-                        | 1,105.00                     | 3.34                                    | 02/2019<br>-          | 02/2019     |
| 319                             | MADURAI - MANIYACHI - TUTICORIN (160 KM)<br>DOUBLING - [N22000451]                                                       | 2/2015           | 760.00<br>-                        | 1,182.31                     | -                                       | 03/2020<br>-          | 03/2020     |
| 320                             | MANIYACHI - NAGERCOIL (102 KM) DOUBLING<br>- [N22000449]                                                                 | 2/2015           | 1,700.00<br>-                      | 1,700.00                     | -                                       | 03/2022<br>-          | 03/2022     |
|                                 | <u>West Central Railway</u>                                                                                              |                  |                                    |                              |                                         |                       |             |
| 321                             | RAMGANJMUNDI-BHOPAL (NL),WCR<br>- [220100314]                                                                            | 4/2001           | 424.60<br>-                        | 2,713.09                     | 898.83                                  | 03/2021<br>-          | 03/2021     |
| 322                             | KATNI-BINA 3RD LINE (263 KM)<br>- [N22000415]                                                                            | 6/2016           | 2,478.23<br>-                      | 2,478.23                     | 112.07                                  | 03/2022<br>-          | 03/2022     |
| 323                             | KATNI GRADE SEPARATOR/BYE PASS<br>- [N22000416]                                                                          | 8/2016           | 582.13<br>-                        | 1,260.61                     | -                                       | 03/2022<br>-          | 03/2022     |
|                                 | <u>Western Railway</u>                                                                                                   |                  |                                    |                              |                                         |                       |             |
| 324                             | AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)<br>- [N22000121]                                                                      | 4/2008           | 829.74<br>-                        | 385.60                       | 500.42                                  | 03/2020<br>03/2020    | 03/2020     |
| 325                             | INDORE-DEWAS-UJJAIN (80 KMS)<br>- [N22000493]                                                                            | 4/2016           | 700.00<br>-                        | 700.00                       | 11.19                                   | 06/2020<br>-          | 06/2020     |
| 326                             | DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION<br>UPTO KEVADIYA(32.68KM) =49.75KM<br>[N22000494]                            | 4/2017           | 691.84<br>-                        | 691.84                       | 15.31                                   | 03/2020<br>-          | 03/2020     |
| 327                             | BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING<br>GC OF MAHESANA-TARANGA HILL AS MATERIAL<br>MODIFICATION - [N22000487]      | 2/1991           | 551.51<br>-                        | 551.51                       | 257.05                                  | 03/2019<br>-          | 03/2019     |
|                                 | Total                                                                                                                    |                  | 2,67,431.21<br>-                   | 3,39,036.97                  | 54,671.05                               |                       |             |
|                                 |                                                                                                                          |                  |                                    |                              |                                         |                       |             |
|                                 | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                       |                  |                                    |                              |                                         |                       |             |
|                                 | <u>Ministry Of Road Transport And Highways</u>                                                                           |                  |                                    |                              |                                         |                       |             |
| 328                             | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT<br>OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE<br>WITH PAVED S - [N24000772] | 12/2017          | 257.34<br>-                        | 257.34                       | -                                       | 12/2019<br>-          | 12/2019     |
| 329                             | RECONSTRUCTION WITH GEOMETIC IMPROVEMENT<br>OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER<br>CONFIGURATION - [N24000777] | 11/2017          | 283.51<br>-                        | 284.00                       | 94.50                                   | 11/2019<br>-          | 11/2019     |
| 330                             | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT<br>OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE<br>WITH EAR - [N24000779]    | 2/2018           | 418.88<br>-                        | 418.88                       | 92.42                                   | 02/2020<br>-          | 02/2020     |
| 331                             | Rehabilitation and up gradation to 2 lane with paved<br>shoulder configuration from existing km. 122.00 -<br>[N24000820] | 11/2017          | 237.80<br>-                        | 238.00                       | 29.43                                   | 11/2019<br>-          | 11/2019     |
| 332                             | CONSTRUCTION OF KUND BYPASS FROM EXISTING<br>KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130<br>KM); DESIGN - [N24000781] | 5/2018           | 248.00<br>-                        | 248.00                       | -                                       | 05/2020<br>-          | 05/2020     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                                                                                    |                  |                                    |                              |                                         | (December 2018)       |             |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                                                                                    |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                                                                            | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                                                                                  | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 333                             | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778  | 11/2017          | 266.52 -                           | 266.52                       | 95.30                                   | 11/2019 -             | 11/2019     |
| 334                             | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776 | 11/2017          | 232.81 -                           | 232.81                       | 48.23                                   | 11/2019 -             | 11/2019     |
| 335                             | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773  | 12/2017          | 200.34 -                           | 200.34                       | 43.14                                   | 12/2019 -             | 12/2019     |
| 336                             | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775  | 6/2017           | 282.08 -                           | 282.08                       | 66.19                                   | 06/2019 -             | 06/2019     |
| 337                             | WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774  | 12/2017          | 248.22 -                           | 248.22                       | 57.01                                   | 12/2019 -             | 12/2019     |
|                                 | <u>National Highways And Infrastructure Development Corporation Ltd.</u>                                           |                  |                                    |                              |                                         |                       |             |
| 338                             | FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321                       | 6/2016           | 829.00 -                           | 829.00                       | 59.85                                   | 01/2019 -             | 01/2019     |
| 339                             | 4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438       | 12/2015          | 289.99 -                           | 289.99                       | -                                       | 12/2018 -             | 12/2018     |
| 340                             | 4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429       | 12/2015          | 225.02 -                           | 159.20                       | -                                       | 12/2018 -             | 12/2018     |
| 341                             | 2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325                              | 10/2015          | 179.82 -                           | 179.82                       | 8.99                                    | 01/2019 -             | 01/2019     |
|                                 | <u>National Highways Authority Of India</u>                                                                        |                  |                                    |                              |                                         |                       |             |
| 342                             | 4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425                                                                | 7/2015           | 2,288.18 -                         | 2,288.18                     | -                                       | 05/2019 -             | 05/2019     |
| 343                             | 4 LANING OF FAGNE - MAH-GUJ BORDER ( PKG-3) - [N24000439                                                           | 7/2015           | 1,885.74 -                         | 1,885.74                     | 1,622.44                                | 05/2019 -             | 05/2019     |
| 344                             | CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442  | 12/2015          | 649.50 -                           | 649.50                       | 86.54                                   | 03/2019 -             | 03/2019     |
| 345                             | 8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449                                                                  | 7/2015           | 2,128.72 -                         | 2,128.72                     | 1,042.73                                | 04/2019 -             | 04/2019     |
| 346                             | FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480                                                           | 12/2015          | 1,041.10 -                         | 1,041.10                     | 175.85                                  | 04/2019 -             | 04/2019     |
| 347                             | CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650  | 1/2017           | 244.90 -                           | 244.90                       | 82.41                                   | 05/2019 -             | 05/2019     |
| 348                             | CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625  | 9/2016           | 1,004.67 -                         | 1,004.67                     | -                                       | 05/2019 -             | 05/2019     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                                                                                   |                  |                                    |                              |                                         | (December 2018)       |             |
|---------------------------------|-------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                                                                                   |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                                                                           | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                                                                                 | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 349                             | TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622 | 9/2016           | 950.69<br>-                        | 950.69                       | 499.54                                  | 08/2019<br>-          | 08/2019     |
| 350                             | DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619 | 9/2016           | 2,510.04<br>-                      | 2,510.04                     | -                                       | 08/2019<br>-          | 08/2019     |
| 351                             | HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603                                                                   | 8/2016           | 1,167.42<br>-                      | 1,167.42                     | 192.72                                  | 03/2019<br>-          | 03/2019     |
| 352                             | BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605                                  | 8/2016           | 227.49<br>-                        | 227.49                       | 15.03                                   | 01/2019<br>-          | 01/2019     |
| 353                             | FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602                             | 8/2016           | 1,664.20<br>-                      | 1,664.20                     | 313.63                                  | 04/2020<br>-          | 04/2020     |
| 354                             | 4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600   | 8/2016           | 1,388.34<br>-                      | 1,388.34                     | 595.70                                  | 09/2019<br>-          | 09/2019     |
| 355                             | NAGPUR RING ROAD PACKAGE-1 - [N24000558                                                                           | 3/2016           | 546.00<br>-                        | 546.00                       | 460.55                                  | 07/2019<br>-          | 07/2019     |
| 356                             | 4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692                                                      | 6/2017           | 2,485.93<br>-                      | 2,485.93                     | -                                       | 06/2020<br>-          | 06/2020     |
| 357                             | 6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672 | 3/2017           | 2,064.99<br>-                      | 2,447.00                     | 1,002.09                                | 03/2020<br>-          | 03/2020     |
| 358                             | REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671  | 3/2017           | 1,288.07<br>-                      | 1,420.00                     | -                                       | 03/2020<br>-          | 03/2020     |
| 359                             | REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667                      | 3/2017           | 648.32<br>-                        | 503.10                       | 15.10                                   | 03/2020<br>-          | 03/2020     |
| 360                             | CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666 | 3/2017           | 235.48<br>-                        | 227.77                       | -                                       | 03/2020<br>-          | 03/2020     |
| 361                             | TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665  | 3/2017           | 672.89<br>-                        | 736.01                       | -                                       | 03/2020<br>-          | 03/2020     |
| 362                             | 4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656                                             | 3/2017           | 744.64<br>-                        | 982.00                       | -                                       | 03/2020<br>-          | 03/2020     |
| 363                             | CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655 | 3/2017           | 247.02<br>-                        | 157.49                       | -                                       | 03/2020<br>-          | 03/2020     |
| 364                             | FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652 | 3/2017           | 848.45<br>-                        | 848.45                       | 5.00                                    | 03/2020<br>-          | 03/2020     |
| 365                             | FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807  | 3/2018           | 1,532.62<br>-                      | 1,532.62                     | -                                       | 03/2021<br>-          | 03/2021     |
| 366                             | FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556 | 3/2016           | 899.00<br>-                        | 899.00                       | 351.90                                  | 04/2019<br>-          | 04/2019     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                                                                                    |                  |                                    |                              |                                         | (December 2018)       |             |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                                                                                    |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                                                                            | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                                                                                  | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 367                             | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]              | 3/2016           | 1,587.49 -                         | 1,587.49                     | 164.42                                  | 04/2019 -             | 04/2019     |
| 368                             | 4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]                                                 | 2/2016           | 997.15 -                           | 997.15                       | 352.03                                  | 03/2019 -             | 03/2019     |
| 369                             | 2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]                                | 2/2016           | 273.20 -                           | 273.20                       | 48.69                                   | 02/2019 -             | 02/2019     |
| 370                             | ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]                                      | 3/2016           | 676.73 -                           | 676.73                       | 409.11                                  | 04/2019 -             | 04/2019     |
| 371                             | DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]                                | 1/2016           | 1,081.57 -                         | 1,081.57                     | 795.28                                  | 06/2019 -             | 06/2019     |
| 372                             | DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]                                                       | 1/2016           | 701.12 -                           | 701.12                       | 842.34                                  | 05/2019 -             | 05/2019     |
| 373                             | FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505] | 6/2015           | 1,583.79 -                         | 1,583.79                     | 1,439.18                                | 01/2019 -             | 01/2019     |
| 374                             | NAGPUR RING ROAD PACKAGE-2 - [N24000560]                                                                           | 3/2016           | 591.66 -                           | 591.66                       | 608.89                                  | 07/2019 -             | 07/2019     |
| 375                             | 6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]                                                                     | 7/2015           | 1,657.20 -                         | 1,657.20                     | 1,945.00                                | 01/2019 -             | 01/2019     |
|                                 | Total                                                                                                              |                  | 42,713.64 -                        | 43,220.47                    | 13,661.23                               |                       |             |
|                                 |                                                                                                                    |                  |                                    |                              |                                         |                       |             |
|                                 | <u>SHIPPING AND PORTS</u>                                                                                          |                  |                                    |                              |                                         |                       |             |
|                                 | <u>Inland Waterways Authority Of India</u>                                                                         |                  |                                    |                              |                                         |                       |             |
| 376                             | JAL MARG VIKAS PROJECT - [N25000072]                                                                               | 1/2018           | 4,200.00 -                         | 4,200.00                     | -                                       | 03/2023 -             | 03/2023     |
|                                 | <u>Kamarajar Port Limited</u>                                                                                      |                  |                                    |                              |                                         |                       |             |
| 377                             | CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]                                                  | 3/2016           | 600.00 258.00                      | 257.90                       | 1.45                                    | 12/2017 05/2020       | 05/2020     |
|                                 | Total                                                                                                              |                  | 4,800.00 -                         | 4,457.90                     | 1.45                                    |                       |             |
|                                 |                                                                                                                    |                  |                                    |                              |                                         |                       |             |
|                                 | <u>STEEL</u>                                                                                                       |                  |                                    |                              |                                         |                       |             |
|                                 | <u>National Mineral Development Corporation (Nmhc)</u>                                                             |                  |                                    |                              |                                         |                       |             |
| 378                             | NMDC INTEGRATED STEEL PLANT - [N12000086]                                                                          | 1/2010           | 15,525.00 -                        | 15,525.00                    | 14,566.77                               | 05/2015 06/2019       | 06/2019     |
| 379                             | 2 MTPA PELLETT PLANT AT NAGARNAR - [N12000115]                                                                     | 11/2015          | 818.00 -                           | 818.00                       | 31.60                                   | 06/2020 -             | 06/2020     |
|                                 | Total                                                                                                              |                  | 16,343.00 -                        | 16,343.00                    | 14,598.37                               |                       |             |
|                                 |                                                                                                                    |                  |                                    |                              |                                         |                       |             |
|                                 | <u>TELECOMMUNICATIONS</u>                                                                                          |                  |                                    |                              |                                         |                       |             |



## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                                                                                     |                  |                                    |                              |                                         | (December 2018)       |             |
|---------------------------------|---------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                                                                                     |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                                                                                             | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                                                                                   | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
|                                 | <u>Bharat Sanchar Nigam Limited</u>                                                                                 |                  |                                    |                              |                                         |                       |             |
| 380                             | MAHARASHTRA CORE (LOT1)<br>- [N26000108]                                                                            | 8/2017           | 167.68<br>-                        | 167.68                       | 32.44                                   | 04/2018<br>02/2019    | 02/2019     |
| 381                             | MAHARASHTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT<br>- [N26000113]                                                  | 1/2018           | 231.80<br>-                        | 231.80                       | 77.65                                   | 10/2018<br>02/2019    | 02/2019     |
| 382                             | MADHYA PRADESH ACCESS (LOT1)<br>- [N26000110]                                                                       | 8/2017           | 215.30<br>-                        | 214.10                       | 33.46                                   | 05/2018<br>02/2019    | 02/2019     |
|                                 | Total                                                                                                               |                  | 614.78<br>-                        | 613.58                       | 143.55                                  |                       |             |
|                                 |                                                                                                                     |                  |                                    |                              |                                         |                       |             |
|                                 | <u>URBAN DEVELOPMENT</u>                                                                                            |                  |                                    |                              |                                         |                       |             |
|                                 | <u>Central Public Works Department</u>                                                                              |                  |                                    |                              |                                         |                       |             |
| 383                             | CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]      | 6/2015           | 197.33<br>-                        | 197.33                       | 14.25                                   | 04/2019<br>06/2020    | 06/2020     |
| 384                             | CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]                              | 10/2017          | 271.90<br>-                        | 271.90                       | 4.44                                    | 11/2019<br>-          | 11/2019     |
| 385                             | C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]  | 9/2017           | 150.29<br>-                        | 150.29                       | 2.58                                    | 03/2020<br>-          | 03/2020     |
| 386                             | CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]                                                   | 11/2017          | 171.72<br>-                        | 171.72                       | -                                       | 03/2020<br>-          | 03/2020     |
| 387                             | CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]                                                 | 1/2018           | 206.58<br>-                        | 206.58                       | .02                                     | 03/2019<br>-          | 03/2019     |
| 388                             | CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]  | 12/2017          | 188.00<br>-                        | 188.00                       | 85.71                                   | 06/2019<br>-          | 06/2019     |
| 389                             | RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]  | 11/2017          | 238.56<br>-                        | 238.56                       | 3.36                                    | 05/2020<br>-          | 05/2020     |
| 390                             | ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]               | 10/2016          | 209.84<br>-                        | 209.84                       | 12.71                                   | 03/2020<br>-          | 03/2020     |
| 391                             | RESIDENTIAL QUARTERS FOR HAL, BANGLORE - [N28000103]                                                                | 12/2016          | 246.31<br>-                        | 246.31                       | 34.88                                   | 02/2020<br>09/2020    | 09/2020     |
| 392                             | C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089] | 12/2015          | 209.00<br>-                        | 209.00                       | 52.00                                   | 10/2019<br>-          | 10/2019     |
|                                 | <u>Lucknow Metro Rail Corporation Limited</u>                                                                       |                  |                                    |                              |                                         |                       |             |
| 393                             | LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]                                                                    | 1/2016           | 6,928.00<br>6,928.00               | 6,928.00                     | 2,536.77                                | 03/2019<br>-          | 03/2019     |
|                                 | <u>Maharashtra Metro Rail Corporation Ltd.</u>                                                                      |                  |                                    |                              |                                         |                       |             |
| 394                             | DELHI MRTS PHASE-III - [N28000056]                                                                                  | 9/2011           | 38,585.00<br>-                     | 38,585.00                    | 37,044.70                               | 03/2016<br>05/2019    | 05/2019     |
| 395                             | PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]                                                                     | 12/2016          | 11,420.00<br>-                     | 11,420.00                    | 1,938.17                                | 11/2021<br>-          | 11/2021     |

### List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs. 150 Crore and above |                                                      |                  |                                    |                              |                                         | (December 2018)       |             |
|---------------------------------|------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                 |                                                      |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                           | Project                                              | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                               | 2                                                    | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
|                                 | <u>Nagpur Metro Rail Corporation Ltd</u>             |                  |                                    |                              |                                         |                       |             |
| 396                             | NAGPUR METRO RAIL<br>- [N28000085                    | 8/2014           | 8,680.00<br>-                      | 8,680.00                     | 4,787.71                                | 03/2018<br>12/2019    | 12/2019     |
|                                 | <u>National Building Construcion Corporation Ltd</u> |                  |                                    |                              |                                         |                       |             |
| 397                             | REDEVELOPMENT OF EAST KIDWAI NAGAR<br>- [N28000080   | 6/2012           | 4,264.00<br>-                      | 4,439.23                     | 3,671.53                                | 11/2019<br>-          | 11/2019     |
|                                 | Total                                                |                  | 71,966.53<br>-                     | 72,141.76                    | 50,188.83                               |                       |             |
|                                 |                                                      |                  |                                    |                              |                                         |                       |             |
|                                 | Grand Total                                          |                  | 8,28,510.16                        | 9,19,477.09                  | 3,20,173.53                             |                       |             |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

### Annexure - XIII

| Costing Rs. 150 Crore and above |                                                                                           |                  |                                   |                             | (December 2018)       |             |                  |
|---------------------------------|-------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                 |                                                                                           |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                            | Project                                                                                   | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                               | 2                                                                                         | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
|                                 | <u>ATOMIC ENERGY</u>                                                                      |                  |                                   |                             |                       |             |                  |
|                                 | <u>Bhavini Limited</u>                                                                    |                  |                                   |                             |                       |             |                  |
| 1                               | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)<br>- [020100044]                        | 09/2003          | 3,492.00<br>-                     | 6,100.00                    | 09/2010<br>-          | 03/2019     | 74.69            |
|                                 | Total                                                                                     |                  | 3,492.00<br>-                     | 6,100.00                    |                       |             |                  |
|                                 | <u>CIVIL AVIATION</u>                                                                     |                  |                                   |                             |                       |             |                  |
|                                 | <u>Airport Authority Of India Limited</u>                                                 |                  |                                   |                             |                       |             |                  |
| 2                               | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR<br>[N04000073] | 10/2013          | 314.61<br>-                       | 441.33                      | 09/2018<br>-          | 06/2020     | 40.28            |
|                                 | Total                                                                                     |                  | 314.61<br>-                       | 441.33                      |                       |             |                  |
|                                 | <u>COAL</u>                                                                               |                  |                                   |                             |                       |             |                  |
|                                 | <u>Neyveli Lignite Corporation</u>                                                        |                  |                                   |                             |                       |             |                  |
| 3                               | NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW<br>- [N06000152]                      | 07/2016          | 17,237.00<br>-                    | 17,237.80                   | 11/2021<br>-          | 11/2021     | .00              |
|                                 | <u>Northern Coal Fields Limited</u>                                                       |                  |                                   |                             |                       |             |                  |
| 4                               | NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI<br>- [N06000033]                   | 10/2007          | 259.40<br>-                       | 486.57                      | 03/2012<br>-          | -           | 87.58            |
|                                 | <u>Singareni Colliers Company Limited</u>                                                 |                  |                                   |                             |                       |             |                  |
| 5                               | RAMAGUNDAM OC-II EXTENSION<br>- [N06000078]                                               | 12/2009          | 418.97<br>-                       | 489.62                      | 03/2012<br>-          | 03/2023     | 16.86            |
| 6                               | SHANTIKHANI LONGWALL PROJ-SCCL<br>- [N06000017]                                           | 10/2006          | 249.03<br>-                       | 448.86                      | 03/2012<br>-          | 03/2024     | 80.24            |
| 7                               | KAKATIYAKHANI OPENCAST-2 PROJECT<br>- [N06000129]                                         | 05/2015          | 397.09<br>-                       | 442.42                      | 03/2019<br>-          | 03/2019     | 11.42            |
| 8                               | RCE OF INDARAM OCP(1.20 MTPA)<br>- [N06000093]                                            | 07/2011          | 162.76<br>-                       | 349.28                      | 03/2015<br>-          | 03/2021     | 114.60           |
|                                 | <u>South-Eastern Coal Fields Limited</u>                                                  |                  |                                   |                             |                       |             |                  |
| 9                               | JAGANNATHPOR OCP(3.00MTY)<br>- [N06000075]                                                | 09/2008          | 152.43<br>-                       | 459.49                      | 03/2015<br>-          | 03/2020     | 201.44           |
|                                 | Total                                                                                     |                  | 18,876.68<br>-                    | 19,914.04                   |                       |             |                  |
|                                 | <u>DEFENCE PRODUCTION</u>                                                                 |                  |                                   |                             |                       |             |                  |
|                                 | <u>Goa Shipyard Limited</u>                                                               |                  |                                   |                             |                       |             |                  |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs. 150 Crore and above |                                                                                       |                  |                                   |                             | (December 2018)       |             |                  |
|---------------------------------|---------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                 |                                                                                       |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                            | Project                                                                               | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                               | 2                                                                                     | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 10                              | CONSTRUCTION WORKS PHASE 4<br>- [N39000001                                            | 12/2016          | 167.69<br>168.00                  | 170.37                      | 05/2018<br>-          | 01/2019     | 1.41             |
| 11                              | CONSTRUCTION WORKS PHASE 3B<br>- [N39000002                                           | 12/2016          | 285.95<br>286.00                  | 291.29                      | 08/2020<br>-          | 08/2020     | 1.85             |
|                                 | Total                                                                                 |                  | 453.64<br>-                       | 461.66                      |                       |             |                  |
|                                 |                                                                                       |                  |                                   |                             |                       |             |                  |
|                                 | <u>HEALTH AND FAMILY WELFARE</u>                                                      |                  |                                   |                             |                       |             |                  |
|                                 | <u>Hospital Services Consultancy Corporation Ltd</u>                                  |                  |                                   |                             |                       |             |                  |
| 12                              | LHMC NEW DELHI-RE-DEVELOPMENT<br>- [N21000003                                         | 02/2013          | 414.11<br>-                       | 513.89                      | 11/2013<br>-          | 10/2020     | 24.10            |
| 13                              | CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI<br>JHAJJAR - [N21000011                    | 09/2014          | 505.58<br>-                       | 523.00                      | 03/2018<br>-          | -           | 3.45             |
| 14                              | GERIATRICS BLOCK- AIIMS DLEHI<br>- [N21000019                                         | 12/2017          | 156.56<br>-                       | 156.65                      | -<br>-                | 02/2020     | .06              |
|                                 | Total                                                                                 |                  | 1,076.25<br>-                     | 1,193.54                    |                       |             |                  |
|                                 |                                                                                       |                  |                                   |                             |                       |             |                  |
|                                 | <u>HEAVY INDUSTRY</u>                                                                 |                  |                                   |                             |                       |             |                  |
|                                 | <u>Natrip Implementation Society</u>                                                  |                  |                                   |                             |                       |             |                  |
| 15                              | NATIONAL AUTOMOTIVE TESTING AND RD<br>INFRASTRUCTURE PROJECT (NATRIP)<br>- [N20000001 | 04/2011          | 1,718.00<br>-                     | 3,827.30                    | 09/2011<br>-          | 06/2019     | 122.78           |
|                                 | Total                                                                                 |                  | 1,718.00<br>-                     | 3,827.30                    |                       |             |                  |
|                                 |                                                                                       |                  |                                   |                             |                       |             |                  |
|                                 | <u>PETROLEUM</u>                                                                      |                  |                                   |                             |                       |             |                  |
|                                 | <u>Hindustan Petroleum Corporation Limited</u>                                        |                  |                                   |                             |                       |             |                  |
| 16                              | 50 MW CAPACITY WIND POWER PROJECT UNDER<br>PHASE II - [N16000209                      | 11/2011          | 310.00<br>-                       | 370.00                      | 03/2013<br>-          | -           | 19.35            |
|                                 | <u>Indian Oil Corporation Limited</u>                                                 |                  |                                   |                             |                       |             |                  |
| 17                              | LPG TERMINAL AT KOCHI<br>- [N16000171                                                 | 10/2015          | 607.06<br>-                       | 714.25                      | 10/2017<br>-          | 03/2019     | 17.66            |
|                                 | <u>Indian Strategic Petroleum Reserves Ltd</u>                                        |                  |                                   |                             |                       |             |                  |
| 18                              | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR<br>- [N16000169                          | 01/2006          | 993.00<br>-                       | 1,693.00                    | 01/2012<br>-          | -           | 70.49            |
|                                 | <u>Mangalore Refinery And Petrochemicals Limited</u>                                  |                  |                                   |                             |                       |             |                  |
| 19                              | CAPACITY ENHANCEMENT/ REVAMP OF NHT-<br>2/PLATFORMER-2/CCR-2/PSA-2/RSU<br>[N16000255  | 05/2015          | 224.00<br>207.00                  | 207.25                      | 04/2019<br>-          | 04/2019     | .12              |
|                                 | <u>Oil &amp; Natural Gas Corporation Limited</u>                                      |                  |                                   |                             |                       |             |                  |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs. 150 Crore and above |                                                                                                         |                  |                                   |                             | (December 2018)       |             |                  |
|---------------------------------|---------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                 |                                                                                                         |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                            | Project                                                                                                 | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                               | 2                                                                                                       | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 20                              | LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS<br>- [N16000213]                       | 12/2015          | 3,190.69<br>-                     | 3,247.19<br>-               | 04/2018<br>-          | 05/2019     | 1.77             |
|                                 | <u>Oil India Limited</u>                                                                                |                  |                                   |                             |                       |             |                  |
| 21                              | SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN<br>- [N16000167] | 07/2011          | 352.56<br>-                       | 438.84<br>-                 | 03/2017<br>-          | 06/2019     | 24.47            |
| 22                              | UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE<br>- [N18000148] | 09/2012          | 871.35<br>-                       | 1,200.00<br>-               | 03/2015<br>-          | -           | 37.72            |
|                                 | Total                                                                                                   |                  | 6,548.66<br>-                     | 7,870.53<br>-               |                       |             |                  |
|                                 |                                                                                                         |                  |                                   |                             |                       |             |                  |
|                                 | <u>POWER</u>                                                                                            |                  |                                   |                             |                       |             |                  |
|                                 | <u>National Hydro-Electric Power Corporation</u>                                                        |                  |                                   |                             |                       |             |                  |
| 23                              | PARBATI HEP (4X200 MW) (NHPC) II<br>- [180100210]                                                       | 09/2002          | 3,919.59<br>-                     | 9,394.80<br>-               | 09/2009<br>-          | 12/2021     | 139.69           |
| 24                              | SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)<br>- [180100221]                                                | 09/2003          | 6,285.33<br>-                     | 19,496.34<br>-              | 09/2010<br>-          | -           | 210.19           |
|                                 | <u>National Thermal Power Corporation</u>                                                               |                  |                                   |                             |                       |             |                  |
| 25                              | GADARWARA SUPER THERMAL POWER PROJECT STAGE-I<br>- [N18000151]                                          | 03/2013          | 11,638.55<br>-                    | 12,865.92<br>-              | 09/2017<br>-          | 06/2019     | 10.55            |
| 26                              | TAPOVAN-VISHNUGAD HEP (4X130MW)<br>- [N18000014]                                                        | 11/2006          | 2,978.48<br>-                     | 3,846.30<br>-               | 03/2013<br>-          | 12/2020     | 29.14            |
| 27                              | DARLIPALLI STPP STAGE-I (2X800 MW)<br>- [N18000176]                                                     | 02/2014          | 12,532.44<br>-                    | 13,740.53<br>-              | 08/2018<br>-          | 06/2019     | 9.64             |
| 28                              | NORTH KARANPURA STPP (3X660 MW)<br>- [N18000177]                                                        | 02/2014          | 14,366.58<br>-                    | 15,164.05<br>-              | 02/2019<br>-          | 10/2020     | 5.55             |
| 29                              | BRBCL-NABINAGAR TPP- JV (4X250 MW)<br>- [N18000190]                                                     | 01/2007          | 5,353.00<br>-                     | 7,998.00<br>-               | 05/2014<br>-          | 05/2019     | 49.41            |
| 30                              | NPGCPL-NABINAGAR STPP - JV (3X660 MW)<br>- [N18000192]                                                  | 01/2013          | 12,964.60<br>-                    | 13,731.26<br>-              | 01/2018<br>-          | 05/2020     | 5.91             |
| 31                              | KUDGI STPP STAGE 1<br>- [N18000131]                                                                     | 01/2012          | 15,166.19<br>-                    | 16,934.65<br>-              | 01/2017<br>-          | -           | 11.66            |
| 32                              | LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)<br>- [N18000140]                                  | 12/2012          | 11,846.00<br>-                    | 12,739.82<br>-              | 06/2017<br>-          | 06/2019     | 7.55             |
| 33                              | LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW<br>- [N18000142]                                      | 07/2012          | 1,527.00<br>-                     | 1,801.07<br>-               | 08/2017<br>-          | -           | 17.95            |
| 34                              | KHARGONE STPP STAGE I (1320 MW)<br>- [N18000205]                                                        | 03/2015          | 9,870.51<br>-                     | 11,148.86<br>-              | 09/2019<br>-          | 09/2019     | 12.95            |
| 35                              | PAKRI BARWADIH COAL MINING PROJECT<br>- [N18000225]                                                     | 10/2004          | 4,237.96<br>4,238.00              | 4,552.00<br>-               | 10/2017<br>-          | -           | 7.41             |
|                                 | <u>North East Electric Power Corporation</u>                                                            |                  |                                   |                             |                       |             |                  |
| 36                              | TRIPURA GAS BASED POWER PROJECT<br>- [N18000071]                                                        | 07/2009          | 421.01<br>-                       | 1,078.31<br>-               | 07/2013<br>-          | -           | 156.12           |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs. 150 Crore and above |                                                                                                                   |                  |                                   |                             | (December 2018)       |             |                  |
|---------------------------------|-------------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                 |                                                                                                                   |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                            | Project                                                                                                           | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                               | 2                                                                                                                 | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
|                                 | <u>Power Grid Corporation Of India Limited</u>                                                                    |                  |                                   |                             |                       |             |                  |
| 37                              | COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103 | 09/2011          | 1,940.13 -                        | 2,702.65                    | 09/2014 -             | -           | 39.30            |
| 38                              | COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144    | 03/2013          | 2,514.88 -                        | 3,190.27                    | 12/2015 -             | -           | 26.86            |
| 39                              | TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215           | 01/2014          | 1,788.41 -                        | 2,333.71                    | 09/2017 -             | 11/2018     | 30.49            |
| 40                              | COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249        | 12/2014          | 4,754.42 -                        | 9,141.97                    | 12/2018 -             | 12/2019     | 92.28            |
| 41                              | NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250                   | 12/2014          | 5,111.33 -                        | 6,652.57                    | 12/2018 -             | 12/2019     | 30.15            |
|                                 | <u>Satluj Jal Vidyut Nigam Limited</u>                                                                            |                  |                                   |                             |                       |             |                  |
| 42                              | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194                                     | 05/2015          | 436.68 -                          | 602.44                      | 12/2016 -             | 03/2019     | 37.96            |
|                                 | <u>Thdc India Limited</u>                                                                                         |                  |                                   |                             |                       |             |                  |
| 43                              | VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042                                                           | 08/2008          | 2,491.58 -                        | 4,105.30                    | 06/2013 -             | 12/2021     | 64.77            |
| 44                              | TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010                                                                   | 07/2006          | 1,657.00 -                        | 4,401.90                    | 02/2016 -             | 05/2021     | 165.65           |
|                                 | Total                                                                                                             |                  | 1,33,801.67 -                     | 1,77,622.72                 |                       |             |                  |
|                                 | <u>RAILWAYS</u>                                                                                                   |                  |                                   |                             |                       |             |                  |
|                                 | <u>Central Railways</u>                                                                                           |                  |                                   |                             |                       |             |                  |
| 45                              | 3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247                                                                    | 04/2011          | 184.06 -                          | 298.70                      | 03/2019 -             | 03/2019     | 62.28            |
| 46                              | AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181                                                                     | 02/1997          | 2,271.50 -                        | 3,712.50                    | 03/2021 -             | 03/2021     | 63.44            |
| 47                              | AMRAVATI-NARKHER NL(CR) - [220100118                                                                              | 06/1994          | 663.01 175.30                     | 858.96                      | 06/1999 -             | -           | 389.99           |
| 48                              | PUNE-NASIK (265 KM) - [N22000354                                                                                  | 02/2016          | 2,425.00 -                        | 5,341.68                    | 03/2024 -             | 03/2024     | 120.28           |
| 49                              | VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355                                                                       | 02/2016          | 2,750.00 -                        | 3,438.51                    | 03/2024 -             | 03/2024     | 25.04            |
|                                 | <u>Container Corporation Of India</u>                                                                             |                  |                                   |                             |                       |             |                  |
| 50                              | MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431                                                               | 08/2016          | 234.50 -                          | 235.00                      | 03/2019 -             | 12/2020     | .21              |
|                                 | <u>East Central Railways</u>                                                                                      |                  |                                   |                             |                       |             |                  |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs. 150 Crore and above |                                                                                                                          |                  |                                   |                             | (December 2018)       |             |                  |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                 |                                                                                                                          |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                            | Project                                                                                                                  | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                               | 2                                                                                                                        | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 51                              | KODERMA-RANCHI VIA BARKAKANA (NL), ECR<br>- [220100222                                                                   | 03/1999          | 1,033.07<br>-                     | 3,020.94                    | -                     | 03/2021     | 192.42           |
| 52                              | HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR<br>- [220100303                                                                   | 04/2003          | 528.65<br>-                       | 2,066.77                    | -                     | 03/2023     | 290.95           |
| 53                              | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN<br>ECR<br>- [N22000002                                                     | 04/1996          | 477.88<br>283.95                  | 749.00                      | 03/2012<br>-          | 03/2020     | 163.78           |
| 54                              | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR<br>- [220100240                                                               | 04/1997          | 324.73<br>-                       | 1,156.41                    | 03/2012<br>-          | 03/2020     | 256.11           |
| 55                              | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)<br>- [220100257                                                                    | 04/1997          | 162.87<br>-                       | 589.15                      | -                     | 03/2022     | 261.73           |
| 56                              | KOSI BRIDGE (NL), ECR<br>- [220100304                                                                                    | 04/2002          | 499.41<br>-                       | 516.02                      | 03/2020<br>-          | 03/2020     | 3.33             |
| 57                              | NAWADA-LAXMIPUR (NL)<br>- [N22000167                                                                                     | 04/2008          | 620.57<br>-                       | 2,626.98                    | -                     | -           | 323.32           |
| 58                              | MOTIHARI-SITAMARHI (NL)<br>- [N22000174                                                                                  | 04/2006          | 211.00<br>-                       | 926.09                      | -                     | -           | 338.91           |
| 59                              | SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)<br>- [N22000175                                                              | 04/2008          | 678.62<br>-                       | 2,393.23                    | -                     | -           | 252.66           |
| 60                              | SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR<br>AND SAHARSA-FORBESGANJ (GC)<br>- [N22000180                                | 04/2004          | 372.14<br>-                       | 1,474.47                    | -                     | 03/2021     | 296.21           |
| 61                              | JAYNAGAR-BIJALPURA INCLUDING EXTENSION<br>BIJALPURA-BARDIBAS(NEPAL) GC<br>- [N22000181                                   | 04/2009          | 548.00<br>-                       | 785.87                      | 03/2020<br>-          | 03/2020     | 43.41            |
| 62                              | HAJIPUR-RAMDAYALUNAGAR DOUBLING<br>- [N22000182                                                                          | 04/2013          | 213.01<br>-                       | 367.17                      | -                     | -           | 72.37            |
| 63                              | MUZAFFARPUR-SITAMARHI NEW LINE<br>- [N22000374                                                                           | 01/1991          | 332.15<br>-                       | 559.91                      | 07/2014<br>-          | -           | 68.57            |
| 64                              | SAGAULI VALMIKINAGAR DOUBLING 109.7 KM<br>- [N22000472                                                                   | 04/2016          | 744.04<br>-                       | 1,215.54                    | 03/2021<br>-          | 03/2022     | 63.37            |
| 65                              | MUZAFFARPUR SAGAULI DOUBLING 100.60 KM<br>- [N22000473                                                                   | 04/2016          | 731.64<br>-                       | 1,185.73                    | 03/2021<br>-          | 03/2022     | 62.06            |
| 66                              | PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN<br>PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM<br>- [N22000474          | 11/2001          | 624.47<br>-                       | 3,550.00                    | 02/2016<br>-          | 03/2021     | 468.48           |
| 67                              | RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR<br>ISLAMPUR<br>- [N22000475                                               | 04/1998          | 180.82<br>-                       | 528.26                      | -                     | -           | 192.15           |
| 68                              | FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW<br>LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-<br>BIHARSHARIF, - [N22000476 | 04/1991          | 329.39<br>-                       | 566.41                      | -                     | 12/2021     | 71.96            |
| <u>East Coast Railway</u>       |                                                                                                                          |                  |                                   |                             |                       |             |                  |
| 69                              | TALCHER-BIMALAGARH(NL)(ECOR)<br>- [220100328                                                                             | 04/2005          | 810.78<br>-                       | 1,928.07                    | 06/2021<br>-          | 03/2023     | 137.80           |
| 70                              | KHURDA ROAD-BOLANGIR(NL)ECOR<br>- [220100284                                                                             | 04/1994          | 2,923.13<br>-                     | 3,798.80                    | 03/2009<br>-          | 06/2021     | 29.96            |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs. 150 Crore and above |                                                                                                                          |                  |                                   |                             | (December 2018)       |             |                  |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                 |                                                                                                                          |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                            | Project                                                                                                                  | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                               | 2                                                                                                                        | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 71                              | KIRANDUL - JAGDALPUR DOUBLING<br>- [N22000318]                                                                           | 12/2012          | 1,160.00<br>-                     | 1,160.83                    | 03/2020<br>-          | 03/2020     | .07              |
| 72                              | SAMBALPUR - ANGUL RLY. ELECTRIFICATION<br>- [N22000319]                                                                  | 03/2012          | 155.81<br>-                       | 238.03                      | 03/2020<br>-          | 03/2020     | 52.77            |
| 73                              | GAYA-DALTONGANJ VIA RAFIGANJ (NL)<br>- [N22000168]                                                                       | 04/2008          | 445.25<br>-                       | 2,860.55                    | -<br>-                | -           | 542.46           |
| 74                              | GAYA-CHATRA (NL)<br>- [N22000169]                                                                                        | 04/2008          | 415.67<br>-                       | 549.75                      | -<br>-                | -           | 32.26            |
| 75                              | BIHTA-AURANGABAD (NL)<br>- [N22000170]                                                                                   | 04/2008          | 326.20<br>-                       | 2,995.01                    | -<br>-                | -           | 818.15           |
| 76                              | SAKRI-HASANPUR ROAD (NL)<br>- [N22000171]                                                                                | 04/1999          | 325.00<br>-                       | 729.92                      | -<br>-                | 03/2021     | 124.59           |
| 77                              | CHHAPRA-MUZAFFARPUR (NL)<br>- [N22000172]                                                                                | 04/2006          | 378.56<br>-                       | 2,614.36                    | -<br>-                | 03/2022     | 590.61           |
| 78                              | JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER<br>ROAD 3RD AND 4TH LINE<br>[N22000380]                                    | 04/2015          | 701.61<br>-                       | 810.02                      | 11/2018<br>-          | 03/2021     | 15.45            |
| <u>Eastern Railways</u>         |                                                                                                                          |                  |                                   |                             |                       |             |                  |
| 79                              | TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER<br>- [220100272]                                                             | 04/2000          | 1,188.91<br>-                     | 1,620.01                    | 03/2019<br>12/2009    | -           | 36.26            |
| 80                              | DEOGHAR - SULTANGANJ (INL), ER<br>- [220100273]                                                                          | 04/2000          | 607.09<br>-                       | 607.91                      | 02/2013<br>-          | -           | .14              |
| 81                              | DAKSHIN-BARASAL-LAKSHMIKANTAPUR<br>- [N22000116]                                                                         | 04/2009          | 259.51<br>-                       | 533.59                      | 02/2012<br>-          | -           | 105.61           |
| 82                              | TARAKESHWAR-MAGRA NEW BG LINE<br>- [N22000235]                                                                           | 04/2010          | 365.17<br>-                       | 527.54                      | -<br>-                | -           | 44.46            |
| 83                              | SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-<br>MINAKHAN VIA GHATAKPUR NL<br>[N22000241]                                  | 04/2000          | 297.47<br>-                       | 299.03                      | -<br>-                | -           | .52              |
| 84                              | CHANDPARA-BANGAON DOUBLING WITH EXENSION TO<br>CHANDBAZAR AND NEW MM FOR BONGAON-<br>PORAMAHESTALA AND CHA - [N22000242] | 04/2003          | 337.96<br>-                       | 355.44                      | -<br>-                | -           | 5.17             |
| 85                              | MAGRAHAT-DIAMOND HARBOUR WITH MM<br>SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND<br>HATBOUR - BAHRAHAT-KULPI NL - [N22000243]  | 04/2009          | 499.96<br>-                       | 665.75                      | 02/2012<br>-          | -           | 33.16            |
| 86                              | LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-<br>JONGALPARA-FURFURA SHARIF NL<br>[N22000244]                                  | 04/2009          | 257.42<br>-                       | 258.73                      | 03/2014<br>-          | -           | .51              |
| 87                              | MONIGRAM- NIMITTA<br>- [N22000301]                                                                                       | 04/2012          | 250.93<br>-                       | 259.23                      | -<br>-                | -           | 3.31             |
| 88                              | BAZAR SAU -AZIMGANJ JN. DOUBLING<br>- [N22000302]                                                                        | 04/2012          | 255.64<br>-                       | 272.20                      | -<br>-                | -           | 6.48             |
| 89                              | MANDARHILL-DUMKA-RAMPURHAT (NL),ER<br>- [220100168]                                                                      | 04/1995          | 1,125.89<br>-                     | 1,126.36                    | 03/2016<br>-          | 03/2020     | .04              |
| 90                              | GHUTIASHARIF-CANNING (ER)<br>- [N22000117]                                                                               | 04/2009          | 193.08<br>-                       | 612.45                      | 12/2011<br>-          | -           | 217.20           |



## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs. 150 Crore and above |                                                                                                                    |                  |                                   |                             | (December 2018)       |             |                  |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                 |                                                                                                                    |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                            | Project                                                                                                            | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                               | 2                                                                                                                  | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 91                              | LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216] | 04/1987          | 406.99<br>-                       | 544.72                      | 03/2006<br>-          | -           | 33.84            |
| 92                              | HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]                                                                     | 04/2010          | 172.03<br>-                       | 260.10                      | -<br>-                | -           | 51.19            |
| 93                              | PIRPAINTI-BHAGALPUR - [N22000222]                                                                                  | 04/2011          | 261.38<br>-                       | 332.14                      | -<br>-                | -           | 27.07            |
| 94                              | KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]                      | 04/2010          | 174.56<br>-                       | 175.99                      | -<br>-                | -           | .82              |
|                                 | <u>Metropolitan Rapid Transport Projects</u>                                                                       |                  |                                   |                             |                       |             |                  |
| 95                              | TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]                      | 03/2000          | 1,049.69<br>-                     | 3,404.92                    | 12/2006<br>-          | -           | 224.37           |
| 96                              | EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]                                                 | 04/2006          | 495.74<br>-                       | 734.01                      | 06/2013<br>-          | 03/2019     | 48.06            |
| 97                              | MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]                                                              | 04/2008          | 5,300.00<br>-                     | 7,986.04                    | 03/2014<br>-          | 03/2019     | 50.68            |
|                                 | <u>North Central Railway</u>                                                                                       |                  |                                   |                             |                       |             |                  |
| 98                              | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]                                                    | 04/1986          | 158.77<br>274.56                  | 634.48                      | 03/1994<br>-          | -           | 131.09           |
| 99                              | ETAWAH-MAINPURI (NL),NCR - [220100318]                                                                             | 04/1997          | 120.00<br>-                       | 245.39                      | 12/2008<br>-          | -           | 104.49           |
| 100                             | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]                                                           | 04/1999          | 108.00<br>-                       | 432.72                      | 12/2009<br>-          | -           | 300.67           |
| 101                             | GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]                                                       | 04/2011          | 2,912.96<br>-                     | 3,845.60                    | 03/2022<br>-          | 03/2022     | 32.02            |
|                                 | <u>North East Frontier Railway</u>                                                                                 |                  |                                   |                             |                       |             |                  |
| 102                             | NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]                              | 04/1983          | 297.32<br>-                       | 614.00                      | 03/2019<br>-          | 03/2020     | 106.51           |
| 103                             | KATIHAR - JOGBANI (GC)(NEFR) - [220100247]                                                                         | 09/2001          | 792.46<br>-                       | 1,320.00                    | 12/2010<br>-          | -           | 66.57            |
| 104                             | BHAIRABI SAIRONG, NL, NEFR - [N22000100]                                                                           | 04/2008          | 2,393.47<br>-                     | 4,968.00                    | 03/2014<br>-          | 12/2020     | 107.56           |
| 105                             | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]                                               | 04/2000          | 1,180.19<br>-                     | 3,040.00                    | 12/2008<br>-          | 03/2019     | 157.59           |
| 106                             | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]                                                                  | 04/2003          | 4,454.17<br>-                     | 13,809.00                   | 03/2011<br>-          | 03/2020     | 210.02           |
| 107                             | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]                                      | 09/2006          | 385.20<br>-                       | 1,532.00                    | 03/2019<br>-          | 03/2020     | 297.72           |
| 108                             | NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]                                             | 09/2006          | 532.87<br>-                       | 2,145.00                    | 03/2019<br>-          | 03/2020     | 302.54           |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs. 150 Crore and above |                                                                                                                 |                  |                                   |                             | (December 2018)       |             |                  |
|---------------------------------|-----------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                 |                                                                                                                 |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                            | Project                                                                                                         | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                               | 2                                                                                                               | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 109                             | NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]                                    | 04/2006          | 2,326.52                          | 3,000.00                    | 03/2015               | 10/2021     | 28.95            |
| 110                             | KISHANGANJ JALALGARH, NL, NEFR - [N22000101]                                                                    | 04/2008          | 333.76                            | 360.00                      | -                     | 03/2020     | 7.86             |
| 111                             | SEVOK RANGPO, NEFR - [N22000102]                                                                                | 04/2008          | 1,339.48                          | 4,084.69                    | 12/2015               | 03/2020     | 204.95           |
| 112                             | NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]                                                          | 04/2010          | 221.42                            | 380.00                      | -                     | 03/2020     | 71.62            |
| 113                             | CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]                                                        | 04/1999          | 895.00                            | 1,733.20                    | 03/2007               | 04/2016     | 93.65            |
| 114                             | AGARTALA-AKHAURA NL - [N22000195]                                                                               | 04/2012          | 569.63                            | 650.00                      | 03/2020               | 10/2022     | 14.11            |
| 115                             | NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]                                                             | 04/2010          | 906.46                            | 6,000.00                    | 03/2021               | 03/2021     | 561.92           |
| 116                             | NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]                                                           | 04/2010          | 242.22                            | 471.00                      | 03/2020               | 03/2020     | 94.45            |
| 117                             | NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]                                                            | 04/2010          | 241.52                            | 394.28                      | -                     | -           | 63.25            |
| 118                             | MURKONGSELEK-PASIGHAT NL - [N22000208]                                                                          | 04/2011          | 414.84                            | 661.00                      | 03/2020               | 03/2020     | 59.34            |
| 119                             | NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209] | 04/1999          | 819.23                            | 1,871.00                    | -                     | -           | 128.39           |
| 120                             | AMBAR FALAKATA TO NEW MAYNAGURI - [N22000210]                                                                   | 04/2011          | 314.00                            | 551.00                      | 03/2019               | 03/2019     | 75.48            |
| 121                             | NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]                                  | 04/2016          | 602.27                            | 612.00                      | 12/2021               | 03/2020     | 1.62             |
| <u>North Eastern Railway</u>    |                                                                                                                 |                  |                                   |                             |                       |             |                  |
| 122                             | MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]                                                                    | 04/2003          | 218.19                            | 413.56                      | 06/2018               | 10/2018     | 89.54            |
| 123                             | KICHHA-KHATIMA (NL) - NER - [220100317]                                                                         | 04/2003          | 142.45                            | 228.40                      | -                     | -           | 60.34            |
| 124                             | HATHUA-BHATNI (N L) (NER) - [220100319]                                                                         | 04/2005          | 230.03                            | 770.08                      | 12/2022               | 05/2019     | 234.77           |
| 125                             | KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]                                                           | 04/1999          | 744.71                            | 1,126.79                    | -                     | -           | 51.31            |
| 126                             | GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]                                                                       | 04/2014          | 182.92                            | 197.73                      | -                     | -           | 8.10             |
| 127                             | ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]                                                             | 03/2013          | 307.00                            | 308.00                      | -                     | -           | .33              |
| 128                             | CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]                                                    | 03/2007          | 243.78                            | 895.00                      | 12/2021               | 12/2021     | 267.13           |
| 129                             | BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]                                                                    | 03/2008          | 195.64                            | 435.00                      | -                     | 03/2018     | 122.35           |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs. 150 Crore and above |                                                                                    |                  |                                   |                             | (December 2018)       |             |                  |
|---------------------------------|------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                 |                                                                                    |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                            | Project                                                                            | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                               | 2                                                                                  | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 130                             | AUNRIHAR MANDUADIH GAZIPUR VARANASI UP<br>- [N22000133]                            | 03/2012          | 199.75<br>-                       | 270.00                      | 08/2018<br>-          | 01/2019     | 35.17            |
| 131                             | CHHAPRA-BALLIA UP<br>- [N22000134]                                                 | 03/2013          | 295.00<br>-                       | 477.31                      | 01/2019<br>-          | 02/2019     | 61.80            |
| 132                             | KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP<br>- [N22000136]        | 03/2013          | 643.00<br>-                       | 644.00                      | -<br>-                | -           | .16              |
| 133                             | GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW<br>- [N22000455]     | 04/1997          | 233.00<br>-                       | 318.42                      | 04/1999<br>-          | -           | 36.66            |
| 134                             | INDARA - DOHRIGHAT GAUGE CONVERSION.<br>- [N22000456]                              | 04/2016          | 213.00<br>-                       | 213.35                      | 04/2016<br>-          | 01/2022     | .16              |
| 135                             | MANDHANA - BRAHMAWART NEW LINE PROJECT.<br>- [N22000458]                           | 04/1997          | 609.04<br>1,063.00                | 1,807.88                    | 04/1999<br>-          | 03/2019     | 70.07            |
| 136                             | BURHWAL - GONDA - 3RD RUNNING LINE.<br>- [N22000468]                               | 04/2016          | 602.50<br>-                       | 714.34                      | -<br>-                | -           | 18.56            |
|                                 | <u>North Western Railway</u>                                                       |                  |                                   |                             |                       |             |                  |
| 137                             | JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR)<br>- [N22000113] | 04/2008          | 653.19<br>-                       | 1,116.00                    | 03/2014<br>-          | 03/2019     | 70.85            |
| 138                             | DAUSA-GANGAPUR CITY(NL),NWR<br>- [220100184]                                       | 02/1997          | 410.08<br>-                       | 795.01                      | 02/2019<br>-          | 02/2019     | 93.87            |
| 139                             | PHULERA - DIGANA DOUBLING<br>- [N22000326]                                         | 05/2015          | 600.00<br>-                       | 685.99                      | 03/2020<br>-          | 03/2020     | 14.33            |
| 140                             | AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL<br>[N22000330]    | 05/2015          | 873.71<br>-                       | 1,103.04                    | -<br>-                | -           | 26.25            |
| 141                             | HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)<br>- [N22000112]                      | 04/2008          | 829.74<br>-                       | 1,216.00                    | 03/2015<br>-          | 06/2020     | 46.55            |
| 142                             | BANGURGRAM-GURIYA PATCH DOUBLING<br>- [N22000137]                                  | 04/2012          | 246.08<br>-                       | 348.55                      | 12/2019<br>-          | 06/2019     | 41.64            |
| 143                             | RATLAM-DUNGARPUR VIA BANSWARA (NL)<br>- [N22000147]                                | 04/2011          | 2,082.75<br>-                     | 2,878.97                    | -<br>-                | -           | 38.23            |
| 144                             | THIYAT HAMIRA-SANU<br>- [N22000149]                                                | 04/2013          | 236.93<br>-                       | 294.90                      | 10/2018<br>-          | 10/2018     | 24.47            |
| 145                             | AJMER-KOTA (NASIRABAD-JAUNDRI)<br>- [N22000150]                                    | 04/2013          | 822.00<br>-                       | 1,099.54                    | -<br>-                | -           | 33.76            |
| 146                             | PUSHKAR-MERTA<br>- [N22000151]                                                     | 04/2013          | 323.00<br>-                       | 432.22                      | -<br>-                | -           | 33.81            |
| 147                             | MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR<br>[N22000152]         | 04/2013          | 420.18<br>-                       | 420.18                      | 03/2020<br>-          | 12/2019     | .00              |
| 148                             | AJMER-BANGURGRAM<br>- [N22000155]                                                  | 04/2011          | 213.39<br>-                       | 244.02                      | 11/2019<br>-          | 11/2019     | 14.35            |
| 149                             | ALWAR-BANDIKUI DOUBLING<br>- [N22000157]                                           | 04/2013          | 242.09<br>-                       | 349.00                      | 02/2019<br>-          | 03/2019     | 44.16            |
|                                 | <u>Northern Railway</u>                                                            |                  |                                   |                             |                       |             |                  |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs. 150 Crore and above |                                                                                                                   |                  |                                   |                             | (December 2018)       |             |                  |
|---------------------------------|-------------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                 |                                                                                                                   |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                            | Project                                                                                                           | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                               | 2                                                                                                                 | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 150                             | JIND-SONEPAT (NL),NR<br>- [220100280]                                                                             | 01/2004          | 238.56<br>-                       | 740.00                      | 03/2012<br>-          | -           | 210.19           |
| 151                             | GRADE SEPERATOR AT DAYABASTI<br>- [N22000269]                                                                     | 04/1999          | 156.65<br>-                       | 197.17                      | -<br>-                | -           | 25.87            |
| 152                             | ROHTAK-MEHAM HANSI<br>- [N22000272]                                                                               | 04/2012          | 287.00<br>-                       | 625.00                      | 12/2011<br>-          | -           | 117.77           |
| 153                             | HARIDWAR-LAKSAR<br>- [N22000289]                                                                                  | 04/2012          | 219.83<br>-                       | 346.63                      | -<br>-                | -           | 57.68            |
| 154                             | CHANDIGARH-BADDI NL<br>- [N22000296]                                                                              | 04/2007          | 328.14<br>-                       | 1,540.00                    | -<br>-                | -           | 369.31           |
| 155                             | NANGALDAM-TALWARA(NL),NR<br>- [220100188]                                                                         | 03/1981          | 450.00<br>-                       | 2,100.00                    | 07/2012<br>-          | -           | 366.67           |
| 156                             | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR<br>- [220100133]                                                              | 03/1995          | 2,500.00<br>-                     | 27,949.00                   | 11/2002<br>-          | 03/2021     | 1,017.96         |
| 157                             | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR<br>- [220100258]                                                           | 03/2002          | 625.30<br>408.76                  | 876.10                      | 06/2007<br>-          | -           | 114.33           |
| 158                             | UTRATIA-ZAFRABAD, NR (LINE DOUBLING)<br>- [N22000088]                                                             | 04/2006          | 369.90<br>-                       | 1,581.53                    | 03/2010<br>-          | -           | 327.56           |
| 159                             | CHANDIGARH-BADDI<br>- [N22000467]                                                                                 | 04/2007          | 328.14<br>-                       | 1,540.00                    | 03/2023<br>-          | 03/2023     | 369.31           |
| 160                             | JALANDHAR-PATHANKOT-JAMMU TAWI<br>- [N22000492]                                                                   | 03/2002          | 625.00<br>-                       | 845.58                      | 03/2016<br>-          | -           | 35.29            |
|                                 | <u>Rail Vikas Nigam Ltd.</u>                                                                                      |                  |                                   |                             |                       |             |                  |
| 161                             | HARIDASPUR-PARADEEP(NL)<br>- [220100285]                                                                          | 04/1996          | 1,185.64<br>-                     | 1,844.47                    | 12/2017<br>-          | 03/2020     | 55.57            |
| 162                             | SUKINDA ROAD - ANGUL (NL)(ECOR)<br>- [220100325]                                                                  | 04/1998          | 1,202.70<br>-                     | 1,202.70                    | 02/2015<br>-          | 12/2021     | .00              |
| 163                             | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)<br>- [220100327]                                                        | 04/2000          | 133.41<br>207.00                  | 385.00                      | 03/2009<br>03/2009    | 02/2019     | 85.99            |
| 164                             | OBULAVARIPALLE-KRISHNAPATNAM(RVNL)<br>- [N22000049]                                                               | 07/2006          | 732.81<br>-                       | 1,850.00                    | 03/2008<br>-          | 03/2020     | 152.45           |
| 165                             | BHANUPALI-BILASPUR BERI NL<br>- [N22000273]                                                                       | 04/2008          | 2,966.99<br>-                     | 7,000.00                    | 12/2026<br>-          | 12/2026     | 135.93           |
| 166                             | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL<br>- [220100149]                                 | 04/1995          | 631.78<br>-                       | 1,195.00                    | 12/2012<br>-          | 03/2022     | 89.15            |
| 167                             | SALKA ROAD -ANUPNAGAR LINE DOUBLING<br>- [N22000075]                                                              | 09/2006          | 383.54<br>-                       | 555.00                      | 03/2010<br>-          | 12/2019     | 44.70            |
| 168                             | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)<br>- [N22000110]     | 04/2010          | 3,951.98<br>-                     | 4,259.48                    | 03/2016<br>-          | 03/2025     | 7.78             |
| 169                             | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)<br>- [N22000109] | 04/2010          | 2,298.42<br>-                     | 2,733.86                    | 03/2014<br>-          | 12/2025     | 18.95            |
| 170                             | MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD<br>- [N22000213]                                            | 04/2012          | 632.68<br>-                       | 816.55                      | 03/2016<br>-          | 12/2020     | 29.06            |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs. 150 Crore and above |                                                                                                      |                  |                                   |                             | (December 2018)       |             |                  |
|---------------------------------|------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                 |                                                                                                      |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                            | Project                                                                                              | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                               | 2                                                                                                    | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 171                             | VIJAYAWADA-GUDUR<br>- [N22000369]                                                                    | 04/2015          | 3,246.26<br>-                     | 3,548.67                    | 12/2023<br>-          | 12/2023     | 9.32             |
| 172                             | LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC<br>- [N22000404]                                         | 04/2011          | 927.01<br>-                       | 977.00                      | 03/2019<br>-          | 03/2020     | 5.39             |
| 173                             | DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)<br>- [N22000407] | 03/2009          | 713.48<br>-                       | 1,750.00                    | 03/2020<br>-          | 03/2020     | 145.28           |
| 174                             | SAMBALPUR - TITLAGARH - DOUBLING<br>- [N22000410]                                                    | 03/2006          | 948.04<br>-                       | 970.00                      | 03/2020<br>-          | 03/2020     | 2.32             |
|                                 | <u>Railway Electrification</u>                                                                       |                  |                                   |                             |                       |             |                  |
| 175                             | ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT<br>- [N22000094]                        | 02/2008          | 171.10<br>-                       | 275.08                      | 03/2012<br>-          | -           | 60.77            |
|                                 | <u>South Central Railway</u>                                                                         |                  |                                   |                             |                       |             |                  |
| 176                             | KOTLPALLI-NARASAPUR (NL) (SCR)<br>- [220100265]                                                      | 12/2001          | 1,045.20<br>-                     | 2,120.16                    | 03/2009<br>-          | 03/2023     | 102.85           |
| 177                             | MANUGURU-RAMAGUNDAM<br>- [N22000259]                                                                 | 04/2013          | 1,112.00<br>-                     | 2,911.84                    | -<br>-                | -           | 161.86           |
| 178                             | KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION<br>- [N22000261]                                    | 04/2012          | 1,856.95<br>-                     | 2,200.00                    | 03/2023<br>-          | 03/2024     | 18.47            |
| 179                             | BHADRACHALAM-KOVVUR<br>- [N22000264]                                                                 | 04/2012          | 923.23<br>-                       | 1,787.00                    | -<br>-                | -           | 93.56            |
| 180                             | CUMBUM-PRODDATUR<br>- [N22000282]                                                                    | 04/2013          | 829.00<br>-                       | 1,599.39                    | -<br>-                | -           | 92.93            |
| 181                             | NANDYAL-YERRAGUNTALA(NL),SCR<br>- [220100192]                                                        | 03/1996          | 164.36<br>-                       | 1,050.00                    | 02/2009<br>-          | -           | 538.84           |
| 182                             | MUNEERABAD-MAHABOBNAGAR(NL),SCR<br>- [220100205]                                                     | 04/1997          | 1,723.00<br>1.00                  | 645.00                      | 03/2000<br>-          | 03/2019     | 64,400.00        |
| 183                             | MACHERLA-NALGONDA(NL)(SCR)<br>- [220100220]                                                          | 07/1998          | 458.25<br>-                       | 458.26                      | -<br>-                | -           | .00              |
| 184                             | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)<br>- [220100106]                                              | 12/1994          | 124.43<br>-                       | 1,025.00                    | -<br>-                | -           | 723.76           |
|                                 | <u>South East Central Railway</u>                                                                    |                  |                                   |                             |                       |             |                  |
| 185                             | CHHINDWARA - NAGPUR (GC)(SECR)<br>- [220100324]                                                      | 04/2005          | 383.79<br>-                       | 1,101.16                    | -<br>-                | -           | 186.92           |
| 186                             | GONDIA-JABALPUR(GC),(SECR)<br>- [220100186]                                                          | 02/1997          | 511.86<br>-                       | 1,756.00                    | 04/2020<br>-          | 04/2020     | 243.06           |
| 187                             | RAJNANDGAON - NAGPUR - 3RD LINE (SECR)<br>- [N22000420]                                              | 09/2016          | 1,908.51<br>-                     | 2,686.63                    | 03/2023<br>-          | 03/2023     | 40.77            |
| 188                             | CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT<br>- [N22000438]                             | 04/2010          | 585.93<br>-                       | 1,420.39                    | 02/2019<br>-          | 02/2019     | 142.42           |
| 189                             | WADSA-GADHCHIROLI NEW LINE (52.36 KM)<br>- [N22000480]                                               | 06/2018          | 229.00<br>-                       | 403.00                      | 12/2021<br>-          | 12/2021     | 75.98            |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs. 150 Crore and above |                                                                                                                    |                  |                                   |                             | (December 2018)       |             |                  |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                 |                                                                                                                    |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                            | Project                                                                                                            | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                               | 2                                                                                                                  | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 190                             | CHHINDWARA-MANDLA FORT GC<br>- [N22000481]                                                                         | 03/2011          | 556.54<br>-                       | 1,342.46                    | 03/2012<br>-          | 03/2020     | 141.22           |
| 191                             | CHAMPA-JHARSUGUDA 3RD LINE<br>- [N22000483]                                                                        | 04/2008          | 872.00<br>-                       | 1,279.00                    | 12/2019<br>-          | 12/2019     | 46.67            |
| 192                             | GEVRA ROAD PENDRA ROAD<br>- [N22000488]                                                                            | 02/2014          | 2,288.00<br>-                     | 4,919.00                    | 03/2022<br>-          | 03/2022     | 114.99           |
|                                 | <u>South Eastern Railway</u>                                                                                       |                  |                                   |                             |                       |             |                  |
| 193                             | MM FROM BURAMARA-CHAKULIA<br>- [N22000305]                                                                         | 04/2008          | 466.48<br>-                       | 1,000.00                    | -<br>-                | 12/2024     | 114.37           |
| 194                             | MM FROM PANSKURA-GHATAL NL<br>- [N22000309]                                                                        | 04/2011          | 276.69<br>-                       | 426.00                      | -<br>-                | 03/2030     | 53.96            |
| 195                             | HOWRAH-AMTA-CHAMPADANGA NL (SER)<br>- [220100208]                                                                  | 04/1974          | 393.46<br>154.30                  | 1,026.00                    | 03/2007<br>03/2007    | -           | 564.94           |
| 196                             | TAMLUK DIGHA, LINE DOUBLING (SER)<br>- [N22000097]                                                                 | 03/1984          | 293.97<br>-                       | 749.69                      | 06/2005<br>-          | -           | 155.02           |
| 197                             | RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM)<br>JHARKHAND - [N22000323]                                             | 04/2012          | 148.77<br>-                       | 377.00                      | 12/2016<br>-          | 09/2019     | 153.41           |
| 198                             | BOWAICHANDI-ARAMBAGH<br>- [N22000159]                                                                              | 04/2010          | 267.37<br>-                       | 620.00                      | -<br>-                | 03/2025     | 131.89           |
| 199                             | DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA<br>- [N22000160]                                                        | 04/2010          | 651.00<br>-                       | 1,009.00                    | 03/2015<br>-          | 03/2024     | 54.99            |
| 200                             | BHADUTOLA-JHARGRAM VIA LALGARH (NL)<br>- [N22000161]                                                               | 04/2011          | 289.64<br>-                       | 760.00                      | -<br>-                | -           | 162.39           |
| 201                             | CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION<br>- [N22000162]                                                         | 04/2010          | 149.90<br>-                       | 230.00                      | 03/2015<br>-          | -           | 53.44            |
| 202                             | DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING<br>- [N22000164]                                                          | 04/2010          | 309.44<br>-                       | 525.81                      | 12/2015<br>-          | 02/2019     | 69.92            |
| 203                             | MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING<br>- [N22000165]                                                           | 04/2012          | 258.20<br>-                       | 365.00                      | -<br>-                | 01/2020     | 41.36            |
| 204                             | ARA-BHABHUA ROAD (NL)<br>- [N22000166]                                                                             | 04/2008          | 633.87<br>-                       | 2,396.88                    | -<br>-                | -           | 278.13           |
| 205                             | ROURKELA JHARSUGUDA THIRD LINE 101 KM<br>- [N22000395]                                                             | 11/2015          | 969.83<br>-                       | 1,151.81                    | 03/2020<br>-          | 06/2020     | 18.76            |
| 206                             | TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN<br>NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM<br>NADAKUMAR BOLAI - [N22000397] | 01/1991          | 1,013.45<br>-                     | 1,428.00                    | 12/2021<br>-          | 12/2021     | 40.90            |
| 207                             | RUPSA BANGRIPOSI 90 KM WITH MM FOR<br>UPGRADATION FROM RUPSA BURAMARA AND<br>EXTENSION OF LINE FRO - [N22000398]   | 04/1995          | 524.43<br>-                       | 939.00                      | 12/2021<br>-          | 12/2024     | 79.05            |
| 208                             | BANKURA DAMODAR VALLEY RLY LINE 96 KM GC<br>WITH 6MMS FOR NL - [N22000402]                                         | 04/1998          | 1,027.40<br>-                     | 2,373.00                    | 03/2003<br>-          | 03/2030     | 130.97           |
|                                 | <u>South Western Railway</u>                                                                                       |                  |                                   |                             |                       |             |                  |
| 209                             | SRINIVASA-PURA-MADANAPALLI NL<br>- [N22000277]                                                                     | 04/2013          | 296.00<br>-                       | 466.65                      | -<br>-                | 12/2023     | 57.65            |
|                                 | <u>Southern Railway</u>                                                                                            |                  |                                   |                             |                       |             |                  |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs. 150 Crore and above |                                                                                              |                  |                                   |                             | (December 2018)       |             |                  |
|---------------------------------|----------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                 |                                                                                              |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                            | Project                                                                                      | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                               | 2                                                                                            | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 210                             | CALICUT-MANGALORE (DL) (SR)<br>- [220100151                                                  | 02/1996          | 240.00<br>-                       | 579.37                      | -<br>-                | -           | 141.40           |
| 211                             | KARUR-SALEM(NL),SR<br>- [220100191                                                           | 02/1997          | 155.55<br>-                       | 920.00                      | -<br>-                | -           | 491.45           |
| 212                             | QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)<br>[220100263                                | 03/1998          | 280.00<br>-                       | 1,122.00                    | -<br>-                | -           | 300.71           |
| 213                             | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU PONDY-AGASTIYAMPALLI<br>[N22000079                  | 09/2007          | 724.69<br>-                       | 2,072.50                    | 02/2019<br>-          | 02/2019     | 185.98           |
| 214                             | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE<br>- [N22000080                            | 09/2006          | 343.17<br>-                       | 1,065.00                    | -<br>-                | -           | 210.34           |
| 215                             | TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)<br>- [N22000084                                        | 09/2006          | 227.40<br>-                       | 900.00                      | -<br>-                | -           | 295.78           |
| 216                             | TIDIVANAM-NAGARI (NL)<br>- [N22000085                                                        | 09/2006          | 582.83<br>-                       | 2,300.00                    | -<br>-                | -           | 294.63           |
| 217                             | ANGAMALI-SABARIMALA (N.L.)(SR)<br>- [220100252                                               | 10/1998          | 1,566.00<br>-                     | 2,815.62                    | -<br>-                | -           | 79.80            |
| 218                             | ATTIPPATTU PUTTUR<br>- [N22000184                                                            | 04/2008          | 151.84<br>-                       | 1,105.00                    | 02/2019<br>-          | 02/2019     | 627.74           |
| 219                             | CHENNAI-CUDDALORE VIA MAMALLAPURAM<br>- [N22000185                                           | 04/2008          | 523.52<br>-                       | 2,350.00                    | -<br>-                | -           | 348.88           |
| 220                             | SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR<br>- [N22000186 | 04/2013          | 839.00<br>-                       | 1,500.00                    | -<br>-                | -           | 78.78            |
| 221                             | CUDDALORE-SALEM VIA VRIDDHACHALAM GC<br>- [N22000187                                         | 04/1999          | 198.68<br>-                       | 556.64                      | -<br>-                | -           | 180.17           |
| 222                             | CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC<br>[N22000188                                | 04/1998          | 271.24<br>-                       | 520.00                      | -<br>-                | -           | 91.71            |
| 223                             | KURUPPANTHARA-CHINGAVANAM<br>- [N22000190                                                    | 04/2007          | 270.14<br>-                       | 457.08                      | -<br>-                | -           | 69.20            |
| 224                             | ERODE-PALANI<br>- [N22000199                                                                 | 04/2008          | 288.57<br>-                       | 1,140.00                    | -<br>-                | -           | 295.05           |
| 225                             | MADURAI-BODINAYAKKANUR<br>- [N22000201                                                       | 04/2008          | 164.41<br>-                       | 450.00                      | -<br>-                | 03/2020     | 173.71           |
| 226                             | CHENGANNUR-CHINGAVANAM<br>- [N22000203                                                       | 04/2006          | 191.72<br>-                       | 369.83                      | -<br>-                | -           | 92.90            |
| 227                             | MADURAI-TUTICORIN VIA ARUPPUKOTTAI<br>- [N22000215                                           | 04/2011          | 120.70<br>-                       | 1,800.00                    | 03/2019<br>-          | 03/2019     | 1,391.30         |
| 228                             | OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM<br>[N22000373                          | 10/2013          | 187.26<br>-                       | 231.67                      | 04/2014<br>-          | 03/2020     | 23.72            |
| 229                             | THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)<br>- [N22000441                | 02/1996          | 268.87<br>-                       | 302.02                      | 03/2005<br>-          | -           | 12.33            |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs. 150 Crore and above |                                                                                                                   |                  |                                   |                             | (December 2018)       |             |                  |
|---------------------------------|-------------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                 |                                                                                                                   |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                            | Project                                                                                                           | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                               | 2                                                                                                                 | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 230                             | VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446                                                       | 02/2005          | 600.00<br>600.00                  | 645.54                      | 03/2010<br>-          | -           | 7.59             |
| 231                             | MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANAL ROAD) (62.05 KM) DOUBLING - [N22000450                             | 02/2003          | 199.55<br>-                       | 330.32                      | 03/2009<br>-          | -           | 65.53            |
| 232                             | MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451                                                    | 02/2015          | 760.00<br>-                       | 1,182.31                    | 03/2020<br>-          | 03/2020     | 55.57            |
|                                 | <u>West Central Railway</u>                                                                                       |                  |                                   |                             |                       |             |                  |
| 233                             | RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314                                                                         | 04/2001          | 424.60<br>-                       | 2,713.09                    | 03/2021<br>-          | 03/2021     | 538.98           |
| 234                             | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232                                                               | 09/1998          | 247.66<br>-                       | 6,093.31                    | 05/2008<br>-          | 03/2023     | 2,360.35         |
| 235                             | KATNI GRADE SEPARATOR/BYE PASS - [N22000416                                                                       | 08/2016          | 582.13<br>-                       | 1,260.61                    | 03/2022<br>-          | 03/2022     | 116.55           |
|                                 | <u>Western Railway</u>                                                                                            |                  |                                   |                             |                       |             |                  |
| 236                             | BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125                                   | 04/2006          | 117.36<br>196.95                  | 203.00                      | 03/2011<br>-          | -           | 3.07             |
| 237                             | BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123                                             | 04/2008          | 318.24<br>-                       | 321.62                      | 03/2012<br>-          | 03/2019     | 1.06             |
|                                 | Total                                                                                                             |                  | 1,34,498.31<br>-                  | 2,97,140.92                 |                       |             |                  |
|                                 |                                                                                                                   |                  |                                   |                             |                       |             |                  |
|                                 | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                |                  |                                   |                             |                       |             |                  |
|                                 | <u>Dept Of Road Transport &amp; Highways</u>                                                                      |                  |                                   |                             |                       |             |                  |
| 238                             | REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262 | 12/2014          | 201.12<br>201.00                  | 201.12                      | 02/2015<br>-          | -           | .06              |
|                                 | <u>Ministry Of Road Transport And Highways</u>                                                                    |                  |                                   |                             |                       |             |                  |
| 239                             | CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316 | 03/2015          | 258.97<br>-                       | 268.92                      | 08/2015<br>-          | -           | 3.84             |
| 240                             | RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777 | 11/2017          | 283.51<br>-                       | 284.00                      | 11/2019<br>-          | 11/2019     | .17              |
| 241                             | REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782 | 03/2018          | 460.73<br>-                       | 461.00                      | -<br>-                | -           | .06              |
| 242                             | Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820 | 11/2017          | 237.80<br>-                       | 238.00                      | 11/2019<br>-          | 11/2019     | .08              |
|                                 | <u>National Highways And Infrastructure Development Corporation Ltd.</u>                                          |                  |                                   |                             |                       |             |                  |
| 243                             | RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695                                                                  | 04/2017          | 388.00<br>-                       | 447.37                      | 10/2017<br>-          | -           | 15.30            |
|                                 | <u>National Highways Authority Of India</u>                                                                       |                  |                                   |                             |                       |             |                  |



## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs. 150 Crore and above |                                                                                                                    |                  |                                   |                             | (December 2018)       |             |                  |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                 |                                                                                                                    |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                            | Project                                                                                                            | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                               | 2                                                                                                                  | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 244                             | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700<br>- [240106277]                                            | 12/2003          | 280.00<br>-                       | 361.00                      | 02/2009<br>-          | 12/2018     | 28.93            |
| 245                             | MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000<br>- [240106278]                                               | 12/2003          | 199.81<br>-                       | 385.13                      | 04/2009<br>-          | 03/2019     | 92.75            |
| 246                             | MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450<br>- [240106280]                                              | 12/2003          | 155.04<br>-                       | 280.13                      | 11/2008<br>-          | -           | 80.68            |
| 247                             | DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)<br>- [N24000049]                                                          | 12/2003          | 160.00<br>-                       | 167.98                      | 05/2008<br>-          | 02/2019     | 4.99             |
| 248                             | HARANGAJO TO MAIBANG, NH-54<br>- [N24000062]                                                                       | 12/2003          | 196.00<br>-                       | 331.23                      | 07/2009<br>-          | -           | 68.99            |
| 249                             | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)<br>- [N24000133]                                                       | 05/2009          | 1,108.00<br>-                     | 2,288.00                    | 11/2011<br>-          | 06/2019     | 106.50           |
| 250                             | BRAHMPUTRA BRIDGE, NH NO-31<br>- [N24000063]                                                                       | 12/2003          | 217.61<br>-                       | 360.84                      | 04/2010<br>-          | 04/2019     | 65.82            |
| 251                             | NALBARI T BIJNI (AS-7)<br>- [N24000048]                                                                            | 12/2003          | 208.00<br>-                       | 230.00                      | 04/2008<br>-          | 03/2019     | 10.58            |
| 252                             | 4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9<br>- [N24000233]                                             | 04/2014          | 1,266.60<br>-                     | 1,544.00                    | 09/2016<br>-          | 06/2019     | 21.90            |
| 253                             | GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION<br>- [N24000125]                                               | 03/2010          | 1,509.10<br>-                     | 3,237.87                    | 09/2012<br>-          | 08/2018     | 114.56           |
| 254                             | INDORE-JHABUA-GUJRAT/MP<br>- [N24000136]                                                                           | 10/2010          | 1,175.00<br>-                     | 1,206.10                    | 04/2013<br>-          | 11/2018     | 2.65             |
| 255                             | DELHI AGRA APPROVED LENGTH 180.0 KM<br>- [N24000224]                                                               | 10/2012          | 1,928.22<br>-                     | 2,945.00                    | 04/2015<br>-          | -           | 52.73            |
| 256                             | FOUR LANNING OF GWALIOR-SHIVPURI<br>- [N24000494]                                                                  | 05/2013          | 1,055.00<br>-                     | 1,601.77                    | 11/2015<br>-          | 12/2018     | 51.83            |
| 257                             | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-I)_NEW<br>- [N24000609]                                | 09/2015          | 771.18<br>-                       | 7,558.00                    | -<br>-                | -           | 880.06           |
| 258                             | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654] | 03/2017          | 1,184.71<br>-                     | 1,310.00                    | 03/2020<br>-          | 08/2020     | 10.58            |
| 259                             | 4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)<br>- [N24000656]                                          | 03/2017          | 744.64<br>-                       | 982.00                      | 03/2020<br>-          | 03/2020     | 31.88            |
| 260                             | 4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)<br>- [N24000657]                                      | 03/2017          | 1,030.44<br>-                     | 1,065.51                    | 03/2020<br>-          | 05/2020     | 3.40             |
| 261                             | 4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)<br>- [N24000658]                                       | 03/2017          | 988.34<br>-                       | 1,043.28                    | 03/2020<br>-          | 08/2020     | 5.56             |
| 262                             | 4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)<br>- [N24000659]                                     | 03/2017          | 1,059.73<br>-                     | 1,071.00                    | 03/2017<br>-          | 11/2020     | 1.06             |
| 263                             | 4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)<br>- [N24000661]                                     | 03/2017          | 1,098.06<br>-                     | 1,160.64                    | 03/2020<br>-          | 08/2020     | 5.70             |
| 264                             | CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662] | 03/2017          | 754.54<br>-                       | 756.27                      | 03/2020<br>-          | 04/2020     | .23              |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs. 150 Crore and above |                                                                                                                   |                  |                                   |                             | (December 2018)       |             |                  |
|---------------------------------|-------------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                 |                                                                                                                   |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                            | Project                                                                                                           | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                               | 2                                                                                                                 | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 265                             | TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665  | 03/2017          | 672.89<br>-                       | 736.01                      | 03/2020<br>-          | 03/2020     | 9.38             |
| 266                             | SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668                 | 03/2017          | 1,041.62<br>-                     | 1,187.10                    | 03/2020<br>-          | 05/2020     | 13.97            |
| 267                             | 4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669                                     | 03/2017          | 165.50<br>-                       | 172.16                      | 03/2020<br>-          | 06/2019     | 4.02             |
| 268                             | REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671  | 03/2017          | 1,288.07<br>-                     | 1,420.00                    | 03/2020<br>-          | 03/2020     | 10.24            |
| 269                             | 6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672 | 03/2017          | 2,064.99<br>-                     | 2,447.00                    | 03/2020<br>-          | 03/2020     | 18.50            |
| 270                             | SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674   | 03/2017          | 831.58<br>-                       | 1,177.00                    | 03/2020<br>-          | 06/2020     | 41.54            |
| 271                             | SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675 | 03/2017          | 993.16<br>-                       | 1,434.00                    | 03/2020<br>-          | 06/2020     | 44.39            |
|                                 | <u>Public Works Dept Of State</u>                                                                                 |                  |                                   |                             |                       |             |                  |
| 272                             | REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247  | 10/2014          | 295.47<br>-                       | 313.27                      | 02/2017<br>-          | -           | 6.02             |
| 273                             | CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWES - [N24000249  | 03/2011          | 218.31<br>-                       | 339.82                      | 12/2015<br>-          | -           | 55.66            |
| 274                             | CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260 | 01/2014          | 255.75<br>348.00                  | 348.43                      | 09/2017<br>-          | -           | .12              |
| 275                             | CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261 | 01/2014          | 267.16<br>352.00                  | 352.05                      | 11/2017<br>-          | -           | .01              |
| 276                             | TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420 | 12/2009          | 104.00<br>-                       | 201.00                      | 09/2010<br>-          | -           | 93.27            |
|                                 | Total                                                                                                             |                  | 27,118.65<br>-                    | 41,914.00                   |                       |             |                  |
|                                 |                                                                                                                   |                  |                                   |                             |                       |             |                  |
|                                 | <u>SHIPPING AND PORTS</u>                                                                                         |                  |                                   |                             |                       |             |                  |
|                                 | <u>Kamarajar Port Limited</u>                                                                                     |                  |                                   |                             |                       |             |                  |
| 277                             | CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066                                               | 02/2015          | 244.50<br>258.00                  | 271.56                      | 12/2017<br>-          | -           | 5.26             |
|                                 | Total                                                                                                             |                  | 244.50<br>-                       | 271.56                      |                       |             |                  |
|                                 |                                                                                                                   |                  |                                   |                             |                       |             |                  |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs. 150 Crore and above |                                                                                                                    |                  |                                   |                             | (December 2018)       |             |                  |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                 |                                                                                                                    |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                            | Project                                                                                                            | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                               | 2                                                                                                                  | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
|                                 | <u>STEEL</u>                                                                                                       |                  |                                   |                             |                       |             |                  |
|                                 | <u>Rastrya Ispat Nigam Limited</u>                                                                                 |                  |                                   |                             |                       |             |                  |
| 278                             | REVAMPING OF SINTER MACHINES - 1 AND 2<br>- [N12000091                                                             | 12/2009          | 343.00<br>-                       | 488.40                      | 10/2016<br>-          | -           | 42.39            |
|                                 | Total                                                                                                              |                  | 343.00<br>-                       | 488.40                      |                       |             |                  |
|                                 | <u>TELECOMMUNICATIONS</u>                                                                                          |                  |                                   |                             |                       |             |                  |
|                                 | <u>Department Of Telecommunication</u>                                                                             |                  |                                   |                             |                       |             |                  |
| 279                             | NETWORK FOR SPECTRUM<br>- [N26000101                                                                               | 03/2012          | 13,334.00<br>-                    | 24,664.00                   | 07/2015<br>-          | 05/2020     | 84.97            |
|                                 | Total                                                                                                              |                  | 13,334.00<br>-                    | 24,664.00                   |                       |             |                  |
|                                 | <u>URBAN DEVELOPMENT</u>                                                                                           |                  |                                   |                             |                       |             |                  |
|                                 | <u>Central Public Works Department</u>                                                                             |                  |                                   |                             |                       |             |                  |
| 280                             | STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM<br>- [N28000060                                                      | 04/2014          | 332.72<br>-                       | 342.00                      | 09/2016<br>-          | -           | 2.79             |
| 281                             | ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE<br>INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW<br>DELHI - [N28000071 | 10/2013          | 1,219.21<br>-                     | 1,592.00                    | 10/2019<br>-          | 03/2020     | 30.58            |
| 282                             | CONSTRUCTION OF ACADEMIC AND RESIDENTIAL<br>COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT<br>PATNA - [N28000100     | 02/2016          | 496.18<br>496.00                  | 498.99                      | 06/2017<br>-          | 06/2020     | .60              |
|                                 | <u>Chennai Metro Rail Ltd</u>                                                                                      |                  |                                   |                             |                       |             |                  |
| 283                             | CHENNAI METRO RAIL LTD (PHASE 1)<br>- [N28000084                                                                   | 02/2009          | 14,600.00<br>-                    | 19,058.00                   | 12/2015<br>-          | -           | 30.53            |
|                                 | <u>Hindustan Steelwork Construction Limited</u>                                                                    |                  |                                   |                             |                       |             |                  |
| 284                             | CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL<br>AT GULBARGA - [N12000101                                           | 05/2005          | 768.88<br>1,070.97                | 1,113.34                    | 02/2014<br>-          | -           | 3.96             |
| 285                             | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD<br>UNDER PMGSY PHASE V - [N12000098                                     | 03/2007          | 149.73<br>173.00                  | 175.94                      | 12/2015<br>-          | -           | 1.70             |
|                                 | <u>National Building Construcion Corporation Ltd</u>                                                               |                  |                                   |                             |                       |             |                  |
| 286                             | REDEVELOPMENT OF EAST KIDWAI NAGAR<br>- [N28000080                                                                 | 06/2012          | 4,264.00<br>-                     | 4,439.23                    | 11/2019<br>-          | 11/2019     | 4.11             |
|                                 | Total                                                                                                              |                  | 21,830.72<br>-                    | 27,219.50                   |                       |             |                  |
|                                 | <b>Grand Total</b>                                                                                                 |                  | <b>3,63,650.69</b>                | <b>6,09,129.50</b>          |                       |             |                  |

## List of Delayed Projects w.r.t. Latest Schedule

### Annexure- XIV

| Costing Rs. 150 Crore and above |                                                                                                            |                  |                                    |                              |                                         | (December 2018)       |             |                                   |                                  |
|---------------------------------|------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|                                 |                                                                                                            |                  |                                    |                              |                                         | Date of Commissioning |             |                                   |                                  |
| S.No                            | Project                                                                                                    | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
| 1                               | 2                                                                                                          | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
|                                 | <u>ATOMIC ENERGY</u>                                                                                       |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|                                 | <u>Bhavini Limited</u>                                                                                     |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 1                               | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU                          | 09/2003          | 3,492.00                           | 6,100.00                     | 5,687.52                                | 09/2010               | 03/2019     | 102                               | -                                |
|                                 | <u>Nuclear Power Corporation Of India Limited</u>                                                          |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 2                               | KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT                                        | 10/2009          | 11,459.00                          | 16,580.00                    | 12,848.00                               | 12/2015               | 06/2020     | 54                                | 43                               |
| 3                               | RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN                          | 10/2009          | 12,320.00                          | 12,320.00                    | 10,138.00                               | 12/2016               | 12/2020     | 48                                | 45                               |
| 4                               | KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL, TAMIL NADU                               | 03/2013          | 39,849.00                          | 39,849.00                    | 11,815.00                               | 11/2020               | 11/2023     | 36                                | -                                |
|                                 | Total                                                                                                      |                  | 67,120.00                          | 74,849.00                    | 40,488.52                               |                       |             |                                   |                                  |
|                                 | <u>CIVIL AVIATION</u>                                                                                      |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|                                 | <u>Airport Authority Of India Limited</u>                                                                  |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 5                               | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, A & N ISLANDS | 10/2013          | 314.61                             | 441.33                       | 85.79                                   | 09/2018               | 06/2020     | 21                                | -                                |
|                                 | Total                                                                                                      |                  | 314.61                             | 441.33                       | 85.79                                   |                       |             |                                   |                                  |
|                                 | <u>COAL</u>                                                                                                |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|                                 | <u>Bharat Coking Coal Limited</u>                                                                          |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 6                               | MOONIDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND                                                           | 08/2011          | 1,230.27                           | 1,230.27                     | 326.22                                  | 04/2015               | 04/2019     | 48                                | -                                |
|                                 | <u>Central Coal Fields Limited</u>                                                                         |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 7                               | NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND                                                    | 12/2007          | 179.87                             | 179.87                       | 174.69                                  | 03/2012               | 03/2019     | 84                                | -                                |
| 8                               | TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND                                                            | 08/2008          | 264.68                             | 264.68                       | 178.37                                  | 03/2012               | 03/2019     | 84                                | -                                |
| 9                               | RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL, JHARKHAND                                                     | 12/2009          | 510.85                             | 510.85                       | 340.29                                  | 03/2016               | 03/2019     | 36                                | -                                |
| 10                              | KARMA OCP (1.0 MTY) - [N06000088]CCL, JHARKHAND                                                            | 06/2009          | 162.46                             | 162.46                       | 89.21                                   | 03/2014               | 03/2019     | 60                                | -                                |
| 11                              | CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND                                                      | 08/2007          | 163.51                             | 163.51                       | 103.41                                  | 03/2011               | 03/2020     | 108                               | -                                |
| 12                              | MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND                                                         | 08/2008          | 706.40                             | 706.40                       | 185.62                                  | 07/2012               | 03/2021     | 104                               | -                                |
|                                 | <u>Eastern Coal Fields Limited</u>                                                                         |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 13                              | SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL                                          | 08/2012          | 1,055.05                           | 1,055.05                     | 383.30                                  | 03/2018               | 03/2020     | 24                                | -                                |
|                                 | <u>Mahanadi Coal Fields Limited</u>                                                                        |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 14                              | BHUBANESHWARI OCP, MCL (20.0 MTY) - [N06000034]MCL, ODISHA                                                 | 12/2007          | 490.10                             | 490.10                       | 413.37                                  | 03/2017               | 03/2020     | 36                                | -                                |

# Costing Rs. 150 Crore and above

(December 2018)

| S.No | Project                                                                                            | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Date of Commissioning |             | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
|------|----------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|      |                                                                                                    |                  |                                    |                              |                                         | Original / Revised    | Anticipated |                                   |                                  |
| 1    | 2                                                                                                  | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 15   | KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA                                               | 12/2007          | 457.77 -                           | 457.77                       | 584.85                                  | 03/2013 -             | 03/2020     | 84                                | -                                |
| 16   | BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA                                        | 12/2007          | 172.08 -                           | 172.08                       | 267.19                                  | 03/2010 -             | 03/2020     | 120                               | -                                |
| 17   | HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA                                        | 11/2008          | 479.53 -                           | 479.53                       | 336.08                                  | 03/2013 -             | 03/2020     | 84                                | -                                |
| 18   | KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL, ODISHA                                                 | 06/2014          | 289.03 -                           | 289.03                       | 28.56                                   | 03/2018 -             | 03/2020     | 24                                | -                                |
| 19   | ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA                                     | 08/2008          | 207.28 -                           | 207.28                       | 235.50                                  | 03/2012 -             | 03/2021     | 108                               | -                                |
| 20   | JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL, ODISHA                                   | 05/2014          | 337.66 -                           | 337.66                       | 65.58                                   | 03/2019 -             | 03/2021     | 24                                | -                                |
| 21   | BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL, ODISHA                                       | 05/2014          | 479.15 -                           | 479.15                       | 120.51                                  | 03/2019 -             | 03/2024     | 60                                | -                                |
|      | <u>Neyveli Lignite Corporation</u>                                                                 |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 22   | NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC, TAMIL NADU                           | 06/2011          | 5,907.11 -                         | 5,907.11                     | 5,828.01                                | 12/2015<br>12/2018    | 03/2019     | 39                                | 3                                |
|      | <u>Northern Coal Fields Limited</u>                                                                |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 23   | KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA, 6MTPA INCREMENTAL) - [N06000091]NCL, UTTAR PRADESH | 06/2011          | 1,131.28 -                         | 1,131.28                     | 711.45                                  | 03/2018 -             | 03/2019     | 12                                | -                                |
|      | <u>Singareni Colliers Company Limited</u>                                                          |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 24   | RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA                                                       | 03/2010          | 209.78 -                           | 209.78                       | 154.21                                  | 03/2015 -             | 03/2019     | 48                                | -                                |
| 25   | RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL, TELANGANA                              | 06/2012          | 365.01 -                           | 365.01                       | 204.26                                  | 06/2015 -             | 03/2019     | 45                                | -                                |
| 26   | RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA                                            | 11/2012          | 430.45 -                           | 415.37                       | 160.45                                  | 03/2016 -             | 03/2019     | 36                                | -                                |
| 27   | KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL, TELANGANA                                            | 10/2015          | 426.79 -                           | 426.79                       | -                                       | 03/2018 -             | 03/2019     | 12                                | -                                |
| 28   | KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA                                         | 07/2012          | 417.33 -                           | 384.32                       | 146.45                                  | 07/2016 -             | 03/2020     | 44                                | -                                |
| 29   | KISTARAM OCP - [N06000089]SCCL, TELANGANA                                                          | 11/2010          | 242.29 -                           | 164.04                       | 12.69                                   | 03/2015 -             | 03/2021     | 72                                | -                                |
| 30   | RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA                                         | 07/2011          | 162.76 -                           | 349.28                       | 1.31                                    | 03/2015 -             | 03/2021     | 72                                | -                                |
| 31   | JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA                                            | 07/2011          | 447.06 -                           | 437.51                       | 353.61                                  | 03/2015 -             | 03/2021     | 72                                | -                                |
| 32   | RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA                                            | 12/2009          | 418.97 -                           | 489.62                       | 477.74                                  | 03/2012 -             | 03/2023     | 132                               | -                                |
| 33   | SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA                                        | 10/2006          | 249.03 -                           | 448.86                       | 186.91                                  | 03/2012 -             | 03/2024     | 144                               | -                                |
|      | <u>South-Eastern Coal Fields Limited</u>                                                           |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 34   | AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL, CHHATISGARH                              | 11/2009          | 198.59 -                           | 198.59                       | 169.50                                  | 03/2016 -             | 03/2019     | 36                                | -                                |
| 35   | BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH                                     | 04/2012          | 258.56 -                           | 258.56                       | 167.63                                  | 03/2016 -             | 03/2019     | 36                                | -                                |
| 36   | JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL, CHHATISGARH                                           | 09/2008          | 152.43 -                           | 459.49                       | 178.93                                  | 03/2015 -             | 03/2020     | 60                                | -                                |
| 37   | KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH                                       | 07/2008          | 178.44 -                           | 178.44                       | 5.16                                    | 03/2014 -             | 03/2020     | 72                                | -                                |

# Costing Rs. 150 Crore and above

(December 2018)

|      |                                                                                               |                  |                                    |                              |                                         | Date of Commissioning |             |                                   |                                  |
|------|-----------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
| S.No | Project                                                                                       | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
| 1    | 2                                                                                             | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 38   | MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH                                 | 12/2009          | 321.50                             | 321.50                       | 202.68                                  | 03/2014               | 03/2020     | 72                                | -                                |
|      | <u>Western Coal Fields Limited</u>                                                            |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 39   | BHANEGAON OC - [N06000121]WCL,MAHARASHTRA                                                     | 02/2015          | 187.94                             | 409.68                       | 95.83                                   | 03/2023               | 03/2023     | 0                                 | 73                               |
| 40   | KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA                                             | 11/2015          | 277.65                             | 313.34                       | 6.12                                    | 03/2021               | 03/2024     | 36                                | 66                               |
|      | Total                                                                                         |                  | 19,168.66                          | 20,054.26                    | 12,895.69                               |                       |             |                                   |                                  |
|      |                                                                                               |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | <u>STEEL</u>                                                                                  |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | <u>Rastriya Ispat Nigam Limited</u>                                                           |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 41   | ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH                   | 07/2015          | 465.85                             | 465.85                       | 276.25                                  | 07/2018               | 01/2019     | 6                                 | -                                |
| 42   | CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH                                        | 08/2015          | 320.66                             | 320.66                       | 125.36                                  | 08/2018               | 02/2019     | 6                                 | -                                |
| 43   | FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH                                            | 04/2014          | 1,682.85                           | 1,682.85                     | 852.10                                  | 09/2018               | 03/2019     | 6                                 | -                                |
| 44   | COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH                                          | 12/2011          | 2,858.00                           | 2,500.00                     | 1,053.76                                | 12/2017               | 09/2019     | 21                                | -                                |
|      | <u>Steel Authority Of India Limited (SAIL)</u>                                                |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 45   | INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA                            | 04/2015          | 3,127.30                           | 3,127.30                     | 2,527.38                                | 04/2018               | 05/2019     | 13                                | -                                |
| 46   | MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND    | 05/2015          | 1,154.18                           | 1,154.18                     | 862.45                                  | 12/2017               | 06/2019     | 18                                | -                                |
| 47   | NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND                            | 03/2015          | 1,034.01                           | 1,034.01                     | 367.64                                  | 10/2017               | 06/2020     | 32                                | -                                |
| 48   | REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND                       | 11/2016          | 262.87                             | 262.87                       | 77.06                                   | 06/2019               | 06/2020     | 12                                | -                                |
|      | Total                                                                                         |                  | 10,905.72                          | 10,547.72                    | 6,142.00                                |                       |             |                                   |                                  |
|      |                                                                                               |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | <u>PETROLEUM</u>                                                                              |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | <u>Gas Authority Of India Limited</u>                                                         |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 49   | PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE                         | 03/2015          | 3,957.00                           | 3,397.00                     | 2,382.96                                | 12/2018               | 03/2019     | 3                                 | -                                |
| 50   | AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]GAIL,UTTAR PRADESH                              | 07/2015          | 1,427.94                           | 800.00                       | 603.92                                  | 12/2018               | 03/2019     | 3                                 | -                                |
| 51   | CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT                        | 04/2016          | 327.78                             | 200.00                       | 116.19                                  | 04/2018               | 03/2019     | 11                                | -                                |
| 52   | KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE           | 06/2009          | 2,915.00                           | 2,915.00                     | 2,009.30                                | 12/2012               | 06/2019     | 78                                | 4                                |
|      | <u>Indian Oil Corporation Limited</u>                                                         |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 53   | LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA                                                | 10/2015          | 607.06                             | 714.25                       | 352.32                                  | 10/2017               | 03/2019     | 17                                | -                                |
| 54   | DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL | 03/2014          | 3,076.00                           | 4,190.00                     | 3,224.62                                | 09/2017               | 03/2019     | 18                                | 9                                |

# Costing Rs. 150 Crore and above

(December 2018)

| S.No | Project                                                                                                                               | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Date of Commissioning |             | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
|------|---------------------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|      |                                                                                                                                       |                  |                                    |                              |                                         | Original / Revised    | Anticipated |                                   |                                  |
| 1    | 2                                                                                                                                     | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 55   | FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL, BIHAR                                          | 07/2015          | 822.66 -                           | 822.66                       | 868.92                                  | 11/2018 -             | 03/2019     | 4                                 | -                                |
| 56   | PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND - [N16000304]IOCL, MADHYA PRADESH | 08/2017          | 236.00 -                           | 236.00                       | 11.66                                   | 06/2020 -             | 10/2020     | 4                                 | -                                |
| 57   | ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL, TAMIL NADU                      | 05/2016          | 4,497.00 -                         | 4,497.00                     | 349.40                                  | 12/2018 -             | 12/2020     | 24                                | -                                |
| 58   | ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL, MAHARASHTRA      | 05/2016          | 212.00 -                           | 212.00                       | 14.11                                   | 01/2021 -             | 04/2021     | 3                                 | -                                |
| 59   | CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL, ANDHRA PRADESH                            | 08/2018          | 466.00 -                           | 466.00                       | 1.53                                    | 04/2021 -             | 07/2021     | 3                                 | -                                |
| 60   | CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL, TAMIL NADU                                                | 12/2017          | 466.43 -                           | 466.43                       | 1.18                                    | 10/2020 -             | 08/2021     | 10                                | -                                |
| 61   | ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL, MAHARASHTRA    | 05/2016          | 348.00 -                           | 348.00                       | 9.20                                    | 01/2021 -             | 10/2021     | 9                                 | -                                |
| 62   | REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL, UTTAR PRADESH                  | 08/2017          | 318.80 -                           | 318.80                       | 13.93                                   | 08/2021 -             | 11/2021     | 3                                 | -                                |
|      | <u>Oil &amp; Natural Gas Corporation Limited</u>                                                                                      |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 63   | Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC, TAMIL NADU                                             | 11/2015          | 390.52 390.52                      | 390.52                       | 174.22                                  | 03/2019 -             | 04/2019     | 1                                 | -                                |
|      | <u>Oil India Limited</u>                                                                                                              |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 64   | CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL, ASSAM                                                            | 07/2011          | 350.00 -                           | 350.00                       | 2.06                                    | 01/2019 -             | 09/2019     | 8                                 | -                                |
|      | Total                                                                                                                                 |                  | 20,418.19 -                        | 20,323.66                    | 10,135.52                               |                       |             |                                   |                                  |
|      |                                                                                                                                       |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | <u>POWER</u>                                                                                                                          |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | <u>Chenab Valley Power Projects [P] Limited</u>                                                                                       |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 65   | PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL, JAMMU AND KASHMIR                                                     | 10/2014          | 8,112.12 -                         | 8,112.12                     | 982.71                                  | 04/2020 -             | 10/2023     | 42                                | -                                |
|      | <u>National Hydro-Electric Power Corporation</u>                                                                                      |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 66   | PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH                                                                  | 09/2002          | 3,919.59 -                         | 9,394.80                     | 7,145.69                                | 09/2009 -             | 12/2021     | 147                               | -                                |
|      | <u>National Thermal Power Corporation</u>                                                                                             |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 67   | BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM                                                                             | 01/2008          | 4,375.35 8,150.00                  | 8,150.00                     | 7,220.84                                | 09/2011 06/2018       | 01/2019     | 88                                | 7                                |
| 68   | BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR                                                                           | 01/2007          | 5,353.00 -                         | 7,998.00                     | 7,511.72                                | 05/2014 -             | 05/2019     | 60                                | -                                |

# Costing Rs. 150 Crore and above

(December 2018)

| S.No | Project                                                                                                                             | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Date of Commissioning |             | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
|------|-------------------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|      |                                                                                                                                     |                  |                                    |                              |                                         | Original / Revised    | Anticipated |                                   |                                  |
| 1    | 2                                                                                                                                   | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 69   | MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH                                                                      | 04/2012          | 9,750.89 -                         | 9,750.89                     | 8,798.00                                | 12/2016 -             | 08/2019     | 32                                | -                                |
| 70   | NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR                                                                       | 01/2013          | 12,964.60 -                        | 13,731.26                    | 12,593.00                               | 01/2018 -             | 05/2020     | 28                                | -                                |
|      | <u>Power Grid Corporation Of India Limited</u>                                                                                      |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 71   | 400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270]PGCIL,MULTI STATE                                             | 08/2008          | 771.00 1,624.00                    | 1,624.00                     | 1,577.20                                | 02/2013 07/2018       | 12/2018     | 70                                | 5                                |
| 72   | TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN                                              | 07/2015          | 307.18 307.18                      | 307.18                       | 210.91                                  | 11/2017 10/2018       | 01/2019     | 14                                | 3                                |
| 73   | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH                                            | 01/2016          | 305.04 305.04                      | 305.04                       | 229.91                                  | 03/2017 09/2018       | 01/2019     | 22                                | 4                                |
| 74   | WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA                                                                | 12/2007          | 477.69 738.48                      | 738.48                       | 686.26                                  | 09/2010 12/2018       | 02/2019     | 101                               | 2                                |
| 75   | SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE                                                         | 12/2011          | 297.33 534.02                      | 534.02                       | 441.08                                  | 08/2014 09/2018       | 02/2019     | 54                                | 5                                |
| 76   | EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE                                                                | 10/2013          | 1,364.52 1,891.41                  | 1,891.41                     | 1,216.98                                | 04/2016 12/2018       | 02/2019     | 34                                | 2                                |
| 77   | AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE                                             | 03/2014          | 155.57 206.42                      | 206.42                       | 145.82                                  | 03/2016 09/2018       | 02/2019     | 35                                | 5                                |
| 78   | TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]PGCIL,MULTI STATE                                                 | 01/2015          | 268.80 340.88                      | 340.88                       | 241.30                                  | 03/2018 09/2018       | 02/2019     | 11                                | 5                                |
| 79   | GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE                                       | 04/2015          | 3,705.61 3,705.61                  | 3,705.61                     | 2,549.30                                | 04/2018 09/2018       | 02/2019     | 10                                | 5                                |
| 80   | EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE                                                               | 05/2016          | 766.21 766.21                      | 766.21                       | 454.34                                  | 11/2018 11/2018       | 02/2019     | 3                                 | 3                                |
| 81   | TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT                                   | 07/2016          | 300.94 300.94                      | 300.94                       | 219.36                                  | 12/2018 12/2018       | 02/2019     | 2                                 | 2                                |
| 82   | WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE                                                              | 07/2016          | 150.99 150.99                      | 150.99                       | 95.16                                   | 07/2018 07/2018       | 02/2019     | 7                                 | 7                                |
| 83   | KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU                                                                 | 05/2005          | 1,779.29 2,187.32                  | 2,187.32                     | 2,092.52                                | 11/2008 09/2018       | 03/2019     | 124                               | 6                                |
| 84   | SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE                                                                  | 10/2011          | 487.49 639.46                      | 639.46                       | 509.60                                  | 06/2014 12/2018       | 03/2019     | 57                                | 3                                |
| 85   | UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE                                                  | 01/2014          | 374.63 374.63                      | 374.63                       | 187.24                                  | 04/2016 12/2017       | 03/2019     | 35                                | 15                               |
| 86   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE                                                    | 02/2014          | 539.82 539.82                      | 539.82                       | 423.73                                  | 06/2016 09/2018       | 03/2019     | 33                                | 6                                |
| 87   | EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE                                                              | 02/2014          | 196.58 225.28                      | 225.28                       | 151.02                                  | 02/2016 09/2018       | 03/2019     | 37                                | 6                                |
| 88   | ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE | 03/2015          | 197.40 197.40                      | 197.40                       | 74.71                                   | 03/2018 -             | 03/2019     | 12                                | -                                |



# Costing Rs. 150 Crore and above

(December 2018)

| S.No | Project                                                                                                                             | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Date of Commissioning |             | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
|------|-------------------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|      |                                                                                                                                     |                  |                                    |                              |                                         | Original / Revised    | Anticipated |                                   |                                  |
| 1    | 2                                                                                                                                   | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 89   | TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN                                                 | 07/2016          | 1,429.38<br>1,429.38               | 1,429.38                     | 849.56                                  | 01/2019<br>01/2019    | 03/2019     | 2                                 | 2                                |
| 90   | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE                                           | 10/2008          | 4,824.12<br>5,071.94               | 5,071.94                     | 4,545.57                                | 10/2012<br>12/2018    | 06/2019     | 80                                | 6                                |
| 91   | TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE            | 06/2014          | 5,151.37<br>5,151.37               | 5,151.37                     | 2,892.80                                | 03/2018<br>03/2019    | 06/2019     | 15                                | 3                                |
| 92   | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE    | 10/2016          | 408.46<br>408.46                   | 408.46                       | 184.94                                  | 01/2019<br>01/2019    | 06/2019     | 5                                 | 5                                |
| 93   | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT                  | 05/2017          | 175.64<br>175.64                   | 175.64                       | 73.94                                   | 09/2018<br>09/2018    | 06/2019     | 9                                 | 9                                |
| 94   | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA        | 05/2017          | 445.89<br>445.89                   | 445.89                       | 220.56                                  | 02/2019<br>02/2019    | 06/2019     | 4                                 | 4                                |
| 95   | TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE | 03/2016          | 808.63<br>808.63                   | 808.63                       | 348.56                                  | 01/2018<br>03/2019    | 09/2019     | 20                                | 6                                |
| 96   | COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE        | 12/2014          | 4,754.42<br>4,754.42               | 9,141.97                     | 993.85                                  | 12/2018<br>12/2018    | 12/2019     | 12                                | 12                               |
| 97   | NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE                   | 12/2014          | 5,111.33<br>5,111.33               | 6,652.57                     | 922.25                                  | 12/2018<br>12/2018    | 12/2019     | 12                                | 12                               |
|      | <u>Satluj Jal Vidyut Nigam Limited</u>                                                                                              |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 98   | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR                                            | 05/2015          | 436.68<br>-                        | 602.44                       | 537.08                                  | 12/2016<br>-          | 03/2019     | 27                                | -                                |
| 99   | WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT                                             | 11/2016          | 330.00<br>-                        | 330.00                       | 310.99                                  | 11/2017<br>-          | 03/2019     | 16                                | -                                |
|      | <u>Thdc India Limited</u>                                                                                                           |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 100  | DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH                                                                       | 05/2011          | 195.42<br>294.60                   | 294.60                       | 221.63                                  | 02/2014<br>02/2018    | 03/2019     | 61                                | 13                               |
| 101  | TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND                                                                  | 07/2006          | 1,657.00<br>2,978.86               | 4,401.90                     | 2,692.27                                | 02/2016<br>12/2020    | 05/2021     | 63                                | 5                                |
| 102  | VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND                                                          | 08/2008          | 2,491.58<br>-                      | 4,105.30                     | 1,592.11                                | 06/2013<br>-          | 12/2021     | 102                               | -                                |
|      | Total                                                                                                                               |                  | 85,141.56<br>-                     | 1,11,192.25                  | 72,144.51                               |                       |             |                                   |                                  |
|      |                                                                                                                                     |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | <u>HEALTH AND FAMILY WELFARE</u>                                                                                                    |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | <u>Hospital Services Consultancy Corporation Ltd</u>                                                                                |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 103  | AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI                                                                                            | 08/2014          | 293.65<br>-                        | 293.65                       | 273.80                                  | 05/2017<br>06/2018    | 03/2019     | 22                                | 9                                |

# Costing Rs. 150 Crore and above

(December 2018)

| S.No | Project                                                                                                             | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Date of Commissioning |             | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
|------|---------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|      |                                                                                                                     |                  |                                    |                              |                                         | Original / Revised    | Anticipated |                                   |                                  |
| 1    | 2                                                                                                                   | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 104  | SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB                                             | 07/2016          | 152.95 -                           | 152.95                       | 83.11                                   | 02/2018<br>02/2018    | 06/2019     | 16                                | 16                               |
| 105  | AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI                                                              | 12/2013          | 204.44 -                           | 204.44                       | 173.67                                  | 05/2017<br>06/2018    | 07/2019     | 26                                | 13                               |
|      | Total                                                                                                               |                  | 651.04 -                           | 651.04                       | 530.58                                  |                       |             |                                   |                                  |
|      |                                                                                                                     |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | <u>RAILWAYS</u>                                                                                                     |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | <u>Central Railways</u>                                                                                             |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 106  | MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA                                                    | 02/2016          | 1,035.16<br>1,035.16               | 1,035.16                     | 19.79                                   | 03/2022<br>-          | 03/2023     | 12                                | -                                |
|      | <u>Container Corporation Of India</u>                                                                               |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 107  | MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH                                                 | 12/2015          | 174.00 -                           | 174.00                       | 139.38                                  | 03/2019<br>-          | 08/2019     | 5                                 | -                                |
| 108  | MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN                                                  | 01/2011          | 493.17 -                           | 493.17                       | 413.97                                  | 03/2018<br>-          | 12/2019     | 21                                | -                                |
| 109  | MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT                                                     | 10/2013          | 343.00 -                           | 343.00                       | 289.38                                  | 03/2019<br>-          | 12/2019     | 9                                 | -                                |
| 110  | MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH                                             | 08/2016          | 234.50 -                           | 235.00                       | 2.98                                    | 03/2019<br>-          | 12/2020     | 21                                | -                                |
|      | <u>East Central Railways</u>                                                                                        |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 111  | KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH                                                  | 08/2015          | 528.57 -                           | 528.57                       | 19.97                                   | 03/2019<br>-          | 12/2019     | 9                                 | -                                |
| 112  | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR                                                    | 04/1997          | 324.73 -                           | 1,156.41                     | 876.49                                  | 03/2012<br>-          | 03/2020     | 96                                | -                                |
| 113  | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR                                            | 04/1996          | 477.88<br>283.95                   | 749.00                       | 495.40                                  | 03/2012<br>-          | 03/2020     | 96                                | -                                |
| 114  | HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE                                                                    | 05/2015          | 678.54 -                           | 678.54                       | -                                       | 03/2019<br>-          | 03/2020     | 12                                | -                                |
| 115  | RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH                                                           | 08/2015          | 2,436.21 -                         | 2,436.21                     | 291.68                                  | 03/2020<br>-          | 03/2021     | 12                                | -                                |
| 116  | PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]ECR,BIHAR | 11/2001          | 624.47 -                           | 3,550.00                     | 97.63                                   | 02/2016<br>-          | 03/2021     | 61                                | -                                |
| 117  | KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR                                                                 | 12/2015          | 1,200.20 -                         | 1,200.20                     | -                                       | 03/2020<br>-          | 10/2021     | 19                                | -                                |
| 118  | RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR                             | 12/2015          | 1,491.47 -                         | 1,491.47                     | -                                       | 03/2020<br>-          | 10/2021     | 19                                | -                                |
| 119  | SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR                                                       | 04/2016          | 744.04 -                           | 1,215.54                     | 1.81                                    | 03/2021<br>-          | 03/2022     | 12                                | -                                |
| 120  | MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR                                                       | 04/2016          | 731.64 -                           | 1,185.73                     | -                                       | 03/2021<br>-          | 03/2022     | 12                                | -                                |
|      | <u>East Coast Railway</u>                                                                                           |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 121  | SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA                                                                 | 03/2011          | 1,111.99<br>1,539.28               | 1,539.28                     | 765.60                                  | 02/2019<br>-          | 03/2021     | 25                                | -                                |
| 122  | BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA                                                                | 03/2013          | 843.04<br>843.04                   | 843.04                       | 81.26                                   | 10/2020<br>-          | 03/2021     | 5                                 | -                                |
| 123  | JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA                        | 04/2015          | 701.61 -                           | 810.02                       | 88.04                                   | 11/2018<br>-          | 03/2021     | 28                                | -                                |

# Costing Rs. 150 Crore and above

(December 2018)

| S.No | Project                                                                                                         | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Date of Commissioning |             | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
|------|-----------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|      |                                                                                                                 |                  |                                    |                              |                                         | Original / Revised    | Anticipated |                                   |                                  |
| 1    | 2                                                                                                               | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 124  | BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR, ODISHA                                  | 04/2015          | 1,172.92 -                         | 1,172.92                     | 245.16                                  | 12/2018 -             | 03/2021     | 27                                | -                                |
| 125  | KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR, ODISHA                                                          | 04/1994          | 2,923.13 -                         | 3,798.80                     | 1,123.73                                | 03/2009 -             | 06/2021     | 147                               | -                                |
| 126  | TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR, ODISHA                                                          | 04/2005          | 810.78 -                           | 1,928.07                     | 574.98                                  | 06/2021 -             | 03/2023     | 21                                | -                                |
|      | <u>Eastern Railways</u>                                                                                         |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 127  | MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER, JHARKHAND                                                   | 04/1995          | 1,125.89 -                         | 1,126.36                     | 2,012.33                                | 03/2016 -             | 03/2020     | 48                                | -                                |
| 128  | SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER, MULTI STATE                       | 04/2010          | 277.28 -                           | 266.52                       | 137.93                                  | 03/2016 -             | 03/2020     | 48                                | -                                |
| 129  | TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL                                        | 04/2000          | 1,188.91 -                         | 1,620.01                     | 844.12                                  | 03/2019 12/2009       | 03/2019     | 0                                 | 111                              |
|      | <u>Metropolitan Rapid Transport Projects</u>                                                                    |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 130  | MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA                                          | 04/2008          | 5,300.00 -                         | 7,986.04                     | 2,423.55                                | 03/2014 -             | 03/2019     | 60                                | -                                |
| 131  | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA                                | 03/1996          | 495.44 1,781.98                    | 1,781.98                     | 1,337.62                                | 03/2004 -             | 03/2020     | 192                               | -                                |
|      | <u>North East Frontier Railway</u>                                                                              |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 132  | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE                           | 04/2000          | 1,180.19 2,531.34                  | 3,040.00                     | 3,065.47                                | 12/2008 -             | 03/2019     | 123                               | -                                |
| 133  | NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL          | 04/1983          | 297.32 200.34                      | 614.00                       | 270.27                                  | 03/2019 -             | 03/2020     | 12                                | -                                |
| 134  | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR                                                   | 04/2003          | 4,454.17 -                         | 13,809.00                    | 8,304.86                                | 03/2011 -             | 03/2020     | 108                               | -                                |
| 135  | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM                         | 09/2006          | 385.20 -                           | 1,532.00                     | 574.07                                  | 03/2019 -             | 03/2020     | 12                                | -                                |
| 136  | NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR                                | 09/2006          | 532.87 2,132.03                    | 2,145.00                     | 930.13                                  | 03/2019 -             | 03/2020     | 12                                | -                                |
| 137  | SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM                                                                     | 04/2008          | 1,339.48 -                         | 4,084.69                     | 383.92                                  | 12/2015 -             | 03/2020     | 51                                | -                                |
| 138  | AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA                                                                   | 04/2012          | 569.63 -                           | 650.00                       | -                                       | 03/2020 -             | 10/2022     | 31                                | -                                |
|      | <u>North Eastern Railway</u>                                                                                    |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 139  | AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER, UTTAR PRADESH                                          | 03/2012          | 199.75 -                           | 270.00                       | 263.56                                  | 08/2018 -             | 01/2019     | 5                                 | -                                |
| 140  | CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE                                                                 | 03/2013          | 295.00 -                           | 477.31                       | 186.71                                  | 01/2019 -             | 02/2019     | 1                                 | -                                |
| 141  | MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]NER, UTTAR PRADESH                                         | 04/1997          | 609.04 1,063.00                    | 1,807.88                     | 1,805.97                                | 04/1999 -             | 03/2019     | 239                               | -                                |
| 142  | SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER, UTTAR PRADESH | 04/2016          | 1,177.96 -                         | 1,028.95                     | 1.54                                    | 03/2014 -             | 04/2021     | 85                                | -                                |
| 143  | INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER, UTTAR PRADESH                                            | 04/2016          | 213.00 -                           | 213.35                       | .55                                     | 04/2016 -             | 01/2022     | 69                                | -                                |
| 144  | ETAH - KASGANJ - NEW LINE - [N22000462]NER, UTTAR PRADESH                                                       | 04/2017          | 276.90 -                           | 276.90                       | -                                       | 04/2017 -             | 04/2022     | 60                                | -                                |

# Costing Rs. 150 Crore and above

(December 2018)

| S.No | Project                                                                                                                    | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Date of Commissioning |             | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
|------|----------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|      |                                                                                                                            |                  |                                    |                              |                                         | Original / Revised    | Anticipated |                                   |                                  |
| 1    | 2                                                                                                                          | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 145  | NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH                                                       | 04/2017          | 150.00 -                           | 150.00                       | -                                       | 04/2017 -             | 10/2022     | 66                                | -                                |
| 146  | PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH                                                    | 04/2017          | 622.50<br>427.00                   | 426.74                       | 40.34                                   | 04/2017 -             | 10/2022     | 66                                | -                                |
|      | <u>North Western Railway</u>                                                                                               |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 147  | ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN                                                                         | 04/2013          | 242.09 -                           | 349.00                       | 293.97                                  | 02/2019 -             | 03/2019     | 1                                 | -                                |
| 148  | HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN                                                    | 04/2008          | 829.74 -                           | 1,216.00                     | 730.74                                  | 03/2015 -             | 06/2020     | 63                                | -                                |
|      | <u>Northern Railway</u>                                                                                                    |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 149  | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR                                                      | 03/1995          | 2,500.00 -                         | 27,949.00                    | 16,834.42                               | 11/2002 -             | 03/2021     | 220                               | -                                |
|      | <u>Rail Vikas Nigam Ltd.</u>                                                                                               |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 150  | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA                                                         | 04/2000          | 133.41<br>207.00                   | 385.00                       | 377.10                                  | 03/2009<br>03/2009    | 02/2019     | 119                               | 119                              |
| 151  | SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH                                                          | 09/2006          | 383.54 -                           | 555.00                       | 726.22                                  | 03/2010 -             | 12/2019     | 117                               | -                                |
| 152  | HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA                                                                           | 04/1996          | 1,185.64 -                         | 1,844.47                     | 1,406.23                                | 12/2017 -             | 03/2020     | 27                                | -                                |
| 153  | OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH                                                        | 07/2006          | 732.81 -                           | 1,850.00                     | 1,981.73                                | 03/2008 -             | 03/2020     | 144                               | -                                |
| 154  | LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH                                                | 04/2011          | 927.01 -                           | 977.00                       | 983.62                                  | 03/2019 -             | 03/2020     | 12                                | -                                |
| 155  | MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA                                          | 04/2012          | 632.68 -                           | 816.55                       | 846.22                                  | 03/2016<br>03/2017    | 12/2020     | 57                                | 45                               |
| 156  | BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA                                                                    | 03/2009          | 942.95 -                           | 942.95                       | 887.88                                  | 03/2019 -             | 03/2021     | 24                                | -                                |
| 157  | BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH                                             | 03/2012          | 1,183.25 -                         | 1,183.25                     | 1,002.84                                | 12/2020 -             | 03/2021     | 3                                 | -                                |
| 158  | SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA                                                                   | 04/1998          | 1,202.70<br>245.00                 | 1,202.70                     | 698.59                                  | 02/2015 -             | 12/2021     | 82                                | -                                |
| 159  | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH                             | 04/1995          | 631.78<br>632.00                   | 1,195.00                     | 624.13                                  | 12/2012 -             | 03/2022     | 111                               | -                                |
| 160  | VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH                                      | 03/2012          | 1,503.71 -                         | 1,503.71                     | 1,134.27                                | 03/2020 -             | 03/2022     | 24                                | -                                |
| 161  | VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH                                                     | 04/2015          | 943.60 -                           | 943.60                       | 298.09                                  | 03/2022 -             | 12/2024     | 33                                | -                                |
| 162  | MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH                                                             | 04/2015          | 1,765.92 -                         | 1,765.92                     | 335.37                                  | 03/2023 -             | 12/2024     | 21                                | -                                |
| 163  | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL | 04/2010          | 3,951.98 -                         | 4,259.48                     | 1,685.82                                | 03/2016 -             | 03/2025     | 108                               | -                                |
| 164  | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL             | 04/2010          | 2,913.51<br>4,200.00               | 2,913.50                     | 885.48                                  | 03/2016 -             | 03/2025     | 108                               | -                                |

# Costing Rs. 150 Crore and above

(December 2018)

| S.No | Project                                                                                                                         | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Date of Commissioning |             | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
|------|---------------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|      |                                                                                                                                 |                  |                                    |                              |                                         | Original / Revised    | Anticipated |                                   |                                  |
| 1    | 2                                                                                                                               | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 165  | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL | 04/2010          | 2,298.42 -                         | 2,733.86                     | 347.70                                  | 03/2014 -             | 12/2025     | 141                               | -                                |
| 166  | RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL, UTTARAKHAND                                                                 | 04/2011          | 16,216.00 -                        | 16,216.00                    | 861.35                                  | 12/2024 -             | 03/2026     | 15                                | -                                |
|      | <u>South Central Railway</u>                                                                                                    |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 167  | MUNEERABAD-MAHABOONNAGAR(NL), SCR - [220100205]SCR, MULTI STATE                                                                 | 04/1997          | 1,723.00 1.00                      | 645.00                       | 725.63                                  | 03/2000 -             | 03/2019     | 228                               | -                                |
| 168  | MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, TELANGANA                                                                  | 04/2006          | 1,160.48 -                         | 1,160.47                     | 111.36                                  | 03/2010 -             | 03/2022     | 144                               | -                                |
| 169  | NADIKUDE-SRI KALAHASTI - [N22000286]SCR, ANDHRA PRADESH                                                                         | 04/2011          | 2,288.70 -                         | 2,288.70                     | 375.28                                  | 03/2021 -             | 03/2022     | 12                                | -                                |
| 170  | KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH                                                                | 12/2001          | 1,045.20 -                         | 2,120.16                     | 289.91                                  | 03/2009 -             | 03/2023     | 168                               | -                                |
| 171  | KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR, MULTI STATE                                                    | 04/2008          | 2,132.77 -                         | 2,132.77                     | 216.07                                  | 03/2014 -             | 03/2023     | 108                               | -                                |
| 172  | GUNTUR-GUNTAKAL - [N22000368]SCR, ANDHRA PRADESH                                                                                | 04/2016          | 3,631.00 -                         | 3,631.00                     | 124.49                                  | 03/2022 -             | 03/2023     | 12                                | -                                |
| 173  | KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR, MULTI STATE                                                  | 04/2012          | 1,856.95 -                         | 2,200.00                     | 227.19                                  | 03/2023 -             | 03/2024     | 12                                | -                                |
|      | <u>South East Central Railway</u>                                                                                               |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 174  | CHHINDWARA-MANDLA FORT GC - [N22000481]SECR, MADHYA PRADESH                                                                     | 03/2011          | 556.54 -                           | 1,342.46                     | 396.00                                  | 03/2012 -             | 03/2020     | 96                                | -                                |
|      | <u>South Eastern Railway</u>                                                                                                    |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 175  | DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND                                                            | 04/2010          | 309.44 -                           | 525.81                       | 507.60                                  | 12/2015 12/2018       | 02/2019     | 38                                | 2                                |
| 176  | RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND                                               | 04/2012          | 148.77 -                           | 377.00                       | 155.96                                  | 12/2016 08/2018       | 09/2019     | 33                                | 13                               |
| 177  | MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND                                                             | 04/2012          | 258.20 -                           | 365.00                       | 192.35                                  | - 12/2018             | 01/2020     | -                                 | 13                               |
| 178  | ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER, ODISHA                                                                  | 11/2015          | 969.83 -                           | 1,151.81                     | 389.91                                  | 03/2020 03/2020       | 06/2020     | 3                                 | 3                                |
| 179  | BONDAMUNDA RANCHI DOUBLING - [N22000396]SER, JHARKHAND                                                                          | 03/2016          | 1,724.20 1,724.20                  | 1,724.20                     | 175.49                                  | 03/2021 03/2021       | 12/2021     | 9                                 | 9                                |
|      | <u>South Western Railway</u>                                                                                                    |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 180  | KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR, KARNATAKA                                                       | 03/1996          | 644.78 889.52                      | 889.52                       | 433.71                                  | 03/2017 -             | 03/2020     | 36                                | -                                |
| 181  | HUBLI- CHIKJAJUR - [N22000325]SWR, KARNATAKA                                                                                    | 03/2015          | 1,156.94 1,156.94                  | 1,156.94                     | 701.76                                  | 03/2020 03/2020       | 03/2021     | 12                                | 12                               |
|      | <u>Southern Railway</u>                                                                                                         |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 182  | OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR, TAMIL NADU                                               | 10/2013          | 187.26 -                           | 231.67                       | 7.62                                    | 04/2014 -             | 03/2020     | 71                                | -                                |
| 183  | TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR, TAMIL NADU                                            | 02/2017          | 1,567.00 -                         | 1,567.00                     | -                                       | 03/2024 -             | 03/2026     | 24                                | -                                |
|      | <u>West Central Railway</u>                                                                                                     |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 184  | KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR, MADHYA PRADESH                                                             | 12/2015          | 1,763.93 -                         | 1,763.93                     | -                                       | 03/2020 -             | 10/2021     | 19                                | -                                |

# Costing Rs. 150 Crore and above

(December 2018)

| S.No | Project                                                                                                                           | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Date of Commissioning |             | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
|------|-----------------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|      |                                                                                                                                   |                  |                                    |                              |                                         | Original / Revised    | Anticipated |                                   |                                  |
| 1    | 2                                                                                                                                 | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 185  | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE                                                               | 09/1998          | 247.66 -                           | 6,093.31                     | 972.82                                  | 05/2008 -             | 03/2023     | 178                               | -                                |
|      | <u>Western Railway</u>                                                                                                            |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 186  | BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT                                                  | 04/2008          | 318.24 -                           | 321.62                       | 83.53                                   | 03/2012 -             | 03/2019     | 84                                | -                                |
| 187  | SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT                                                                                     | 04/2015          | 1,002.39 -                         | 1,002.39                     | 232.37                                  | 03/2021 03/2019       | 03/2020     | -12                               | 12                               |
| 188  | RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH                                                                     | 04/2008          | 3,503.69 2,473.40                  | 1,030.29                     | 1,081.52                                | 03/2022 03/2019       | 03/2022     | 0                                 | 36                               |
| 189  | CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE                                                                                 | 04/2007          | 1,347.26 -                         | 1,347.26                     | 606.41                                  | 03/2022 03/2019       | 03/2022     | 0                                 | 36                               |
| 190  | DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE                                                      | 04/2007          | 1,640.04 -                         | 1,640.04                     | 603.75                                  | 03/2022 03/2019       | 03/2022     | 0                                 | 36                               |
| 191  | RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT             | 04/1994          | 320.66 1,378.12                    | 858.96                       | 549.56                                  | 03/2019 03/2019       | 03/2022     | 36                                | 36                               |
| 192  | MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT                                                                        | 04/2011          | 844.10 -                           | 844.10                       | 61.85                                   | - 03/2022             | 03/2023     | -                                 | 12                               |
|      | Total                                                                                                                             |                  | 1,13,241.35 -                      | 1,79,084.26                  | 70,274.10                               |                       |             |                                   |                                  |
|      |                                                                                                                                   |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                                |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | <u>Ministry Of Road Transport And Highways</u>                                                                                    |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 193  | WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN | 02/2015          | 383.40 -                           | 383.40                       | 224.68                                  | 03/2015 -             | 06/2019     | 51                                | -                                |
|      | <u>National Highways And Infrastructure Development Corporation Ltd.</u>                                                          |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 194  | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND | 03/2016          | 373.07 -                           | 373.07                       | -                                       | 08/2016 -             | 08/2019     | 36                                | -                                |
| 195  | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND | 03/2016          | 396.52 -                           | 396.52                       | -                                       | 08/2016 -             | 08/2019     | 36                                | -                                |
| 196  | FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND | 03/2016          | 429.52 -                           | 429.52                       | -                                       | 08/2016 -             | 08/2019     | 36                                | -                                |
| 197  | CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH                       | 12/2016          | 138.93 155.00                      | 155.00                       | -                                       | 01/2017 -             | 01/2020     | 36                                | -                                |
|      | <u>National Highways Authority Of India</u>                                                                                       |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 198  | 2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU                                            | 04/2012          | 624.00 -                           | 624.00                       | 350.79                                  | 04/2014 -             | 12/2019     | 68                                | -                                |
| 199  | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM                                                    | 12/2003          | 280.00 -                           | 361.00                       | 410.32                                  | 02/2009 -             | 12/2018     | 118                               | -                                |

# Costing Rs. 150 Crore and above

(December 2018)

| S.No | Project                                                                                                                          | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Date of Commissioning |             | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
|------|----------------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|      |                                                                                                                                  |                  |                                    |                              |                                         | Original / Revised    | Anticipated |                                   |                                  |
| 1    | 2                                                                                                                                | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 200  | SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU                            | 09/2011          | 1,250.00 -                         | 1,250.00                     | 1,329.17                                | 12/2013 -             | 12/2018     | 60                                | -                                |
| 201  | KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT                                                                                   | 01/2011          | 953.88 -                           | 953.88                       | 976.28                                  | 07/2013 -             | 12/2018     | 65                                | -                                |
| 202  | TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU                                                  | 05/2010          | 374.00 -                           | 374.00                       | 237.00                                  | 05/2013 -             | 12/2018     | 67                                | -                                |
| 203  | 2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU                                                       | 09/2011          | 485.00 -                           | 485.00                       | 406.68                                  | 08/2013 -             | 12/2018     | 64                                | -                                |
| 204  | TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH                                                                  | 04/2011          | 571.00 -                           | 571.00                       | 582.52                                  | 10/2013 -             | 12/2018     | 62                                | -                                |
| 205  | PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR                                                                   | 09/2011          | 574.00 -                           | 574.00                       | 768.62                                  | 03/2014 -             | 12/2018     | 57                                | -                                |
| 206  | 2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR                                                                      | 05/2011          | 511.54 -                           | 511.54                       | 564.35                                  | 11/2013 -             | 12/2018     | 61                                | -                                |
| 207  | TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 ( NEW NH NO -50) - [N24000342]NHAI,KARNATAKA  | 05/2015          | 709.00 -                           | 709.00                       | 380.95                                  | 09/2017 -             | 12/2018     | 15                                | -                                |
| 208  | 4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA                                                              | 12/2015          | 602.95 -                           | 602.95                       | 54.89                                   | 06/2016 -             | 12/2018     | 30                                | -                                |
| 209  | 4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA                                                      | 01/2015          | 972.50 -                           | 972.50                       | 1,484.99                                | 07/2017 -             | 12/2018     | 17                                | -                                |
| 210  | FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH                                                                 | 05/2013          | 1,055.00 -                         | 1,601.77                     | 1,393.40                                | 11/2015 -             | 12/2018     | 37                                | -                                |
| 211  | FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA                                                                | 07/2015          | 1,871.34 -                         | 1,871.34                     | 2,304.41                                | 01/2018 -             | 12/2018     | 11                                | -                                |
| 212  | FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA                | 04/2010          | 1,170.52 -                         | 1,170.52                     | 2,042.41                                | 06/2012 -             | 12/2018     | 78                                | -                                |
| 213  | TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR                                                   | 08/2015          | 516.13 -                           | 516.13                       | 400.35                                  | 04/2018 -             | 12/2018     | 8                                 | -                                |
| 214  | SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM                                                                                | 12/2003          | 245.00 174.34                      | 174.34                       | 214.88                                  | 03/2008 -             | 01/2019     | 130                               | -                                |
| 215  | JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA                                                                                    | 01/2011          | 536.00 -                           | 536.00                       | 837.81                                  | 01/2014 -             | 01/2019     | 60                                | -                                |
| 216  | PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN                                        | 09/2015          | 567.51 -                           | 567.51                       | 53.70                                   | 03/2018 -             | 01/2019     | 10                                | -                                |
| 217  | 2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN                                                               | 10/2015          | 597.00 -                           | 597.00                       | 604.80                                  | 10/2017 -             | 01/2019     | 15                                | -                                |
| 218  | DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM                                                                  | 12/2003          | 160.00 -                           | 167.98                       | 198.82                                  | 05/2008 -             | 02/2019     | 129                               | -                                |
| 219  | 2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN | 11/2012          | 530.07 -                           | 530.07                       | 556.02                                  | 08/2016 -             | 02/2019     | 30                                | -                                |
| 220  | 2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN                                                        | 08/2016          | 320.30 -                           | 320.30                       | 193.54                                  | 01/2019 -             | 02/2019     | 1                                 | -                                |



# Costing Rs. 150 Crore and above

(December 2018)

| S.No | Project                                                                                                                              | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Date of Commissioning |             | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
|------|--------------------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|      |                                                                                                                                      |                  |                                    |                              |                                         | Original / Revised    | Anticipated |                                   |                                  |
| 1    | 2                                                                                                                                    | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 221  | MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [N240106278]NHAI,ASSAM                                                         | 12/2003          | 199.81 -                           | 385.13                       | 209.80                                  | 04/2009 -             | 03/2019     | 119                               | -                                |
| 222  | NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM                                                                                       | 12/2003          | 208.00 -                           | 230.00                       | 297.81                                  | 04/2008 -             | 03/2019     | 131                               | -                                |
| 223  | HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA                                                        | 09/2010          | 946.00 -                           | 946.00                       | 818.53                                  | 06/2018 -             | 03/2019     | 9                                 | -                                |
| 224  | SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA                                                 | 02/2010          | 617.00 -                           | 617.00                       | 943.17                                  | 08/2012 -             | 03/2019     | 79                                | -                                |
| 225  | QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR                                                         | 07/2010          | 1,987.00 -                         | 1,987.00                     | 2,403.47                                | 07/2015 -             | 03/2019     | 44                                | -                                |
| 226  | PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA                                                                                            | 03/2012          | 1,410.00 -                         | 1,410.00                     | 1,555.96                                | 09/2014 -             | 03/2019     | 54                                | -                                |
| 227  | TWO LANING WITH PAVED SHOULDER OF KARAUUI - DHOLPUR - [N24000344]NHAI,RAJASTHAN                                                      | 09/2014          | 425.19 -                           | 425.19                       | 274.20                                  | 09/2016 -             | 03/2019     | 30                                | -                                |
| 228  | CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270( D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 ( D - [N24000432]NHAI,MAHARASHTRA   | 09/2015          | 414.51 -                           | 414.00                       | 230.34                                  | 05/2018 -             | 03/2019     | 10                                | -                                |
| 229  | BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM.55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN      | 08/2014          | 822.90 -                           | 822.90                       | 688.00                                  | 04/2018 -             | 03/2019     | 11                                | -                                |
| 230  | 4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA                                                                  | 01/2016          | 574.28 -                           | 574.28                       | 79.56                                   | 07/2018 -             | 03/2019     | 8                                 | -                                |
| 231  | 4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA                                                        | 05/2014          | 1,655.01 -                         | 1,655.01                     | 1,515.16                                | 08/2016 -             | 03/2019     | 31                                | -                                |
| 232  | GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN                                                                   | 02/2008          | 1,673.70 -                         | 1,673.70                     | 3,326.93                                | 10/2011<br>09/2017    | 03/2019     | 89                                | 18                               |
| 233  | FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH                                                                    | 09/2015          | 934.46 -                           | 934.46                       | 104.98                                  | 03/2018 -             | 03/2019     | 12                                | -                                |
| 234  | FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH | 06/2015          | 1,012.90 -                         | 1,012.90                     | 1,042.73                                | 03/2016 -             | 03/2019     | 36                                | -                                |
| 235  | TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA                                     | 12/2015          | 479.20 -                           | 479.20                       | 14.31                                   | 05/2018 -             | 03/2019     | 10                                | -                                |
| 236  | NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM                                                                                      | 12/2003          | 225.00 -                           | 225.00                       | 312.79                                  | 06/2008 -             | 04/2019     | 130                               | -                                |
| 237  | BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM                                                                                   | 12/2003          | 217.61 -                           | 360.84                       | 390.19                                  | 04/2010 -             | 04/2019     | 108                               | -                                |
| 238  | CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH                                                      | 11/2010          | 1,585.00 -                         | 1,585.00                     | 2,167.31                                | 05/2013 -             | 04/2019     | 71                                | -                                |
| 239  | FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH                                 | 11/2013          | 1,916.79 -                         | 1,916.79                     | 1,948.92                                | 11/2016 -             | 04/2019     | 29                                | -                                |
| 240  | CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 ( OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA                    | 10/2015          | 593.26 -                           | 593.26                       | 45.11                                   | 05/2018 -             | 04/2019     | 11                                | -                                |



# Costing Rs. 150 Crore and above

(December 2018)

|      |                                                                                                                                   |                  |                                    |                              |                                         | Date of Commissioning |             |                                   |                                  |
|------|-----------------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
| S.No | Project                                                                                                                           | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
| 1    | 2                                                                                                                                 | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 241  | 6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA                   | 08/2015          | 505.00 -                           | 505.00                       | 194.09                                  | 05/2018 -             | 04/2019     | 11                                | -                                |
| 242  | FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA                                                                   | 03/2015          | 1,388.00 -                         | 1,388.00                     | 924.40                                  | 08/2018 -             | 04/2019     | 8                                 | -                                |
| 243  | FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB                                                                       | 10/2015          | 447.29 -                           | 447.29                       | 31.96                                   | 12/2017 -             | 04/2019     | 16                                | -                                |
| 244  | CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL                                                    | 03/2016          | 229.37 -                           | 229.37                       | 10.43                                   | 11/2018 -             | 04/2019     | 5                                 | -                                |
| 245  | FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU | 02/2016          | 641.17 -                           | 641.17                       | 259.00                                  | 07/2018 -             | 04/2019     | 9                                 | -                                |
| 246  | 4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA     | 04/2016          | 804.97 -                           | 804.97                       | 21.80                                   | 06/2018 -             | 04/2019     | 10                                | -                                |
| 247  | FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU | 03/2016          | 641.17 -                           | 641.17                       | 244.33                                  | 07/2016 -             | 04/2019     | 33                                | -                                |
| 248  | 6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL                                                              | 04/2012          | 1,396.18 -                         | 1,396.18                     | 2,614.84                                | 09/2014 -             | 05/2019     | 56                                | -                                |
| 249  | KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL                                                                              | 02/2012          | 702.16 -                           | 702.16                       | 454.81                                  | 07/2014 -             | 05/2019     | 58                                | -                                |
| 250  | FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU      | 05/2015          | 1,387.11 -                         | 1,387.11                     | 915.30                                  | 11/2017 -             | 05/2019     | 18                                | -                                |
| 251  | CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 ( - [N24000435]NHAI,MAHARASHTRA  | 10/2015          | 531.13 -                           | 531.13                       | 163.10                                  | 05/2018 -             | 05/2019     | 12                                | -                                |
| 252  | 4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI ( KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL                          | 12/2015          | 1,083.00 -                         | 1,083.00                     | 155.25                                  | 06/2018 -             | 05/2019     | 11                                | -                                |
| 253  | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA                                                             | 05/2009          | 1,108.00 -                         | 2,288.00                     | 3,953.66                                | 11/2011 -             | 06/2019     | 91                                | -                                |
| 254  | PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA                                                                                   | 10/2010          | 1,724.55 -                         | 1,724.55                     | 2,253.40                                | 03/2013 -             | 06/2019     | 75                                | -                                |
| 255  | PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR                                                                                        | 08/2010          | 671.30 -                           | 671.30                       | 884.43                                  | 02/2013 -             | 06/2019     | 76                                | -                                |
| 256  | 4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR                                                                               | 01/2011          | 575.00 -                           | 575.00                       | 831.49                                  | 07/2013 -             | 06/2019     | 71                                | -                                |
| 257  | 4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL                                                                          | 02/2011          | 1,078.84 -                         | 1,078.84                     | 2,312.98                                | 08/2013 -             | 06/2019     | 70                                | -                                |
| 258  | PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA                                                                                      | 12/2011          | 942.69 -                           | 942.69                       | 668.59                                  | 06/2014 -             | 06/2019     | 60                                | -                                |
| 259  | WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA                                     | 05/2013          | 1,348.20 -                         | 1,348.20                     | 1,792.90                                | 02/2014 -             | 06/2019     | 64                                | -                                |
| 260  | 4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA                                                 | 04/2014          | 1,266.60 -                         | 1,544.00                     | 1,411.79                                | 09/2016 -             | 06/2019     | 33                                | -                                |

# Costing Rs. 150 Crore and above

(December 2018)

| S.No | Project                                                                                                                            | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Date of Commissioning |             | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
|------|------------------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|      |                                                                                                                                    |                  |                                    |                              |                                         | Original / Revised    | Anticipated |                                   |                                  |
| 1    | 2                                                                                                                                  | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 261  | TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU                                                        | 06/2015          | 563.92 -                           | 563.92                       | 96.48                                   | 12/2017 -             | 06/2019     | 18                                | -                                |
| 262  | 4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA                                                  | 06/2014          | 923.04 -                           | 923.04                       | 650.92                                  | 11/2016 -             | 06/2019     | 31                                | -                                |
| 263  | FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH                                                                      | 12/2015          | 596.67 -                           | 596.67                       | 41.87                                   | 05/2018 -             | 06/2019     | 13                                | -                                |
| 264  | FOUR / SIX LANING OF RAIPUR - SIMGA ( PKG-1) - [N24000510]NHAI,CHHATISGARH                                                         | 12/2015          | 726.67 -                           | 726.67                       | 50.67                                   | 04/2018 -             | 06/2019     | 14                                | -                                |
| 265  | FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU  | 02/2016          | 707.82 -                           | 707.82                       | 208.92                                  | 08/2018 -             | 06/2019     | 10                                | -                                |
| 266  | BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR                                                           | 05/2015          | 581.84 -                           | 581.84                       | 77.43                                   | 05/2017 -             | 06/2019     | 25                                | -                                |
| 267  | HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND                                                                 | 11/2011          | 478.51 -                           | 478.00                       | 409.17                                  | 10/2013 -             | 07/2019     | 69                                | -                                |
| 268  | FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA                                                                      | 12/2015          | 1,423.96 -                         | 1,423.96                     | 514.42                                  | 11/2018 -             | 07/2019     | 8                                 | -                                |
| 269  | 4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA                                         | 03/2016          | 701.40 -                           | 701.40                       | 22.02                                   | 03/2019 -             | 07/2019     | 4                                 | -                                |
| 270  | CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA                                                          | 08/2016          | 248.97 -                           | 248.97                       | 27.57                                   | 05/2019 -             | 08/2019     | 3                                 | -                                |
| 271  | TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGPUR - [N24000586]NHAI,RAJASTHAN                                                      | 06/2016          | 637.18 -                           | 637.18                       | 576.75                                  | 06/2019 -             | 09/2019     | 3                                 | -                                |
| 272  | FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN                          | 06/2016          | 649.00 -                           | 649.00                       | -                                       | 06/2019 -             | 09/2019     | 3                                 | -                                |
| 273  | FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL | 09/2016          | 767.03 -                           | 767.03                       | 156.04                                  | 08/2018 -             | 09/2019     | 13                                | -                                |
| 274  | 4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA | 11/2016          | 400.25 -                           | 400.25                       | 38.57                                   | 03/2019 -             | 09/2019     | 6                                 | -                                |
| 275  | FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR                                              | 12/2015          | 2,136.97 -                         | 2,136.97                     | 87.69                                   | 12/2018 -             | 10/2019     | 10                                | -                                |
| 276  | TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR                                                      | 08/2015          | 399.54 -                           | 399.54                       | 142.41                                  | 04/2019 -             | 10/2019     | 6                                 | -                                |
| 277  | FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN     | 06/2016          | 763.23 -                           | 763.23                       | 154.91                                  | 06/2019 -             | 11/2019     | 5                                 | -                                |
| 278  | 4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH                                     | 08/2016          | 2,016.00 -                         | 2,016.00                     | 1,663.22                                | 04/2019 -             | 11/2019     | 7                                 | -                                |
| 279  | 4-LANNING OF KODEBAD-DHARTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA | 11/2016          | 446.17 -                           | 446.17                       | 2.42                                    | 03/2019 -             | 11/2019     | 8                                 | -                                |

# Costing Rs. 150 Crore and above

(December 2018)

| S.No | Project                                                                                                                              | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Date of Commissioning |             | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
|------|--------------------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|      |                                                                                                                                      |                  |                                    |                              |                                         | Original / Revised    | Anticipated |                                   |                                  |
| 1    | 2                                                                                                                                    | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 280  | FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH      | 06/2017          | 648.33 -                           | 648.33                       | 15.89                                   | 06/2017 -             | 11/2019     | 29                                | -                                |
| 281  | VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE                                                                | 09/2011          | 2,848.00 -                         | 2,848.00                     | 1,141.90                                | 03/2014 -             | 12/2019     | 69                                | -                                |
| 282  | MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE                                                                                 | 09/2011          | 754.00 -                           | 754.00                       | 1,363.43                                | 03/2013 -             | 12/2019     | 81                                | -                                |
| 283  | FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH | 10/2017          | 639.97 -                           | 639.97                       | 58.04                                   | 10/2017 -             | 01/2020     | 27                                | -                                |
| 284  | FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR                                                                          | 08/2015          | 322.09 -                           | 322.09                       | 71.28                                   | 04/2018 -             | 04/2020     | 24                                | -                                |
| 285  | CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB         | 03/2017          | 754.54 -                           | 756.27                       | 30.30                                   | 03/2020 -             | 04/2020     | 1                                 | -                                |
| 286  | FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA                                                                  | 02/2017          | 904.16 -                           | 904.16                       | 155.12                                  | 02/2020 -             | 05/2020     | 3                                 | -                                |
| 287  | 4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA                                           | 03/2017          | 1,030.44 -                         | 1,065.51                     | 355.02                                  | 03/2020 -             | 05/2020     | 2                                 | -                                |
| 288  | DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH | 03/2017          | 1,989.00 -                         | 1,989.00                     | 842.34                                  | 03/2020 -             | 05/2020     | 2                                 | -                                |
| 289  | SIX LANNING OF RANASTALAM- ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH               | 03/2017          | 1,041.62 -                         | 1,187.10                     | 43.99                                   | 03/2020 -             | 05/2020     | 2                                 | -                                |
| 290  | 4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL                                                                          | 02/2011          | 998.79 -                           | 998.79                       | 1,825.92                                | 08/2013 -             | 06/2020     | 82                                | -                                |
| 291  | SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA       | 03/2017          | 831.58 -                           | 1,177.00                     | 121.00                                  | 03/2020 -             | 06/2020     | 3                                 | -                                |
| 292  | SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA     | 03/2017          | 993.16 -                           | 1,434.00                     | 413.53                                  | 03/2020 -             | 06/2020     | 3                                 | -                                |
| 293  | 4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA                                                                         | 09/2017          | 1,124.11 -                         | 1,124.11                     | -                                       | 09/2017 -             | 06/2020     | 33                                | -                                |
| 294  | GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE                                                                                  | 12/2003          | 604.00 -                           | 604.00                       | 423.83                                  | 12/2009 -             | 08/2020     | 128                               | -                                |
| 295  | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH | 03/2017          | 1,184.71 -                         | 1,310.00                     | -                                       | 03/2020 -             | 08/2020     | 5                                 | -                                |
| 296  | 4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA                                            | 03/2017          | 988.34 -                           | 1,043.28                     | 451.51                                  | 03/2020 -             | 08/2020     | 5                                 | -                                |
| 297  | 4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA                                          | 03/2017          | 1,098.06 -                         | 1,160.64                     | 413.75                                  | 03/2020 -             | 08/2020     | 5                                 | -                                |

# Costing Rs. 150 Crore and above

(December 2018)

| S.No | Project                                                                                                                                       | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Date of Commissioning |             | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
|------|-----------------------------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|      |                                                                                                                                               |                  |                                    |                              |                                         | Original / Revised    | Anticipated |                                   |                                  |
| 1    | 2                                                                                                                                             | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 298  | 4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT                                                       | 06/2017          | 1,958.88 -                         | 1,958.88                     | 364.31                                  | 06/2020 -             | 08/2020     | 2                                 | -                                |
| 299  | 4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA                                                      | 03/2016          | 870.00 -                           | 870.00                       | 9.12                                    | 03/2019 -             | 11/2020     | 20                                | -                                |
| 300  | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH           | 03/2017          | 1,373.28 -                         | 1,373.28                     | -                                       | 03/2020 -             | 11/2020     | 8                                 | -                                |
| 301  | 4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA                                                   | 03/2017          | 1,059.73 -                         | 1,071.00                     | 152.79                                  | 03/2017 -             | 11/2020     | 44                                | -                                |
| 302  | REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA                                           | 07/2017          | 476.56 -                           | 476.56                       | -                                       | 07/2017 -             | 11/2020     | 40                                | -                                |
| 303  | FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR                                                          | 12/2015          | 2,168.66 -                         | 2,168.66                     | -                                       | 06/2019 -             | 12/2020     | 18                                | -                                |
|      | <u>National Highways Development Project</u>                                                                                                  |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 304  | BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH                                                                             | 11/2011          | 704.26 -                           | 704.26                       | 5.21                                    | 05/2015 -             | 01/2020     | 56                                | -                                |
|      | Total                                                                                                                                         |                  | 96,101.97 -                        | 99,712.68                    | 68,218.96                               |                       |             |                                   |                                  |
|      |                                                                                                                                               |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | <u>SHIPPING AND PORTS</u>                                                                                                                     |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | <u>Mumbai Port Trust</u>                                                                                                                      |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 305  | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA | 01/2007          | 366.39 669.46                      | 669.46                       | 413.91                                  | 12/2010 -             | 12/2018     | 96                                | -                                |
|      | <u>Port Trust</u>                                                                                                                             |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 306  | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU                                                | 10/2002          | 150.00 600.00                      | 600.00                       | 550.78                                  | 03/2006 03/2016       | 02/2019     | 155                               | 35                               |
|      | Total                                                                                                                                         |                  | 516.39 -                           | 1,269.46                     | 964.69                                  |                       |             |                                   |                                  |
|      |                                                                                                                                               |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | <u>TELECOMMUNICATIONS</u>                                                                                                                     |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | <u>Department Of Telecommunication</u>                                                                                                        |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 307  | NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE                                                                                             | 03/2012          | 13,334.00 -                        | 24,664.00                    | 8,397.00                                | 07/2015 -             | 05/2020     | 58                                | -                                |
|      | Total                                                                                                                                         |                  | 13,334.00 -                        | 24,664.00                    | 8,397.00                                |                       |             |                                   |                                  |
|      |                                                                                                                                               |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | <u>URBAN DEVELOPMENT</u>                                                                                                                      |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | <u>Bangalore Metro Rail Corporation Limited</u>                                                                                               |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 308  | BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA                                                                             | 02/2014          | 26,405.14 -                        | 26,405.14                    | 499.85                                  | 02/2019 -             | 03/2020     | 13                                | -                                |
|      | <u>Central Public Works Department</u>                                                                                                        |                  |                                    |                              |                                         |                       |             |                                   |                                  |

# Costing Rs. 150 Crore and above

(December 2018)

| S.No | Project                                                                                                                           | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Date of Commissioning |             | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
|------|-----------------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|      |                                                                                                                                   |                  |                                    |                              |                                         | Original / Revised    | Anticipated |                                   |                                  |
| 1    | 2                                                                                                                                 | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 309  | DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH                                | 11/2012          | 270.83 -                           | 270.83                       | 163.97                                  | 11/2014 -             | 02/2019     | 51                                | -                                |
| 310  | CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL                     | 02/2014          | 156.57 -                           | 156.57                       | 146.40                                  | 08/2016 -             | 03/2019     | 31                                | -                                |
| 311  | CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA                                                    | 01/2010          | 165.23 -                           | 165.23                       | 58.85                                   | 10/2012 -             | 03/2019     | 77                                | -                                |
| 312  | CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB                         | 02/2014          | 388.00 -                           | 388.00                       | 395.14                                  | 05/2017 02/2019       | 03/2019     | 22                                | 1                                |
| 313  | NSG AT KOLKATA - [N28000104]CPWD, WEST BENGAL                                                                                     | 10/2014          | 162.88 -                           | 162.88                       | 96.48                                   | 04/2018 -             | 07/2019     | 15                                | -                                |
| 314  | CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB                                   | 08/2016          | 294.00 -                           | 294.00                       | 134.64                                  | 04/2019 06/2019       | 09/2019     | 5                                 | 3                                |
| 315  | CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND | 12/2008          | 114.26 266.00                      | 266.00                       | -                                       | 12/2013 -             | 10/2019     | 70                                | -                                |
| 316  | DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN               | 12/2016          | 549.31 -                           | 540.42                       | 215.67                                  | 07/2019 -             | 10/2019     | 3                                 | -                                |
| 317  | NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR                                                                 | 02/2014          | 216.69 -                           | 216.69                       | 52.00                                   | 03/2015 -             | 11/2019     | 56                                | -                                |
| 318  | ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI           | 10/2013          | 1,219.21 -                         | 1,592.00                     | 331.12                                  | 10/2019 -             | 03/2020     | 5                                 | -                                |
| 319  | 2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND                                              | 09/2012          | 171.86 -                           | 171.86                       | 41.28                                   | 03/2016 -             | 04/2020     | 49                                | -                                |
| 320  | CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR               | 02/2016          | 496.18 496.00                      | 498.99                       | 34.09                                   | 06/2017 07/2017       | 06/2020     | 36                                | 35                               |
| 321  | CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA                                     | 01/2018          | 223.37 -                           | 223.37                       | 4.00                                    | 07/2020 09/2018       | 09/2020     | 2                                 | 24                               |
|      | <u>Hindustan Steelwork Construction Limited</u>                                                                                   |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 322  | CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA | 04/2014          | 151.33 -                           | 151.33                       | 7.15                                    | 09/2017 -             | 12/2018     | 15                                | -                                |
| 323  | CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND                                      | 02/2014          | 787.29 -                           | 787.29                       | 285.30                                  | 12/2016 -             | 12/2018     | 24                                | -                                |
| 324  | IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR                                                                                | 10/2005          | 956.00 -                           | 956.00                       | 651.21                                  | 03/2015 -             | 03/2021     | 72                                | -                                |
|      | <u>Kochi Metro Rail Corporation Ltd</u>                                                                                           |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 325  | KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA                                                                                | 07/2012          | 5,181.79 -                         | 5,181.79                     | -                                       | 07/2017 -             | 12/2019     | 29                                | -                                |
|      | <u>Mumbai Metro Rail Corporation Ltd</u>                                                                                          |                  |                                    |                              |                                         |                       |             |                                   |                                  |

# Costing Rs. 150 Crore and above

(December 2018)

|      |                                                                           |                  |                                    |                              |                                         | Date of Commissioning |             |                                   |                                  |
|------|---------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
| S.No | Project                                                                   | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
| 1    | 2                                                                         | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 326  | MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA | 07/2013          | 23,136.00 -                        | 23,136.00                    | -                                       | 01/2015 -             | 05/2020     | 64                                | -                                |
|      | Total                                                                     |                  | 61,045.94 -                        | 61,564.39                    | 3,117.15                                |                       |             |                                   |                                  |
|      |                                                                           |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | Grand Total                                                               |                  | 4,87,959.43                        | 6,04,354.05                  | 2,93,394.51                             |                       |             |                                   |                                  |

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( DECEMBER 2018 )

## ATOMIC ENERGY

| Sn | Project                                            | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|----|----------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 1  | RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) | NPCIL  | 10/2009 | 12/2016      | 12/2020         | 12320                     | 48           |
| 2  | KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4            | NPCIL  | 10/2009 | 12/2015      | 06/2020         | 11459                     | 54           |
| 3  | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)  | BHAVNI | 09/2003 | 09/2010      | 03/2019         | 3492                      | 102          |
| 4  | KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4      | NPCIL  | 03/2013 | 11/2020      | 11/2023         | 39849                     | 36           |

## CIVIL AVIATION

| Sn | Project                                                                    | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|----|----------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 5  | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR | AAI    | 10/2013 | 09/2018      | 06/2020         | 314.61                    | 21           |

## COAL

| Sn | Project                                                           | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|----|-------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 6  | RFR OF MANUGURU OC PROJECT                                        | SCCL   | 11/2012 | 03/2016      | 03/2019         | 430.45                    | 36           |
| 7  | KALYANIKHANI OPENCAST PROJECT                                     | SCCL   | 07/2012 | 07/2016      | 03/2020         | 417.33                    | 44           |
| 8  | RG OC -III EXTENSION (PHASE -II) PROJECT                          | SCCL   | 06/2012 | 06/2015      | 03/2019         | 365.01                    | 45           |
| 9  | MOONIDIH XV SEAM UG                                               | BCCL   | 08/2011 | 04/2015      | 04/2019         | 1230.27                   | 48           |
| 10 | RKP OCP PHASE-I                                                   | SCCL   | 03/2010 | 03/2015      | 03/2019         | 209.78                    | 48           |
| 11 | ANANTA OC EXPANSION PH-III (15.0 MTY)                             | MCL    | 08/2008 | 03/2012      | 03/2021         | 207.28                    | 108          |
| 12 | MANIKPUR OC EXPANSION (3.5 MTY)                                   | SECL   | 12/2009 | 03/2014      | 03/2020         | 321.5                     | 72           |
| 13 | KAMPTEE DEEP OC MINE                                              | WCL    | 11/2015 | 03/2021      | 03/2024         | 277.65                    | 36           |
| 14 | SONEPUR BAZARI (COMB) OCP (8.0 MTY)                               | ECL    | 08/2012 | 03/2018      | 03/2020         | 1055.05                   | 24           |
| 15 | BASUNDHARA (WEST) OC EXTN(7.00 MTY)                               | MCL    | 05/2014 | 03/2019      | 03/2024         | 479.15                    | 60           |
| 16 | JAGANNATH RE-ORGANISATION OC.(6.00 MTY)                           | MCL    | 05/2014 | 03/2019      | 03/2021         | 337.66                    | 24           |
| 17 | KULDA EXPN OC. (5.00 MTY)                                         | MCL    | 06/2014 | 03/2018      | 03/2020         | 289.03                    | 24           |
| 18 | ADASA UG TO OC                                                    | WCL    | 08/2015 | 03/2023      | 03/2024         | 288.9                     | 12           |
| 19 | KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) | NCL    | 06/2011 | 03/2018      | 03/2019         | 1131.28                   | 12           |
| 20 | RAJRAPPA RCE OCP ( 3.0 MTY)                                       | CCL    | 12/2009 | 03/2016      | 03/2019         | 510.85                    | 36           |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( DECEMBER 2018 )

| Sn | Project                                                         | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|----|-----------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 21 | KANIHA OCP, MCL, (10.0 MTY)                                     | MCL    | 12/2007 | 03/2013         | 03/2020            | 457.77                          | 84              |
| 22 | CHURI BENTI UG (0.81 MTY)                                       | CCL    | 08/2007 | 03/2011         | 03/2020            | 163.51                          | 108             |
| 23 | NORTH URIMARI OCP (3.0 MTY)                                     | CCL    | 12/2007 | 03/2012         | 03/2019            | 179.87                          | 84              |
| 24 | TAPIN OCP (2.5 MTY)                                             | CCL    | 08/2008 | 03/2012         | 03/2019            | 264.68                          | 84              |
| 25 | KARMA OCP (1.0MTY)                                              | CCL    | 06/2009 | 03/2014         | 03/2019            | 162.46                          | 60              |
| 26 | SHANTIKHANI LONGWALL PROJ-SCCL                                  | SCCL   | 10/2006 | 03/2012         | 03/2024            | 249.03                          | 144             |
| 27 | KISTARAM OCP                                                    | SCCL   | 11/2010 | 03/2015         | 03/2021            | 242.29                          | 72              |
| 28 | KARTALI (EAST) OCP (2.50 MTY)                                   | SECL   | 07/2008 | 03/2014         | 03/2020            | 178.44                          | 72              |
| 29 | AMLAI OC EXPANSION SECTOR B (1.50 MTY)                          | SECL   | 11/2009 | 03/2016         | 03/2019            | 198.59                          | 36              |
| 30 | EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) | NLC    | 04/2013 | 06/2015         | 09/2019            | 1458.17                         | 51              |
| 31 | KOYAGUDEM OPENCAST PROJECT                                      | SCCL   | 10/2015 | 03/2018         | 03/2019            | 426.79                          | 12              |
| 32 | JAGANNATHPOR OCP(3.00MTY)                                       | SECL   | 09/2008 | 03/2015         | 03/2020            | 152.43                          | 60              |
| 33 | MAGADH OC 20 MTY (CCL)                                          | CCL    | 08/2008 | 07/2012         | 03/2021            | 706.4                           | 104             |
| 34 | RAMAGUNDAM OC-II EXTENSION                                      | SCCL   | 12/2009 | 03/2012         | 03/2023            | 418.97                          | 132             |
| 35 | BHUBANESWARI OCP, MCL (20.0 MTY)                                | MCL    | 12/2007 | 03/2017         | 03/2020            | 490.1                           | 36              |
| 36 | HINGULA OC-II EXP. PH-III (15 MTY)                              | MCL    | 11/2008 | 03/2013         | 03/2020            | 479.53                          | 84              |
| 37 | BALRAM OCP EXTENSION, MCL 8.00 MTY                              | MCL    | 12/2007 | 03/2010         | 03/2020            | 172.08                          | 120             |
| 38 | BAROUD OC EXPANSION (RCE)- 3MTY                                 | SECL   | 04/2012 | 03/2016         | 03/2019            | 258.56                          | 36              |
| 39 | NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)                     | NLC    | 06/2011 | 12/2015         | 03/2019            | 5907.11                         | 39              |
| 40 | JALAGAM VENGALA RAO OCP-II                                      | SCCL   | 07/2011 | 03/2015         | 03/2021            | 447.06                          | 72              |
| 41 | RCE OF INDARAM OCP(1.20 MTPA)                                   | SCCL   | 07/2011 | 03/2015         | 03/2021            | 162.76                          | 72              |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun



## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( DECEMBER 2018 )

## DEFENCE PRODUCTION

| Sn | Project                    | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|----|----------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 42 | CONSTRUCTION WORKS PHASE 4 | GSL    | 12/2016 | 05/2018      | 01/2019         | 167.69                    | 8            |

## FERTILISERS

| Sn | Project                                                                 | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|----|-------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 43 | GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. | RCF    | 02/2016 | 12/2017      | 01/2019         | 482.85                    | 13           |
| 44 | NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY                         | RCF    | 10/2014 | 11/2016      | 04/2019         | 197.79                    | 29           |

## HEALTH AND FAMILY WELFARE

| Sn | Project                                        | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|----|------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 45 | NEIGRIHMS SHILLONG MEGHALYA                    | HSCC   | 10/2016 | 05/2018      | 08/2019         | 363.99                    | 15           |
| 46 | SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB | HSCC   | 07/2016 | 02/2018      | 06/2019         | 152.95                    | 16           |
| 47 | AIIMS - MOTHER AND CHILD BLOCK                 | HSCC   | 12/2013 | 05/2017      | 07/2019         | 204.44                    | 26           |
| 48 | LHMC NEW DELHI-RE-DEVELOPMENT                  | HSCC   | 02/2013 | 11/2013      | 10/2020         | 414.11                    | 83           |
| 49 | AIIMS - OPD(NEW)                               | HSCC   | 08/2014 | 05/2017      | 03/2019         | 293.65                    | 22           |

## HEAVY INDUSTRY

| Sn | Project                                                            | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|----|--------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 50 | NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) | NATIS  | 04/2011 | 09/2011      | 06/2019         | 1718                      | 93           |

## PETROLEUM

| Sn | Project                                                                                             | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|----|-----------------------------------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 51 | CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU                                            | IOCL   | 12/2017 | 10/2020      | 08/2021         | 466.43                    | 10           |
| 52 | CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN                                                  | OIL    | 07/2011 | 01/2019      | 09/2019         | 350                       | 8            |
| 53 | ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE | IOCL   | 05/2016 | 01/2021      | 10/2021         | 348                       | 9            |
| 54 | LPG TERMINAL AT KOCHI                                                                               | IOCL   | 10/2015 | 10/2017      | 03/2019         | 607.06                    | 17           |
| 55 | DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY                                     | IOCL   | 03/2014 | 09/2017      | 03/2019         | 3076                      | 18           |
| 56 | POLYPROPYLENE PLANT AT PARADIP REFINERY                                                             | IOCL   | 03/2014 | 09/2017      | 12/2018         | 3150                      | 15           |
| 57 | PARADIP LPG IMPORT FACILITY                                                                         | IOCL   | 01/2015 | 07/2018      | 10/2020         | 690                       | 27           |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( DECEMBER 2018 )

| Sn | Project                                                                                         | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|----|-------------------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 58 | NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY                             | ONGC   | 08/2015 | 03/2019         | 05/2020            | 2818.88                         | 14              |
| 59 | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)                          | ONGC   | 06/2010 | 01/2014         | 11/2019            | 202.94                          | 70              |
| 60 | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)                         | ONGC   | 03/2011 | 05/2013         | 03/2019            | 861.79                          | 70              |
| 61 | INTEGRATED DEVELOPMENT OF B-127 FIELDS                                                          | ONGC   | 12/2011 | 03/2015         | 12/2019            | 2059.63                         | 57              |
| 62 | URAN CHAKAN SHIKRAPUR LPG PIPELINE                                                              | HPCL   | 12/2009 | 10/2014         | 02/2019            | 309.81                          | 52              |
| 63 | ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA | ONGC   | 01/2015 | 12/2017         | 03/2020            | 4619.94                         | 27              |
| 64 | LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS                                | ONGC   | 12/2015 | 04/2018         | 05/2019            | 3190.69                         | 13              |
| 65 | KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II                                           | GAIL   | 06/2009 | 12/2012         | 06/2019            | 2915                            | 78              |
| 66 | ASSAM RENEWAL PROJECT FOR GROUP A                                                               | ONGC   | 03/2009 | 03/2013         | 03/2019            | 2465.15                         | 72              |
| 67 | SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN          | OIL    | 07/2011 | 03/2017         | 06/2019            | 352.56                          | 27              |
| 68 | PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY                             | BPCL   | 11/2014 | 08/2018         | 11/2019            | 4588.29                         | 15              |
| 69 | HALDIA LPG IMPORT FACILITY                                                                      | BPCL   | 03/2015 | 10/2018         | 06/2019            | 694                             | 8               |
| 70 | CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE                                                    | GAIL   | 04/2016 | 04/2018         | 03/2019            | 327.78                          | 11              |
| 71 | MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY                          | BPCL   | 02/2016 | 02/2020         | 10/2020            | 3313                            | 8               |
| 72 | KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT                                                      | ONGC   | 03/2016 | 06/2020         | 08/2021            | 34012                           | 14              |
| 73 | ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE              | IOCL   | 05/2016 | 12/2018         | 12/2020            | 4497                            | 24              |

## POWER

| Sn | Project                                                       | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|----|---------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 74 | 400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV)      | PGCIL  | 08/2008 | 02/2013         | 12/2018            | 771                             | 70              |
| 75 | WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) | SJVN   | 11/2016 | 11/2017         | 03/2019            | 330                             | 16              |
| 76 | GADARWARA SUPER THERMAL POWER PROJECT STAGE-I                 | NTPC   | 03/2013 | 09/2017         | 06/2019            | 11638.55                        | 21              |
| 77 | NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT            | PGCIL  | 02/2009 | 08/2013         | 03/2022            | 11130.19                        | 103             |
| 78 | EASTERN REGION STRENGTHENING SCHEME-V                         | PGCIL  | 10/2013 | 04/2016         | 02/2019            | 1364.52                         | 34              |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( DECEMBER 2018 )

| Sn  | Project                                                                                              | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|-----|------------------------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 79  | UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I                                                  | PGCIL  | 01/2014 | 04/2016         | 03/2019            | 374.63                          | 35              |
| 80  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX                                                    | PGCIL  | 02/2014 | 06/2016         | 03/2019            | 539.82                          | 33              |
| 81  | PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)                                                           | CVPPPL | 10/2014 | 04/2020         | 10/2023            | 8112.12                         | 42              |
| 82  | TANDA TPP STAGE-II (2X660 MW)                                                                        | NTPC   | 09/2014 | 03/2019         | 09/2019            | 9188.98                         | 6               |
| 83  | DARLIPALLI STPP STAGE-I (2X800 MW)                                                                   | NTPC   | 02/2014 | 08/2018         | 06/2019            | 12532.44                        | 10              |
| 84  | NORTH KARANPURA STPP (3X660 MW)                                                                      | NTPC   | 02/2014 | 02/2019         | 10/2020            | 14366.58                        | 20              |
| 85  | RAMMAM-III HEPP (3X40 MW)                                                                            | NTPC   | 09/2014 | 09/2019         | 02/2022            | 1381.84                         | 29              |
| 86  | TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP                                                 | PGCIL  | 01/2015 | 03/2018         | 02/2019            | 268.8                           | 11              |
| 87  | TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)                                   | PGCIL  | 01/2015 | 10/2017         | 09/2019            | 871.62                          | 23              |
| 88  | SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII                                                      | PGCIL  | 01/2015 | 07/2017         | 06/2019            | 203.28                          | 23              |
| 89  | ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO | PGCIL  | 03/2015 | 03/2018         | 03/2019            | 197.4                           | 12              |
| 90  | EASTERN REGION STRENGTHENING SCHEME-XII                                                              | PGCIL  | 05/2014 | 11/2016         | 06/2019            | 522.29                          | 31              |
| 91  | AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B                                             | PGCIL  | 03/2014 | 03/2016         | 02/2019            | 155.57                          | 35              |
| 92  | TAPOVAN-VISHNUGAD HEP (4X130MW)                                                                      | NTPC   | 11/2006 | 03/2013         | 12/2020            | 2978.48                         | 93              |
| 93  | BONGAIGAON THERMAL POWER PROJECT                                                                     | NTPC   | 01/2008 | 09/2011         | 01/2019            | 4375.35                         | 88              |
| 94  | TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH            | PGCIL  | 06/2014 | 03/2018         | 06/2019            | 5151.37                         | 15              |
| 95  | EASTERN REGION STRENGTHENING SCHEME - IX                                                             | PGCIL  | 02/2014 | 02/2016         | 03/2019            | 196.58                          | 37              |
| 96  | CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)                  | PGCIL  | 03/2015 | 05/2017         | 06/2019            | 1394.52                         | 25              |
| 97  | DHUKWAN SMALL HYDRO PROJECT                                                                          | THDCIL | 05/2011 | 02/2014         | 03/2019            | 195.42                          | 61              |
| 98  | BRBCL-NABINAGAR TPP- JV (4X250 MW)                                                                   | NTPC   | 01/2007 | 05/2014         | 05/2019            | 5353                            | 60              |
| 99  | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT                                     | SJVN   | 05/2015 | 12/2016         | 03/2019            | 436.68                          | 27              |
| 100 | GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B                                       | PGCIL  | 04/2015 | 04/2018         | 02/2019            | 3705.61                         | 10              |
| 101 | TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B                                            | PGCIL  | 07/2015 | 11/2017         | 01/2019            | 307.18                          | 14              |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( DECEMBER 2018 )

| Sn  | Project                                                                                              | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|-----|------------------------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 102 | VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT                                                           | THDCIL | 08/2008 | 06/2013         | 12/2021            | 2491.58                         | 102             |
| 103 | SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV                                                        | PGCIL  | 12/2011 | 08/2014         | 02/2019            | 297.33                          | 54              |
| 104 | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT              | PGCIL  | 05/2017 | 09/2018         | 06/2019            | 175.64                          | 9               |
| 105 | NPGCPL-NABINAGAR STPP - JV (3X660 MW)                                                                | NTPC   | 01/2013 | 01/2018         | 05/2020            | 12964.6                         | 28              |
| 106 | MUNPL-MEJA TPP - JV (2X660 MW)                                                                       | NTPC   | 04/2012 | 12/2016         | 08/2019            | 9750.89                         | 32              |
| 107 | PARBATI HEP (4X200 MW) (NHPC) II                                                                     | NHPC   | 09/2002 | 09/2009         | 12/2021            | 3919.59                         | 147             |
| 108 | WESTERN REGION STRENGTHENING SCHEME-V                                                                | PGCIL  | 12/2007 | 09/2010         | 02/2019            | 477.69                          | 101             |
| 109 | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT                                           | PGCIL  | 10/2008 | 10/2012         | 06/2019            | 4824.12                         | 80              |
| 110 | KUNADANKULAM APP TRANS SYSTEM (PGCIL)                                                                | PGCIL  | 05/2005 | 11/2008         | 03/2019            | 1779.29                         | 124             |
| 111 | BARH STPP(3X660MW) NTPC                                                                              | NTPC   | 02/2005 | 01/2011         | 04/2021            | 8692.97                         | 123             |
| 112 | SOLAPUR STPP                                                                                         | NTPC   | 03/2012 | 11/2016         | 03/2019            | 9395.18                         | 28              |
| 113 | LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)                                                | NTPC   | 12/2012 | 06/2017         | 06/2019            | 11846                           | 24              |
| 114 | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW)                                               | PGCIL  | 01/2016 | 03/2017         | 01/2019            | 305.04                          | 22              |
| 115 | TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR | PGCIL  | 03/2016 | 01/2018         | 09/2019            | 808.63                          | 20              |
| 116 | EASTERN REGION STRENGTHENING SCHEME-XV                                                               | PGCIL  | 04/2016 | 04/2018         | 01/2020            | 454.11                          | 21              |
| 117 | WESTERN REGION STRENGTHENING SCHEME-XVI                                                              | PGCIL  | 07/2016 | 07/2018         | 02/2019            | 150.99                          | 7               |
| 118 | KAMENG HYDROELECTRIC PROJECT (NEEPCO)                                                                | NEEPCO | 12/2004 | 12/2009         | 03/2019            | 2496.9                          | 111             |
| 119 | TEHRI PUMPED STORAGE PLANT(1000MW)                                                                   | THDCIL | 07/2006 | 02/2016         | 05/2021            | 1657                            | 63              |
| 120 | SYSTEM STRENGTHENING XIII OF SR GRID                                                                 | PGCIL  | 10/2011 | 06/2014         | 03/2019            | 487.49                          | 57              |
| 121 | NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES                   | PGCIL  | 12/2014 | 12/2018         | 12/2019            | 5111.33                         | 12              |
| 122 | COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P        | PGCIL  | 12/2014 | 12/2018         | 12/2019            | 4754.42                         | 12              |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( DECEMBER 2018 )

## RAILWAYS

| Sn  | Project                                                                                      | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|-----|----------------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 123 | KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)                                                | SWR    | 03/1996 | 03/2017         | 03/2020            | 644.78                          | 36              |
| 124 | CHHINDWARA-MANDLA FORT GC                                                                    | SECR   | 03/2011 | 03/2012         | 03/2020            | 556.54                          | 96              |
| 125 | PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM | ECR    | 11/2001 | 02/2016         | 03/2021            | 624.47                          | 61              |
| 126 | MUZAFFARPUR SAGALI DOUBLING 100.60 KM                                                        | ECR    | 04/2016 | 03/2021         | 03/2022            | 731.64                          | 12              |
| 127 | SAGALI VALMIKINAGAR DOUBLING 109.7 KM                                                        | ECR    | 04/2016 | 03/2021         | 03/2022            | 744.04                          | 12              |
| 128 | SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.              | NER    | 04/2016 | 03/2014         | 04/2021            | 1177.96                         | 85              |
| 129 | KIUL - GAYA DOUBLING PROJECT                                                                 | ECR    | 12/2015 | 03/2020         | 10/2021            | 1200.2                          | 19              |
| 130 | RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE                             | ECR    | 12/2015 | 03/2020         | 10/2021            | 1491.47                         | 19              |
| 131 | KATNI - SINGRAULI DOUBLING PROJECT                                                           | WCR    | 12/2015 | 03/2020         | 10/2021            | 1763.93                         | 19              |
| 132 | MANMAD - JALGAON - 3RD LINE (160 KM)                                                         | CR     | 02/2016 | 03/2022         | 03/2023            | 1035.16                         | 12              |
| 133 | GUNTUR-GUNTAKAL                                                                              | SCR    | 04/2016 | 03/2022         | 03/2023            | 3631                            | 12              |
| 134 | OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM                                        | SR     | 10/2013 | 04/2014         | 03/2020            | 187.26                          | 71              |
| 135 | BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL                                    | SER    | 04/1998 | 03/2003         | 03/2030            | 1027.4                          | 324             |
| 136 | LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC                                                  | RVNL   | 04/2011 | 03/2019         | 03/2020            | 927.01                          | 12              |
| 137 | MAU-GHAZIPUR-TARIGHAT NEW LINE                                                               | RVNL   | 04/2015 | 03/2023         | 12/2024            | 1765.92                         | 21              |
| 138 | RISHIKESH - KARNAPRAYAG NEW LINE                                                             | RVNL   | 04/2011 | 12/2024         | 03/2026            | 16216                           | 15              |
| 139 | BANASPANI- JAKHPURA - DOUBLING                                                               | RVNL   | 03/2009 | 03/2019         | 03/2021            | 942.95                          | 24              |
| 140 | RAMNA - SINGRAULI DOUBLING                                                                   | ECR    | 08/2015 | 03/2020         | 03/2021            | 2436.21                         | 12              |
| 141 | KARAILA ROAD - SHAKTINAGAR DOUBLING                                                          | ECR    | 08/2015 | 03/2019         | 12/2019            | 528.57                          | 9               |
| 142 | MULTI MODAL LOGISTICS PARK AT KATHUWAS                                                       | CCOI   | 01/2011 | 03/2018         | 12/2019            | 493.17                          | 21              |
| 143 | MULTI MODAL LOGISTICS PARK AT VARNAMA                                                        | CCOI   | 10/2013 | 03/2019         | 12/2019            | 343                             | 9               |
| 144 | NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR                      | NFR    | 04/1983 | 03/2019         | 03/2020            | 297.32                          | 12              |
| 145 | KOTLPALLI-NARASAPUR (NL) (SCR)                                                               | SCR    | 12/2001 | 03/2009         | 03/2023            | 1045.2                          | 168             |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( DECEMBER 2018 )

| Sn  | Project                                                                                | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|-----|----------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 146 | HARIDASPUR-PARADEEP(NL)                                                                | RVNL   | 04/1996 | 12/2017         | 03/2020            | 1185.64                         | 27              |
| 147 | SUKINDA ROAD - ANGUL (NL)(ECOR)                                                        | RVNL   | 04/1998 | 02/2015         | 12/2021            | 1202.7                          | 82              |
| 148 | KHURDA ROAD - BARANG 3RD LINE (DL)<br>(ECOR)                                           | RVNL   | 04/2000 | 03/2009         | 02/2019            | 133.41                          | 119             |
| 149 | TALCHER-BIMALAGARH(NL)(ECOR)                                                           | ECOR   | 04/2005 | 06/2021         | 03/2023            | 810.78                          | 21              |
| 150 | BHAIRABI SAIRONG, NL, NEFR                                                             | NFR    | 04/2008 | 03/2014         | 12/2020            | 2393.47                         | 81              |
| 151 | MANSI-PURNIA (EXTENSION OF MANSI-<br>SAHARSA) GAN ECR                                  | ECR    | 04/1996 | 03/2012         | 03/2020            | 477.88                          | 96              |
| 152 | MANOHARABAD-KOTHPALL NEW LINE(SCR)                                                     | SCR    | 04/2006 | 03/2010         | 03/2022            | 1160.48                         | 144             |
| 153 | OBULAVARIPALLE-KRISHNAPATNAM(RVNL)                                                     | RVNL   | 07/2006 | 03/2008         | 03/2020            | 732.81                          | 144             |
| 154 | NEW WORK FOR CONSTRUCTION OF METRO<br>RAILWAY FROM JOKA TO BINOY BADAL<br>DINESH BAGH. | RVNL   | 04/2010 | 03/2016         | 03/2025            | 2913.51                         | 108             |
| 155 | JAIPUR - RINGUS - CHURU AND SIKAR -<br>LOHARU GUAGE CONVERSION (NWR)                   | NWR    | 04/2008 | 03/2014         | 03/2019            | 653.19                          | 60              |
| 156 | SONDALIA-CHAMPAPUKUR DOUBLING WITH<br>NEW MM FOR BIRA-CHAKIA NL                        | ER     | 04/2010 | 03/2016         | 03/2020            | 277.28                          | 48              |
| 157 | BAGALKOT-KUDACHI NL                                                                    | SWR    | 04/2010 | 03/2016         | 12/2023            | 986.3                           | 93              |
| 158 | KAZIPET-VIJAYAWADA 3RD LINE WITH<br>ELECTRIFICATION                                    | SCR    | 04/2012 | 03/2023         | 03/2024            | 1856.95                         | 12              |
| 159 | SHIMOGA-HARIHAR NL                                                                     | SWR    | 04/2011 | 03/2016         | 03/2024            | 832.47                          | 96              |
| 160 | NADIKUDE-SRI KALAHASTI                                                                 | SCR    | 04/2011 | 03/2021         | 03/2022            | 2288.7                          | 12              |
| 161 | KADAPA-BANGALORE (NL), KADAPA-<br>PENDLIMARRI PH-I                                     | SCR    | 04/2008 | 03/2014         | 03/2023            | 2132.77                         | 108             |
| 162 | GADAG-WADI NL                                                                          | SWR    | 04/2013 | 12/2018         | 12/2024            | 2841.84                         | 72              |
| 163 | MARIKUPPAM - KUPPAM                                                                    | SWR    | 04/2012 | 03/2016         | 12/2023            | 279.54                          | 93              |
| 164 | BELAPUR-SEAWOOD-URAN ELECTRIFIED<br>DOUBLE LINE(MTP)                                   | M RTP  | 03/1996 | 03/2004         | 03/2020            | 495.44                          | 192             |
| 165 | MANDARHILL-DUMKA-RAMPURHAT (NL), ER                                                    | ER     | 04/1995 | 03/2016         | 03/2020            | 1125.89                         | 48              |
| 166 | LALITPUR-SATNA-REWA-SINGRULI NL,<br>(NCR)                                              | WCR    | 09/1998 | 05/2008         | 03/2023            | 247.66                          | 178             |
| 167 | JAYANAGAR-DARBHANGA-NARKATIA<br>GANJ(GC), ECR                                          | ECR    | 04/1997 | 03/2012         | 03/2020            | 324.73                          | 96              |
| 168 | NEW MAYNAGURI TO JOGIGHOPA VIA<br>CHANGRABANDHA (NL), NEFR                             | NFR    | 04/2000 | 12/2008         | 03/2019            | 1180.19                         | 123             |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( DECEMBER 2018 )

| Sn  | Project                                                                                          | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|-----|--------------------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 169 | KHURDA ROAD-BOLANGIR(NL)ECOR                                                                     | ECOR   | 04/1994 | 03/2009         | 06/2021            | 2923.13                         | 147             |
| 170 | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)                                                              | NFR    | 04/2003 | 03/2011         | 03/2020            | 4454.17                         | 108             |
| 171 | EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP                                             | MRTTP  | 04/2006 | 06/2013         | 03/2019            | 495.74                          | 69              |
| 172 | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR                                  | NFR    | 09/2006 | 03/2019         | 03/2020            | 385.2                           | 12              |
| 173 | NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR                                         | NFR    | 09/2006 | 03/2019         | 03/2020            | 532.87                          | 12              |
| 174 | NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)                                   | NFR    | 04/2006 | 03/2015         | 10/2021            | 2326.52                         | 79              |
| 175 | MUMBAI URBAN TRANSPORT PROJECT PHASE-II                                                          | MRTTP  | 04/2008 | 03/2014         | 03/2019            | 5300                            | 60              |
| 176 | AGARTALA SABROOM, NL, NEFR                                                                       | NFR    | 04/2008 | 03/2014         | 03/2019            | 1142                            | 60              |
| 177 | SEVOK RANGPO, NEFR                                                                               | NFR    | 04/2008 | 12/2015         | 03/2020            | 1339.48                         | 51              |
| 178 | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR                                                              | NR     | 03/1995 | 11/2002         | 03/2021            | 2500                            | 220             |
| 179 | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL                               | RVNL   | 04/1995 | 12/2012         | 03/2022            | 631.78                          | 111             |
| 180 | SALKA ROAD -ANUPNAGAR LINE DOUBLING                                                              | RVNL   | 09/2006 | 03/2010         | 12/2019            | 383.54                          | 117             |
| 181 | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)     | RVNL   | 04/2010 | 03/2016         | 03/2025            | 3951.98                         | 108             |
| 182 | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) | RVNL   | 04/2010 | 03/2014         | 12/2025            | 2298.42                         | 141             |
| 183 | MUNEERABAD-MAHABOONNAGAR(NL),SCR                                                                 | SCR    | 04/1997 | 03/2000         | 03/2019            | 1723                            | 228             |
| 184 | BANGLORE - SATYAMANGALAM (NL)(SWR)                                                               | SWR    | 04/1996 | 03/2002         | 03/2024            | 1382.78                         | 264             |
| 185 | BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)                                         | WR     | 04/2008 | 03/2012         | 03/2019            | 318.24                          | 84              |
| 186 | VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)                                             | RVNL   | 03/2012 | 03/2020         | 03/2022            | 1503.71                         | 24              |
| 187 | SAMBALPUR-TALCHER DOUBLING                                                                       | ECOR   | 03/2011 | 02/2019         | 03/2021            | 1111.99                         | 25              |
| 188 | RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND                                            | SER    | 04/2012 | 12/2016         | 09/2019            | 148.77                          | 33              |
| 189 | RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)    | WR     | 04/1994 | 03/2019         | 03/2022            | 320.66                          | 36              |
| 190 | DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA                                                       | SER    | 04/2010 | 03/2015         | 03/2024            | 651                             | 108             |
| 191 | DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING                                                         | SER    | 04/2010 | 12/2015         | 02/2019            | 309.44                          | 38              |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( DECEMBER 2018 )

| Sn  | Project                                                                                            | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|-----|----------------------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 192 | AGARTALA-AKHAURA NL                                                                                | NFR    | 04/2012 | 03/2020         | 10/2022            | 569.63                          | 31              |
| 193 | MULTI MODAL TRANSPORT SYSTEM(MMTS)<br>PHASE-II HYDERABAD                                           | RVNL   | 04/2012 | 03/2016         | 12/2020            | 632.68                          | 57              |
| 194 | JARAPADA - BUDHAPANK WITH FLY OVER AT<br>TALCHER ROAD 3RD AND 4TH LINE                             | ECOR   | 04/2015 | 11/2018         | 03/2021            | 701.61                          | 28              |
| 195 | BUDHAPANK - SALEGAON VIA RAJATGARH<br>3RD AND 4TH LINE.                                            | ECOR   | 04/2015 | 12/2018         | 03/2021            | 1172.92                         | 27              |
| 196 | BONDAMUNDA RANCHI DOUBLING                                                                         | SER    | 03/2016 | 03/2021         | 12/2021            | 1724.2                          | 9               |
| 197 | RUPSA BANGRIPOSI 90 KM WITH MM<br>FOR UPGRADATION FROM RUPSA BURAMARA<br>AND EXTENSION OF LINE FRO | SER    | 04/1995 | 12/2021         | 12/2024            | 524.43                          | 36              |
| 198 | VARANASI-MODHOSINGH-ALLAHABAD<br>DOUBLING                                                          | RVNL   | 04/2015 | 03/2022         | 12/2024            | 943.6                           | 33              |
| 199 | HUBLI- CHIKJAJUR                                                                                   | SWR    | 03/2015 | 03/2020         | 03/2021            | 1156.94                         | 12              |
| 200 | HOTGI-KUDGI-GADAG                                                                                  | SWR    | 03/2015 | 03/2019         | 03/2021            | 1614.59                         | 24              |
| 201 | HAJIPUR - BACHAWARA                                                                                | ECR    | 05/2015 | 03/2019         | 03/2020            | 678.54                          | 12              |
| 202 | HIMMATNAGAR - UDAIPUR GAUGE<br>CANVESSION (NWR)                                                    | NWR    | 04/2008 | 03/2015         | 06/2020            | 829.74                          | 63              |
| 203 | MULTI MODAL LOGISTICS PARK AT<br>KAKINADA                                                          | CCOI   | 08/2016 | 03/2019         | 12/2020            | 234.5                           | 21              |
| 204 | ETAH - KASGANJ - NEW LINE                                                                          | NER    | 04/2017 | 04/2017         | 04/2022            | 276.9                           | 60              |
| 205 | PILIBHIT - SHAHJAHANPUR GAUGE<br>CONVERSION                                                        | NER    | 04/2017 | 04/2017         | 10/2022            | 622.5                           | 66              |
| 206 | NANPARA - NEPALGANJ GAUGE CONVERSION.                                                              | NER    | 04/2017 | 04/2017         | 10/2022            | 150                             | 66              |
| 207 | MANDHANA - BRAHMAWART NEW LINE<br>PROJECT.                                                         | NER    | 04/1997 | 04/1999         | 03/2019            | 609.04                          | 239             |
| 208 | INDARA - DOHRIGHAT GAUGE CONVERSION.                                                               | NER    | 04/2016 | 04/2016         | 01/2022            | 213                             | 69              |
| 209 | TRANSMISSION LINE BETWEEN CHENNAI-<br>HOWRAH ROUTE (1662 KM)                                       | SR     | 02/2017 | 03/2024         | 03/2026            | 1567                            | 24              |

## ROAD TRANSPORT AND HIGHWAYS

| Sn  | Project                                                                                                    | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|-----|------------------------------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 210 | FOUR LANING OF EXISTING DIMAPUR<br>KOHIMA ROAD FROM DESIGN KM 152.490 TO<br>KM 166.700 (EXISTING KM 156.00 | NHIDCL | 03/2016 | 08/2016         | 08/2019            | 429.52                          | 36              |
| 211 | GURGAON - KOTPUTLI - JAIPUR (SIX<br>LANE)                                                                  | NHAI   | 02/2008 | 10/2011         | 03/2019            | 1673.7                          | 89              |
| 212 | FOUR LANING OF HOSPET - CHITRADURGA                                                                        | NHAI   | 03/2015 | 08/2018         | 04/2019            | 1388                            | 8               |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun



## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( DECEMBER 2018 )

| Sn  | Project                                                                                                    | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|-----|------------------------------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 213 | FOUR LANING OF GWALIOR-SHIVPURI                                                                            | NHAI   | 05/2013 | 11/2015         | 12/2018            | 1055                            | 37              |
| 214 | FOUR LANING OF AURANGABAD - YEDISHI                                                                        | NHAI   | 07/2015 | 01/2018         | 12/2018            | 1871.34                         | 11              |
| 215 | HARANGAJO TO MAIBANG (AS-23),<br>KM.126.450 TO KM.140.700                                                  | NHAI   | 12/2003 | 02/2009         | 12/2018            | 280                             | 118             |
| 216 | MAIBANG TO LUMDING (AS-25), KM.83.400<br>TO KM.111.000                                                     | NHAI   | 12/2003 | 04/2009         | 03/2019            | 199.81                          | 119             |
| 217 | HARIDWAR DEHRADUN APPROVED LENGTH 69                                                                       | NHAI   | 11/2011 | 10/2013         | 07/2019            | 478.51                          | 69              |
| 218 | PANVEL-INDAPUR                                                                                             | NHAI   | 12/2011 | 06/2014         | 06/2019            | 942.69                          | 60              |
| 219 | FOUR LANING OF PARWANOO -SOLAN                                                                             | NHAI   | 09/2015 | 03/2018         | 03/2019            | 934.46                          | 12              |
| 220 | FOUR LANING OF VILLUKURI KANNIYAKUMAR<br>ROAD OF KM 70.250 TO 96.700 AND<br>NAGERCOIL TO KAVALKINARU OF NH | NHAI   | 03/2016 | 07/2016         | 04/2019            | 641.17                          | 33              |
| 221 | REHABILITATION AND UP-GRADATION OF<br>BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-<br>I)                          | NHAI   | 07/2017 | 07/2017         | 11/2020            | 476.56                          | 40              |
| 222 | FOUR LANNING OF AP/TN BORDER TO<br>NALAGAMPALLI VILLAGE(KM 133.360 TO<br>172.00) OF NH-4 (NEW NH-40)       | NHAI   | 06/2017 | 06/2017         | 11/2019            | 648.33                          | 29              |
| 223 | FOUR LANNING BALANCE WORK FOR<br>BHOPAL-BIAORA SECTION OF NH-12 FROM<br>MUBARAKPUR TO BIAORA FROM KM 124.  | NHAI   | 10/2017 | 10/2017         | 01/2020            | 639.97                          | 27              |
| 224 | 4-LANNING OF THALSERRY -MAHE BYPASS                                                                        | NHAI   | 09/2017 | 09/2017         | 06/2020            | 1124.11                         | 33              |
| 225 | WIDENING AND STRENGTHENING OF NH-15<br>TO TWO LANES WITH PAVED SHOULDER FROM<br>EXISTING KM 173/0 TO KM 24 | MORTH  | 02/2015 | 03/2015         | 06/2019            | 383.4                           | 51              |
| 226 | BHOPAL-BIORA (4L) OF NH-12 IN MP                                                                           | NHDP   | 11/2011 | 05/2015         | 01/2020            | 704.26                          | 56              |
| 227 | GWALIOR-JHANSI, NH-75                                                                                      | NHAI   | 12/2003 | 12/2009         | 08/2020            | 604                             | 128             |
| 228 | QUAZIGUND-BANIHAL KM.220.00 TO<br>KM.188.00                                                                | NHAI   | 07/2010 | 07/2015         | 03/2019            | 1987                            | 44              |
| 229 | PATNA-MUZZAFFARPUR                                                                                         | NHAI   | 08/2010 | 02/2013         | 06/2019            | 671.3                           | 76              |
| 230 | TWO LANING OF TRICHY - KARAIKUDI AND<br>TRYCHI BYPASS                                                      | NHAI   | 05/2010 | 05/2013         | 12/2018            | 374                             | 67              |
| 231 | 2 LANING OF DINDIGUL - PERIGULAM<br>THENI- KUMILI                                                          | NHAI   | 09/2011 | 08/2013         | 12/2018            | 485                             | 64              |
| 232 | JORBAT - BARAPANI                                                                                          | NHAI   | 01/2011 | 01/2014         | 01/2019            | 536                             | 60              |
| 233 | 4-LANNING OF CHAPRA-HAJIPUR                                                                                | NHAI   | 01/2011 | 07/2013         | 06/2019            | 575                             | 71              |
| 234 | 2 LANNING OF MUZZAFFARPUR - SONBARSA                                                                       | NHAI   | 05/2011 | 11/2013         | 12/2018            | 511.54                          | 61              |
| 235 | KRISHNANAGAR-BERHAMPUR                                                                                     | NHAI   | 02/2012 | 07/2014         | 05/2019            | 702.16                          | 58              |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( DECEMBER 2018 )

| Sn  | Project                                                                                              | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|-----|------------------------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 236 | 2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM)                                          | NHAI   | 04/2012 | 04/2014         | 12/2019            | 624                             | 68              |
| 237 | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)                                                          | NHAI   | 05/2009 | 11/2011         | 06/2019            | 1108                            | 91              |
| 238 | WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50                                      | NHAI   | 05/2013 | 02/2014         | 06/2019            | 1348.2                          | 64              |
| 239 | SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM                                          | NHAI   | 02/2010 | 08/2012         | 03/2019            | 617                             | 79              |
| 240 | PUNE-SATARA(NH-4)                                                                                    | NHAI   | 10/2010 | 03/2013         | 06/2019            | 1724.55                         | 75              |
| 241 | CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM                                                       | NHAI   | 11/2010 | 05/2013         | 04/2019            | 1585                            | 71              |
| 242 | FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)                                    | NHAI   | 11/2013 | 11/2016         | 04/2019            | 1916.79                         | 29              |
| 243 | 4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9                                                | NHAI   | 04/2014 | 09/2016         | 06/2019            | 1266.6                          | 33              |
| 244 | SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46                              | NHAI   | 09/2011 | 12/2013         | 12/2018            | 1250                            | 60              |
| 245 | KANDLA - MUNDRA PORT                                                                                 | NHAI   | 01/2011 | 07/2013         | 12/2018            | 953.88                          | 65              |
| 246 | TIRUPATI - TIRUTHANI - CHENNAI                                                                       | NHAI   | 04/2011 | 10/2013         | 12/2018            | 571                             | 62              |
| 247 | VARANASI-AURANGABAD KM.786 TO KM.978.40                                                              | NHAI   | 09/2011 | 03/2014         | 12/2019            | 2848                            | 69              |
| 248 | PATNA-BAKTZARPUR KM.181.3 TO KM.231.95                                                               | NHAI   | 09/2011 | 03/2014         | 12/2018            | 574                             | 57              |
| 249 | PANIKHOLI-RIMOLI                                                                                     | NHAI   | 03/2012 | 09/2014         | 03/2019            | 1410                            | 54              |
| 250 | MUZAFFARNAGAR-HARIDWAR                                                                               | NHAI   | 09/2011 | 03/2013         | 12/2019            | 754                             | 81              |
| 251 | 4-LANING OF FARAKA-RAIGANJ                                                                           | NHAI   | 02/2011 | 08/2013         | 06/2019            | 1078.84                         | 70              |
| 252 | 4-LANING OF BRAHAMPORE-FARAKA                                                                        | NHAI   | 02/2011 | 08/2013         | 06/2020            | 998.79                          | 82              |
| 253 | 6-LANING OF DHANKUNI-KHARAGPUR SECTION                                                               | NHAI   | 04/2012 | 09/2014         | 05/2019            | 1396.18                         | 56              |
| 254 | 2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA | NHAI   | 11/2012 | 08/2016         | 02/2019            | 530.07                          | 30              |
| 255 | BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM  | NHAI   | 08/2014 | 04/2018         | 03/2019            | 822.9                           | 11              |
| 256 | 4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211                                                        | NHAI   | 01/2015 | 07/2017         | 12/2018            | 972.5                           | 17              |
| 257 | 4-LANING OF SOLAPUR - MAHARASHTRA/KARNATKA SECTION                                                   | NHAI   | 06/2014 | 11/2016         | 06/2019            | 923.04                          | 31              |
| 258 | 4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION                                                    | NHAI   | 05/2014 | 08/2016         | 03/2019            | 1655.01                         | 31              |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( DECEMBER 2018 )

| Sn  | Project                                                                                                    | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|-----|------------------------------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 259 | FOUR LANING OF YADGIRI - WARANGAL                                                                          | NHAI   | 12/2015 | 11/2018         | 07/2019            | 1423.96                         | 8               |
| 260 | FOUR LANING OF UDHAMBUR - RAMBAN<br>SECTION OF NH-1A                                                       | NHAI   | 12/2015 | 12/2018         | 10/2019            | 2136.97                         | 10              |
| 261 | FOUR LANING OF SIMGA - SARAGAON                                                                            | NHAI   | 12/2015 | 05/2018         | 06/2019            | 596.67                          | 13              |
| 262 | FOUR LANING OF GUNA TO BIAORA SECTION<br>OF NH-3 FROM KM 332.100 TO KM.<br>426.100 IN THE STATE OF MADHYA  | NHAI   | 06/2015 | 03/2016         | 03/2019            | 1012.9                          | 36              |
| 263 | FOUR LANING OF FORBESGANJ - JOGBANI                                                                        | NHAI   | 08/2015 | 04/2018         | 04/2020            | 322.09                          | 24              |
| 264 | FOUR LANING OF CHANDIGARH - KHARAR                                                                         | NHAI   | 10/2015 | 12/2017         | 04/2019            | 447.29                          | 16              |
| 265 | FOUR LANING FROM MPMAHARASHTRA BORDER<br>TO NAGPUR IC KAMPTEE KANOON AND<br>NAGPUR BYPASS                  | NHAI   | 04/2010 | 06/2012         | 12/2018            | 1170.52                         | 78              |
| 266 | FOUR / SIX LANING OF RAIPUR - SIMGA ( PKG-1)                                                               | NHAI   | 12/2015 | 04/2018         | 06/2019            | 726.67                          | 14              |
| 267 | DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)                                                                   | NHAI   | 12/2003 | 05/2008         | 02/2019            | 160                             | 129             |
| 268 | TWO LANE WITH PAVED SHOULDERS OF<br>BIJAPUR - GULBARGA - HONNABAD -<br>SECTION OF NH-218 ( NEW NH NO -50)  | NHAI   | 05/2015 | 09/2017         | 12/2018            | 709                             | 15              |
| 269 | TWO LANING WITH PAVED SHOULDER OF<br>KARAUJI - DHOLPUR                                                     | NHAI   | 09/2014 | 09/2016         | 03/2019            | 425.19                          | 30              |
| 270 | FOUR LANING OF MADURAI -<br>RAMANATHAPURAM (KM 5. TO KM 81) AND<br>TWO LANING WITH PS KM 81 TO KM 120      | NHAI   | 05/2015 | 11/2017         | 05/2019            | 1387.11                         | 18              |
| 271 | TWO LANING WITH PS OF NAGAPATTINAM -<br>THANJAVUR                                                          | NHAI   | 06/2015 | 12/2017         | 06/2019            | 563.92                          | 18              |
| 272 | PHALODI -JAISALMER SECTION OF NH-15<br>TO TWO/FOUR LANE WITH PS                                            | NHAI   | 09/2015 | 03/2018         | 01/2019            | 567.51                          | 10              |
| 273 | 2 LANING WITH PS OF GULABPURA -<br>UNIARA                                                                  | NHAI   | 10/2015 | 10/2017         | 01/2019            | 597                             | 15              |
| 274 | CONSTRUCTION OF NH-4B FROM KM.21.200<br>TO KM.27.270( D TO E SECTION) AND<br>FROM KM.0.000 TO KM.4.492 ( D | NHAI   | 09/2015 | 05/2018         | 03/2019            | 414.51                          | 10              |
| 275 | CONSTRUCTION OF KARALPHATA<br>INTERCHANGE FROM 3.600 TO KM 6.073<br>OF NH4B AND FROM 5.300 TO KM 7.422 (   | NHAI   | 10/2015 | 05/2018         | 05/2019            | 531.13                          | 12              |
| 276 | CONSTRUCTION OF GAVANPHATA<br>INTERCHANGE FROM 14.740 TO KM 15.894<br>( OLD SH -54) PKG-2                  | NHAI   | 10/2015 | 05/2018         | 04/2019            | 593.26                          | 11              |
| 277 | 4 LANING OF AMBALA - KAITHAL -<br>PACKAGE -1                                                               | NHAI   | 12/2015 | 06/2016         | 12/2018            | 602.95                          | 30              |
| 278 | 4 LANING OF AMBALA - KAITHAL -<br>PACKAGE -2                                                               | NHAI   | 01/2016 | 07/2018         | 03/2019            | 574.28                          | 8               |
| 279 | 6/8 LANING OF ROAD PORT CONNECTIVITY<br>JNPT PHASE II -CONSTRUCTION OF NH-348<br>- PKG3                    | NHAI   | 08/2015 | 05/2018         | 04/2019            | 505                             | 11              |
| 280 | 4 LANING OF NH-31D FROM GHOSHPUKUR -<br>SALSALABARI ( KM 0.00 TO KM . 83.785)                              | NHAI   | 12/2015 | 06/2018         | 05/2019            | 1083                            | 11              |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( DECEMBER 2018 )

| Sn  | Project                                                                                              | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|-----|------------------------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 281 | FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A                                                     | NHAI   | 12/2015 | 06/2019         | 12/2020            | 2168.66                         | 18              |
| 282 | SONAPUR TO GUWAHTI (AS-3)                                                                            | NHAI   | 12/2003 | 03/2008         | 01/2019            | 245                             | 130             |
| 283 | BRAHMPUTRA BRIDGE, NH NO-31                                                                          | NHAI   | 12/2003 | 04/2010         | 04/2019            | 217.61                          | 108             |
| 284 | NALBARI T BIJNI (AS-7)                                                                               | NHAI   | 12/2003 | 04/2008         | 03/2019            | 208                             | 131             |
| 285 | NALBARI TO BIJNI (AS-6)                                                                              | NHAI   | 12/2003 | 06/2008         | 04/2019            | 225                             | 130             |
| 286 | TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44                                 | NHAI   | 12/2015 | 05/2018         | 03/2019            | 479.2                           | 10              |
| 287 | TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA                                                | NHAI   | 08/2015 | 04/2019         | 10/2019            | 399.54                          | 6               |
| 288 | TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR                                               | NHAI   | 08/2015 | 04/2018         | 12/2018            | 516.13                          | 8               |
| 289 | 4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL                                         | NHAI   | 03/2016 | 03/2019         | 11/2020            | 870                             | 20              |
| 290 | FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH | NHAI   | 02/2016 | 08/2018         | 06/2019            | 707.82                          | 10              |
| 291 | FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K | NHAI   | 02/2016 | 07/2018         | 04/2019            | 641.17                          | 9               |
| 292 | 4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T | NHAI   | 04/2016 | 06/2018         | 04/2019            | 804.97                          | 10              |
| 293 | BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ                                                      | NHAI   | 05/2015 | 05/2017         | 06/2019            | 581.84                          | 25              |
| 294 | HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER                                                    | NHAI   | 09/2010 | 06/2018         | 03/2019            | 946                             | 9               |
| 295 | 4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500                                       | NHAI   | 08/2016 | 04/2019         | 11/2019            | 2016                            | 7               |
| 296 | FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA | NHAI   | 09/2016 | 08/2018         | 09/2019            | 767.03                          | 13              |
| 297 | 4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI | NHAI   | 11/2016 | 03/2019         | 09/2019            | 400.25                          | 6               |
| 298 | 4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT | NHAI   | 11/2016 | 03/2019         | 11/2019            | 446.17                          | 8               |
| 299 | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2  | NHAI   | 03/2017 | 03/2020         | 11/2020            | 1373.28                         | 8               |
| 300 | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 | NHIDCL | 03/2016 | 08/2016         | 08/2019            | 373.07                          | 36              |
| 301 | CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120                                | NHIDCL | 12/2016 | 01/2017         | 01/2020            | 138.93                          | 36              |
| 302 | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 | NHIDCL | 03/2016 | 08/2016         | 08/2019            | 396.52                          | 36              |
| 303 | 4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)                                        | NHAI   | 03/2017 | 03/2017         | 11/2020            | 1059.73                         | 44              |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( DECEMBER 2018 )

## SHIPPING AND PORTS

| Sn  | Project                                                                                              | Agency         | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|-----|------------------------------------------------------------------------------------------------------|----------------|---------|--------------|-----------------|---------------------------|--------------|
| 304 | CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT                                                  | KPL            | 03/2016 | 12/2017      | 05/2020         | 600                       | 29           |
| 305 | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB | MUMBAI PORT TR | 01/2007 | 12/2010      | 12/2018         | 366.39                    | 96           |
| 306 | ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)                                         | PORT TRUST     | 10/2002 | 03/2006      | 02/2019         | 150                       | 155          |

## STEEL

| Sn  | Project                                                        | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|-----|----------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 307 | ADDITIONAL WATER STORAGE RESERVOIR(KBR-II)                     | RINL   | 07/2015 | 07/2018      | 01/2019         | 465.85                    | 6            |
| 308 | FORGED WHEEL PLANT                                             | RINL   | 04/2014 | 09/2018      | 03/2019         | 1682.85                   | 6            |
| 309 | NEW SINTER PLANT AT BOKARO STEEL PLANT                         | SAIL   | 03/2015 | 10/2017      | 06/2020         | 1034.01                   | 32           |
| 310 | INSTALLATION OF NEW HOT STRIP MILL AT RSP                      | SAIL   | 04/2015 | 04/2018      | 05/2019         | 3127.3                    | 13           |
| 311 | NMDC INTEGRATED STEEL PLANT                                    | NMDC   | 01/2010 | 05/2015      | 06/2019         | 15525                     | 49           |
| 312 | MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT | SAIL   | 05/2015 | 12/2017      | 06/2019         | 1154.18                   | 18           |
| 313 | COKE OVEN BATTERY-5                                            | RINL   | 12/2011 | 12/2017      | 09/2019         | 2858                      | 21           |
| 314 | REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL                    | SAIL   | 11/2016 | 06/2019      | 06/2020         | 262.87                    | 12           |
| 315 | CENTRAL DISPATCH YARD                                          | RINL   | 08/2015 | 08/2018      | 02/2019         | 320.66                    | 6            |

## TELECOMMUNICATIONS

| Sn  | Project                      | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|-----|------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 316 | NETWORK FOR SPECTRUM         | DOT    | 03/2012 | 07/2015      | 05/2020         | 13334                     | 58           |
| 317 | MAHARASHTRA CORE (LOT1)      | BSNL   | 08/2017 | 04/2018      | 02/2019         | 167.68                    | 10           |
| 318 | MADHYA PRADESH ACCESS (LOT1) | BSNL   | 08/2017 | 05/2018      | 02/2019         | 215.3                     | 9            |

## URBAN DEVELOPMENT

| Sn  | Project                               | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|-----|---------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 319 | RESIDENTIAL QUATERS FOR HAL, BANGLORE | CPWD   | 12/2016 | 02/2020      | 09/2020         | 246.31                    | 7            |
| 320 | NSG AT KOLKATA                        | CPWD   | 10/2014 | 04/2018      | 07/2019         | 162.88                    | 15           |
| 321 | BANGALORE METRO RAIL PROJECT PHASE-2  | BMRL   | 02/2014 | 02/2019      | 03/2020         | 26405.14                  | 13           |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( DECEMBER 2018 )

| Sn  | Project                                                                                               | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|-----|-------------------------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 322 | CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCPR | HSCL   | 04/2014 | 09/2017         | 12/2018            | 151.33                          | 15              |
| 323 | IRRIGATION WORK OF BAGMATI                                                                            | HSCL   | 10/2005 | 03/2015         | 03/2021            | 956                             | 72              |
| 324 | CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII                                      | HSCL   | 02/2014 | 12/2016         | 12/2018            | 787.29                          | 24              |
| 325 | CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI      | CPWD   | 06/2015 | 04/2019         | 06/2020            | 197.33                          | 14              |
| 326 | CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB                      | CPWD   | 02/2014 | 05/2017         | 03/2019            | 388                             | 22              |
| 327 | CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA                        | CPWD   | 02/2014 | 08/2016         | 03/2019            | 156.57                          | 31              |
| 328 | DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND                                       | CPWD   | 11/2012 | 11/2014         | 02/2019            | 270.83                          | 51              |
| 329 | 2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD                                              | CPWD   | 09/2012 | 03/2016         | 04/2020            | 171.86                          | 49              |
| 330 | NIT ACADEMIC BUILDING AT IMPHAL MANIPUR                                                               | CPWD   | 02/2014 | 03/2015         | 11/2019            | 216.69                          | 56              |
| 331 | CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA                                                 | CPWD   | 01/2010 | 10/2012         | 03/2019            | 165.23                          | 77              |
| 332 | KOCHI METRO RAIL PROJECT                                                                              | KMRCL  | 07/2012 | 07/2017         | 12/2019            | 5181.79                         | 29              |
| 333 | NAGPUR METRO RAIL                                                                                     | NMRCL  | 08/2014 | 03/2018         | 12/2019            | 8680                            | 21              |
| 334 | MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)                                                             | MMRCL  | 07/2013 | 01/2015         | 05/2020            | 23136                           | 64              |
| 335 | DELHI MRTS PHASE-III                                                                                  | MMRC   | 09/2011 | 03/2016         | 05/2019            | 38585                           | 38              |
| 336 | CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA           | CPWD   | 02/2016 | 06/2017         | 06/2020            | 496.18                          | 36              |
| 337 | CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA   | CPWD   | 12/2008 | 12/2013         | 10/2019            | 114.26                          | 70              |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( DECEMBER 2018 )

**ATOMIC ENERGY**

| Sn | Project                                           | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|----|---------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 1  | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) | BHAVNI | 09/2003 | 09/2010      | 3492                     | 6100                        | 2608                    |
| 2  | KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4           | NPCIL  | 10/2009 | 12/2015      | 11459                    | 16580                       | 5121                    |

**CIVIL AVIATION**

| Sn | Project                                                                    | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|----|----------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 3  | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR | AAI    | 10/2013 | 09/2018      | 314.61                   | 441.33                      | 126.72                  |

**COAL**

| Sn | Project                                                 | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|----|---------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 4  | JAGANNATHPOR OCP(3.00MTY)                               | SECL   | 09/2008 | 03/2015      | 152.43                   | 459.49                      | 307.06                  |
| 5  | NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI | NCL    | 10/2007 | 03/2012      | 259.4                    | 486.57                      | 227.17                  |
| 6  | RCE OF INDARAM OCP(1.20 MTPA)                           | SCCL   | 07/2011 | 03/2015      | 162.76                   | 349.28                      | 186.52                  |
| 7  | SHANTIKHANI LONGWALL PROJ-SCCL                          | SCCL   | 10/2006 | 03/2012      | 249.03                   | 448.86                      | 199.83                  |
| 8  | BHANEGAON OC                                            | WCL    | 02/2015 | 03/2023      | 187.94                   | 409.68                      | 221.74                  |

**HEAVY INDUSTRY**

| Sn | Project                                                             | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|----|---------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 9  | NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) | NATIS  | 04/2011 | 09/2011      | 1718                     | 3827.3                      | 2109.3                  |

**PETROLEUM**

| Sn | Project                                                                                | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|----|----------------------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 10 | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR                                           | ISPRL  | 01/2006 | 01/2012      | 993                      | 1693                        | 700                     |
| 11 | LPG TERMINAL AT KOCHI                                                                  | IOCL   | 10/2015 | 10/2017      | 607.06                   | 714.25                      | 107.19                  |
| 12 | DEVELOPMENT PLAN OF CBM - BOKARO BLOCK                                                 | ONGC   | 12/2015 | 03/2023      | 658.62                   | 910.23                      | 251.61                  |
| 13 | PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY                    | BPCL   | 11/2014 | 08/2018      | 4588.29                  | 5245.96                     | 657.67                  |
| 14 | UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE | OIL    | 09/2012 | 03/2015      | 871.35                   | 1200                        | 328.65                  |
| 15 | URAN CHAKAN SHIKRAPUR LPG PIPELINE                                                     | HPCL   | 12/2009 | 10/2014      | 309.81                   | 723.4                       | 413.59                  |
| 16 | INTEGRATED DEVELOPMENT OF B-127 FIELDS                                                 | ONGC   | 12/2011 | 03/2015      | 2059.63                  | 2665.65                     | 606.02                  |
| 17 | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)                | ONGC   | 03/2011 | 05/2013      | 861.79                   | 1577.15                     | 715.36                  |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( DECEMBER 2018 )

| Sn           | Project                                                                                             | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|--------------|-----------------------------------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 18           | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)                              | ONGC   | 06/2010 | 01/2014      | 202.94                   | 330.35                      | 127.41                  |
| 19           | DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY                                     | IOCL   | 03/2014 | 09/2017      | 3076                     | 4190                        | 1114                    |
| 20           | PARADIP HYDERABAD PIPELINE                                                                          | IOCL   | 01/2015 | 12/2020      | 2321                     | 3338                        | 1017                    |
| <b>POWER</b> |                                                                                                     |        |         |              |                          |                             |                         |
| Sn           | Project                                                                                             | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
| 21           | PARBATI HEP (4X200 MW) (NHPC) II                                                                    | NHPC   | 09/2002 | 09/2009      | 3919.59                  | 9394.8                      | 5475.21                 |
| 22           | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT                                          | PGCIL  | 10/2008 | 10/2012      | 4824.12                  | 5071.94                     | 247.82                  |
| 23           | WESTERN REGION STRENGTHENING SCHEME-V                                                               | PGCIL  | 12/2007 | 09/2010      | 477.69                   | 738.48                      | 260.79                  |
| 24           | SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)                                                             | NHPC   | 09/2003 | 09/2010      | 6285.33                  | 19496.34                    | 13211.01                |
| 25           | GADARWARA SUPER THERMAL POWER PROJECT STAGE-I                                                       | NTPC   | 03/2013 | 09/2017      | 11638.55                 | 12865.92                    | 1227.37                 |
| 26           | EASTERN REGION STRENGTHENING SCHEME-V                                                               | PGCIL  | 10/2013 | 04/2016      | 1364.52                  | 1891.41                     | 526.89                  |
| 27           | KUDGI STPP STAGE 1                                                                                  | NTPC   | 01/2012 | 01/2017      | 15166.19                 | 16934.65                    | 1768.46                 |
| 28           | TRIPURA GAS BASED POWER PROJECT                                                                     | NEEPCO | 07/2009 | 07/2013      | 421.01                   | 1078.31                     | 657.3                   |
| 29           | BARH STPP(3X660MW) NTPC                                                                             | NTPC   | 02/2005 | 01/2011      | 8692.97                  | 15095.67                    | 6402.7                  |
| 30           | KUNADANKULAM APP TRANS SYSTEM (PGCIL)                                                               | PGCIL  | 05/2005 | 11/2008      | 1779.29                  | 2187.32                     | 408.03                  |
| 31           | SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV                                                       | PGCIL  | 12/2011 | 08/2014      | 297.33                   | 534.02                      | 236.69                  |
| 32           | SYSTEM STRENGTHENING XIII OF SR GRID                                                                | PGCIL  | 10/2011 | 06/2014      | 487.49                   | 639.46                      | 151.97                  |
| 33           | TEHRI PUMPED STORAGE PLANT(1000MW)                                                                  | THDCIL | 07/2006 | 02/2016      | 1657                     | 4401.9                      | 2744.9                  |
| 34           | COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGY PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L | PGCIL  | 09/2011 | 09/2014      | 1940.13                  | 2702.65                     | 762.52                  |
| 35           | KAMENG HYDROELECTRIC PROJECT (NEEPCO)                                                               | NEEPCO | 12/2004 | 12/2009      | 2496.9                   | 6179.96                     | 3683.06                 |
| 36           | VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT                                                          | THDCIL | 08/2008 | 06/2013      | 2491.58                  | 4105.3                      | 1613.72                 |
| 37           | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT                                    | SJVN   | 05/2015 | 12/2016      | 436.68                   | 602.44                      | 165.76                  |
| 38           | NPGCPL-NABINAGAR STPP - JV (3X660 MW)                                                               | NTPC   | 01/2013 | 01/2018      | 12964.6                  | 13731.26                    | 766.66                  |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning



## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( DECEMBER 2018 )

| Sn | Project                                                                                           | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|----|---------------------------------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 39 | BRBCL-NABINAGAR TPP- JV (4X250 MW)                                                                | NTPC   | 01/2007 | 05/2014      | 5353                     | 7998                        | 2645                    |
| 40 | NORTH KARANPURA STPP (3X660 MW)                                                                   | NTPC   | 02/2014 | 02/2019      | 14366.58                 | 15164.05                    | 797.47                  |
| 41 | DARLIPALLI STPP STAGE-I (2X800 MW)                                                                | NTPC   | 02/2014 | 08/2018      | 12532.44                 | 13740.53                    | 1208.09                 |
| 42 | BONGAIGAON THERMAL POWER PROJECT                                                                  | NTPC   | 01/2008 | 09/2011      | 4375.35                  | 8150                        | 3774.65                 |
| 43 | TAPOVAN-VISHNUGAD HEP (4X130MW)                                                                   | NTPC   | 11/2006 | 03/2013      | 2978.48                  | 3846.3                      | 867.82                  |
| 44 | 400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV)                                          | PGCIL  | 08/2008 | 02/2013      | 771                      | 1624                        | 853                     |
| 45 | NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES                | PGCIL  | 12/2014 | 12/2018      | 5111.33                  | 6652.57                     | 1541.24                 |
| 46 | COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P     | PGCIL  | 12/2014 | 12/2018      | 4754.42                  | 9141.97                     | 4387.55                 |
| 47 | PAKRI BARWADIH COAL MINING PROJECT                                                                | NTPC   | 10/2004 | 10/2017      | 4237.96                  | 4552                        | 314.04                  |
| 48 | TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT       | PGCIL  | 01/2014 | 09/2017      | 1788.41                  | 2333.71                     | 545.3                   |
| 49 | KHARGONE STPP STAGE I (1320 MW)                                                                   | NTPC   | 03/2015 | 09/2019      | 9870.51                  | 11148.86                    | 1278.35                 |
| 50 | COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B | PGCIL  | 03/2013 | 12/2015      | 2514.88                  | 3190.27                     | 675.39                  |
| 51 | LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW                                                 | NTPC   | 07/2012 | 08/2017      | 1527                     | 1801.07                     | 274.07                  |
| 52 | LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)                                             | NTPC   | 12/2012 | 06/2017      | 11846                    | 12739.82                    | 893.82                  |
| 53 | NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT                                                | PGCIL  | 02/2009 | 08/2013      | 11130.19                 | 13762.8                     | 2632.61                 |

## RAILWAYS

| Sn | Project                                                                 | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|----|-------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 54 | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)                       | NCR    | 04/1986 | 03/1994      | 158.77                   | 634.48                      | 475.71                  |
| 55 | NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR | NFR    | 04/1983 | 03/2019      | 297.32                   | 614                         | 316.68                  |
| 56 | CALICUT-MANGALORE (DL) (SR)                                             | SR     | 02/1996 | N.A.         | 240                      | 579.37                      | 339.37                  |
| 57 | KARUR-SALEM(NL),SR                                                      | SR     | 02/1997 | N.A.         | 155.55                   | 920                         | 764.45                  |
| 58 | KODERMA-RANCHI VIA BARKAKANA (NL),ECR                                   | ECR    | 03/1999 | N.A.         | 1033.07                  | 3020.94                     | 1987.87                 |
| 59 | KATI HAR - JOGBANI (GC)(NEFR)                                           | NFR    | 09/2001 | 12/2010      | 792.46                   | 1320                        | 527.54                  |
| 60 | QUILON-TIRUNELVELI-TENKASI-                                             | SR     | 03/1998 | N.A.         | 280                      | 1122                        | 842                     |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( DECEMBER 2018 )

| Sn | Project                                                         | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|----|-----------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
|    | VIRUDHUNAGAR(SR)(GC)                                            |        |         |              |                          |                             |                         |
| 61 | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE               | SR     | 09/2006 | N.A.         | 343.17                   | 1065                        | 721.83                  |
| 62 | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI | SR     | 09/2007 | 02/2019      | 724.69                   | 2072.5                      | 1347.81                 |
| 63 | TALCHER-BIMALAGARH(NL)(ECOR)                                    | ECOR   | 04/2005 | 06/2021      | 810.78                   | 1928.07                     | 1117.29                 |
| 64 | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)                       | RVNL   | 04/2000 | 03/2009      | 133.41                   | 385                         | 251.59                  |
| 65 | CHHINDWARA - NAGPUR (GC)(SECR)                                  | SECR   | 04/2005 | N.A.         | 383.79                   | 1101.16                     | 717.37                  |
| 66 | HATHUA-BHATNI (N L) (NER)                                       | NER    | 04/2005 | 12/2022      | 230.03                   | 770.08                      | 540.05                  |
| 67 | ETAWAH-MAINPURI (NL),NCR                                        | NCR    | 04/1997 | 12/2008      | 120                      | 245.39                      | 125.39                  |
| 68 | MAHARAJGANJ-MASRAKH (NL) - NER                                  | NER    | 04/2003 | 06/2018      | 218.19                   | 413.56                      | 195.37                  |
| 69 | RAMGANJMUNDI-BHOPAL (NL),WCR                                    | WCR    | 04/2001 | 03/2021      | 424.6                    | 2713.09                     | 2288.49                 |
| 70 | OBULAVARIPALLE-KRISHNAPATNAM(RVNL)                              | RVNL   | 07/2006 | 03/2008      | 732.81                   | 1850                        | 1117.19                 |
| 71 | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR               | ECR    | 04/1996 | 03/2012      | 477.88                   | 749                         | 271.12                  |
| 72 | HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR                          | ECR    | 04/2003 | N.A.         | 528.65                   | 2066.77                     | 1538.12                 |
| 73 | BHAIRABI SAIRONG, NL, NEFR                                      | NFR    | 04/2008 | 03/2014      | 2393.47                  | 4968                        | 2574.53                 |
| 74 | ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT    | RE     | 02/2008 | 03/2012      | 171.1                    | 275.08                      | 103.98                  |
| 75 | TIDIVANAM-NAGARI (NL)                                           | SR     | 09/2006 | N.A.         | 582.83                   | 2300                        | 1717.17                 |
| 76 | TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)                           | SR     | 09/2006 | N.A.         | 227.4                    | 900                         | 672.6                   |
| 77 | KOTLPALLI-NARASAPUR (NL) (SCR)                                  | SCR    | 12/2001 | 03/2009      | 1045.2                   | 2120.16                     | 1074.96                 |
| 78 | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)                           | ECR    | 04/1997 | N.A.         | 162.87                   | 589.15                      | 426.28                  |
| 79 | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR                      | NCR    | 04/1999 | 12/2009      | 108                      | 432.72                      | 324.72                  |
| 80 | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR                      | ECR    | 04/1997 | 03/2012      | 324.73                   | 1156.41                     | 831.68                  |
| 81 | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)                          | WCR    | 09/1998 | 05/2008      | 247.66                   | 6093.31                     | 5845.65                 |
| 82 | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)               | M RTP  | 03/1996 | 03/2004      | 495.44                   | 1781.98                     | 1286.54                 |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( DECEMBER 2018 )

| Sn  | Project                                                                                       | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|-----|-----------------------------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 83  | AHMEDNAGAR-PARLI VAIJNATH(NL) CR                                                              | CR     | 02/1997 | 03/2021      | 2271.5                   | 3712.5                      | 1441                    |
| 84  | MM FROM PANSKURA-GHATAL NL                                                                    | SER    | 04/2011 | N.A.         | 276.69                   | 426                         | 149.31                  |
| 85  | MM FROM BURAMARA-CHAKULIA                                                                     | SER    | 04/2008 | N.A.         | 466.48                   | 1000                        | 533.52                  |
| 86  | CHANDIGARH-BADDI NL                                                                           | NR     | 04/2007 | N.A.         | 328.14                   | 1540                        | 1211.86                 |
| 87  | PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM  | ECR    | 11/2001 | 02/2016      | 624.47                   | 3550                        | 2925.53                 |
| 88  | MUZAFFARPUR SAGALI DOUBLING 100.60 KM                                                         | ECR    | 04/2016 | 03/2021      | 731.64                   | 1185.73                     | 454.09                  |
| 89  | SAGALI VALMIKINAGAR DOUBLING 109.7 KM                                                         | ECR    | 04/2016 | 03/2021      | 744.04                   | 1215.54                     | 471.5                   |
| 90  | BURHWAL - GONDA - 3RD RUNNING LINE.                                                           | NER    | 04/2016 | N.A.         | 602.5                    | 714.34                      | 111.84                  |
| 91  | CHANDIGARH-BADDI                                                                              | NR     | 04/2007 | 03/2023      | 328.14                   | 1540                        | 1211.86                 |
| 92  | WESTERN DEDICATED FREIGHT CORRIDOR                                                            | DFCC   | 11/2007 | 03/2020      | 16592                    | 51101                       | 34509                   |
| 93  | MANDHANA - BRAHMAWART NEW LINE PROJECT.                                                       | NER    | 04/1997 | 04/1999      | 609.04                   | 1807.88                     | 1198.84                 |
| 94  | MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING                                             | SR     | 02/2015 | 03/2020      | 760                      | 1182.31                     | 422.31                  |
| 95  | MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANAL ROAD) (62.05 KM) DOUBLING                      | SR     | 02/2003 | 03/2009      | 199.55                   | 330.32                      | 130.77                  |
| 96  | CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT                                       | SECR   | 04/2010 | 02/2019      | 585.93                   | 1420.39                     | 834.46                  |
| 97  | RAJNANDGAON - NAGPUR - 3RD LINE (SECR)                                                        | SECR   | 09/2016 | 03/2023      | 1908.51                  | 2686.63                     | 778.12                  |
| 98  | KATNI GRADE SEPARATOR/BYE PASS                                                                | WCR    | 08/2016 | 03/2022      | 582.13                   | 1260.61                     | 678.48                  |
| 99  | DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)           | RVNL   | 03/2009 | 03/2020      | 713.48                   | 1750                        | 1036.52                 |
| 100 | BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL                                     | SER    | 04/1998 | 03/2003      | 1027.4                   | 2373                        | 1345.6                  |
| 101 | RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADEATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO | SER    | 04/1995 | 12/2021      | 524.43                   | 939                         | 414.57                  |
| 102 | TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NADIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI | SER    | 01/1991 | 12/2021      | 1013.45                  | 1428                        | 414.55                  |
| 103 | ROURKELA JHARSUGUDA THIRD LINE 101 KM                                                         | SER    | 11/2015 | 03/2020      | 969.83                   | 1151.81                     | 181.98                  |
| 104 | JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE                           | ECOR   | 04/2015 | 11/2018      | 701.61                   | 810.02                      | 108.41                  |
| 105 | MUZAFFARPUR-SITAMARHI NEW LINE                                                                | ECR    | 01/1991 | 07/2014      | 332.15                   | 559.91                      | 227.76                  |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( DECEMBER 2018 )

| Sn  | Project                                                                                              | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|-----|------------------------------------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 106 | VIJAYAWADA-GUDUR                                                                                     | RVNL   | 04/2015 | 12/2023      | 3246.26                  | 3548.67                     | 302.41                  |
| 107 | DAUND - MANMAD (236 KM)                                                                              | CR     | 02/2016 | 03/2023      | 1876                     | 2081.27                     | 205.27                  |
| 108 | VAIBHAVWADI -KOLHAPUR (107 KM)                                                                       | CR     | 02/2016 | 03/2024      | 2750                     | 3438.51                     | 688.51                  |
| 109 | PUNE-NASIK (265 KM)                                                                                  | CR     | 02/2016 | 03/2024      | 2425                     | 5341.68                     | 2916.68                 |
| 110 | EASTERN DEDICATED FREIGHT CORRIDOR PROJECT                                                           | DFCC   | 10/2006 | N.A.         | 11589                    | 28181                       | 16592                   |
| 111 | LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG | ER     | 04/1987 | 03/2006      | 406.99                   | 544.72                      | 137.73                  |
| 112 | MADURAI-TUTICORIN VIA ARUPPUKKOTTAI                                                                  | SR     | 04/2011 | 03/2019      | 120.7                    | 1800                        | 1679.3                  |
| 113 | MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD                                                | RVNL   | 04/2012 | 03/2016      | 632.68                   | 816.55                      | 183.87                  |
| 114 | LUMDING-HOJAI PATCH DOUBLING PROJECT                                                                 | NFR    | 04/2012 | 03/2019      | 246.07                   | 398.93                      | 152.86                  |
| 115 | AMBARI FALAKATA TO NEW MAYNAGURI                                                                     | NFR    | 04/2011 | 03/2019      | 314                      | 551                         | 237                     |
| 116 | NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI    | NFR    | 04/1999 | N.A.         | 819.23                   | 1871                        | 1051.77                 |
| 117 | MURKONGSELEK-PASIGHAT NL                                                                             | NFR    | 04/2011 | 03/2020      | 414.84                   | 661                         | 246.16                  |
| 118 | NEW BG LINE FROM JAGBANI TO BIRATNAGAR                                                               | NFR    | 04/2010 | N.A.         | 241.52                   | 394.28                      | 152.76                  |
| 119 | NEW BG LINE FROM BALURGHAT TO HILLY NFR                                                              | NFR    | 04/2010 | 03/2020      | 242.22                   | 471                         | 228.78                  |
| 120 | NEW BG LINE FROM BYRNIHAT TO SHILLONG                                                                | NFR    | 04/2010 | 03/2021      | 906.46                   | 6000                        | 5093.54                 |
| 121 | CHENGANNUR-CHINGAVANAM                                                                               | SR     | 04/2006 | N.A.         | 191.72                   | 369.83                      | 178.11                  |
| 122 | MADURAI-BODINAYAKKANUR                                                                               | SR     | 04/2008 | N.A.         | 164.41                   | 450                         | 285.59                  |
| 123 | ERODE-PALANI                                                                                         | SR     | 04/2008 | N.A.         | 288.57                   | 1140                        | 851.43                  |
| 124 | CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA                                                           | NFR    | 04/1999 | 03/2007      | 895                      | 1733.2                      | 838.2                   |
| 125 | NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR                                                             | NFR    | 04/2010 | N.A.         | 221.42                   | 380                         | 158.58                  |
| 126 | KURUPPANTHARA-CHINGAVANAM                                                                            | SR     | 04/2007 | N.A.         | 270.14                   | 457.08                      | 186.94                  |
| 127 | CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC                                                      | SR     | 04/1998 | N.A.         | 271.24                   | 520                         | 248.76                  |
| 128 | CUDDALORE-SALEM VIA VRIDDHACHALAM GC                                                                 | SR     | 04/1999 | N.A.         | 198.68                   | 556.64                      | 357.96                  |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( DECEMBER 2018 )

| Sn  | Project                                                                      | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|-----|------------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 129 | SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR | SR     | 04/2013 | N.A.         | 839                      | 1500                        | 661                     |
| 130 | CHENNAI-CUDDALORE VIA MAMALLAPURAM                                           | SR     | 04/2008 | N.A.         | 523.52                   | 2350                        | 1826.48                 |
| 131 | ATTIPPATTU PUTTUR                                                            | SR     | 04/2008 | 02/2019      | 151.84                   | 1105                        | 953.16                  |
| 132 | HAJIPUR-RAMDAYALUNAGAR DOUBLING                                              | ECR    | 04/2013 | N.A.         | 213.01                   | 367.17                      | 154.16                  |
| 133 | JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC          | ECR    | 04/2009 | 03/2020      | 548                      | 785.87                      | 237.87                  |
| 134 | SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)       | ECR    | 04/2004 | N.A.         | 372.14                   | 1474.47                     | 1102.33                 |
| 135 | SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)                                  | ECR    | 04/2008 | N.A.         | 678.62                   | 2393.23                     | 1714.61                 |
| 136 | MOTIHARI-SITAMARHI (NL)                                                      | ECR    | 04/2006 | N.A.         | 211                      | 926.09                      | 715.09                  |
| 137 | CHHAPRA-MUZAFFARPUR (NL)                                                     | ECOR   | 04/2006 | N.A.         | 378.56                   | 2614.36                     | 2235.8                  |
| 138 | SAKRI-HASANPUR ROAD (NL)                                                     | ECOR   | 04/1999 | N.A.         | 325                      | 729.92                      | 404.92                  |
| 139 | BIHTA-AURANGABAD (NL)                                                        | ECOR   | 04/2008 | N.A.         | 326.2                    | 2995.01                     | 2668.81                 |
| 140 | GAYA-CHATRA (NL)                                                             | ECOR   | 04/2008 | N.A.         | 415.67                   | 549.75                      | 134.08                  |
| 141 | GAYA-DALTONGANJ VIA RAFIGANJ (NL)                                            | ECOR   | 04/2008 | N.A.         | 445.25                   | 2860.55                     | 2415.3                  |
| 142 | NAWADA-LAXMIPUR (NL)                                                         | ECR    | 04/2008 | N.A.         | 620.57                   | 2626.98                     | 2006.41                 |
| 143 | ARA-BHABHUA ROAD (NL)                                                        | SER    | 04/2008 | N.A.         | 633.87                   | 2396.88                     | 1763.01                 |
| 144 | MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING                                      | SER    | 04/2012 | N.A.         | 258.2                    | 365                         | 106.8                   |
| 145 | DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING                                      | SER    | 04/2010 | 12/2015      | 309.44                   | 525.81                      | 216.37                  |
| 146 | BHADUTOLA-JHARGRAM VIA LALGARH (NL)                                          | SER    | 04/2011 | N.A.         | 289.64                   | 760                         | 470.36                  |
| 147 | DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA                                   | SER    | 04/2010 | 03/2015      | 651                      | 1009                        | 358                     |
| 148 | BOWAICHANDI-ARAMBAGH                                                         | SER    | 04/2010 | N.A.         | 267.37                   | 620                         | 352.63                  |
| 149 | ALWAR-BANDIKUI DOUBLING                                                      | NWR    | 04/2013 | 02/2019      | 242.09                   | 349                         | 106.91                  |
| 150 | PUSHKAR-MERTA                                                                | NWR    | 04/2013 | N.A.         | 323                      | 432.22                      | 109.22                  |
| 151 | AJMER-KOTA (NASIRABAD-JAUNDRI)                                               | NWR    | 04/2013 | N.A.         | 822                      | 1099.54                     | 277.54                  |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( DECEMBER 2018 )

| Sn  | Project                                                                                              | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|-----|------------------------------------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 152 | GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)                                                       | NCR    | 04/2011 | 03/2022      | 2912.96                  | 3845.6                      | 932.64                  |
| 153 | RATLAM-DUNGARPUR VIA BANSWARA (NL)                                                                   | NWR    | 04/2011 | N.A.         | 2082.75                  | 2878.97                     | 796.22                  |
| 154 | RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)       | WR     | 04/1994 | 03/2019      | 320.66                   | 858.96                      | 538.3                   |
| 155 | BANGURGRAM-GURIYA PATCH DOUBLING                                                                     | NWR    | 04/2012 | 12/2019      | 246.08                   | 348.55                      | 102.47                  |
| 156 | CHHAPRA-BALLIA UP                                                                                    | NER    | 03/2013 | 01/2019      | 295                      | 477.31                      | 182.31                  |
| 157 | BHOJIPUR TANAKPUR VIA PILIBHIT                                                                       | NER    | 03/2008 | N.A.         | 195.64                   | 435                         | 239.36                  |
| 158 | CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP                                                       | NER    | 03/2007 | 12/2021      | 243.78                   | 895                         | 651.22                  |
| 159 | UTRATIA-ZAFRABAD, NR (LINE DOUBLING)                                                                 | NR     | 04/2006 | 03/2010      | 369.9                    | 1581.53                     | 1211.63                 |
| 160 | JALANDHAR-PATHANKOT-JAMMU TAWI                                                                       | NR     | 03/2002 | 03/2016      | 625                      | 845.58                      | 220.58                  |
| 161 | GEVRA ROAD PENDRA ROAD                                                                               | SECR   | 02/2014 | 03/2022      | 2288                     | 4919                        | 2631                    |
| 162 | KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)                                                        | SWR    | 03/1996 | 03/2017      | 644.78                   | 889.52                      | 244.74                  |
| 163 | CHAMPA-JHARSUGUDA 3RD LINE                                                                           | SECR   | 04/2008 | 12/2019      | 872                      | 1279                        | 407                     |
| 164 | CHHINDWARA-MANDLA FORT GC                                                                            | SECR   | 03/2011 | 03/2012      | 556.54                   | 1342.46                     | 785.92                  |
| 165 | WADSA-GADHCHIROLI NEW LINE (52.36 KM)                                                                | SECR   | 06/2018 | 12/2021      | 229                      | 403                         | 174                     |
| 166 | FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, | ECR    | 04/1991 | N.A.         | 329.39                   | 566.41                      | 237.02                  |
| 167 | RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR                                              | ECR    | 04/1998 | N.A.         | 180.82                   | 528.26                      | 347.44                  |
| 168 | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR                                                              | NR     | 03/2002 | 06/2007      | 625.3                    | 876.1                       | 250.8                   |
| 169 | UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR                                                                 | NR     | 03/1995 | 11/2002      | 2500                     | 27949                       | 25449                   |
| 170 | NANGALDAM-TALWARA(NL), NR                                                                            | NR     | 03/1981 | 07/2012      | 450                      | 2100                        | 1650                    |
| 171 | DAUSA-GANGAPUR CITY(NL), NWR                                                                         | NWR    | 02/1997 | 02/2019      | 410.08                   | 795.01                      | 384.93                  |
| 172 | KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)                                                              | NER    | 04/1999 | N.A.         | 744.71                   | 1126.79                     | 382.08                  |
| 173 | SEVOK RANGPO, NEFR                                                                                   | NFR    | 04/2008 | 12/2015      | 1339.48                  | 4084.69                     | 2745.21                 |
| 174 | AGARTALA SABROOM, NL, NEFR                                                                           | NFR    | 04/2008 | 03/2014      | 1142                     | 3407                        | 2265                    |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( DECEMBER 2018 )

| Sn  | Project                                                                                          | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|-----|--------------------------------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 175 | MUMBAI URBAN TRANSPORT PROJECT PHASE-II                                                          | MRTPT  | 04/2008 | 03/2014      | 5300                     | 7986.04                     | 2686.04                 |
| 176 | ANGAMALI-SABARIMALA (N.L.)(SR)                                                                   | SR     | 10/1998 | N.A.         | 1566                     | 2815.62                     | 1249.62                 |
| 177 | AMRAVATI-NARKHER NL(CR)                                                                          | CR     | 06/1994 | 06/1999      | 663.01                   | 858.96                      | 195.95                  |
| 178 | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)                                                           | SCR    | 12/1994 | N.A.         | 124.43                   | 1025                        | 900.57                  |
| 179 | HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR)                                                     | NWR    | 04/2008 | 03/2015      | 829.74                   | 1216                        | 386.26                  |
| 180 | HOTGI-KUDGI-GADAG                                                                                | SWR    | 03/2015 | 03/2019      | 1614.59                  | 1870.41                     | 255.82                  |
| 181 | AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUDH KA BARWARA) VIS TONK NL                                 | NWR    | 05/2015 | N.A.         | 873.71                   | 1103.04                     | 229.33                  |
| 182 | RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND                                            | SER    | 04/2012 | 12/2016      | 148.77                   | 377                         | 228.23                  |
| 183 | SAMBALPUR-TALCHER DOUBLING                                                                       | ECOR   | 03/2011 | 02/2019      | 1111.99                  | 1539.28                     | 427.29                  |
| 184 | TAMLUK DIGHA, LINE DOUBLING (SER)                                                                | SER    | 03/1984 | 06/2005      | 293.97                   | 749.69                      | 455.72                  |
| 185 | HOWRAH-AMTA-CHAMPADANGA NL (SER)                                                                 | SER    | 04/1974 | 03/2007      | 393.46                   | 1026                        | 632.54                  |
| 186 | GONDIA-JABALPUR(GC), (SECR)                                                                      | SECR   | 02/1997 | 04/2020      | 511.86                   | 1756                        | 1244.14                 |
| 187 | NANDYAL-YERRAGUNTALA(NL), SCR                                                                    | SCR    | 03/1996 | 02/2009      | 164.36                   | 1050                        | 885.64                  |
| 188 | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) | RVNL   | 04/2010 | 03/2014      | 2298.42                  | 2733.86                     | 435.44                  |
| 189 | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)     | RVNL   | 04/2010 | 03/2016      | 3951.98                  | 4259.48                     | 307.5                   |
| 190 | SALKA ROAD -ANUPNAGAR LINE DOUBLING                                                              | RVNL   | 09/2006 | 03/2010      | 383.54                   | 555                         | 171.46                  |
| 191 | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL                               | RVNL   | 04/1995 | 12/2012      | 631.78                   | 1195                        | 563.22                  |
| 192 | NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)                                   | NFR    | 04/2006 | 03/2015      | 2326.52                  | 3000                        | 673.48                  |
| 193 | GHUTIASHARIF-CANNING (ER)                                                                        | ER     | 04/2009 | 12/2011      | 193.08                   | 612.45                      | 419.37                  |
| 194 | NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR                                         | NFR    | 09/2006 | 03/2019      | 532.87                   | 2145                        | 1612.13                 |
| 195 | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR                                  | NFR    | 09/2006 | 03/2019      | 385.2                    | 1532                        | 1146.8                  |
| 196 | EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP                                             | MRTPT  | 04/2006 | 06/2013      | 495.74                   | 734.01                      | 238.27                  |
| 197 | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)                                                              | NFR    | 04/2003 | 03/2011      | 4454.17                  | 13809                       | 9354.83                 |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( DECEMBER 2018 )

| Sn                                 | Project                                                                                             | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|------------------------------------|-----------------------------------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 198                                | KHURDA ROAD-BOLANGIR(NL)ECOR                                                                        | ECOR   | 04/1994 | 03/2009      | 2923.13                  | 3798.8                      | 875.67                  |
| 199                                | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR                                             | NFR    | 04/2000 | 12/2008      | 1180.19                  | 3040                        | 1859.81                 |
| 200                                | HARIDWAR-LAKSAR                                                                                     | NR     | 04/2012 | N.A.         | 219.83                   | 346.63                      | 126.8                   |
| 201                                | CUMBUM-PRODDATUR                                                                                    | SCR    | 04/2013 | N.A.         | 829                      | 1599.39                     | 770.39                  |
| 202                                | SRINIVASA-PURA-MADANAPALLI NL                                                                       | SWR    | 04/2013 | N.A.         | 296                      | 466.65                      | 170.65                  |
| 203                                | CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL                                                  | SWR    | 04/2013 | N.A.         | 558                      | 692.43                      | 134.43                  |
| 204                                | BHANUPALI-BILASPUR BERI NL                                                                          | RVNL   | 04/2008 | 12/2026      | 2966.99                  | 7000                        | 4033.01                 |
| 205                                | ROHTAK-MEHAM HANSI                                                                                  | NR     | 04/2012 | 12/2011      | 287                      | 625                         | 338                     |
| 206                                | BHADRACHALAM-KOVVUR                                                                                 | SCR    | 04/2012 | N.A.         | 923.23                   | 1787                        | 863.77                  |
| 207                                | KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION                                                    | SCR    | 04/2012 | 03/2023      | 1856.95                  | 2200                        | 343.05                  |
| 208                                | MANUGURU-RAMAGUNDAM                                                                                 | SCR    | 04/2013 | N.A.         | 1112                     | 2911.84                     | 1799.84                 |
| 209                                | MUNIRABAD (GINGERA) -RAICHUR NL                                                                     | SWR    | 04/2007 | N.A.         | 179.65                   | 1350.91                     | 1171.26                 |
| 210                                | 3RD LINE BETWEEN BHUSAWAL-JALGAON                                                                   | CR     | 04/2011 | 03/2019      | 184.06                   | 298.7                       | 114.64                  |
| 211                                | MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL | ER     | 04/2009 | 02/2012      | 499.96                   | 665.75                      | 165.79                  |
| 212                                | TARAKESHWAR-MAGRA NEW BG LINE                                                                       | ER     | 04/2010 | N.A.         | 365.17                   | 527.54                      | 162.37                  |
| 213                                | DAKSHIN-BARASAL-LAKSHMIKANTAPUR                                                                     | ER     | 04/2009 | 02/2012      | 259.51                   | 533.59                      | 274.08                  |
| 214                                | JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)                                   | NWR    | 04/2008 | 03/2014      | 653.19                   | 1116                        | 462.81                  |
| 215                                | TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)                     | M RTP  | 03/2000 | 12/2006      | 1049.69                  | 3404.92                     | 2355.23                 |
| 216                                | TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER                                                         | ER     | 04/2000 | 03/2019      | 1188.91                  | 1620.01                     | 431.1                   |
| 217                                | JIND-SONEPAT (NL), NR                                                                               | NR     | 01/2004 | 03/2012      | 238.56                   | 740                         | 501.44                  |
| 218                                | HARIDASPUR-PARADEEP(NL)                                                                             | RVNL   | 04/1996 | 12/2017      | 1185.64                  | 1844.47                     | 658.83                  |
| <b>ROAD TRANSPORT AND HIGHWAYS</b> |                                                                                                     |        |         |              |                          |                             |                         |
| Sn                                 | Project                                                                                             | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
| 219                                | MAIBANG TO LUMDING (AS-25), KM.83.400 TO                                                            | NHAI   | 12/2003 | 04/2009      | 199.81                   | 385.13                      | 185.32                  |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning



## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( DECEMBER 2018 )

| Sn  | Project                                                                                               | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|-----|-------------------------------------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
|     | KM.111.000                                                                                            |        |         |              |                          |                             |                         |
| 220 | BRAHMPUTRA BRIDGE,NH NO-31                                                                            | NHAI   | 12/2003 | 04/2010      | 217.61                   | 360.84                      | 143.23                  |
| 221 | GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION                                                   | NHAI   | 03/2010 | 09/2012      | 1509.1                   | 3237.87                     | 1728.77                 |
| 222 | DELHI AGRA APPROVED LENGTH 180.0 KM                                                                   | NHAI   | 10/2012 | 04/2015      | 1928.22                  | 2945                        | 1016.78                 |
| 223 | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-I)_NEW                                    | NHAI   | 09/2015 | N.A.         | 771.18                   | 7558                        | 6786.82                 |
| 224 | SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O  | NHAI   | 03/2017 | 03/2020      | 993.16                   | 1434                        | 440.84                  |
| 225 | SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA    | NHAI   | 03/2017 | 03/2020      | 831.58                   | 1177                        | 345.42                  |
| 226 | 6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA  | NHAI   | 03/2017 | 03/2020      | 2064.99                  | 2447                        | 382.01                  |
| 227 | REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM   | NHAI   | 03/2017 | 03/2020      | 1288.07                  | 1420                        | 131.93                  |
| 228 | SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000                  | NHAI   | 03/2017 | 03/2020      | 1041.62                  | 1187.1                      | 145.48                  |
| 229 | 4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)                                              | NHAI   | 03/2017 | 03/2020      | 744.64                   | 982                         | 237.36                  |
| 230 | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C  | NHAI   | 03/2017 | 03/2020      | 1184.71                  | 1310                        | 125.29                  |
| 231 | FOUR LANING OF GWALIOR-SHIVPURI                                                                       | NHAI   | 05/2013 | 11/2015      | 1055                     | 1601.77                     | 546.77                  |
| 232 | CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LW E S | PWD    | 03/2011 | 12/2015      | 218.31                   | 339.82                      | 121.51                  |
| 233 | 4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9                                                 | NHAI   | 04/2014 | 09/2016      | 1266.6                   | 1544                        | 277.4                   |
| 234 | TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA  | PWD    | 12/2011 | 02/2012      | 156.63                   | 276                         | 119.37                  |
| 235 | MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450                                                  | NHAI   | 12/2003 | 11/2008      | 155.04                   | 280.13                      | 125.09                  |
| 236 | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)                                                           | NHAI   | 05/2009 | 11/2011      | 1108                     | 2288                        | 1180                    |
| 237 | HARANGAJO TO MAIBANG, NH-54                                                                           | NHAI   | 12/2003 | 07/2009      | 196                      | 331.23                      | 135.23                  |

## SHIPPING AND PORTS

| Sn  | Project                                                                                              | Agency      | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|-----|------------------------------------------------------------------------------------------------------|-------------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 238 | ENMORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)                                          | PORT TRUST  | 10/2002 | 03/2006      | 150                      | 600                         | 450                     |
| 239 | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB | MUMBAI PORT | 01/2007 | 12/2010      | 366.39                   | 669.46                      | 303.07                  |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( DECEMBER 2018 )

| <b>STEEL</b>              |                                                                                                     |        |         |              |                          |                             |                         |
|---------------------------|-----------------------------------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| Sn                        | Project                                                                                             | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
| 240                       | REVAMPING OF SINTER MACHINES - 1 AND 2                                                              | RINL   | 12/2009 | 10/2016      | 343                      | 488.4                       | 145.4                   |
| <b>TELECOMMUNICATIONS</b> |                                                                                                     |        |         |              |                          |                             |                         |
| Sn                        | Project                                                                                             | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
| 241                       | NETWORK FOR SPECTRUM                                                                                | DOT    | 03/2012 | 07/2015      | 13334                    | 24664                       | 11330                   |
| <b>URBAN DEVELOPMENT</b>  |                                                                                                     |        |         |              |                          |                             |                         |
| Sn                        | Project                                                                                             | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
| 242                       | CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA                                            | HSCL   | 05/2005 | 02/2014      | 768.88                   | 1113.34                     | 344.46                  |
| 243                       | CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA | CPWD   | 12/2008 | 12/2013      | 114.26                   | 266                         | 151.74                  |
| 244                       | CHENNAI METRO RAIL LTD (PHASE 1)                                                                    | CMRL   | 02/2009 | 12/2015      | 14600                    | 19058                       | 4458                    |
| 245                       | REDEVELOPMENT OF EAST KIDWAI NAGAR                                                                  | NBCC   | 06/2012 | 11/2019      | 4264                     | 4439.23                     | 175.23                  |
| 246                       | ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI     | CPWD   | 10/2013 | 10/2019      | 1219.21                  | 1592                        | 372.79                  |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning

**DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE**

**(DECEMBER 2018)**

**ATOMIC ENERGY**

| Sn | Project                                           | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|---------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 1  | KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4           | NPCIL  | 10/2009 | 12/2015      | 06/2020         | 1,1459.00                 | 1,6580.00                    | 5121            | 54           |
| 2  | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) | BHAVNI | 09/2003 | 09/2010      | 03/2019         | 3492.00                   | 6100.00                      | 2608            | 102          |

**CIVIL AVIATION**

| Sn | Project                                                                    | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|----------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 3  | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR | AAI    | 10/2013 | 09/2018      | 06/2020         | 314.61                    | 441.33                       | 126.72          | 21           |

**COAL**

| Sn | Project                        | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|--------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 4  | RCE OF INDARAM OCP(1.20 MTPA)  | SCCL   | 07/2011 | 03/2015      | 03/2021         | 162.76                    | 349.28                       | 186.52          | 72           |
| 5  | SHANTIKHANI LONGWALL PROJ-SCCL | SCCL   | 10/2006 | 03/2012      | 03/2024         | 249.03                    | 448.86                       | 199.83          | 144          |
| 6  | JAGANNATHPOR OCP(3.00MTY)      | SECL   | 09/2008 | 03/2015      | 03/2020         | 152.43                    | 459.49                       | 307.06          | 60           |

**HEAVY INDUSTRY**

| Sn | Project                                                            | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|--------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 7  | NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) | NATIS  | 04/2011 | 09/2011      | 06/2019         | 1718.00                   | 3827.30                      | 2109.3          | 93           |

**PETROLEUM**

| Sn | Project                                                             | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|---------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 8  | PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY | BPCL   | 11/2014 | 08/2018      | 11/2019         | 4588.29                   | 5245.96                      | 657.67          | 15           |
| 9  | URAN CHAKAN SHIKRAPUR LPG PIPELINE                                  | HPCL   | 12/2009 | 10/2014      | 02/2019         | 309.81                    | 723.40                       | 413.59          | 52           |
| 10 | DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY     | IOCL   | 03/2014 | 09/2017      | 03/2019         | 3076.00                   | 4190.00                      | 1114            | 18           |
| 11 | LPG TERMINAL AT KOCHI                                               | IOCL   | 10/2015 | 10/2017      | 03/2019         | 607.06                    | 714.25                       | 107.19          | 17           |
| 12 | INTEGRATED DEVELOPMENT OF B-127 FIELDS                              | ONGC   | 12/2011 | 03/2015      | 12/2019         | 2059.63                   | 2665.65                      | 606.02          | 57           |

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

**DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE**

**(DECEMBER 2018)**

| Sn | Project                                                                 | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|-------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 13 | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)  | ONGC   | 06/2010 | 01/2014      | 11/2019         | 202.94                    | 330.35                       | 127.41          | 70           |
| 14 | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) | ONGC   | 03/2011 | 05/2013      | 03/2019         | 861.79                    | 1577.15                      | 715.36          | 70           |

**POWER**

| Sn | Project                                                                            | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|------------------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 15 | 400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV)                           | PGCIL  | 08/2008 | 02/2013      | 12/2018         | 771.00                    | 1624.00                      | 853             | 70           |
| 16 | NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES | PGCIL  | 12/2014 | 12/2018      | 12/2019         | 5111.33                   | 6652.57                      | 1541.24         | 12           |
| 17 | BARH STPP(3X660MW) NTPC                                                            | NTPC   | 02/2005 | 01/2011      | 04/2021         | 8692.97                   | 1,5095.67                    | 6402.7          | 123          |
| 18 | SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV                                      | PGCIL  | 12/2011 | 08/2014      | 02/2019         | 297.33                    | 534.02                       | 236.69          | 54           |
| 19 | NPGCPL-NABINAGAR STPP - JV (3X660 MW)                                              | NTPC   | 01/2013 | 01/2018      | 05/2020         | 1,2964.60                 | 1,3731.26                    | 766.66          | 28           |
| 20 | PARBATI HEP (4X200 MW) (NHPC) II                                                   | NHPC   | 09/2002 | 09/2009      | 12/2021         | 3919.59                   | 9394.80                      | 5475.21         | 147          |
| 21 | BONGAIGAON THERMAL POWER PROJECT                                                   | NTPC   | 01/2008 | 09/2011      | 01/2019         | 4375.35                   | 8150.00                      | 3774.65         | 88           |
| 22 | DARLIPALLI STPP STAGE-I (2X800 MW)                                                 | NTPC   | 02/2014 | 08/2018      | 06/2019         | 1,2532.44                 | 1,3740.53                    | 1208.09         | 10           |
| 23 | NORTH KARANPURA STPP (3X660 MW)                                                    | NTPC   | 02/2014 | 02/2019      | 10/2020         | 1,4366.58                 | 1,5164.05                    | 797.47          | 20           |
| 24 | BRBCL-NABINAGAR TPP- JV (4X250 MW)                                                 | NTPC   | 01/2007 | 05/2014      | 05/2019         | 5353.00                   | 7998.00                      | 2645            | 60           |
| 25 | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT                   | SJVN   | 05/2015 | 12/2016      | 03/2019         | 436.68                    | 602.44                       | 165.76          | 27           |
| 26 | VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT                                         | THDCIL | 08/2008 | 06/2013      | 12/2021         | 2491.58                   | 4105.30                      | 1613.72         | 102          |
| 27 | KAMENG HYDROELECTRIC PROJECT (NEEPCO)                                              | NEEPCO | 12/2004 | 12/2009      | 03/2019         | 2496.90                   | 6179.96                      | 3683.06         | 111          |
| 28 | TEHRI PUMPED STORAGE PLANT(1000MW)                                                 | THDCIL | 07/2006 | 02/2016      | 05/2021         | 1657.00                   | 4401.90                      | 2744.9          | 63           |

DOA -&gt; Date of Approval

COR -&gt; Cost Overrun

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

**DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE**

**(DECEMBER 2018)**

| Sn | Project                                                                                       | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|-----------------------------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 29 | SYTEM STRENGTHENING XIII OF SR GRID                                                           | PGCIL  | 10/2011 | 06/2014      | 03/2019         | 487.49                    | 639.46                       | 151.97          | 57           |
| 30 | WESTERN REGION STRENGTHENING SCHEME-V                                                         | PGCIL  | 12/2007 | 09/2010      | 02/2019         | 477.69                    | 738.48                       | 260.79          | 101          |
| 31 | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT                                    | PGCIL  | 10/2008 | 10/2012      | 06/2019         | 4824.12                   | 5071.94                      | 247.82          | 80           |
| 32 | GADARWARA SUPER THERMAL POWER PROJECT STAGE-I                                                 | NTPC   | 03/2013 | 09/2017      | 06/2019         | 1,1638.55                 | 1,2865.92                    | 1227.37         | 21           |
| 33 | NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT                                            | PGCIL  | 02/2009 | 08/2013      | 03/2022         | 1,1130.19                 | 1,3762.80                    | 2632.61         | 103          |
| 34 | EASTERN REGION STRENGTHENING SCHEME-V                                                         | PGCIL  | 10/2013 | 04/2016      | 02/2019         | 1364.52                   | 1891.41                      | 526.89          | 34           |
| 35 | TAPOVAN-VISHNUGAD HEP (4X130MW)                                                               | NTPC   | 11/2006 | 03/2013      | 12/2020         | 2978.48                   | 3846.30                      | 867.82          | 93           |
| 36 | KUNADANKULAM APP TRANS SYSTEM (PGCIL)                                                         | PGCIL  | 05/2005 | 11/2008      | 03/2019         | 1779.29                   | 2187.32                      | 408.03          | 124          |
| 37 | COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P | PGCIL  | 12/2014 | 12/2018      | 12/2019         | 4754.42                   | 9141.97                      | 4387.55         | 12           |
| 38 | LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)                                         | NTPC   | 12/2012 | 06/2017      | 06/2019         | 1,1846.00                 | 1,2739.82                    | 893.82          | 24           |

**RAILWAYS**

| Sn | Project                                                                 | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|-------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 39 | KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)                           | SWR    | 03/1996 | 03/2017      | 03/2020         | 644.78                    | 889.52                       | 244.74          | 36           |
| 40 | CHHINDWARA-MANDLA FORT GC                                               | SECR   | 03/2011 | 03/2012      | 03/2020         | 556.54                    | 1342.46                      | 785.92          | 96           |
| 41 | BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL               | SER    | 04/1998 | 03/2003      | 03/2030         | 1027.40                   | 2373.00                      | 1345.6          | 324          |
| 42 | JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE     | ECOR   | 04/2015 | 11/2018      | 03/2021         | 701.61                    | 810.02                       | 108.41          | 28           |
| 43 | DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING                                | SER    | 04/2010 | 12/2015      | 02/2019         | 309.44                    | 525.81                       | 216.37          | 38           |
| 44 | NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR | NFR    | 04/1983 | 03/2019      | 03/2020         | 297.32                    | 614.00                       | 316.68          | 12           |

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

**DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS  
OF RS.100 CRORE AND ABOVE  
(DECEMBER 2018)**

| Sn | Project                                                                 | Agency | DOA     | DOC<br>Original | DOC<br>Anticipa<br>ted | Cost<br>Original<br>(Rs. crore) | Cost<br>Anticipated<br>(Rs. crore) | COR<br>(Rs.<br>crore) | TOR<br>(Months) |
|----|-------------------------------------------------------------------------|--------|---------|-----------------|------------------------|---------------------------------|------------------------------------|-----------------------|-----------------|
| 45 | KOTLPALLI-NARASAPUR (NL)<br>(SCR)                                       | SCR    | 12/2001 | 03/2009         | 03/2023                | 1045.20                         | 2120.16                            | 1074.96               | 168             |
| 46 | HARIDASPUR-PARADEEP(NL)                                                 | RVNL   | 04/1996 | 12/2017         | 03/2020                | 1185.64                         | 1844.47                            | 658.83                | 27              |
| 47 | KHURDA ROAD - BARANG 3RD LINE<br>(DL) (ECOR)                            | RVNL   | 04/2000 | 03/2009         | 02/2019                | 133.41                          | 385.00                             | 251.59                | 119             |
| 48 | TALCHER-BIMALAGARH(NL)(ECOR)                                            | ECOR   | 04/2005 | 06/2021         | 03/2023                | 810.78                          | 1928.07                            | 1117.29               | 21              |
| 49 | BHAIRABI SAIRONG, NL, NEFR                                              | NFR    | 04/2008 | 03/2014         | 12/2020                | 2393.47                         | 4968.00                            | 2574.53               | 81              |
| 50 | LALITPUR-SATNA-REWA-SINGRULI<br>NL, (NCR)                               | WCR    | 09/1998 | 05/2008         | 03/2023                | 247.66                          | 6093.31                            | 5845.65               | 178             |
| 51 | JAYANAGAR-DARBHANGA-NARKATIA<br>GANJ(GC), ECR                           | ECR    | 04/1997 | 03/2012         | 03/2020                | 324.73                          | 1156.41                            | 831.68                | 96              |
| 52 | NEW MAYNAGURI TO JOGIGHOPA VIA<br>CHANGRABANDHA (NL), NEFR              | NFR    | 04/2000 | 12/2008         | 03/2019                | 1180.19                         | 3040.00                            | 1859.81               | 123             |
| 53 | KHURDA ROAD-BOLANGIR(NL)ECOR                                            | ECOR   | 04/1994 | 03/2009         | 06/2021                | 2923.13                         | 3798.80                            | 875.67                | 147             |
| 54 | JIRIBAM TO IMPHAL<br>(TUPUI)(NL)(NEFR)                                  | NFR    | 04/2003 | 03/2011         | 03/2020                | 4454.17                         | 1,3809.00                          | 9354.83               | 108             |
| 55 | EXTENSION OF MRTS FROM<br>VELACHERY TO STN. THOMAS, MTP                 | M RTP  | 04/2006 | 06/2013         | 03/2019                | 495.74                          | 734.01                             | 238.27                | 69              |
| 56 | NEW B.G. LINE FROM TETELIA TO<br>BYRNIHAT (NATIONAL PROJECT),<br>NEFR   | NFR    | 09/2006 | 03/2019         | 03/2020                | 385.20                          | 1532.00                            | 1146.8                | 12              |
| 57 | NEW B.G. LINE FROM ARARIA TO<br>GALGALIA (THAKURGUNG), NEFR             | NFR    | 09/2006 | 03/2019         | 03/2020                | 532.87                          | 2145.00                            | 1612.13               | 12              |
| 58 | NEW LINE FROM DIMAPUR TO<br>ZUBZA(KOHIMA) NATIONAL PROJECT<br>(NEFR)    | NFR    | 04/2006 | 03/2015         | 10/2021                | 2326.52                         | 3000.00                            | 673.48                | 79              |
| 59 | MANSI-PURNIA (EXTENSION OF<br>MANSI-SAHARSA) GAN ECR                    | ECR    | 04/1996 | 03/2012         | 03/2020                | 477.88                          | 749.00                             | 271.12                | 96              |
| 60 | OBULAVARIPALLE-<br>KRISHNAPATNAM(RVNL)                                  | RVNL   | 07/2006 | 03/2008         | 03/2020                | 732.81                          | 1850.00                            | 1117.19               | 144             |
| 61 | JAIPUR - RINGUS - CHURU AND<br>SIKAR - LOHARU GUAGE<br>CONVERSION (NWR) | NWR    | 04/2008 | 03/2014         | 03/2019                | 653.19                          | 1116.00                            | 462.81                | 60              |
| 62 | KAZIPET-VIJAYAWADA 3RD LINE                                             | SCR    | 04/2012 | 03/2023         | 03/2024                | 1856.95                         | 2200.00                            | 343.05                | 12              |

DOA -&gt; Date of Approval

COR -&gt; Cost Overrun

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

**DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE**

**(DECEMBER 2018)**

| Sn | Project                                                                                          | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|--------------------------------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
|    | WITH ELECTRIFICATION                                                                             |        |         |              |                 |                           |                              |                 |              |
| 63 | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)                                                | M RTP  | 03/1996 | 03/2004      | 03/2020         | 495.44                    | 1781.98                      | 1286.54         | 192          |
| 64 | MUMBAI URBAN TRANSPORT PROJECT PHASE-II                                                          | M RTP  | 04/2008 | 03/2014      | 03/2019         | 5300.00                   | 7986.04                      | 2686.04         | 60           |
| 65 | AGARTALA SABROOM, NL, NEFR                                                                       | NFR    | 04/2008 | 03/2014      | 03/2019         | 1142.00                   | 3407.00                      | 2265            | 60           |
| 66 | SEVOK RANGPO, NEFR                                                                               | NFR    | 04/2008 | 12/2015      | 03/2020         | 1339.48                   | 4084.69                      | 2745.21         | 51           |
| 67 | UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR                                                             | NR     | 03/1995 | 11/2002      | 03/2021         | 2500.00                   | 2,7949.00                    | 25449           | 220          |
| 68 | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL                               | RVNL   | 04/1995 | 12/2012      | 03/2022         | 631.78                    | 1195.00                      | 563.22          | 111          |
| 69 | SALKA ROAD -ANUPNAGAR LINE DOUBLING                                                              | RVNL   | 09/2006 | 03/2010      | 12/2019         | 383.54                    | 555.00                       | 171.46          | 117          |
| 70 | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)     | RVNL   | 04/2010 | 03/2016      | 03/2025         | 3951.98                   | 4259.48                      | 307.5           | 108          |
| 71 | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) | RVNL   | 04/2010 | 03/2014      | 12/2025         | 2298.42                   | 2733.86                      | 435.44          | 141          |
| 72 | SAMBALPUR-TALCHER DOUBLING                                                                       | ECOR   | 03/2011 | 02/2019      | 03/2021         | 1111.99                   | 1539.28                      | 427.29          | 25           |
| 73 | RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND                                            | SER    | 04/2012 | 12/2016      | 09/2019         | 148.77                    | 377.00                       | 228.23          | 33           |
| 74 | HOTGI-KUDGI-GADAG                                                                                | SWR    | 03/2015 | 03/2019      | 03/2021         | 1614.59                   | 1870.41                      | 255.82          | 24           |
| 75 | HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)                                                     | NWR    | 04/2008 | 03/2015      | 06/2020         | 829.74                    | 1216.00                      | 386.26          | 63           |
| 76 | RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)   | WR     | 04/1994 | 03/2019      | 03/2022         | 320.66                    | 858.96                       | 538.3           | 36           |
| 77 | DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA                                                       | SER    | 04/2010 | 03/2015      | 03/2024         | 651.00                    | 1009.00                      | 358             | 108          |
| 78 | MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD                                            | RVNL   | 04/2012 | 03/2016      | 12/2020         | 632.68                    | 816.55                       | 183.87          | 57           |
| 79 | RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM                                              | SER    | 04/1995 | 12/2021      | 12/2024         | 524.43                    | 939.00                       | 414.57          | 36           |

DOA -&gt; Date of Approval

COR -&gt; Cost Overrun

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

**DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE**

**(DECEMBER 2018)**

| Sn | Project                                                                                      | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|----------------------------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
|    | RUPSA BURAMARA AND EXTENSION OF LINE FRO                                                     |        |         |              |                 |                           |                              |                 |              |
| 80 | PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM | ECR    | 11/2001 | 02/2016      | 03/2021         | 624.47                    | 3550.00                      | 2925.53         | 61           |
| 81 | MUZAFFARPUR SAGALI DOUBLING 100.60 KM                                                        | ECR    | 04/2016 | 03/2021      | 03/2022         | 731.64                    | 1185.73                      | 454.09          | 12           |
| 82 | SAGALI VALMIKINAGAR DOUBLING 109.7 KM                                                        | ECR    | 04/2016 | 03/2021      | 03/2022         | 744.04                    | 1215.54                      | 471.5           | 12           |
| 83 | MANDHANA - BRAHMAWART NEW LINE PROJECT.                                                      | NER    | 04/1997 | 04/1999      | 03/2019         | 609.04                    | 1807.88                      | 1198.84         | 239          |

**ROAD TRANSPORT AND HIGHWAYS**

| Sn | Project                                               | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|-------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 84 | BRAHMPUTRA BRIDGE, NH NO-31                           | NHAI   | 12/2003 | 04/2010      | 04/2019         | 217.61                    | 360.84                       | 143.23          | 108          |
| 85 | 4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 | NHAI   | 04/2014 | 09/2016      | 06/2019         | 1266.60                   | 1544.00                      | 277.4           | 33           |
| 86 | PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)          | NHAI   | 05/2009 | 11/2011      | 06/2019         | 1108.00                   | 2288.00                      | 1180            | 91           |
| 87 | MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000   | NHAI   | 12/2003 | 04/2009      | 03/2019         | 199.81                    | 385.13                       | 185.32          | 119          |
| 88 | FOUR LANING OF GWALIOR-SHIVPURI                       | NHAI   | 05/2013 | 11/2015      | 12/2018         | 1055.00                   | 1601.77                      | 546.77          | 37           |

**SHIPPING AND PORTS**

| Sn | Project                                                                                              | Agency          | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|------------------------------------------------------------------------------------------------------|-----------------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 89 | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB | MUMBAI PORT TRU | 01/2007 | 12/2010      | 12/2018         | 366.39                    | 669.46                       | 303.07          | 96           |
| 90 | ENMORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)                                         | PORT TRUST      | 10/2002 | 03/2006      | 02/2019         | 150.00                    | 600.00                       | 450             | 155          |

**TELECOMMUNICATIONS**

| Sn | Project              | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|----------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 91 | NETWORK FOR SPECTRUM | DOT    | 03/2012 | 07/2015      | 05/2020         | 1,3334.00                 | 2,4664.00                    | 11330           | 58           |

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun



**DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS  
OF RS.100 CRORE AND ABOVE**

**(DECEMBER 2018)**

**URBAN DEVELOPMENT**

| Sn | Project                                                                                                      | Agency | DOA     | DOC<br>Original | DOC<br>Anticipa<br>ted | Cost<br>Original<br>(Rs. crore) | Cost<br>Anticipated<br>(Rs. crore) | COR<br>(Rs.<br>crore) | TOR<br>(Months) |
|----|--------------------------------------------------------------------------------------------------------------|--------|---------|-----------------|------------------------|---------------------------------|------------------------------------|-----------------------|-----------------|
| 92 | CONSTRUCTION OF ITBP ROAD TO<br>INDO-CHINA BORDER FROM NYU<br>SOBLA SELA TO TEDANG IN THE<br>STATE OF UTTARA | CPWD   | 12/2008 | 12/2013         | 10/2019                | 114.26                          | 266.00                             | 151.74                | 70              |

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

## Details of Central Sector Projects

Annexure-XIX

| Details of Central Sector Projects Costing Rs.150 crore and above (as on 31.12.2018 ) |                                                                                                      |                                 |                                                                       |                                                   |                                                                                            |
|---------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------|---------------------------------|-----------------------------------------------------------------------|---------------------------------------------------|--------------------------------------------------------------------------------------------|
| Sl.No                                                                                 | Project                                                                                              | Date of Approval (month / year) | Original (Revised) [Anticipated] Date of Commissioning (month / year) | Original (Revised) [Anticipated] Cost (Rs. crore) | Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [ Time Overrun in months ] |
|                                                                                       | <u>A &amp; N ISLANDS</u>                                                                             |                                 |                                                                       |                                                   |                                                                                            |
|                                                                                       | <u>Civil Aviation</u>                                                                                |                                 |                                                                       |                                                   |                                                                                            |
| 1                                                                                     | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR                           | 10/2013                         | 9/2018<br>(-)<br>[6/2020]                                             | 314.61<br>(-)<br>[441.33]                         | 85.79<br>(126.72)<br>[21]                                                                  |
|                                                                                       | <u>Road Transport And Highways</u>                                                                   |                                 |                                                                       |                                                   |                                                                                            |
| 2                                                                                     | 2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N | 3/2017                          | 12/2017<br>(-)<br>[0/0]                                               | 409.85<br>(-)<br>[409.85]                         | 0.00<br>(0.00)<br>[0]                                                                      |
| 3                                                                                     | CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C | 3/2015                          | 4/2017<br>(-)<br>[0/0]                                                | 277.17<br>(-)<br>[277.17]                         | 0.00<br>(0.00)<br>[0]                                                                      |
| 4                                                                                     | CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 ( | 3/2015                          | 10/2018<br>(-)<br>[0/0]                                               | 262.97<br>(-)<br>[262.97]                         | 0.00<br>(0.00)<br>[0]                                                                      |
| 5                                                                                     | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S | 11/2017                         | 11/2019<br>(12/2019)<br>[11/2019]                                     | 257.34<br>(-)<br>[238.00]                         | 41.09<br>(-19.34)<br>[0]                                                                   |
| 6                                                                                     | REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM | 2/2018                          | 10/2018<br>(-)<br>[0/0]                                               | 391.00<br>(-)<br>[391.00]                         | 0.00<br>(0.00)<br>[0]                                                                      |
| 7                                                                                     | REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O | 3/2018                          | 10/2018<br>(-)<br>[0/0]                                               | 234.27<br>(-)<br>[234.27]                         | 0.00<br>(0.00)<br>[0]                                                                      |
| 8                                                                                     | Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 | 11/2017                         | 11/2019<br>(-)<br>[11/2019]                                           | 237.80<br>(-)<br>[238.00]                         | 29.43<br>(0.20)<br>[0]                                                                     |
|                                                                                       | <u>ANDHRA PRADESH</u>                                                                                |                                 |                                                                       |                                                   |                                                                                            |
|                                                                                       | <u>Health And Family Welfare</u>                                                                     |                                 |                                                                       |                                                   |                                                                                            |
| 9                                                                                     | HOSPITAL AND TEACHING- AIIMS GUNTUR                                                                  | 3/2018                          | /<br>(-)<br>[2/2020]                                                  | 601.02<br>(-)<br>[601.02]                         | 79.63<br>(0.00)<br>[-]                                                                     |
| 10                                                                                    | RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH                          | 8/2017                          | 3/2019<br>(-)<br>[3/2019]                                             | 272.19<br>(-)<br>[272.19]                         | 104.84<br>(0.00)<br>[0]                                                                    |
|                                                                                       | <u>Petroleum</u>                                                                                     |                                 |                                                                       |                                                   |                                                                                            |
| 11                                                                                    | ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE              | 1/2015                          | 3/2021<br>(-)<br>[3/2021]                                             | 342.00<br>(-)<br>[342.00]                         | 0.00<br>(0.00)<br>[0]                                                                      |
| 12                                                                                    | CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH                             | 8/2018                          | 4/2021<br>(-)<br>[7/2021]                                             | 466.00<br>(-)<br>[466.00]                         | 1.53<br>(0.00)<br>[3]                                                                      |
| 13                                                                                    | CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP                                                       | 8/2017                          | 4/2021<br>(-)<br>[4/2021]                                             | 384.58<br>(-)<br>[384.58]                         | 41.38<br>(0.00)<br>[0]                                                                     |

|    |                                                                                                 |         |                                |                                 |                                 |
|----|-------------------------------------------------------------------------------------------------|---------|--------------------------------|---------------------------------|---------------------------------|
| 14 | FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG                                     | 4/2017  | 9/2018<br>(2/2019)<br>[2/2019] | 420.76<br>(207.80)<br>[207.80]  | 32.71<br>(-212.96)<br>[5]       |
| 15 | KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT                                                      | 3/2016  | 6/2020<br>(8/2021)<br>[8/2021] | 34,012.00<br>(-)<br>[34,012.00] | 1,647.21<br>(0.00)<br>[14]      |
| 16 | REVAMPING OF FACILITIES AT VIZAG TERMINAL                                                       | 4/2018  | 4/2022<br>(-)<br>[4/2022]      | 355.00<br>(-)<br>[355.00]       | 0.00<br>(0.00)<br>[0]           |
| 17 | REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM                                               | 7/2014  | 3/2021<br>(-)<br>[3/2021]      | 247.00<br>(-)<br>[247.00]       | 0.00<br>(0.00)<br>[0]           |
| 18 | VISAKH REFINERY MODERNISATION PROJECT                                                           | 7/2016  | 7/2020<br>(-)<br>[7/2020]      | 20,928.00<br>(-)<br>[20,928.00] | 2,757.64<br>(0.00)<br>[0]       |
| 19 | VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT                             | 9/2016  | 9/2019<br>(-)<br>[9/2019]      | 407.00<br>(-)<br>[407.00]       | 262.64<br>(0.00)<br>[0]         |
|    | <u>Railways</u>                                                                                 |         |                                |                                 |                                 |
| 20 | CUMBUM-PRODDATUR                                                                                | 4/2013  | /<br>(-)<br>[0/0]              | 829.00<br>(-)<br>[1,599.39]     | 0.94<br>(770.39)<br>[0]         |
| 21 | DUVVADA-VIJAYAWADA                                                                              | 4/2015  | /<br>(-)<br>[0/0]              | 3,873.07<br>(-)<br>[3,873.07]   | 0.07<br>(0.00)<br>[0]           |
| 22 | GUDUR-DURGARAJAPATNAM                                                                           | 4/2011  | /<br>(-)<br>[0/0]              | 761.37<br>(-)<br>[761.37]       | 0.52<br>(0.00)<br>[0]           |
| 23 | GUNTUR-GUNTAKAL                                                                                 | 4/2016  | 3/2022<br>(-)<br>[3/2023]      | 3,631.00<br>(-)<br>[3,631.00]   | 124.49<br>(0.00)<br>[12]        |
| 24 | KOTLPALLI-NARASAPUR (NL) (SCR)                                                                  | 12/2001 | 3/2009<br>(-)<br>[3/2023]      | 1,045.20<br>(-)<br>[2,120.16]   | 289.91<br>(1,074.96)<br>[168]   |
| 25 | KOTTAVALSA - KORAPUT DOUBLING                                                                   | 4/2015  | 3/2022<br>(-)<br>[3/2022]      | 2,499.71<br>(-)<br>[2,499.71]   | 183.68<br>(0.00)<br>[0]         |
| 26 | MULTI MODAL LOGISTICS PARK AT KAKINADA                                                          | 8/2016  | 3/2019<br>(-)<br>[12/2020]     | 234.50<br>(-)<br>[235.00]       | 2.98<br>(0.50)<br>[21]          |
| 27 | MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM                                                    | 1/2013  | 3/2018<br>(-)<br>[0/0]         | 387.70<br>(-)<br>[387.70]       | 323.91<br>(0.00)<br>[0]         |
| 28 | NADIKUDE-SRI KALAHASTI                                                                          | 4/2011  | 3/2021<br>(-)<br>[3/2022]      | 2,288.70<br>(-)<br>[2,288.70]   | 375.28<br>(0.00)<br>[12]        |
| 29 | NANDYAL-YERRAGUNTALA(NL),SCR                                                                    | 3/1996  | 2/2009<br>(-)<br>[0/0]         | 164.36<br>(-)<br>[1,050.00]     | 999.64<br>(885.64)<br>[0]       |
| 30 | OBULAVARIPALLE-KRISHNAPATNAM(RVNL)                                                              | 7/2006  | 3/2008<br>(-)<br>[3/2020]      | 732.81<br>(-)<br>[1,850.00]     | 1,981.73<br>(1,117.19)<br>[144] |
| 31 | VIJAYAWADA-GUDUR                                                                                | 4/2015  | 12/2023<br>(-)<br>[12/2023]    | 3,246.26<br>(-)<br>[3,548.67]   | 132.79<br>(302.41)<br>[0]       |
| 32 | VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)                                            | 3/2012  | 3/2020<br>(-)<br>[3/2022]      | 1,503.71<br>(-)<br>[1,503.71]   | 1,134.27<br>(0.00)<br>[24]      |
|    | <u>Road Transport And Highways</u>                                                              |         |                                |                                 |                                 |
| 33 | 6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE | 12/2017 | /<br>(-)                       | 328.67<br>(-)                   | 0.00<br>(0.00)                  |

|    |                                                                                                       |         |                             |                                |                            |
|----|-------------------------------------------------------------------------------------------------------|---------|-----------------------------|--------------------------------|----------------------------|
|    | FROM                                                                                                  |         | [0/0]                       | [328.67]                       | [0]                        |
| 34 | CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O  | 12/2017 | /<br>(-)<br>[0/0]           | 357.00<br>(-)<br>[357.00]      | 0.00<br>(0.00)<br>[0]      |
| 35 | CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA FROM KM 470.415 | 3/2018  | /<br>(-)<br>[0/0]           | 557.30<br>(-)<br>[557.30]      | 0.00<br>(0.00)<br>[0]      |
| 36 | CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1  | 3/2018  | /<br>(-)<br>[0/0]           | 314.43<br>(-)<br>[314.43]      | 0.00<br>(0.00)<br>[0]      |
| 37 | CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM                                                        | 11/2010 | 5/2013<br>(-)<br>[4/2019]   | 1,585.00<br>(-)<br>[1,585.00]  | 2,167.31<br>(0.00)<br>[71] |
| 38 | FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C  | 10/2015 | 11/2015<br>(-)<br>[0/0]     | 333.21<br>(-)<br>[333.21]      | 0.00<br>(0.00)<br>[0]      |
| 39 | FOUR LANING OF 5.122 KM OF NH9 ( NEW NH 65) FROM KM 269.900 ( DESIGN CH0.0 ) TO KM 275-622( DESIGN C  | 7/2015  | 12/2015<br>(-)<br>[0/0]     | 333.21<br>(333.21)<br>[333.21] | 0.00<br>(0.00)<br>[0]      |
| 40 | FOUR LANING OF 5.122 KM OF NH9( NEW NH 65) FROM KM 269.900( DESIGN CH0.0 )                            | 7/2015  | 12/2015<br>(-)<br>[0/0]     | 333.21<br>(-)<br>[333.21]      | 0.00<br>(0.00)<br>[0]      |
| 41 | FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)   | 3/2018  | 3/2021<br>(-)<br>[3/2021]   | 1,532.62<br>(-)<br>[1,532.62]  | 0.00<br>(0.00)<br>[0]      |
| 42 | FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)        | 6/2017  | 6/2017<br>(-)<br>[11/2019]  | 648.33<br>(-)<br>[648.33]      | 15.89<br>(0.00)<br>[29]    |
| 43 | FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800)                                 | 1/2016  | 11/2018<br>(-)<br>[11/2018] | 1,134.97<br>(-)<br>[1,134.97]  | 28.73<br>(0.00)<br>[0]     |
| 44 | REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K  | 10/2015 | /<br>(-)<br>[0/0]           | 480.21<br>(-)<br>[480.21]      | 0.00<br>(0.00)<br>[0]      |
| 45 | REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR  | 7/2015  | /<br>(-)<br>[0/0]           | 314.43<br>(-)<br>[314.43]      | 0.00<br>(0.00)<br>[0]      |
| 46 | REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUEDEM TO A | 12/2014 | 2/2015<br>(-)<br>[0/0]      | 201.12<br>(201.00)<br>[201.12] | 0.00<br>(0.00)<br>[0]      |
| 47 | REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC   | 1/2014  | 7/2014<br>(-)<br>[0/0]      | 361.30<br>(-)<br>[207.40]      | 44.08<br>(-153.90)<br>[0]  |
| 48 | REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150                        | 2/2015  | 5/2015<br>(-)<br>[0/0]      | 224.83<br>(-)<br>[224.83]      | 0.00<br>(0.00)<br>[0]      |
| 49 | REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T   | 1/2014  | 11/2014<br>(-)<br>[0/0]     | 195.45<br>(-)<br>[195.45]      | 0.00<br>(0.00)<br>[0]      |
| 50 | REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO     | 2/2014  | 11/2014<br>(-)<br>[0/0]     | 170.21<br>(-)<br>[170.21]      | 5.65<br>(0.00)<br>[0]      |
| 51 | REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS  | 3/2018  | /<br>(-)<br>[0/0]           | 565.09<br>(-)<br>[565.09]      | 0.00<br>(0.00)<br>[0]      |
| 52 | REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T  | 3/2015  | /<br>(-)<br>[0/0]           | 175.03<br>(-)<br>[175.00]      | 0.00<br>(-0.03)<br>[0]     |
| 53 | REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION )      | 2/2015  | 2/2017<br>(-)<br>[0/0]      | 241.61<br>(-)<br>[241.61]      | 7.71<br>(0.00)<br>[0]      |

|    |                                                                                                      |         |                             |                                |                               |
|----|------------------------------------------------------------------------------------------------------|---------|-----------------------------|--------------------------------|-------------------------------|
| 54 | REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70                                                  | 2/2015  | 4/2015<br>(-)<br>[0/0]      | 224.83<br>(-)<br>[224.83]      | 0.00<br>(0.00)<br>[0]         |
| 55 | REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES  | 3/2015  | 10/2015<br>(-)<br>[0/0]     | 271.45<br>(-)<br>[271.45]      | 0.00<br>(0.00)<br>[0]         |
| 56 | REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER                      | 3/2017  | 3/2020<br>(-)<br>[3/2020]   | 648.32<br>(-)<br>[503.10]      | 15.10<br>(-145.22)<br>[0]     |
| 57 | REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP | 2/2015  | /<br>(-)<br>[0/0]           | 266.00<br>(-)<br>[266.00]      | 0.00<br>(0.00)<br>[0]         |
| 58 | REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU  | 3/2015  | 9/2015<br>(-)<br>[0/0]      | 309.01<br>(-)<br>[309.01]      | 0.00<br>(0.00)<br>[0]         |
| 59 | REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) | 2/2014  | 7/2014<br>(-)<br>[0/0]      | 258.99<br>(-)<br>[258.99]      | 16.54<br>(0.00)<br>[0]        |
| 60 | REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION | 2/2014  | 6/2014<br>(-)<br>[0/0]      | 417.61<br>(-)<br>[417.61]      | 0.00<br>(0.00)<br>[0]         |
| 61 | REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN | 11/2014 | 2/2017<br>(-)<br>[0/0]      | 297.78<br>(330.00)<br>[330.00] | 0.00<br>(32.22)<br>[0]        |
| 62 | REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC | 7/2014  | 2/2015<br>(-)<br>[0/0]      | 251.55<br>(-)<br>[251.55]      | 7.74<br>(0.00)<br>[0]         |
| 63 | SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM | 2/2018  | /<br>(-)<br>[0/0]           | 1,959.00<br>(-)<br>[1,959.00]  | 0.00<br>(0.00)<br>[0]         |
| 64 | SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN | 12/2017 | /<br>(-)<br>[0/0]           | 1,323.15<br>(-)<br>[1,323.15]  | 0.00<br>(0.00)<br>[0]         |
| 65 | SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG | 3/2018  | /<br>(-)<br>[0/0]           | 1,550.98<br>(-)<br>[1,550.98]  | 0.00<br>(0.00)<br>[0]         |
| 66 | SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547                                      | 11/2011 | 5/2014<br>(-)<br>[0/0]      | 1,535.00<br>(-)<br>[1,535.00]  | 2,993.77<br>(0.00)<br>[0]     |
| 67 | SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000                 | 3/2017  | 3/2020<br>(-)<br>[5/2020]   | 1,041.62<br>(-)<br>[1,187.10]  | 43.99<br>(145.48)<br>[2]      |
| 68 | TIRUPATI - TIRUTHANI - CHENNAI                                                                       | 4/2011  | 10/2013<br>(-)<br>[12/2018] | 571.00<br>(-)<br>[571.00]      | 582.52<br>(0.00)<br>[62]      |
| 69 | VIJAYAWADA-GUNDUGOLANU SECTION                                                                       | 9/2014  | 2/2017<br>(-)<br>[0/0]      | 1,684.00<br>(-)<br>[1,684.00]  | 54.13<br>(0.00)<br>[0]        |
|    | <u>Steel</u>                                                                                         |         |                             |                                |                               |
| 70 | ADDITIONAL WATER STORAGE RESERVOIR(KBR-II)                                                           | 7/2015  | 7/2018<br>(-)<br>[1/2019]   | 465.85<br>(-)<br>[465.85]      | 276.25<br>(0.00)<br>[6]       |
| 71 | CENTRAL DISPATCH YARD                                                                                | 8/2015  | 8/2018<br>(-)<br>[2/2019]   | 320.66<br>(-)<br>[320.66]      | 125.36<br>(0.00)<br>[6]       |
| 72 | COKE OVEN BATTERY-5                                                                                  | 12/2011 | 12/2017<br>(-)<br>[9/2019]  | 2,858.00<br>(-)<br>[2,500.00]  | 1,053.76<br>(-358.00)<br>[21] |
| 73 | REVAMPING OF SINTER MACHINES - 1 AND 2                                                               | 12/2009 | 10/2016<br>(-)<br>[0/0]     | 343.00<br>(-)<br>[488.40]      | 239.65<br>(145.40)<br>[0]     |

|    |                                                                                                       |         |                                 |                                      |                                 |
|----|-------------------------------------------------------------------------------------------------------|---------|---------------------------------|--------------------------------------|---------------------------------|
|    | <u>Urban Development</u>                                                                              |         |                                 |                                      |                                 |
| 74 | CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP                                                 | 1/2018  | 3/2019<br>(-)<br>[3/2019]       | 206.58<br>(-)<br>[206.58]            | 0.02<br>(0.00)<br>[0]           |
| 75 | CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA      | 7/2014  | /<br>(-)<br>[0/0]               | 232.00<br>(-)<br>[232.00]            | 0.00<br>(0.00)<br>[0]           |
| 76 | CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD                           | 6/2014  | 3/2017<br>(-)<br>[0/0]          | 157.84<br>(-)<br>[157.84]            | 134.62<br>(0.00)<br>[0]         |
| 77 | REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2       | 8/2007  | /<br>(-)<br>[0/0]               | 246.90<br>(-)<br>[246.90]            | 0.00<br>(0.00)<br>[0]           |
|    | <u>ARUNACHAL PRADESH</u>                                                                              |         |                                 |                                      |                                 |
|    | <u>Petroleum</u>                                                                                      |         |                                 |                                      |                                 |
| 78 | RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH                                                 | 1/2016  | 2/2019<br>(-)<br>[1/2019]       | 247.52<br>(-)<br>[247.52]            | 144.38<br>(0.00)<br>[-1]        |
|    | <u>Power</u>                                                                                          |         |                                 |                                      |                                 |
| 79 | KAMENG HYDROELECTRIC PROJECT (NEEPCO)                                                                 | 12/2004 | 12/2009<br>(3/2019)<br>[3/2019] | 2,496.90<br>(6,179.96)<br>[6,179.96] | 6,881.48<br>(3,683.06)<br>[111] |
| 80 | SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)                                                               | 9/2003  | 9/2010<br>(-)<br>[0/0]          | 6,285.33<br>(-)<br>[19,496.34]       | 10,421.62<br>(13,211.01)<br>[0] |
|    | <u>Road Transport And Highways</u>                                                                    |         |                                 |                                      |                                 |
| 81 | 2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH              | 3/2015  | 6/2018<br>(-)<br>[0/0]          | 394.00<br>(-)<br>[394.00]            | 0.00<br>(0.00)<br>[0]           |
| 82 | 2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28                                 | 3/2015  | 5/2018<br>(-)<br>[0/0]          | 235.08<br>(-)<br>[235.08]            | 47.81<br>(0.00)<br>[0]          |
| 83 | 2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59  | 3/2015  | 5/2018<br>(-)<br>[0/0]          | 194.11<br>(-)<br>[194.11]            | 30.54<br>(0.00)<br>[0]          |
| 84 | 2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS                              | 10/2015 | 1/2019<br>(-)<br>[1/2019]       | 179.82<br>(-)<br>[179.82]            | 8.99<br>(0.00)<br>[0]           |
| 85 | 2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450 | 1/2016  | 11/2016<br>(-)<br>[0/0]         | 183.65<br>(-)<br>[183.65]            | 0.00<br>(0.00)<br>[0]           |
| 86 | CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120                                 | 12/2016 | 1/2017<br>(-)<br>[1/2020]       | 138.93<br>(155.00)<br>[155.00]       | 0.00<br>(16.07)<br>[36]         |
| 87 | CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD( NEAR ITHUN BRIDGE) TO KM 37  | 4/2016  | /<br>(-)<br>[0/0]               | 245.79<br>(-)<br>[245.79]            | 0.00<br>(0.00)<br>[0]           |
| 88 | CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.   | 4/2016  | 10/2016<br>(-)<br>[0/0]         | 198.00<br>(-)<br>[198.00]            | 0.00<br>(0.00)<br>[0]           |
| 89 | CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH  | 7/2015  | 10/2018<br>(-)<br>[0/0]         | 197.16<br>(-)<br>[197.16]            | 38.50<br>(0.00)<br>[0]          |
| 90 | CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN      | 1/2017  | 3/2017<br>(-)<br>[0/0]          | 1,253.10<br>(-)<br>[1,253.10]        | 0.00<br>(0.00)<br>[0]           |
| 91 | CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI  | 2/2017  | 4/2017<br>(-)<br>[0/0]          | 167.28<br>(-)<br>[167.28]            | 0.00<br>(0.00)<br>[0]           |
| 92 | CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON                      | 2/2017  | 4/2017<br>(-)                   | 216.71<br>(-)                        | 0.00<br>(0.00)                  |

|     |                                                                                                      |         |          |            |          |
|-----|------------------------------------------------------------------------------------------------------|---------|----------|------------|----------|
|     | EPC BASIS FROM EXIS                                                                                  |         | [0/0]    | [216.71]   | [0]      |
| 93  | FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K | 3/2018  | /        | 392.60     | 0.00     |
|     |                                                                                                      |         | (-)      | (-)        | (0.00)   |
|     |                                                                                                      |         | [0/0]    | [392.60]   | [0]      |
| 94  | FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A'  | 1/2011  | /        | 264.16     | 0.00     |
|     |                                                                                                      |         | (-)      | (-)        | (0.00)   |
|     |                                                                                                      |         | [0/0]    | [264.16]   | [0]      |
| 95  | FUNDED ) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE | 1/2016  | 6/2016   | 334.22     | 0.00     |
|     |                                                                                                      |         | (-)      | (-)        | (0.00)   |
|     |                                                                                                      |         | [0/0]    | [334.22]   | [0]      |
| 96  | FUNDED ) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH | 11/2015 | /        | 434.06     | 0.00     |
|     |                                                                                                      |         | (-)      | (-)        | (0.00)   |
|     |                                                                                                      |         | [0/0]    | [434.06]   | [0]      |
| 97  | TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM | 3/2017  | 4/2017   | 284.09     | 0.00     |
|     |                                                                                                      |         | (-)      | (-)        | (0.00)   |
|     |                                                                                                      |         | [0/0]    | [284.09]   | [0]      |
| 98  | TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 | 2/2017  | 4/2017   | 195.23     | 0.00     |
|     |                                                                                                      |         | (-)      | (-)        | (0.00)   |
|     |                                                                                                      |         | [0/0]    | [195.23]   | [0]      |
| 99  | TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST | 2/2017  | 4/2017   | 203.36     | 0.00     |
|     |                                                                                                      |         | (-)      | (-)        | (0.00)   |
|     |                                                                                                      |         | [0/0]    | [203.36]   | [0]      |
| 100 | TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.  | 1/2017  | 4/2017   | 194.66     | 0.00     |
|     |                                                                                                      |         | (-)      | (-)        | (0.00)   |
|     |                                                                                                      |         | [0/0]    | [194.66]   | [0]      |
| 101 | TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.  | 1/2017  | 4/2017   | 198.22     | 0.00     |
|     |                                                                                                      |         | (-)      | (-)        | (0.00)   |
|     |                                                                                                      |         | [0/0]    | [198.22]   | [0]      |
| 102 | TWO LANING OF GOBOK - SIJON NALLAH (CORRECSponding TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR | 3/2012  | 5/2012   | 207.03     | 0.00     |
|     |                                                                                                      |         | (-)      | (-)        | (0.00)   |
|     |                                                                                                      |         | [0/0]    | [207.03]   | [0]      |
| 103 | TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA | 12/2009 | 9/2010   | 165.00     | 0.00     |
|     |                                                                                                      |         | (-)      | (-)        | (0.00)   |
|     |                                                                                                      |         | [0/0]    | [165.00]   | [0]      |
| 104 | TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX  | 2/2017  | 4/2017   | 180.57     | 0.00     |
|     |                                                                                                      |         | (-)      | (-)        | (0.00)   |
|     |                                                                                                      |         | [0/0]    | [180.57]   | [0]      |
| 105 | TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS  | 2/2017  | 4/2017   | 168.32     | 0.00     |
|     |                                                                                                      |         | (-)      | (-)        | (0.00)   |
|     |                                                                                                      |         | [0/0]    | [168.32]   | [0]      |
| 106 | TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA | 12/2011 | 2/2012   | 156.63     | 132.21   |
|     |                                                                                                      |         | (-)      | (276.00)   | (119.37) |
|     |                                                                                                      |         | [0/0]    | [276.00]   | [0]      |
| 107 | TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P | 11/2010 | 3/2011   | 305.49     | 0.00     |
|     |                                                                                                      |         | (-)      | (-)        | (0.00)   |
|     |                                                                                                      |         | [0/0]    | [305.49]   | [0]      |
| 108 | TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF | 12/2009 | 9/2010   | 104.00     | 0.00     |
|     |                                                                                                      |         | (-)      | (-)        | (97.00)  |
|     |                                                                                                      |         | [0/0]    | [201.00]   | [0]      |
|     | <u>ASSAM</u>                                                                                         |         |          |            |          |
|     | <u>Health And Family Welfare</u>                                                                     |         |          |            |          |
| 109 | ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM                                            | 5/2017  | 5/2021   | 875.00     | 174.00   |
|     |                                                                                                      |         | (-)      | (-)        | (0.00)   |
|     |                                                                                                      |         | [5/2021] | [875.00]   | [0]      |
| 110 | LGBRIMH-TEZPUR, ASSAM                                                                                | 7/2012  | 12/2014  | 175.57     | 113.50   |
|     |                                                                                                      |         | (-)      | (-)        | (0.00)   |
|     |                                                                                                      |         | [0/0]    | [175.57]   | [0]      |
|     | <u>Petroleum</u>                                                                                     |         |          |            |          |
| 111 | ASSAM RENEWAL PROJECT FOR GROUP A                                                                    | 3/2009  | 3/2013   | 2,465.15   | 2,107.69 |
|     |                                                                                                      |         | (3/2019) | (-)        | (-86.29) |
|     |                                                                                                      |         | [3/2019] | [2,378.86] | [72]     |

|     |                                                                                                      |         |                                  |                                      |                                |
|-----|------------------------------------------------------------------------------------------------------|---------|----------------------------------|--------------------------------------|--------------------------------|
| 112 | BS VI PROJECT AT GUWAHATI REFINERY                                                                   | 8/2018  | 2/2020<br>(-)<br>[2/2020]        | 557.00<br>(-)<br>[557.00]            | 71.41<br>(0.00)<br>[0]         |
| 113 | BS-VI PROJECT AT BONGAIGAON REFINERY                                                                 | 5/2018  | 9/2019<br>(-)<br>[9/2019]        | 1,222.00<br>(-)<br>[1,222.00]        | 287.90<br>(0.00)<br>[0]        |
| 114 | CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN                                                   | 7/2011  | 1/2019<br>(-)<br>[9/2019]        | 350.00<br>(-)<br>[350.00]            | 2.06<br>(0.00)<br>[8]          |
| 115 | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)                               | 6/2010  | 1/2014<br>(11/2019)<br>[11/2019] | 202.94<br>(341.70)<br>[330.35]       | 81.98<br>(127.41)<br>[70]      |
| 116 | DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT   | 6/2016  | 8/2019<br>(-)<br>[8/2019]        | 423.00<br>(-)<br>[423.00]            | 217.07<br>(0.00)<br>[0]        |
| 117 | DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA | 1/2018  | 2/2020<br>(-)<br>[2/2020]        | 543.91<br>(-)<br>[543.91]            | 1.65<br>(0.00)<br>[0]          |
| 118 | INDMAX PROJECT AT BONGAIGAON REFINERY                                                                | 2/2016  | 11/2019<br>(-)<br>[11/2019]      | 2,582.00<br>(-)<br>[2,582.00]        | 1,281.75<br>(0.00)<br>[0]      |
| 119 | PIPELINE NETWORK PROJECT GELEKI, ASSAM                                                               | 7/2016  | 5/2020<br>(5/2020)<br>[5/2020]   | 249.85<br>(249.85)<br>[244.70]       | 101.71<br>(-5.15)<br>[0]       |
| 120 | UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE               | 9/2012  | 3/2015<br>(-)<br>[0/0]           | 871.35<br>(-)<br>[1,200.00]          | 565.63<br>(328.65)<br>[0]      |
|     | <u>Power</u>                                                                                         |         |                                  |                                      |                                |
| 121 | BONGAIGAON THERMAL POWER PROJECT                                                                     | 1/2008  | 9/2011<br>(6/2018)<br>[1/2019]   | 4,375.35<br>(8,150.00)<br>[8,150.00] | 7,220.84<br>(3,774.65)<br>[88] |
|     | <u>Railways</u>                                                                                      |         |                                  |                                      |                                |
| 122 | AMBARI FALAKATA TO NEW MAYNAGURI                                                                     | 4/2011  | 3/2019<br>(-)<br>[3/2019]        | 314.00<br>(486.96)<br>[551.00]       | 602.54<br>(237.00)<br>[0]      |
| 123 | BONGAIGAON-GOALPARA-GUWAHATI (176 KM)                                                                | 4/2015  | 3/2022<br>(-)<br>[3/2020]        | 2,232.32<br>(-)<br>[2,182.00]        | 235.52<br>(-50.32)<br>[-24]    |
| 124 | DIGARU-HOJAI (102 KM)                                                                                | 4/2015  | 3/2021<br>(-)<br>[3/2021]        | 870.96<br>(-)<br>[821.00]            | 214.95<br>(-49.96)<br>[0]      |
| 125 | LUMDING-HOJAI PATCH DOUBLING PROJECT                                                                 | 4/2012  | 3/2019<br>(-)<br>[3/2019]        | 246.07<br>(614.81)<br>[398.93]       | 328.77<br>(152.86)<br>[0]      |
| 126 | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR                                      | 9/2006  | 3/2019<br>(-)<br>[3/2020]        | 385.20<br>(-)<br>[1,532.00]          | 574.07<br>(1,146.80)<br>[12]   |
|     | <u>Road Transport And Highways</u>                                                                   |         |                                  |                                      |                                |
| 127 | 2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM               | 11/2010 | 5/2017<br>(-)<br>[0/0]           | 268.08<br>(-)<br>[268.08]            | 0.00<br>(0.00)<br>[0]          |
| 128 | 2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR   | 11/2010 | 2/2011<br>(-)<br>[0/0]           | 470.20<br>(-)<br>[470.20]            | 0.00<br>(0.00)<br>[0]          |
| 129 | 4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS      | 12/2015 | 12/2018<br>(-)<br>[12/2018]      | 225.02<br>(-)<br>[159.20]            | 0.00<br>(-65.82)<br>[0]        |
| 130 | 4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A                | 12/2015 | 6/2018<br>(-)<br>[0/0]           | 223.30<br>(-)<br>[223.30]            | 0.00<br>(0.00)<br>[0]          |
| 131 | 4 LANING FROM JAMUGURI TO BISWANATH CHARIALI                                                         | 1/1991  | /                                | 520.01                               | 0.00                           |



|     |                                                                                                      |         |                             |                           |                             |
|-----|------------------------------------------------------------------------------------------------------|---------|-----------------------------|---------------------------|-----------------------------|
|     | FROM KM 182 TO KM 208 OF NH-52                                                                       |         | (-)<br>[0/0]                | (-)<br>[520.01]           | (0.00)<br>[0]               |
| 132 | 4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL  | 10/2014 | 11/2018<br>(-)<br>[0/0]     | 588.95<br>(-)<br>[588.95] | 80.00<br>(0.00)<br>[0]      |
| 133 | 4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.      | 12/2015 | 12/2018<br>(-)<br>[12/2018] | 289.99<br>(-)<br>[289.99] | 0.00<br>(0.00)<br>[0]       |
| 134 | 4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561   | 1/2016  | 1/2016<br>(-)<br>[0/0]      | 252.00<br>(-)<br>[252.00] | 0.00<br>(0.00)<br>[0]       |
| 135 | 4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) | 6/2015  | 6/2018<br>(-)<br>[0/0]      | 437.39<br>(-)<br>[437.39] | 21.86<br>(0.00)<br>[0]      |
| 136 | 4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O   | 1/2016  | 1/2016<br>(-)<br>[0/0]      | 294.17<br>(-)<br>[294.17] | 0.00<br>(0.00)<br>[0]       |
| 137 | BRAHMPUTRA BRIDGE,NH NO-31                                                                           | 12/2003 | 4/2010<br>(-)<br>[4/2019]   | 217.61<br>(-)<br>[360.84] | 390.19<br>(143.23)<br>[108] |
| 138 | DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)                                                              | 12/2003 | 5/2008<br>(-)<br>[2/2019]   | 160.00<br>(-)<br>[167.98] | 198.82<br>(7.98)<br>[129]   |
| 139 | FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52                      | 6/2016  | 1/2019<br>(-)<br>[1/2019]   | 829.00<br>(-)<br>[829.00] | 59.85<br>(0.00)<br>[0]      |
| 140 | FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A             | 3/2015  | 11/2018<br>(-)<br>[0/0]     | 168.39<br>(-)<br>[168.39] | 16.84<br>(0.00)<br>[0]      |
| 141 | FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 | 6/2015  | 6/2018<br>(-)<br>[0/0]      | 463.49<br>(-)<br>[463.49] | 9.26<br>(0.00)<br>[0]       |
| 142 | FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL | 3/2015  | 1/2016<br>(-)<br>[0/0]      | 829.00<br>(-)<br>[829.00] | 0.00<br>(0.00)<br>[0]       |
| 143 | FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM | 5/2015  | 5/2018<br>(-)<br>[0/0]      | 454.89<br>(-)<br>[454.89] | 22.74<br>(0.00)<br>[0]      |
| 144 | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700                                               | 12/2003 | 2/2009<br>(-)<br>[12/2018]  | 280.00<br>(-)<br>[361.00] | 410.32<br>(81.00)<br>[118]  |
| 145 | HARANGAJO TO MAIBANG, NH-54                                                                          | 12/2003 | 7/2009<br>(-)<br>[0/0]      | 196.00<br>(-)<br>[331.23] | 340.12<br>(135.23)<br>[0]   |
| 146 | MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450                                                 | 12/2003 | 11/2008<br>(-)<br>[0/0]     | 155.04<br>(-)<br>[280.13] | 195.35<br>(125.09)<br>[0]   |
| 147 | MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000                                                  | 12/2003 | 4/2009<br>(-)<br>[3/2019]   | 199.81<br>(-)<br>[385.13] | 209.80<br>(185.32)<br>[119] |
| 148 | MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54                                            | 12/2003 | 11/2008<br>(-)<br>[9/2018]  | 167.64<br>(-)<br>[167.64] | 268.94<br>(0.00)<br>[0]     |
| 149 | NALBARI T BIJNI (AS-7)                                                                               | 12/2003 | 4/2008<br>(-)<br>[3/2019]   | 208.00<br>(-)<br>[230.00] | 297.81<br>(22.00)<br>[131]  |
| 150 | NALBARI TO BIJNI (AS-6)                                                                              | 12/2003 | 6/2008<br>(-)<br>[4/2019]   | 225.00<br>(-)<br>[225.00] | 312.79<br>(0.00)<br>[130]   |
| 151 | SONAPUR TO GUWAHTI (AS-3)                                                                            | 12/2003 | 3/2008<br>(-)               | 245.00<br>(174.34)        | 214.88<br>(-70.66)          |

|     |                                                                                                      |         |                                |                                        |                                  |
|-----|------------------------------------------------------------------------------------------------------|---------|--------------------------------|----------------------------------------|----------------------------------|
|     |                                                                                                      |         | [1/2019]                       | [174.34]                               | [130]                            |
| 152 | STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM | 5/2011  | 2/2018<br>(-)<br>[0/0]         | 176.22<br>(-)<br>[176.22]              | 0.00<br>(0.00)<br>[0]            |
| 153 | STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ  | 11/2014 | 2/2018<br>(-)<br>[0/0]         | 218.31<br>(-)<br>[218.31]              | 0.00<br>(0.00)<br>[0]            |
|     | <b>BIHAR</b>                                                                                         |         |                                |                                        |                                  |
|     | <b>Petroleum</b>                                                                                     |         |                                |                                        |                                  |
| 154 | BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL                                             | 5/2016  | 12/2020<br>(-)<br>[2/2020]     | 664.00<br>(-)<br>[664.00]              | 455.62<br>(0.00)<br>[-10]        |
| 155 | CITY GAS DISTRIBUTION (CGD) NETWORK PATNA                                                            | 10/2017 | 10/2022<br>(-)<br>[10/2022]    | 359.25<br>(-)<br>[359.25]              | 38.05<br>(0.00)<br>[0]           |
| 156 | CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR                                           | 4/2018  | 3/2021<br>(-)<br>[3/2021]      | 522.00<br>(-)<br>[522.00]              | 2.56<br>(0.00)<br>[0]            |
| 157 | DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY            | 12/2017 | 10/2020<br>(-)<br>[10/2020]    | 199.36<br>(-)<br>[199.36]              | 0.00<br>(0.00)<br>[0]            |
| 158 | FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY                                  | 7/2015  | 11/2018<br>(-)<br>[3/2019]     | 822.66<br>(-)<br>[822.66]              | 868.92<br>(0.00)<br>[4]          |
| 159 | INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY                                                    | 7/2018  | 1/2021<br>(-)<br>[1/2021]      | 189.00<br>(-)<br>[189.00]              | 4.04<br>(0.00)<br>[0]            |
| 160 | LPG BP PROJECT MOTIHARI                                                                              | 5/2018  | 3/2021<br>(-)<br>[3/2021]      | 206.50<br>(-)<br>[206.50]              | 0.00<br>(0.00)<br>[0]            |
| 161 | MOTIHARI AMLEKHGANJ PIPELINE                                                                         | 9/2015  | 6/2020<br>(-)<br>[6/2020]      | 324.00<br>(-)<br>[324.00]              | 96.21<br>(0.00)<br>[0]           |
|     | <b>Power</b>                                                                                         |         |                                |                                        |                                  |
| 162 | ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS                                                 | 4/2016  | 6/2019<br>(6/2019)<br>[6/2019] | 790.13<br>(790.30)<br>[790.30]         | 524.14<br>(0.17)<br>[0]          |
| 163 | BARH STPP(3X660MW) NTPC                                                                              | 2/2005  | 1/2011<br>(4/2021)<br>[4/2021] | 8,692.97<br>(15,095.67)<br>[15,095.67] | 15,278.98<br>(6,402.70)<br>[123] |
| 164 | BRBCL-NABINAGAR TPP- JV (4X250 MW)                                                                   | 1/2007  | 5/2014<br>(-)<br>[5/2019]      | 5,353.00<br>(-)<br>[7,998.00]          | 7,511.72<br>(2,645.00)<br>[60]   |
| 165 | NPGCPL-NABINAGAR STPP - JV (3X660 MW)                                                                | 1/2013  | 1/2018<br>(-)<br>[5/2020]      | 12,964.60<br>(-)<br>[13,731.26]        | 12,593.00<br>(766.66)<br>[28]    |
| 166 | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT                                     | 5/2015  | 12/2016<br>(-)<br>[3/2019]     | 436.68<br>(-)<br>[602.44]              | 537.08<br>(165.76)<br>[27]       |
|     | <b>Railways</b>                                                                                      |         |                                |                                        |                                  |
| 167 | ARA-BHABHUA ROAD (NL)                                                                                | 4/2008  | /<br>(-)<br>[0/0]              | 633.87<br>(-)<br>[2,396.88]            | 0.39<br>(1,763.01)<br>[0]        |
| 168 | ARARIA-SUPAUL (NL)                                                                                   | 4/2008  | /<br>(-)<br>[3/2023]           | 1,605.17<br>(-)<br>[1,605.17]          | 0.19<br>(0.00)<br>[-]            |
| 169 | BIHTA-AURANGABAD (NL)                                                                                | 4/2008  | /<br>(-)<br>[0/0]              | 326.20<br>(-)<br>[2,995.01]            | 1.68<br>(2,668.81)<br>[0]        |
| 170 | CHHAPRA-MUZAFFARPUR (NL)                                                                             | 4/2006  | /<br>(-)                       | 378.56<br>(-)                          | 111.71<br>(2,235.80)             |

|     |                                                                                                      |         |           |            |            |
|-----|------------------------------------------------------------------------------------------------------|---------|-----------|------------|------------|
|     |                                                                                                      |         | [3/2022]  | [2,614.36] | [-]        |
| 171 | DANIAWAN-BIHARSARIF (NL), ECR                                                                        | 4/2001  | /         | 406.92     | 200.00     |
|     |                                                                                                      |         | (-)       | (-)        | (-67.92)   |
|     |                                                                                                      |         | [0/0]     | [339.00]   | [0]        |
| 172 | DARBANGHA-KUSHESHWARSTHAN (NL)                                                                       | 4/2005  | /         | 205.00     | 5.21       |
|     |                                                                                                      |         | (-)       | (-)        | (0.00)     |
|     |                                                                                                      |         | [0/0]     | [205.00]   | [0]        |
| 173 | FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, | 4/1991  | /         | 329.39     | 759.20     |
|     |                                                                                                      |         | (-)       | (-)        | (237.02)   |
|     |                                                                                                      |         | [12/2021] | [566.41]   | [-]        |
| 174 | GAYA-DALTONGANJ VIA RAFIGANJ (NL)                                                                    | 4/2008  | /         | 445.25     | 0.00       |
|     |                                                                                                      |         | (-)       | (-)        | (2,415.30) |
|     |                                                                                                      |         | [0/0]     | [2,860.55] | [0]        |
| 175 | HAJIPUR-RAMDAYALUNAGAR DOUBLING                                                                      | 4/2013  | /         | 213.01     | 13.00      |
|     |                                                                                                      |         | (-)       | (-)        | (154.16)   |
|     |                                                                                                      |         | [0/0]     | [367.17]   | [0]        |
| 176 | HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR                                                               | 4/2003  | /         | 528.65     | 330.82     |
|     |                                                                                                      |         | (-)       | (-)        | (1,538.12) |
|     |                                                                                                      |         | [3/2023]  | [2,066.77] | [-]        |
| 177 | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR                                                            | 4/1997  | 3/2012    | 324.73     | 876.49     |
|     |                                                                                                      |         | (-)       | (-)        | (831.68)   |
|     |                                                                                                      |         | [3/2020]  | [1,156.41] | [96]       |
| 178 | JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC                                  | 4/2009  | 3/2020    | 548.00     | 40.00      |
|     |                                                                                                      |         | (-)       | (-)        | (237.87)   |
|     |                                                                                                      |         | [3/2020]  | [785.87]   | [0]        |
| 179 | KATIHAR - JOGBANI (GC)(NEFR)                                                                         | 9/2001  | 12/2010   | 792.46     | 929.63     |
|     |                                                                                                      |         | (-)       | (724.31)   | (527.54)   |
|     |                                                                                                      |         | [0/0]     | [1,320.00] | [0]        |
| 180 | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)                                                                | 4/1997  | /         | 162.87     | 183.72     |
|     |                                                                                                      |         | (-)       | (-)        | (426.28)   |
|     |                                                                                                      |         | [3/2022]  | [589.15]   | [-]        |
| 181 | KISHANGANJ JALALGARH, NL, NEFR                                                                       | 4/2008  | /         | 333.76     | 4.98       |
|     |                                                                                                      |         | (-)       | (-)        | (26.24)    |
|     |                                                                                                      |         | [3/2020]  | [360.00]   | [-]        |
| 182 | KIUL - GAYA DOUBLING PROJECT                                                                         | 12/2015 | 3/2020    | 1,200.20   | 0.00       |
|     |                                                                                                      |         | (-)       | (-)        | (0.00)     |
|     |                                                                                                      |         | [10/2021] | [1,200.20] | [19]       |
| 183 | KOSI BRIDGE (NL), ECR                                                                                | 4/2002  | 3/2020    | 499.41     | 640.78     |
|     |                                                                                                      |         | (-)       | (-)        | (16.61)    |
|     |                                                                                                      |         | [3/2020]  | [516.02]   | [0]        |
| 184 | KURSELA-BIHARIGANJ (NL)                                                                              | 4/2008  | /         | 192.56     | 0.38       |
|     |                                                                                                      |         | (-)       | (-)        | (0.00)     |
|     |                                                                                                      |         | [0/0]     | [192.56]   | [0]        |
| 185 | MAHARAJGANJ-MASRAKH (NL) - NER                                                                       | 4/2003  | 6/2018    | 218.19     | 372.16     |
|     |                                                                                                      |         | (-)       | (-)        | (195.37)   |
|     |                                                                                                      |         | [10/2018] | [413.56]   | [0]        |
| 186 | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR                                                    | 4/1996  | 3/2012    | 477.88     | 495.40     |
|     |                                                                                                      |         | (-)       | (283.95)   | (271.12)   |
|     |                                                                                                      |         | [3/2020]  | [749.00]   | [96]       |
| 187 | MOTIHARI-SITAMARHI (NL)                                                                              | 4/2006  | /         | 211.00     | 4.41       |
|     |                                                                                                      |         | (-)       | (-)        | (715.09)   |
|     |                                                                                                      |         | [0/0]     | [926.09]   | [0]        |
| 188 | MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM                                                              | 4/2016  | 3/2021    | 731.64     | 0.00       |
|     |                                                                                                      |         | (-)       | (-)        | (454.09)   |
|     |                                                                                                      |         | [3/2022]  | [1,185.73] | [12]       |
| 189 | MUZAFFARPUR-DARBANGHA (NL)                                                                           | 4/2008  | /         | 281.30     | 0.58       |
|     |                                                                                                      |         | (-)       | (-)        | (0.00)     |
|     |                                                                                                      |         | [0/0]     | [281.30]   | [0]        |
| 190 | MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL)                                                            | 4/2008  | /         | 228.05     | 1.52       |
|     |                                                                                                      |         | (-)       | (-)        | (0.00)     |
|     |                                                                                                      |         | [0/0]     | [228.05]   | [0]        |

|     |                                                                                                             |         |                             |                                    |                              |
|-----|-------------------------------------------------------------------------------------------------------------|---------|-----------------------------|------------------------------------|------------------------------|
| 191 | MUZAFFARPUR-SITAMARHI NEW LINE                                                                              | 1/1991  | 7/2014<br>(-)<br>[0/0]      | 332.15<br>(-)<br>[559.91]          | 538.21<br>(227.76)<br>[0]    |
| 192 | NAWADA-LAXMIPUR (NL)                                                                                        | 4/2008  | /                           | 620.57<br>(-)<br>[2,626.98]        | 0.00<br>(2,006.41)<br>[0]    |
| 193 | NEW B.G. LINE FROM ARARIA TO GALGALIA<br>(THAKURGUNG), NEFR                                                 | 9/2006  | 3/2019<br>(-)<br>[3/2020]   | 532.87<br>(2,132.03)<br>[2,145.00] | 930.13<br>(1,612.13)<br>[12] |
| 194 | PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN<br>PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM             | 11/2001 | 2/2016<br>(-)<br>[3/2021]   | 624.47<br>(-)<br>[3,550.00]        | 97.63<br>(2,925.53)<br>[61]  |
| 195 | RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR<br>ISLAMPUR                                                  | 4/1998  | /                           | 180.82<br>(-)<br>[528.26]          | 462.75<br>(347.44)<br>[-]    |
| 196 | RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING<br>INCLUDING GANGA BRIDGE                                         | 12/2015 | 3/2020<br>(-)<br>[10/2021]  | 1,491.47<br>(-)<br>[1,491.47]      | 0.00<br>(0.00)<br>[19]       |
| 197 | SAGauli VALMIKINAGAR DOUBLING 109.7 KM                                                                      | 4/2016  | 3/2021<br>(-)<br>[3/2022]   | 744.04<br>(-)<br>[1,215.54]        | 1.81<br>(471.50)<br>[12]     |
| 198 | SAKRI-HASANPUR ROAD (NL)                                                                                    | 4/1999  | /                           | 325.00<br>(-)<br>[729.92]          | 253.10<br>(404.92)<br>[-]    |
| 199 | SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR<br>AND SAHARSA-FORBESGANJ (GC)                                   | 4/2004  | /                           | 372.14<br>(-)<br>[1,474.47]        | 338.44<br>(1,102.33)<br>[-]  |
| 200 | SAMASTIPUR-DARBANGHA                                                                                        | 5/2015  | /                           | 380.00<br>(-)<br>[380.00]          | 0.00<br>(0.00)<br>[0]        |
| 201 | SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)                                                                 | 4/2008  | /                           | 678.62<br>(-)<br>[2,393.23]        | 17.17<br>(1,714.61)<br>[0]   |
|     | <u>Road Transport And Highways</u>                                                                          |         |                             |                                    |                              |
| 202 | 2 LANNING OF MOKAMA-MUNGER                                                                                  | 5/2011  | 5/2013<br>(-)<br>[0/0]      | 351.54<br>(-)<br>[351.54]          | 351.23<br>(0.00)<br>[0]      |
| 203 | 2 LANNING OF MUZAFFARPUR - SONBARSA                                                                         | 5/2011  | 11/2013<br>(-)<br>[12/2018] | 511.54<br>(-)<br>[511.54]          | 564.35<br>(0.00)<br>[61]     |
| 204 | 2-LANNING WITH PS MOTIHARI-RAXAUL                                                                           | 10/2011 | 4/2014<br>(-)<br>[0/0]      | 375.09<br>(-)<br>[375.09]          | 494.33<br>(0.00)<br>[0]      |
| 205 | 4-LANNING OF CHAPRA-HAJIPUR                                                                                 | 1/2011  | 7/2013<br>(-)<br>[6/2019]   | 575.00<br>(-)<br>[575.00]          | 831.49<br>(0.00)<br>[71]     |
| 206 | BALANCE WORK OF 4 LANING OF GORAKPUR -<br>GOPALGANJ                                                         | 5/2015  | 5/2017<br>(-)<br>[6/2019]   | 581.84<br>(-)<br>[581.84]          | 77.43<br>(0.00)<br>[25]      |
| 207 | CONSTRUCTION OF BHAGALPUR BYPASS FROM KM<br>124/175 TO 140/200 OF NH-80 UNDER EPC MODE                      | 8/2015  | 11/2015<br>(-)<br>[0/0]     | 288.24<br>(-)<br>[288.24]          | 0.00<br>(0.00)<br>[0]        |
| 208 | CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00<br>(KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM<br>15  | 12/2017 | /                           | 2,598.00<br>(-)<br>[2,598.00]      | 0.00<br>(0.00)<br>[0]        |
| 209 | CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-<br>ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER<br>GHAT NEAR MUNGE | 3/2017  | 3/2020<br>(-)<br>[3/2020]   | 235.48<br>(-)<br>[227.77]          | 0.00<br>(-7.71)<br>[0]       |
| 210 | DEVELOPMENT OF NEWLY DECLARED NH-527C FROM<br>MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH<br>PAVED SHOULDER  | 3/2018  | /                           | 496.20<br>(-)<br>[496.20]          | 0.00<br>(0.00)<br>[0]        |

|     |                                                                                                       |         |                            |                               |                          |
|-----|-------------------------------------------------------------------------------------------------------|---------|----------------------------|-------------------------------|--------------------------|
| 211 | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P | 11/2013 | 7/2016<br>(-)<br>[0/0]     | 683.83<br>(-)<br>[683.83]     | 0.00<br>(0.00)<br>[0]    |
| 212 | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P | 2/2016  | 5/2016<br>(-)<br>[0/0]     | 178.85<br>(-)<br>[178.85]     | 0.00<br>(0.00)<br>[0]    |
| 213 | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P | 2/2016  | 5/2016<br>(-)<br>[0/0]     | 553.30<br>(-)<br>[553.30]     | 0.00<br>(0.00)<br>[0]    |
| 214 | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P | 2/2016  | 6/2016<br>(-)<br>[0/0]     | 369.77<br>(-)<br>[369.77]     | 0.00<br>(0.00)<br>[0]    |
| 215 | FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31                                                 | 12/2015 | /<br>(-)<br>[12/2019]      | 1,167.45<br>(-)<br>[1,167.45] | 33.45<br>(0.00)<br>[-]   |
| 216 | FOUR LANING OF BHOJPUR TO BUXAR                                                                       | 1/1991  | /<br>(-)<br>[10/2020]      | 642.41<br>(-)<br>[642.41]     | 9.45<br>(0.00)<br>[-]    |
| 217 | FOUR LANING OF FORBESGANJ - JOGBANI                                                                   | 8/2015  | 4/2018<br>(-)<br>[4/2020]  | 322.09<br>(-)<br>[322.09]     | 71.28<br>(0.00)<br>[24]  |
| 218 | FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR    | 1/2014  | 10/2016<br>(-)<br>[0/0]    | 1,408.85<br>(-)<br>[1,408.85] | 0.00<br>(0.00)<br>[0]    |
| 219 | FOUR LANING OF KOILWAR TO BHOJPUR                                                                     | 8/2015  | /<br>(-)<br>[1/2020]       | 814.04<br>(-)<br>[814.04]     | 261.47<br>(0.00)<br>[-]  |
| 220 | FOUR LANING OF PATNA TO KOILWAR                                                                       | 8/2015  | /<br>(-)<br>[0/0]          | 556.07<br>(-)<br>[556.07]     | 0.00<br>(0.00)<br>[0]    |
| 221 | FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31                                                           | 12/2015 | 4/2019<br>(-)<br>[4/2019]  | 1,041.10<br>(-)<br>[1,041.10] | 175.85<br>(0.00)<br>[0]  |
| 222 | PATNA-BAKTZARPUR KM.181.3 TO KM.231.95                                                                | 9/2011  | 3/2014<br>(-)<br>[12/2018] | 574.00<br>(-)<br>[574.00]     | 768.62<br>(0.00)<br>[57] |
| 223 | PATNA-MUZZAFFARPUR                                                                                    | 8/2010  | 2/2013<br>(-)<br>[6/2019]  | 671.30<br>(-)<br>[671.30]     | 884.43<br>(0.00)<br>[76] |
| 224 | REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM  | 8/2016  | 12/2016<br>(-)<br>[0/0]    | 1,742.01<br>(-)<br>[1,742.01] | 0.00<br>(0.00)<br>[0]    |
| 225 | REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I        | 1/2018  | /<br>(-)<br>[0/0]          | 573.70<br>(-)<br>[573.70]     | 0.00<br>(0.00)<br>[0]    |
| 226 | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH  | 10/2014 | 3/2014<br>(-)<br>[0/0]     | 377.64<br>(-)<br>[377.64]     | 0.00<br>(0.00)<br>[0]    |
| 227 | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH  | 10/2013 | 8/2014<br>(-)<br>[0/0]     | 278.39<br>(-)<br>[278.39]     | 0.00<br>(0.00)<br>[0]    |
| 228 | REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF                  | 1/1991  | /<br>(-)<br>[0/0]          | 478.35<br>(-)<br>[478.35]     | 0.00<br>(0.00)<br>[0]    |
| 229 | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104   | 1/1991  | /<br>(-)<br>[0/0]          | 319.68<br>(-)<br>[319.68]     | 0.00<br>(0.00)<br>[0]    |
| 230 | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING   | 2/2014  | 7/2016<br>(-)<br>[0/0]     | 665.50<br>(-)<br>[665.50]     | 0.00<br>(0.00)<br>[0]    |
| 231 | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE                                                        | 1/1991  | 8/2016                     | 282.41                        | 67.52                    |

|     |                                                                                                      |         |                                |                                |                          |
|-----|------------------------------------------------------------------------------------------------------|---------|--------------------------------|--------------------------------|--------------------------|
|     | WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG                                                |         | (-)<br>[0/0]                   | (-)<br>[282.41]                | (0.00)<br>[0]            |
| 232 | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG | 1/2013  | 8/2014<br>(-)<br>[0/0]         | 322.01<br>(-)<br>[322.01]      | 0.00<br>(0.00)<br>[0]    |
| 233 | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG | 1/1991  | 10/2016<br>(-)<br>[0/0]        | 358.22<br>(-)<br>[358.22]      | 188.71<br>(0.00)<br>[0]  |
| 234 | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR | 1/1991  | /<br>(-)<br>[0/0]              | 675.00<br>(-)<br>[675.00]      | 0.00<br>(0.00)<br>[0]    |
| 235 | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40  | 1/1991  | /<br>(-)<br>[0/0]              | 154.62<br>(-)<br>[154.62]      | 0.00<br>(0.00)<br>[0]    |
| 236 | SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION                              | 1/2018  | /<br>(-)<br>[0/0]              | 895.39<br>(-)<br>[895.39]      | 0.00<br>(0.00)<br>[0]    |
| 237 | SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31                      | 8/2017  | 8/2017<br>(-)<br>[0/0]         | 950.64<br>(-)<br>[950.64]      | 0.00<br>(0.00)<br>[0]    |
| 238 | STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV | 3/2015  | 7/2016<br>(-)<br>[0/0]         | 206.80<br>(-)<br>[206.80]      | 0.00<br>(0.00)<br>[0]    |
| 239 | TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA                                                 | 8/2015  | 4/2019<br>(-)<br>[10/2019]     | 399.54<br>(-)<br>[399.54]      | 142.41<br>(0.00)<br>[6]  |
| 240 | TWO LANING WITH PS OF CHHAPRA -GOPALGANJ                                                             | 8/2015  | /<br>(-)<br>[3/2019]           | 854.80<br>(-)<br>[854.80]      | 551.98<br>(0.00)<br>[-]  |
| 241 | TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR                                                | 8/2015  | 4/2018<br>(-)<br>[12/2018]     | 516.13<br>(-)<br>[516.13]      | 400.35<br>(0.00)<br>[8]  |
| 242 | TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN  | 3/2017  | 3/2020<br>(-)<br>[3/2020]      | 672.89<br>(-)<br>[736.01]      | 0.00<br>(63.12)<br>[0]   |
|     | <u>Urban Development</u>                                                                             |         |                                |                                |                          |
| 243 | CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA          | 2/2016  | 6/2017<br>(7/2017)<br>[6/2020] | 496.18<br>(496.00)<br>[498.99] | 34.09<br>(2.81)<br>[36]  |
| 244 | IRRIGATION WORK OF BAGMATI                                                                           | 10/2005 | 3/2015<br>(-)<br>[3/2021]      | 956.00<br>(-)<br>[956.00]      | 651.21<br>(0.00)<br>[72] |
|     | <u>CHHATISGARH</u>                                                                                   |         |                                |                                |                          |
|     | <u>Coal</u>                                                                                          |         |                                |                                |                          |
| 245 | AMERA OC RCE                                                                                         | 2/2015  | 3/2018<br>(-)<br>[3/2018]      | 335.97<br>(-)<br>[335.97]      | 52.41<br>(0.00)<br>[0]   |
| 246 | AMGAON OPENCAST PROJECT RCE                                                                          | 7/2015  | 3/2020<br>(-)<br>[3/2020]      | 316.10<br>(-)<br>[316.10]      | 59.99<br>(0.00)<br>[0]   |
| 247 | AMLAI OC EXPANSION SECTOR B (1.50 MTY)                                                               | 11/2009 | 3/2016<br>(-)<br>[3/2019]      | 198.59<br>(-)<br>[198.59]      | 169.50<br>(0.00)<br>[36] |
| 248 | BAROUD OC EXPANSION (RCE)- 3MTY                                                                      | 4/2012  | 3/2016<br>(-)<br>[3/2019]      | 258.56<br>(-)<br>[258.56]      | 167.63<br>(0.00)<br>[36] |
| 249 | BIJARI OC RCE (1.50 MTY)                                                                             | 5/2014  | 3/2020<br>(-)<br>[3/2020]      | 164.49<br>(-)<br>[164.49]      | 67.20<br>(0.00)<br>[0]   |
| 250 | CHHAL OC SEAM -III (6.00 MTY)                                                                        | 12/2013 | 3/2022<br>(-)                  | 610.63<br>(-)                  | 81.27<br>(0.00)          |

|     |                                                                                                     |         |                                |                                  |                               |
|-----|-----------------------------------------------------------------------------------------------------|---------|--------------------------------|----------------------------------|-------------------------------|
|     |                                                                                                     |         | [3/2022]                       | [610.63]                         | [0]                           |
| 251 | DURGAPUR OPENCAST PROJECT                                                                           | 2/2015  | 3/2023<br>(-)<br>[3/2023]      | 916.24<br>(-)<br>[916.24]        | 3.81<br>(0.00)<br>[0]         |
| 252 | GEVRA EXPANSION OCP (SECL) (35-70) MTY                                                              | 6/2010  | 3/2023<br>(-)<br>[3/2023]      | 11,816.40<br>(-)<br>[11,816.40]  | 2,848.30<br>(0.00)<br>[0]     |
| 253 | JAGANNATHPOR OCP(3.00MTY)                                                                           | 9/2008  | 3/2015<br>(-)<br>[3/2020]      | 152.43<br>(-)<br>[459.49]        | 178.93<br>(307.06)<br>[60]    |
| 254 | JHIRIA WEST OPENCAST PROJECT                                                                        | 11/2018 | 3/2026<br>(-)<br>[3/2026]      | 389.97<br>(-)<br>[389.97]        | 0.00<br>(0.00)<br>[0]         |
| 255 | KARTALI (EAST) OCP (2.50 MTY)                                                                       | 7/2008  | 3/2014<br>(-)<br>[3/2020]      | 178.44<br>(-)<br>[178.44]        | 5.16<br>(0.00)<br>[72]        |
| 256 | KUSMUNDA EXPN.OCP(SECL)(15-50)MTY                                                                   | 8/2013  | 3/2023<br>(-)<br>[3/2023]      | 7,612.33<br>(-)<br>[7,612.33]    | 1,913.96<br>(0.00)<br>[0]     |
| 257 | MADANNAGAR OPENCAST PROJECT                                                                         | 10/2015 | 3/2024<br>(-)<br>[3/2024]      | 1,875.32<br>(-)<br>[1,875.32]    | 0.00<br>(0.00)<br>[0]         |
| 258 | MAHAMAYA OPENCAST PROJECT                                                                           | 5/2018  | 3/2026<br>(-)<br>[3/2026]      | 410.26<br>(-)<br>[410.26]        | 9.53<br>(0.00)<br>[0]         |
| 259 | MANIKPUR OC EXPANSION (3.5 MTY)                                                                     | 12/2009 | 3/2014<br>(-)<br>[3/2020]      | 321.50<br>(-)<br>[321.50]        | 202.68<br>(0.00)<br>[72]      |
| 260 | PELMA OCP(15.00MTY)                                                                                 | 11/2014 | 3/2023<br>(-)<br>[3/2023]      | 1,624.59<br>(-)<br>[1,624.59]    | 6.13<br>(0.00)<br>[0]         |
| 261 | VIJAY WEST OPENCAST PROJECT                                                                         | 5/2017  | 3/2026<br>(-)<br>[3/2026]      | 976.95<br>(-)<br>[976.95]        | 75.96<br>(0.00)<br>[0]        |
|     | <u>Petroleum</u>                                                                                    |         |                                |                                  |                               |
| 262 | CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH | 12/2016 | 4/2021<br>(-)<br>[4/2021]      | 300.00<br>(-)<br>[300.00]        | 0.00<br>(0.00)<br>[0]         |
|     | <u>Power</u>                                                                                        |         |                                |                                  |                               |
| 263 | LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)                                               | 12/2012 | 6/2017<br>(6/2019)<br>[6/2019] | 11,846.00<br>(-)<br>[12,739.82]  | 10,831.46<br>(893.82)<br>[24] |
| 264 | TALAIPELLI COAL MINING PROJECT                                                                      | 9/2015  | 11/2019<br>(-)<br>[11/2019]    | 3,004.00<br>(-)<br>[3,004.00]    | 1,293.72<br>(0.00)<br>[0]     |
|     | <u>Railways</u>                                                                                     |         |                                |                                  |                               |
| 265 | CHAMPA-JHARSUGUDA 3RD LINE                                                                          | 4/2008  | 12/2019<br>(-)<br>[12/2019]    | 872.00<br>(-)<br>[1,279.00]      | 0.00<br>(407.00)<br>[0]       |
| 266 | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL                                    | 4/1995  | 12/2012<br>(-)<br>[3/2022]     | 631.78<br>(632.00)<br>[1,195.00] | 624.13<br>(563.22)<br>[111]   |
| 267 | GEVRA ROAD PENDRA ROAD                                                                              | 2/2014  | 3/2022<br>(-)<br>[3/2022]      | 2,288.00<br>(-)<br>[4,919.00]    | 67.00<br>(2,631.00)<br>[0]    |
| 268 | JHARSUGUDA-BILASPUR 4TH LINE                                                                        | 4/2015  | 3/2021<br>(-)<br>[3/2021]      | 1,973.00<br>(-)<br>[1,973.00]    | 78.00<br>(0.00)<br>[0]        |
| 269 | KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM                                                            | 4/2011  | 3/2022<br>(-)<br>[3/2022]      | 1,471.93<br>(-)<br>[543.00]      | 0.00<br>(-928.93)<br>[0]      |

|     |                                                                                                      |         |                            |                               |                              |
|-----|------------------------------------------------------------------------------------------------------|---------|----------------------------|-------------------------------|------------------------------|
| 270 | KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I                                           | 4/2013  | 9/2018<br>(-)<br>[0/0]     | 3,055.00<br>(-)<br>[3,055.00] | 600.00<br>(0.00)<br>[0]      |
| 271 | KIRANDUL - JAGDALPUR DOUBLING                                                                        | 12/2012 | 3/2020<br>(-)<br>[3/2020]  | 1,160.00<br>(-)<br>[1,160.83] | 571.51<br>(0.83)<br>[0]      |
| 272 | MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR                                                            | 5/2014  | 3/2018<br>(-)<br>[0/0]     | 207.00<br>(-)<br>[207.00]     | 153.83<br>(0.00)<br>[0]      |
| 273 | RAIPUR - TITLAGARH - DOUBLING                                                                        | 3/2007  | 3/2020<br>(-)<br>[3/2020]  | 1,402.02<br>(-)<br>[758.09]   | 1,001.84<br>(-643.93)<br>[0] |
| 274 | SALKA ROAD -ANUPNAGAR LINE DOUBLING                                                                  | 9/2006  | 3/2010<br>(-)<br>[12/2019] | 383.54<br>(-)<br>[555.00]     | 726.22<br>(171.46)<br>[117]  |
|     | <b>Road Transport And Highways</b>                                                                   |         |                            |                               |                              |
| 275 | 4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF  | 3/2018  | /<br>(-)<br>[0/0]          | 1,029.96<br>(-)<br>[1,029.96] | 0.00<br>(0.00)<br>[0]        |
| 276 | CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- | 12/2010 | 12/2012<br>(-)<br>[0/0]    | 169.26<br>(-)<br>[169.26]     | 0.00<br>(0.00)<br>[0]        |
| 277 | FOUR / SIX LANING OF RAIPUR - SIMGA ( PKG-1)                                                         | 12/2015 | 4/2018<br>(-)<br>[6/2019]  | 726.67<br>(-)<br>[726.67]     | 50.67<br>(0.00)<br>[14]      |
| 278 | FOUR LANING OF SARAGAON - BILASPUR                                                                   | 12/2015 | 4/2018<br>(-)<br>[0/0]     | 509.13<br>(-)<br>[509.13]     | 7.21<br>(0.00)<br>[0]        |
| 279 | FOUR LANING OF SIMGA - SARAGAON                                                                      | 12/2015 | 5/2018<br>(-)<br>[6/2019]  | 596.67<br>(-)<br>[596.67]     | 41.87<br>(0.00)<br>[13]      |
| 280 | REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION.          | 10/2014 | 3/2015<br>(-)<br>[0/0]     | 213.47<br>(-)<br>[213.47]     | 0.00<br>(0.00)<br>[0]        |
| 281 | REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION.        | 12/2015 | /<br>(-)<br>[0/0]          | 291.05<br>(-)<br>[291.05]     | 0.00<br>(0.00)<br>[0]        |
| 282 | REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION.         | 12/2014 | /<br>(-)<br>[0/0]          | 394.20<br>(-)<br>[394.20]     | 0.00<br>(0.00)<br>[0]        |
| 283 | REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION  | 11/2015 | 12/2015<br>(-)<br>[0/0]    | 485.44<br>(-)<br>[485.44]     | 0.00<br>(0.00)<br>[0]        |
| 284 | REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 ( BEDMA-DAHAKONDA) UNDER NHDP-IV        | 10/2014 | 3/2015<br>(-)<br>[0/0]     | 298.34<br>(-)<br>[298.34]     | 0.00<br>(0.00)<br>[0]        |
| 285 | REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHAKONDA TO JAGDALPUR) UNDER NHDP-I | 11/2014 | 3/2015<br>(-)<br>[0/0]     | 262.54<br>(-)<br>[262.54]     | 0.00<br>(0.00)<br>[0]        |
| 286 | REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I | 3/2015  | /<br>(-)<br>[0/0]          | 422.34<br>(-)<br>[422.34]     | 22.25<br>(0.00)<br>[0]       |
|     | <b>Steel</b>                                                                                         |         |                            |                               |                              |
| 287 | 2 MTPA PELLET PLANT AT NAGARNAR                                                                      | 11/2015 | 6/2020<br>(-)<br>[6/2020]  | 818.00<br>(-)<br>[818.00]     | 31.60<br>(0.00)<br>[0]       |
| 288 | DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT                                 | 4/2014  | 4/2015<br>(-)<br>[0/0]     | 188.93<br>(-)<br>[188.93]     | 124.84<br>(0.00)<br>[0]      |
| 289 | NMDC INTEGRATED STEEL PLANT                                                                          | 1/2010  | 5/2015<br>(6/2019)         | 15,525.00<br>(-)              | 14,566.77<br>(0.00)          |



|     |                                                                                                      |         |                                   |                                      |                              |
|-----|------------------------------------------------------------------------------------------------------|---------|-----------------------------------|--------------------------------------|------------------------------|
|     |                                                                                                      |         | [6/2019]                          | [15,525.00]                          | [49]                         |
|     | <u>D &amp; N HAVELI</u>                                                                              |         |                                   |                                      |                              |
|     | <u>Petroleum</u>                                                                                     |         |                                   |                                      |                              |
| 290 | DAMAN DEVELOPMENT PROJECT                                                                            | 8/2014  | 5/2019<br>(10/2019)<br>[10/2019]  | 6,086.08<br>(5,842.31)<br>[5,842.31] | 4,513.89<br>(-243.77)<br>[5] |
|     | <u>DELHI</u>                                                                                         |         |                                   |                                      |                              |
|     | <u>Health And Family Welfare</u>                                                                     |         |                                   |                                      |                              |
| 291 | AIIMS - MOTHER AND CHILD BLOCK                                                                       | 12/2013 | 5/2017<br>(6/2018)<br>[7/2019]    | 204.44<br>(-)<br>[204.44]            | 173.67<br>(0.00)<br>[26]     |
| 292 | AIIMS - OPD(NEW)                                                                                     | 8/2014  | 5/2017<br>(6/2018)<br>[3/2019]    | 293.65<br>(-)<br>[293.65]            | 273.80<br>(0.00)<br>[22]     |
| 293 | GERIATRICS BLOCK- AIIMS DLEHI                                                                        | 12/2017 | /<br>(-)<br>[2/2020]              | 156.56<br>(-)<br>[156.65]            | 49.34<br>(0.09)<br>[-]       |
| 294 | LHMC NEW DELHI-RE-DEVELOPMENT                                                                        | 2/2013  | 11/2013<br>(10/2020)<br>[10/2020] | 414.11<br>(-)<br>[513.89]            | 141.00<br>(99.78)<br>[83]    |
|     | <u>Heavy Industry</u>                                                                                |         |                                   |                                      |                              |
| 295 | LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA               | 8/2016  | 9/2019<br>(-)<br>[9/2019]         | 1,554.00<br>(-)<br>[1,554.00]        | 161.86<br>(0.00)<br>[0]      |
|     | <u>Power</u>                                                                                         |         |                                   |                                      |                              |
| 296 | CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)                  | 3/2015  | 5/2017<br>(6/2019)<br>[6/2019]    | 1,394.52<br>(1,394.52)<br>[1,394.52] | 260.99<br>(0.00)<br>[25]     |
|     | <u>Railways</u>                                                                                      |         |                                   |                                      |                              |
| 297 | ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE                                                            | 4/2012  | /<br>(-)<br>[0/0]                 | 295.68<br>(-)<br>[295.68]            | 1.20<br>(0.00)<br>[0]        |
| 298 | GRADE SEPERATOR AT DAYABASTI                                                                         | 4/1999  | /<br>(-)<br>[0/0]                 | 156.65<br>(-)<br>[197.17]            | 56.10<br>(40.52)<br>[0]      |
|     | <u>Road Transport And Highways</u>                                                                   |         |                                   |                                      |                              |
| 299 | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-I)_NEW                                   | 9/2015  | /<br>(-)<br>[0/0]                 | 771.18<br>(-)<br>[7,558.00]          | 261.77<br>(6,786.82)<br>[0]  |
|     | <u>Telecommunications</u>                                                                            |         |                                   |                                      |                              |
| 300 | GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)                                                            | 6/2016  | 6/2017<br>(-)<br>[0/0]            | 418.26<br>(-)<br>[418.26]            | 172.30<br>(0.00)<br>[0]      |
|     | <u>Urban Development</u>                                                                             |         |                                   |                                      |                              |
| 301 | CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI     | 6/2015  | 4/2019<br>(6/2020)<br>[6/2020]    | 197.33<br>(-)<br>[197.33]            | 14.25<br>(0.00)<br>[14]      |
| 302 | CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN   | 7/2012  | 12/2015<br>(-)<br>[0/0]           | 884.30<br>(-)<br>[884.30]            | 647.07<br>(0.00)<br>[0]      |
| 303 | CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI                             | 10/2017 | 11/2019<br>(-)<br>[11/2019]       | 271.90<br>(-)<br>[271.90]            | 4.44<br>(0.00)<br>[0]        |
| 304 | CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU | 12/2017 | 6/2019<br>(-)<br>[6/2019]         | 188.00<br>(-)<br>[188.00]            | 85.71<br>(0.00)<br>[0]       |
| 305 | DELHI MRTS PHASE-III                                                                                 | 9/2011  | 3/2016<br>(5/2019)<br>[5/2019]    | 38,585.00<br>(-)<br>[38,585.00]      | 37,044.70<br>(0.00)<br>[38]  |
| 306 | ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW            | 10/2013 | 10/2019<br>(-)                    | 1,219.21<br>(-)                      | 331.12<br>(372.79)           |

|     |                                                                                                      |         |                                  |                                         |                                 |
|-----|------------------------------------------------------------------------------------------------------|---------|----------------------------------|-----------------------------------------|---------------------------------|
|     | DELHI                                                                                                |         | [3/2020]                         | [1,592.00]                              | [5]                             |
| 307 | RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B | 11/2017 | 5/2020<br>(-)<br>[5/2020]        | 238.56<br>(-)<br>[238.56]               | 3.36<br>(0.00)<br>[0]           |
| 308 | REDEVELOPMENT OF EAST KIDWAI NAGAR                                                                   | 6/2012  | 11/2019<br>(-)<br>[11/2019]      | 4,264.00<br>(-)<br>[4,439.23]           | 3,671.53<br>(175.23)<br>[0]     |
| 309 | REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N | 10/2016 | /<br>(-)<br>[0/0]                | 392.00<br>(-)<br>[392.00]               | 0.00<br>(0.00)<br>[0]           |
| 310 | REDEVELOPMENT OF GPRA AT MOHAMMADPUR                                                                 | 10/2016 | /<br>(-)<br>[0/0]                | 422.00<br>(-)<br>[422.00]               | 0.00<br>(0.00)<br>[0]           |
| 311 | REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR                                                        | 7/2016  | /<br>(-)<br>[0/0]                | 2,694.00<br>(-)<br>[2,694.00]           | 0.00<br>(0.00)<br>[0]           |
| 312 | SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT | 10/2016 | 4/2018<br>(-)<br>[0/0]           | 248.20<br>(-)<br>[248.20]               | 1.21<br>(0.00)<br>[0]           |
|     | <u>GOA</u>                                                                                           |         |                                  |                                         |                                 |
|     | <u>Defence Production</u>                                                                            |         |                                  |                                         |                                 |
| 313 | CONSTRUCTION WORKS PHASE 3B                                                                          | 12/2016 | 8/2020<br>(-)<br>[8/2020]        | 285.95<br>(286.00)<br>[291.29]          | 56.87<br>(5.34)<br>[0]          |
| 314 | CONSTRUCTION WORKS PHASE 4                                                                           | 12/2016 | 5/2018<br>(1/2019)<br>[1/2019]   | 167.69<br>(168.00)<br>[170.37]          | 103.91<br>(2.68)<br>[8]         |
|     | <u>Health And Family Welfare</u>                                                                     |         |                                  |                                         |                                 |
| 315 | SUPER SPECIALITY BLOCK PMSSY GOA                                                                     | 1/2018  | /<br>(-)<br>[5/2020]             | 249.01<br>(-)<br>[249.01]               | 38.72<br>(0.00)<br>[-]          |
|     | <u>Road Transport And Highways</u>                                                                   |         |                                  |                                         |                                 |
| 316 | CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE | 3/2015  | /<br>(-)<br>[0/0]                | 280.16<br>(-)<br>[280.16]               | 16.06<br>(0.00)<br>[0]          |
| 317 | CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD       | 3/2015  | /<br>(-)<br>[0/0]                | 184.05<br>(-)<br>[184.05]               | 10.72<br>(0.00)<br>[0]          |
| 318 | CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM- MANGALORE | 10/2015 | /<br>(-)<br>[0/0]                | 936.40<br>(-)<br>[936.40]               | 0.00<br>(0.00)<br>[0]           |
| 319 | CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66 ) FROM KM. 26 /200 ( CHAINAGE 00/00) TO K | 3/2015  | /<br>(-)<br>[0/0]                | 298.33<br>(-)<br>[298.33]               | 16.10<br>(0.00)<br>[0]          |
| 320 | FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE                      | 3/2015  | 4/2018<br>(-)<br>[0/0]           | 297.00<br>(-)<br>[297.00]               | 38.33<br>(0.00)<br>[0]          |
| 321 | WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER | 12/2015 | /<br>(-)<br>[0/0]                | 773.98<br>(-)<br>[773.98]               | 0.00<br>(0.00)<br>[0]           |
| 322 | WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR | 12/2015 | /<br>(-)<br>[0/0]                | 819.95<br>(-)<br>[819.95]               | 0.00<br>(0.00)<br>[0]           |
|     | <u>GUJARAT</u>                                                                                       |         |                                  |                                         |                                 |
|     | <u>Atomic Energy</u>                                                                                 |         |                                  |                                         |                                 |
| 323 | KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4                                                              | 10/2009 | 12/2015<br>(11/2016)<br>[6/2020] | 11,459.00<br>(16,580.00)<br>[16,580.00] | 12,848.00<br>(5,121.00)<br>[54] |
|     | <u>Petroleum</u>                                                                                     |         |                                  |                                         |                                 |
| 324 | AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT                   | 3/2018  | /<br>(-)                         | 588.20<br>(-)                           | 0.00<br>(0.00)                  |

|     |                                                                                                 |         |                                  |                                      |                              |
|-----|-------------------------------------------------------------------------------------------------|---------|----------------------------------|--------------------------------------|------------------------------|
|     |                                                                                                 |         | [0/0]                            | [588.20]                             | [0]                          |
| 325 | BS-VI PROJECT AT GUJARAT REFINERY                                                               | 3/2018  | 9/2019<br>(-)<br>[9/2019]        | 3,380.00<br>(-)<br>[3,380.00]        | 1,246.09<br>(0.00)<br>[0]    |
| 326 | CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE                                                    | 4/2016  | 4/2018<br>(-)<br>[3/2019]        | 327.78<br>(-)<br>[200.00]            | 116.19<br>(-127.78)<br>[11]  |
| 327 | CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY           | 8/2017  | 8/2020<br>(-)<br>[8/2020]        | 1,342.00<br>(-)<br>[1,342.00]        | 3.90<br>(0.00)<br>[0]        |
| 328 | CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE    | 10/2017 | 2/2020<br>(-)<br>[2/2020]        | 906.00<br>(-)<br>[906.00]            | 13.52<br>(0.00)<br>[0]       |
| 329 | GAMJI REDEVELOPMENT PROJECT                                                                     | 5/2015  | 11/2019<br>(-)<br>[11/2019]      | 1,671.22<br>(567.22)<br>[567.22]     | 449.95<br>(-1,104.00)<br>[0] |
| 330 | INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY         | 9/2016  | 7/2020<br>(-)<br>[7/2020]        | 208.35<br>(-)<br>[208.35]            | 67.71<br>(0.00)<br>[0]       |
| 331 | REDEVELOPMENT OF SANTHAL FIELD                                                                  | 2/2017  | 3/2026<br>(3/2026)<br>[3/2026]   | 1,162.56<br>(1,162.56)<br>[1,162.56] | 294.16<br>(0.00)<br>[0]      |
| 332 | REPLACEMENT OF KV SECTION OF KSPL                                                               | 10/2014 | 8/2018<br>(-)<br>[0/0]           | 279.00<br>(-)<br>[279.00]            | 200.05<br>(0.00)<br>[0]      |
|     | <u>Power</u>                                                                                    |         |                                  |                                      |                              |
| 333 | SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT                       | 12/2017 | 6/2019<br>(6/2019)<br>[6/2019]   | 193.14<br>(193.14)<br>[193.14]       | 4.00<br>(0.00)<br>[0]        |
| 334 | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT         | 5/2017  | 9/2018<br>(9/2018)<br>[6/2019]   | 175.64<br>(175.64)<br>[175.64]       | 73.94<br>(0.00)<br>[9]       |
| 335 | TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B)                          | 7/2016  | 12/2018<br>(12/2018)<br>[2/2019] | 300.94<br>(300.94)<br>[300.94]       | 219.36<br>(0.00)<br>[2]      |
| 336 | WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT)                                   | 11/2016 | 11/2017<br>(-)<br>[3/2019]       | 330.00<br>(-)<br>[330.00]            | 310.99<br>(0.00)<br>[16]     |
|     | <u>Railways</u>                                                                                 |         |                                  |                                      |                              |
| 337 | AHMEDABAD-BOTAD (GC)                                                                            | 4/2012  | 12/2021<br>(-)<br>[12/2021]      | 975.62<br>(-)<br>[975.62]            | 518.92<br>(0.00)<br>[0]      |
| 338 | AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)                                                              | 4/2008  | 3/2020<br>(3/2020)<br>[3/2020]   | 829.74<br>(416.86)<br>[385.60]       | 500.42<br>(-444.14)<br>[0]   |
| 339 | BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)                              | 4/2006  | 3/2011<br>(-)<br>[0/0]           | 117.36<br>(196.95)<br>[203.00]       | 202.29<br>(85.64)<br>[0]     |
| 340 | BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION | 2/1991  | 3/2019<br>(-)<br>[3/2019]        | 551.51<br>(-)<br>[551.51]            | 257.05<br>(0.00)<br>[0]      |
| 341 | BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)                                        | 4/2008  | 3/2012<br>(-)<br>[3/2019]        | 318.24<br>(-)<br>[321.62]            | 83.53<br>(3.38)<br>[84]      |
| 342 | DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM                     | 4/2017  | 3/2020<br>(-)<br>[3/2020]        | 691.84<br>(-)<br>[691.84]            | 15.31<br>(0.00)<br>[0]       |
| 343 | DHASA-JETALSAR (GC)                                                                             | 4/2012  | 3/2021<br>(-)<br>[3/2021]        | 644.38<br>(-)<br>[644.38]            | 127.98<br>(0.00)<br>[0]      |
| 344 | GANDHINAGAR REDEVELOPMENT OF STATION                                                            | 3/2017  | /                                | 243.60                               | 0.00                         |

|     |                                                                                                      |         |                             |                               |                         |
|-----|------------------------------------------------------------------------------------------------------|---------|-----------------------------|-------------------------------|-------------------------|
|     | ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO                                      |         | (-)<br>[0/0]                | (-)<br>[243.60]               | (0.00)<br>[0]           |
| 345 | MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)                                                                   | 4/2011  | / (3/2022)<br>[3/2023]      | 844.10 (-)<br>[844.10]        | 61.85 (0.00)<br>[-]     |
| 346 | MULTI MODAL LOGISTICS PARK AT VARNAMA                                                                | 10/2013 | 3/2019 (-)<br>[12/2019]     | 343.00 (-)<br>[343.00]        | 289.38 (0.00)<br>[9]    |
| 347 | PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220                | 3/2012  | / (-)<br>[0/0]              | 153.83 (-)<br>[153.83]        | 0.00 (0.00)<br>[0]      |
| 348 | PALANPUR-SAMAKHAYALI (DL)                                                                            | 4/2013  | 12/2021 (-)<br>[12/2021]    | 1,548.66 (-)<br>[1,548.66]    | 777.72 (0.00)<br>[0]    |
| 349 | RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)        | 4/1994  | 3/2019 (3/2019)<br>[3/2022] | 320.66 (1,378.12)<br>[858.96] | 549.56 (538.30)<br>[36] |
| 350 | SURENDRA NAGAR RAJKOT                                                                                | 4/2015  | 3/2021 (3/2019)<br>[3/2020] | 1,002.39 (-)<br>[1,002.39]    | 232.37 (0.00)<br>[-12]  |
| 351 | VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON | 3/2012  | / (-)<br>[0/0]              | 248.26 (-)<br>[248.26]        | 0.00 (0.00)<br>[0]      |
|     | <u>Road Transport And Highways</u>                                                                   |         |                             |                               |                         |
| 352 | 2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION                                                | 12/2016 | / (-)<br>[9/2019]           | 417.19 (-)<br>[417.19]        | 122.81 (0.00)<br>[-]    |
| 353 | 4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000                       | 7/2016  | / (-)<br>[1/2020]           | 829.97 (-)<br>[829.97]        | 71.29 (0.00)<br>[-]     |
| 354 | 4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT                                        | 6/2017  | 6/2020 (-)<br>[8/2020]      | 1,958.88 (-)<br>[1,958.88]    | 364.31 (0.00)<br>[2]    |
| 355 | AHMEDABAD TO VADODARA SECTION                                                                        | 1/2013  | 12/2015 (-)<br>[0/0]        | 2,125.24 (-)<br>[2,125.24]    | 4,659.71 (0.00)<br>[0]  |
| 356 | CONSTRUCTION OF 4-LANE LADDOWAL BYPASS                                                               | 5/2016  | / (-)<br>[12/2019]          | 364.56 (-)<br>[364.56]        | 24.94 (0.00)<br>[-]     |
| 357 | CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR  | 3/2018  | / (-)<br>[0/0]              | 1,161.39 (-)<br>[1,161.39]    | 0.00 (0.00)<br>[0]      |
| 358 | CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S | 3/2018  | / (-)<br>[0/0]              | 1,437.64 (-)<br>[1,437.64]    | 0.00 (0.00)<br>[0]      |
| 359 | CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S | 3/2018  | / (-)<br>[0/0]              | 2,702.05 (-)<br>[2,702.05]    | 0.00 (0.00)<br>[0]      |
| 360 | FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. | 5/2016  | / (-)<br>[8/2019]           | 998.18 (-)<br>[998.18]        | 199.22 (0.00)<br>[-]    |
| 361 | FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST | 5/2016  | / (-)<br>[9/2019]           | 723.64 (-)<br>[723.64]        | 211.88 (0.00)<br>[-]    |
| 362 | FOUR LANING OF TALAJA – MAHUYA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR | 5/2016  | / (-)<br>[10/2019]          | 834.64 (-)<br>[834.64]        | 137.94 (0.00)<br>[-]    |
| 363 | FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU | 5/2016  | / (-)<br>[8/2019]           | 763.08 (-)<br>[763.08]        | 137.01 (0.00)<br>[-]    |
| 364 | GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT                                                          | 3/2010  | 9/2012                      | 1,509.10                      | 3,187.21                |

|     |                                                                                                      |         |                             |                               |                           |
|-----|------------------------------------------------------------------------------------------------------|---------|-----------------------------|-------------------------------|---------------------------|
|     | SECTION                                                                                              |         | (-)<br>[8/2018]             | (-)<br>[3,237.87]             | (1,728.77)<br>[0]         |
| 365 | JUNAGADH BYPASS                                                                                      | 10/2017 | 10/2017<br>(-)<br>[0/0]     | 232.49<br>(-)<br>[232.49]     | 0.00<br>(0.00)<br>[0]     |
| 366 | KANDLA - MUNDRA PORT                                                                                 | 1/2011  | 7/2013<br>(-)<br>[12/2018]  | 953.88<br>(-)<br>[953.88]     | 976.28<br>(0.00)<br>[65]  |
| 367 | SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF  | 2/2018  | /<br>(-)<br>[0/0]           | 1,052.21<br>(-)<br>[1,052.21] | 0.00<br>(0.00)<br>[0]     |
| 368 | SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.      | 1/2017  | /<br>(-)<br>[0/0]           | 1,251.11<br>(-)<br>[1,251.11] | 0.00<br>(0.00)<br>[0]     |
| 369 | SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME | 5/2016  | /<br>(-)<br>[3/2019]        | 425.60<br>(-)<br>[425.60]     | 0.00<br>(0.00)<br>[-]     |
| 370 | VADODARA-SURAT SECTION                                                                               | 3/2014  | 8/2016<br>(-)<br>[0/0]      | 503.16<br>(-)<br>[503.16]     | 346.60<br>(0.00)<br>[0]   |
|     | <u>Urban Development</u>                                                                             |         |                             |                               |                           |
| 371 | CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT                                | 1/2013  | /<br>(-)<br>[0/0]           | 175.00<br>(-)<br>[175.00]     | 1.83<br>(0.00)<br>[0]     |
|     | <u>HARYANA</u>                                                                                       |         |                             |                               |                           |
|     | <u>Fertilisers</u>                                                                                   |         |                             |                               |                           |
| 372 | GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT                            | 1/2018  | 11/2019<br>(-)<br>[11/2019] | 215.92<br>(-)<br>[215.92]     | 27.51<br>(0.00)<br>[0]    |
|     | <u>Health And Family Welfare</u>                                                                     |         |                             |                               |                           |
| 373 | CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR                                                   | 9/2014  | 3/2018<br>(-)<br>[0/0]      | 505.58<br>(-)<br>[523.00]     | 491.16<br>(17.42)<br>[0]  |
|     | <u>Petroleum</u>                                                                                     |         |                             |                               |                           |
| 374 | BS-VI PROJECT AT PANIPAT REFINERY                                                                    | 12/2017 | 7/2019<br>(-)<br>[7/2019]   | 3,529.00<br>(-)<br>[3,529.00] | 952.69<br>(0.00)<br>[0]   |
| 375 | CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY                                | 4/2018  | 2/2020<br>(-)<br>[2/2020]   | 206.63<br>(-)<br>[206.63]     | 0.52<br>(0.00)<br>[0]     |
| 376 | CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA                         | 11/2017 | 11/2020<br>(-)<br>[11/2020] | 255.00<br>(-)<br>[255.00]     | 15.68<br>(0.00)<br>[0]    |
| 377 | NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT                                                         | 8/2018  | 8/2020<br>(-)<br>[8/2020]   | 1,636.00<br>(-)<br>[1,636.00] | 128.78<br>(0.00)<br>[0]   |
|     | <u>Railways</u>                                                                                      |         |                             |                               |                           |
| 378 | HISSAR-SIRSA VIA AGROHA AND FATEHABAD                                                                | 4/2013  | /<br>(-)<br>[0/0]           | 400.00<br>(-)<br>[400.00]     | 0.00<br>(0.00)<br>[0]     |
| 379 | JIND-SONEPAT (NL),NR                                                                                 | 1/2004  | 3/2012<br>(-)<br>[0/0]      | 238.56<br>(-)<br>[740.00]     | 722.65<br>(501.44)<br>[0] |
| 380 | MULTI MODAL LOGISTICS PARK AT BARHI                                                                  | 12/2015 | 3/2019<br>(-)<br>[3/2019]   | 346.32<br>(-)<br>[300.00]     | 272.72<br>(-46.32)<br>[0] |
| 381 | ROHTAK-MEHAM HANSI                                                                                   | 4/2012  | 12/2011<br>(-)<br>[0/0]     | 287.00<br>(-)<br>[625.00]     | 4.38<br>(338.00)<br>[0]   |
|     | <u>Road Transport And Highways</u>                                                                   |         |                             |                               |                           |
| 382 | 4 LANING OF AMBALA - KAITHAL - PACKAGE -1                                                            | 12/2015 | 6/2016                      | 602.95                        | 54.89                     |

|     |                                                                                                       |         |                            |                               |                                |
|-----|-------------------------------------------------------------------------------------------------------|---------|----------------------------|-------------------------------|--------------------------------|
|     |                                                                                                       |         | (-)<br>[12/2018]           | (-)<br>[602.95]               | (0.00)<br>[30]                 |
| 383 | 4 LANING OF AMBALA - KAITHAL - PACKAGE -2                                                             | 1/2016  | 7/2018<br>(-)<br>[3/2019]  | 574.28<br>(-)<br>[574.28]     | 79.56<br>(0.00)<br>[8]         |
| 384 | 4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL   | 3/2017  | 3/2020<br>(-)<br>[6/2019]  | 639.79<br>(-)<br>[552.90]     | 46.24<br>(-86.89)<br>[-9]      |
| 385 | 8 LANING OF MUKARBA CHOWK TO PANIPAT                                                                  | 7/2015  | 4/2019<br>(-)<br>[4/2019]  | 2,128.72<br>(-)<br>[2,128.72] | 1,042.73<br>(0.00)<br>[0]      |
| 386 | CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73                                                       | 8/2016  | 5/2019<br>(-)<br>[8/2019]  | 248.97<br>(-)<br>[248.97]     | 27.57<br>(0.00)<br>[3]         |
| 387 | CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P  | 3/2018  | /<br>(-)<br>[0/0]          | 1,484.30<br>(-)<br>[1,484.30] | 0.00<br>(0.00)<br>[0]          |
| 388 | CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211  | 9/2016  | 5/2019<br>(-)<br>[5/2019]  | 1,004.67<br>(-)<br>[1,004.67] | 0.00<br>(0.00)<br>[0]          |
| 389 | DELHI/ HARYANA BORDER TO ROHTAK                                                                       | 4/2007  | 5/2010<br>(-)<br>[10/2018] | 486.00<br>(-)<br>[486.00]     | 470.01<br>(0.00)<br>[0]        |
| 390 | FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2                                           | 11/2015 | 5/2018<br>(-)<br>[0/0]     | 867.66<br>(-)<br>[867.66]     | 502.66<br>(0.00)<br>[0]        |
| 391 | FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I                                           | 8/2015  | 2/2018<br>(-)<br>[0/0]     | 723.54<br>(-)<br>[723.54]     | 530.94<br>(0.00)<br>[0]        |
| 392 | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)                                                           | 5/2009  | 11/2011<br>(-)<br>[6/2019] | 1,108.00<br>(-)<br>[2,288.00] | 3,953.66<br>(1,180.00)<br>[91] |
| 393 | REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION & STRENGTHENING OF ROHNA/HASS  | 3/2018  | /<br>(-)<br>[0/0]          | 551.58<br>(-)<br>[551.58]     | 0.00<br>(0.00)<br>[0]          |
| 394 | REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE  | 3/2018  | /<br>(-)<br>[0/0]          | 275.12<br>(-)<br>[275.12]     | 0.00<br>(0.00)<br>[0]          |
| 395 | REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI | 3/2018  | /<br>(-)<br>[0/0]          | 307.79<br>(-)<br>[307.79]     | 0.00<br>(0.00)<br>[0]          |
| 396 | REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN  | 3/2018  | /<br>(-)<br>[0/0]          | 181.78<br>(-)<br>[181.78]     | 0.00<br>(0.00)<br>[0]          |
| 397 | REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN  | 3/2018  | /<br>(-)<br>[0/0]          | 198.05<br>(-)<br>[198.05]     | 0.00<br>(0.00)<br>[0]          |
| 398 | ROHTAK-BAWAL                                                                                          | 5/2011  | 11/2013<br>(-)<br>[0/0]    | 650.00<br>(-)<br>[650.00]     | 832.39<br>(0.00)<br>[0]        |
| 399 | SIX LANING & STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) I | 3/2018  | /<br>(-)<br>[0/0]          | 795.50<br>(-)<br>[795.50]     | 0.00<br>(0.00)<br>[0]          |
| 400 | SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA  | 3/2018  | /<br>(-)<br>[0/0]          | 634.70<br>(-)<br>[634.70]     | 0.00<br>(0.00)<br>[0]          |
|     | <u>HIMACHAL PRADESH</u>                                                                               |         |                            |                               |                                |
|     | <u>Petroleum</u>                                                                                      |         |                            |                               |                                |
| 401 | BRANCH PIPELINE OF PAJPL TO UNA                                                                       | 2/2016  | 9/2019<br>(-)<br>[2/2019]  | 151.00<br>(-)<br>[151.00]     | 112.58<br>(0.00)<br>[-7]       |

|     |                                                                                                      |         |                                 |                                      |                                   |
|-----|------------------------------------------------------------------------------------------------------|---------|---------------------------------|--------------------------------------|-----------------------------------|
| 402 | CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP                                              | 2/2016  | 5/2019<br>(-)<br>[1/2019]       | 356.00<br>(-)<br>[356.00]            | 205.41<br>(0.00)<br>[-4]          |
|     | <u>Power</u>                                                                                         |         |                                 |                                      |                                   |
| 403 | PARBATI HEP (4X200 MW) (NHPC) II                                                                     | 9/2002  | 9/2009<br>(-)<br>[12/2021]      | 3,919.59<br>(-)<br>[9,394.80]        | 7,145.69<br>(5,475.21)<br>[147]   |
|     | <u>Railways</u>                                                                                      |         |                                 |                                      |                                   |
| 404 | BHANUPALI-BILASPUR BERI NL                                                                           | 4/2008  | 12/2026<br>(-)<br>[12/2026]     | 2,966.99<br>(-)<br>[7,000.00]        | 221.19<br>(4,033.01)<br>[0]       |
|     | <u>Road Transport And Highways</u>                                                                   |         |                                 |                                      |                                   |
| 405 | 2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)                                | 2/2016  | 2/2019<br>(-)<br>[2/2019]       | 273.20<br>(-)<br>[273.20]            | 48.69<br>(0.00)<br>[0]            |
| 406 | 4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P                                                      | 6/2017  | 6/2020<br>(-)<br>[6/2020]       | 2,485.93<br>(-)<br>[2,485.93]        | 0.00<br>(0.00)<br>[0]             |
| 407 | FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM)                                   | 11/2013 | 11/2016<br>(-)<br>[4/2019]      | 1,916.79<br>(-)<br>[1,916.79]        | 1,948.92<br>(0.00)<br>[29]        |
| 408 | FOUR LANING OF PARWANOO -SOLAN                                                                       | 9/2015  | 3/2018<br>(-)<br>[3/2019]       | 934.46<br>(-)<br>[934.46]            | 104.98<br>(0.00)<br>[12]          |
| 409 | FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M | 3/2018  | /<br>(-)<br>[0/0]               | 478.74<br>(-)<br>[478.74]            | 0.00<br>(0.00)<br>[0]             |
| 410 | FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH | 9/2016  | /<br>(-)<br>[7/2020]            | 1,273.71<br>(-)<br>[1,273.71]        | 0.00<br>(0.00)<br>[-]             |
| 411 | FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)                             | 10/2016 | /<br>(-)<br>[11/2019]           | 447.75<br>(-)<br>[447.75]            | 54.46<br>(0.00)<br>[-]            |
| 412 | TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS                                    | 8/2016  | /<br>(-)<br>[9/2020]            | 1,583.18<br>(-)<br>[1,583.18]        | 0.00<br>(0.00)<br>[-]             |
|     | <u>Urban Development</u>                                                                             |         |                                 |                                      |                                   |
| 413 | DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND                                      | 11/2012 | 11/2014<br>(-)<br>[2/2019]      | 270.83<br>(-)<br>[270.83]            | 163.97<br>(0.00)<br>[51]          |
|     | <u>JAMMU AND KASHMIR</u>                                                                             |         |                                 |                                      |                                   |
|     | <u>Power</u>                                                                                         |         |                                 |                                      |                                   |
| 414 | PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)                                                           | 10/2014 | 4/2020<br>(-)<br>[10/2023]      | 8,112.12<br>(-)<br>[8,112.12]        | 982.71<br>(0.00)<br>[42]          |
| 415 | TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT           | 1/2014  | 9/2017<br>(9/2017)<br>[11/2018] | 1,788.41<br>(1,788.41)<br>[2,333.71] | 1,697.38<br>(545.30)<br>[0]       |
|     | <u>Railways</u>                                                                                      |         |                                 |                                      |                                   |
| 416 | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR                                                                  | 3/1995  | 11/2002<br>(-)<br>[3/2021]      | 2,500.00<br>(-)<br>[27,949.00]       | 16,834.42<br>(25,449.00)<br>[220] |
|     | <u>Road Transport And Highways</u>                                                                   |         |                                 |                                      |                                   |
| 417 | CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE  | 12/2017 | /<br>(-)<br>[0/0]               | 1,471.75<br>(-)<br>[1,471.75]        | 0.00<br>(0.00)<br>[0]             |
| 418 | FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A                                                     | 12/2015 | 6/2019<br>(-)<br>[12/2020]      | 2,168.66<br>(-)<br>[2,168.66]        | 0.00<br>(0.00)<br>[18]            |
| 419 | FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A                                                    | 12/2015 | 12/2018<br>(-)                  | 2,136.97<br>(-)                      | 87.69<br>(0.00)                   |

|     |                                                  |         |                            |                               |                            |
|-----|--------------------------------------------------|---------|----------------------------|-------------------------------|----------------------------|
|     |                                                  |         | [10/2019]                  | [2,136.97]                    | [10]                       |
| 420 | JAMMU-UDHAMPUR KM.27.5 TO KM.67.00               | 7/2010  | 7/2013<br>(-)<br>[0/0]     | 1,813.76<br>(-)<br>[1,813.76] | 2,393.99<br>(0.00)<br>[0]  |
| 421 | NASHRI- CHANANI                                  | 5/2011  | 6/2015<br>(-)<br>[0/0]     | 2,159.00<br>(-)<br>[2,159.00] | 3,986.82<br>(0.00)<br>[0]  |
| 422 | QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00         | 7/2010  | 7/2015<br>(-)<br>[3/2019]  | 1,987.00<br>(-)<br>[1,987.00] | 2,403.47<br>(0.00)<br>[44] |
| 423 | SRINAGAR TO BANIHAI                              | 6/2011  | 6/2014<br>(-)<br>[0/0]     | 1,100.70<br>(-)<br>[1,100.70] | 1,288.68<br>(0.00)<br>[0]  |
|     | <u>JHARKHAND</u>                                 |         |                            |                               |                            |
|     | <u>Coal</u>                                      |         |                            |                               |                            |
| 424 | AMRAPALI OC(12MTY)                               | 2/2012  | 3/2020<br>(-)<br>[3/2020]  | 858.11<br>(-)<br>[858.11]     | 184.43<br>(0.00)<br>[0]    |
| 425 | CHURI BENTI UG (0.81 MTY)                        | 8/2007  | 3/2011<br>(-)<br>[3/2020]  | 163.51<br>(-)<br>[163.51]     | 103.41<br>(0.00)<br>[108]  |
| 426 | HURA - C OC (3 MTY)                              | 10/2015 | 3/2022<br>(-)<br>[3/2022]  | 359.69<br>(-)<br>[359.69]     | 42.44<br>(0.00)<br>[0]     |
| 427 | KAPURIA UG(PSLW)                                 | 8/2011  | 4/2017<br>(-)<br>[0/0]     | 988.35<br>(-)<br>[988.35]     | 45.26<br>(0.00)<br>[0]     |
| 428 | KARMA OCP (1.0MTY)                               | 6/2009  | 3/2014<br>(-)<br>[3/2019]  | 162.46<br>(-)<br>[162.46]     | 89.21<br>(0.00)<br>[60]    |
| 429 | MADHUBAND NLW WASHERY                            | 8/2010  | 5/2014<br>(-)<br>[4/2018]  | 289.45<br>(-)<br>[289.45]     | 194.20<br>(0.00)<br>[0]    |
| 430 | MAGADH OC 20 MTY (CCL)                           | 8/2008  | 7/2012<br>(-)<br>[3/2021]  | 706.40<br>(-)<br>[706.40]     | 185.62<br>(0.00)<br>[104]  |
| 431 | MOONIDIH XV SEAM UG                              | 8/2011  | 4/2015<br>(-)<br>[4/2019]  | 1,230.27<br>(-)<br>[1,230.27] | 326.22<br>(0.00)<br>[48]   |
| 432 | MURAI DIH UG TURN-KEY PROJECT                    | 2/2011  | 4/2014<br>(-)<br>[10/2018] | 339.88<br>(-)<br>[339.88]     | 12.08<br>(0.00)<br>[0]     |
| 433 | NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) | 2/2014  | 3/2021<br>(-)<br>[3/2021]  | 555.52<br>(-)<br>[555.52]     | 5.01<br>(0.00)<br>[0]      |
| 434 | NORTH URIMARI OCP (3.0 MTY)                      | 12/2007 | 3/2012<br>(-)<br>[3/2019]  | 179.87<br>(-)<br>[179.87]     | 174.69<br>(0.00)<br>[84]   |
| 435 | PATHERDIH NLW WASHERY                            | 10/2012 | 4/2014<br>(-)<br>[4/2018]  | 269.82<br>(-)<br>[269.82]     | 179.30<br>(0.00)<br>[0]    |
| 436 | RAJRAPPA RCE OCP ( 3.0 MTY)                      | 12/2009 | 3/2016<br>(-)<br>[3/2019]  | 510.85<br>(-)<br>[510.85]     | 340.29<br>(0.00)<br>[36]   |
| 437 | TAPIN OCP (2.5 MTY)                              | 8/2008  | 3/2012<br>(-)<br>[3/2019]  | 264.68<br>(-)<br>[264.68]     | 178.37<br>(0.00)<br>[84]   |
|     | <u>Petroleum</u>                                 |         |                            |                               |                            |
| 438 | 120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE  | 6/2017  | 6/2020<br>(-)<br>[6/2020]  | 161.50<br>(-)<br>[161.50]     | 17.78<br>(0.00)<br>[0]     |



|     |                                                                                                      |         |                                  |                                      |                              |
|-----|------------------------------------------------------------------------------------------------------|---------|----------------------------------|--------------------------------------|------------------------------|
| 439 | CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR                                                      | 10/2017 | 10/2022<br>(-)<br>[10/2022]      | 221.45<br>(-)<br>[221.45]            | 23.92<br>(0.00)<br>[0]       |
| 440 | CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI                                                          | 10/2017 | 10/2022<br>(-)<br>[10/2022]      | 226.45<br>(-)<br>[226.45]            | 25.11<br>(0.00)<br>[0]       |
| 441 | DEVELOPMENT PLAN OF CBM - BOKARO BLOCK                                                               | 12/2015 | 3/2023<br>(3/2022)<br>[3/2022]   | 658.62<br>(910.23)<br>[910.23]       | 109.60<br>(251.61)<br>[-12]  |
| 442 | RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)                                      | 4/2011  | 5/2015<br>(-)<br>[0/0]           | 191.96<br>(-)<br>[191.96]            | 176.28<br>(0.00)<br>[0]      |
|     | <u>Power</u>                                                                                         |         |                                  |                                      |                              |
| 443 | NORTH KARANPURA STPP (3X660 MW)                                                                      | 2/2014  | 2/2019<br>(10/2020)<br>[10/2020] | 14,366.58<br>(-)<br>[15,164.05]      | 7,916.41<br>(797.47)<br>[20] |
| 444 | PAKRI BARWADIH COAL MINING PROJECT                                                                   | 10/2004 | 10/2017<br>(-)<br>[12/2016]      | 4,237.96<br>(4,238.00)<br>[4,552.00] | 2,922.12<br>(314.04)<br>[0]  |
|     | <u>Railways</u>                                                                                      |         |                                  |                                      |                              |
| 445 | BONDAMUNDA RANCHI DOUBLING                                                                           | 3/2016  | 3/2021<br>(3/2021)<br>[12/2021]  | 1,724.20<br>(1,724.20)<br>[1,724.20] | 175.49<br>(0.00)<br>[9]      |
| 446 | DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING                                                              | 4/2010  | 12/2015<br>(12/2018)<br>[2/2019] | 309.44<br>(-)<br>[525.81]            | 507.60<br>(216.37)<br>[38]   |
| 447 | GARHWA ROAD-RAMNA                                                                                    | 3/2015  | 3/2021<br>(-)<br>[12/2020]       | 348.23<br>(-)<br>[348.23]            | 104.98<br>(0.00)<br>[-3]     |
| 448 | KODERMA-RANCHI VIA BARKAKANA (NL),ECR                                                                | 3/1999  | /<br>(-)<br>[3/2021]             | 1,033.07<br>(-)<br>[3,020.94]        | 0.00<br>(1,987.87)<br>[-]    |
| 449 | KODERMA-TILAIYA (NL), ECR                                                                            | 4/2002  | /<br>(-)<br>[0/0]                | 459.91<br>(-)<br>[459.91]            | 221.54<br>(0.00)<br>[0]      |
| 450 | MANDARHILL-DUMKA-RAMPURHAT (NL),ER                                                                   | 4/1995  | 3/2016<br>(-)<br>[3/2020]        | 1,125.89<br>(-)<br>[1,126.36]        | 2,012.33<br>(0.47)<br>[48]   |
| 451 | MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING                                                              | 4/2012  | /<br>(12/2018)<br>[1/2020]       | 258.20<br>(-)<br>[365.00]            | 192.35<br>(106.80)<br>[-]    |
| 452 | RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND                                                | 4/2012  | 12/2016<br>(8/2018)<br>[9/2019]  | 148.77<br>(-)<br>[377.00]            | 155.96<br>(228.23)<br>[33]   |
|     | <u>Road Transport And Highways</u>                                                                   |         |                                  |                                      |                              |
| 453 | 4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00)                           | 3/2017  | 3/2020<br>(-)<br>[6/2019]        | 239.68<br>(-)<br>[235.90]            | 46.25<br>(-3.78)<br>[-9]     |
| 454 | 4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00)                                     | 3/2017  | 3/2020<br>(-)<br>[6/2019]        | 165.50<br>(-)<br>[172.16]            | 20.01<br>(6.66)<br>[-9]      |
| 455 | 4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K | 3/2018  | /<br>(-)<br>[0/0]                | 1,005.08<br>(-)<br>[1,005.08]        | 0.00<br>(0.00)<br>[0]        |
| 456 | 4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION                                                 | 2/2016  | 3/2019<br>(-)<br>[3/2019]        | 997.15<br>(-)<br>[997.15]            | 352.03<br>(0.00)<br>[0]      |
| 457 | FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31                                                    | 1/2018  | /<br>(-)<br>[0/0]                | 273.46<br>(-)<br>[273.46]            | 0.00<br>(0.00)<br>[0]        |
| 458 | FOUR LANING OF BARHI-HAZARIBAGH NH-33                                                                | 8/2016  | 8/2018                           | 323.72                               | 37.20                        |

|     |                                                                                                           |         |                             |                                      |                             |
|-----|-----------------------------------------------------------------------------------------------------------|---------|-----------------------------|--------------------------------------|-----------------------------|
|     |                                                                                                           |         | (-)<br>[8/2018]             | (-)<br>[323.72]                      | (0.00)<br>[0]               |
| 459 | RANCHI-RARGA-JAMSETHPUR                                                                                   | 12/2012 | 6/2015<br>(-)<br>[0/0]      | 1,479.00<br>(-)<br>[1,479.00]        | 740.26<br>(0.00)<br>[0]     |
| 460 | SIX LANING OF BIHAR - JHARKHAND BORDER<br>(CHORDAHA) TO GORHAR SECTION                                    | 1/2018  | /<br>(-)<br>[0/0]           | 1,155.16<br>(-)<br>[1,155.16]        | 0.00<br>(0.00)<br>[0]       |
| 461 | TWO/FOUR LANNING WITH PAVED SHOULDERS OF<br>GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER<br>SECTION OF NH- | 7/2016  | /<br>(-)<br>[12/2019]       | 458.03<br>(-)<br>[458.03]            | 20.00<br>(0.00)<br>[-]      |
|     | <u>Steel</u>                                                                                              |         |                             |                                      |                             |
| 462 | EXPANSION OF GUA ORE MINES WITH BENEFICIATION<br>FACILITIES AND INSTALLATION OF PELLET PLANT              | 2/2014  | 9/2017<br>(-)<br>[0/0]      | 4,749.00<br>(-)<br>[4,749.00]        | 108.28<br>(0.00)<br>[0]     |
| 463 | MODERNISATION OF STEEL MELTING SHOP NO.1 AT<br>BOKARO STEEL PLANT                                         | 5/2015  | 12/2017<br>(-)<br>[6/2019]  | 1,154.18<br>(-)<br>[1,154.18]        | 862.45<br>(0.00)<br>[18]    |
| 464 | NEW SINTER PLANT AT BOKARO STEEL PLANT                                                                    | 3/2015  | 10/2017<br>(-)<br>[6/2020]  | 1,034.01<br>(-)<br>[1,034.01]        | 367.64<br>(0.00)<br>[32]    |
| 465 | REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL                                                               | 11/2016 | 6/2019<br>(-)<br>[6/2020]   | 262.87<br>(-)<br>[262.87]            | 77.06<br>(0.00)<br>[12]     |
|     | <u>Urban Development</u>                                                                                  |         |                             |                                      |                             |
| 466 | 2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT<br>ISM DHANBAD                                               | 9/2012  | 3/2016<br>(-)<br>[4/2020]   | 171.86<br>(-)<br>[171.86]            | 41.28<br>(0.00)<br>[49]     |
| 467 | CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI,<br>KODERMA, HAZARIBAG, RAMGARH AND CHATRA<br>DISTRICT         | 12/2007 | 3/2018<br>(-)<br>[0/0]      | 200.00<br>(-)<br>[200.00]            | 131.15<br>(0.00)<br>[0]     |
| 468 | CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY                                                               | 4/2013  | 4/2018<br>(-)<br>[0/0]      | 170.00<br>(-)<br>[170.00]            | 88.91<br>(0.00)<br>[0]      |
| 469 | CONSTRUCTION OF RURAL ROAD DEVELOPMENT<br>AUTHORITY UNDER PHASE-XII                                       | 2/2014  | 12/2016<br>(-)<br>[12/2018] | 787.29<br>(-)<br>[787.29]            | 285.30<br>(0.00)<br>[24]    |
| 470 | CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR<br>MAINTAINANCE UNDER PMGSY-JHARKHAND                          | 12/2007 | 6/2016<br>(-)<br>[0/0]      | 253.92<br>(253.92)<br>[253.92]       | 193.97<br>(0.00)<br>[0]     |
|     | <u>KARNATAKA</u>                                                                                          |         |                             |                                      |                             |
|     | <u>Petroleum</u>                                                                                          |         |                             |                                      |                             |
| 471 | BSVI UPGRADATION                                                                                          | 9/2016  | 12/2019<br>(-)<br>[12/2019] | 1,810.00<br>(1,810.00)<br>[1,810.00] | 130.79<br>(0.00)<br>[0]     |
| 472 | CAPACITY ENHANCEMENT/ REVAMP OF NHT-<br>2/PLATFORMER-2/CCR-2/PSA-2/RSU                                    | 5/2015  | 4/2019<br>(-)<br>[4/2019]   | 224.00<br>(207.00)<br>[207.25]       | 99.99<br>(-16.75)<br>[0]    |
| 473 | GAIL GAS LTD BENGALURU CGD PROJECT                                                                        | 2/2015  | 2/2020<br>(-)<br>[2/2020]   | 749.00<br>(-)<br>[749.00]            | 733.62<br>(0.00)<br>[0]     |
| 474 | RAILWAY SIDING PROJECT FOR EVACUATION OF<br>PETCOKE                                                       | 10/2015 | 3/2019<br>(-)<br>[3/2019]   | 135.00<br>(171.00)<br>[170.70]       | 124.25<br>(35.70)<br>[0]    |
| 475 | SEA WATER DESALINATION PLANT                                                                              | 11/2017 | 3/2020<br>(-)<br>[3/2020]   | 581.00<br>(-)<br>[581.00]            | 0.00<br>(0.00)<br>[0]       |
| 476 | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR                                                              | 1/2006  | 1/2012<br>(-)<br>[0/0]      | 993.00<br>(-)<br>[1,693.00]          | 1,549.85<br>(700.00)<br>[0] |
|     | <u>Power</u>                                                                                              |         |                             |                                      |                             |

|     |                                                                                                 |        |                                   |                                      |                                |
|-----|-------------------------------------------------------------------------------------------------|--------|-----------------------------------|--------------------------------------|--------------------------------|
| 477 | KUDGI STPP STAGE 1                                                                              | 1/2012 | 1/2017<br>(-)<br>[0/0]            | 15,166.19<br>(-)<br>[16,934.65]      | 15,364.00<br>(1,768.46)<br>[0] |
| 478 | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) | 5/2017 | 2/2019<br>(2/2019)<br>[6/2019]    | 445.89<br>(445.89)<br>[445.89]       | 220.56<br>(0.00)<br>[4]        |
|     | <b>Railways</b>                                                                                 |        |                                   |                                      |                                |
| 479 | ARSIKERE-TUMKUR                                                                                 | 3/2015 | 3/2020<br>(3/2020)<br>[3/2020]    | 578.00<br>(578.00)<br>[578.00]       | 458.72<br>(0.00)<br>[0]        |
| 480 | BAGALKOT-KUDACHI NL                                                                             | 4/2010 | 3/2016<br>(12/2023)<br>[12/2023]  | 986.30<br>(986.30)<br>[986.30]       | 287.03<br>(0.00)<br>[93]       |
| 481 | BANGLORE - SATYAMANGALAM (NL)(SWR)                                                              | 4/1996 | 3/2002<br>(3/2024)<br>[3/2024]    | 1,382.78<br>(1,382.78)<br>[1,382.78] | 7.35<br>(0.00)<br>[264]        |
| 482 | CHIKBALLA-PUR-GOWRIBIDANUR NL                                                                   | 4/2013 | /<br>(12/2023)<br>[12/2023]       | 327.25<br>(367.77)<br>[367.77]       | 0.31<br>(40.52)<br>[-]         |
| 483 | CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL                                             | 4/2013 | /<br>(12/2023)<br>[12/2023]       | 558.00<br>(692.43)<br>[692.43]       | 0.00<br>(134.43)<br>[-]        |
| 484 | GADAG-WADI NL                                                                                   | 4/2013 | 12/2018<br>(12/2024)<br>[12/2024] | 2,841.84<br>(2,841.84)<br>[2,841.84] | 39.98<br>(0.00)<br>[72]        |
| 485 | HOSPET-HUBLI-LONDA-VASCODAGAMA DL                                                               | 4/2010 | 3/2023<br>(-)<br>[3/2023]         | 2,127.00<br>(-)<br>[2,127.00]        | 1,042.32<br>(0.00)<br>[0]      |
| 486 | HUBLI- CHIKJAJUR                                                                                | 3/2015 | 3/2020<br>(3/2020)<br>[3/2021]    | 1,156.94<br>(1,156.94)<br>[1,156.94] | 701.76<br>(0.00)<br>[12]       |
| 487 | HUBLI-ANKOLA(NL),SWR                                                                            | 4/1997 | /<br>(12/2024)<br>[12/2024]       | 2,315.00<br>(-)<br>[2,135.00]        | 144.75<br>(-180.00)<br>[-]     |
| 488 | KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)                                                   | 3/1996 | 3/2017<br>(-)<br>[3/2020]         | 644.78<br>(889.52)<br>[889.52]       | 433.71<br>(244.74)<br>[36]     |
| 489 | MARIKUPPAM - KUPPAM                                                                             | 4/2012 | 3/2016<br>(12/2023)<br>[12/2023]  | 279.54<br>(279.54)<br>[279.54]       | 8.80<br>(0.00)<br>[93]         |
| 490 | MUNIRABAD (GINGERA) -RAICHUR NL                                                                 | 4/2007 | /<br>(-)<br>[12/2023]             | 179.65<br>(1,350.91)<br>[1,350.91]   | 924.08<br>(1,171.26)<br>[-]    |
| 491 | SHIMOGA-HARIHAR NL                                                                              | 4/2011 | 3/2016<br>(3/2024)<br>[3/2024]    | 832.47<br>(-)<br>[832.47]            | 0.94<br>(0.00)<br>[96]         |
| 492 | TORANAGALLU-RANJITPURA DL                                                                       | 4/2011 | /<br>(12/2023)<br>[12/2023]       | 146.75<br>(167.50)<br>[167.50]       | 0.34<br>(20.75)<br>[-]         |
| 493 | TUMKUR-CHITRADURGA-DAVENGERE NL                                                                 | 4/2011 | /<br>(12/2023)<br>[12/2023]       | 1,801.01<br>(-)<br>[1,801.01]        | 13.67<br>(0.00)<br>[-]         |
| 494 | WHITE FIELD-KOLAR NL                                                                            | 4/2011 | /<br>(12/2023)<br>[12/2023]       | 348.85<br>(-)<br>[348.85]            | 0.36<br>(0.00)<br>[-]          |
|     | <b>Road Transport And Highways</b>                                                              |        |                                   |                                      |                                |
| 495 | HOSPET-BELLARY-KARNATAKA AP BORDER                                                              | 8/2016 | 3/2019<br>(-)<br>[3/2019]         | 1,167.42<br>(-)<br>[1,167.42]        | 192.72<br>(0.00)<br>[0]        |
| 496 | 2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER    | 2/2018 | /<br>(-)                          | 486.78<br>(-)                        | 0.00<br>(0.00)                 |

|     |                                                                                                      |         |                            |                                    |                             |
|-----|------------------------------------------------------------------------------------------------------|---------|----------------------------|------------------------------------|-----------------------------|
|     | FROM KM                                                                                              |         | [0/0]                      | [486.78]                           | [0]                         |
| 497 | 4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION                                                    | 5/2014  | 8/2016<br>(-)<br>[3/2019]  | 1,655.01<br>(-)<br>[1,655.01]      | 1,515.16<br>(0.00)<br>[31]  |
| 498 | 4-LANING OF HOSKOTE-DOBBASPET                                                                        | 5/2014  | /<br>(-)<br>[0/0]          | 720.69<br>(-)<br>[720.69]          | 99.03<br>(0.00)<br>[0]      |
| 499 | 4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY                                       | 3/2016  | 3/2019<br>(-)<br>[7/2019]  | 701.40<br>(-)<br>[701.40]          | 22.02<br>(0.00)<br>[4]      |
| 500 | 4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL                                         | 3/2016  | 3/2019<br>(-)<br>[11/2020] | 870.00<br>(-)<br>[870.00]          | 9.12<br>(0.00)<br>[20]      |
| 501 | FOUR LANING OF HOSPET - CHITRADURGA                                                                  | 3/2015  | 8/2018<br>(-)<br>[4/2019]  | 1,388.00<br>(-)<br>[1,388.00]      | 924.40<br>(0.00)<br>[8]     |
| 502 | FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB                             | 8/2016  | 4/2020<br>(-)<br>[4/2020]  | 1,664.20<br>(-)<br>[1,664.20]      | 313.63<br>(0.00)<br>[0]     |
| 503 | HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER                                                    | 9/2010  | 6/2018<br>(-)<br>[3/2019]  | 946.00<br>(-)<br>[946.00]          | 818.53<br>(0.00)<br>[9]     |
| 504 | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB | 1/1991  | 1/2018<br>(-)<br>[0/0]     | 219.40<br>(-)<br>[219.40]          | 0.00<br>(0.00)<br>[0]       |
| 505 | SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O | 3/2017  | 3/2020<br>(-)<br>[6/2020]  | 993.16<br>(-)<br>[1,434.00]        | 413.53<br>(440.84)<br>[3]   |
| 506 | SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA   | 3/2017  | 3/2020<br>(-)<br>[6/2020]  | 831.58<br>(-)<br>[1,177.00]        | 121.00<br>(345.42)<br>[3]   |
| 507 | SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA  | 2/2018  | /<br>(-)<br>[0/0]          | 2,177.80<br>(-)<br>[2,177.80]      | 0.00<br>(0.00)<br>[0]       |
| 508 | SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT | 2/2018  | /<br>(-)<br>[0/0]          | 1,995.34<br>(-)<br>[1,995.34]      | 0.00<br>(0.00)<br>[0]       |
| 509 | STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP | 3/2015  | 11/2015<br>(-)<br>[0/0]    | 165.67<br>(-)<br>[165.67]          | 0.00<br>(0.00)<br>[0]       |
| 510 | STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU | 3/2015  | 11/2015<br>(-)<br>[0/0]    | 159.12<br>(-)<br>[159.12]          | 0.00<br>(0.00)<br>[0]       |
| 511 | TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 ( NEW NH NO -50)  | 5/2015  | 9/2017<br>(-)<br>[12/2018] | 709.00<br>(-)<br>[709.00]          | 380.95<br>(0.00)<br>[15]    |
| 512 | TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM | 9/2016  | 8/2019<br>(-)<br>[8/2019]  | 950.69<br>(-)<br>[950.69]          | 499.54<br>(0.00)<br>[0]     |
|     | <u>Urban Development</u>                                                                             |         |                            |                                    |                             |
| 513 | BANGALORE METRO RAIL PROJECT PHASE-2                                                                 | 2/2014  | 2/2019<br>(-)<br>[3/2020]  | 26,405.14<br>(-)<br>[26,405.14]    | 499.85<br>(0.00)<br>[13]    |
| 514 | CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA                                             | 5/2005  | 2/2014<br>(-)<br>[0/0]     | 768.88<br>(1,070.97)<br>[1,113.34] | 1,085.64<br>(344.46)<br>[0] |
| 515 | CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA                                  | 7/2011  | 12/2015<br>(-)<br>[0/0]    | 324.87<br>(324.87)<br>[324.87]     | 262.93<br>(0.00)<br>[0]     |
| 516 | RESIDENTIAL QUATERS FOR HAL,BANGLORE                                                                 | 12/2016 | 2/2020<br>(9/2020)         | 246.31<br>(-)                      | 34.88<br>(0.00)             |

|     |                                                                                                      |         |                                  |                                      |                              |
|-----|------------------------------------------------------------------------------------------------------|---------|----------------------------------|--------------------------------------|------------------------------|
|     |                                                                                                      |         | [9/2020]                         | [246.31]                             | [7]                          |
|     | <u>KERALA</u>                                                                                        |         |                                  |                                      |                              |
|     | <u>Petroleum</u>                                                                                     |         |                                  |                                      |                              |
| 517 | KOCHI SALEM LPG PIPELINE PROJECT                                                                     | 12/2015 | 6/2019<br>(-)<br>[6/2019]        | 1,112.00<br>(-)<br>[1,112.00]        | 108.79<br>(0.00)<br>[0]      |
| 518 | LPG TERMINAL AT KOCHI                                                                                | 10/2015 | 10/2017<br>(-)<br>[3/2019]       | 607.06<br>(-)<br>[714.25]            | 352.32<br>(107.19)<br>[17]   |
| 519 | MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY                               | 2/2016  | 2/2020<br>(10/2020)<br>[10/2020] | 3,313.00<br>(3,288.96)<br>[3,288.96] | 404.03<br>(-24.04)<br>[8]    |
| 520 | PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY                                  | 11/2014 | 8/2018<br>(11/2019)<br>[11/2019] | 4,588.29<br>(5,245.96)<br>[5,245.96] | 2,543.09<br>(657.67)<br>[15] |
|     | <u>Railways</u>                                                                                      |         |                                  |                                      |                              |
| 521 | ANGAMALI-SABARIMALA (N.L.)(SR)                                                                       | 10/1998 | /<br>(-)<br>[0/0]                | 1,566.00<br>(-)<br>[2,815.62]        | 254.53<br>(1,249.62)<br>[0]  |
| 522 | CHENGANNUR-CHINGAVANAM                                                                               | 4/2006  | /<br>(-)<br>[0/0]                | 191.72<br>(-)<br>[369.83]            | 432.50<br>(178.11)<br>[0]    |
| 523 | ERNAKULAM-KUMBALAM                                                                                   | 4/2010  | /<br>(-)<br>[0/0]                | 189.24<br>(-)<br>[189.24]            | 6.70<br>(0.00)<br>[0]        |
| 524 | KUMBALAM-TURAVUR                                                                                     | 4/2011  | /<br>(-)<br>[0/0]                | 252.96<br>(-)<br>[252.96]            | 8.50<br>(0.00)<br>[0]        |
| 525 | MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING.                                                        | 2/2005  | 3/2014<br>(-)<br>[0/0]           | 241.00<br>(-)<br>[241.00]            | 294.63<br>(0.00)<br>[0]      |
| 526 | PALAKKAD - SETTING UP OF RAIL COACH FACTORY                                                          | 2/2012  | 3/2016<br>(-)<br>[0/0]           | 550.00<br>(-)<br>[550.00]            | 0.00<br>(0.00)<br>[0]        |
| 527 | TRIVANDRUM-KANYAKUMARI DOUBLING                                                                      | 2/2015  | /<br>(-)<br>[0/0]                | 1,431.90<br>(-)<br>[1,431.90]        | 23.84<br>(0.00)<br>[0]       |
| 528 | TURAVUR-AMBALAPUZHA DOUBLING                                                                         | 2/2015  | /<br>(-)<br>[0/0]                | 1,000.00<br>(-)<br>[828.50]          | 0.08<br>(-171.50)<br>[0]     |
|     | <u>Road Transport And Highways</u>                                                                   |         |                                  |                                      |                              |
| 529 | 4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47                                                 | 6/2015  | /<br>(-)<br>[4/2019]             | 845.24<br>(-)<br>[845.24]            | 127.87<br>(0.00)<br>[-]      |
| 530 | 4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T | 4/2016  | 6/2018<br>(-)<br>[4/2019]        | 804.97<br>(-)<br>[804.97]            | 21.80<br>(0.00)<br>[10]      |
| 531 | 4-LANNING OF THALSERRY -MAHE BYPASS                                                                  | 9/2017  | 9/2017<br>(-)<br>[6/2020]        | 1,124.11<br>(-)<br>[1,124.11]        | 0.00<br>(0.00)<br>[33]       |
| 532 | 6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH | 2/2018  | /<br>(-)<br>[0/0]                | 1,424.77<br>(-)<br>[1,424.77]        | 0.00<br>(0.00)<br>[0]        |
| 533 | CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 | 1/2014  | 11/2017<br>(-)<br>[0/0]          | 267.16<br>(352.00)<br>[352.05]       | 201.35<br>(84.89)<br>[0]     |
| 534 | CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 | 1/2014  | 9/2017<br>(-)<br>[0/0]           | 255.75<br>(348.00)<br>[348.43]       | 231.56<br>(92.68)<br>[0]     |
| 535 | SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM                                          | 2/2010  | 8/2012<br>(-)                    | 617.00<br>(-)                        | 943.17<br>(0.00)             |

|     |                                                                                                      |         |                                |                                 |                                 |
|-----|------------------------------------------------------------------------------------------------------|---------|--------------------------------|---------------------------------|---------------------------------|
|     |                                                                                                      |         | [3/2019]                       | [617.00]                        | [79]                            |
|     | <u>Urban Development</u>                                                                             |         |                                |                                 |                                 |
| 536 | C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) | 9/2017  | 3/2020<br>(-)<br>[3/2020]      | 150.29<br>(-)<br>[150.29]       | 2.58<br>(0.00)<br>[0]           |
| 537 | CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA                                                | 1/2010  | 10/2012<br>(-)<br>[3/2019]     | 165.23<br>(-)<br>[165.23]       | 58.85<br>(0.00)<br>[77]         |
| 538 | KOCHI METRO RAIL PROJECT                                                                             | 7/2012  | 7/2017<br>(-)<br>[12/2019]     | 5,181.79<br>(-)<br>[5,181.79]   | 0.00<br>(0.00)<br>[29]          |
|     | <u>MADHYA PRADESH</u>                                                                                |         |                                |                                 |                                 |
|     | <u>Coal</u>                                                                                          |         |                                |                                 |                                 |
| 539 | AMADAND OPENCAST EXPANSION PROJECT                                                                   | 3/2016  | 3/2021<br>(-)<br>[3/2021]      | 869.44<br>(-)<br>[869.44]       | 111.89<br>(0.00)<br>[0]         |
| 540 | AMRITDHARA OC PROJECT                                                                                | 2/2015  | 3/2023<br>(-)<br>[3/2023]      | 481.60<br>(-)<br>[481.60]       | 0.00<br>(0.00)<br>[0]           |
| 541 | BATURA HIGHWALL PROJECT                                                                              | 7/2015  | 3/2022<br>(-)<br>[3/2022]      | 231.92<br>(-)<br>[231.92]       | 0.00<br>(0.00)<br>[0]           |
| 542 | BATURA OCP (2.0 MTY)                                                                                 | 8/2015  | 3/2023<br>(-)<br>[3/2021]      | 1,186.64<br>(-)<br>[203.82]     | 103.85<br>(-982.82)<br>[-24]    |
| 543 | COAL PROJECT NAME JAMUNIA UG (0.84 MTY)                                                              | 7/2016  | 3/2022<br>(-)<br>[3/2022]      | 409.87<br>(-)<br>[409.87]       | 17.50<br>(0.00)<br>[0]          |
| 544 | DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)                                                              | 11/2017 | 3/2022<br>(-)<br>[3/2022]      | 1,255.17<br>(-)<br>[1,255.17]   | 94.68<br>(0.00)<br>[0]          |
| 545 | JAYANT EXPANSION OCP 10 TO 20 MTPA                                                                   | 5/2017  | 3/2021<br>(-)<br>[3/2021]      | 1,783.09<br>(-)<br>[1,783.09]   | 229.76<br>(0.00)<br>[0]         |
| 546 | KANCHAN OC EXPANSION                                                                                 | 12/2014 | 3/2021<br>(-)<br>[3/2021]      | 371.04<br>(-)<br>[371.04]       | 41.52<br>(0.00)<br>[0]          |
| 547 | MALACHUA OPENCAST PROJECT                                                                            | 10/2015 | 3/2023<br>(-)<br>[3/2023]      | 488.33<br>(-)<br>[488.33]       | 24.16<br>(0.00)<br>[0]          |
| 548 | NIGAHU OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI                                              | 10/2007 | 3/2012<br>(-)<br>[0/0]         | 259.40<br>(-)<br>[486.57]       | 266.38<br>(227.17)<br>[0]       |
| 549 | RAJNAGAR OCP RPR (1.70 MTY)                                                                          | 12/2014 | 3/2021<br>(-)<br>[3/2021]      | 357.80<br>(-)<br>[357.80]       | 113.19<br>(0.00)<br>[0]         |
|     | <u>Petroleum</u>                                                                                     |         |                                |                                 |                                 |
| 550 | PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND   | 8/2017  | 6/2020<br>(-)<br>[10/2020]     | 236.00<br>(-)<br>[236.00]       | 11.66<br>(0.00)<br>[4]          |
|     | <u>Power</u>                                                                                         |         |                                |                                 |                                 |
| 551 | AMELIA COAL MINE                                                                                     | 1/2017  | 9/2020<br>(-)<br>[9/2020]      | 2,104.21<br>(-)<br>[2,104.21]   | 66.05<br>(0.00)<br>[0]          |
| 552 | GADARWARA SUPER THERMAL POWER PROJECT STAGE-I                                                        | 3/2013  | 9/2017<br>(6/2019)<br>[6/2019] | 11,638.55<br>(-)<br>[12,865.92] | 10,375.32<br>(1,227.37)<br>[21] |
| 553 | KHARGONE STPP STAGE I (1320 MW)                                                                      | 3/2015  | 9/2019<br>(-)<br>[9/2019]      | 9,870.51<br>(-)<br>[11,148.86]  | 6,693.90<br>(1,278.35)<br>[0]   |
| 554 | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK                                                        | 1/2016  | 3/2017                         | 305.04                          | 229.91                          |

|     |                                                                                                           |         |                                |                                      |                                |
|-----|-----------------------------------------------------------------------------------------------------------|---------|--------------------------------|--------------------------------------|--------------------------------|
|     | (750 MW)                                                                                                  |         | (9/2018)<br>[1/2019]           | (305.04)<br>[305.04]                 | (0.00)<br>[22]                 |
|     | <b>Railways</b>                                                                                           |         |                                |                                      |                                |
| 555 | ANUPPUR-KATNI                                                                                             | 4/2015  | 12/2021<br>(-)<br>[12/2021]    | 1,370.00<br>(-)<br>[1,370.00]        | 101.00<br>(0.00)<br>[0]        |
| 556 | BINA - KOTA DOUBLING WITH RE                                                                              | 4/2011  | 12/2020<br>(-)<br>[12/2020]    | 1,485.85<br>(-)<br>[1,485.85]        | 1,038.90<br>(0.00)<br>[0]      |
| 557 | CHHINDWARA - NAGPUR (GC)(SECR)                                                                            | 4/2005  | /<br>(-)<br>[0/0]              | 383.79<br>(-)<br>[1,101.16]          | 194.91<br>(717.37)<br>[0]      |
| 558 | CHHINDWARA NAINPUR MANDLA FORT GAUGE<br>CONVERSION PROJECT                                                | 4/2010  | 2/2019<br>(-)<br>[2/2019]      | 585.93<br>(-)<br>[1,420.39]          | 104.10<br>(834.46)<br>[0]      |
| 559 | CHHINDWARA-MANDLA FORT GC                                                                                 | 3/2011  | 3/2012<br>(-)<br>[3/2020]      | 556.54<br>(-)<br>[1,342.46]          | 396.00<br>(785.92)<br>[96]     |
| 560 | INDORE-DEWAS-UJJAIN (80 KMS)                                                                              | 4/2016  | 6/2020<br>(-)<br>[6/2020]      | 700.00<br>(-)<br>[700.00]            | 11.19<br>(0.00)<br>[0]         |
| 561 | KATNI - SINGRAULI DOUBLING PROJECT                                                                        | 12/2015 | 3/2020<br>(-)<br>[10/2021]     | 1,763.93<br>(-)<br>[1,763.93]        | 0.00<br>(0.00)<br>[19]         |
| 562 | KATNI GRADE SEPARATOR/BYE PASS                                                                            | 8/2016  | 3/2022<br>(-)<br>[3/2022]      | 582.13<br>(-)<br>[1,260.61]          | 0.00<br>(678.48)<br>[0]        |
| 563 | KATNI-BINA 3RD LINE (263 KM)                                                                              | 6/2016  | 3/2022<br>(-)<br>[3/2022]      | 2,478.23<br>(-)<br>[2,478.23]        | 112.07<br>(0.00)<br>[0]        |
| 564 | MULTI MODAL LOGISTICS PARK AT TIHI                                                                        | 12/2015 | 3/2019<br>(-)<br>[8/2019]      | 174.00<br>(-)<br>[174.00]            | 139.38<br>(0.00)<br>[5]        |
| 565 | RAMGANJMUNDI-BHOPAL (NL),WCR                                                                              | 4/2001  | 3/2021<br>(-)<br>[3/2021]      | 424.60<br>(-)<br>[2,713.09]          | 898.83<br>(2,288.49)<br>[0]    |
| 566 | RATLAM-MHOW-KHANDWA-AKOLA (GC)                                                                            | 4/2008  | 3/2022<br>(3/2019)<br>[3/2022] | 3,503.69<br>(2,473.40)<br>[1,030.29] | 1,081.52<br>(-2,473.40)<br>[0] |
|     | <b>Road Transport And Highways</b>                                                                        |         |                                |                                      |                                |
| 567 | BALANCE WORK FOR FOUR LANING OF ITARSI TO<br>BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00<br>(DESIGN | 12/2017 | /<br>(-)<br>[0/0]              | 950.27<br>(-)<br>[950.27]            | 0.00<br>(0.00)<br>[0]          |
| 568 | BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF<br>BHOPAL-SANCHI SECTION                                    | 8/2016  | 1/2019<br>(-)<br>[1/2019]      | 227.49<br>(-)<br>[227.49]            | 15.03<br>(0.00)<br>[0]         |
| 569 | BALANCE WORK OF 4-LANNING OF LALGHATI TO<br>MUBARAKPUR OF NH-12                                           | 9/2017  | 9/2017<br>(-)<br>[0/0]         | 374.40<br>(-)<br>[374.40]            | 0.00<br>(0.00)<br>[0]          |
| 570 | BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO<br>ITARSI SECTION OF NH-69                                   | 9/2017  | 9/2017<br>(-)<br>[0/0]         | 990.61<br>(-)<br>[990.61]            | 0.00<br>(0.00)<br>[0]          |
| 571 | BAMITHA-SATANA (2L+PS) OF NH-75 IN MP                                                                     | 8/2015  | /<br>(-)<br>[0/0]              | 257.80<br>(-)<br>[257.00]            | 12.38<br>(-0.80)<br>[0]        |
| 572 | BARELA-MANDLA SECTION OF NH-12A IN MADHYA<br>PRADESH KM 22/8 TO KM 89/6 OF NH-12A                         | 6/2015  | /<br>(-)<br>[0/0]              | 390.51<br>(-)<br>[390.51]            | 43.25<br>(0.00)<br>[0]         |
| 573 | BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP                                                                | 11/2011 | 2/2015<br>(-)<br>[0/0]         | 670.82<br>(-)<br>[670.82]            | 590.00<br>(0.00)<br>[0]        |

|     |                                                                                                      |         |                             |                               |                              |
|-----|------------------------------------------------------------------------------------------------------|---------|-----------------------------|-------------------------------|------------------------------|
| 574 | BHOPAL-BIARA (4L) OF NH-12 IN MP                                                                     | 11/2011 | 5/2015<br>(-)<br>[1/2020]   | 704.26<br>(-)<br>[704.26]     | 5.21<br>(0.00)<br>[56]       |
| 575 | BIARA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP                                                        | 3/2013  | 2/2016<br>(-)<br>[0/0]      | 257.80<br>(-)<br>[257.80]     | 59.30<br>(0.00)<br>[0]       |
| 576 | FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR | 6/2015  | 1/2019<br>(-)<br>[1/2019]   | 1,583.79<br>(-)<br>[1,583.79] | 1,439.18<br>(0.00)<br>[0]    |
| 577 | FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO | 1/2018  | /<br>(-)<br>[8/2020]        | 960.24<br>(-)<br>[960.24]     | 0.00<br>(0.00)<br>[-]        |
| 578 | FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA  | 6/2015  | 3/2016<br>(-)<br>[3/2019]   | 1,012.90<br>(-)<br>[1,012.90] | 1,042.73<br>(0.00)<br>[36]   |
| 579 | FOUR LANING OF GWALIOR-SHIVPURI                                                                      | 5/2013  | 11/2015<br>(-)<br>[12/2018] | 1,055.00<br>(-)<br>[1,601.77] | 1,393.40<br>(546.77)<br>[37] |
| 580 | FOUR LANING OF JABALPUR - LAKHNADON                                                                  | 3/2015  | /<br>(-)<br>[3/2019]        | 928.83<br>(-)<br>[928.83]     | 202.91<br>(0.00)<br>[-]      |
| 581 | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I                                                  | 3/2015  | /<br>(-)<br>[5/2019]        | 794.30<br>(-)<br>[794.30]     | 152.81<br>(0.00)<br>[-]      |
| 582 | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II                                                 | 3/2015  | /<br>(-)<br>[3/2019]        | 795.76<br>(-)<br>[795.76]     | 171.72<br>(0.00)<br>[-]      |
| 583 | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV                                                 | 3/2015  | /<br>(-)<br>[3/2019]        | 810.22<br>(-)<br>[810.22]     | 121.57<br>(0.00)<br>[-]      |
| 584 | FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.  | 10/2017 | 10/2017<br>(-)<br>[1/2020]  | 639.97<br>(-)<br>[639.97]     | 58.04<br>(0.00)<br>[27]      |
| 585 | FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE | 1/2018  | /<br>(-)<br>[0/0]           | 770.73<br>(-)<br>[770.73]     | 0.00<br>(0.00)<br>[0]        |
| 586 | GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93                                   | 12/2015 | 6/2018<br>(-)<br>[0/0]      | 927.54<br>(-)<br>[927.54]     | 29.17<br>(0.00)<br>[0]       |
| 587 | INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870                    | 11/2013 | 5/2017<br>(-)<br>[0/0]      | 497.05<br>(-)<br>[497.05]     | 0.00<br>(0.00)<br>[0]        |
| 588 | INDORE-DEWAS(NH-3)                                                                                   | 11/2010 | 5/2013<br>(-)<br>[0/0]      | 325.00<br>(-)<br>[325.00]     | 469.54<br>(0.00)<br>[0]      |
| 589 | INDORE-JHABUA-GUJRAT/MP                                                                              | 10/2010 | 4/2013<br>(-)<br>[11/2018]  | 1,175.00<br>(-)<br>[1,206.10] | 1,342.77<br>(31.10)<br>[0]   |
| 590 | JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400                       | 11/2015 | 3/2018<br>(-)<br>[0/0]      | 628.45<br>(-)<br>[628.45]     | 20.74<br>(0.00)<br>[0]       |
| 591 | JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A            | 2/2015  | 5/2017<br>(-)<br>[0/0]      | 327.32<br>(-)<br>[327.32]     | 142.73<br>(0.00)<br>[0]      |
| 592 | KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4                                      | 2/2015  | 7/2017<br>(-)<br>[0/0]      | 377.83<br>(-)<br>[377.83]     | 57.42<br>(0.00)<br>[0]       |
| 593 | MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A                      | 6/2015  | 12/2017<br>(-)<br>[0/0]     | 641.02<br>(-)<br>[641.02]     | 89.88<br>(0.00)<br>[0]       |
| 594 | MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN                                                        | 1/2012  | 4/2015                      | 381.86                        | 252.03                       |



|     |                                                                                                      |         |                                |                                |                          |
|-----|------------------------------------------------------------------------------------------------------|---------|--------------------------------|--------------------------------|--------------------------|
|     | MP                                                                                                   |         | (-)<br>[0/0]                   | (-)<br>[381.86]                | (0.00)<br>[0]            |
| 595 | SATANA-BELA SECTION OF NH-75(4L) IN MP                                                               | 1/2012  | 8/2015<br>(-)<br>[0/0]         | 320.48<br>(-)<br>[320.48]      | 189.49<br>(0.00)<br>[0]  |
| 596 | SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER<br>SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO<br>245/0 | 6/2015  | 5/2017<br>(-)<br>[0/0]         | 532.49<br>(-)<br>[532.49]      | 137.08<br>(0.00)<br>[0]  |
| 597 | SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP                                                      | 11/2011 | 9/2015<br>(-)<br>[0/0]         | 871.15<br>(-)<br>[871.15]      | 332.25<br>(0.00)<br>[0]  |
| 598 | UMARIYA TO SHAHOL SECTION OF NH-78 IN MADYA<br>PRADESH KM 68/4 TO 142/200                            | 3/2015  | 8/2017<br>(-)<br>[0/0]         | 511.83<br>(-)<br>[511.83]      | 40.87<br>(0.00)<br>[0]   |
|     | <u>MAHARASHTRA</u>                                                                                   |         |                                |                                |                          |
|     | <u>Coal</u>                                                                                          |         |                                |                                |                          |
| 599 | ADASA UG TO OC                                                                                       | 8/2015  | 3/2023<br>(3/2024)<br>[3/2024] | 288.90<br>(333.43)<br>[333.43] | 0.02<br>(44.53)<br>[12]  |
| 600 | AMALGAMATED GONDEGAON GHATROHAN OC                                                                   | 2/2016  | 3/2019<br>(-)<br>[3/2019]      | 198.68<br>(-)<br>[198.68]      | 254.72<br>(0.00)<br>[0]  |
| 601 | AMALGAMATED PAUNI-II III OC MINE                                                                     | 6/2015  | 3/2021<br>(-)<br>[3/2021]      | 483.69<br>(-)<br>[483.69]      | 89.91<br>(0.00)<br>[0]   |
| 602 | AMALGAMATED YEKONA-I YEKONA-II                                                                       | 8/2015  | 3/2025<br>(-)<br>[3/2025]      | 727.28<br>(-)<br>[727.28]      | 238.43<br>(0.00)<br>[0]  |
| 603 | BHANEKAON OC                                                                                         | 2/2015  | 3/2023<br>(2/2017)<br>[3/2023] | 187.94<br>(409.68)<br>[409.68] | 95.83<br>(221.74)<br>[0] |
| 604 | BHATADI EXPANSION OC MINE                                                                            | 2/2016  | 3/2019<br>(-)<br>[3/2019]      | 304.52<br>(-)<br>[304.52]      | 129.39<br>(0.00)<br>[0]  |
| 605 | DINESH OCP                                                                                           | 11/2014 | 3/2020<br>(-)<br>[3/2020]      | 611.16<br>(-)<br>[611.16]      | 395.73<br>(0.00)<br>[0]  |
| 606 | GOKUL                                                                                                | 11/2014 | 3/2018<br>(-)<br>[3/2018]      | 267.67<br>(-)<br>[267.67]      | 207.74<br>(0.00)<br>[0]  |
| 607 | KAMPTEE DEEP OC MINE                                                                                 | 11/2015 | 3/2021<br>(9/2018)<br>[3/2024] | 277.65<br>(313.34)<br>[313.34] | 6.12<br>(35.69)<br>[36]  |
| 608 | KOLAR PIMPRI EXTENSION OC                                                                            | 3/2017  | 3/2020<br>(-)<br>[3/2020]      | 362.73<br>(-)<br>[362.73]      | 258.23<br>(0.00)<br>[0]  |
| 609 | MAKARDHOKRA I OC                                                                                     | 9/2014  | 3/2021<br>(-)<br>[3/2021]      | 266.23<br>(-)<br>[266.23]      | 143.29<br>(0.00)<br>[0]  |
| 610 | MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE                                                            | 11/2015 | 3/2020<br>(-)<br>[3/2020]      | 498.42<br>(-)<br>[498.42]      | 59.20<br>(0.00)<br>[0]   |
| 611 | NEW MAJRI UG TO OC                                                                                   | 5/2015  | 3/2019<br>(-)<br>[3/2019]      | 295.56<br>(-)<br>[295.56]      | 88.13<br>(0.00)<br>[0]   |
| 612 | PENGANGA OCP(REVISED)                                                                                | 9/2014  | 3/2020<br>(-)<br>[3/2020]      | 441.82<br>(-)<br>[441.82]      | 187.02<br>(0.00)<br>[0]  |
| 613 | SINGHORI OC MINE                                                                                     | 6/2015  | 3/2020<br>(-)<br>[3/2020]      | 205.49<br>(-)<br>[205.49]      | 105.34<br>(0.00)<br>[0]  |

|     |                                                                                                      |         |                                   |                                      |                              |
|-----|------------------------------------------------------------------------------------------------------|---------|-----------------------------------|--------------------------------------|------------------------------|
|     | <b>Fertilisers</b>                                                                                   |         |                                   |                                      |                              |
| 614 | GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY                       | 4/2018  | 4/2020<br>(-)<br>[4/2020]         | 426.72<br>(-)<br>[426.72]            | 50.89<br>(0.00)<br>[0]       |
| 615 | GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL.                              | 2/2016  | 12/2017<br>(1/2019)<br>[1/2019]   | 482.85<br>(482.85)<br>[482.85]       | 413.00<br>(0.00)<br>[13]     |
| 616 | NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY                                                      | 10/2014 | 11/2016<br>(4/2019)<br>[4/2019]   | 197.79<br>(209.44)<br>[209.44]       | 140.10<br>(11.65)<br>[29]    |
|     | <b>Health And Family Welfare</b>                                                                     |         |                                   |                                      |                              |
| 617 | HOSPITAL AND TEACHING- AIIMS NAGPUR                                                                  | 3/2018  | /<br>(-)<br>[2/2020]              | 582.99<br>(-)<br>[582.99]            | 57.09<br>(0.00)<br>[-]       |
| 618 | RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA                                          | 8/2017  | 3/2019<br>(-)<br>[3/2019]         | 274.19<br>(-)<br>[274.19]            | 114.89<br>(0.00)<br>[0]      |
|     | <b>Petroleum</b>                                                                                     |         |                                   |                                      |                              |
| 619 | 180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA                                      | 6/2017  | 6/2020<br>(-)<br>[6/2020]         | 249.26<br>(-)<br>[249.26]            | 58.33<br>(0.00)<br>[0]       |
| 620 | 4TH PHASE DEVELOPMENT OF NBP FIELD                                                                   | 2/2017  | 11/2019<br>(11/2019)<br>[11/2019] | 968.61<br>(968.61)<br>[968.61]       | 601.19<br>(0.00)<br>[0]      |
| 621 | ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI | 5/2016  | 1/2021<br>(-)<br>[1/2021]         | 261.00<br>(-)<br>[261.00]            | 8.48<br>(0.00)<br>[0]        |
| 622 | ADDITIONAL FACILITIES AT MANMAD FOR COVERION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE     | 5/2016  | 1/2021<br>(-)<br>[4/2021]         | 212.00<br>(-)<br>[212.00]            | 14.11<br>(0.00)<br>[3]       |
| 623 | ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE  | 5/2016  | 1/2021<br>(-)<br>[10/2021]        | 348.00<br>(-)<br>[348.00]            | 9.20<br>(0.00)<br>[9]        |
| 624 | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)                              | 3/2011  | 5/2013<br>(3/2019)<br>[3/2019]    | 861.79<br>(1,577.15)<br>[1,577.15]   | 1,195.62<br>(715.36)<br>[70] |
| 625 | DEVELOPMENT OF B-147 FIELD                                                                           | 2/2017  | 11/2019<br>(11/2019)<br>[11/2019] | 546.15<br>(546.15)<br>[546.15]       | 226.78<br>(0.00)<br>[0]      |
| 626 | DEVELOPMENT OF BSE-11 BLOCK                                                                          | 2/2017  | 11/2019<br>(11/2019)<br>[11/2019] | 511.30<br>(511.30)<br>[511.30]       | 197.90<br>(0.00)<br>[0]      |
| 627 | DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)                                     | 2/2017  | 5/2021<br>(5/2021)<br>[5/2021]    | 4,006.83<br>(4,006.83)<br>[4,006.83] | 1,651.58<br>(0.00)<br>[0]    |
| 628 | ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA      | 1/2015  | 12/2017<br>(3/2020)<br>[3/2020]   | 4,619.94<br>(4,619.94)<br>[4,619.94] | 3,951.60<br>(0.00)<br>[27]   |
| 629 | INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY             | 2/2016  | 2/2020<br>(-)<br>[2/2020]         | 554.00<br>(-)<br>[554.00]            | 158.76<br>(0.00)<br>[0]      |
| 630 | INTEGRATED DEVELOPMENT OF B-127 FIELDS                                                               | 12/2011 | 3/2015<br>(12/2019)<br>[12/2019]  | 2,059.63<br>(2,665.65)<br>[2,665.65] | 1,842.42<br>(606.02)<br>[57] |
| 631 | KOYALI AHMEDNAGAR SOLAPUR PIPELINE                                                                   | 5/2016  | 8/2021<br>(-)<br>[8/2021]         | 1,945.00<br>(-)<br>[1,945.00]        | 514.20<br>(0.00)<br>[0]      |
| 632 | LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS                                     | 12/2015 | 4/2018<br>(5/2019)<br>[5/2019]    | 3,190.69<br>(-)<br>[3,247.19]        | 2,110.87<br>(56.50)<br>[13]  |
| 633 | MMPL PIPELINE REROUTING PROJECT                                                                      | 4/2013  | 12/2019                           | 449.58                               | 118.17                       |

|     |                                                                                     |         |                                 |                                      |                                 |
|-----|-------------------------------------------------------------------------------------|---------|---------------------------------|--------------------------------------|---------------------------------|
|     |                                                                                     |         | (-)<br>[12/2019]                | (-)<br>[449.58]                      | (0.00)<br>[0]                   |
| 634 | MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III                                     | 11/2014 | 4/2019<br>(3/2019)<br>[3/2019]  | 6,068.80<br>(6,068.80)<br>[5,296.93] | 4,576.40<br>(-771.87)<br>[-1]   |
| 635 | MUMBAI REFINERY EXPANSION PROJECT                                                   | 9/2015  | 3/2020<br>(-)<br>[7/2019]       | 4,199.00<br>(-)<br>[4,199.00]        | 194.97<br>(0.00)<br>[-8]        |
| 636 | NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY                 | 8/2015  | 3/2019<br>(5/2020)<br>[5/2020]  | 2,818.88<br>(-)<br>[2,818.88]        | 1,724.53<br>(0.00)<br>[14]      |
| 637 | NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY                            | 1/2017  | 5/2019<br>(5/2019)<br>[5/2019]  | 474.15<br>(474.15)<br>[474.15]       | 299.26<br>(0.00)<br>[0]         |
| 638 | PIPELINE REPLACEMENT PROJECT-V (OFFSHORE)                                           | 4/2018  | 12/2019<br>(-)<br>[12/2019]     | 766.37<br>(-)<br>[766.37]            | 0.00<br>(0.00)<br>[0]           |
| 639 | PUNE POL STORAGE DEPOT                                                              | 8/2016  | 8/2020<br>(-)<br>[8/2020]       | 282.64<br>(-)<br>[282.64]            | 63.91<br>(0.00)<br>[0]          |
|     | <u>Power</u>                                                                        |         |                                 |                                      |                                 |
| 640 | MOUDA STPP STAGE 2                                                                  | 3/2012  | 9/2016<br>(-)<br>[0/0]          | 7,921.47<br>(-)<br>[7,921.47]        | 5,302.00<br>(0.00)<br>[0]       |
| 641 | SOLAPUR STPP                                                                        | 3/2012  | 11/2016<br>(3/2019)<br>[3/2019] | 9,395.18<br>(-)<br>[9,395.18]        | 9,026.43<br>(0.00)<br>[28]      |
| 642 | WESTERN REGION STRENGTHENING SCHEME-V                                               | 12/2007 | 9/2010<br>(12/2018)<br>[2/2019] | 477.69<br>(738.48)<br>[738.48]       | 686.26<br>(260.79)<br>[101]     |
|     | <u>Railways</u>                                                                     |         |                                 |                                      |                                 |
| 643 | 3RD LINE BETWEEN BHUSAVAL-JALGAON                                                   | 4/2011  | 3/2019<br>(-)<br>[3/2019]       | 184.06<br>(199.12)<br>[298.70]       | 240.89<br>(114.64)<br>[0]       |
| 644 | AHMEDNAGAR-PARLI VAJINATH(NL) CR                                                    | 2/1997  | 3/2021<br>(-)<br>[3/2021]       | 2,271.50<br>(2,271.50)<br>[3,712.50] | 1,909.57<br>(1,441.00)<br>[0]   |
| 645 | AMRAVATI-NARKHER NL(CR)                                                             | 6/1994  | 6/1999<br>(-)<br>[0/0]          | 663.01<br>(668.34)<br>[858.96]       | 716.80<br>(195.95)<br>[0]       |
| 646 | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)                                   | 3/1996  | 3/2004<br>(-)<br>[3/2020]       | 495.44<br>(1,781.98)<br>[1,781.98]   | 1,337.62<br>(1,286.54)<br>[192] |
| 647 | DAUND - MANMAD (236 KM)                                                             | 2/2016  | 3/2023<br>(-)<br>[3/2023]       | 1,876.00<br>(2,081.27)<br>[2,081.27] | 1.27<br>(205.27)<br>[0]         |
| 648 | DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) | 3/2009  | 3/2020<br>(-)<br>[3/2020]       | 713.48<br>(-)<br>[1,750.00]          | 1,618.00<br>(1,036.52)<br>[0]   |
| 649 | DIGHI PORT NEW LINE                                                                 | 4/2015  | 12/2025<br>(-)<br>[3/2025]      | 723.78<br>(-)<br>[723.78]            | 0.22<br>(0.00)<br>[-9]          |
| 650 | INDORE - MANMAD VIA MALEGAON (368 KM)                                               | 2/2016  | 3/2024<br>(-)<br>[3/2024]       | 9,968.00<br>(-)<br>[8,857.98]        | 0.00<br>(-1,110.02)<br>[0]      |
| 651 | ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)                                            | 2/2015  | 3/2023<br>(-)<br>[3/2023]       | 2,449.91<br>(2,449.91)<br>[2,449.91] | 89.27<br>(0.00)<br>[0]          |
| 652 | KALYAN-KASARA 3RD LINE                                                              | 4/2011  | 3/2021<br>(-)<br>[3/2021]       | 792.89<br>(792.89)<br>[792.89]       | 275.17<br>(0.00)<br>[0]         |

|                                    |                                                                                                            |         |                             |                                      |                                |
|------------------------------------|------------------------------------------------------------------------------------------------------------|---------|-----------------------------|--------------------------------------|--------------------------------|
| 653                                | MANMAD - JALGAON - 3RD LINE (160 KM)                                                                       | 2/2016  | 3/2022<br>(-)<br>[3/2023]   | 1,035.16<br>(1,035.16)<br>[1,035.16] | 19.79<br>(0.00)<br>[12]        |
| 654                                | MULTI MODAL LOGISTICS TRANSPORT AT MIHAN                                                                   | 10/2013 | 3/2019<br>(-)<br>[3/2019]   | 305.00<br>(-)<br>[305.00]            | 253.22<br>(0.00)<br>[0]        |
| 655                                | MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD<br>TRAIN PROTECTION SYSTEM 500 RKM                                | 3/2010  | /<br>(-)<br>[0/0]           | 265.88<br>(-)<br>[265.88]            | 0.00<br>(0.00)<br>[0]          |
| 656                                | MUMBAI URBAN TRANSPORT PROJECT PHASE-II                                                                    | 4/2008  | 3/2014<br>(-)<br>[3/2019]   | 5,300.00<br>(-)<br>[7,986.04]        | 2,423.55<br>(2,686.04)<br>[60] |
| 657                                | PUNE-MIRAJ-LONDA (467 KM)                                                                                  | 2/2015  | 3/2024<br>(-)<br>[3/2024]   | 3,627.47<br>(3,627.47)<br>[3,627.47] | 332.55<br>(0.00)<br>[0]        |
| 658                                | PUNE-NASIK (265 KM)                                                                                        | 2/2016  | 3/2024<br>(-)<br>[3/2024]   | 2,425.00<br>(-)<br>[5,341.68]        | 0.00<br>(2,916.68)<br>[0]      |
| 659                                | RAJNANDGAON - NAGPUR - 3RD LINE (SECR)                                                                     | 9/2016  | 3/2023<br>(-)<br>[3/2023]   | 1,908.51<br>(-)<br>[2,686.63]        | 0.00<br>(778.12)<br>[0]        |
| 660                                | RUNNING OF 12 CAR TRAINS ON HARBOUR LINE                                                                   | 4/2012  | 4/2016<br>(-)<br>[0/0]      | 714.10<br>(-)<br>[714.10]            | 65.20<br>(0.00)<br>[0]         |
| 661                                | VAIBHAVWADI - KOLHAPUR (107 KM)                                                                            | 2/2016  | 3/2024<br>(-)<br>[3/2024]   | 2,750.00<br>(-)<br>[3,438.51]        | 0.00<br>(688.51)<br>[0]        |
| 662                                | VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL<br>CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137<br>A | 3/2012  | /<br>(-)<br>[0/0]           | 217.38<br>(-)<br>[217.38]            | 0.00<br>(0.00)<br>[0]          |
| 663                                | WADSA-GADHCHIROLI NEW LINE (52.36 KM)                                                                      | 6/2018  | 12/2021<br>(-)<br>[12/2021] | 229.00<br>(-)<br>[403.00]            | 36.28<br>(174.00)<br>[0]       |
| 664                                | WARDHA - NAGPUR - 4TH LINE (76 KM)                                                                         | 2/2016  | 3/2023<br>(-)<br>[3/2023]   | 637.95<br>(637.95)<br>[637.95]       | 28.96<br>(0.00)<br>[0]         |
| 665                                | WARDHA-BALHARSHAH - 3RD LINE (132 KM)                                                                      | 2/2015  | 3/2022<br>(-)<br>[3/2022]   | 1,272.19<br>(1,272.19)<br>[1,272.19] | 162.38<br>(0.00)<br>[0]        |
| 666                                | WARDHA-NANDED MAHARASHTRA                                                                                  | 4/2008  | 3/2023<br>(-)<br>[3/2023]   | 3,168.29<br>(3,168.29)<br>[3,168.29] | 992.77<br>(0.00)<br>[0]        |
| 667                                | WARDHA-SEWAGRAM NGP 3RD LINE                                                                               | 4/2012  | 3/2022<br>(-)<br>[3/2022]   | 540.02<br>(540.02)<br>[540.02]       | 168.97<br>(0.00)<br>[0]        |
| <b>Road Transport And Highways</b> |                                                                                                            |         |                             |                                      |                                |
| 668                                | 4 LANING OF AMRAVATI - CHIKHLI (PKG-I)                                                                     | 7/2015  | 5/2019<br>(-)<br>[5/2019]   | 2,288.18<br>(-)<br>[2,288.18]        | 0.00<br>(0.00)<br>[0]          |
| 669                                | 4 LANING OF FAGNE - MAH-GUJ BORDER ( PKG-3)                                                                | 7/2015  | 5/2019<br>(-)<br>[5/2019]   | 1,885.74<br>(-)<br>[1,885.74]        | 1,622.44<br>(0.00)<br>[0]      |
| 670                                | 4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211                                                              | 1/2015  | 7/2017<br>(-)<br>[12/2018]  | 972.50<br>(-)<br>[972.50]            | 1,484.99<br>(0.00)<br>[17]     |
| 671                                | 4-LANING FROM AURANGABAD TO KARODI (KM 290.200<br>TO 320.104)                                              | 1/2018  | /<br>(-)<br>[0/0]           | 607.00<br>(-)<br>[607.00]            | 0.00<br>(0.00)<br>[0]          |
| 672                                | 4-LANING FROM KARODI TO TELWADI (KM 320.104 TO<br>375.000)                                                 | 1/2018  | /<br>(-)<br>[0/0]           | 621.00<br>(-)<br>[621.00]            | 0.00<br>(0.00)<br>[0]          |

|     |                                                                                                       |         |                            |                               |                           |
|-----|-------------------------------------------------------------------------------------------------------|---------|----------------------------|-------------------------------|---------------------------|
| 673 | 4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION                                                   | 6/2014  | 11/2016<br>(-)<br>[6/2019] | 923.04<br>(-)<br>[923.04]     | 650.92<br>(0.00)<br>[31]  |
| 674 | 4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)                                              | 3/2017  | 3/2020<br>(-)<br>[3/2020]  | 744.64<br>(-)<br>[982.00]     | 0.00<br>(237.36)<br>[0]   |
| 675 | 4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)                                                  | 11/2016 | /<br>(-)<br>[0/0]          | 1,071.61<br>(-)<br>[1,071.61] | 0.00<br>(0.00)<br>[0]     |
| 676 | 4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT  | 11/2016 | 3/2019<br>(-)<br>[11/2019] | 446.17<br>(-)<br>[446.17]     | 2.42<br>(0.00)<br>[8]     |
| 677 | 4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)                                         | 3/2017  | 3/2020<br>(-)<br>[8/2020]  | 1,098.06<br>(-)<br>[1,160.64] | 413.75<br>(62.58)<br>[5]  |
| 678 | 4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE               | 3/2016  | /<br>(-)<br>[0/0]          | 1,142.62<br>(-)<br>[1,142.62] | 0.00<br>(0.00)<br>[0]     |
| 679 | 4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE               | 3/2016  | /<br>(-)<br>[0/0]          | 1,101.58<br>(-)<br>[1,101.58] | 0.00<br>(0.00)<br>[0]     |
| 680 | 4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI  | 11/2016 | 3/2019<br>(-)<br>[9/2019]  | 400.25<br>(-)<br>[400.25]     | 38.57<br>(0.00)<br>[6]    |
| 681 | 4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)                                                     | 11/2016 | /<br>(-)<br>[0/0]          | 1,064.88<br>(-)<br>[1,064.88] | 0.00<br>(0.00)<br>[0]     |
| 682 | 4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)                                         | 3/2017  | 3/2017<br>(-)<br>[11/2020] | 1,059.73<br>(-)<br>[1,071.00] | 152.79<br>(11.27)<br>[44] |
| 683 | 4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)                                          | 3/2017  | 3/2020<br>(-)<br>[5/2020]  | 1,030.44<br>(-)<br>[1,065.51] | 355.02<br>(35.07)<br>[2]  |
| 684 | 4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)                                           | 3/2017  | 3/2020<br>(-)<br>[8/2020]  | 988.34<br>(-)<br>[1,043.28]   | 451.51<br>(54.94)<br>[5]  |
| 685 | 6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3                     | 8/2015  | 5/2018<br>(-)<br>[4/2019]  | 505.00<br>(-)<br>[505.00]     | 194.09<br>(0.00)<br>[11]  |
| 686 | BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62            | 3/2016  | 7/2018<br>(-)<br>[7/2018]  | 197.69<br>(-)<br>[197.69]     | 0.60<br>(0.00)<br>[0]     |
| 687 | BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60             | 3/2016  | 7/2018<br>(-)<br>[0/0]     | 244.00<br>(-)<br>[244.00]     | 0.00<br>(0.00)<br>[0]     |
| 688 | CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF | 3/2018  | /<br>(-)<br>[0/0]          | 1,162.92<br>(-)<br>[1,162.92] | 0.00<br>(0.00)<br>[0]     |
| 689 | CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN  | 12/2015 | 3/2019<br>(-)<br>[3/2019]  | 649.50<br>(-)<br>[649.50]     | 86.54<br>(0.00)<br>[0]    |
| 690 | CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6)                                           | 3/2018  | /<br>(-)<br>[0/0]          | 291.53<br>(-)<br>[291.53]     | 0.00<br>(0.00)<br>[0]     |
| 691 | CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDELLAGANJ ROAD IN THE ST  | 1/2017  | 5/2019<br>(-)<br>[5/2019]  | 244.90<br>(-)<br>[244.90]     | 82.41<br>(0.00)<br>[0]    |
| 692 | CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6)                                            | 3/2018  | /<br>(-)<br>[0/0]          | 289.21<br>(-)<br>[289.21]     | 0.00<br>(0.00)<br>[0]     |
| 693 | CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM                                                           | 10/2015 | 5/2018                     | 593.26                        | 45.11                     |

|     |                                                                                                      |         |                 |                 |                |
|-----|------------------------------------------------------------------------------------------------------|---------|-----------------|-----------------|----------------|
|     | 14.740 TO KM 15.894 ( OLD SH -54) PKG-2                                                              |         | (-)<br>[4/2019] | (-)<br>[593.26] | (0.00)<br>[11] |
| 694 | CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION | 12/2011 | /               | 156.26          | 65.16          |
|     |                                                                                                      |         | (-)             | (227.00)        | (0.00)         |
|     |                                                                                                      |         | [0/0]           | [156.26]        | [0]            |
| 695 | CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA | 3/2011  | /               | 185.82          | 205.97         |
|     |                                                                                                      |         | (-)             | (292.00)        | (0.00)         |
|     |                                                                                                      |         | [0/0]           | [185.82]        | [0]            |
| 696 | CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (   | 10/2015 | 5/2018          | 531.13          | 163.10         |
|     |                                                                                                      |         | (-)             | (-)             | (0.00)         |
|     |                                                                                                      |         | [5/2019]        | [531.13]        | [12]           |
| 697 | CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)         | 3/2015  | /               | 168.30          | 13.43          |
|     |                                                                                                      |         | (-)             | (-)             | (0.00)         |
|     |                                                                                                      |         | [0/0]           | [168.30]        | [0]            |
| 698 | CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO | 8/2014  | 7/2016          | 187.79          | 57.60          |
|     |                                                                                                      |         | (-)             | (-)             | (0.00)         |
|     |                                                                                                      |         | [0/0]           | [187.79]        | [0]            |
| 699 | CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST | 3/2017  | 3/2020          | 247.02          | 0.00           |
|     |                                                                                                      |         | (-)             | (-)             | (-89.53)       |
|     |                                                                                                      |         | [3/2020]        | [157.49]        | [0]            |
| 700 | CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270( D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 ( D | 9/2015  | 5/2018          | 414.51          | 230.34         |
|     |                                                                                                      |         | (-)             | (-)             | (-0.51)        |
|     |                                                                                                      |         | [3/2019]        | [414.00]        | [10]           |
| 701 | DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000)     | 3/2017  | 3/2020          | 296.19          | 97.80          |
|     |                                                                                                      |         | (-)             | (-)             | (-42.19)       |
|     |                                                                                                      |         | [5/2019]        | [254.00]        | [-10]          |
| 702 | FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS                  | 4/2010  | 6/2012          | 1,170.52        | 2,042.41       |
|     |                                                                                                      |         | (-)             | (-)             | (0.00)         |
|     |                                                                                                      |         | [12/2018]       | [1,170.52]      | [78]           |
| 703 | FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 | 3/2018  | /               | 642.13          | 0.00           |
|     |                                                                                                      |         | (-)             | (-)             | (0.00)         |
|     |                                                                                                      |         | [0/0]           | [642.13]        | [0]            |
| 704 | FOUR LANING OF AURANGABAD - YEDISHI                                                                  | 7/2015  | 1/2018          | 1,871.34        | 2,304.41       |
|     |                                                                                                      |         | (-)             | (-)             | (0.00)         |
|     |                                                                                                      |         | [12/2018]       | [1,871.34]      | [11]           |
| 705 | FOUR LANNING OF TULJAPUR-AUSA SECTION                                                                | 2/2017  | 2/2020          | 904.16          | 155.12         |
|     |                                                                                                      |         | (-)             | (-)             | (0.00)         |
|     |                                                                                                      |         | [5/2020]        | [904.16]        | [3]            |
| 706 | NAGPUR - KONDHALI                                                                                    | 9/2005  | 6/2006          | 168.00          | 226.24         |
|     |                                                                                                      |         | (-)             | (-)             | (0.00)         |
|     |                                                                                                      |         | [0/0]           | [168.00]        | [0]            |
| 707 | NAGPUR RING ROAD PACKAGE-1                                                                           | 3/2016  | 7/2019          | 546.00          | 460.55         |
|     |                                                                                                      |         | (-)             | (-)             | (0.00)         |
|     |                                                                                                      |         | [7/2019]        | [546.00]        | [0]            |
| 708 | NAGPUR RING ROAD PACKAGE-2                                                                           | 3/2016  | 7/2019          | 591.66          | 608.89         |
|     |                                                                                                      |         | (-)             | (-)             | (0.00)         |
|     |                                                                                                      |         | [7/2019]        | [591.66]        | [0]            |
| 709 | PANVEL-INDAPUR                                                                                       | 12/2011 | 6/2014          | 942.69          | 668.59         |
|     |                                                                                                      |         | (-)             | (-)             | (0.00)         |
|     |                                                                                                      |         | [6/2019]        | [942.69]        | [60]           |
| 710 | PUNE-SATARA(NH-4)                                                                                    | 10/2010 | 3/2013          | 1,724.55        | 2,253.40       |
|     |                                                                                                      |         | (-)             | (-)             | (0.00)         |
|     |                                                                                                      |         | [6/2019]        | [1,724.55]      | [75]           |
| 711 | REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00                                | 12/2013 | 11/2016         | 220.72          | 95.02          |
|     |                                                                                                      |         | (-)             | (-)             | (0.00)         |
|     |                                                                                                      |         | [0/0]           | [220.72]        | [0]            |
| 712 | REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337                                       | 6/2014  | 11/2016         | 260.39          | 87.43          |
|     |                                                                                                      |         | (-)             | (-)             | (0.00)         |
|     |                                                                                                      |         | [0/0]           | [260.39]        | [0]            |
| 713 | REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00                                 | 1/2014  | /               | 446.77          | 87.62          |
|     |                                                                                                      |         | (-)             | (-)             | (0.00)         |

|     |                                                                                                      |         |                                  |                                      |                                 |
|-----|------------------------------------------------------------------------------------------------------|---------|----------------------------------|--------------------------------------|---------------------------------|
|     |                                                                                                      |         | [0/0]                            | [446.77]                             | [0]                             |
| 714 | REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO | 1/2014  | 11/2014<br>(-)<br>[0/0]          | 292.98<br>(-)<br>[292.98]            | 95.60<br>(0.00)<br>[0]          |
| 715 | REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM | 1/2015  | /<br>(-)<br>[0/0]                | 225.81<br>(-)<br>[225.81]            | 6.50<br>(0.00)<br>[0]           |
| 716 | SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH | 12/2017 | /<br>(-)<br>[0/0]                | 404.94<br>(-)<br>[404.94]            | 0.00<br>(0.00)<br>[0]           |
| 717 | SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE | 11/2016 | /<br>(-)<br>[5/2019]             | 290.73<br>(-)<br>[290.73]            | 57.93<br>(0.00)<br>[-]          |
| 718 | WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16  | 10/2015 | /<br>(-)<br>[0/0]                | 289.60<br>(-)<br>[289.60]            | 0.00<br>(0.00)<br>[0]           |
| 719 | WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50                                      | 5/2013  | 2/2014<br>(-)<br>[6/2019]        | 1,348.20<br>(-)<br>[1,348.20]        | 1,792.90<br>(0.00)<br>[64]      |
|     | <u>Shipping And Ports</u>                                                                            |         |                                  |                                      |                                 |
| 720 | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB | 1/2007  | 12/2010<br>(-)<br>[12/2018]      | 366.39<br>(669.46)<br>[669.46]       | 413.91<br>(303.07)<br>[96]      |
|     | <u>Telecommunications</u>                                                                            |         |                                  |                                      |                                 |
| 721 | MADHYA PRADESH ACCESS (LOT1)                                                                         | 8/2017  | 5/2018<br>(2/2019)<br>[2/2019]   | 215.30<br>(214.10)<br>[214.10]       | 33.46<br>(-1.20)<br>[9]         |
| 722 | MAHARASHTRA CORE (LOT1)                                                                              | 8/2017  | 4/2018<br>(2/2019)<br>[2/2019]   | 167.68<br>(-)<br>[167.68]            | 32.44<br>(0.00)<br>[10]         |
| 723 | MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT                                                     | 1/2018  | 10/2018<br>(2/2019)<br>[2/2019]  | 231.80<br>(231.80)<br>[231.80]       | 77.65<br>(0.00)<br>[4]          |
|     | <u>Urban Development</u>                                                                             |         |                                  |                                      |                                 |
| 724 | CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI                                      | 1/2018  | 7/2020<br>(9/2018)<br>[9/2020]   | 223.37<br>(-)<br>[223.37]            | 4.00<br>(0.00)<br>[2]           |
| 725 | MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)                                                            | 7/2013  | 1/2015<br>(-)<br>[5/2020]        | 23,136.00<br>(-)<br>[23,136.00]      | 0.00<br>(0.00)<br>[64]          |
| 726 | NAGPUR METRO RAIL                                                                                    | 8/2014  | 3/2018<br>(12/2019)<br>[12/2019] | 8,680.00<br>(8,680.00)<br>[8,680.00] | 4,787.71<br>(0.00)<br>[21]      |
| 727 | PUNE METRO RAIL PROJECT (PHASE 1)                                                                    | 12/2016 | 11/2021<br>(-)<br>[11/2021]      | 11,420.00<br>(-)<br>[11,420.00]      | 1,938.17<br>(0.00)<br>[0]       |
|     | <u>MANIPUR</u>                                                                                       |         |                                  |                                      |                                 |
|     | <u>Railways</u>                                                                                      |         |                                  |                                      |                                 |
| 728 | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)                                                                  | 4/2003  | 3/2011<br>(-)<br>[3/2020]        | 4,454.17<br>(-)<br>[13,809.00]       | 8,304.86<br>(9,354.83)<br>[108] |
|     | <u>Urban Development</u>                                                                             |         |                                  |                                      |                                 |
| 729 | NIT ACADEMIC BUILDING AT IMPHAL MANIPUR                                                              | 2/2014  | 3/2015<br>(-)<br>[11/2019]       | 216.69<br>(-)<br>[216.69]            | 52.00<br>(0.00)<br>[56]         |
|     | <u>MEGHALAYA</u>                                                                                     |         |                                  |                                      |                                 |
|     | <u>Health And Family Welfare</u>                                                                     |         |                                  |                                      |                                 |
| 730 | NEIGRIHMS SHILLONG MEGHALYA                                                                          | 10/2016 | 5/2018<br>(9/2019)<br>[8/2019]   | 363.99<br>(-)<br>[363.99]            | 112.29<br>(0.00)<br>[15]        |
|     | <u>Railways</u>                                                                                      |         |                                  |                                      |                                 |

|     |                                                                                                      |         |                                  |                                      |                                |
|-----|------------------------------------------------------------------------------------------------------|---------|----------------------------------|--------------------------------------|--------------------------------|
| 731 | NEW BG LINE FROM BYRNIHAT TO SHILLONG                                                                | 4/2010  | 3/2021<br>(-)<br>[3/2021]        | 906.46<br>(1,202.33)<br>[6,000.00]   | 259.95<br>(5,093.54)<br>[0]    |
|     | <u>Road Transport And Highways</u>                                                                   |         |                                  |                                      |                                |
| 732 | 2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA    | 12/2010 | 2/2011<br>(-)<br>[0/0]           | 1,494.48<br>(-)<br>[1,494.48]        | 0.00<br>(0.00)<br>[0]          |
| 733 | JORBAT - BARAPANI                                                                                    | 1/2011  | 1/2014<br>(-)<br>[1/2019]        | 536.00<br>(-)<br>[536.00]            | 837.81<br>(0.00)<br>[60]       |
| 734 | TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44                                 | 12/2015 | 5/2018<br>(-)<br>[3/2019]        | 479.20<br>(-)<br>[479.20]            | 14.31<br>(0.00)<br>[10]        |
| 735 | WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T | 4/2017  | /<br>(-)<br>[0/0]                | 553.51<br>(-)<br>[553.51]            | 159.00<br>(0.00)<br>[0]        |
|     | <u>Urban Development</u>                                                                             |         |                                  |                                      |                                |
| 736 | CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR | 4/2014  | 9/2017<br>(-)<br>[12/2018]       | 151.33<br>(-)<br>[151.33]            | 7.15<br>(0.00)<br>[15]         |
|     | <u>MIZORAM</u>                                                                                       |         |                                  |                                      |                                |
|     | <u>Railways</u>                                                                                      |         |                                  |                                      |                                |
| 737 | BHAIRABI SAIRONG, NL, NEFR                                                                           | 4/2008  | 3/2014<br>(12/2020)<br>[12/2020] | 2,393.47<br>(2,393.48)<br>[4,968.00] | 2,516.15<br>(2,574.53)<br>[81] |
|     | <u>Road Transport And Highways</u>                                                                   |         |                                  |                                      |                                |
| 738 | CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)                          | 8/2010  | 10/2010<br>(-)<br>[0/0]          | 195.04<br>(-)<br>[195.04]            | 130.82<br>(0.00)<br>[0]        |
| 739 | CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD  | 8/2010  | 10/2010<br>(-)<br>[0/0]          | 193.69<br>(-)<br>[193.69]            | 0.00<br>(0.00)<br>[0]          |
| 740 | WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN  | 11/2010 | 3/2011<br>(-)<br>[0/0]           | 624.41<br>(-)<br>[624.41]            | 0.00<br>(0.00)<br>[0]          |
|     | <u>MULTI STATE</u>                                                                                   |         |                                  |                                      |                                |
|     | <u>Coal</u>                                                                                          |         |                                  |                                      |                                |
| 741 | DHANKASA UG (1.00 MTY)                                                                               | 9/2016  | 3/2022<br>(-)<br>[3/2022]        | 458.07<br>(-)<br>[458.07]            | 16.00<br>(0.00)<br>[0]         |
| 742 | DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)                                                               | 2/2017  | 3/2021<br>(-)<br>[3/2021]        | 328.00<br>(-)<br>[328.00]            | 90.65<br>(0.00)<br>[0]         |
| 743 | NILJAI EXPANSION (DEEP) OC (3.5 MTY)                                                                 | 8/2016  | 3/2022<br>(-)<br>[3/2022]        | 319.76<br>(-)<br>[319.76]            | 58.04<br>(0.00)<br>[0]         |
|     | <u>Heavy Industry</u>                                                                                |         |                                  |                                      |                                |
| 744 | NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)                                  | 4/2011  | 9/2011<br>(6/2019)<br>[6/2019]   | 1,718.00<br>(3,727.30)<br>[3,827.30] | 2,933.23<br>(2,109.30)<br>[93] |
|     | <u>Petroleum</u>                                                                                     |         |                                  |                                      |                                |
| 745 | 50MW WIND ENERGY POWER PROJECT                                                                       | 11/2015 | 6/2017<br>(-)<br>[0/0]           | 500.00<br>(-)<br>[500.00]            | 0.00<br>(0.00)<br>[0]          |
| 746 | AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR    | 1/2015  | 12/2020<br>(-)<br>[12/2020]      | 1,823.00<br>(-)<br>[1,823.00]        | 579.41<br>(0.00)<br>[0]        |
| 747 | AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II                               | 9/2016  | 12/2019<br>(-)<br>[12/2019]      | 571.66<br>(-)<br>[571.66]            | 42.33<br>(0.00)<br>[0]         |
| 748 | BARAUNI-GUWAHATI PIPELINE                                                                            | 6/2018  | 12/2021                          | 3,308.00                             | 2.63                           |



|     |                                                                                                      |         |                                   |                                      |                              |
|-----|------------------------------------------------------------------------------------------------------|---------|-----------------------------------|--------------------------------------|------------------------------|
|     |                                                                                                      |         | (-)<br>[12/2021]                  | (-)<br>[3,308.00]                    | (0.00)<br>[0]                |
| 749 | BOKARO-ANGUL PIPELINE PROJECT                                                                        | 3/2017  | 12/2020<br>(-)<br>[12/2020]       | 3,437.00<br>(-)<br>[3,437.00]        | 1,006.30<br>(0.00)<br>[0]    |
| 750 | CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)                                                      | 6/2007  | 9/2011<br>(-)<br>[0/0]            | 736.65<br>(-)<br>[571.47]            | 543.05<br>(-165.18)<br>[0]   |
| 751 | DOBHI-DURGAPUR PIPELINE PROJECT                                                                      | 3/2017  | 12/2020<br>(-)<br>[12/2020]       | 2,433.00<br>(-)<br>[2,433.00]        | 956.29<br>(0.00)<br>[0]      |
| 752 | EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST | 9/2017  | 3/2021<br>(-)<br>[3/2021]         | 2,677.00<br>(-)<br>[2,677.00]        | 49.88<br>(0.00)<br>[0]       |
| 753 | JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE           | 2/2015  | 10/2019<br>(-)<br>[3/2019]        | 890.00<br>(-)<br>[887.00]            | 551.16<br>(-3.00)<br>[-7]    |
| 754 | KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II                                                | 6/2009  | 12/2012<br>(2/2019)<br>[6/2019]   | 2,915.00<br>(3,030.00)<br>[2,915.00] | 2,009.30<br>(0.00)<br>[78]   |
| 755 | LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT             | 7/2015  | 12/2019<br>(12/2020)<br>[12/2019] | 2,881.40<br>(-)<br>[2,000.00]        | 1,090.43<br>(-881.40)<br>[0] |
| 756 | MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION                                     | 9/2016  | 6/2020<br>(-)<br>[6/2020]         | 1,879.00<br>(-)<br>[1,879.00]        | 1,015.35<br>(0.00)<br>[0]    |
| 757 | PARADIP HYDERABAD PIPELINE                                                                           | 1/2015  | 12/2020<br>(-)<br>[8/2020]        | 2,321.00<br>(3,338.00)<br>[3,338.00] | 941.59<br>(1,017.00)<br>[-4] |
| 758 | PARADIP LPG IMPORT FACILITY                                                                          | 1/2015  | 7/2018<br>(10/2020)<br>[10/2020]  | 690.00<br>(-)<br>[690.00]            | 191.48<br>(0.00)<br>[27]     |
| 759 | PARADIP-RAIPUR- RANCHI PIPELINE                                                                      | 8/2009  | 12/2016<br>(-)<br>[0/0]           | 1,793.00<br>(-)<br>[1,793.00]        | 1,788.86<br>(0.00)<br>[0]    |
| 760 | PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I                                                              | 3/2015  | 12/2018<br>(-)<br>[3/2019]        | 3,957.00<br>(3,561.00)<br>[3,397.00] | 2,382.96<br>(-560.00)<br>[3] |
| 761 | PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)                                                  | 5/2016  | 10/2020<br>(-)<br>[10/2020]       | 406.00<br>(-)<br>[406.00]            | 23.61<br>(0.00)<br>[0]       |
| 762 | RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA)                          | 11/2016 | 2/2019<br>(-)<br>[2/2019]         | 230.00<br>(-)<br>[230.00]            | 114.14<br>(0.00)<br>[0]      |
| 763 | SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN               | 7/2011  | 3/2017<br>(6/2019)<br>[6/2019]    | 352.56<br>(-)<br>[438.84]            | 196.39<br>(86.28)<br>[27]    |
| 764 | URAN CHAKAN SHIKRAPUR LPG PIPELINE                                                                   | 12/2009 | 10/2014<br>(2/2019)<br>[2/2019]   | 309.81<br>(723.40)<br>[723.40]       | 586.10<br>(413.59)<br>[52]   |
|     | <u>Power</u>                                                                                         |         |                                   |                                      |                              |
| 765 | 400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION)                          | 9/2017  | 9/2019<br>(2/2020)<br>[2/2020]    | 198.49<br>(198.49)<br>[198.49]       | 15.70<br>(0.00)<br>[5]       |
| 766 | 400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV)                                             | 8/2008  | 2/2013<br>(7/2018)<br>[12/2018]   | 771.00<br>(1,624.00)<br>[1,624.00]   | 1,577.20<br>(853.00)<br>[70] |
| 767 | AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B                                             | 3/2014  | 3/2016<br>(9/2018)<br>[2/2019]    | 155.57<br>(206.42)<br>[206.42]       | 145.82<br>(50.85)<br>[35]    |
| 768 | COMMON SYS. ASSOCIATED WITH EAST COAST                                                               | 3/2013  | 12/2015                           | 2,514.88                             | 2,281.28                     |

|     |                                                                                                             |         |                                   |                                         |                                  |
|-----|-------------------------------------------------------------------------------------------------------------|---------|-----------------------------------|-----------------------------------------|----------------------------------|
|     | ENERGY PVT LTD AND NCC POWER PROJECTS LTD<br>LTOA GEN PART- B                                               |         | (-)<br>[0/0]                      | (-)<br>[3,190.27]                       | (675.39)<br>[0]                  |
| 769 | COMPREHENSIVE SCHEME FOR THE STRENGTHENING<br>OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN<br>A P         | 12/2014 | 12/2018<br>(12/2018)<br>[12/2019] | 4,754.42<br>(4,754.42)<br>[9,141.97]    | 993.85<br>(4,387.55)<br>[12]     |
| 770 | EASTERN REGION STRENGTHENING SCHEME XX                                                                      | 11/2017 | 5/2020<br>(5/2020)<br>[5/2020]    | 358.83<br>(358.83)<br>[358.83]          | 0.00<br>(0.00)<br>[0]            |
| 771 | EASTERN REGION STRENGTHENING SCHEME -IX                                                                     | 2/2014  | 2/2016<br>(9/2018)<br>[3/2019]    | 196.58<br>(225.28)<br>[225.28]          | 151.02<br>(28.70)<br>[37]        |
| 772 | EASTERN REGION STRENGTHENING SCHEME XI                                                                      | 5/2016  | 11/2018<br>(11/2018)<br>[2/2019]  | 766.21<br>(766.21)<br>[766.21]          | 454.34<br>(0.00)<br>[3]          |
| 773 | EASTERN REGION STRENGTHENING SCHEME-V                                                                       | 10/2013 | 4/2016<br>(12/2018)<br>[2/2019]   | 1,364.52<br>(1,891.41)<br>[1,891.41]    | 1,216.98<br>(526.89)<br>[34]     |
| 774 | EASTERN REGION STRENGTHENING SCHEME-XII                                                                     | 5/2014  | 11/2016<br>(6/2019)<br>[6/2019]   | 522.29<br>(55,018.00)<br>[550.18]       | 445.93<br>(27.89)<br>[31]        |
| 775 | EASTERN REGION STRENGTHENING SCHEME-XVIII                                                                   | 3/2017  | 7/2020<br>(-)<br>[7/2020]         | 3,500.00<br>(3,500.00)<br>[3,500.00]    | 690.00<br>(0.00)<br>[0]          |
| 776 | EASTERN REGION STRENGTHENING SCHEME XVII( PART<br>B)                                                        | 2/2017  | 6/2019<br>(6/2019)<br>[6/2019]    | 235.53<br>(235.53)<br>[235.53]          | 42.49<br>(0.00)<br>[0]           |
| 777 | ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH<br>ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS<br>TO 400/  | 2/2017  | 2/2019<br>(2/2019)<br>[2/2019]    | 322.30<br>(322.30)<br>[322.30]          | 119.48<br>(0.00)<br>[0]          |
| 778 | ESTABLISHMENT OF FIBER OPTIC COMMUNICATION<br>SYSTEM IN NR UNDER FIBER OPTIC EXPANSION<br>PROJECT (ADDITIO  | 3/2015  | 3/2018<br>(-)<br>[3/2019]         | 197.40<br>(197.40)<br>[197.40]          | 74.71<br>(0.00)<br>[12]          |
| 779 | GREEN ENERGY CORRIDORS - INTER STATE<br>TRANSMISSION SCHEME PART-D                                          | 5/2016  | 5/2019<br>(5/2019)<br>[5/2019]    | 3,519.59<br>(3,519.59)<br>[3,519.59]    | 2,073.40<br>(0.00)<br>[0]        |
| 780 | GREEN ENERGY CORRIDORS INTER-STATE<br>TRANSMISSION SCHEME -PART B                                           | 4/2015  | 4/2018<br>(9/2018)<br>[2/2019]    | 3,705.61<br>(3,705.61)<br>[3,705.61]    | 2,549.30<br>(0.00)<br>[10]       |
| 781 | HVDC BIPOLE LINK BETWEEN WESTERN REGION<br>(RAIGARH, CHATTISGARH) AND SOUTHERN REGION<br>(PUGALAR, TM) NOR  | 2/2017  | 4/2020<br>(4/2020)<br>[4/2020]    | 5,070.13<br>(5,070.13)<br>[5,070.13]    | 1,044.71<br>(0.00)<br>[0]        |
| 782 | HVDC BIPOLE LINK BETWEEN WR (RAIGARH,<br>CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-<br>SCHEME-I: RAIGARH-P | 5/2016  | 11/2019<br>(11/2019)<br>[11/2019] | 14,733.37<br>(14,733.37)<br>[14,733.37] | 5,084.05<br>(0.00)<br>[0]        |
| 783 | HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH<br>TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT<br>PUGALUR EN  | 8/2017  | 2/2020<br>(2/2020)<br>[2/2020]    | 1,931.39<br>(1,931.39)<br>[1,931.39]    | 592.69<br>(0.00)<br>[0]          |
| 784 | INSTALLATION OF BUS REACTORS AT CUDDAPAH<br>NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB<br>STATION            | 3/2017  | 6/2019<br>(6/2019)<br>[6/2019]    | 251.60<br>(251.60)<br>[251.60]          | 112.11<br>(0.00)<br>[0]          |
| 785 | NORTH EASTERN REGION POWER SYSTEM<br>IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES                       | 12/2014 | 12/2018<br>(12/2018)<br>[12/2019] | 5,111.33<br>(5,111.33)<br>[6,652.57]    | 922.25<br>(1,541.24)<br>[12]     |
| 786 | NORTH- EAST NORTH WESTERN INTERCONNECTOR I<br>PROJECT                                                       | 2/2009  | 8/2013<br>(3/2022)<br>[3/2022]    | 11,130.19<br>(13,762.80)<br>[13,762.80] | 12,723.70<br>(2,632.61)<br>[103] |
| 787 | NORTHERN REGION SYSTEM STRENGTHENING SCHEME<br>- XXX                                                        | 2/2014  | 6/2016<br>(9/2018)<br>[3/2019]    | 539.82<br>(539.82)<br>[539.82]          | 423.73<br>(0.00)<br>[33]         |
| 788 | PG WORK ASSOCIATED WITH TBCB LINES UNDER<br>COMMON TRANSMISSION SYSTEM FOR PH -II GEN.                      | 3/2017  | 3/2019<br>(3/2019)                | 162.31<br>(162.31)                      | 86.70<br>(0.00)                  |

|     |                                                                                                      |         |                                   |                                      |                              |
|-----|------------------------------------------------------------------------------------------------------|---------|-----------------------------------|--------------------------------------|------------------------------|
|     | PROJ. IN ODHISHA                                                                                     |         | [3/2019]                          | [162.31]                             | [0]                          |
| 789 | POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN | 7/2016  | 3/2019<br>(3/2019)<br>[3/2019]    | 333.17<br>(333.17)<br>[333.17]       | 257.53<br>(0.00)<br>[0]      |
| 790 | PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION                                     | 8/2016  | 2/2019<br>(2/2019)<br>[2/2019]    | 431.89<br>(431.89)<br>[431.89]       | 213.66<br>(0.00)<br>[0]      |
| 791 | S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO | 3/2017  | 11/2019<br>(11/2019)<br>[11/2019] | 283.72<br>(283.72)<br>[283.72]       | 109.75<br>(0.00)<br>[0]      |
| 792 | SOUTHERN REGION STRENGTHENING SCHEME-XXI                                                             | 9/2016  | 3/2019<br>(3/2019)<br>[3/2019]    | 562.25<br>(562.25)<br>[562.25]       | 103.00<br>(0.00)<br>[0]      |
| 793 | STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI                                                 | 12/2015 | 4/2019<br>(-)<br>[4/2019]         | 3,654.00<br>(-)<br>[3,654.00]        | 2,873.42<br>(0.00)<br>[0]    |
| 794 | SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI                | 10/2016 | 4/2019<br>(4/2019)<br>[4/2019]    | 608.24<br>(608.24)<br>[608.24]       | 376.20<br>(0.00)<br>[0]      |
| 795 | SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII                                                      | 1/2015  | 7/2017<br>(6/2019)<br>[6/2019]    | 203.28<br>(260.03)<br>[260.03]       | 187.06<br>(56.75)<br>[23]    |
| 796 | SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII                                                   | 3/2017  | 12/2019<br>(12/2019)<br>[12/2019] | 379.95<br>(379.95)<br>[379.95]       | 22.22<br>(0.00)<br>[0]       |
| 797 | SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII                                               | 3/2017  | 6/2019<br>(6/2019)<br>[6/2019]    | 337.75<br>(337.75)<br>[337.75]       | 26.00<br>(0.00)<br>[0]       |
| 798 | SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION                                                         | 1/2016  | 7/2018<br>(-)<br>[0/0]            | 1,455.47<br>(-)<br>[1,455.47]        | 1,028.69<br>(0.00)<br>[0]    |
| 799 | SYTEM STRENGTHENING OF SOUTHERN REGION - XIV                                                         | 12/2011 | 8/2014<br>(9/2018)<br>[2/2019]    | 297.33<br>(534.02)<br>[534.02]       | 441.08<br>(236.69)<br>[54]   |
| 800 | SYTEM STRENGTHENING XIII OF SR GRID                                                                  | 10/2011 | 6/2014<br>(12/2018)<br>[3/2019]   | 487.49<br>(639.46)<br>[639.46]       | 509.60<br>(151.97)<br>[57]   |
| 801 | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT                                           | 10/2008 | 10/2012<br>(12/2018)<br>[6/2019]  | 4,824.12<br>(5,071.94)<br>[5,071.94] | 4,545.57<br>(247.82)<br>[80] |
| 802 | TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP                                                 | 1/2015  | 3/2018<br>(9/2018)<br>[2/2019]    | 268.80<br>(340.88)<br>[340.88]       | 241.30<br>(72.08)<br>[11]    |
| 803 | TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)                                   | 1/2015  | 10/2017<br>(9/2019)<br>[9/2019]   | 871.62<br>(871.62)<br>[871.62]       | 432.72<br>(0.00)<br>[23]     |
| 804 | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)    | 10/2016 | 1/2019<br>(1/2019)<br>[6/2019]    | 408.46<br>(408.46)<br>[408.46]       | 184.94<br>(0.00)<br>[5]      |
| 805 | TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH            | 6/2014  | 3/2018<br>(3/2019)<br>[6/2019]    | 5,151.37<br>(5,151.37)<br>[5,151.37] | 2,892.80<br>(0.00)<br>[15]   |
| 806 | TRANSMISSION SYSTEM STRENTHENNING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR | 3/2016  | 1/2018<br>(3/2019)<br>[9/2019]    | 808.63<br>(808.63)<br>[808.63]       | 348.56<br>(0.00)<br>[20]     |
| 807 | UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I                                                  | 1/2014  | 4/2016<br>(12/2017)<br>[3/2019]   | 374.63<br>(374.63)<br>[374.63]       | 187.24<br>(0.00)<br>[35]     |
| 808 | WESTERN REGION STRENGTENING SCHEME-XVI                                                               | 7/2016  | 7/2018<br>(7/2018)<br>[2/2019]    | 150.99<br>(150.99)<br>[150.99]       | 95.16<br>(0.00)<br>[7]       |

|     |                                                                                                      |         |                                   |                                     |                             |
|-----|------------------------------------------------------------------------------------------------------|---------|-----------------------------------|-------------------------------------|-----------------------------|
| 809 | WESTERN REGION STRENGTHENING SCHEME XVII                                                             | 2/2017  | 9/2019<br>(9/2019)<br>[3/2019]    | 204.12<br>(204.12)<br>[204.12]      | 102.17<br>(0.00)<br>[-6]    |
| 810 | WESTERN REGION STRENGTHENING SCHEME XVIII                                                            | 2/2017  | 2/2020<br>(2/2020)<br>[2/2020]    | 195.05<br>(195.05)<br>[195.05]      | 92.00<br>(0.00)<br>[0]      |
|     | <b>Railways</b>                                                                                      |         |                                   |                                     |                             |
| 811 | MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT                                                             | 12/2015 | 12/2023<br>(12/2023)<br>[12/2023] | 1,08,000.00<br>(-)<br>[1,08,000.00] | 1,057.80<br>(0.00)<br>[0]   |
| 812 | AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH                                          | 4/2010  | /<br>(-)<br>[0/0]                 | 338.54<br>(-)<br>[338.54]           | 212.64<br>(0.00)<br>[0]     |
| 813 | BANDEL-BOINCHI 3RD LINE                                                                              | 4/2011  | /<br>(-)<br>[0/0]                 | 288.35<br>(-)<br>[238.36]           | 291.43<br>(-49.99)<br>[0]   |
| 814 | BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT                                                 | 4/2007  | /<br>(-)<br>[0/0]                 | 450.55<br>(-)<br>[250.55]           | 19.82<br>(-200.00)<br>[0]   |
| 815 | BHADRACHALAM ROAD-SATTUPALLI                                                                         | 4/2010  | 3/2020<br>(-)<br>[3/2020]         | 704.31<br>(-)<br>[704.31]           | 119.69<br>(0.00)<br>[0]     |
| 816 | BHADRACHALAM-KOVVUR                                                                                  | 4/2012  | /<br>(-)<br>[0/0]                 | 923.23<br>(-)<br>[1,787.00]         | 2.46<br>(863.77)<br>[0]     |
| 817 | BOINCHI-SHAKTIGARH 3RD LINE                                                                          | 4/2011  | /<br>(-)<br>[0/0]                 | 175.80<br>(-)<br>[173.91]           | 153.48<br>(-1.89)<br>[0]    |
| 818 | CALICUT-MANGALORE (DL) (SR)                                                                          | 2/1996  | /<br>(-)<br>[0/0]                 | 240.00<br>(-)<br>[579.37]           | 537.30<br>(339.37)<br>[0]   |
| 819 | CHANDIGARH-BADDI                                                                                     | 4/2007  | 3/2023<br>(-)<br>[3/2023]         | 328.14<br>(-)<br>[1,540.00]         | 229.95<br>(1,211.86)<br>[0] |
| 820 | CHANDIGARH-BADDI NL                                                                                  | 4/2007  | /<br>(-)<br>[0/0]                 | 328.14<br>(-)<br>[1,540.00]         | 45.20<br>(1,211.86)<br>[0]  |
| 821 | CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA | 4/2003  | /<br>(-)<br>[0/0]                 | 337.96<br>(-)<br>[355.44]           | 72.84<br>(17.48)<br>[0]     |
| 822 | CHENNAI-CUDDALORE VIA MAMALLAPURAM                                                                   | 4/2008  | /<br>(-)<br>[0/0]                 | 523.52<br>(-)<br>[2,350.00]         | 2.27<br>(1,826.48)<br>[0]   |
| 823 | CHHAPRA-BALLIA UP                                                                                    | 3/2013  | 1/2019<br>(-)<br>[2/2019]         | 295.00<br>(-)<br>[477.31]           | 186.71<br>(182.31)<br>[1]   |
| 824 | CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP                                                       | 3/2007  | 12/2021<br>(-)<br>[12/2021]       | 243.78<br>(-)<br>[895.00]           | 99.33<br>(651.22)<br>[0]    |
| 825 | CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL                     | 4/2005  | 3/2017<br>(-)<br>[0/0]            | 595.51<br>(-)<br>[538.37]           | 109.04<br>(-57.14)<br>[0]   |
| 826 | CHOTTAUDEPUR-DHAR(NL)                                                                                | 4/2007  | 3/2022<br>(3/2019)<br>[3/2022]    | 1,347.26<br>(-)<br>[1,347.26]       | 606.41<br>(0.00)<br>[0]     |
| 827 | DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)                                                     | 4/2007  | 3/2022<br>(3/2019)<br>[3/2022]    | 1,640.04<br>(-)<br>[1,640.04]       | 603.75<br>(0.00)<br>[0]     |
| 828 | DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL   | 4/2010  | 3/2017<br>(-)<br>[0/0]            | 365.17<br>(-)<br>[296.43]           | 134.36<br>(-68.74)<br>[0]   |

|     |                                                                                               |         |           |             |             |
|-----|-----------------------------------------------------------------------------------------------|---------|-----------|-------------|-------------|
| 829 | DELHI-SOHNANUHIROZPUR-JHIRKA-ALWAR                                                            | 4/2013  | /         | 1,239.00    | 0.00        |
|     |                                                                                               |         | (-)       | (-)         | (0.00)      |
|     |                                                                                               |         | [0/0]     | [1,239.00]  | [0]         |
| 830 | DEOBAND (MUZAFFARNAGAR)- ROORKEE NL                                                           | 4/2007  | /         | 336.91      | 143.18      |
|     |                                                                                               |         | (-)       | (-)         | (0.00)      |
|     |                                                                                               |         | [0/0]     | [336.91]    | [0]         |
| 831 | DEOGHAR - SULTANGANJ (INL), ER                                                                | 4/2000  | 2/2013    | 607.09      | 634.08      |
|     |                                                                                               |         | (-)       | (-)         | (0.82)      |
|     |                                                                                               |         | [0/0]     | [607.91]    | [0]         |
| 832 | DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR | 4/2010  | /         | 2,030.50    | 10.34       |
|     |                                                                                               |         | (-)       | (-)         | (0.00)      |
|     |                                                                                               |         | [12/2022] | [2,030.50]  | [-]         |
| 833 | DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA                                                    | 4/2010  | 3/2015    | 651.00      | 7.96        |
|     |                                                                                               |         | (3/2024)  | (-)         | (358.00)    |
|     |                                                                                               |         | [3/2024]  | [1,009.00]  | [108]       |
| 834 | EASTERN DEDICATED FREIGHT CORRIDOR PROJECT                                                    | 10/2006 | /         | 11,589.00   | 0.00        |
|     |                                                                                               |         | (-)       | (30,357.00) | (16,592.00) |
|     |                                                                                               |         | [0/0]     | [28,181.00] | [0]         |
| 835 | GAYA-CHATRA (NL)                                                                              | 4/2008  | /         | 415.67      | 14.62       |
|     |                                                                                               |         | (-)       | (-)         | (134.08)    |
|     |                                                                                               |         | [0/0]     | [549.75]    | [0]         |
| 836 | GONDIA-JABALPUR(GC),(SECR)                                                                    | 2/1997  | 4/2020    | 511.86      | 967.96      |
|     |                                                                                               |         | (-)       | (-)         | (1,244.14)  |
|     |                                                                                               |         | [4/2020]  | [1,756.00]  | [0]         |
| 837 | GOOTY-DHARMAVARAM-BANGLORE                                                                    | 4/2015  | /         | 636.38      | 0.00        |
|     |                                                                                               |         | (-)       | (-)         | (0.00)      |
|     |                                                                                               |         | [0/0]     | [636.38]    | [0]         |
| 838 | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)                                             | 4/1986  | 3/1994    | 158.77      | 629.43      |
|     |                                                                                               |         | (-)       | (274.56)    | (475.71)    |
|     |                                                                                               |         | [0/0]     | [634.48]    | [0]         |
| 839 | GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)                                                | 4/2011  | 3/2022    | 2,912.96    | 1.92        |
|     |                                                                                               |         | (-)       | (-)         | (932.64)    |
|     |                                                                                               |         | [3/2022]  | [3,845.60]  | [0]         |
| 840 | HAJIPUR - BACHAWARA                                                                           | 5/2015  | 3/2019    | 678.54      | 0.00        |
|     |                                                                                               |         | (-)       | (-)         | (0.00)      |
|     |                                                                                               |         | [3/2020]  | [678.54]    | [12]        |
| 841 | HANSDIHA-GODDA NL                                                                             | 4/2011  | 3/2020    | 542.18      | 311.90      |
|     |                                                                                               |         | (-)       | (-)         | (0.00)      |
|     |                                                                                               |         | [3/2020]  | [542.18]    | [0]         |
| 842 | HANSNABAD-HINGALGANJ NEW BG LINE                                                              | 4/2010  | /         | 172.03      | 10.84       |
|     |                                                                                               |         | (-)       | (-)         | (88.07)     |
|     |                                                                                               |         | [0/0]     | [260.10]    | [0]         |
| 843 | HATHUA-BHATNI (N L) (NER)                                                                     | 4/2005  | 12/2022   | 230.03      | 274.67      |
|     |                                                                                               |         | (-)       | (-)         | (540.05)    |
|     |                                                                                               |         | [5/2019]  | [770.08]    | [-43]       |
| 844 | HOTGI-KUDGI-GADAG                                                                             | 3/2015  | 3/2019    | 1,614.59    | 732.88      |
|     |                                                                                               |         | (3/2021)  | (1,870.41)  | (255.82)    |
|     |                                                                                               |         | [3/2021]  | [1,870.41]  | [24]        |
| 845 | HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)                                    | 4/2010  | 11/2018   | 157.94      | 50.69       |
|     |                                                                                               |         | (-)       | (-)         | (0.00)      |
|     |                                                                                               |         | [0/0]     | [157.94]    | [0]         |
| 846 | HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES  | 4/2011  | /         | 166.89      | 246.00      |
|     |                                                                                               |         | (-)       | (-)         | (0.00)      |
|     |                                                                                               |         | [0/0]     | [166.89]    | [0]         |
| 847 | JAKHAL-MANSA DOUBLING ON SPR SECTION                                                          | 4/2008  | /         | 162.96      | 153.31      |
|     |                                                                                               |         | (-)       | (-)         | (0.00)      |
|     |                                                                                               |         | [0/0]     | [162.96]    | [0]         |
| 848 | JALANDHAR-PATHANKOT-JAMMU TAWI                                                                | 3/2002  | 3/2016    | 625.00      | 0.00        |
|     |                                                                                               |         | (-)       | (-)         | (220.58)    |
|     |                                                                                               |         | [0/0]     | [845.58]    | [0]         |
| 849 | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR                                                        | 3/2002  | 6/2007    | 625.30      | 841.57      |

|     |                                                                                                             |        |                               |                                      |                                |
|-----|-------------------------------------------------------------------------------------------------------------|--------|-------------------------------|--------------------------------------|--------------------------------|
|     |                                                                                                             |        | (-)<br>[0/0]                  | (408.76)<br>[876.10]                 | (250.80)<br>[0]                |
| 850 | KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I                                                              | 4/2008 | 3/2014<br>(-)<br>[3/2023]     | 2,132.77<br>(-)<br>[2,132.77]        | 216.07<br>(0.00)<br>[108]      |
| 851 | KALINARAYANPUR-KRISHNANAGAR DOUBLING<br>ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND<br>NAIHATI-RANAGHAT 3  | 4/2001 | 3/2016<br>(-)<br>[0/0]        | 923.52<br>(-)<br>[792.27]            | 336.43<br>(-131.25)<br>[0]     |
| 852 | KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW<br>MM FOR RANAGHAT-DUTTAPHULIA NEW LINE                          | 4/2010 | /<br>(-)<br>[0/0]             | 174.56<br>(-)<br>[175.99]            | 57.52<br>(1.43)<br>[0]         |
| 853 | KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)                                                                     | 4/1999 | /<br>(-)<br>[0/0]             | 744.71<br>(-)<br>[1,126.79]          | 751.05<br>(382.08)<br>[0]      |
| 854 | KAZIPET-BALHRSHA                                                                                            | 4/2015 | 3/2021<br>(-)<br>[3/2021]     | 2,063.03<br>(-)<br>[2,063.03]        | 368.22<br>(0.00)<br>[0]        |
| 855 | KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION                                                            | 4/2012 | 3/2023<br>(-)<br>[3/2024]     | 1,856.95<br>(-)<br>[2,200.00]        | 227.19<br>(343.05)<br>[12]     |
| 856 | KURUPPANTHARA-CHINGAVANAM                                                                                   | 4/2007 | /<br>(-)<br>[0/0]             | 270.14<br>(-)<br>[457.08]            | 317.14<br>(186.94)<br>[0]      |
| 857 | LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM<br>FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-<br>BUDAKHALI AND CHANDRANAG | 4/1987 | 3/2006<br>(-)<br>[0/0]        | 406.99<br>(-)<br>[544.72]            | 147.26<br>(137.73)<br>[0]      |
| 858 | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)                                                                      | 9/1998 | 5/2008<br>(-)<br>[3/2023]     | 247.66<br>(-)<br>[6,093.31]          | 972.82<br>(5,845.65)<br>[178]  |
| 859 | LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-<br>JONGALPARA-FURFURA SHARIF NL                                    | 4/2009 | 3/2014<br>(-)<br>[0/0]        | 257.42<br>(-)<br>[258.73]            | 113.58<br>(1.31)<br>[0]        |
| 860 | MADURAI-TUTICORIN VIA ARUPPUKKOTTAI                                                                         | 4/2011 | 3/2019<br>(-)<br>[3/2019]     | 120.70<br>(-)<br>[1,800.00]          | 112.10<br>(1,679.30)<br>[0]    |
| 861 | MAGRAHAT-DIAMOND HARBOUR WITH MM<br>SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND<br>HATBOUR - BAHRAHAT-KULPI NL   | 4/2009 | 2/2012<br>(-)<br>[0/0]        | 499.96<br>(-)<br>[665.75]            | 149.39<br>(165.79)<br>[0]      |
| 862 | MIRAJ-LONDA                                                                                                 | 3/2015 | /<br>(3/2021)<br>[3/2021]     | 1,830.00<br>(1,190.92)<br>[1,190.92] | 207.68<br>(-639.08)<br>[-]     |
| 863 | MM FROM BURAMARA-CHAKULIA                                                                                   | 4/2008 | 0/0<br>(12/2024)<br>[12/2024] | 466.48<br>(-)<br>[1,000.00]          | 0.83<br>(533.52)<br>[-]        |
| 864 | MONIGRAM- NIMTITA                                                                                           | 4/2012 | /<br>(-)<br>[0/0]             | 250.93<br>(-)<br>[259.23]            | 208.85<br>(8.30)<br>[0]        |
| 865 | MUNEERABAD-MAHABOBNAGAR(NL),SCR                                                                             | 4/1997 | 3/2000<br>(-)<br>[3/2019]     | 1,723.00<br>(1.00)<br>[645.00]       | 725.63<br>(-1,078.00)<br>[228] |
| 866 | MURKONGSELEK-PASIGHAT NL                                                                                    | 4/2011 | 3/2020<br>(-)<br>[3/2020]     | 414.84<br>(-)<br>[661.00]            | 121.37<br>(246.16)<br>[0]      |
| 867 | NANGALDAM-TALWARA(NL),NR                                                                                    | 3/1981 | 7/2012<br>(-)<br>[0/0]        | 450.00<br>(-)<br>[2,100.00]          | 484.14<br>(1,650.00)<br>[0]    |
| 868 | NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI<br>NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-<br>BAHRAHAT NL | 4/2010 | 3/2005<br>(-)<br>[0/0]        | 494.54<br>(-)<br>[492.68]            | 32.00<br>(-1.86)<br>[0]        |
| 869 | NEW BG LINE FROM BALURGHAT TO HILLY NFR                                                                     | 4/2010 | 3/2020<br>(-)                 | 242.22<br>(-)                        | 64.68<br>(228.78)              |

|     |                                                                                                   |         |           |             |             |
|-----|---------------------------------------------------------------------------------------------------|---------|-----------|-------------|-------------|
|     |                                                                                                   |         | [3/2020]  | [471.00]    | [0]         |
| 870 | NEW BG LINE FROM JAGBANI TO BIRATNAGAR                                                            | 4/2010  | /         | 241.52      | 148.33      |
|     |                                                                                                   |         | (-)       | (-)         | (152.76)    |
|     |                                                                                                   |         | [0/0]     | [394.28]    | [0]         |
| 871 | NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING                                                          | 4/2013  | 3/2019    | 1,798.00    | 0.00        |
|     |                                                                                                   |         | (-)       | (-)         | (0.00)      |
|     |                                                                                                   |         | [3/2019]  | [1,798.00]  | [0]         |
| 872 | NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI | 4/1999  | /         | 819.23      | 1,082.01    |
|     |                                                                                                   |         | (-)       | (-)         | (1,051.77)  |
|     |                                                                                                   |         | [0/0]     | [1,871.00]  | [0]         |
| 873 | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR                                            | 4/2000  | 12/2008   | 1,180.19    | 3,065.47    |
|     |                                                                                                   |         | (-)       | (2,531.34)  | (1,859.81)  |
|     |                                                                                                   |         | [3/2019]  | [3,040.00]  | [123]       |
| 874 | PHULERA - DIGANA DOUBLING                                                                         | 5/2015  | 3/2020    | 600.00      | 3.52        |
|     |                                                                                                   |         | (-)       | (-)         | (85.99)     |
|     |                                                                                                   |         | [3/2020]  | [685.99]    | [0]         |
| 875 | PIRPAINTI-BHAGALPUR                                                                               | 4/2011  | /         | 261.38      | 378.90      |
|     |                                                                                                   |         | (-)       | (-)         | (70.76)     |
|     |                                                                                                   |         | [0/0]     | [332.14]    | [0]         |
| 876 | PIRPAINTI-JASIDIH                                                                                 | 4/2013  | 3/2022    | 915.98      | 319.53      |
|     |                                                                                                   |         | (-)       | (-)         | (-0.02)     |
|     |                                                                                                   |         | [3/2022]  | [915.96]    | [0]         |
| 877 | PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY                                                 | 4/2011  | 3/2017    | 299.60      | 1.12        |
|     |                                                                                                   |         | (-)       | (-)         | (0.00)      |
|     |                                                                                                   |         | [0/0]     | [299.60]    | [0]         |
| 878 | QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)                                                   | 3/1998  | /         | 280.00      | 834.87      |
|     |                                                                                                   |         | (-)       | (-)         | (842.00)    |
|     |                                                                                                   |         | [0/0]     | [1,122.00]  | [0]         |
| 879 | RATLAM-DUNGARPUR VIA BANSWARA (NL)                                                                | 4/2011  | /         | 2,082.75    | 183.40      |
|     |                                                                                                   |         | (-)       | (-)         | (796.22)    |
|     |                                                                                                   |         | [0/0]     | [2,878.97]  | [0]         |
| 880 | RAYADURGA-TUMKUR NL                                                                               | 4/2007  | /         | 2,062.30    | 674.76      |
|     |                                                                                                   |         | (-)       | (-)         | (-0.10)     |
|     |                                                                                                   |         | [3/2022]  | [2,062.20]  | [-]         |
| 881 | SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE                                              | 4/2010  | /         | 268.52      | 78.81       |
|     |                                                                                                   |         | (-)       | (-)         | (0.00)      |
|     |                                                                                                   |         | [0/0]     | [268.52]    | [0]         |
| 882 | SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL                              | 4/2000  | /         | 297.47      | 53.11       |
|     |                                                                                                   |         | (-)       | (-)         | (1.56)      |
|     |                                                                                                   |         | [0/0]     | [299.03]    | [0]         |
| 883 | SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL                                      | 4/2010  | 3/2016    | 277.28      | 137.93      |
|     |                                                                                                   |         | (-)       | (-)         | (-10.76)    |
|     |                                                                                                   |         | [3/2020]  | [266.52]    | [48]        |
| 884 | SRINIVASA-PURA-MADANAPALLI NL                                                                     | 4/2013  | /         | 296.00      | 0.00        |
|     |                                                                                                   |         | (12/2023) | (-)         | (170.65)    |
|     |                                                                                                   |         | [12/2023] | [466.65]    | [-]         |
| 885 | SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR                                               | 4/2007  | /         | 450.00      | 9.31        |
|     |                                                                                                   |         | (-)       | (-)         | (-161.15)   |
|     |                                                                                                   |         | [0/0]     | [288.85]    | [0]         |
| 886 | TARAKESHWAR-MAGRA NEW BG LINE                                                                     | 4/2010  | /         | 365.17      | 1.73        |
|     |                                                                                                   |         | (-)       | (-)         | (162.37)    |
|     |                                                                                                   |         | [0/0]     | [527.54]    | [0]         |
| 887 | WESTERN DEDICATED FREIGHT CORRIDOR                                                                | 11/2007 | 3/2020    | 16,592.00   | 22,485.00   |
|     |                                                                                                   |         | (-)       | (51,101.00) | (34,509.00) |
|     |                                                                                                   |         | [3/2020]  | [51,101.00] | [0]         |
| 888 | YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH                                                   | 4/2013  | /         | 876.00      | 0.00        |
|     |                                                                                                   |         | (-)       | (-)         | (0.00)      |
|     |                                                                                                   |         | [0/0]     | [876.00]    | [0]         |
| 889 | YELAHANKA-PENUKONDA                                                                               | 5/2015  | 3/2020    | 860.43      | 503.45      |
|     |                                                                                                   |         | (3/2020)  | (860.43)    | (0.00)      |
|     |                                                                                                   |         | [3/2020]  | [860.43]    | [0]         |

|     |                                                                                                      |         |                                  |                                      |                                 |
|-----|------------------------------------------------------------------------------------------------------|---------|----------------------------------|--------------------------------------|---------------------------------|
|     | <b>Road Transport And Highways</b>                                                                   |         |                                  |                                      |                                 |
| 890 | 4 LANING OF NAGPUR-BETUL                                                                             | 2/2011  | 8/2014<br>(-)<br>[0/0]           | 2,498.76<br>(-)<br>[2,498.76]        | 2,525.46<br>(0.00)<br>[0]       |
| 891 | DELHI AGRA APPROVED LENGTH 180.0 KM                                                                  | 10/2012 | 4/2015<br>(-)<br>[0/0]           | 1,928.22<br>(-)<br>[2,945.00]        | 2,970.11<br>(1,016.78)<br>[0]   |
| 892 | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-III)                                     | 9/2015  | 3/2018<br>(-)<br>[0/0]           | 788.51<br>(-)<br>[788.51]            | 103.37<br>(0.00)<br>[0]         |
| 893 | FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. | 3/2018  | /<br>(-)<br>[0/0]                | 1,294.47<br>(-)<br>[1,294.47]        | 0.00<br>(0.00)<br>[0]           |
| 894 | FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE | 3/2018  | /<br>(-)<br>[0/0]                | 998.70<br>(-)<br>[998.70]            | 0.00<br>(0.00)<br>[0]           |
| 895 | GWALIOR-JHANSI, NH-75                                                                                | 12/2003 | 12/2009<br>(-)<br>[8/2020]       | 604.00<br>(-)<br>[604.00]            | 423.83<br>(0.00)<br>[128]       |
| 896 | MUZAFFARNAGAR-HARIDWAR                                                                               | 9/2011  | 3/2013<br>(-)<br>[12/2019]       | 754.00<br>(-)<br>[754.00]            | 1,363.43<br>(0.00)<br>[81]      |
| 897 | SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP | 9/2016  | /<br>(-)<br>[2/2020]             | 1,244.10<br>(-)<br>[1,244.10]        | 85.00<br>(0.00)<br>[-]          |
| 898 | SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502                                                            | 2/2009  | 8/2011<br>(-)<br>[0/0]           | 1,693.75<br>(-)<br>[1,693.75]        | 2,675.28<br>(0.00)<br>[0]       |
| 899 | VARANASI-AURANGABAD KM.786 TO KM.978.40                                                              | 9/2011  | 3/2014<br>(-)<br>[12/2019]       | 2,848.00<br>(-)<br>[2,848.00]        | 1,141.90<br>(0.00)<br>[69]      |
| 900 | WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA | 3/2015  | /<br>(-)<br>[0/0]                | 789.83<br>(-)<br>[789.83]            | 109.77<br>(0.00)<br>[0]         |
|     | <b>Shipping And Ports</b>                                                                            |         |                                  |                                      |                                 |
| 901 | JAL MARG VIKAS PROJECT                                                                               | 1/2018  | 3/2023<br>(-)<br>[3/2023]        | 4,200.00<br>(-)<br>[4,200.00]        | 0.00<br>(0.00)<br>[0]           |
|     | <b>Telecommunications</b>                                                                            |         |                                  |                                      |                                 |
| 902 | NETWORK FOR SPECTRUM                                                                                 | 3/2012  | 7/2015<br>(-)<br>[5/2020]        | 13,334.00<br>(-)<br>[24,664.00]      | 8,397.00<br>(11,330.00)<br>[58] |
| 903 | NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY                                | 9/2014  | 9/2014<br>(-)<br>[0/0]           | 2,111.17<br>(-)<br>[2,011.17]        | 253.90<br>(-100.00)<br>[0]      |
|     | <b>NAGALAND</b>                                                                                      |         |                                  |                                      |                                 |
|     | <b>Railways</b>                                                                                      |         |                                  |                                      |                                 |
| 904 | DIMAPUR-TIZIT NL                                                                                     | 4/2013  | 3/2020<br>(-)<br>[3/2020]        | 4,274.00<br>(-)<br>[4,274.00]        | 0.00<br>(0.00)<br>[0]           |
| 905 | NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)                                       | 4/2006  | 3/2015<br>(10/2021)<br>[10/2021] | 2,326.52<br>(2,446.57)<br>[3,000.00] | 677.37<br>(673.48)<br>[79]      |
|     | <b>Road Transport And Highways</b>                                                                   |         |                                  |                                      |                                 |
| 906 | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO  | 3/2018  | 9/2018<br>(-)<br>[0/0]           | 239.30<br>(-)<br>[239.30]            | 0.00<br>(0.00)<br>[0]           |
| 907 | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO  | 3/2018  | 9/2018<br>(-)<br>[0/0]           | 285.68<br>(-)<br>[285.68]            | 0.00<br>(0.00)<br>[0]           |
| 908 | CONSTRUCTION OF TWO LANE WITH HARD                                                                   | 3/2018  | 9/2018                           | 282.98                               | 0.00                            |



|     |                                                                                                      |         |                           |                               |                           |
|-----|------------------------------------------------------------------------------------------------------|---------|---------------------------|-------------------------------|---------------------------|
|     | SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.                                     |         | (-)<br>[0/0]              | (-)<br>[282.98]               | (0.00)<br>[0]             |
| 909 | (I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. | 2/2017  | 9/2018<br>(-)<br>[0/0]    | 387.00<br>(-)<br>[387.00]     | 0.00<br>(0.00)<br>[0]     |
| 910 | (II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING  | 3/2018  | 9/2018<br>(-)<br>[0/0]    | 500.09<br>(-)<br>[500.09]     | 0.00<br>(0.00)<br>[0]     |
| 911 | CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 | 2/2017  | 4/2017<br>(-)<br>[0/0]    | 507.68<br>(-)<br>[507.68]     | 0.00<br>(0.00)<br>[0]     |
| 912 | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO  | 3/2018  | 9/2018<br>(-)<br>[0/0]    | 339.57<br>(-)<br>[339.57]     | 0.00<br>(0.00)<br>[0]     |
| 913 | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO  | 3/2018  | 9/2018<br>(-)<br>[0/0]    | 315.03<br>(-)<br>[315.03]     | 0.00<br>(0.00)<br>[0]     |
| 914 | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO  | 3/2018  | 9/2018<br>(-)<br>[0/0]    | 240.64<br>(-)<br>[240.64]     | 0.00<br>(0.00)<br>[0]     |
| 915 | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO | 3/2018  | 9/2018<br>(-)<br>[0/0]    | 215.12<br>(-)<br>[215.12]     | 0.00<br>(0.00)<br>[0]     |
| 916 | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO | 3/2018  | 9/2018<br>(-)<br>[0/0]    | 215.79<br>(-)<br>[215.79]     | 0.00<br>(0.00)<br>[0]     |
| 917 | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO | 3/2018  | 9/2018<br>(-)<br>[0/0]    | 272.89<br>(-)<br>[272.89]     | 0.00<br>(0.00)<br>[0]     |
| 918 | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO | 3/2018  | 9/2018<br>(-)<br>[0/0]    | 323.98<br>(-)<br>[323.98]     | 0.00<br>(0.00)<br>[0]     |
| 919 | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 | 3/2018  | 9/2018<br>(-)<br>[0/0]    | 251.97<br>(-)<br>[251.97]     | 0.00<br>(0.00)<br>[0]     |
| 920 | CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 | 3/2018  | 9/2018<br>(-)<br>[0/0]    | 237.72<br>(-)<br>[237.72]     | 0.00<br>(0.00)<br>[0]     |
| 921 | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 | 3/2016  | 8/2016<br>(-)<br>[8/2019] | 373.07<br>(-)<br>[373.07]     | 0.00<br>(0.00)<br>[36]    |
| 922 | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 | 3/2016  | 8/2016<br>(-)<br>[8/2019] | 396.52<br>(-)<br>[396.52]     | 0.00<br>(0.00)<br>[36]    |
| 923 | FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 | 3/2016  | 8/2016<br>(-)<br>[8/2019] | 429.52<br>(-)<br>[429.52]     | 0.00<br>(0.00)<br>[36]    |
| 924 | WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA | 12/2010 | 2/2011<br>(-)<br>[0/0]    | 1,296.00<br>(-)<br>[1,296.00] | 0.00<br>(0.00)<br>[0]     |
|     | <u>ODISHA</u>                                                                                        |         |                           |                               |                           |
|     | <u>Coal</u>                                                                                          |         |                           |                               |                           |
| 925 | ANANTA OC EXPANSION PH-III (15.0 MTY)                                                                | 8/2008  | 3/2012<br>(-)<br>[3/2021] | 207.28<br>(-)<br>[207.28]     | 235.50<br>(0.00)<br>[108] |
| 926 | BALRAM OCP EXTENSION,MCL 8.00 MTY                                                                    | 12/2007 | 3/2010<br>(-)<br>[3/2020] | 172.08<br>(-)<br>[172.08]     | 267.19<br>(0.00)<br>[120] |
| 927 | BASUNDHARA (WEST) OC EXTN(7.00 MTY)                                                                  | 5/2014  | 3/2019<br>(-)<br>[3/2024] | 479.15<br>(-)<br>[479.15]     | 120.51<br>(0.00)<br>[60]  |

|     |                                                                                                      |         |                                |                                      |                          |
|-----|------------------------------------------------------------------------------------------------------|---------|--------------------------------|--------------------------------------|--------------------------|
| 928 | BHUBANESWARI OCP, MCL (20.0 MTY)                                                                     | 12/2007 | 3/2017<br>(-)<br>[3/2020]      | 490.10<br>(-)<br>[490.10]            | 413.37<br>(0.00)<br>[36] |
| 929 | GARJANBAHAL OCP                                                                                      | 11/2014 | 3/2021<br>(-)<br>[3/2021]      | 1,375.38<br>(-)<br>[1,375.38]        | 424.90<br>(0.00)<br>[0]  |
| 930 | HINGULA OC-II EXP. PH-III (15 MTY)                                                                   | 11/2008 | 3/2013<br>(-)<br>[3/2020]      | 479.53<br>(-)<br>[479.53]            | 336.08<br>(0.00)<br>[84] |
| 931 | INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP                                                             | 5/2018  | 3/2027<br>(-)<br>[3/2027]      | 2,434.75<br>(-)<br>[2,434.75]        | 0.00<br>(0.00)<br>[0]    |
| 932 | JAGANNATH RE-ORGANISATION OC.(6.00 MTY)                                                              | 5/2014  | 3/2019<br>(-)<br>[3/2021]      | 337.66<br>(-)<br>[337.66]            | 65.58<br>(0.00)<br>[24]  |
| 933 | KANIHA OCP, MCL, (10.0 MTY)                                                                          | 12/2007 | 3/2013<br>(-)<br>[3/2020]      | 457.77<br>(-)<br>[457.77]            | 584.85<br>(0.00)<br>[84] |
| 934 | KULDA EXPN OC. (5.00 MTY)                                                                            | 6/2014  | 3/2018<br>(-)<br>[3/2020]      | 289.03<br>(-)<br>[289.03]            | 28.56<br>(0.00)<br>[24]  |
| 935 | KULDA OCP (MAHANADI COALFIELDS LTD)                                                                  | 1/2005  | 3/2010<br>(-)<br>[3/2018]      | 302.96<br>(-)<br>[302.96]            | 302.96<br>(0.00)<br>[0]  |
| 936 | SIARMAL OCP (40.00MTY)                                                                               | 5/2014  | 3/2026<br>(-)<br>[3/2026]      | 3,756.36<br>(-)<br>[3,756.36]        | 689.33<br>(0.00)<br>[0]  |
|     | <u>Mines</u>                                                                                         |         |                                |                                      |                          |
| 937 | 5TH STREAM ALUMINA REFINERY EXPANSION PROJECT                                                        | 12/2014 | 4/2021<br>(4/2021)<br>[4/2021] | 5,540.00<br>(5,540.00)<br>[5,540.00] | 96.98<br>(0.00)<br>[0]   |
| 938 | CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND | 12/2015 | 11/2020<br>(-)<br>[11/2020]    | 355.00<br>(-)<br>[355.00]            | 31.92<br>(0.00)<br>[0]   |
| 939 | SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN | 11/2017 | 4/2021<br>(4/2021)<br>[4/2021] | 483.00<br>(483.00)<br>[483.00]       | 0.00<br>(0.00)<br>[0]    |
| 940 | UTKAL D AND E COAL BLOCK                                                                             | 5/2016  | 1/2020<br>(1/2020)<br>[1/2020] | 534.00<br>(534.00)<br>[534.00]       | 302.60<br>(0.00)<br>[0]  |
|     | <u>Petroleum</u>                                                                                     |         |                                |                                      |                          |
| 941 | 2G ETHANOL BIO REFINERY AT BARGARH                                                                   | 8/2017  | 12/2020<br>(-)<br>[12/2020]    | 750.00<br>(-)<br>[750.00]            | 24.43<br>(0.00)<br>[0]   |
| 942 | CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY                                           | 8/2017  | 12/2021<br>(-)<br>[12/2021]    | 315.00<br>(-)<br>[315.00]            | 2.87<br>(0.00)<br>[0]    |
| 943 | CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR                                                     | 7/2017  | 7/2022<br>(-)<br>[7/2022]      | 243.53<br>(243.53)<br>[243.53]       | 35.47<br>(0.00)<br>[0]   |
| 944 | CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK                                                         | 7/2017  | 7/2022<br>(-)<br>[7/2022]      | 181.20<br>(-)<br>[181.20]            | 15.72<br>(0.00)<br>[0]   |
| 945 | DHAMRA-ANGUL PIPELINE PROJECT                                                                        | 3/2017  | 12/2020<br>(-)<br>[12/2020]    | 1,933.00<br>(-)<br>[1,933.00]        | 814.01<br>(0.00)<br>[0]  |
| 946 | ETHYLENE GLYCOL PROJECT AT PARADIP                                                                   | 4/2018  | 7/2021<br>(-)<br>[7/2021]      | 4,807.08<br>(-)<br>[4,807.08]        | 24.09<br>(0.00)<br>[0]   |
| 947 | INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY                                   | 5/2016  | 1/2019<br>(-)                  | 429.00<br>(-)                        | 291.90<br>(0.00)         |

|     |                                                                                               |         |                                   |                                 |                                |
|-----|-----------------------------------------------------------------------------------------------|---------|-----------------------------------|---------------------------------|--------------------------------|
|     |                                                                                               |         | [1/2019]                          | [429.00]                        | [0]                            |
| 948 | LPG BP PROJECT KHORDHA                                                                        | 12/2016 | 12/2019<br>(-)<br>[12/2019]       | 161.59<br>(-)<br>[161.59]       | 33.93<br>(0.00)<br>[0]         |
| 949 | PARADIP SOMNATHPUR HALDIA PIPELINE                                                            | 10/2018 | 10/2021<br>(-)<br>[10/2021]       | 1,297.50<br>(-)<br>[1,297.50]   | 0.00<br>(0.00)<br>[0]          |
| 950 | POLYPROPYLENE PLANT AT PARADIP REFINERY                                                       | 3/2014  | 9/2017<br>(12/2018)<br>[12/2018]  | 3,150.00<br>(-)<br>[3,150.00]   | 2,494.51<br>(0.00)<br>[15]     |
|     | <u>Power</u>                                                                                  |         |                                   |                                 |                                |
| 951 | DARLIPALLI STPP STAGE-I (2X800 MW)                                                            | 2/2014  | 8/2018<br>(6/2019)<br>[6/2019]    | 12,532.44<br>(-)<br>[13,740.53] | 8,441.41<br>(1,208.09)<br>[10] |
| 952 | PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA | 4/2016  | 4/2019<br>(-)<br>[4/2019]         | 844.64<br>(-)<br>[844.64]       | 303.70<br>(0.00)<br>[0]        |
|     | <u>Railways</u>                                                                               |         |                                   |                                 |                                |
| 953 | BANASPANI- JAKHPURA - DOUBLING                                                                | 3/2009  | 3/2019<br>(-)<br>[3/2021]         | 942.95<br>(-)<br>[942.95]       | 887.88<br>(0.00)<br>[24]       |
| 954 | BHADRAK - NERGUNDI 3RD LINE                                                                   | 3/2013  | 10/2020<br>(-)<br>[3/2021]        | 843.04<br>(843.04)<br>[843.04]  | 81.26<br>(0.00)<br>[5]         |
| 955 | BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.                                          | 4/2015  | 12/2018<br>(-)<br>[3/2021]        | 1,172.92<br>(-)<br>[1,172.92]   | 245.16<br>(0.00)<br>[27]       |
| 956 | CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION                                                     | 4/2010  | 3/2015<br>(-)<br>[0/0]            | 149.90<br>(-)<br>[230.00]       | 54.96<br>(80.10)<br>[0]        |
| 957 | EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL             | 4/2016  | 3/2020<br>(-)<br>[3/2020]         | 5,200.00<br>(-)<br>[5,200.00]   | 0.00<br>(0.00)<br>[0]          |
| 958 | HARIDASPUR-PARADEEP(NL)                                                                       | 4/1996  | 12/2017<br>(-)<br>[3/2020]        | 1,185.64<br>(-)<br>[1,844.47]   | 1,406.23<br>(658.83)<br>[27]   |
| 959 | JAGADALPUR-KORAPUT DOUBLING                                                                   | 4/2015  | 3/2022<br>(-)<br>[3/2022]         | 1,547.38<br>(-)<br>[1,547.38]   | 189.40<br>(0.00)<br>[0]        |
| 960 | JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE                           | 4/2015  | 11/2018<br>(-)<br>[3/2021]        | 701.61<br>(-)<br>[810.02]       | 88.04<br>(108.41)<br>[28]      |
| 961 | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)                                                     | 4/2000  | 3/2009<br>(3/2009)<br>[2/2019]    | 133.41<br>(207.00)<br>[385.00]  | 377.10<br>(251.59)<br>[119]    |
| 962 | KHURDA ROAD-BOLANGIR(NL)ECOR                                                                  | 4/1994  | 3/2009<br>(-)<br>[6/2021]         | 2,923.13<br>(-)<br>[3,798.80]   | 1,123.73<br>(875.67)<br>[147]  |
| 963 | KORAPUT - SINGAPUR ROAD DOUBLING                                                              | 4/2015  | 3/2022<br>(-)<br>[3/2022]         | 2,361.74<br>(-)<br>[2,361.74]   | 81.06<br>(0.00)<br>[0]         |
| 964 | ROURKELA JHARSUGUDA THIRD LINE 101 KM                                                         | 11/2015 | 3/2020<br>(3/2020)<br>[6/2020]    | 969.83<br>(-)<br>[1,151.81]     | 389.91<br>(181.98)<br>[3]      |
| 965 | RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO  | 4/1995  | 12/2021<br>(12/2024)<br>[12/2024] | 524.43<br>(-)<br>[939.00]       | 184.10<br>(414.57)<br>[36]     |
| 966 | SAMBALPUR - ANGUL RLY. ELECTRIFICATION                                                        | 3/2012  | 3/2020<br>(-)<br>[3/2020]         | 155.81<br>(-)<br>[238.03]       | 180.78<br>(82.22)<br>[0]       |
| 967 | SAMBALPUR - TITLAGARH - DOUBLING                                                              | 3/2006  | 3/2020                            | 948.04                          | 910.62                         |

|     |                                                                                                             |         |                             |                                      |                              |
|-----|-------------------------------------------------------------------------------------------------------------|---------|-----------------------------|--------------------------------------|------------------------------|
|     |                                                                                                             |         | (-)<br>[3/2020]             | (-)<br>[970.00]                      | (21.96)<br>[0]               |
| 968 | SAMBALPUR-TALCHER DOUBLING                                                                                  | 3/2011  | 2/2019<br>(-)<br>[3/2021]   | 1,111.99<br>(1,539.28)<br>[1,539.28] | 765.60<br>(427.29)<br>[25]   |
| 969 | SUKINDA ROAD - ANGUL (NL)(ECOR)                                                                             | 4/1998  | 2/2015<br>(-)<br>[12/2021]  | 1,202.70<br>(245.00)<br>[1,202.70]   | 698.59<br>(0.00)<br>[82]     |
| 970 | TALCHER-BIMALAGARH(NL)(ECOR)                                                                                | 4/2005  | 6/2021<br>(-)<br>[3/2023]   | 810.78<br>(-)<br>[1,928.07]          | 574.98<br>(1,117.29)<br>[21] |
| 971 | VIZIANAGARAM -SAMABALPUR 3RD LINE                                                                           | 1/1991  | 12/2024<br>(-)<br>[12/2024] | 2,335.67<br>(2,335.67)<br>[2,335.67] | 316.27<br>(0.00)<br>[0]      |
|     | <u>Road Transport And Highways</u>                                                                          |         |                             |                                      |                              |
| 972 | 4 LANING OF BAHARAGORA - SINGHARA                                                                           | 7/2015  | /<br>(-)<br>[4/2020]        | 1,282.94<br>(-)<br>[1,282.94]        | 0.00<br>(0.00)<br>[-]        |
| 973 | DEVELOPMENT OF FOUR LANNING OF ANGUL-<br>SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42<br>(NEW NH-55 IN THE S | 9/2016  | 8/2019<br>(-)<br>[8/2019]   | 2,510.04<br>(-)<br>[2,510.04]        | 0.00<br>(0.00)<br>[0]        |
| 974 | FOUR LANING WITH PS TALEBANI -SMBALPUR                                                                      | 12/2015 | /<br>(-)<br>[11/2019]       | 752.28<br>(-)<br>[752.28]            | 0.00<br>(0.00)<br>[-]        |
| 975 | IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO<br>JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY<br>WITH PAVED   | 12/2013 | 5/2016<br>(-)<br>[0/0]      | 319.80<br>(320.00)<br>[320.00]       | 0.00<br>(0.20)<br>[0]        |
| 976 | IMPROVEMENT FROM KM 0/0 TO 68/0                                                                             | 12/2013 | 10/2016<br>(-)<br>[0/0]     | 319.80<br>(-)<br>[319.80]            | 0.00<br>(0.00)<br>[0]        |
| 977 | JHARPOKHARIA-BARIPADA-BALESHWAR SECTION                                                                     | 2/2016  | /<br>(-)<br>[6/2019]        | 1,069.65<br>(-)<br>[1,069.65]        | 0.00<br>(0.00)<br>[-]        |
| 978 | PANIKHOLI-RIMOLI                                                                                            | 3/2012  | 9/2014<br>(-)<br>[3/2019]   | 1,410.00<br>(-)<br>[1,410.00]        | 1,555.96<br>(0.00)<br>[54]   |
| 979 | REHABILITAITON AND UPGRADATION TO FOUR LANING<br>OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO<br>KM 4  | 10/2016 | /<br>(-)<br>[7/2020]        | 1,008.96<br>(-)<br>[1,008.96]        | 32.50<br>(0.00)<br>[-]       |
| 980 | REHABILITATION AND UP GRADATION OF EXISTING 2-<br>LANE TO 4-LANE STANDARDS TO END OF<br>KAMAKHYANAGAR BYPAS | 1/2018  | /<br>(-)<br>[0/0]           | 564.66<br>(-)<br>[564.66]            | 0.00<br>(0.00)<br>[0]        |
| 981 | REHABILITATION AND UP-GRADATION OF<br>BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)                               | 7/2017  | 7/2017<br>(-)<br>[11/2020]  | 476.56<br>(-)<br>[476.56]            | 0.00<br>(0.00)<br>[40]       |
| 982 | REHABILITATION AND UP-GRADATION OF EXISTING 2-<br>LANE TO 4 LANE OF DUBURI (KM 388.376) TO<br>CHANDIKHOLE ( | 1/2018  | /<br>(-)<br>[0/0]           | 633.68<br>(-)<br>[633.68]            | 0.00<br>(0.00)<br>[0]        |
| 983 | REHABILITATION AND UP-GRADATION OF EXISTING 2-<br>LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA<br>(KM 25 | 1/2018  | /<br>(-)<br>[0/0]           | 953.09<br>(-)<br>[953.09]            | 0.00<br>(0.00)<br>[0]        |
| 984 | REHABILITATION AND UP-GRADATION OF EXISTING 2-<br>LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM<br>206.2 | 1/2018  | /<br>(-)<br>[0/0]           | 668.86<br>(-)<br>[668.86]            | 0.00<br>(0.00)<br>[0]        |
| 985 | REHABILITATION AND UP-GRADATION OF EXISTING 2-<br>LANE TO FOUR LANE FROM TALCHAR TO END OF<br>KAMAKHYANAG   | 1/2018  | /<br>(-)<br>[0/0]           | 614.48<br>(-)<br>[614.48]            | 0.00<br>(0.00)<br>[0]        |
| 986 | REHABILITATION AND UP-GRADATION OF NH-149 FROM<br>KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN<br>TH  | 7/2014  | 1/2017<br>(-)<br>[0/0]      | 342.05<br>(-)<br>[342.05]            | 0.00<br>(0.00)<br>[0]        |
| 987 | REHABILITATION AND UP-GRADATION OF SIX-LANING                                                               | 1/2018  | /                           | 1,522.00                             | 0.00                         |

|      |                                                                                                      |         |                 |                      |                 |
|------|------------------------------------------------------------------------------------------------------|---------|-----------------|----------------------|-----------------|
|      | OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM                                               |         | (-)<br>[0/0]    | (-)<br>[1,522.00]    | (0.00)<br>[0]   |
| 988  | REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) ( | 1/2018  | /               | 503.88               | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[503.88]      | (0.00)<br>[0]   |
| 989  | REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM  | 3/2017  | 3/2020          | 1,288.07             | 0.00            |
|      |                                                                                                      |         | (-)<br>[3/2020] | (-)<br>[1,420.00]    | (131.93)<br>[0] |
| 990  | REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO | 12/2017 | /               | 686.65               | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[686.65]      | (0.00)<br>[0]   |
| 991  | REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON | 1/2018  | /               | 686.65               | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[686.65]      | (0.00)<br>[0]   |
| 992  | REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA | 12/2017 | /               | 417.51               | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[417.51]      | (0.00)<br>[0]   |
| 993  | REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN  | 7/2014  | 1/2017          | 342.05               | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (342.00)<br>[342.00] | (-0.05)<br>[0]  |
| 994  | REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 | 1/2018  | /               | 999.00               | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[999.00]      | (0.00)<br>[0]   |
| 995  | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR | 8/2013  | 6/2016          | 171.96               | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (172.00)<br>[172.00] | (0.04)<br>[0]   |
| 996  | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB | 1/1991  | 10/2017         | 218.63               | 29.27           |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[218.63]      | (0.00)<br>[0]   |
| 997  | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK | 1/1991  | 5/2018          | 229.41               | 6.65            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[229.41]      | (0.00)<br>[0]   |
| 998  | SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR                                                        | 12/2011 | 6/2014          | 1,047.00             | 1,613.62        |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[1,047.00]    | (0.00)<br>[0]   |
| 999  | SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000)                | 3/2018  | /               | 806.11               | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[806.11]      | (0.00)<br>[0]   |
| 1000 | WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 | 3/2014  | 5/2016          | 162.51               | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (163.00)<br>[163.00] | (0.49)<br>[0]   |
| 1001 | WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO | 3/2014  | 5/2016          | 191.50               | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (192.00)<br>[192.00] | (0.50)<br>[0]   |
| 1002 | WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM    | 2/2015  | 10/2017         | 239.91               | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (240.00)<br>[240.00] | (0.09)<br>[0]   |
| 1003 | WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY    | 1/2015  | 4/2018          | 326.63               | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (327.00)<br>[327.00] | (0.37)<br>[0]   |
| 1004 | WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG | 6/2016  | 6/2018          | 157.30               | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (157.00)<br>[157.00] | (-0.30)<br>[0]  |
| 1005 | WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA     | 12/2011 | 11/2017         | 159.39               | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[159.39]      | (0.00)<br>[0]   |
| 1006 | WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA | 12/2011 | 8/2015          | 191.08               | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[191.08]      | (0.00)<br>[0]   |
| 1007 | WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010                | 3/2015  | 10/2017         | 226.31               | 0.00            |
|      |                                                                                                      |         | (-)             | (226.00)             | (-0.31)         |

|      |                                                                                                      |         |                                |                                |                            |
|------|------------------------------------------------------------------------------------------------------|---------|--------------------------------|--------------------------------|----------------------------|
|      | TO KM 224.900                                                                                        |         | [0/0]                          | [226.00]                       | [0]                        |
|      | <u>Steel</u>                                                                                         |         |                                |                                |                            |
| 1008 | INSTALLATION OF NEW HOT STRIP MILL AT RSP                                                            | 4/2015  | 4/2018<br>(-)<br>[5/2019]      | 3,127.30<br>(-)<br>[3,127.30]  | 2,527.38<br>(0.00)<br>[13] |
|      | <u>PUNJAB</u>                                                                                        |         |                                |                                |                            |
|      | <u>Fertilisers</u>                                                                                   |         |                                |                                |                            |
| 1009 | GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA                           | 1/2018  | 11/2019<br>(-)<br>[11/2019]    | 218.83<br>(-)<br>[218.83]      | 26.47<br>(0.00)<br>[0]     |
| 1010 | GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL                             | 1/2018  | 11/2019<br>(-)<br>[11/2019]    | 239.81<br>(-)<br>[239.81]      | 32.18<br>(0.00)<br>[0]     |
|      | <u>Health And Family Welfare</u>                                                                     |         |                                |                                |                            |
| 1011 | ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB                                           | 7/2016  | 6/2020<br>(-)<br>[6/2020]      | 703.00<br>(-)<br>[703.00]      | 272.00<br>(0.00)<br>[0]    |
| 1012 | SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB                                                       | 7/2016  | 2/2018<br>(2/2018)<br>[6/2019] | 152.95<br>(-)<br>[152.95]      | 83.11<br>(0.00)<br>[16]    |
|      | <u>Railways</u>                                                                                      |         |                                |                                |                            |
| 1013 | MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL              | 4/2009  | /<br>(-)<br>[0/0]              | 396.04<br>(-)<br>[369.00]      | 186.27<br>(-27.04)<br>[0]  |
| 1014 | QADIAN-BEAS                                                                                          | 4/2011  | /<br>(-)<br>[0/0]              | 205.22<br>(-)<br>[205.22]      | 3.18<br>(0.00)<br>[0]      |
|      | <u>Road Transport And Highways</u>                                                                   |         |                                |                                |                            |
| 1015 | 4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM  | 11/2014 | /<br>(-)<br>[0/0]              | 573.96<br>(605.00)<br>[605.00] | 209.74<br>(31.04)<br>[0]   |
| 1016 | 4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64( | 2/2015  | /<br>(-)<br>[0/0]              | 486.74<br>(-)<br>[486.74]      | 189.39<br>(0.00)<br>[0]    |
| 1017 | 4 LANING FROM PHAGWARA TO RUPNAGAR                                                                   | 8/2016  | /<br>(-)<br>[4/2020]           | 1,169.61<br>(-)<br>[1,169.61]  | 234.38<br>(0.00)<br>[-]    |
| 1018 | 4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO  | 11/2014 | /<br>(-)<br>[0/0]              | 463.65<br>(546.00)<br>[463.65] | 280.16<br>(0.00)<br>[0]    |
| 1019 | 4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI  | 2/2015  | /<br>(-)<br>[0/0]              | 483.38<br>(-)<br>[483.38]      | 65.76<br>(0.00)<br>[0]     |
| 1020 | 4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0  | 2/2015  | /<br>(-)<br>[0/0]              | 616.36<br>(-)<br>[616.36]      | 68.58<br>(0.00)<br>[0]     |
| 1021 | 4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600                                  | 11/2015 | /<br>(-)<br>[0/0]              | 847.02<br>(-)<br>[847.02]      | 299.81<br>(0.00)<br>[0]    |
| 1022 | 4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00                                 | 11/2015 | /<br>(-)<br>[0/0]              | 889.24<br>(-)<br>[889.24]      | 389.64<br>(0.00)<br>[0]    |
| 1023 | 4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)   | 8/2016  | 9/2019<br>(-)<br>[9/2019]      | 1,388.34<br>(-)<br>[1,388.34]  | 595.70<br>(0.00)<br>[0]    |
| 1024 | CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15( | 3/2015  | /<br>(-)<br>[0/0]              | 312.79<br>(-)<br>[312.79]      | 17.57<br>(0.00)<br>[0]     |
| 1025 | CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOLA BYPASS(EXISTING KM.138.030 TO K  | 7/2014  | /<br>(-)<br>[0/0]              | 319.80<br>(-)<br>[319.80]      | 102.55<br>(0.00)<br>[0]    |

|      |                                                                                                      |         |                                  |                                 |                             |
|------|------------------------------------------------------------------------------------------------------|---------|----------------------------------|---------------------------------|-----------------------------|
| 1026 | CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN | 3/2017  | 3/2020<br>(-)<br>[4/2020]        | 754.54<br>(-)<br>[756.27]       | 30.30<br>(1.73)<br>[1]      |
| 1027 | DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS | 12/2015 | /<br>(-)<br>[0/0]                | 766.36<br>(-)<br>[766.36]       | 99.86<br>(0.00)<br>[0]      |
| 1028 | DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM  | 12/2015 | /<br>(-)<br>[0/0]                | 578.38<br>(-)<br>[578.38]       | 128.53<br>(0.00)<br>[0]     |
| 1029 | FOUR LANING OF CHANDIGARH - KHARAR                                                                   | 10/2015 | 12/2017<br>(-)<br>[4/2019]       | 447.29<br>(-)<br>[447.29]       | 31.96<br>(0.00)<br>[16]     |
| 1030 | FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB       | 2/2018  | /<br>(-)<br>[0/0]                | 261.76<br>(-)<br>[261.76]       | 0.00<br>(0.00)<br>[0]       |
| 1031 | FOUR LANNING OF LUDHIYANA- TALWANDI SECTION                                                          | 9/2014  | /<br>(-)<br>[3/2019]             | 479.00<br>(-)<br>[479.00]       | 453.09<br>(0.00)<br>[-]     |
| 1032 | IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1     | 9/2015  | /<br>(-)<br>[4/2019]             | 273.06<br>(-)<br>[273.06]       | 28.90<br>(0.00)<br>[-]      |
| 1033 | REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI | 3/2018  | /<br>(-)<br>[1/2020]             | 196.05<br>(-)<br>[196.05]       | 21.93<br>(0.00)<br>[-]      |
| 1034 | REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN | 3/2018  | /<br>(-)<br>[0/0]                | 199.90<br>(-)<br>[199.90]       | 0.00<br>(0.00)<br>[0]       |
| 1035 | REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE | 3/2015  | /<br>(-)<br>[0/0]                | 435.90<br>(-)<br>[435.90]       | 31.02<br>(0.00)<br>[0]      |
| 1036 | WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 | 1/2015  | /<br>(-)<br>[0/0]                | 279.68<br>(-)<br>[279.68]       | 25.28<br>(0.00)<br>[0]      |
| 1037 | WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO | 6/2015  | /<br>(-)<br>[0/0]                | 899.21<br>(-)<br>[899.21]       | 25.08<br>(0.00)<br>[0]      |
| 1038 | WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA | 6/2015  | /<br>(-)<br>[0/0]                | 892.17<br>(-)<br>[892.17]       | 26.92<br>(0.00)<br>[0]      |
|      | <u>Urban Development</u>                                                                             |         |                                  |                                 |                             |
| 1039 | CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB                     | 2/2014  | 5/2017<br>(2/2019)<br>[3/2019]   | 388.00<br>(-)<br>[388.00]       | 395.14<br>(0.00)<br>[22]    |
| 1040 | CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB                                | 1/2018  | 9/2018<br>(-)<br>[9/2018]        | 430.00<br>(-)<br>[430.00]       | 25.56<br>(0.00)<br>[0]      |
| 1041 | CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB                               | 8/2016  | 4/2019<br>(6/2019)<br>[9/2019]   | 294.00<br>(-)<br>[294.00]       | 134.64<br>(0.00)<br>[5]     |
|      | <u>RAJASTHAN</u>                                                                                     |         |                                  |                                 |                             |
|      | <u>Atomic Energy</u>                                                                                 |         |                                  |                                 |                             |
| 1042 | RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)                                                   | 10/2009 | 12/2016<br>(3/2017)<br>[12/2020] | 12,320.00<br>(-)<br>[12,320.00] | 10,138.00<br>(0.00)<br>[48] |
|      | <u>Coal</u>                                                                                          |         |                                  |                                 |                             |
| 1043 | BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)                                                             | 3/2015  | 12/2019<br>(-)<br>[12/2019]      | 513.63<br>(-)<br>[513.63]       | 173.06<br>(0.00)<br>[0]     |
| 1044 | HADLA LIGNITE MINE PROJECT(1.90 MTPA)                                                                | 3/2015  | 9/2019<br>(-)<br>[9/2019]        | 522.45<br>(-)<br>[522.45]       | 8.71<br>(0.00)<br>[0]       |

|      |                                                                   |         |                                  |                                      |                            |
|------|-------------------------------------------------------------------|---------|----------------------------------|--------------------------------------|----------------------------|
|      | <b>Petroleum</b>                                                  |         |                                  |                                      |                            |
| 1045 | 50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II                  | 11/2011 | 3/2013<br>(-)<br>[0/0]           | 310.00<br>(-)<br>[370.00]            | 17.84<br>(60.00)<br>[0]    |
| 1046 | LPG BP PROJECT JODHPUR                                            | 3/2018  | /<br>(-)<br>[0/0]                | 229.80<br>(-)<br>[229.80]            | 69.04<br>(0.00)<br>[0]     |
|      | <b>Power</b>                                                      |         |                                  |                                      |                            |
| 1047 | TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN            | 7/2016  | 1/2019<br>(1/2019)<br>[3/2019]   | 1,429.38<br>(1,429.38)<br>[1,429.38] | 849.56<br>(0.00)<br>[2]    |
| 1048 | TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B         | 7/2015  | 11/2017<br>(10/2018)<br>[1/2019] | 307.18<br>(307.18)<br>[307.18]       | 210.91<br>(0.00)<br>[14]   |
|      | <b>Railways</b>                                                   |         |                                  |                                      |                            |
| 1049 | AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL  | 5/2015  | /<br>(-)<br>[0/0]                | 873.71<br>(-)<br>[1,103.04]          | 2.32<br>(229.33)<br>[0]    |
| 1050 | AJMER-BANGURGRAM                                                  | 4/2011  | 11/2019<br>(-)<br>[11/2019]      | 213.39<br>(-)<br>[244.02]            | 217.81<br>(30.63)<br>[0]   |
| 1051 | AJMER-KOTA (NASIRABAD-JAUNDRI)                                    | 4/2013  | /<br>(-)<br>[0/0]                | 822.00<br>(-)<br>[1,099.54]          | 0.00<br>(277.54)<br>[0]    |
| 1052 | ALWAR-BANDIKUI DOUBLING                                           | 4/2013  | 2/2019<br>(-)<br>[3/2019]        | 242.09<br>(-)<br>[349.00]            | 293.97<br>(106.91)<br>[1]  |
| 1053 | BANGURGRAM-GURIYA PATCH DOUBLING                                  | 4/2012  | 12/2019<br>(-)<br>[6/2019]       | 246.08<br>(-)<br>[348.55]            | 139.09<br>(102.47)<br>[-6] |
| 1054 | DAUSA-GANGAPUR CITY(NL),NWR                                       | 2/1997  | 2/2019<br>(-)<br>[2/2019]        | 410.08<br>(780.98)<br>[795.01]       | 458.50<br>(384.93)<br>[0]  |
| 1055 | HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)                      | 4/2008  | 3/2015<br>(-)<br>[6/2020]        | 829.74<br>(-)<br>[1,216.00]          | 730.74<br>(386.26)<br>[63] |
| 1056 | JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) | 4/2008  | 3/2014<br>(3/2019)<br>[3/2019]   | 653.19<br>(-)<br>[1,116.00]          | 820.02<br>(462.81)<br>[60] |
| 1057 | JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)                  | 8/2018  | 8/2022<br>(-)<br>[8/2022]        | 808.85<br>(-)<br>[808.85]            | 0.00<br>(0.00)<br>[0]      |
| 1058 | MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR       | 4/2013  | 3/2020<br>(-)<br>[12/2019]       | 420.18<br>(295.02)<br>[420.18]       | 89.61<br>(0.00)<br>[-3]    |
| 1059 | MULTI MODAL LOGISTICS PARK AT KATHUWAS                            | 1/2011  | 3/2018<br>(-)<br>[12/2019]       | 493.17<br>(-)<br>[493.17]            | 413.97<br>(0.00)<br>[21]   |
| 1060 | PUSHKAR-MERTA                                                     | 4/2013  | /<br>(-)<br>[0/0]                | 323.00<br>(-)<br>[432.22]            | 0.00<br>(109.22)<br>[0]    |
| 1061 | THIYAT HAMIRA-SANU                                                | 4/2013  | 10/2018<br>(-)<br>[10/2018]      | 236.93<br>(-)<br>[294.90]            | 165.26<br>(57.97)<br>[0]   |
|      | <b>Road Transport And Highways</b>                                |         |                                  |                                      |                            |
| 1062 | 2 LANING WITH PS OF GULABPURA - UNIARA                            | 10/2015 | 10/2017<br>(-)<br>[1/2019]       | 597.00<br>(-)<br>[597.00]            | 604.80<br>(0.00)<br>[15]   |
| 1063 | 2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR                     | 8/2016  | 1/2019<br>(-)<br>[2/2019]        | 320.30<br>(-)<br>[320.30]            | 193.54<br>(0.00)<br>[1]    |



|      |                                                                                                      |         |                                 |                               |                            |
|------|------------------------------------------------------------------------------------------------------|---------|---------------------------------|-------------------------------|----------------------------|
| 1064 | 2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA | 11/2012 | 8/2016<br>(-)<br>[2/2019]       | 530.07<br>(-)<br>[530.07]     | 556.02<br>(0.00)<br>[30]   |
| 1065 | 4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A                                           | 7/2016  | /<br>(-)<br>[11/2019]           | 688.70<br>(-)<br>[688.70]     | 470.78<br>(0.00)<br>[-]    |
| 1066 | 6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- | 12/2016 | /<br>(-)<br>[8/2020]            | 1,031.95<br>(-)<br>[1,031.95] | 367.00<br>(0.00)<br>[-]    |
| 1067 | BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM  | 8/2014  | 4/2018<br>(-)<br>[3/2019]       | 822.90<br>(-)<br>[822.90]     | 688.00<br>(0.00)<br>[11]   |
| 1068 | CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM  | 3/2018  | /<br>(-)<br>[0/0]               | 1,158.35<br>(-)<br>[1,158.35] | 0.00<br>(0.00)<br>[0]      |
| 1069 | CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH.  | 2/2018  | /<br>(-)<br>[0/0]               | 716.76<br>(-)<br>[716.76]     | 0.00<br>(0.00)<br>[0]      |
| 1070 | CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA | 2/2018  | /<br>(-)<br>[0/0]               | 741.86<br>(-)<br>[741.86]     | 0.00<br>(0.00)<br>[0]      |
| 1071 | FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO    | 12/2017 | /<br>(-)<br>[0/0]               | 1,308.73<br>(-)<br>[1,308.73] | 0.00<br>(0.00)<br>[0]      |
| 1072 | FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM   | 6/2016  | 6/2019<br>(-)<br>[11/2019]      | 763.23<br>(-)<br>[763.23]     | 154.91<br>(0.00)<br>[5]    |
| 1073 | FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM                         | 6/2016  | 6/2019<br>(-)<br>[9/2019]       | 649.00<br>(-)<br>[649.00]     | 0.00<br>(0.00)<br>[3]      |
| 1074 | FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540                                  | 10/2017 | 10/2017<br>(-)<br>[0/0]         | 964.17<br>(-)<br>[964.17]     | 0.00<br>(0.00)<br>[0]      |
| 1075 | GURGAON - KOTPUTLI - JAIPUR (SIX LANE)                                                               | 2/2008  | 10/2011<br>(9/2017)<br>[3/2019] | 1,673.70<br>(-)<br>[1,673.70] | 3,326.93<br>(0.00)<br>[89] |
| 1076 | NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING           | 9/2012  | 10/2013<br>(-)<br>[0/0]         | 511.00<br>(-)<br>[511.00]     | 0.00<br>(0.00)<br>[0]      |
| 1077 | NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A | 9/2012  | 10/2013<br>(-)<br>[0/0]         | 511.00<br>(-)<br>[511.00]     | 0.00<br>(0.00)<br>[0]      |
| 1078 | PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS                                        | 9/2015  | 3/2018<br>(-)<br>[1/2019]       | 567.51<br>(-)<br>[567.51]     | 53.70<br>(0.00)<br>[10]    |
| 1079 | REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS                                  | 10/2013 | 5/2014<br>(-)<br>[0/0]          | 278.87<br>(-)<br>[278.87]     | 0.00<br>(0.00)<br>[0]      |
| 1080 | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI  | 1/1991  | 5/2016<br>(-)<br>[0/0]          | 208.87<br>(-)<br>[208.87]     | 206.78<br>(0.00)<br>[0]    |
| 1081 | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI | 1/1991  | 10/2016<br>(-)<br>[0/0]         | 269.26<br>(-)<br>[269.26]     | 212.72<br>(0.00)<br>[0]    |
| 1082 | REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O | 1/1991  | 4/2014<br>(-)<br>[0/0]          | 376.52<br>(-)<br>[376.52]     | 0.00<br>(0.00)<br>[0]      |
| 1083 | SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I | 9/2016  | /<br>(-)<br>[12/2019]           | 1,100.19<br>(-)<br>[1,100.19] | 650.00<br>(0.00)<br>[-]    |
| 1084 | SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD                                                          | 9/2016  | /                               | 1,239.82                      | 668.12                     |

|      |                                                                                                      |         |                             |                               |                              |
|------|------------------------------------------------------------------------------------------------------|---------|-----------------------------|-------------------------------|------------------------------|
|      | SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (                                             |         | (-)<br>[5/2020]             | (-)<br>[1,239.82]             | (0.00)<br>[-]                |
| 1085 | SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV                                             | 4/2017  | 4/2020<br>(-)<br>[11/2019]  | 894.00<br>(-)<br>[894.00]     | 15.00<br>(0.00)<br>[-5]      |
| 1086 | TWO LANING WITH PAVED SHOULDER OF KARAUII - DHOLPUR                                                  | 9/2014  | 9/2016<br>(-)<br>[3/2019]   | 425.19<br>(-)<br>[425.19]     | 274.20<br>(0.00)<br>[30]     |
| 1087 | TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR                                      | 8/2015  | /<br>(-)<br>[3/2019]        | 275.90<br>(-)<br>[275.90]     | 256.10<br>(0.00)<br>[-]      |
| 1088 | TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM  | 7/2016  | 10/2018<br>(-)<br>[11/2018] | 331.46<br>(-)<br>[331.46]     | 248.53<br>(0.00)<br>[0]      |
| 1089 | TWO LANNING WITH PAVED SHOULDER OF SALASAR- NAGLAUR                                                  | 6/2016  | 6/2019<br>(-)<br>[9/2019]   | 637.18<br>(-)<br>[637.18]     | 576.75<br>(0.00)<br>[3]      |
| 1090 | UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE - DANTOUR-JA | 3/2018  | /<br>(-)<br>[0/0]           | 874.25<br>(-)<br>[874.25]     | 0.00<br>(0.00)<br>[0]        |
| 1091 | UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION | 2/2018  | /<br>(-)<br>[0/0]           | 1,103.88<br>(-)<br>[1,103.88] | 0.00<br>(0.00)<br>[0]        |
| 1092 | WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING                  | 10/2014 | 1/2015<br>(-)<br>[0/0]      | 257.09<br>(-)<br>[257.09]     | 14.80<br>(0.00)<br>[0]       |
| 1093 | WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 | 2/2015  | 3/2015<br>(-)<br>[6/2019]   | 383.40<br>(-)<br>[383.40]     | 224.68<br>(0.00)<br>[51]     |
| 1094 | WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K | 10/2014 | 1/2015<br>(-)<br>[0/0]      | 269.22<br>(-)<br>[269.22]     | 33.24<br>(0.00)<br>[0]       |
| 1095 | WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH  | 12/2015 | 6/2018<br>(-)<br>[0/0]      | 621.43<br>(-)<br>[621.43]     | 0.00<br>(0.00)<br>[0]        |
|      | <b>Urban Development</b>                                                                             |         |                             |                               |                              |
| 1096 | CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS | 5/2015  | 3/2017<br>(-)<br>[0/0]      | 189.00<br>(-)<br>[189.00]     | 0.00<br>(0.00)<br>[0]        |
| 1097 | DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN              | 12/2016 | 7/2019<br>(-)<br>[10/2019]  | 549.31<br>(-)<br>[540.42]     | 215.67<br>(-8.89)<br>[3]     |
|      | <b>SIKKIM</b>                                                                                        |         |                             |                               |                              |
|      | <b>Railways</b>                                                                                      |         |                             |                               |                              |
| 1098 | SEVOK RANGPO, NEFR                                                                                   | 4/2008  | 12/2015<br>(-)<br>[3/2020]  | 1,339.48<br>(-)<br>[4,084.69] | 383.92<br>(2,745.21)<br>[51] |
|      | <b>Road Transport And Highways</b>                                                                   |         |                             |                               |                              |
| 1099 | CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM                                      | 1/2013  | 2/2013<br>(-)<br>[0/0]      | 182.28<br>(-)<br>[182.00]     | 24.36<br>(-0.28)<br>[0]      |
| 1100 | CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.                                      | 4/2013  | 8/2013<br>(-)<br>[0/0]      | 151.59<br>(-)<br>[151.59]     | 0.00<br>(0.00)<br>[0]        |
| 1101 | CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.                                   | 4/2013  | 8/2013<br>(-)<br>[0/0]      | 166.27<br>(-)<br>[166.27]     | 0.00<br>(0.00)<br>[0]        |
| 1102 | CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 | 3/2017  | /<br>(-)<br>[0/0]           | 375.80<br>(-)<br>[375.80]     | 0.00<br>(0.00)<br>[0]        |
| 1103 | CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER                                                           | 11/2017 | 11/2017                     | 290.05                        | 18.12                        |

|      |                                                                                                      |         |                                  |                                  |                                 |
|------|------------------------------------------------------------------------------------------------------|---------|----------------------------------|----------------------------------|---------------------------------|
|      | INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5                                            |         | (-)<br>[0/0]                     | (-)<br>[290.05]                  | (0.00)<br>[0]                   |
| 1104 | CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA | 4/2017  | 11/2017<br>(-)<br>[0/0]          | 318.42<br>(-)<br>[318.42]        | 7.50<br>(0.00)<br>[0]           |
| 1105 | CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM | 3/2018  | 6/2018<br>(-)<br>[0/0]           | 264.84<br>(-)<br>[264.84]        | 0.00<br>(0.00)<br>[0]           |
| 1106 | RHENOK-RORATHANG-PAKYONG ON NH 717A                                                                  | 4/2017  | 10/2017<br>(-)<br>[0/0]          | 388.00<br>(-)<br>[447.37]        | 0.00<br>(59.37)<br>[0]          |
|      | <u>TAMIL NADU</u>                                                                                    |         |                                  |                                  |                                 |
|      | <u>Atomic Energy</u>                                                                                 |         |                                  |                                  |                                 |
| 1107 | KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4                                                        | 3/2013  | 11/2020<br>(-)<br>[11/2023]      | 39,849.00<br>(-)<br>[39,849.00]  | 11,815.00<br>(0.00)<br>[36]     |
| 1108 | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)                                                    | 9/2003  | 9/2010<br>(-)<br>[3/2019]        | 3,492.00<br>(-)<br>[6,100.00]    | 5,687.52<br>(2,608.00)<br>[102] |
|      | <u>Coal</u>                                                                                          |         |                                  |                                  |                                 |
| 1109 | EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)                                      | 4/2013  | 6/2015<br>(9/2019)<br>[9/2019]   | 1,458.17<br>(709.06)<br>[709.06] | 399.03<br>(-749.11)<br>[51]     |
| 1110 | NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)                                                          | 6/2011  | 12/2015<br>(12/2018)<br>[3/2019] | 5,907.11<br>(-)<br>[5,907.11]    | 5,828.01<br>(0.00)<br>[39]      |
|      | <u>Mines</u>                                                                                         |         |                                  |                                  |                                 |
| 1111 | 25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU                                                  | 9/2017  | 6/2019<br>(6/2019)<br>[6/2019]   | 166.62<br>(166.62)<br>[166.62]   | 125.00<br>(0.00)<br>[0]         |
|      | <u>Petroleum</u>                                                                                     |         |                                  |                                  |                                 |
| 1112 | AUGMENTATION OF CTMPL                                                                                | 12/2016 | 6/2020<br>(-)<br>[6/2020]        | 228.00<br>(-)<br>[228.00]        | 1.84<br>(0.00)<br>[0]           |
| 1113 | BS-VI PROJECTS                                                                                       | 9/2017  | 12/2019<br>(-)<br>[12/2019]      | 1,858.00<br>(-)<br>[1,858.00]    | 620.25<br>(0.00)<br>[0]         |
| 1114 | CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU                                             | 12/2017 | 10/2020<br>(-)<br>[8/2021]       | 466.43<br>(-)<br>[466.43]        | 1.18<br>(0.00)<br>[10]          |
| 1115 | ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE                   | 5/2016  | 12/2018<br>(-)<br>[12/2020]      | 4,497.00<br>(-)<br>[4,497.00]    | 349.40<br>(0.00)<br>[24]        |
| 1116 | ENNORE-TRICHY-MADURAI LPG PIPELINE                                                                   | 5/2013  | 6/2020<br>(-)<br>[6/2020]        | 711.00<br>(-)<br>[711.00]        | 11.12<br>(0.00)<br>[0]          |
| 1117 | Field Development Plan of Madanam NELP-IV Block CY-ONN-2002                                          | 11/2015 | 3/2019<br>(-)<br>[4/2019]        | 390.52<br>(390.52)<br>[390.52]   | 174.22<br>(0.00)<br>[1]         |
| 1118 | IRUGUR-DEVANGONTHI POL PIPELINE                                                                      | 11/2012 | 2/2017<br>(-)<br>[0/0]           | 678.00<br>(-)<br>[678.00]        | 5.12<br>(0.00)<br>[0]           |
| 1119 | RE-LIQUIFIED NATURAL GAS                                                                             | 8/2017  | 8/2020<br>(-)<br>[8/2020]        | 421.00<br>(-)<br>[421.00]        | 19.68<br>(0.00)<br>[0]          |
| 1120 | RESID UPGRADATION PROJECT                                                                            | 3/2013  | 11/2015<br>(-)<br>[0/0]          | 3,110.36<br>(-)<br>[3,110.36]    | 2,915.42<br>(0.00)<br>[0]       |
|      | <u>Power</u>                                                                                         |         |                                  |                                  |                                 |
| 1121 | COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH                         | 9/2011  | 9/2014<br>(-)                    | 1,940.13<br>(-)                  | 2,529.92<br>(762.52)            |

|      |                                                                                                       |         |                                 |                                      |                               |
|------|-------------------------------------------------------------------------------------------------------|---------|---------------------------------|--------------------------------------|-------------------------------|
|      | POWER(MADRAS) LIMITED L                                                                               |         | [0/0]                           | [2,702.65]                           | [0]                           |
| 1122 | KUNADANKULAM APP TRANS SYSTEM (PGCIL)                                                                 | 5/2005  | 11/2008<br>(9/2018)<br>[3/2019] | 1,779.29<br>(2,187.32)<br>[2,187.32] | 2,092.52<br>(408.03)<br>[124] |
| 1123 | TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY | 5/2017  | 7/2019<br>(7/2019)<br>[7/2019]  | 186.17<br>(186.17)<br>[186.17]       | 63.07<br>(0.00)<br>[0]        |
|      | <b>Railways</b>                                                                                       |         |                                 |                                      |                               |
| 1124 | ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING                                                 | 2/1999  | 3/2018<br>(-)<br>[3/2018]       | 257.00<br>(-)<br>[257.00]            | 0.00<br>(0.00)<br>[0]         |
| 1125 | ATTIPPATTU PUTTUR                                                                                     | 4/2008  | 2/2019<br>(-)<br>[2/2019]       | 151.84<br>(-)<br>[1,105.00]          | 3.34<br>(953.16)<br>[0]       |
| 1126 | CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC                                                       | 4/1998  | /<br>(-)<br>[0/0]               | 271.24<br>(-)<br>[520.00]            | 468.18<br>(248.76)<br>[0]     |
| 1127 | CUDDALORE-SALEM VIA VRIDDHACHALAM GC                                                                  | 4/1999  | /<br>(-)<br>[0/0]               | 198.68<br>(-)<br>[556.64]            | 303.72<br>(357.96)<br>[0]     |
| 1128 | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE                                                     | 9/2006  | /<br>(-)<br>[0/0]               | 343.17<br>(-)<br>[1,065.00]          | 1,049.68<br>(721.83)<br>[0]   |
| 1129 | ERODE-PALANI                                                                                          | 4/2008  | /<br>(-)<br>[0/0]               | 288.57<br>(-)<br>[1,140.00]          | 1.63<br>(851.43)<br>[0]       |
| 1130 | EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP                                                  | 4/2006  | 6/2013<br>(3/2019)<br>[3/2019]  | 495.74<br>(495.74)<br>[734.01]       | 445.91<br>(238.27)<br>[69]    |
| 1131 | KARUR-SALEM(NL),SR                                                                                    | 2/1997  | /<br>(-)<br>[0/0]               | 155.55<br>(-)<br>[920.00]            | 856.94<br>(764.45)<br>[0]     |
| 1132 | MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING                                                     | 2/2015  | 3/2020<br>(-)<br>[3/2020]       | 760.00<br>(-)<br>[1,182.31]          | 0.00<br>(422.31)<br>[0]       |
| 1133 | MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION                                                        | 2/1997  | 3/2015<br>(-)<br>[0/0]          | 458.63<br>(-)<br>[458.63]            | 0.92<br>(0.00)<br>[0]         |
| 1134 | MADURAI-BODINAYAKKANUR                                                                                | 4/2008  | /<br>(-)<br>[3/2020]            | 164.41<br>(-)<br>[450.00]            | 83.15<br>(285.59)<br>[-]      |
| 1135 | MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANNAL ROAD) (62.05 KM) DOUBLING                             | 2/2003  | 3/2009<br>(-)<br>[0/0]          | 199.55<br>(-)<br>[330.32]            | 2.12<br>(130.77)<br>[0]       |
| 1136 | MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION.                                               | 2/2006  | 3/2012<br>(-)<br>[0/0]          | 208.00<br>(-)<br>[208.00]            | 3.58<br>(0.00)<br>[0]         |
| 1137 | MANIYACHI - NAGERCOIL (102 KM) DOUBLING                                                               | 2/2015  | 3/2022<br>(-)<br>[3/2022]       | 1,700.00<br>(-)<br>[1,700.00]        | 0.00<br>(0.00)<br>[0]         |
| 1138 | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI                                       | 9/2007  | 2/2019<br>(-)<br>[2/2019]       | 724.69<br>(-)<br>[2,072.50]          | 1,169.07<br>(1,347.81)<br>[0] |
| 1139 | OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM                                                 | 10/2013 | 4/2014<br>(-)<br>[3/2020]       | 187.26<br>(-)<br>[231.67]            | 7.62<br>(44.41)<br>[71]       |
| 1140 | SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR                          | 4/2013  | /<br>(-)<br>[0/0]               | 839.00<br>(-)<br>[1,500.00]          | 0.61<br>(661.00)<br>[0]       |
| 1141 | THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)                                         | 2/1996  | 3/2005<br>(-)                   | 268.87<br>(-)                        | 304.07<br>(33.15)             |

|      |                                                                                                      |         |           |            |            |
|------|------------------------------------------------------------------------------------------------------|---------|-----------|------------|------------|
|      |                                                                                                      |         | [0/0]     | [302.02]   | [0]        |
| 1142 | TIDIVANAM-NAGARI (NL)                                                                                | 9/2006  | /         | 582.83     | 237.73     |
|      |                                                                                                      |         | (-)       | (-)        | (1,717.17) |
|      |                                                                                                      |         | [0/0]     | [2,300.00] | [0]        |
| 1143 | TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)                                                                | 9/2006  | /         | 227.40     | 61.97      |
|      |                                                                                                      |         | (-)       | (-)        | (672.60)   |
|      |                                                                                                      |         | [0/0]     | [900.00]   | [0]        |
| 1144 | TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)                                             | 2/2017  | 3/2024    | 1,567.00   | 0.00       |
|      |                                                                                                      |         | (-)       | (-)        | (0.00)     |
|      |                                                                                                      |         | [3/2026]  | [1,567.00] | [24]       |
| 1145 | TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION                                                       | 2/2000  | 3/2014    | 200.84     | 394.26     |
|      |                                                                                                      |         | (-)       | (-)        | (0.00)     |
|      |                                                                                                      |         | [0/0]     | [200.84]   | [0]        |
| 1146 | VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION                                                       | 2/2005  | 3/2010    | 600.00     | 671.00     |
|      |                                                                                                      |         | (-)       | (600.00)   | (45.54)    |
|      |                                                                                                      |         | [0/0]     | [645.54]   | [0]        |
|      | <u>Road Transport And Highways</u>                                                                   |         |           |            |            |
| 1147 | 2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI                                                       | 9/2011  | 8/2013    | 485.00     | 406.68     |
|      |                                                                                                      |         | (-)       | (-)        | (0.00)     |
|      |                                                                                                      |         | [12/2018] | [485.00]   | [64]       |
| 1148 | 2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHHTH 170 KM)                                         | 4/2012  | 4/2014    | 624.00     | 350.79     |
|      |                                                                                                      |         | (-)       | (-)        | (0.00)     |
|      |                                                                                                      |         | [12/2019] | [624.00]   | [68]       |
| 1149 | 4-LANNING OF OTTANCHATRAM BYPASS                                                                     | 9/2017  | 9/2017    | 244.27     | 0.00       |
|      |                                                                                                      |         | (-)       | (-)        | (0.00)     |
|      |                                                                                                      |         | [0/0]     | [244.27]   | [0]        |
| 1150 | 4-LANNING OF STHIYATHOPU-CHOLOPURAM                                                                  | 9/2017  | 9/2017    | 1,227.87   | 0.00       |
|      |                                                                                                      |         | (-)       | (-)        | (0.00)     |
|      |                                                                                                      |         | [0/0]     | [1,227.87] | [0]        |
| 1151 | CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT | 3/2015  | 8/2015    | 258.97     | 0.00       |
|      |                                                                                                      |         | (-)       | (-)        | (9.95)     |
|      |                                                                                                      |         | [0/0]     | [268.92]   | [0]        |
| 1152 | CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I-  | 11/2015 | 8/2015    | 154.14     | 0.00       |
|      |                                                                                                      |         | (-)       | (-)        | (0.00)     |
|      |                                                                                                      |         | [0/0]     | [154.14]   | [0]        |
| 1153 | DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY                       | 6/2011  | 6/2013    | 600.00     | 325.55     |
|      |                                                                                                      |         | (-)       | (-)        | (0.00)     |
|      |                                                                                                      |         | [0/0]     | [600.00]   | [0]        |
| 1154 | FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS  | 3/2018  | /         | 1,016.92   | 0.00       |
|      |                                                                                                      |         | (-)       | (-)        | (0.00)     |
|      |                                                                                                      |         | [0/0]     | [1,016.92] | [0]        |
| 1155 | FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120      | 5/2015  | 11/2017   | 1,387.11   | 915.30     |
|      |                                                                                                      |         | (-)       | (-)        | (0.00)     |
|      |                                                                                                      |         | [5/2019]  | [1,387.11] | [18]       |
| 1156 | FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) | 3/2018  | /         | 628.71     | 0.00       |
|      |                                                                                                      |         | (-)       | (-)        | (0.00)     |
|      |                                                                                                      |         | [0/0]     | [628.71]   | [0]        |
| 1157 | FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N | 3/2018  | /         | 2,065.96   | 0.00       |
|      |                                                                                                      |         | (-)       | (-)        | (0.00)     |
|      |                                                                                                      |         | [0/0]     | [2,065.96] | [0]        |
| 1158 | FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU                       | 2/2018  | /         | 1,166.26   | 0.00       |
|      |                                                                                                      |         | (-)       | (-)        | (0.00)     |
|      |                                                                                                      |         | [0/0]     | [1,166.26] | [0]        |
| 1159 | FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH | 3/2016  | 7/2016    | 641.17     | 244.33     |
|      |                                                                                                      |         | (-)       | (-)        | (0.00)     |
|      |                                                                                                      |         | [4/2019]  | [641.17]   | [33]       |
| 1160 | FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 | 3/2018  | /         | 505.35     | 0.00       |
|      |                                                                                                      |         | (-)       | (-)        | (0.00)     |
|      |                                                                                                      |         | [0/0]     | [505.35]   | [0]        |
| 1161 | FOUR LANNING OF CHOLOPURAM-THANJAVUR                                                                 | 8/2017  | 8/2017    | 1,176.37   | 0.00       |
|      |                                                                                                      |         | (-)       | (-)        | (0.00)     |

|      |                                                                                                      |         |                                 |                                 |                                |
|------|------------------------------------------------------------------------------------------------------|---------|---------------------------------|---------------------------------|--------------------------------|
|      |                                                                                                      |         | [0/0]                           | [1,176.37]                      | [0]                            |
| 1162 | FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH | 2/2016  | 8/2018<br>(-)<br>[6/2019]       | 707.82<br>(-)<br>[707.82]       | 208.92<br>(0.00)<br>[10]       |
| 1163 | FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65.  | 3/2017  | 3/2020<br>(-)<br>[3/2020]       | 848.45<br>(-)<br>[848.45]       | 5.00<br>(0.00)<br>[0]          |
| 1164 | FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K | 2/2016  | 7/2018<br>(-)<br>[4/2019]       | 641.17<br>(-)<br>[641.17]       | 259.00<br>(0.00)<br>[9]        |
| 1165 | REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO | 3/2015  | 7/2015<br>(-)<br>[0/0]          | 157.18<br>(162.00)<br>[162.00]  | 0.00<br>(4.82)<br>[0]          |
| 1166 | SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE  | 12/2017 | /<br>(-)<br>[0/0]               | 379.90<br>(-)<br>[379.90]       | 0.00<br>(0.00)<br>[0]          |
| 1167 | SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46                             | 9/2011  | 12/2013<br>(-)<br>[12/2018]     | 1,250.00<br>(-)<br>[1,250.00]   | 1,329.17<br>(0.00)<br>[60]     |
| 1168 | THANJAVUR - PUDUKOTTAI SECTION OF NH-226                                                             | 11/2014 | 11/2016<br>(-)<br>[0/0]         | 563.92<br>(-)<br>[563.92]       | 186.50<br>(0.00)<br>[0]        |
| 1169 | THIRUMAYAM - MANAMADURAI SECTION                                                                     | 7/2014  | 1/2017<br>(-)<br>[0/0]          | 401.11<br>(-)<br>[401.11]       | 273.89<br>(0.00)<br>[0]        |
| 1170 | TRICHY - KARUR                                                                                       | 3/2007  | 7/2008<br>(-)<br>[0/0]          | 516.00<br>(-)<br>[516.00]       | 627.42<br>(0.00)<br>[0]        |
| 1171 | TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS                                                   | 5/2010  | 5/2013<br>(-)<br>[12/2018]      | 374.00<br>(-)<br>[374.00]       | 237.00<br>(0.00)<br>[67]       |
| 1172 | TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N | 3/2018  | /<br>(-)<br>[0/0]               | 633.55<br>(-)<br>[633.55]       | 0.00<br>(0.00)<br>[0]          |
| 1173 | TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR                                                       | 6/2015  | 12/2017<br>(-)<br>[6/2019]      | 563.92<br>(-)<br>[563.92]       | 96.48<br>(0.00)<br>[18]        |
|      | <u>Shipping And Ports</u>                                                                            |         |                                 |                                 |                                |
| 1174 | CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT                                                  | 3/2016  | 12/2017<br>(5/2020)<br>[5/2020] | 600.00<br>(257.90)<br>[257.90]  | 1.45<br>(-342.10)<br>[29]      |
| 1175 | CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED                                               | 2/2015  | 12/2017<br>(3/2018)<br>[0/0]    | 244.50<br>(258.33)<br>[271.56]  | 271.56<br>(27.06)<br>[0]       |
| 1176 | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)                                          | 10/2002 | 3/2006<br>(3/2016)<br>[2/2019]  | 150.00<br>(600.00)<br>[600.00]  | 550.78<br>(450.00)<br>[155]    |
| 1177 | SETHUSAMUDRAM SHIP CHANNEL PROJECT                                                                   | 6/2005  | 10/2008<br>(-)<br>[0/0]         | 2,427.40<br>(-)<br>[2,427.40]   | 831.21<br>(0.00)<br>[0]        |
|      | <u>Urban Development</u>                                                                             |         |                                 |                                 |                                |
| 1178 | C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI   | 12/2015 | 10/2019<br>(-)<br>[10/2019]     | 209.00<br>(-)<br>[209.00]       | 52.00<br>(0.00)<br>[0]         |
| 1179 | CHENNAI METRO RAIL LTD (PHASE 1 EXT)                                                                 | 6/2016  | 3/2018<br>(-)<br>[0/0]          | 3,770.00<br>(-)<br>[3,770.00]   | 0.00<br>(0.00)<br>[0]          |
| 1180 | CHENNAI METRO RAIL LTD (PHASE 1)                                                                     | 2/2009  | 12/2015<br>(-)<br>[0/0]         | 14,600.00<br>(-)<br>[19,058.00] | 16,352.77<br>(4,458.00)<br>[0] |
| 1181 | CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS                                                         | 11/2017 | /                               | 348.77                          | 0.00                           |

|      |                                                       |         |                                  |                                 |                             |
|------|-------------------------------------------------------|---------|----------------------------------|---------------------------------|-----------------------------|
|      | CHENNAI                                               |         | (-)<br>[0/0]                     | (-)<br>[348.77]                 | (0.00)<br>[0]               |
| 1182 | STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM         | 4/2014  | 9/2016<br>(-)<br>[0/0]           | 332.72<br>(-)<br>[342.00]       | 321.13<br>(9.28)<br>[0]     |
|      | <u>TELANGANA</u>                                      |         |                                  |                                 |                             |
|      | <u>Coal</u>                                           |         |                                  |                                 |                             |
| 1183 | KALYANIKHANI 6 INCLINE PROJECT                        | 12/2015 | 3/2020<br>(-)<br>[3/2020]        | 477.65<br>(-)<br>[477.65]       | 0.00<br>(0.00)<br>[0]       |
| 1184 | KOYAGUDEM OPENCASST PROJECT                           | 10/2015 | 3/2018<br>(-)<br>[3/2019]        | 426.79<br>(-)<br>[426.79]       | 0.00<br>(0.00)<br>[12]      |
| 1185 | JALAGAM VENGALA RAO OCP-II                            | 7/2011  | 3/2015<br>(-)<br>[3/2021]        | 447.06<br>(-)<br>[437.51]       | 353.61<br>(-9.55)<br>[72]   |
| 1186 | KAKATIYA LONGWALL                                     | 12/2008 | 12/2012<br>(-)<br>[0/0]          | 453.63<br>(-)<br>[453.63]       | 121.91<br>(0.00)<br>[0]     |
| 1187 | KAKATIYAKHANI OPENCASST III PROJECT PHASE-1           | 3/2017  | 3/2019<br>(-)<br>[3/2019]        | 413.84<br>(-)<br>[413.84]       | 0.00<br>(0.00)<br>[0]       |
| 1188 | KAKATIYAKHANI OPENCASST-2 PROJECT                     | 5/2015  | 3/2019<br>(-)<br>[3/2019]        | 397.09<br>(-)<br>[442.42]       | 79.96<br>(45.33)<br>[0]     |
| 1189 | KALYANIKHANI OPENCASST PROJECT                        | 7/2012  | 7/2016<br>(-)<br>[3/2020]        | 417.33<br>(-)<br>[384.32]       | 146.45<br>(-33.01)<br>[44]  |
| 1190 | KISTARAM OCP                                          | 11/2010 | 3/2015<br>(-)<br>[3/2021]        | 242.29<br>(-)<br>[164.04]       | 12.69<br>(-78.25)<br>[72]   |
| 1191 | MANUGURU OC-II EXTENSION PHASE-II                     | 3/2010  | 3/2012<br>(-)<br>[0/0]           | 181.19<br>(-)<br>[181.19]       | 159.87<br>(0.00)<br>[0]     |
| 1192 | RAMAGUNDAM OC-II EXTENSION                            | 12/2009 | 3/2012<br>(-)<br>[3/2023]        | 418.97<br>(-)<br>[489.62]       | 477.74<br>(70.65)<br>[132]  |
| 1193 | RCE OF INDARAM OCP(1.20 MTPA)                         | 7/2011  | 3/2015<br>(-)<br>[3/2021]        | 162.76<br>(-)<br>[349.28]       | 1.31<br>(186.52)<br>[72]    |
| 1194 | RFR OF MANUGURU OC PROJECT                            | 11/2012 | 3/2016<br>(-)<br>[3/2019]        | 430.45<br>(-)<br>[415.37]       | 160.45<br>(-15.08)<br>[36]  |
| 1195 | RG OC -III EXTENSION (PHASE -II) PROJECT              | 6/2012  | 6/2015<br>(-)<br>[3/2019]        | 365.01<br>(-)<br>[365.01]       | 204.26<br>(0.00)<br>[45]    |
| 1196 | RKP OCP PHASE-I                                       | 3/2010  | 3/2015<br>(-)<br>[3/2019]        | 209.78<br>(-)<br>[209.78]       | 154.21<br>(0.00)<br>[48]    |
| 1197 | SHANTIKHANI LONGWALL PROJ-SCCL                        | 10/2006 | 3/2012<br>(-)<br>[3/2024]        | 249.03<br>(-)<br>[448.86]       | 186.91<br>(199.83)<br>[144] |
|      | <u>Power</u>                                          |         |                                  |                                 |                             |
| 1198 | TELANGANA SUPER THERMAL POWER PROJECT PHASE I         | 1/2016  | 7/2020<br>(10/2020)<br>[10/2020] | 10,598.98<br>(-)<br>[10,598.98] | 3,272.35<br>(0.00)<br>[3]   |
|      | <u>Railways</u>                                       |         |                                  |                                 |                             |
| 1199 | MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD | 4/2012  | 3/2016<br>(3/2017)<br>[12/2020]  | 632.68<br>(-)<br>[816.55]       | 846.22<br>(183.87)<br>[57]  |
| 1200 | DOUBLING OF TRACK BETWEEN GOOTY AND                   | 3/2015  | 3/2021                           | 636.38                          | 169.16                      |

|      |                                                                                                       |         |                  |                      |                   |
|------|-------------------------------------------------------------------------------------------------------|---------|------------------|----------------------|-------------------|
|      | DHARMAVARAM OF SOUTH CENTRAL RAILWAY                                                                  |         | (-)<br>[3/2021]  | (-)<br>[636.38]      | (0.00)<br>[0]     |
| 1201 | KONDAPALLI-KOTHAGUDEM                                                                                 | 4/2013  | /                | 723.00               | 0.00              |
|      |                                                                                                       |         | (-)<br>[0/0]     | (-)<br>[616.08]      | (-106.92)<br>[0]  |
| 1202 | MACHERLA-NALGONDA(NL)(SCR)                                                                            | 7/1998  | /                | 458.25               | 3.69              |
|      |                                                                                                       |         | (-)<br>[0/0]     | (-)<br>[458.26]      | (0.01)<br>[0]     |
| 1203 | MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K  | 4/2017  | 3/2022           | 119.73               | 0.00              |
|      |                                                                                                       |         | (-)<br>[3/2022]  | (185.00)<br>[184.97] | (65.24)<br>[0]    |
| 1204 | MANOHARABAD-KOTHPALL NEW LINE(SCR)                                                                    | 4/2006  | 3/2010           | 1,160.48             | 111.36            |
|      |                                                                                                       |         | (-)<br>[3/2022]  | (-)<br>[1,160.47]    | (-0.01)<br>[144]  |
| 1205 | MANUGURU-RAMAGUNDAM                                                                                   | 4/2013  | /                | 1,112.00             | 0.92              |
|      |                                                                                                       |         | (-)<br>[0/0]     | (-)<br>[2,911.84]    | (1,799.84)<br>[0] |
| 1206 | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)                                                                | 12/1994 | /                | 124.43               | 1,021.82          |
|      |                                                                                                       |         | (-)<br>[3/2017]  | (-)<br>[1,025.00]    | (900.57)<br>[0]   |
| 1207 | SECUNDERABAD-MAHABUBNAGAR DOUBLING                                                                    | 4/2015  | 12/2024          | 773.94               | 412.07            |
|      |                                                                                                       |         | (-)<br>[12/2024] | (-)<br>[773.94]      | (0.00)<br>[0]     |
|      | <u>Road Transport And Highways</u>                                                                    |         |                  |                      |                   |
| 1208 | REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T   | 1/2014  | 3/2016           | 340.00               | 0.00              |
|      |                                                                                                       |         | (-)<br>[0/0]     | (-)<br>[340.00]      | (0.00)<br>[0]     |
| 1209 | 4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9                                                 | 4/2014  | 9/2016           | 1,266.60             | 1,411.79          |
|      |                                                                                                       |         | (-)<br>[6/2019]  | (-)<br>[1,544.00]    | (277.40)<br>[33]  |
| 1210 | CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S  | 3/2011  | 12/2015          | 218.31               | 208.28            |
|      |                                                                                                       |         | (-)<br>[0/0]     | (-)<br>[339.82]      | (121.51)<br>[0]   |
| 1211 | EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM  | 3/2015  | 1/2017           | 153.21               | 0.00              |
|      |                                                                                                       |         | (-)<br>[0/0]     | (-)<br>[153.21]      | (0.00)<br>[0]     |
| 1212 | FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB                                                | 3/2017  | 3/2017           | 4,429.00             | 0.00              |
|      |                                                                                                       |         | (-)<br>[0/0]     | (-)<br>[4,429.00]    | (0.00)<br>[0]     |
| 1213 | FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3  | 3/2018  | /                | 857.62               | 0.00              |
|      |                                                                                                       |         | (-)<br>[0/0]     | (-)<br>[857.62]      | (0.00)<br>[0]     |
| 1214 | FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K  | 3/2018  | /                | 802.65               | 0.00              |
|      |                                                                                                       |         | (-)<br>[0/0]     | (-)<br>[802.65]      | (0.00)<br>[0]     |
| 1215 | FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM   | 3/2018  | /                | 950.63               | 0.00              |
|      |                                                                                                       |         | (-)<br>[0/0]     | (-)<br>[950.63]      | (0.00)<br>[0]     |
| 1216 | FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT  | 3/2018  | /                | 828.29               | 0.00              |
|      |                                                                                                       |         | (-)<br>[0/0]     | (-)<br>[828.29]      | (0.00)<br>[0]     |
| 1217 | FOUR LANING OF YADGIRI - WARANGAL                                                                     | 12/2015 | 11/2018          | 1,423.96             | 514.42            |
|      |                                                                                                       |         | (-)<br>[7/2019]  | (-)<br>[1,423.96]    | (0.00)<br>[8]     |
| 1218 | REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO | 12/2013 | 3/2016           | 158.65               | 103.50            |
|      |                                                                                                       |         | (-)<br>[0/0]     | (-)<br>[158.65]      | (0.00)<br>[0]     |
| 1219 | REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S   | 12/2013 | 3/2016           | 177.18               | 40.51             |
|      |                                                                                                       |         | (-)<br>[0/0]     | (-)<br>[177.18]      | (0.00)<br>[0]     |
| 1220 | REHABILITATION AND UPGRADATION OF NH -565 FROM                                                        | 1/2014  | 3/2016           | 270.00               | 19.84             |



|      |                                                                                                      |         |                                 |                                      |                                |
|------|------------------------------------------------------------------------------------------------------|---------|---------------------------------|--------------------------------------|--------------------------------|
|      | KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT                                                |         | (-)<br>[0/0]                    | (-)<br>[270.00]                      | (0.00)<br>[0]                  |
| 1221 | REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR  | 10/2014 | 2/2017<br>(-)<br>[0/0]          | 295.47<br>(-)<br>[313.27]            | 0.00<br>(17.80)<br>[0]         |
| 1222 | REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO | 10/2014 | 12/2016<br>(-)<br>[0/0]         | 244.30<br>(-)<br>[156.09]            | 0.00<br>(-88.21)<br>[0]        |
| 1223 | YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW    | 12/2013 | 3/2016<br>(-)<br>[0/0]          | 244.08<br>(-)<br>[244.08]            | 38.32<br>(0.00)<br>[0]         |
|      | <u>Urban Development</u>                                                                             |         |                                 |                                      |                                |
| 1224 | ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD              | 10/2016 | 3/2020<br>(-)<br>[3/2020]       | 209.84<br>(-)<br>[209.84]            | 12.71<br>(0.00)<br>[0]         |
|      | <u>TRIPURA</u>                                                                                       |         |                                 |                                      |                                |
|      | <u>Power</u>                                                                                         |         |                                 |                                      |                                |
| 1225 | TRIPURA GAS BASED POWER PROJECT                                                                      | 7/2009  | 7/2013<br>(-)<br>[0/0]          | 421.01<br>(-)<br>[1,078.31]          | 963.23<br>(657.30)<br>[0]      |
|      | <u>Railways</u>                                                                                      |         |                                 |                                      |                                |
| 1226 | AGARTALA SABROOM, NL, NEFR                                                                           | 4/2008  | 3/2014<br>(12/2019)<br>[3/2019] | 1,142.00<br>(3,407.00)<br>[3,407.00] | 3,112.16<br>(2,265.00)<br>[60] |
| 1227 | AGARTALA-AKHAURA NL                                                                                  | 4/2012  | 3/2020<br>(-)<br>[10/2022]      | 569.63<br>(-)<br>[650.00]            | 0.00<br>(80.37)<br>[31]        |
| 1228 | CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA                                                           | 4/1999  | 3/2007<br>(-)<br>[4/2016]       | 895.00<br>(984.97)<br>[1,733.20]     | 1,549.55<br>(838.20)<br>[0]    |
|      | <u>Road Transport And Highways</u>                                                                   |         |                                 |                                      |                                |
| 1229 | 2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S | 10/2014 | 3/2018<br>(-)<br>[0/0]          | 369.00<br>(-)<br>[369.00]            | 246.46<br>(0.00)<br>[0]        |
| 1230 | IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO  | 5/2014  | 4/2017<br>(-)<br>[0/0]          | 497.89<br>(-)<br>[497.89]            | 70.47<br>(0.00)<br>[0]         |
|      | <u>Urban Development</u>                                                                             |         |                                 |                                      |                                |
| 1231 | CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V                                      | 3/2007  | 12/2015<br>(-)<br>[0/0]         | 149.73<br>(173.00)<br>[175.94]       | 178.65<br>(26.21)<br>[0]       |
| 1232 | CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI                                     | 12/2007 | 12/2016<br>(-)<br>[0/0]         | 202.61<br>(227.00)<br>[227.00]       | 199.95<br>(24.39)<br>[0]       |
| 1233 | CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII                                   | 10/2011 | 12/2016<br>(-)<br>[0/0]         | 175.49<br>(206.71)<br>[206.71]       | 141.28<br>(31.22)<br>[0]       |
|      | <u>UTTAR PRADESH</u>                                                                                 |         |                                 |                                      |                                |
|      | <u>Coal</u>                                                                                          |         |                                 |                                      |                                |
| 1234 | KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL)                                    | 6/2011  | 3/2018<br>(-)<br>[3/2019]       | 1,131.28<br>(-)<br>[1,131.28]        | 711.45<br>(0.00)<br>[12]       |
| 1235 | NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW                                                  | 7/2016  | 11/2021<br>(-)<br>[11/2021]     | 17,237.00<br>(-)<br>[17,237.80]      | 4,026.50<br>(0.80)<br>[0]      |
|      | <u>Health And Family Welfare</u>                                                                     |         |                                 |                                      |                                |
| 1236 | ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)                                           | 7/2016  | 4/2020<br>(-)<br>[4/2020]       | 785.00<br>(-)<br>[785.00]            | 39.35<br>(0.00)<br>[0]         |
| 1237 | HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI                                                         | 3/2018  | /                               | 268.84                               | 66.44                          |
|      |                                                                                                      |         | (-)                             | (-)                                  | (0.00)                         |

|      |                                                                                                      |        |                                |                                |                            |
|------|------------------------------------------------------------------------------------------------------|--------|--------------------------------|--------------------------------|----------------------------|
|      |                                                                                                      |        | [4/2020]                       | [268.84]                       | [-]                        |
|      | <u>Petroleum</u>                                                                                     |        |                                |                                |                            |
| 1238 | AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A | 3/2018 | 12/2021<br>(-)<br>[12/2021]    | 676.00<br>(-)<br>[676.00]      | 4.83<br>(0.00)<br>[0]      |
| 1239 | AURAIYA PHULPUR PIPELINE PROJECT                                                                     | 7/2015 | 12/2018<br>(-)<br>[3/2019]     | 1,427.94<br>(-)<br>[800.00]    | 603.92<br>(-627.94)<br>[3] |
| 1240 | BS-VI PROJECT AT MATHURA REFINERY                                                                    | 1/2018 | 9/2019<br>(-)<br>[9/2019]      | 666.64<br>(-)<br>[666.64]      | 223.54<br>(0.00)<br>[0]    |
| 1241 | CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI                                                         | 4/2017 | 4/2022<br>(-)<br>[4/2022]      | 287.49<br>(-)<br>[287.49]      | 102.07<br>(0.00)<br>[0]    |
| 1242 | INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY     | 8/2017 | 8/2020<br>(-)<br>[8/2020]      | 255.40<br>(-)<br>[255.40]      | 0.06<br>(0.00)<br>[0]      |
| 1243 | REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR                  | 8/2017 | 8/2021<br>(-)<br>[11/2021]     | 318.80<br>(-)<br>[318.80]      | 13.93<br>(0.00)<br>[3]     |
|      | <u>Power</u>                                                                                         |        |                                |                                |                            |
| 1244 | DHUKWAN SMALL HYDRO PROJECT                                                                          | 5/2011 | 2/2014<br>(2/2018)<br>[3/2019] | 195.42<br>(294.60)<br>[294.60] | 221.63<br>(99.18)<br>[61]  |
| 1245 | FGUTPP, UNCHAHAH STAGE-IV (1X500 MW)                                                                 | 7/2013 | 12/2016<br>(-)<br>[0/0]        | 3,363.12<br>(-)<br>[3,363.12]  | 2,244.00<br>(0.00)<br>[0]  |
| 1246 | MUNPL-MEJA TPP - JV (2X660 MW)                                                                       | 4/2012 | 12/2016<br>(-)<br>[8/2019]     | 9,750.89<br>(-)<br>[9,750.89]  | 8,798.00<br>(0.00)<br>[32] |
| 1247 | TANDA TPP STAGE-II (2X660 MW)                                                                        | 9/2014 | 3/2019<br>(9/2019)<br>[9/2019] | 9,188.98<br>(-)<br>[9,188.98]  | 5,433.65<br>(0.00)<br>[6]  |
|      | <u>Railways</u>                                                                                      |        |                                |                                |                            |
| 1248 | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR                                                           | 4/1999 | 12/2009<br>(-)<br>[0/0]        | 108.00<br>(-)<br>[432.72]      | 446.52<br>(324.72)<br>[0]  |
| 1249 | ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP                                                                | 3/2013 | /<br>(-)<br>[0/0]              | 307.00<br>(-)<br>[308.00]      | 0.00<br>(1.00)<br>[0]      |
| 1250 | AUNRIHAR - JAUNPUR PATCH DOUBLING .                                                                  | 4/2016 | 1/2022<br>(-)<br>[1/2022]      | 600.00<br>(-)<br>[366.71]      | 0.46<br>(-233.29)<br>[0]   |
| 1251 | AUNRIHAR MANDUADIH GAZIPUR VARANASI UP                                                               | 3/2012 | 8/2018<br>(-)<br>[1/2019]      | 199.75<br>(-)<br>[270.00]      | 263.56<br>(70.25)<br>[5]   |
| 1252 | BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.                                    | 4/2016 | 1/2022<br>(-)<br>[1/2022]      | 1,900.00<br>(-)<br>[1,277.06]  | 0.00<br>(-622.94)<br>[0]   |
| 1253 | BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION                                                       | 3/2012 | 12/2020<br>(-)<br>[3/2021]     | 1,183.25<br>(-)<br>[1,183.25]  | 1,002.84<br>(0.00)<br>[3]  |
| 1254 | BHOJIPUR TANAKPUR VIA PILIBHIT                                                                       | 3/2008 | /<br>(-)<br>[3/2018]           | 195.64<br>(-)<br>[435.00]      | 451.80<br>(239.36)<br>[0]  |
| 1255 | BURHWAL - GONDA - 3RD RUNNING LINE.                                                                  | 4/2016 | /<br>(-)<br>[0/0]              | 602.50<br>(-)<br>[714.34]      | 0.00<br>(111.84)<br>[0]    |
| 1256 | ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT                                         | 2/2008 | 3/2012<br>(-)<br>[0/0]         | 171.10<br>(-)<br>[275.08]      | 141.55<br>(103.98)<br>[0]  |

|      |                                                               |        |                            |                                    |                                 |
|------|---------------------------------------------------------------|--------|----------------------------|------------------------------------|---------------------------------|
| 1257 | ETAH - KASGANJ - NEW LINE                                     | 4/2017 | 4/2017<br>(-)<br>[4/2022]  | 276.90<br>(-)<br>[276.90]          | 0.00<br>(0.00)<br>[60]          |
| 1258 | ETAWAH-MAINPURI (NL),NCR                                      | 4/1997 | 12/2008<br>(-)<br>[0/0]    | 120.00<br>(-)<br>[245.39]          | 210.67<br>(125.39)<br>[0]       |
| 1259 | FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI     | 4/2013 | /<br>(-)<br>[0/0]          | 654.00<br>(-)<br>[654.00]          | 0.00<br>(0.00)<br>[0]           |
| 1260 | GHAZIPUR - AUNRIHAR (40 KM)                                   | 4/2014 | /<br>(-)<br>[0/0]          | 182.92<br>(-)<br>[197.73]          | 0.00<br>(14.81)<br>[0]          |
| 1261 | GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW | 4/1997 | 4/1999<br>(-)<br>[0/0]     | 233.00<br>(-)<br>[318.42]          | 339.23<br>(85.42)<br>[0]        |
| 1262 | INDARA - DOHRIGHAT GAUGE CONVERSION.                          | 4/2016 | 4/2016<br>(-)<br>[1/2022]  | 213.00<br>(-)<br>[213.35]          | 0.55<br>(0.35)<br>[69]          |
| 1263 | JHANSI BINA DOUBLING                                          | 9/2016 | 3/2021<br>(-)<br>[3/2021]  | 2,001.00<br>(-)<br>[2,001.00]      | 0.00<br>(0.00)<br>[0]           |
| 1264 | JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING                  | 3/2018 | 3/2023<br>(-)<br>[3/2023]  | 4,329.53<br>(-)<br>[4,329.53]      | 0.00<br>(0.00)<br>[0]           |
| 1265 | KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP    | 3/2013 | /<br>(-)<br>[0/0]          | 643.00<br>(-)<br>[644.00]          | 0.00<br>(1.00)<br>[0]           |
| 1266 | KARAILA ROAD - SHAKTINAGAR DOUBLING                           | 8/2015 | 3/2019<br>(-)<br>[12/2019] | 528.57<br>(-)<br>[528.57]          | 19.97<br>(0.00)<br>[9]          |
| 1267 | LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC                   | 4/2011 | 3/2019<br>(-)<br>[3/2020]  | 927.01<br>(-)<br>[977.00]          | 983.62<br>(49.99)<br>[12]       |
| 1268 | MANDHANA - BRAHMAWART NEW LINE PROJECT.                       | 4/1997 | 4/1999<br>(-)<br>[3/2019]  | 609.04<br>(1,063.00)<br>[1,807.88] | 1,805.97<br>(1,198.84)<br>[239] |
| 1269 | MATHURA-PLWAL 4TH LINE (80KM)                                 | 4/2015 | 3/2020<br>(-)<br>[3/2020]  | 668.70<br>(668.00)<br>[668.00]     | 0.00<br>(-0.70)<br>[0]          |
| 1270 | MAU-GHAZIPUR-TARIGHAT NEW LINE                                | 4/2015 | 3/2023<br>(-)<br>[12/2024] | 1,765.92<br>(-)<br>[1,765.92]      | 335.37<br>(0.00)<br>[21]        |
| 1271 | MEERUT-MUZAFARNAGAR PATCH DL                                  | 4/2012 | /<br>(-)<br>[0/0]          | 377.44<br>(-)<br>[377.44]          | 182.85<br>(0.00)<br>[0]         |
| 1272 | NANPARA - NEPALGANJ GAUGE CONVERSION.                         | 4/2017 | 4/2017<br>(-)<br>[10/2022] | 150.00<br>(-)<br>[150.00]          | 0.00<br>(0.00)<br>[66]          |
| 1273 | PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE                | 4/2017 | 1/2018<br>(-)<br>[0/0]     | 1,343.00<br>(-)<br>[1,343.00]      | 0.00<br>(0.00)<br>[0]           |
| 1274 | PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION                      | 4/2017 | 4/2017<br>(-)<br>[10/2022] | 622.50<br>(427.00)<br>[426.74]     | 40.34<br>(-195.76)<br>[66]      |
| 1275 | RAMNA - SINGRAULI DOUBLING                                    | 8/2015 | 3/2020<br>(-)<br>[3/2021]  | 2,436.21<br>(-)<br>[2,436.21]      | 291.68<br>(0.00)<br>[12]        |
| 1276 | ROSA-SITAPUR CANTT-BURHWAL DOUBLING                           | 3/2015 | 3/2022<br>(-)<br>[2/2019]  | 1,295.42<br>(-)<br>[1,295.42]      | 99.33<br>(0.00)<br>[-37]        |
| 1277 | SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ                  | 4/2016 | 3/2014                     | 1,177.96                           | 1.54                            |

|      |                                                                                                      |         |                  |                   |                   |
|------|------------------------------------------------------------------------------------------------------|---------|------------------|-------------------|-------------------|
|      | (EXCL. MAU-INDARA) PATCH DOUBLING.                                                                   |         | (-)<br>[4/2021]  | (-)<br>[1,028.95] | (-149.01)<br>[85] |
| 1278 | UNCHAHAH-AMETHI                                                                                      | 4/2012  | /                | 1,229.00          | 4.12              |
|      |                                                                                                      |         | (-)<br>[0/0]     | (-)<br>[380.00]   | (-849.00)<br>[0]  |
| 1279 | UTRATIA-ZAFRABAD, NR (LINE DOUBLING)                                                                 | 4/2006  | 3/2010           | 369.90            | 618.19            |
|      |                                                                                                      |         | (-)<br>[0/0]     | (-)<br>[1,581.53] | (1,211.63)<br>[0] |
| 1280 | VARANASI-MODHOSINGH-ALLAHABAD DOUBLING                                                               | 4/2015  | 3/2022           | 943.60            | 298.09            |
|      |                                                                                                      |         | (-)<br>[12/2024] | (-)<br>[943.60]   | (0.00)<br>[33]    |
|      | <b>Road Transport And Highways</b>                                                                   |         |                  |                   |                   |
| 1281 | 2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125                                | 9/2015  | 9/2016           | 368.73            | 235.41            |
|      |                                                                                                      |         | (-)<br>[0/0]     | (-)<br>[368.73]   | (0.00)<br>[0]     |
| 1282 | 2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE  | 11/2010 | 3/2017           | 305.49            | 0.00              |
|      |                                                                                                      |         | (-)<br>[0/0]     | (-)<br>[305.49]   | (0.00)<br>[0]     |
| 1283 | 2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232                                 | 4/2014  | 1/2016           | 351.34            | 425.99            |
|      |                                                                                                      |         | (-)<br>[0/0]     | (-)<br>[351.34]   | (0.00)<br>[0]     |
| 1284 | 2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI                                                   | 4/2014  | 1/2016           | 495.78            | 608.73            |
|      |                                                                                                      |         | (-)<br>[0/0]     | (-)<br>[495.78]   | (0.00)<br>[0]     |
| 1285 | 2-LANING WITH PS RAIBAREILI TO ALLAHABAD                                                             | 7/2012  | 1/2014           | 291.36            | 442.51            |
|      |                                                                                                      |         | (-)<br>[9/2018]  | (-)<br>[291.36]   | (0.00)<br>[0]     |
| 1286 | 2-LANING WITH PS SITARGANJ BAREILY SECTION                                                           | 6/2014  | 1/2016           | 301.04            | 194.60            |
|      |                                                                                                      |         | (-)<br>[0/0]     | (-)<br>[301.04]   | (0.00)<br>[0]     |
| 1287 | 4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500                                       | 8/2016  | 4/2019           | 2,016.00          | 1,663.22          |
|      |                                                                                                      |         | (-)<br>[11/2019] | (-)<br>[2,016.00] | (0.00)<br>[7]     |
| 1288 | 4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C | 3/2018  | /                | 1,120.57          | 0.00              |
|      |                                                                                                      |         | (-)<br>[0/0]     | (-)<br>[1,120.57] | (0.00)<br>[0]     |
| 1289 | 4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (  | 3/2016  | /                | 1,668.00          | 322.13            |
|      |                                                                                                      |         | (-)<br>[2/2020]  | (-)<br>[1,668.00] | (0.00)<br>[-]     |
| 1290 | 4-LANING OF GHAGHRA BRIDGE TO VARANSI ( PACKAGE -I)                                                  | 12/2015 | 6/2016           | 611.65            | 681.34            |
|      |                                                                                                      |         | (-)<br>[0/0]     | (-)<br>[611.65]   | (0.00)<br>[0]     |
| 1291 | 4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00        | 3/2016  | /                | 1,408.00          | 0.00              |
|      |                                                                                                      |         | (-)<br>[7/2020]  | (-)<br>[1,408.00] | (0.00)<br>[-]     |
| 1292 | 4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00                             | 3/2016  | /                | 1,737.00          | 50.71             |
|      |                                                                                                      |         | (-)<br>[4/2020]  | (-)<br>[1,737.00] | (0.00)<br>[-]     |
| 1293 | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR)      | 3/2016  | /                | 1,404.50          | 193.08            |
|      |                                                                                                      |         | (-)<br>[0/0]     | (-)<br>[1,404.50] | (0.00)<br>[0]     |
| 1294 | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]                 | 3/2016  | 4/2019           | 1,587.49          | 164.42            |
|      |                                                                                                      |         | (-)<br>[4/2019]  | (-)<br>[1,587.49] | (0.00)<br>[0]     |
| 1295 | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU | 3/2016  | /                | 1,396.74          | 153.06            |
|      |                                                                                                      |         | (-)<br>[0/0]     | (-)<br>[1,396.74] | (0.00)<br>[0]     |
| 1296 | 6 LANING OF AGRA - ETAWAH BYPASS                                                                     | 7/2015  | 1/2019           | 1,657.20          | 1,945.00          |
|      |                                                                                                      |         | (-)<br>[1/2019]  | (-)<br>[1,657.20] | (0.00)<br>[0]     |
| 1297 | 6-LANNING OF HANDIA-VARANASI SECTION OF NH-2                                                         | 3/2017  | 3/2020           | 2,064.99          | 1,002.09          |

|      |                                                                                                      |         |                 |                   |                 |
|------|------------------------------------------------------------------------------------------------------|---------|-----------------|-------------------|-----------------|
|      | FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA                                              |         | (-)<br>[3/2020] | (-)<br>[2,447.00] | (382.01)<br>[0] |
| 1298 | ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN | 12/2017 | /               | 207.00            | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[207.00]   | (0.00)<br>[0]   |
| 1299 | ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020                                      | 3/2016  | 4/2019          | 676.73            | 409.11          |
|      |                                                                                                      |         | (-)<br>[4/2019] | (-)<br>[676.73]   | (0.00)<br>[0]   |
| 1300 | ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH                                          | 6/2015  | 3/2018          | 774.57            | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[774.57]   | (0.00)<br>[0]   |
| 1301 | BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150                              | 1/2014  | 10/2016         | 397.04            | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[397.04]   | (0.00)<br>[0]   |
| 1302 | BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43          | 10/2013 | 3/2017          | 317.76            | 15.47           |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[317.76]   | (0.00)<br>[0]   |
| 1303 | BAREILY-SITAPUR (NH-24)                                                                              | 3/2011  | 9/2013          | 1,046.00          | 805.19          |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[1,046.00] | (0.00)<br>[0]   |
| 1304 | CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE)    | 3/2015  | /               | 629.74            | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[629.74]   | (0.00)<br>[0]   |
| 1305 | CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA | 2/2018  | /               | 972.77            | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[972.77]   | (0.00)<br>[0]   |
| 1306 | CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T | 12/2016 | /               | 534.55            | 258.50          |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[534.55]   | (0.00)<br>[0]   |
| 1307 | CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O | 12/2017 | /               | 305.00            | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[305.00]   | (0.00)<br>[0]   |
| 1308 | CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO | 3/2018  | /               | 1,117.84          | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[1,117.84] | (0.00)<br>[0]   |
| 1309 | CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650  | 1/2017  | /               | 450.68            | 328.73          |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[450.68]   | (0.00)<br>[0]   |
| 1310 | CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B                    | 1/2014  | 3/2016          | 282.41            | 0.00            |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[282.41]   | (0.00)<br>[0]   |
| 1311 | DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM                                                       | 1/2016  | 5/2019          | 701.12            | 842.34          |
|      |                                                                                                      |         | (-)<br>[5/2019] | (-)<br>[701.12]   | (0.00)<br>[0]   |
| 1312 | DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM                                | 1/2016  | 6/2019          | 1,081.57          | 795.28          |
|      |                                                                                                      |         | (-)<br>[6/2019] | (-)<br>[1,081.57] | (0.00)<br>[0]   |
| 1313 | DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM   | 12/2017 | /               | 1,232.21          | 637.48          |
|      |                                                                                                      |         | (-)<br>[5/2020] | (-)<br>[1,232.21] | (0.00)<br>[-]   |
| 1314 | DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO | 3/2017  | 3/2020          | 1,989.00          | 842.34          |
|      |                                                                                                      |         | (-)<br>[5/2020] | (-)<br>[1,989.00] | (0.00)<br>[2]   |
| 1315 | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-II)                                      | 9/2015  | 3/2018          | 785.78            | 839.63          |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[785.78]   | (0.00)<br>[0]   |
| 1316 | ETAWAH CHAKERI                                                                                       | 3/2013  | 9/2015          | 1,573.00          | 1,998.25        |
|      |                                                                                                      |         | (-)<br>[0/0]    | (-)<br>[1,573.00] | (0.00)<br>[0]   |
| 1317 | FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER       | 2/2018  | /               | 670.50            | 0.00            |
|      |                                                                                                      |         | (-)             | (-)               | (0.00)          |

|      |                                                                                                      |         |                            |                               |                           |
|------|------------------------------------------------------------------------------------------------------|---------|----------------------------|-------------------------------|---------------------------|
|      | NHDP                                                                                                 |         | [0/0]                      | [670.50]                      | [0]                       |
| 1318 | FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS                                 | 3/2018  | /<br>(-)<br>[0/0]          | 809.07<br>(-)<br>[809.07]     | 0.00<br>(0.00)<br>[0]     |
| 1319 | FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.                             | 3/2018  | /<br>(-)<br>[0/0]          | 925.40<br>(-)<br>[925.40]     | 0.00<br>(0.00)<br>[0]     |
| 1320 | FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)                                                   | 12/2015 | 6/2018<br>(-)<br>[0/0]     | 667.00<br>(-)<br>[667.00]     | 439.40<br>(0.00)<br>[0]   |
| 1321 | FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)                                                  | 6/2016  | 7/2018<br>(-)<br>[0/0]     | 667.00<br>(-)<br>[667.00]     | 374.97<br>(0.00)<br>[0]   |
| 1322 | FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)                                                         | 1/2016  | 6/2018<br>(-)<br>[0/0]     | 1,027.53<br>(-)<br>[1,027.53] | 433.51<br>(0.00)<br>[0]   |
| 1323 | FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)                                                        | 1/2016  | 6/2018<br>(-)<br>[0/0]     | 815.28<br>(-)<br>[815.28]     | 328.63<br>(0.00)<br>[0]   |
| 1324 | FOUR LANING OF VARANASI BYPASS                                                                       | 5/2015  | 5/2017<br>(-)<br>[0/0]     | 261.09<br>(-)<br>[261.09]     | 240.96<br>(0.00)<br>[0]   |
| 1325 | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2  | 3/2017  | 3/2020<br>(-)<br>[11/2020] | 1,373.28<br>(-)<br>[1,373.28] | 0.00<br>(0.00)<br>[8]     |
| 1326 | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C | 3/2017  | 3/2020<br>(-)<br>[8/2020]  | 1,184.71<br>(-)<br>[1,310.00] | 0.00<br>(125.29)<br>[5]   |
| 1327 | FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 | 3/2016  | 4/2019<br>(-)<br>[4/2019]  | 899.00<br>(-)<br>[899.00]     | 351.90<br>(0.00)<br>[0]   |
| 1328 | GHAZIABAD-ALIGARH NH-91                                                                              | 2/2011  | 8/2013<br>(-)<br>[0/0]     | 1,141.00<br>(-)<br>[1,141.00] | 1,948.72<br>(0.00)<br>[0] |
| 1329 | JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93          | 10/2013 | 10/2016<br>(-)<br>[0/0]    | 283.45<br>(-)<br>[283.45]     | 0.00<br>(0.00)<br>[0]     |
| 1330 | MEERUT-BULANDSHAHR                                                                                   | 1/2016  | /<br>(-)<br>[0/0]          | 683.24<br>(-)<br>[683.24]     | 536.60<br>(0.00)<br>[0]   |
| 1331 | REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU | 3/2018  | /<br>(-)<br>[0/0]          | 1,025.80<br>(-)<br>[1,025.80] | 0.00<br>(0.00)<br>[0]     |
| 1332 | REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA | 3/2018  | /<br>(-)<br>[0/0]          | 1,115.28<br>(-)<br>[1,115.28] | 0.00<br>(0.00)<br>[0]     |
| 1333 | RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270                    | 10/2013 | 3/2017<br>(-)<br>[0/0]     | 445.89<br>(-)<br>[445.89]     | 0.00<br>(0.00)<br>[0]     |
| 1334 | SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA | 3/2018  | /<br>(-)<br>[0/0]          | 2,140.93<br>(-)<br>[2,140.93] | 0.00<br>(0.00)<br>[0]     |
| 1335 | SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0                               | 10/2013 | 3/2017<br>(-)<br>[0/0]     | 493.94<br>(-)<br>[493.94]     | 0.00<br>(0.00)<br>[0]     |
| 1336 | STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE          | 10/2014 | 10/2016<br>(-)<br>[0/0]    | 227.74<br>(-)<br>[227.74]     | 0.00<br>(0.00)<br>[0]     |
| 1337 | VARANASI RING ROAD PKG - I                                                                           | 1/2018  | /<br>(-)<br>[0/0]          | 450.77<br>(-)<br>[450.77]     | 0.00<br>(0.00)<br>[0]     |

|      |                                                                                                      |         |                                  |                                      |                                 |
|------|------------------------------------------------------------------------------------------------------|---------|----------------------------------|--------------------------------------|---------------------------------|
| 1338 | WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE)                             | 12/2014 | /<br>(-)<br>[0/0]                | 207.88<br>(-)<br>[207.88]            | 0.00<br>(0.00)<br>[0]           |
| 1339 | WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE)                              | 12/2014 | /<br>(-)<br>[0/0]                | 207.88<br>(-)<br>[207.88]            | 0.00<br>(0.00)<br>[0]           |
| 1340 | WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE                                   | 5/2013  | 8/2015<br>(-)<br>[0/0]           | 164.54<br>(-)<br>[164.54]            | 0.00<br>(0.00)<br>[0]           |
|      | <u>Steel</u>                                                                                         |         |                                  |                                      |                                 |
| 1341 | FORGED WHEEL PLANT                                                                                   | 4/2014  | 9/2018<br>(-)<br>[3/2019]        | 1,682.85<br>(-)<br>[1,682.85]        | 852.10<br>(0.00)<br>[6]         |
|      | <u>Urban Development</u>                                                                             |         |                                  |                                      |                                 |
| 1342 | CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR                                                  | 11/2017 | 3/2020<br>(-)<br>[3/2020]        | 171.72<br>(-)<br>[171.72]            | 0.00<br>(0.00)<br>[0]           |
| 1343 | LUCKNOW METRO RAIL CORPORATION LTD                                                                   | 1/2016  | 3/2019<br>(-)<br>[3/2019]        | 6,928.00<br>(6,928.00)<br>[6,928.00] | 2,536.77<br>(0.00)<br>[0]       |
|      | <u>UTTARAKHAND</u>                                                                                   |         |                                  |                                      |                                 |
|      | <u>Petroleum</u>                                                                                     |         |                                  |                                      |                                 |
| 1344 | SITARGANJ LPG PROJECT                                                                                | 2/2017  | 2/2020<br>(-)<br>[2/2020]        | 160.10<br>(-)<br>[160.10]            | 27.35<br>(0.00)<br>[0]          |
|      | <u>Power</u>                                                                                         |         |                                  |                                      |                                 |
| 1345 | LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW                                                    | 7/2012  | 8/2017<br>(-)<br>[0/0]           | 1,527.00<br>(-)<br>[1,801.07]        | 151.63<br>(274.07)<br>[0]       |
| 1346 | NAITWAR MORI HEP                                                                                     | 10/2017 | 12/2021<br>(-)<br>[12/2021]      | 648.33<br>(-)<br>[648.33]            | 148.40<br>(0.00)<br>[0]         |
| 1347 | TAPOVAN-VISHNUGAD HEP (4X130MW)                                                                      | 11/2006 | 3/2013<br>(12/2020)<br>[12/2020] | 2,978.48<br>(-)<br>[3,846.30]        | 3,775.64<br>(867.82)<br>[93]    |
| 1348 | TEHRI PUMPED STORAGE PLANT(1000MW)                                                                   | 7/2006  | 2/2016<br>(12/2020)<br>[5/2021]  | 1,657.00<br>(2,978.86)<br>[4,401.90] | 2,692.27<br>(2,744.90)<br>[63]  |
| 1349 | VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT                                                           | 8/2008  | 6/2013<br>(-)<br>[12/2021]       | 2,491.58<br>(-)<br>[4,105.30]        | 1,592.11<br>(1,613.72)<br>[102] |
|      | <u>Railways</u>                                                                                      |         |                                  |                                      |                                 |
| 1350 | HARIDWAR-LAKSAR                                                                                      | 4/2012  | /<br>(-)<br>[0/0]                | 219.83<br>(-)<br>[346.63]            | 38.33<br>(126.80)<br>[0]        |
| 1351 | KICHHA-KHATIMA (NL) - NER                                                                            | 4/2003  | /<br>(-)<br>[0/0]                | 142.45<br>(-)<br>[228.40]            | 0.15<br>(85.95)<br>[0]          |
| 1352 | RISHIKESH - KARNAPRAYAG NEW LINE                                                                     | 4/2011  | 12/2024<br>(-)<br>[3/2026]       | 16,216.00<br>(-)<br>[16,216.00]      | 861.35<br>(0.00)<br>[15]        |
|      | <u>Road Transport And Highways</u>                                                                   |         |                                  |                                      |                                 |
| 1353 | 2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI | 3/2018  | 6/2018<br>(-)<br>[0/0]           | 403.36<br>(-)<br>[403.36]            | 0.00<br>(0.00)<br>[0]           |
| 1354 | 2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA  | 3/2018  | 5/2018<br>(-)<br>[0/0]           | 417.24<br>(-)<br>[417.24]            | 0.00<br>(0.00)<br>[0]           |
| 1355 | 4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20                                     | 11/2012 | 7/2018<br>(-)<br>[7/2018]        | 605.84<br>(-)<br>[605.84]            | 722.46<br>(0.00)<br>[0]         |

|      |                                                                                                      |         |                             |                                |                           |
|------|------------------------------------------------------------------------------------------------------|---------|-----------------------------|--------------------------------|---------------------------|
| 1356 | 4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900  | 3/2016  | /<br>(-)<br>[2/2020]        | 1,443.00<br>(-)<br>[1,443.00]  | 122.72<br>(0.00)<br>[-]   |
| 1357 | CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 | 3/2018  | 5/2018<br>(-)<br>[0/0]      | 274.31<br>(-)<br>[274.31]      | 0.00<br>(0.00)<br>[0]     |
| 1358 | CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN | 5/2018  | 5/2020<br>(-)<br>[5/2020]   | 248.00<br>(-)<br>[248.00]      | 0.00<br>(0.00)<br>[0]     |
| 1359 | FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88  | 3/2016  | /<br>(-)<br>[10/2019]       | 720.00<br>(-)<br>[720.00]      | 181.70<br>(0.00)<br>[-]   |
| 1360 | HARIDWAR DEHRADUN APPROVED LENGTH 69                                                                 | 11/2011 | 10/2013<br>(-)<br>[7/2019]  | 478.51<br>(-)<br>[478.00]      | 409.17<br>(-0.51)<br>[69] |
| 1361 | RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG | 11/2017 | 11/2019<br>(-)<br>[11/2019] | 232.81<br>(-)<br>[232.81]      | 48.23<br>(0.00)<br>[0]    |
| 1362 | RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION | 11/2017 | 11/2019<br>(-)<br>[11/2019] | 283.51<br>(-)<br>[284.00]      | 94.50<br>(0.49)<br>[0]    |
| 1363 | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S | 12/2017 | 12/2019<br>(-)<br>[12/2019] | 257.34<br>(-)<br>[257.34]      | 0.00<br>(0.00)<br>[0]     |
| 1364 | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S | 6/2017  | 6/2019<br>(-)<br>[6/2019]   | 282.08<br>(-)<br>[282.08]      | 66.19<br>(0.00)<br>[0]    |
| 1365 | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S | 12/2017 | 12/2019<br>(-)<br>[12/2019] | 200.34<br>(-)<br>[200.34]      | 43.14<br>(0.00)<br>[0]    |
| 1366 | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR    | 2/2018  | 2/2020<br>(-)<br>[2/2020]   | 418.88<br>(-)<br>[418.88]      | 92.42<br>(0.00)<br>[0]    |
| 1367 | RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S | 11/2017 | 11/2019<br>(-)<br>[11/2019] | 266.52<br>(-)<br>[266.52]      | 95.30<br>(0.00)<br>[0]    |
| 1368 | REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K | 2/2018  | /<br>(-)<br>[0/0]           | 293.68<br>(-)<br>[293.68]      | 0.26<br>(0.00)<br>[0]     |
| 1369 | REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 | 3/2018  | /<br>(-)<br>[0/0]           | 460.73<br>(-)<br>[461.00]      | 0.74<br>(0.27)<br>[0]     |
| 1370 | WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 | 12/2017 | 12/2019<br>(-)<br>[12/2019] | 248.22<br>(-)<br>[248.22]      | 57.01<br>(0.00)<br>[0]    |
|      | <u>Urban Development</u>                                                                             |         |                             |                                |                           |
| 1371 | CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA  | 12/2008 | 12/2013<br>(-)<br>[10/2019] | 114.26<br>(266.00)<br>[266.00] | 0.00<br>(151.74)<br>[70]  |
|      | <u>WEST BENGAL</u>                                                                                   |         |                             |                                |                           |
|      | <u>Coal</u>                                                                                          |         |                             |                                |                           |
| 1372 | JHANJRA COMBINED PR(3.50 MTY)                                                                        | 11/2015 | 3/2022<br>(-)<br>[3/2022]   | 602.86<br>(-)<br>[602.86]      | 298.21<br>(0.00)<br>[0]   |
| 1373 | RANIGANJ MASTER PLAN                                                                                 | 8/2009  | 8/2019<br>(-)<br>[0/0]      | 2,661.73<br>(-)<br>[2,661.73]  | 215.14<br>(0.00)<br>[0]   |
| 1374 | SIDULI MINE (OC AND UG)                                                                              | 5/2018  | 3/2026<br>(-)<br>[3/2026]   | 535.18<br>(-)<br>[535.18]      | 0.00<br>(0.00)<br>[0]     |
| 1375 | SONEPUR BAZARI (COMB) OCP (8.0 MTY)                                                                  | 8/2012  | 3/2018                      | 1,055.05                       | 383.30                    |



|      |                                                                                                      |        |                                 |                                      |                                |
|------|------------------------------------------------------------------------------------------------------|--------|---------------------------------|--------------------------------------|--------------------------------|
|      |                                                                                                      |        | (-)<br>[3/2020]                 | (-)<br>[1,055.05]                    | (0.00)<br>[24]                 |
|      | <u>Health And Family Welfare</u>                                                                     |        |                                 |                                      |                                |
| 1376 | CNCI KOLKATA WEST BENGAL                                                                             | 8/2016 | 9/2018<br>(-)<br>[9/2018]       | 244.00<br>(-)<br>[244.00]            | 238.97<br>(0.00)<br>[0]        |
| 1377 | HOSPITAL AND TEACHING- AIIMS KALYANI                                                                 | 4/2018 | /<br>(-)<br>[2/2020]            | 651.99<br>(-)<br>[651.99]            | 43.81<br>(0.00)<br>[-]         |
| 1378 | RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL                                         | 8/2017 | 3/2019<br>(-)<br>[3/2019]       | 355.15<br>(-)<br>[355.15]            | 112.08<br>(0.00)<br>[0]        |
|      | <u>Petroleum</u>                                                                                     |        |                                 |                                      |                                |
| 1379 | 30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL | 3/2018 | 9/2022<br>(-)<br>[6/2021]       | 3,712.00<br>(-)<br>[3,712.00]        | 6.28<br>(0.00)<br>[-15]        |
| 1380 | BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY                                                           | 5/2018 | 9/2019<br>(-)<br>[9/2019]       | 2,934.40<br>(-)<br>[2,934.40]        | 843.32<br>(0.00)<br>[0]        |
| 1381 | DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY                                      | 3/2014 | 9/2017<br>(6/2018)<br>[3/2019]  | 3,076.00<br>(4,190.00)<br>[4,190.00] | 3,224.62<br>(1,114.00)<br>[18] |
| 1382 | DURGAPUR-HALDIA PIPELINE PROJECT                                                                     | 3/2017 | 12/2020<br>(-)<br>[12/2020]     | 1,740.00<br>(-)<br>[1,740.00]        | 22.96<br>(0.00)<br>[0]         |
| 1383 | HALDIA BARAUNI PRODUCT PIPELINE                                                                      | 4/2016 | 12/2020<br>(-)<br>[12/2020]     | 1,021.00<br>(-)<br>[1,021.00]        | 4.45<br>(0.00)<br>[0]          |
| 1384 | HALDIA LPG IMPORT FACILITY                                                                           | 3/2015 | 10/2018<br>(6/2019)<br>[6/2019] | 694.00<br>(1,097.54)<br>[694.00]     | 530.79<br>(0.00)<br>[8]        |
| 1385 | KHARAGPUR LPG BOTTLING PLANT                                                                         | 4/2017 | 4/2020<br>(-)<br>[4/2020]       | 163.02<br>(-)<br>[163.02]            | 32.69<br>(0.00)<br>[0]         |
|      | <u>Power</u>                                                                                         |        |                                 |                                      |                                |
| 1386 | EASTERN REGION STRENGTHENING SCHEME-XV                                                               | 4/2016 | 4/2018<br>(1/2020)<br>[1/2020]  | 454.11<br>(454.11)<br>[454.11]       | 249.92<br>(0.00)<br>[21]       |
| 1387 | RAMMAM-III HEPP (3X40 MW)                                                                            | 9/2014 | 9/2019<br>(2/2022)<br>[2/2022]  | 1,381.84<br>(-)<br>[1,381.84]        | 384.28<br>(0.00)<br>[29]       |
|      | <u>Railways</u>                                                                                      |        |                                 |                                      |                                |
| 1388 | BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL                                            | 4/1998 | 3/2003<br>(3/2030)<br>[3/2030]  | 1,027.40<br>(1,966.70)<br>[2,373.00] | 484.85<br>(1,345.60)<br>[324]  |
| 1389 | BARDHAMAN-KATWA (GC)                                                                                 | 4/2007 | 12/2010<br>(-)<br>[0/0]         | 1,106.62<br>(-)<br>[1,092.20]        | 620.93<br>(-14.42)<br>[0]      |
| 1390 | BAZAR SAU -AZIMGANJ JN. DOUBLING                                                                     | 4/2012 | /<br>(-)<br>[0/0]               | 255.64<br>(-)<br>[272.20]            | 89.78<br>(16.56)<br>[0]        |
| 1391 | BHADUTOLA-JHARGRAM VIA LALGARH (NL)                                                                  | 4/2011 | /<br>(-)<br>[0/0]               | 289.64<br>(-)<br>[760.00]            | 0.13<br>(470.36)<br>[0]        |
| 1392 | BOWAICHANDI-ARAMBAGH                                                                                 | 4/2010 | /<br>(3/2025)<br>[3/2025]       | 267.37<br>(-)<br>[620.00]            | 40.77<br>(352.63)<br>[-]       |
| 1393 | CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR                                               | 4/2009 | /<br>(-)<br>[0/0]               | 573.78<br>(-)<br>[268.52]            | 0.67<br>(-305.26)<br>[0]       |
| 1394 | DAKSHIN-BARASAL-LAKSHMIKANTAPUR                                                                      | 4/2009 | 2/2012                          | 259.51                               | 145.79                         |

|      |                                                                                                  |         |                                   |                                      |                               |
|------|--------------------------------------------------------------------------------------------------|---------|-----------------------------------|--------------------------------------|-------------------------------|
|      |                                                                                                  |         | (-)<br>[0/0]                      | (-)<br>[533.59]                      | (274.08)<br>[0]               |
| 1395 | EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE                                         | 3/2013  | 3/2016<br>(-)<br>[0/0]            | 4,874.58<br>(-)<br>[4,874.58]        | 1,881.65<br>(0.00)<br>[0]     |
| 1396 | GHUTIASHARIF-CANNING (ER)                                                                        | 4/2009  | 12/2011<br>(-)<br>[0/0]           | 193.08<br>(-)<br>[612.45]            | 150.71<br>(419.37)<br>[0]     |
| 1397 | HOWRAH-AMTA-CHAMPADANGA NL (SER)                                                                 | 4/1974  | 3/2007<br>(3/2007)<br>[0/0]       | 393.46<br>(154.30)<br>[1,026.00]     | 182.49<br>(632.54)<br>[0]     |
| 1398 | MM FROM PANSKURA-GHATAL NL                                                                       | 4/2011  | 0/0<br>(3/2030)<br>[3/2030]       | 276.69<br>(-)<br>[426.00]            | 0.00<br>(149.31)<br>[-]       |
| 1399 | NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR                                                         | 4/2010  | /<br>(-)<br>[3/2020]              | 221.42<br>(-)<br>[380.00]            | 101.10<br>(158.58)<br>[-]     |
| 1400 | NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR                          | 4/1983  | 3/2019<br>(-)<br>[3/2020]         | 297.32<br>(200.34)<br>[614.00]       | 270.27<br>(316.68)<br>[12]    |
| 1401 | NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)                                 | 4/2016  | 12/2021<br>(-)<br>[3/2020]        | 602.27<br>(-)<br>[612.00]            | 23.69<br>(9.73)<br>[-21]      |
| 1402 | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) | 4/2010  | 3/2014<br>(-)<br>[12/2025]        | 2,298.42<br>(-)<br>[2,733.86]        | 347.70<br>(435.44)<br>[141]   |
| 1403 | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.                 | 4/2010  | 3/2016<br>(-)<br>[3/2025]         | 2,913.51<br>(4,200.00)<br>[2,913.50] | 885.48<br>(-0.01)<br>[108]    |
| 1404 | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)            | 4/2010  | 3/2016<br>(-)<br>[0/0]            | 2,397.72<br>(-)<br>[2,397.72]        | 197.20<br>(0.00)<br>[0]       |
| 1405 | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)     | 4/2010  | 3/2016<br>(-)<br>[3/2025]         | 3,951.98<br>(-)<br>[4,259.48]        | 1,685.82<br>(307.50)<br>[108] |
| 1406 | TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI   | 1/1991  | 12/2021<br>(12/2021)<br>[12/2021] | 1,013.45<br>(1,013.45)<br>[1,428.00] | 484.49<br>(414.55)<br>[0]     |
| 1407 | TAMLUK DIGHA,LINE DOUBLING (SER)                                                                 | 3/1984  | 6/2005<br>(-)<br>[0/0]            | 293.97<br>(-)<br>[749.69]            | 0.00<br>(455.72)<br>[0]       |
| 1408 | TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER                                                      | 4/2000  | 3/2019<br>(12/2009)<br>[3/2019]   | 1,188.91<br>(-)<br>[1,620.01]        | 844.12<br>(431.10)<br>[0]     |
| 1409 | TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)                  | 3/2000  | 12/2006<br>(-)<br>[0/0]           | 1,049.69<br>(-)<br>[3,404.92]        | 3,544.30<br>(2,355.23)<br>[0] |
|      | <u>Road Transport And Highways</u>                                                               |         |                                   |                                      |                               |
| 1410 | 4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI ( KM 0.00 TO KM . 83.785)                       | 12/2015 | 6/2018<br>(-)<br>[5/2019]         | 1,083.00<br>(-)<br>[1,083.00]        | 155.25<br>(0.00)<br>[11]      |
| 1411 | 4-LANING OF BRAHAMPORE-FARAKA                                                                    | 2/2011  | 8/2013<br>(-)<br>[6/2020]         | 998.79<br>(-)<br>[998.79]            | 1,825.92<br>(0.00)<br>[82]    |
| 1412 | 4-LANING OF FARAKA-RAIGANJ                                                                       | 2/2011  | 8/2013<br>(-)<br>[6/2019]         | 1,078.84<br>(-)<br>[1,078.84]        | 2,312.98<br>(0.00)<br>[70]    |
| 1413 | 6-LANING OF DHANKUNI-KHARAGPUR SECTION                                                           | 4/2012  | 9/2014<br>(-)<br>[5/2019]         | 1,396.18<br>(-)<br>[1,396.18]        | 2,614.84<br>(0.00)<br>[56]    |
| 1414 | CONSTRUCTION OF ISLAMPUR BY PASS                                                                 | 10/2015 | /                                 | 361.15                               | 0.00                          |

|      |                                                                                                      |         |                            |                                                 |                              |
|------|------------------------------------------------------------------------------------------------------|---------|----------------------------|-------------------------------------------------|------------------------------|
|      |                                                                                                      |         | (-)<br>[1/2020]            | (-)<br>[361.15]                                 | (0.00)<br>[-]                |
| 1415 | CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I | 3/2017  | 6/2018<br>(-)<br>[0/0]     | 158.65<br>(-)<br>[158.65]                       | 0.00<br>(0.00)<br>[0]        |
| 1416 | CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA                                                     | 3/2016  | 11/2018<br>(-)<br>[4/2019] | 229.37<br>(-)<br>[229.37]                       | 10.43<br>(0.00)<br>[5]       |
| 1417 | FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA | 9/2016  | 8/2018<br>(-)<br>[9/2019]  | 767.03<br>(-)<br>[767.03]                       | 156.04<br>(0.00)<br>[13]     |
| 1418 | KRISHNANAGAR-BERHAMPUR                                                                               | 2/2012  | 7/2014<br>(-)<br>[5/2019]  | 702.16<br>(-)<br>[702.16]                       | 454.81<br>(0.00)<br>[58]     |
| 1419 | REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) | 3/2018  | /<br>(-)<br>[0/0]          | 1,261.98<br>(-)<br>[1,261.98]                   | 0.00<br>(0.00)<br>[0]        |
| 1420 | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL | 1/1991  | 3/2018<br>(-)<br>[0/0]     | 322.00<br>(-)<br>[322.00]                       | 56.41<br>(0.00)<br>[0]       |
| 1421 | SIX-LANING OF BARWA ADDA-PANAGARH                                                                    | 4/2014  | /<br>(-)<br>[3/2019]       | 1,665.00<br>(-)<br>[1,665.00]                   | 1,836.44<br>(0.00)<br>[-]    |
|      | <u>Urban Development</u>                                                                             |         |                            |                                                 |                              |
| 1422 | CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA                       | 2/2014  | 8/2016<br>(-)<br>[3/2019]  | 156.57<br>(-)<br>[156.57]                       | 146.40<br>(0.00)<br>[31]     |
| 1423 | CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG | 8/2012  | 3/2016<br>(-)<br>[0/0]     | 185.37<br>(-)<br>[185.37]                       | 178.30<br>(0.00)<br>[0]      |
| 1424 | NSG AT KOLKATA                                                                                       | 10/2014 | 4/2018<br>(-)<br>[7/2019]  | 162.88<br>(-)<br>[162.88]                       | 96.48<br>(0.00)<br>[15]      |
|      | Total                                                                                                |         |                            | 18,17,469.76<br>(4,57,159.01)<br>[21,33,649.81] | 8,06,997.78<br>(3,16,180.05) |
|      |                                                                                                      |         |                            |                                                 |                              |

## North East Ongoing Project

## Annexure-XX

| Details of Central Sector Projects Costing Rs.150 crore and above (as on |                                                                                                        |                                 |                                                                       |                                                   | 31.12.2018 )                                                                               |
|--------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------|---------------------------------|-----------------------------------------------------------------------|---------------------------------------------------|--------------------------------------------------------------------------------------------|
| Sl.No                                                                    | Project                                                                                                | Date of Approval (month / year) | Original (Revised) [Anticipated] Date of Commissioning (month / year) | Original (Revised) [Anticipated] Cost (Rs. crore) | Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [ Time Overrun in months ] |
|                                                                          | <u>ARUNACHAL PRADESH</u>                                                                               |                                 |                                                                       |                                                   |                                                                                            |
|                                                                          | <u>Petroleum</u>                                                                                       |                                 |                                                                       |                                                   |                                                                                            |
| 1                                                                        | RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUMKH                                                 | 1/2016                          | 2/2019<br>(-)<br>[1/2019]                                             | 247.52<br>(-)<br>[247.52]                         | 144.38<br>(0.00)<br>[-1]                                                                   |
|                                                                          | <u>Power</u>                                                                                           |                                 |                                                                       |                                                   |                                                                                            |
| 2                                                                        | KAMENG HYDROELECTRIC PROJECT (NEEPCO)                                                                  | 12/2004                         | 12/2009<br>(3/2019)<br>[3/2019]                                       | 2,496.90<br>(6,179.96)<br>[6,179.96]              | 6,881.48<br>(3,683.06)<br>[111]                                                            |
| 3                                                                        | SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)                                                                | 9/2003                          | 9/2010<br>(-)<br>[0/0]                                                | 6,285.33<br>(-)<br>[19,496.34]                    | 10,421.62<br>(13,211.01)<br>[0]                                                            |
|                                                                          | <u>Road Transport And Highways</u>                                                                     |                                 |                                                                       |                                                   |                                                                                            |
| 4                                                                        | 2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH               | 3/2015                          | 6/2018<br>(-)<br>[0/0]                                                | 394.00<br>(-)<br>[394.00]                         | 0.00<br>(0.00)<br>[0]                                                                      |
| 5                                                                        | 2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28                                  | 3/2015                          | 5/2018<br>(-)<br>[0/0]                                                | 235.08<br>(-)<br>[235.08]                         | 47.81<br>(0.00)<br>[0]                                                                     |
| 6                                                                        | 2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59)  | 3/2015                          | 5/2018<br>(-)<br>[0/0]                                                | 194.11<br>(-)<br>[194.11]                         | 30.54<br>(0.00)<br>[0]                                                                     |
| 7                                                                        | 2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS                               | 10/2015                         | 1/2019<br>(-)<br>[1/2019]                                             | 179.82<br>(-)<br>[179.82]                         | 8.99<br>(0.00)<br>[0]                                                                      |
| 8                                                                        | 2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450) | 1/2016                          | 11/2016<br>(-)<br>[0/0]                                               | 183.65<br>(-)<br>[183.65]                         | 0.00<br>(0.00)<br>[0]                                                                      |
| 9                                                                        | CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120                                  | 12/2016                         | 1/2017<br>(-)<br>[1/2020]                                             | 138.93<br>(155.00)<br>[155.00]                    | 0.00<br>(16.07)<br>[36]                                                                    |
| 10                                                                       | CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD( NEAR ITHUN BRIDGE) TO KM 37   | 4/2016                          | /<br>(-)<br>[0/0]                                                     | 245.79<br>(-)<br>[245.79]                         | 0.00<br>(0.00)<br>[0]                                                                      |
| 11                                                                       | CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.    | 4/2016                          | 10/2016<br>(-)<br>[0/0]                                               | 198.00<br>(-)<br>[198.00]                         | 0.00<br>(0.00)<br>[0]                                                                      |
| 12                                                                       | CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH   | 7/2015                          | 10/2018<br>(-)<br>[0/0]                                               | 197.16<br>(-)<br>[197.16]                         | 38.50<br>(0.00)<br>[0]                                                                     |
| 13                                                                       | CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN       | 1/2017                          | 3/2017<br>(-)<br>[0/0]                                                | 1,253.10<br>(-)<br>[1,253.10]                     | 0.00<br>(0.00)<br>[0]                                                                      |
| 14                                                                       | CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI   | 2/2017                          | 4/2017<br>(-)<br>[0/0]                                                | 167.28<br>(-)<br>[167.28]                         | 0.00<br>(0.00)<br>[0]                                                                      |
| 15                                                                       | CONSTRUCTION OF TWOLANE WITH PAVED                                                                     | 2/2017                          | 4/2017                                                                | 216.71                                            | 0.00                                                                                       |

|    |                                                                                                      |         |                    |                      |                      |
|----|------------------------------------------------------------------------------------------------------|---------|--------------------|----------------------|----------------------|
|    | SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS                                    |         | (-)<br>[0/0]       | (-)<br>[216.71]      | (0.00)<br>[0]        |
| 16 | FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K | 3/2018  | /                  | 392.60               | 0.00                 |
|    |                                                                                                      |         | (-)<br>[0/0]       | (-)<br>[392.60]      | (0.00)<br>[0]        |
| 17 | FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A'  | 1/2011  | /                  | 264.16               | 0.00                 |
|    |                                                                                                      |         | (-)<br>[0/0]       | (-)<br>[264.16]      | (0.00)<br>[0]        |
| 18 | FUNDED ) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE | 1/2016  | 6/2016             | 334.22               | 0.00                 |
|    |                                                                                                      |         | (-)<br>[0/0]       | (-)<br>[334.22]      | (0.00)<br>[0]        |
| 19 | FUNDED ) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH | 11/2015 | /                  | 434.06               | 0.00                 |
|    |                                                                                                      |         | (-)<br>[0/0]       | (-)<br>[434.06]      | (0.00)<br>[0]        |
| 20 | TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM | 3/2017  | 4/2017             | 284.09               | 0.00                 |
|    |                                                                                                      |         | (-)<br>[0/0]       | (-)<br>[284.09]      | (0.00)<br>[0]        |
| 21 | TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 | 2/2017  | 4/2017             | 195.23               | 0.00                 |
|    |                                                                                                      |         | (-)<br>[0/0]       | (-)<br>[195.23]      | (0.00)<br>[0]        |
| 22 | TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST | 2/2017  | 4/2017             | 203.36               | 0.00                 |
|    |                                                                                                      |         | (-)<br>[0/0]       | (-)<br>[203.36]      | (0.00)<br>[0]        |
| 23 | TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.  | 1/2017  | 4/2017             | 194.66               | 0.00                 |
|    |                                                                                                      |         | (-)<br>[0/0]       | (-)<br>[194.66]      | (0.00)<br>[0]        |
| 24 | TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.  | 1/2017  | 4/2017             | 198.22               | 0.00                 |
|    |                                                                                                      |         | (-)<br>[0/0]       | (-)<br>[198.22]      | (0.00)<br>[0]        |
| 25 | TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR | 3/2012  | 5/2012             | 207.03               | 0.00                 |
|    |                                                                                                      |         | (-)<br>[0/0]       | (-)<br>[207.03]      | (0.00)<br>[0]        |
| 26 | TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA | 12/2009 | 9/2010             | 165.00               | 0.00                 |
|    |                                                                                                      |         | (-)<br>[0/0]       | (-)<br>[165.00]      | (0.00)<br>[0]        |
| 27 | TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX  | 2/2017  | 4/2017             | 180.57               | 0.00                 |
|    |                                                                                                      |         | (-)<br>[0/0]       | (-)<br>[180.57]      | (0.00)<br>[0]        |
| 28 | TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS  | 2/2017  | 4/2017             | 168.32               | 0.00                 |
|    |                                                                                                      |         | (-)<br>[0/0]       | (-)<br>[168.32]      | (0.00)<br>[0]        |
| 29 | TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA | 12/2011 | 2/2012             | 156.63               | 132.21               |
|    |                                                                                                      |         | (-)<br>[0/0]       | (276.00)<br>[276.00] | (119.37)<br>[0]      |
| 30 | TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P | 11/2010 | 3/2011             | 305.49               | 0.00                 |
|    |                                                                                                      |         | (-)<br>[0/0]       | (-)<br>[305.49]      | (0.00)<br>[0]        |
| 31 | TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF | 12/2009 | 9/2010             | 104.00               | 0.00                 |
|    |                                                                                                      |         | (-)<br>[0/0]       | (-)<br>[201.00]      | (97.00)<br>[0]       |
|    | <b>ASSAM</b>                                                                                         |         |                    |                      |                      |
|    | <b>Health And Family Welfare</b>                                                                     |         |                    |                      |                      |
| 32 | ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM                                            | 5/2017  | 5/2021             | 875.00               | 174.00               |
|    |                                                                                                      |         | (-)<br>[5/2021]    | (-)<br>[875.00]      | (0.00)<br>[0]        |
| 33 | LGBRIMH-TEZPUR, ASSAM                                                                                | 7/2012  | 12/2014            | 175.57               | 113.50               |
|    |                                                                                                      |         | (-)<br>[0/0]       | (-)<br>[175.57]      | (0.00)<br>[0]        |
|    | <b>Petroleum</b>                                                                                     |         |                    |                      |                      |
| 34 | ASSAM RENEWAL PROJECT FOR GROUP A                                                                    | 3/2009  | 3/2013<br>(3/2019) | 2,465.15<br>(-)      | 2,107.69<br>(-86.29) |

|    |                                                                                                      |         |                                  |                                      |                                |
|----|------------------------------------------------------------------------------------------------------|---------|----------------------------------|--------------------------------------|--------------------------------|
|    |                                                                                                      |         | [3/2019]                         | [2,378.86]                           | [72]                           |
| 35 | BS VI PROJECT AT GUWAHATI REFINERY                                                                   | 8/2018  | 2/2020<br>(-)<br>[2/2020]        | 557.00<br>(-)<br>[557.00]            | 71.41<br>(0.00)<br>[0]         |
| 36 | BS-VI PROJECT AT BONGAIGAON REFINERY                                                                 | 5/2018  | 9/2019<br>(-)<br>[9/2019]        | 1,222.00<br>(-)<br>[1,222.00]        | 287.90<br>(0.00)<br>[0]        |
| 37 | CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN                                                   | 7/2011  | 1/2019<br>(-)<br>[9/2019]        | 350.00<br>(-)<br>[350.00]            | 2.06<br>(0.00)<br>[8]          |
| 38 | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)                               | 6/2010  | 1/2014<br>(11/2019)<br>[11/2019] | 202.94<br>(341.70)<br>[330.35]       | 81.98<br>(127.41)<br>[70]      |
| 39 | DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT   | 6/2016  | 8/2019<br>(-)<br>[8/2019]        | 423.00<br>(-)<br>[423.00]            | 217.07<br>(0.00)<br>[0]        |
| 40 | DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA | 1/2018  | 2/2020<br>(-)<br>[2/2020]        | 543.91<br>(-)<br>[543.91]            | 1.65<br>(0.00)<br>[0]          |
| 41 | INDMAX PROJECT AT BONGAIGAON REFINERY                                                                | 2/2016  | 11/2019<br>(-)<br>[11/2019]      | 2,582.00<br>(-)<br>[2,582.00]        | 1,281.75<br>(0.00)<br>[0]      |
| 42 | PIPELINE NETWORK PROJECT GELEKI, ASSAM                                                               | 7/2016  | 5/2020<br>(5/2020)<br>[5/2020]   | 249.85<br>(249.85)<br>[244.70]       | 101.71<br>(-5.15)<br>[0]       |
| 43 | UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE               | 9/2012  | 3/2015<br>(-)<br>[0/0]           | 871.35<br>(-)<br>[1,200.00]          | 565.63<br>(328.65)<br>[0]      |
|    | <u>Power</u>                                                                                         |         |                                  |                                      |                                |
| 44 | BONGAIGAON THERMAL POWER PROJECT                                                                     | 1/2008  | 9/2011<br>(6/2018)<br>[1/2019]   | 4,375.35<br>(8,150.00)<br>[8,150.00] | 7,220.84<br>(3,774.65)<br>[88] |
|    | <u>Railways</u>                                                                                      |         |                                  |                                      |                                |
| 45 | AMBARI FALAKATA TO NEW MAYNAGURI                                                                     | 4/2011  | 3/2019<br>(-)<br>[3/2019]        | 314.00<br>(486.96)<br>[551.00]       | 602.54<br>(237.00)<br>[0]      |
| 46 | BONGAIGAON-GOALPARA-GUWAHATI (176 KM)                                                                | 4/2015  | 3/2022<br>(-)<br>[3/2020]        | 2,232.32<br>(-)<br>[2,182.00]        | 235.52<br>(-50.32)<br>[-24]    |
| 47 | DIGARU-HOJAI (102 KM)                                                                                | 4/2015  | 3/2021<br>(-)<br>[3/2021]        | 870.96<br>(-)<br>[821.00]            | 214.95<br>(-49.96)<br>[0]      |
| 48 | LUMDING-HOJAI PATCH DOUBLING PROJECT                                                                 | 4/2012  | 3/2019<br>(-)<br>[3/2019]        | 246.07<br>(614.81)<br>[398.93]       | 328.77<br>(152.86)<br>[0]      |
| 49 | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR                                      | 9/2006  | 3/2019<br>(-)<br>[3/2020]        | 385.20<br>(-)<br>[1,532.00]          | 574.07<br>(1,146.80)<br>[12]   |
|    | <u>Road Transport And Highways</u>                                                                   |         |                                  |                                      |                                |
| 50 | 2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM               | 11/2010 | 5/2017<br>(-)<br>[0/0]           | 268.08<br>(-)<br>[268.08]            | 0.00<br>(0.00)<br>[0]          |
| 51 | 2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR   | 11/2010 | 2/2011<br>(-)<br>[0/0]           | 470.20<br>(-)<br>[470.20]            | 0.00<br>(0.00)<br>[0]          |
| 52 | 4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS      | 12/2015 | 12/2018<br>(-)<br>[12/2018]      | 225.02<br>(-)<br>[159.20]            | 0.00<br>(-65.82)<br>[0]        |
| 53 | 4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A                | 12/2015 | 6/2018<br>(-)<br>[0/0]           | 223.30<br>(-)<br>[223.30]            | 0.00<br>(0.00)<br>[0]          |

|    |                                                                                                      |         |                             |                           |                             |
|----|------------------------------------------------------------------------------------------------------|---------|-----------------------------|---------------------------|-----------------------------|
| 54 | 4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52                          | 1/1991  | /<br>(-)<br>[0/0]           | 520.01<br>(-)<br>[520.01] | 0.00<br>(0.00)<br>[0]       |
| 55 | 4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL  | 10/2014 | 11/2018<br>(-)<br>[0/0]     | 588.95<br>(-)<br>[588.95] | 80.00<br>(0.00)<br>[0]      |
| 56 | 4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.      | 12/2015 | 12/2018<br>(-)<br>[12/2018] | 289.99<br>(-)<br>[289.99] | 0.00<br>(0.00)<br>[0]       |
| 57 | 4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561   | 1/2016  | 1/2016<br>(-)<br>[0/0]      | 252.00<br>(-)<br>[252.00] | 0.00<br>(0.00)<br>[0]       |
| 58 | 4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) | 6/2015  | 6/2018<br>(-)<br>[0/0]      | 437.39<br>(-)<br>[437.39] | 21.86<br>(0.00)<br>[0]      |
| 59 | 4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O   | 1/2016  | 1/2016<br>(-)<br>[0/0]      | 294.17<br>(-)<br>[294.17] | 0.00<br>(0.00)<br>[0]       |
| 60 | BRAHMPUTRA BRIDGE,NH NO-31                                                                           | 12/2003 | 4/2010<br>(-)<br>[4/2019]   | 217.61<br>(-)<br>[360.84] | 390.19<br>(143.23)<br>[108] |
| 61 | DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)                                                              | 12/2003 | 5/2008<br>(-)<br>[2/2019]   | 160.00<br>(-)<br>[167.98] | 198.82<br>(7.98)<br>[129]   |
| 62 | FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52                      | 6/2016  | 1/2019<br>(-)<br>[1/2019]   | 829.00<br>(-)<br>[829.00] | 59.85<br>(0.00)<br>[0]      |
| 63 | FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A             | 3/2015  | 11/2018<br>(-)<br>[0/0]     | 168.39<br>(-)<br>[168.39] | 16.84<br>(0.00)<br>[0]      |
| 64 | FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 | 6/2015  | 6/2018<br>(-)<br>[0/0]      | 463.49<br>(-)<br>[463.49] | 9.26<br>(0.00)<br>[0]       |
| 65 | FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL | 3/2015  | 1/2016<br>(-)<br>[0/0]      | 829.00<br>(-)<br>[829.00] | 0.00<br>(0.00)<br>[0]       |
| 66 | FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM | 5/2015  | 5/2018<br>(-)<br>[0/0]      | 454.89<br>(-)<br>[454.89] | 22.74<br>(0.00)<br>[0]      |
| 67 | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700                                               | 12/2003 | 2/2009<br>(-)<br>[12/2018]  | 280.00<br>(-)<br>[361.00] | 410.32<br>(81.00)<br>[118]  |
| 68 | HARANGAJO TO MAIBANG, NH-54                                                                          | 12/2003 | 7/2009<br>(-)<br>[0/0]      | 196.00<br>(-)<br>[331.23] | 340.12<br>(135.23)<br>[0]   |
| 69 | MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450                                                 | 12/2003 | 11/2008<br>(-)<br>[0/0]     | 155.04<br>(-)<br>[280.13] | 195.35<br>(125.09)<br>[0]   |
| 70 | MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000                                                  | 12/2003 | 4/2009<br>(-)<br>[3/2019]   | 199.81<br>(-)<br>[385.13] | 209.80<br>(185.32)<br>[119] |
| 71 | MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54                                            | 12/2003 | 11/2008<br>(-)<br>[9/2018]  | 167.64<br>(-)<br>[167.64] | 268.94<br>(0.00)<br>[0]     |
| 72 | NALBARI T BIJNI (AS-7)                                                                               | 12/2003 | 4/2008<br>(-)<br>[3/2019]   | 208.00<br>(-)<br>[230.00] | 297.81<br>(22.00)<br>[131]  |
| 73 | NALBARI TO BIJNI (AS-6)                                                                              | 12/2003 | 6/2008<br>(-)<br>[4/2019]   | 225.00<br>(-)<br>[225.00] | 312.79<br>(0.00)<br>[130]   |
| 74 | SONAPUR TO GUWAHTI (AS-3)                                                                            | 12/2003 | 3/2008                      | 245.00                    | 214.88                      |

|    |                                                                                                      |         |                                  |                                      |                                 |
|----|------------------------------------------------------------------------------------------------------|---------|----------------------------------|--------------------------------------|---------------------------------|
|    |                                                                                                      |         | (-)<br>[1/2019]                  | (174.34)<br>[174.34]                 | (-70.66)<br>[130]               |
| 75 | STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM | 5/2011  | 2/2018<br>(-)<br>[0/0]           | 176.22<br>(-)<br>[176.22]            | 0.00<br>(0.00)<br>[0]           |
| 76 | STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ  | 11/2014 | 2/2018<br>(-)<br>[0/0]           | 218.31<br>(-)<br>[218.31]            | 0.00<br>(0.00)<br>[0]           |
|    | <u>MANIPUR</u>                                                                                       |         |                                  |                                      |                                 |
|    | <u>Railways</u>                                                                                      |         |                                  |                                      |                                 |
| 77 | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)                                                                  | 4/2003  | 3/2011<br>(-)<br>[3/2020]        | 4,454.17<br>(-)<br>[13,809.00]       | 8,304.86<br>(9,354.83)<br>[108] |
|    | <u>Urban Development</u>                                                                             |         |                                  |                                      |                                 |
| 78 | NIT ACADEMIC BUILDING AT IMPHAL MANIPUR                                                              | 2/2014  | 3/2015<br>(-)<br>[11/2019]       | 216.69<br>(-)<br>[216.69]            | 52.00<br>(0.00)<br>[56]         |
|    | <u>MEGHALAYA</u>                                                                                     |         |                                  |                                      |                                 |
|    | <u>Health And Family Welfare</u>                                                                     |         |                                  |                                      |                                 |
| 79 | NEIGRIHMS SHILLONG MEGHALYA                                                                          | 10/2016 | 5/2018<br>(9/2019)<br>[8/2019]   | 363.99<br>(-)<br>[363.99]            | 112.29<br>(0.00)<br>[15]        |
|    | <u>Railways</u>                                                                                      |         |                                  |                                      |                                 |
| 80 | NEW BG LINE FROM BYRNIHAT TO SHILLONG                                                                | 4/2010  | 3/2021<br>(-)<br>[3/2021]        | 906.46<br>(1,202.33)<br>[6,000.00]   | 259.95<br>(5,093.54)<br>[0]     |
|    | <u>Road Transport And Highways</u>                                                                   |         |                                  |                                      |                                 |
| 81 | 2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA    | 12/2010 | 2/2011<br>(-)<br>[0/0]           | 1,494.48<br>(-)<br>[1,494.48]        | 0.00<br>(0.00)<br>[0]           |
| 82 | JORBAT - BARAPANI                                                                                    | 1/2011  | 1/2014<br>(-)<br>[1/2019]        | 536.00<br>(-)<br>[536.00]            | 837.81<br>(0.00)<br>[60]        |
| 83 | TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44                                 | 12/2015 | 5/2018<br>(-)<br>[3/2019]        | 479.20<br>(-)<br>[479.20]            | 14.31<br>(0.00)<br>[10]         |
| 84 | WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T | 4/2017  | /<br>(-)<br>[0/0]                | 553.51<br>(-)<br>[553.51]            | 159.00<br>(0.00)<br>[0]         |
|    | <u>Urban Development</u>                                                                             |         |                                  |                                      |                                 |
| 85 | CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR | 4/2014  | 9/2017<br>(-)<br>[12/2018]       | 151.33<br>(-)<br>[151.33]            | 7.15<br>(0.00)<br>[15]          |
|    | <u>MIZORAM</u>                                                                                       |         |                                  |                                      |                                 |
|    | <u>Railways</u>                                                                                      |         |                                  |                                      |                                 |
| 86 | BHAIRABI SAIRONG, NL, NEFR                                                                           | 4/2008  | 3/2014<br>(12/2020)<br>[12/2020] | 2,393.47<br>(2,393.48)<br>[4,968.00] | 2,516.15<br>(2,574.53)<br>[81]  |
|    | <u>Road Transport And Highways</u>                                                                   |         |                                  |                                      |                                 |
| 87 | CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)                          | 8/2010  | 10/2010<br>(-)<br>[0/0]          | 195.04<br>(-)<br>[195.04]            | 130.82<br>(0.00)<br>[0]         |
| 88 | CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD  | 8/2010  | 10/2010<br>(-)<br>[0/0]          | 193.69<br>(-)<br>[193.69]            | 0.00<br>(0.00)<br>[0]           |
| 89 | WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN  | 11/2010 | 3/2011<br>(-)<br>[0/0]           | 624.41<br>(-)<br>[624.41]            | 0.00<br>(0.00)<br>[0]           |
|    | <u>NAGALAND</u>                                                                                      |         |                                  |                                      |                                 |
|    | <u>Railways</u>                                                                                      |         |                                  |                                      |                                 |
| 90 | DIMAPUR-TIZIT NL                                                                                     | 4/2013  | 3/2020                           | 4,274.00                             | 0.00                            |



|     |                                                                                                            |         |                                  |                                      |                            |
|-----|------------------------------------------------------------------------------------------------------------|---------|----------------------------------|--------------------------------------|----------------------------|
|     |                                                                                                            |         | (-)<br>[3/2020]                  | (-)<br>[4,274.00]                    | (0.00)<br>[0]              |
| 91  | NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA)<br>NATIONAL PROJECT (NEFR)                                          | 4/2006  | 3/2015<br>(10/2021)<br>[10/2021] | 2,326.52<br>(2,446.57)<br>[3,000.00] | 677.37<br>(673.48)<br>[79] |
|     | <b>Road Transport And Highways</b>                                                                         |         |                                  |                                      |                            |
| 92  | CONSTRUCTION OF TWO LANE WITH HARD<br>SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM<br>EXISTING KM 25.760 TO  | 3/2018  | 9/2018<br>(-)<br>[0/0]           | 239.30<br>(-)<br>[239.30]            | 0.00<br>(0.00)<br>[0]      |
| 93  | CONSTRUCTION OF TWO LANE WITH HARD<br>SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM<br>EXISTING KM 52.370 TO  | 3/2018  | 9/2018<br>(-)<br>[0/0]           | 285.68<br>(-)<br>[285.68]            | 0.00<br>(0.00)<br>[0]      |
| 94  | CONSTRUCTION OF TWO LANE WITH HARD<br>SHOULDERS OF PFUTSERO-PHEK ROAD FROM<br>EXISTING KM 40.090 TO KM65.  | 3/2018  | 9/2018<br>(-)<br>[0/0]           | 282.98<br>(-)<br>[282.98]            | 0.00<br>(0.00)<br>[0]      |
| 95  | (I) CONSTRUCTION OF FOUR/SIX LANING FROM KM<br>132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH<br>OF 20. | 2/2017  | 9/2018<br>(-)<br>[0/0]           | 387.00<br>(-)<br>[387.00]            | 0.00<br>(0.00)<br>[0]      |
| 96  | (II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM<br>PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM<br>EXISTING  | 3/2018  | 9/2018<br>(-)<br>[0/0]           | 500.09<br>(-)<br>[500.09]            | 0.00<br>(0.00)<br>[0]      |
| 97  | CONSTRUCTION OF FOUR/ SIX LANING FROM KM<br>132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH<br>OF 20.683 | 2/2017  | 4/2017<br>(-)<br>[0/0]           | 507.68<br>(-)<br>[507.68]            | 0.00<br>(0.00)<br>[0]      |
| 98  | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS<br>OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM<br>00.000 TO  | 3/2018  | 9/2018<br>(-)<br>[0/0]           | 339.57<br>(-)<br>[339.57]            | 0.00<br>(0.00)<br>[0]      |
| 99  | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS<br>OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM<br>79.040 TO  | 3/2018  | 9/2018<br>(-)<br>[0/0]           | 315.03<br>(-)<br>[315.03]            | 0.00<br>(0.00)<br>[0]      |
| 100 | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS<br>OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING<br>KM100.345 TO  | 3/2018  | 9/2018<br>(-)<br>[0/0]           | 240.64<br>(-)<br>[240.64]            | 0.00<br>(0.00)<br>[0]      |
| 101 | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS<br>OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING<br>KM 00.000 TO | 3/2018  | 9/2018<br>(-)<br>[0/0]           | 215.12<br>(-)<br>[215.12]            | 0.00<br>(0.00)<br>[0]      |
| 102 | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS<br>OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING<br>KM 20.456 TO | 3/2018  | 9/2018<br>(-)<br>[0/0]           | 215.79<br>(-)<br>[215.79]            | 0.00<br>(0.00)<br>[0]      |
| 103 | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS<br>OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING<br>KM 41.065 TO | 3/2018  | 9/2018<br>(-)<br>[0/0]           | 272.89<br>(-)<br>[272.89]            | 0.00<br>(0.00)<br>[0]      |
| 104 | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS<br>OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING<br>KM 60.345 TO | 3/2018  | 9/2018<br>(-)<br>[0/0]           | 323.98<br>(-)<br>[323.98]            | 0.00<br>(0.00)<br>[0]      |
| 105 | CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS<br>OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900<br>TO KM40.0 | 3/2018  | 9/2018<br>(-)<br>[0/0]           | 251.97<br>(-)<br>[251.97]            | 0.00<br>(0.00)<br>[0]      |
| 106 | CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS<br>OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000<br>TO KM19.9 | 3/2018  | 9/2018<br>(-)<br>[0/0]           | 237.72<br>(-)<br>[237.72]            | 0.00<br>(0.00)<br>[0]      |
| 107 | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM<br>DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100<br>TO KM 1 | 3/2016  | 8/2016<br>(-)<br>[8/2019]        | 373.07<br>(-)<br>[373.07]            | 0.00<br>(0.00)<br>[36]     |
| 108 | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM<br>DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000<br>TO KM 1 | 3/2016  | 8/2016<br>(-)<br>[8/2019]        | 396.52<br>(-)<br>[396.52]            | 0.00<br>(0.00)<br>[36]     |
| 109 | FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD<br>FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM<br>156.00 | 3/2016  | 8/2016<br>(-)<br>[8/2019]        | 429.52<br>(-)<br>[429.52]            | 0.00<br>(0.00)<br>[36]     |
| 110 | WIDENING OF 2(TWO) LANING OF LONGLENG-                                                                     | 12/2010 | 2/2011                           | 1,296.00                             | 0.00                       |

|     |                                                                                                      |         |                                 |                                      |                                |
|-----|------------------------------------------------------------------------------------------------------|---------|---------------------------------|--------------------------------------|--------------------------------|
|     | CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA                                       |         | (-)<br>[0/0]                    | (-)<br>[1,296.00]                    | (0.00)<br>[0]                  |
|     | <u>SIKKIM</u>                                                                                        |         |                                 |                                      |                                |
|     | <u>Railways</u>                                                                                      |         |                                 |                                      |                                |
| 111 | SEVOK RANGPO, NEFR                                                                                   | 4/2008  | 12/2015<br>(-)<br>[3/2020]      | 1,339.48<br>(-)<br>[4,084.69]        | 383.92<br>(2,745.21)<br>[51]   |
|     | <u>Road Transport And Highways</u>                                                                   |         |                                 |                                      |                                |
| 112 | CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM                                      | 1/2013  | 2/2013<br>(-)<br>[0/0]          | 182.28<br>(-)<br>[182.00]            | 24.36<br>(-0.28)<br>[0]        |
| 113 | CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.                                      | 4/2013  | 8/2013<br>(-)<br>[0/0]          | 151.59<br>(-)<br>[151.59]            | 0.00<br>(0.00)<br>[0]          |
| 114 | CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.                                   | 4/2013  | 8/2013<br>(-)<br>[0/0]          | 166.27<br>(-)<br>[166.27]            | 0.00<br>(0.00)<br>[0]          |
| 115 | CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 | 3/2017  | /<br>(-)<br>[0/0]               | 375.80<br>(-)<br>[375.80]            | 0.00<br>(0.00)<br>[0]          |
| 116 | CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 | 11/2017 | 11/2017<br>(-)<br>[0/0]         | 290.05<br>(-)<br>[290.05]            | 18.12<br>(0.00)<br>[0]         |
| 117 | CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA | 4/2017  | 11/2017<br>(-)<br>[0/0]         | 318.42<br>(-)<br>[318.42]            | 7.50<br>(0.00)<br>[0]          |
| 118 | CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM | 3/2018  | 6/2018<br>(-)<br>[0/0]          | 264.84<br>(-)<br>[264.84]            | 0.00<br>(0.00)<br>[0]          |
| 119 | RHENOK-RORATHANG-PAKYONG ON NH 717A                                                                  | 4/2017  | 10/2017<br>(-)<br>[0/0]         | 388.00<br>(-)<br>[447.37]            | 0.00<br>(59.37)<br>[0]         |
|     | <u>TRIPURA</u>                                                                                       |         |                                 |                                      |                                |
|     | <u>Power</u>                                                                                         |         |                                 |                                      |                                |
| 120 | TRIPURA GAS BASED POWER PROJECT                                                                      | 7/2009  | 7/2013<br>(-)<br>[0/0]          | 421.01<br>(-)<br>[1,078.31]          | 963.23<br>(657.30)<br>[0]      |
|     | <u>Railways</u>                                                                                      |         |                                 |                                      |                                |
| 121 | AGARTALA SABROOM, NL, NEFR                                                                           | 4/2008  | 3/2014<br>(12/2019)<br>[3/2019] | 1,142.00<br>(3,407.00)<br>[3,407.00] | 3,112.16<br>(2,265.00)<br>[60] |
| 122 | AGARTALA-AKHAURA NL                                                                                  | 4/2012  | 3/2020<br>(-)<br>[10/2022]      | 569.63<br>(-)<br>[650.00]            | 0.00<br>(80.37)<br>[31]        |
| 123 | CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA                                                           | 4/1999  | 3/2007<br>(-)<br>[4/2016]       | 895.00<br>(984.97)<br>[1,733.20]     | 1,549.55<br>(838.20)<br>[0]    |
|     | <u>Road Transport And Highways</u>                                                                   |         |                                 |                                      |                                |
| 124 | 2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S | 10/2014 | 3/2018<br>(-)<br>[0/0]          | 369.00<br>(-)<br>[369.00]            | 246.46<br>(0.00)<br>[0]        |
| 125 | IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO  | 5/2014  | 4/2017<br>(-)<br>[0/0]          | 497.89<br>(-)<br>[497.89]            | 70.47<br>(0.00)<br>[0]         |
|     | <u>Urban Development</u>                                                                             |         |                                 |                                      |                                |
| 126 | CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V                                      | 3/2007  | 12/2015<br>(-)<br>[0/0]         | 149.73<br>(173.00)<br>[175.94]       | 178.65<br>(26.21)<br>[0]       |
| 127 | CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI                                     | 12/2007 | 12/2016<br>(-)<br>[0/0]         | 202.61<br>(227.00)<br>[227.00]       | 199.95<br>(24.39)<br>[0]       |

|     |                                                                    |         |                         |                                            |                          |
|-----|--------------------------------------------------------------------|---------|-------------------------|--------------------------------------------|--------------------------|
| 128 | CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII | 10/2011 | 12/2016<br>(-)<br>[0/0] | 175.49<br>(206.71)<br>[206.71]             | 141.28<br>(31.22)<br>[0] |
|     | Total                                                              |         |                         | 78,297.80<br>(27,669.68)<br>[1,25,986.70 ] | 54,905.50<br>(47,688.90) |
|     |                                                                    |         |                         |                                            |                          |
