

**383<sup>rd</sup>**  
**FLASH REPORT**  
**ON**  
**CENTRAL SECTOR PROJECTS**  
**(Rs.150 crore and above)**  
**September 2017**



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



Government of India  
**Ministry of Statistics and Programme Implementation**  
**Infrastructure and Project Monitoring Division**  
Sardar Patel Bhavan, Sansad Marg  
New Delhi-110001  
Website: [www.cspm.gov.in](http://www.cspm.gov.in)

## **Abbreviations used in the report**

|                |                                            |
|----------------|--------------------------------------------|
| <b>AAI</b>     | Airport Authority of India Ltd.            |
| <b>AERB</b>    | Atomic Energy Regulatory Board             |
| <b>AIBP</b>    | Accelerated Irrigation Benefit Programme   |
| <b>AIR</b>     | All India Radio                            |
| <b>APW</b>     | Active Process Water                       |
| <b>ATU</b>     | Atomic Treating Unit                       |
| <b>BCM</b>     | Billion Cubic Meter                        |
| <b>BHEL</b>    | Bharat Heavy Electricals Ltd.              |
| <b>BHPV</b>    | Bharat Heavy Plates & Vessel Ltd.          |
| <b>BLU</b>     | Boiler Light Up                            |
| <b>BOLT</b>    | Build , Operate, Lease & Transfer          |
| <b>BPST</b>    | Bureau of Parliamentary Studies & Training |
| <b>CCEA</b>    | Cabinet Committee on Economic Affairs      |
| <b>CCU</b>     | Catalytic Cracking Unit                    |
| <b>CDS</b>     | Crude Distribution System                  |
| <b>CDU</b>     | Crude Distillation Unit                    |
| <b>CEA</b>     | Central Electricity Authority              |
| <b>CEC</b>     | Central Empowered Committee                |
| <b>CHP</b>     | Coal Handling Plant                        |
| <b>CLW</b>     | Chittaranjan Locomotive Works              |
| <b>CMPDI</b>   | Central Mine Planning & Design Institute   |
| <b>COS</b>     | Committee of Secretaries                   |
| <b>COR</b>     | Cost Overrun                               |
| <b>CPP</b>     | Captive Power Plant                        |
| <b>CRIS</b>    | Centre for Railway Information System      |
| <b>CRL</b>     | Cochin Refinery Ltd.                       |
| <b>CSL</b>     | Cochin Shipyard Ltd.                       |
| <b>CTU</b>     | Crude Topping Unit                         |
| <b>DAE</b>     | Department of Atomic Energy                |
| <b>DB</b>      | Dumb Barges                                |
| <b>DCME</b>    | Digital Circuit Multiplexing Equipment     |
| <b>DGMS</b>    | Director General Mines Safety              |
| <b>DHDS</b>    | Diesel Hydro Desulphurisation project      |
| <b>DOA</b>     | Date of Approval                           |
| <b>DOC</b>     | Date of Commissioning                      |
| <b>DOT</b>     | Department of Telecommunication            |
| <b>DVC</b>     | Damodar Valley Corporation                 |
| <b>ECL</b>     | Eastern Coalfields Ltd.                    |
| <b>EIL</b>     | Engineers India Ltd.                       |
| <b>EMP</b>     | Environment Management Plan                |
| <b>EOT</b>     | Electrical Overhead Travelling crane       |
| <b>ESP</b>     | Electrostatic Precipitator                 |
| <b>FCCU</b>    | Fluidised Catalytic Cracker Unit           |
| <b>ERP</b>     | Enterprise Resource Planning               |
| <b>FE</b>      | Foreign Exchange                           |
| <b>FOIS</b>    | Freight Operation Information System       |
| <b>FPU</b>     | Feed Preparation Unit                      |
| <b>GAIL</b>    | Gas Authority of India Ltd.                |
| <b>GC</b>      | Gauge Conversion                           |
| <b>GDS</b>     | Gateway Digital Switch                     |
| <b>GIS</b>     | Gas Insulated Station                      |
| <b>GT</b>      | Gas Turbine                                |
| <b>GTPP</b>    | Gas Turbine Power Plant                    |
| <b>HCU</b>     | Hydro- cracker Unit                        |
| <b>HEC</b>     | Heavy Engineering Corporation              |
| <b>HEMM</b>    | Heavy Equipment & Mining Machinery         |
| <b>HEP</b>     | Hydro Electric Project                     |
| <b>HPCL</b>    | Hindustan Petroleum Corporation Ltd.       |
| <b>HRT</b>     | Head Race Tunnel                           |
| <b>HSCL</b>    | Hindustan Steel Construction Ltd.          |
| <b>HVDC</b>    | High Voltage Direct Current                |
| <b>IAAI</b>    | International Airport Authority of India   |
| <b>ICT</b>     | Inter Connecting Transformer               |
| <b>IDC</b>     | Interest During construction               |
| <b>IFFCO</b>   | Indian Farmer Fertilizer Co-operative Ltd. |
| <b>IMG</b>     | Inter Ministerial Group                    |
| <b>IOC</b>     | Indian Oil Corporation Ltd.                |
| <b>IPCL</b>    | Indian Petrochemicals Ltd.                 |
| <b>KV</b>      | Kilo Volts.                                |
| <b>L&amp;T</b> | Larsen & Toubro                            |

|                  |                                               |
|------------------|-----------------------------------------------|
| <b>LEP</b>       | Life Extension Program                        |
| <b>LOI</b>       | Letter of Intent                              |
| <b>LPG</b>       | Liquified Petroleum Gas                       |
| <b>LSTK</b>      | Lump sum Turnkey contract                     |
| <b>MAMC</b>      | Minning & Allied Machinery Corporation.       |
| <b>MFL</b>       | Madras Fertilizer Ltd.                        |
| <b>MGCL</b>      | Madras Gas Cracker Complex                    |
| <b>MIS</b>       | Management Information System                 |
| <b>MMSCMD</b>    | Million Metric Standard Cubic Meter day       |
| <b>MMT</b>       | Million Metric Tonnes                         |
| <b>MOE&amp;F</b> | Ministry of Environment & Forest              |
| <b>MT</b>        | Metric Tonnes                                 |
| <b>MTY</b>       | Metric Tonne per year                         |
| <b>MU</b>        | Million Unit                                  |
| <b>MW</b>        | Mega Watts                                    |
| <b>NAC</b>       | New Anticipated Cost                          |
| <b>NALCO</b>     | National Aluminium Company                    |
| <b>NBCC</b>      | National Building Construction Corporation.   |
| <b>NCL</b>       | Northern Coalfields Ltd                       |
| <b>NEC</b>       | North East Council                            |
| <b>NEEPCO</b>    | North-Eastern Electric Power Corporation Ltd. |
| <b>NFL</b>       | National Fertilizer Ltd.                      |
| <b>NH</b>        | National Highway                              |
| <b>NHPC</b>      | National Hydro-Electric Power Corporation     |
| <b>NIRE</b>      | National Institute of Renewable Energy        |
| <b>NIT</b>       | Notice Inviting Tender                        |
| <b>NJPC</b>      | Nathpa Jhakri Power Corporation Ltd.          |
| <b>NGN</b>       | Next Generation Network                       |
| <b>NLC</b>       | Neyveli Lignite Corporation Ltd.              |
| <b>NMDC</b>      | National Mineral Development Corporation Ltd. |
| <b>NPC</b>       | Nuclear Power Corporation Ltd.                |
| <b>NRL</b>       | Numaligarh Refinery Ltd.                      |
| <b>OB</b>        | Over Burden                                   |
| <b>OC</b>        | Opencast                                      |
| <b>OECE</b>      | Overseas Economic Co-operation Fund           |
| <b>ONGC</b>      | Oil & Natural Gas Commission                  |
| <b>OPGC</b>      | Orissa Power Generation Corporation           |
| <b>P &amp; M</b> | Plant & Machinery                             |
| <b>PERT</b>      | Project Evaluation & Review Technique         |
| <b>PSTN</b>      | Public Switched Telephone Network             |
| <b>PHT</b>       | Primary Heat Transport                        |
| <b>PIB</b>       | Public Investment Board                       |
| <b>PSLW</b>      | Powered Support Longwall                      |
| <b>QRC</b>       | Quick Roll Changer                            |
| <b>RAPP</b>      | Rajasthan Atomic Power Plant                  |
| <b>RCE</b>       | Revised Cost Estimates                        |
| <b>RCF</b>       | Railway Coach Factory                         |
| <b>ROB</b>       | Road Over Bridge                              |
| <b>ROH</b>       | Regular Overhauling                           |
| <b>RTU</b>       | Remote Terminal Unit                          |
| <b>SAIL</b>      | Steel Authority of India Ltd.                 |
| <b>SCI</b>       | Shipping Corporation of India Ltd.            |
| <b>SDH</b>       | Synchronous Digital Hierarchy                 |
| <b>SG</b>        | Steam Generator                               |
| <b>SP</b>        | Self Propelled                                |
| <b>ST</b>        | Steam Turbine                                 |
| <b>STPS</b>      | Super Thermal Power Station                   |
| <b>SUR</b>       | Sulphur Recovery Unit                         |
| <b>SWSU</b>      | Sour Water Stripping Unit                     |
| <b>TBM</b>       | Tunnel Boring Machine                         |
| <b>TG</b>        | Turbo Generator                               |
| <b>TPA</b>       | Tonnes Per Annum                              |
| <b>TPS</b>       | Thermal Power Station                         |
| <b>TOR</b>       | Time Overrun                                  |
| <b>TPY</b>       | Tonnes per year                               |
| <b>UG</b>        | Under Ground                                  |
| <b>ULDCS</b>     | Unified Load Despatch & Communication Scheme  |
| <b>VDU</b>       | Vacuum Distillation Unit                      |
| <b>WHRB</b>      | Waste Heat Recovery Boiler                    |
| <b>WO_DOC</b>    | With out Date of Commissioning                |
| <b>WO_ODC</b>    | With out original Date of Commissioning       |

## EXECUTIVE SUMMARY

1. The Flash Report for September 2017 contains information on the status of the 1263 Central Sector Infrastructure Projects costing ₹150 crore and above.

2. The implementation status of **Central Sector Projects (costing Rs 150 crore and above)** may be summarized as below:-

(i). During the reference month, 43 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 43 projects, 13 are **Mega** Projects costing ₹1000 crore and above.

(ii). Total original cost of implementation of the 1263 projects was Rs.15,53,683.89 crore and their anticipated completion cost is likely to be Rs.17,49,427.56 crore, which reflects overall cost overruns of Rs.1,95,743.67 crore (12.60% of original cost). The expenditure incurred on these projects till September 2017 is Rs. 6,79,801.38 crore, which is 38.86% of the anticipated cost of the projects.

(iii). Out of a total of 1263 projects, 11 projects have reported completion and 8 new projects have been initiated on the monitor of this ministry during the current month. Of these, 14 projects are ahead of schedule, 307 are on schedule, 297 are delayed, 350 projects are showing cost overrun and 103 projects are showing both time and cost overrun with respect to original implementation schedules. However, the number of delayed projects decreases to 249 if delay is calculated with reference to latest revised schedules of completion. For 645 projects, where original/anticipated commissioning date has not been reported, all concerned have been requested to provide the original/anticipated commissioning date so that these projects can be monitored for completion vis-a-vis the targeted dates.

(iv). Out of 297 delayed projects, 52 projects have overall delay in the range of 1 to 12 months, 63 projects have delay in the range of 13 to 24 months, 109 projects have delay in the range of 25 to 60 months and 73 projects have delay of 61 months and above.

(v). Further, out of the 297 delayed projects, 103 projects have cost overruns. Out of these, the cost for 51 projects has been revised and for 52 projects the cost has not yet been revised. Of the 51 projects where cost has been revised, the anticipated cost of 8 projects has again exceeded the revised cost. Out of 297 delayed projects, 154 projects have not provided any milestones and in 92 cases the dates of completion of the milestones have already lapsed.

(vi). In addition to above there are 247 projects which though on schedule but are having cost overruns. Of these, the cost for 59 projects has since been revised. Of the 59 projects where cost has been revised, the anticipated cost of 25 projects has exceeded even the revised costs. Out of these 247 projects, 168 projects have not provided any milestones and for 3 projects the completion date of milestone(s) has already lapsed.

(vii). In the current month, there are 287 projects showing time overrun of more than 6 months; 252 projects showing cost overruns of more than Rs.100 crore and 85 projects showing both time overruns of more than 6 months and cost overruns of more than Rs.100 crore. Further, expenditure has exceeded the approved cost in 149 projects and in 924 projects milestones have not been reported. Concerned secretaries have been requested to take a review of these projects to fix time lines and cost estimates.

3. The implementation status of **Central Sector Mega Projects** (costing Rs.1000 crore and above) may be summaries as below:-

(i) During the reference month out of 1263 projects 380 are mega projects. Total original cost of implementation of these 380 projects was Rs. 11,96,304.11 crore and their anticipated completion cost is likely to be Rs. 13,62,966.94 crore, which reflects overall cost overruns of Rs. 1,66,662.83 crore (13.93% of original cost). The expenditure incurred on these projects till September 2017 is Rs. 5,64,940.14 crore, which is 41.45% of the anticipated cost of the projects. Out of the 380 mega projects, 145 projects have cost overruns with respect to original scost and the number of such projects decreases to 114 when cost overrun is calculated on the basis of revised cost.

(ii) Further, out of the 128 delayed mega projects, 59 projects have cost overruns. Out of these, the cost for 26 projects has been revised and for 33 projects the cost has not yet been revised. Of the 26 projects where cost has been revised, the anticipated cost of 5 projects has again exceeded the revised cost. Out of 123 delayed projects, 65 projects have not provided any milestones and in 44 cases the dates of completion of the milestones have already lapsed.

(iii) In addition to above there are 86 mega projects which though are on schedule but are having cost overruns. Of these, the cost for 20 projects has since been revised. Of the 20 projects where cost has been revised, the anticipated cost of 10 projects has exceeded even the revised costs. Out of these 86 projects, 54 projects have not provided any milestones and for 2 projects the completion date of milestone(s) has already lapsed.

(iv). In the current month, there are 123 mega projects showing time overruns of more than 6 months; 136 mega projects showing cost overruns of more than Rs.100 crore and 57 mega projects showing both time overruns of more than 6 months and cost overruns of more than Rs.100 crore.

Further, expenditure has exceeded the approved cost in 71 mega projects and in 268 mega projects milestones have not been reported. Concerned secretaries have been requested to take a review of these projects to fix time lines and cost estimate.

4. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

5. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones.

6. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported.


7. Ministry of Railways have provided the latest information of all its ongoing projects costing ₹500 crore and above on the OCMS of this Ministry. The recent and latest updated information in respect of projects costing below ₹500 crore is reported as and when received.

8. The status as on 30.09.2017 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report available at [www.cspm.gov.in /publication](http://www.cspm.gov.in/publication).

9. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

TABLE-1

| EXECUTIVE SUMMARY COSTING Rs.150 crore and above |                             |                     |                               |
|--------------------------------------------------|-----------------------------|---------------------|-------------------------------|
| Sl.No.                                           | Sector                      | Projects on Monitor | Projects Additionally Delayed |
| 1                                                | ROAD TRANSPORT AND HIGHWAYS | 482                 | 1                             |
| 2                                                | RAILWAYS                    | 353                 | 10                            |
| 3                                                | POWER                       | 124                 | 17                            |
| 4                                                | PETROLEUM                   | 104                 | 2                             |
| 5                                                | COAL                        | 92                  | 3                             |
| 6                                                | URBAN DEVELOPMENT           | 36                  | 5                             |
| 7                                                | STEEL                       | 34                  | 3                             |
| 8                                                | HEALTH AND FAMILY WELFARE   | 13                  | 0                             |
| 9                                                | SHIPPING AND PORTS          | 8                   | 0                             |
| 10                                               | MINES                       | 4                   | 0                             |
| 11                                               | ATOMIC ENERGY               | 3                   | 1                             |
| 12                                               | TELECOMMUNICATIONS          | 3                   | 1                             |
| 13                                               | CIVIL AVIATION              | 2                   | 0                             |
| 14                                               | FERTILISERS                 | 2                   | 0                             |
| 15                                               | DEFENCE PRODUCTION          | 2                   | 0                             |
| 16                                               | HEAVY INDUSTRY              | 1                   | 0                             |
|                                                  | Total                       | 1263                | 43                            |

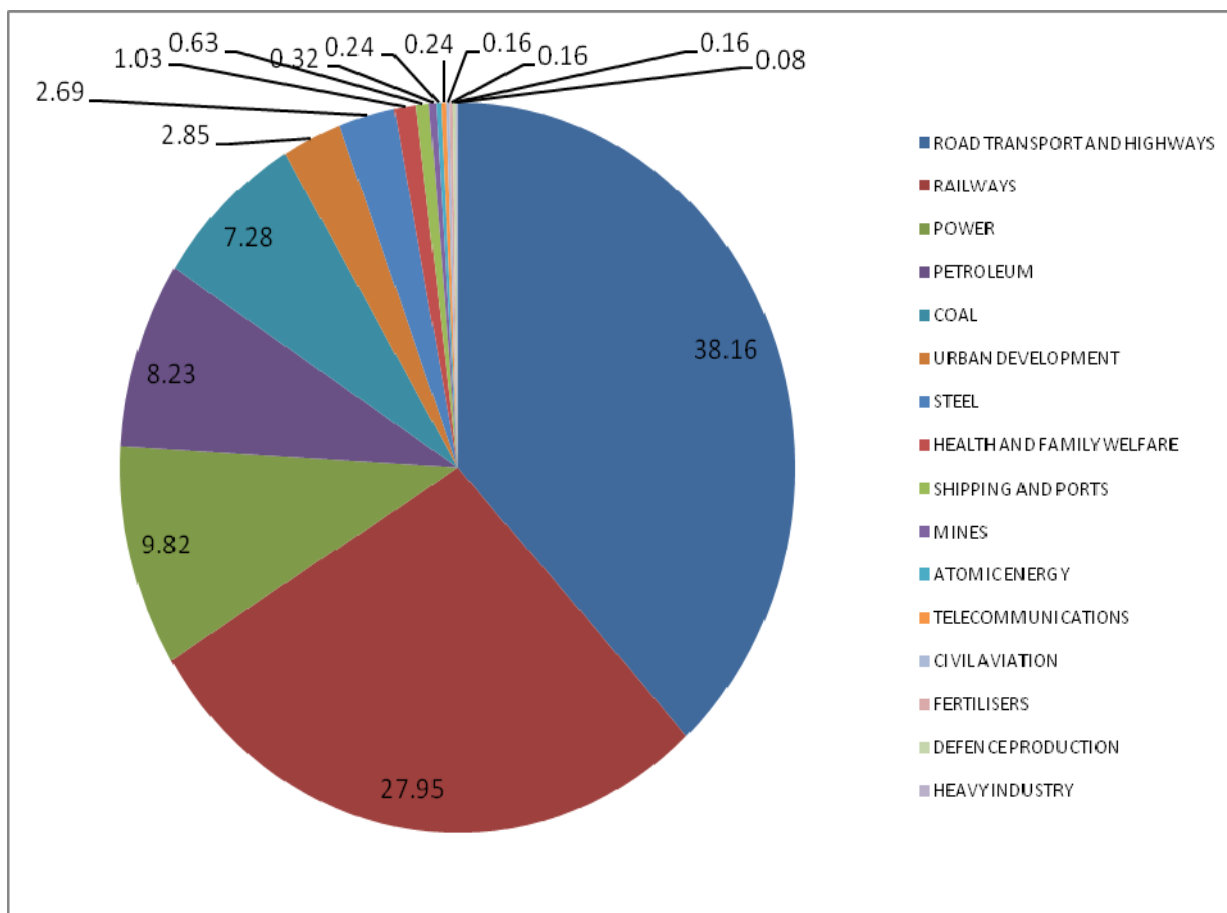

**TABLE-2**

| Month wise List of Completed Projects Costing Rs.150 crore and above during |                                                                                                                                                                     |                              |                                   |                                          |
|-----------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------|-----------------------------------|------------------------------------------|
| 2017-2018                                                                   |                                                                                                                                                                     |                              |                                   |                                          |
| Sl. No                                                                      | Project Name                                                                                                                                                        | Original Cost<br>(Rs. crore) | Original Date of<br>commissioning | Cumulative<br>Expenditure<br>(Rs. crore) |
|                                                                             |                                                                                                                                                                     |                              |                                   |                                          |
|                                                                             | April,2017                                                                                                                                                          |                              |                                   |                                          |
|                                                                             |                                                                                                                                                                     |                              |                                   |                                          |
|                                                                             | <u>PETROCHEMICALS</u>                                                                                                                                               |                              |                                   |                                          |
| 1                                                                           | ASSAM GAS CRACKER PROJECT<br>G(BRAHMAPUTRA CRECKER & POLYMER LTD.) - [N16000106]                                                                                    | 5,460.61                     | 04/2012                           | 9,895.05                                 |
|                                                                             |                                                                                                                                                                     |                              |                                   |                                          |
|                                                                             | <u>POWER</u>                                                                                                                                                        |                              |                                   |                                          |
| 2                                                                           | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII<br>G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000053]                                                       | 509.66                       | 11/2011                           | 566.26                                   |
| 3                                                                           | SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP)<br>G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000081]                                                  | 1,216.83                     | 08/2012                           | 1,074.89                                 |
| 4                                                                           | ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH<br>FOR IPP GENERATION PROJECT IN CHHATTISGARH G(POWER<br>GRID CORPORATION OF INDIA LIMITED) - [N18000101]   | 1,961.87                     | 05/2014                           | 1,817.05                                 |
| 5                                                                           | SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP<br>PROJECTS IN CHHATTISGARH G(POWER GRID<br>CORPORATION OF INDIA LIMITED) - [N18000117]                      | 1,422.85                     | 01/2015                           | 1,490.42                                 |
| 6                                                                           | COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT.<br>LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI G(POWER<br>GRID CORPORATION OF INDIA LIMITED) - [N18000145]  | 1,909.24                     | 06/2015                           | 1,093.03                                 |
| 7                                                                           | INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION<br>G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000163]                                                    | 303.07                       | 07/2016                           | 48.50                                    |
| 8                                                                           | SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING<br>IN SOUTHERN REGION FOR IMPORT OF POWER FROM E G(POWER<br>GRID CORPORATION OF INDIA LIMITED) - [N18000173] | 972.42                       | 11/2017                           | 92.20                                    |
|                                                                             |                                                                                                                                                                     |                              |                                   |                                          |
|                                                                             | May,2017                                                                                                                                                            |                              |                                   |                                          |
|                                                                             |                                                                                                                                                                     |                              |                                   |                                          |
|                                                                             | <u>CIVIL AVIATION</u>                                                                                                                                               |                              |                                   |                                          |
| 9                                                                           | SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS<br>G(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000071]                                                   | 217.60                       | 03/2015                           | 196.94                                   |
|                                                                             |                                                                                                                                                                     |                              |                                   |                                          |
|                                                                             | June,2017                                                                                                                                                           |                              |                                   |                                          |
|                                                                             |                                                                                                                                                                     |                              |                                   |                                          |
|                                                                             | <u>STEEL</u>                                                                                                                                                        |                              |                                   |                                          |
| 10                                                                          | SMS-1 CONVERTERS REVAMPING<br>G(RASTRIYA ISPAT NIGAM LIMITED) - [N12000090]                                                                                         | 404.16                       | 07/2015                           | 394.74                                   |
|                                                                             |                                                                                                                                                                     |                              |                                   |                                          |
|                                                                             | <u>POWER</u>                                                                                                                                                        |                              |                                   |                                          |
| 11                                                                          | TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC<br>POWER PROJECT - 3 AND 4 G(POWER GRID<br>CORPORATION OF INDIA LIMITED) - [N18000166]                          | 378.71                       | 10/2016                           | 257.90                                   |



## Month wise List of Completed Projects Costing Rs.150 crore and above during

**2017-2018**

| Sl. No | Project Name                                                                                                                                                       | Original Cost<br>(Rs. crore) | Original Date of<br>commissioning | Cumulative<br>Expenditure<br>(Rs. crore) |
|--------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------|-----------------------------------|------------------------------------------|
| 12     | TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800)<br>GEN. PROJECT OF NTPC G(POWER GRID<br>CORPORATION OF INDIA LIMITED) - [N18000167]                        | 400.47                       | 04/2017                           | 265.20                                   |
| 13     | TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS<br>G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000211]                                                     | 187.04                       | 06/2018                           | 54.60                                    |
|        | July,2017                                                                                                                                                          |                              |                                   |                                          |
| 14     | NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI<br>G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000094]                                                        | 752.64                       | 07/2013                           | 633.62                                   |
| 15     | WARDHA-HYDERABAD 765 KV LINK<br>G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000183]                                                                           | 3,662.02                     | 05/2018                           | 2,302.40                                 |
|        | August,2017                                                                                                                                                        |                              |                                   |                                          |
| 16     | TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II<br>G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000153]                                                     | 1,575.30                     | 05/2016                           | 1,328.51                                 |
|        | September,2017                                                                                                                                                     |                              |                                   |                                          |
|        | <u>ATOMIC ENERGY</u>                                                                                                                                               |                              |                                   |                                          |
| 17     | KUDANKULAM APP (NPCIL)<br>G(NUCLEAR POWER CORPORATION OF INDIA LIMITED) - [020100040]                                                                              | 13,171.00                    | 12/2008                           | 22,340.00                                |
|        | <u>CIVIL AVIATION</u>                                                                                                                                              |                              |                                   |                                          |
| 18     | CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)<br>G(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000069]                                                    | 335.61                       | 05/2012                           | 305.59                                   |
|        | <u>PETROLEUM</u>                                                                                                                                                   |                              |                                   |                                          |
| 19     | DE-BOTTLENECKING OF SMPL<br>G(INDIAN OIL CORPORATION LIMITED) - [N16000089]                                                                                        | 1,584.00                     | 03/2017                           | 1,355.45                                 |
| 20     | INTEGRATED REFINERY EXPANSION PROJECT<br>G(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000143]                                                                     | 16,504.00                    | 03/2017                           | 15,090.99                                |
| 21     | MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)<br>G(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000146]                                                   | 666.00                       | 11/2015                           | 606.13                                   |
| 22     | AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE<br>G(INDIAN OIL CORPORATION LIMITED) - [N16000149]                                                                 | 586.00                       | 08/2015                           | 440.20                                   |
| 23     | MARKETING TOP AT KORBA<br>G(INDIAN OIL CORPORATION LIMITED) - [N16000186]                                                                                          | 141.86                       | 09/2016                           | 174.37                                   |
| 24     | INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND<br>ASSOCIATED FACILITIES G(BHARAT PETROLEUM<br>CORPORATION LIMITED) - [N16000205]                             | 1,714.00                     | 06/2017                           | 1,067.89                                 |
|        | <u>POWER</u>                                                                                                                                                       |                              |                                   |                                          |
| 25     | TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF<br>WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH G(POWER<br>GRID CORPORATION OF INDIA LIMITED) - [N18000112] | 2,127.51                     | 07/2014                           | 2,582.69                                 |

| Month wise List of Completed Projects Costing Rs.150 crore and above during |                                                                                                                           |                              |                                   |                                          |
|-----------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------|------------------------------|-----------------------------------|------------------------------------------|
| 2017-2018                                                                   |                                                                                                                           |                              |                                   |                                          |
| Sl. No                                                                      | Project Name                                                                                                              | Original Cost<br>(Rs. crore) | Original Date of<br>commissioning | Cumulative<br>Expenditure<br>(Rs. crore) |
| 26                                                                          | WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN<br>CHHATTISGARH G(Power Grid<br>Corporation of India Limited) - [N18000125] | 9,569.76                     | 06/2015                           | 7,311.17                                 |
| 27                                                                          | KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW)<br>G(National Thermal Power Corporation) - [N18000191]              | 3,984.03                     | 01/2013                           | 3,290.44                                 |
|                                                                             |                                                                                                                           |                              |                                   |                                          |
|                                                                             |                                                                                                                           |                              |                                   |                                          |
|                                                                             |                                                                                                                           |                              |                                   |                                          |

TABLE-3

| Month wise List of Deleted Projects Costing Rs.150 crore and above during |                                                                                                                                                          |                           |                                |                                    |
|---------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------|--------------------------------|------------------------------------|
| 2017-2018                                                                 |                                                                                                                                                          |                           |                                |                                    |
| Sl. No                                                                    | Project Name                                                                                                                                             | Original Cost (Rs. crore) | Original Date of Commissioning | Cumulative Expenditure (Rs. crore) |
|                                                                           | July,2017                                                                                                                                                |                           |                                |                                    |
|                                                                           | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                                                       |                           |                                |                                    |
| 1                                                                         | PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000123]                                                       | 940.00                    | 07/2012                        | 1,415.36                           |
| 2                                                                         | 4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000153]                          | 359.00                    | 09/2013                        | 2.74                               |
| 3                                                                         | BHUBANESWAR TO PURI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000195]                                                                                 | 500.29                    | 08/2013                        | 869.91                             |
| 4                                                                         | 4-LANING OF RAIGANJ-DALKOLA (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000204]                                                                         | 580.43                    | 08/2013                        | 226.67                             |
| 5                                                                         | 4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000225]                                         | 828.00                    | 09/2014                        | 870.15                             |
| 6                                                                         | 2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000366] | 996.37                    | 12/2017                        | 0.00                               |
| 7                                                                         | SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000588]             | 725.95                    | 06/2019                        | 0.00                               |
|                                                                           | September,2017                                                                                                                                           |                           |                                |                                    |
|                                                                           | <u>POWER</u>                                                                                                                                             |                           |                                |                                    |
| 8                                                                         | TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP (POWER GRID CORPORATION OF INDIA LIMITED) - [180100261]                                             | 358.42                    | 12/2008                        | 0.00                               |
| 9                                                                         | TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000099]                | 1,585.12                  | 11/2013                        | 1,452.46                           |
| 10                                                                        | TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000114]                              | 552.44                    | 02/2014                        | 501.60                             |
| 11                                                                        | TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000170]                                 | 188.75                    | 02/2017                        | 0.00                               |
| 12                                                                        | PATAN WIND FARM SITE, GUJARAT 50 MW (THDC INDIA LIMITED) - [N18000204]                                                                                   | 315.00                    | 10/2016                        | 311.96                             |
| 13                                                                        | KANDORNA AND BHANWAD WIND FARM (THDC INDIA LIMITED) - [N18000234]                                                                                        | 415.49                    | 03/2017                        | 415.50                             |


## Summary of projects in the Flash Report for the month of September, 2017

### Project Implementation - Current Status:

|                                                              |      |
|--------------------------------------------------------------|------|
| Number of Projects in Previous Month                         | 1272 |
| Number of Projects completed/dropped/frozen in Current Month | 17   |
|                                                              | 0    |
| Number of Projects Added in Current Month                    | 8    |
| Number of Projects in Current Month                          | 1263 |

### Brief Analysis


Project Status with respect to Original Schedule: Out of 1263 projects, 14 projects are ahead of schedule, 307 projects are on schedule 297 projects are delayed. 510 projects do not have fixed dates of commissioning. 135 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

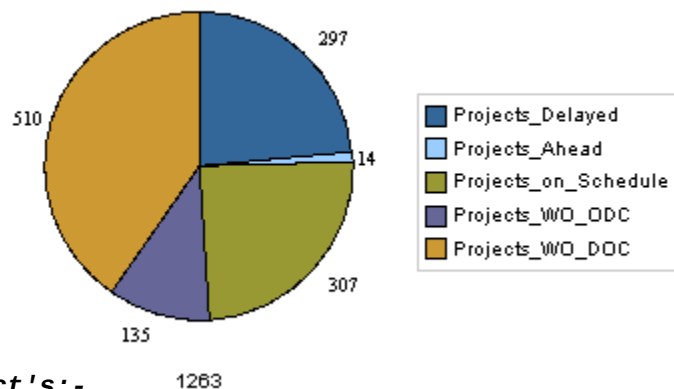

Total No Of Project's:-

### Investment Scenario

Total original cost of implementation of 1263 projects when sanctioned, was of the order of Rs. 1553683.89 crore but this was subsequently revised to Rs. 1749427.56 crore implying a cost overrun of 12.6%. The expenditure incurred on these projects till September, 2017 is Rs. 679801.38 crore, which is 38.9% of the anticipated cost of the projects.

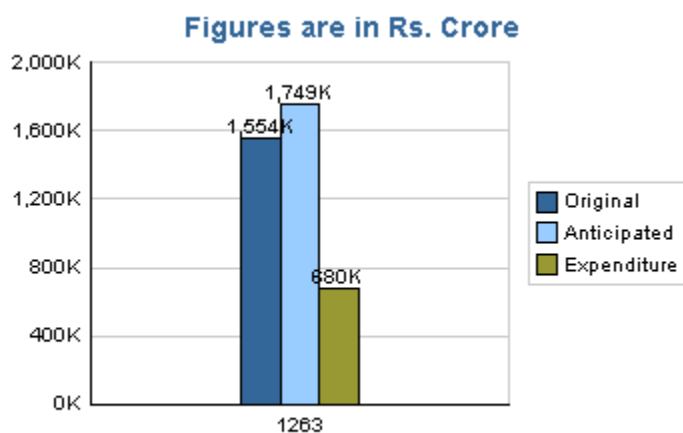

**TABLE-4**

**Projects Added / Completed / Dropped / Frozen Rs.150 Crore and above**

|                                                          |      |
|----------------------------------------------------------|------|
| No of Projects in Previous Month                         | 1272 |
| No of Projects Completed/Dropped/Frozen in Current Month | 17   |
| No of Projects added in Current Month                    | 8    |
| No of Projects in Current Month                          | 1263 |

| Project status Rs. 150 Crore and above |               |             |               |                               |               |       |
|----------------------------------------|---------------|-------------|---------------|-------------------------------|---------------|-------|
| Number of Projects                     |               |             |               |                               |               |       |
| With Respect To                        | Delayed       | Ahead       | On schedule   | Without ODC but DOC available | Without D.O.C | Total |
| Original ( Date )                      | 297 ( 23.52%) | 14 ( 1.11%) | 307 ( 24.31%) | 135 ( 10.69%)                 | 510 (40.38%)  | 1263  |
| Latest Approved ( Date)                | 249 ( 19.71%) | 12 ( .95%)  | 360 ( 28.50%) | 131 ( 10.37%)                 | 511 (40.46%)  | 1263  |

| Project cost Rs.150 Crore and above   |                 |                 |                  |                  |                               |             |       |
|---------------------------------------|-----------------|-----------------|------------------|------------------|-------------------------------|-------------|-------|
| (All Cost/ Expenditure in Rs. crore ) |                 |                 |                  |                  |                               |             |       |
| Cost overrun                          |                 |                 |                  |                  |                               |             |       |
|                                       | No. of Projects | Sanctioned Cost | Anticipated Cost | Expenditure Cost | % cost w.r.t anticipated cost | Rs crore    | %     |
| Project with No Revision in Cost      | 1111            | 13,59,988.63    | 14,84,857.87     | 5,07,885.85      | 34.20                         | 1,24,869.24 | 9.20  |
| Project with Revision in Cost         | 152             | 2,55,879.52     | 2,64,569.69      | 1,71,915.53      | 65.00                         | 8,690.17    | 3.40  |
| Total                                 | 1,263           | 16,15,868.15    | 17,49,427.56     | 6,79,801.38      | 38.86                         | 1,33,559.41 | 8.27  |
| Original Cost of All Projects         |                 |                 |                  |                  |                               |             |       |
| Original Cost                         | 1,263           | 15,53,683.89    | 17,49,427.56     | 6,79,801.38      | 38.86                         | 1,95,743.67 | 12.60 |

| Delayed Project cost Rs. 150 Crore and above |                 |                 |                  |                  |                               |             |       |
|----------------------------------------------|-----------------|-----------------|------------------|------------------|-------------------------------|-------------|-------|
| (All Cost/ Expenditure in Rs. crore )        |                 |                 |                  |                  |                               |             |       |
| Cost overrun                                 |                 |                 |                  |                  |                               |             |       |
| With Respect to                              | No. of Projects | Sanctioned Cost | Anticipated Cost | Expenditure Cost | % cost w.r.t anticipated cost | Rs crore    | %     |
| Original (OCE)                               | 297             | 5,39,754.44     | 6,75,032.54      | 4,16,614.31      | 61.70                         | 1,35,278.10 | 25.10 |
| Latest Approved (RCE)                        | 249             | 4,47,646.16     | 5,44,622.43      | 3,19,949.99      | 58.70                         | 96,976.27   | 21.70 |
|                                              |                 |                 |                  |                  |                               |             |       |

| Additional Delayed Project cost Rs.150 Crore and above |                 |                 |                  |                  |                               |           |       |
|--------------------------------------------------------|-----------------|-----------------|------------------|------------------|-------------------------------|-----------|-------|
| (All Cost/ Expenditure in Rs. crore )                  |                 |                 |                  |                  |                               |           |       |
| Cost overrun                                           |                 |                 |                  |                  |                               |           |       |
| With Respect to                                        | No. of Projects | Sanctioned Cost | Anticipated Cost | Expenditure Cost | % cost w.r.t anticipated cost | Rs crore  | %     |
| Latest Approved                                        | 43              | 83,785.71       | 1,01,361.72      | 56,450.06        | 55.70                         | 17,576.01 | 21.00 |

**TABLE-5**

| Extent of cost overrun in projects with respect to original schedule (Sector Wise) Rs.150 Crore and above |                             |                 |               |                  |                  |                                         |               |                  |                  |
|-----------------------------------------------------------------------------------------------------------|-----------------------------|-----------------|---------------|------------------|------------------|-----------------------------------------|---------------|------------------|------------------|
| (All Cost/ Expenditure in Rs. crore )                                                                     |                             |                 |               |                  |                  |                                         |               |                  |                  |
|                                                                                                           |                             |                 |               |                  |                  | Projects with cost overrun <sup>^</sup> |               |                  |                  |
| Sl.No                                                                                                     | Sector                      | No. of Projects | Original Cost | Anticipated cost | Cost overrun (%) | No.                                     | Original Cost | Anticipated Cost | Cost overrun (%) |
| 1                                                                                                         | ATOMIC ENERGY               | 3               | 27,271.00     | 29,779.00        | 9.20             | 1                                       | 3,492.00      | 6,000.00         | 71.82            |
| 2                                                                                                         | CIVIL AVIATION              | 2               | 624.07        | 994.86           | 59.41            | 2                                       | 624.07        | 994.86           | 59.41            |
| 3                                                                                                         | COAL                        | 92              | 88,124.99     | 88,310.36        | 0.21             | 7                                       | 18,876.68     | 19,914.04        | 5.50             |
| 4                                                                                                         | FERTILISERS                 | 2               | 680.64        | 703.44           | 3.35             | 2                                       | 680.64        | 703.44           | 3.35             |
| 5                                                                                                         | MINES                       | 4               | 6,773.63      | 6,773.63         | 0.00             | 0                                       | 0.00          | 0.00             | 0.00             |
| 6                                                                                                         | STEEL                       | 34              | 57,349.49     | 57,563.17        | 0.37             | 5                                       | 1,639.71      | 2,211.39         | 34.86            |
| 7                                                                                                         | PETROLEUM                   | 104             | 1,90,142.65   | 1,91,522.05      | 0.73             | 17                                      | 24,522.27     | 30,950.70        | 26.21            |
| 8                                                                                                         | POWER                       | 124             | 3,39,545.24   | 3,97,302.11      | 17.01            | 44                                      | 1,05,404.62   | 1,63,161.49      | 54.80            |
| 9                                                                                                         | HEAVY INDUSTRY              | 1               | 1,718.00      | 3,827.30         | 122.78           | 1                                       | 1,718.00      | 3,827.30         | 122.78           |
| 10                                                                                                        | HEALTH AND FAMILY WELFARE   | 13              | 3,637.08      | 3,649.38         | 0.34             | 1                                       | 196.70        | 209.00           | 6.25             |
| 11                                                                                                        | RAILWAYS                    | 353             | 3,54,063.17   | 4,54,173.45      | 28.27            | 213                                     | 1,21,595.36   | 2,83,482.35      | 133.14           |
| 12                                                                                                        | ROAD TRANSPORT AND HIGHWAYS | 482             | 3,17,373.88   | 3,23,746.08      | 2.01             | 43                                      | 25,598.69     | 32,656.93        | 27.57            |
| 13                                                                                                        | SHIPPING AND PORTS          | 8               | 4,117.75      | 5,085.02         | 23.49            | 5                                       | 1,205.50      | 2,172.77         | 80.24            |
| 14                                                                                                        | TELECOMMUNICATIONS          | 3               | 15,863.43     | 27,093.43        | 70.79            | 1                                       | 13,334.00     | 24,664.00        | 84.97            |
| 15                                                                                                        | URBAN DEVELOPMENT           | 36              | 1,45,945.23   | 1,58,435.24      | 8.56             | 6                                       | 22,919.82     | 35,590.21        | 55.28            |
| 16                                                                                                        | DEFENCE PRODUCTION          | 2               | 453.64        | 469.04           | 3.39             | 2                                       | 453.64        | 469.04           | 3.39             |
| Total                                                                                                     |                             | 1263            | 15,53,683.89  | 17,49,427.56     | 12.60            | 350                                     | 3,42,261.70   | 6,07,007.52      | 77.35            |

<sup>^</sup> - Cost Overrun = Anticipated Cost minus Original Cost

**TABLE-6**

| <b>Extent of cost overrun in projects with respect to original schedule (State Wise) Rs. 150 Crore and above</b> |                           |                 |                     |                     |                  |                                               |                    |                    |                  |
|------------------------------------------------------------------------------------------------------------------|---------------------------|-----------------|---------------------|---------------------|------------------|-----------------------------------------------|--------------------|--------------------|------------------|
| (All Cost/ Expenditure in Rs. crore)                                                                             |                           |                 |                     |                     |                  |                                               |                    |                    |                  |
|                                                                                                                  |                           |                 |                     |                     |                  | <b>Projects with cost overrun<sup>^</sup></b> |                    |                    |                  |
| Sl.No                                                                                                            | State                     | No. of Projects | Original Cost       | Anticipated Cost    | Cost overrun (%) | No.                                           | Original Cost      | Anticipated Cost   | Cost overrun (%) |
| 1                                                                                                                | ANDHRA PRADESH            | 59              | 97,268.72           | 1,01,271.75         | 4.12             | 9                                             | 6,577.56           | 11,606.74          | 76.46            |
| 2                                                                                                                | ARUNACHAL PRADESH         | 31              | 16,602.41           | 33,555.84           | 102.11           | 6                                             | 9,755.78           | 26,709.21          | 173.78           |
| 3                                                                                                                | ASSAM                     | 50              | 33,769.60           | 47,399.82           | 40.36            | 16                                            | 15,110.50          | 28,922.44          | 91.41            |
| 4                                                                                                                | BIHAR                     | 77              | 64,823.58           | 81,651.84           | 25.96            | 20                                            | 33,420.33          | 50,544.54          | 51.24            |
| 5                                                                                                                | GOA                       | 9               | 4,043.51            | 4,058.91            | 0.38             | 2                                             | 453.64             | 469.04             | 3.39             |
| 6                                                                                                                | GUJARAT                   | 41              | 38,827.45           | 41,398.82           | 6.62             | 10                                            | 5,641.30           | 9,568.61           | 69.62            |
| 7                                                                                                                | HARYANA                   | 21              | 14,081.22           | 15,967.45           | 13.40            | 3                                             | 1,633.56           | 3,653.00           | 123.62           |
| 8                                                                                                                | HIMACHAL PRADESH          | 12              | 14,659.32           | 22,591.60           | 54.11            | 2                                             | 4,966.47           | 12,898.75          | 159.72           |
| 9                                                                                                                | JAMMU AND KASHMIR         | 10              | 27,408.66           | 47,277.79           | 72.49            | 3                                             | 7,930.45           | 27,799.58          | 250.54           |
| 10                                                                                                               | KARNATAKA                 | 46              | 78,727.90           | 96,951.71           | 23.15            | 22                                            | 17,213.22          | 36,600.81          | 112.63           |
| 11                                                                                                               | KERALA                    | 20              | 20,650.14           | 26,747.71           | 29.53            | 7                                             | 3,017.36           | 9,114.93           | 202.08           |
| 12                                                                                                               | MADHYA PRADESH            | 54              | 57,610.99           | 62,057.28           | 7.72             | 8                                             | 6,120.00           | 10,574.83          | 72.79            |
| 13                                                                                                               | MAHARASHTRA               | 112             | 1,69,907.76         | 1,79,607.21         | 5.71             | 27                                            | 33,696.88          | 47,111.29          | 39.81            |
| 14                                                                                                               | MANIPUR                   | 2               | 944.25              | 9,874.69            | 945.77           | 1                                             | 727.56             | 9,658.00           | 1227.45          |
| 15                                                                                                               | MEGHALAYA                 | 6               | 7,108.02            | 9,025.00            | 26.97            | 1                                             | 4,083.02           | 6,000.00           | 46.95            |
| 16                                                                                                               | MIZORAM                   | 5               | 2,001.20            | 6,942.57            | 246.92           | 2                                             | 988.06             | 5,929.43           | 500.11           |
| 17                                                                                                               | NAGALAND                  | 7               | 8,126.79            | 10,276.79           | 26.46            | 1                                             | 850.00             | 3,000.00           | 252.94           |
| 18                                                                                                               | ODISHA                    | 66              | 72,116.99           | 79,785.64           | 10.63            | 19                                            | 6,641.38           | 14,326.32          | 115.71           |
| 19                                                                                                               | PUNJAB                    | 28              | 15,555.77           | 15,561.50           | 0.04             | 2                                             | 1,328.50           | 1,361.27           | 2.47             |
| 20                                                                                                               | RAJASTHAN                 | 62              | 44,007.10           | 46,296.19           | 5.20             | 15                                            | 6,007.10           | 8,296.19           | 38.11            |
| 21                                                                                                               | SIKKIM                    | 6               | 2,537.08            | 5,585.45            | 120.15           | 3                                             | 2,036.94           | 5,085.59           | 149.67           |
| 22                                                                                                               | TAMIL NADU                | 56              | 63,625.39           | 77,115.53           | 21.20            | 19                                            | 26,024.11          | 40,263.36          | 54.72            |
| 23                                                                                                               | TRIPURA                   | 11              | 4,400.64            | 9,067.42            | 106.05           | 7                                             | 2,909.18           | 7,575.96           | 160.42           |
| 24                                                                                                               | UTTAR PRADESH             | 83              | 1,09,253.66         | 1,12,943.92         | 3.38             | 18                                            | 27,633.82          | 31,778.66          | 15.00            |
| 25                                                                                                               | WEST BENGAL               | 53              | 56,102.34           | 71,007.29           | 26.57            | 22                                            | 25,345.31          | 40,619.94          | 60.27            |
| 26                                                                                                               | D & N HAVELI              | 1               | 6,086.08            | 5,479.75            | -9.96            | 0                                             | 0.00               | 0.00               | 0.00             |
| 27                                                                                                               | DELHI                     | 17              | 50,925.07           | 51,204.68           | 0.55             | 3                                             | 1,572.56           | 1,998.17           | 27.06            |
| 28                                                                                                               | CHHATISGARH               | 38              | 82,769.79           | 84,975.67           | 2.67             | 5                                             | 3,354.55           | 5,560.43           | 65.76            |
| 29                                                                                                               | JHARKHAND                 | 48              | 46,724.53           | 50,436.69           | 7.94             | 10                                            | 9,447.31           | 13,163.25          | 39.33            |
| 30                                                                                                               | UTTARAKHAND               | 13              | 16,833.35           | 17,673.56           | 4.99             | 5                                             | 5,112.02           | 8,626.44           | 68.75            |
| 31                                                                                                               | ANDAMAN & NICOBAR ISLANDS | 1               | 314.61              | 441.33              | 40.28            | 1                                             | 314.61             | 441.33             | 40.28            |
| 32                                                                                                               | TELANGANA                 | 35              | 24,832.84           | 27,489.74           | 10.70            | 10                                            | 3,002.30           | 5,850.29           | 94.86            |
| 33                                                                                                               | MULTI STATE               | 183             | 3,01,037.13         | 2,97,706.42         | -1.11            | 71                                            | 69,346.32          | 1,21,899.12        | 75.78            |
| <b>Total</b>                                                                                                     |                           | <b>1263</b>     | <b>15,53,683.89</b> | <b>17,49,427.56</b> | <b>12.60</b>     | <b>350</b>                                    | <b>3,42,261.70</b> | <b>6,07,007.52</b> | <b>77.35</b>     |

<sup>^</sup> - Cost Overrun = Anticipated Cost minus Original Cost

**TABLE-7**

**Extent of time overrun in projects with respect to original schedule Rs.150 Crore and above**

(All Cost/ Expenditure in Rs. crore)

|       |                             |                 |               |                  |                   | Projects with time overruns\$ |               |                  |                            |
|-------|-----------------------------|-----------------|---------------|------------------|-------------------|-------------------------------|---------------|------------------|----------------------------|
| Sl.No | Sector                      | No. of Projects | Original Cost | Anticipated Cost | Cost Overrun^ (%) | No.                           | Original Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1     | ATOMIC ENERGY               | 3               | 27,271.00     | 29,779.00        | 9.20              | 3                             | 27,271.00     | 29,779.00        | 47 - 89                    |
| 2     | CIVIL AVIATION              | 2               | 624.07        | 994.86           | 59.41             | 2                             | 624.07        | 994.86           | 21 - 80                    |
| 3     | COAL                        | 92              | 88,124.99     | 88,310.36        | 0.21              | 39                            | 20,618.90     | 20,758.14        | 4 - 132                    |
| 4     | FERTILISERS                 | 2               | 680.64        | 703.44           | 3.35              | 1                             | 197.79        | 209.44           | 29 - 29                    |
| 5     | MINES                       | 4               | 6,773.63      | 6,773.63         | 0.00              | 0                             | 0.00          | 0.00             | -                          |
| 6     | STEEL                       | 34              | 57,349.49     | 57,563.17        | 0.37              | 17                            | 46,224.80     | 46,036.59        | 5 - 72                     |
| 7     | PETROLEUM                   | 104             | 1,90,142.65   | 1,91,522.05      | 0.73              | 35                            | 59,790.32     | 63,010.99        | 1 - 93                     |
| 8     | POWER                       | 124             | 3,39,545.24   | 3,97,302.11      | 17.01             | 61                            | 1,99,151.68   | 2,36,516.58      | 3 - 136                    |
| 9     | HEAVY INDUSTRY              | 1               | 1,718.00      | 3,827.30         | 122.78            | 1                             | 1,718.00      | 3,827.30         | 75 - 75                    |
| 10    | HEALTH AND FAMILY WELFARE   | 13              | 3,637.08      | 3,649.38         | 0.34              | 5                             | 1,183.93      | 1,183.93         | 6 - 15                     |
| 11    | RAILWAYS                    | 353             | 3,54,063.17   | 4,54,173.45      | 28.27             | 36                            | 44,219.60     | 1,13,147.29      | 12 - 261                   |
| 12    | ROAD TRANSPORT AND HIGHWAYS | 482             | 3,17,373.88   | 3,23,746.08      | 2.01              | 74                            | 64,849.16     | 68,524.01        | 5 - 116                    |
| 13    | SHIPPING AND PORTS          | 8               | 4,117.75      | 5,085.02         | 23.49             | 2                             | 516.39        | 1,269.46         | 96 - 141                   |
| 14    | TELECOMMUNICATIONS          | 3               | 15,863.43     | 27,093.43        | 70.79             | 1                             | 13,334.00     | 24,664.00        | 47 - 47                    |
| 15    | URBAN DEVELOPMENT           | 36              | 1,45,945.23   | 1,58,435.24      | 8.56              | 20                            | 60,054.80     | 65,110.95        | 2 - 72                     |
| 16    | DEFENCE PRODUCTION          | 2               | 453.64        | 469.04           | 3.39              | 0                             | 0.00          | 0.00             | -                          |
| Total |                             | 1263            | 15,53,683.89  | 17,49,427.56     | 12.60             | 297                           | 5,39,754.44   | 6,75,032.54      |                            |

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning



**TABLE-8**

**Extent of time overrun in projects with respect to original schedule (State Wise) Rs. 150 Crore and above**

(All Cost/ Expenditure in Rs. crore)

|       |                           |                 |               |                  |                  | Projects with time overruns |               |                  |                            |
|-------|---------------------------|-----------------|---------------|------------------|------------------|-----------------------------|---------------|------------------|----------------------------|
| Sl.No | State                     | No. of Projects | Original Cost | Anticipated cost | Cost overrun (%) | No.                         | Original Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1     | ANDHRA PRADESH            | 59              | 97,268.72     | 1,01,271.75      | 4.12             | 11                          | 11,159.39     | 12,840.03        | 6 - 144                    |
| 2     | ARUNACHAL PRADESH         | 31              | 16,602.41     | 33,555.84        | 102.11           | 3                           | 3,209.82      | 7,672.72         | 36 - 99                    |
| 3     | ASSAM                     | 50              | 33,769.60     | 47,399.82        | 40.36            | 12                          | 12,400.35     | 24,231.10        | 15 - 122                   |
| 4     | BIHAR                     | 77              | 64,823.58     | 81,651.84        | 25.96            | 10                          | 31,086.63     | 41,066.75        | 11 - 98                    |
| 5     | GOA                       | 9               | 4,043.51      | 4,058.91         | 0.38             | 0                           | 0.00          | 0.00             | -                          |
| 6     | GUJARAT                   | 41              | 38,827.45     | 41,398.82        | 6.62             | 7                           | 16,203.35     | 17,884.87        | 7 - 84                     |
| 7     | HARYANA                   | 21              | 14,081.22     | 15,967.45        | 13.40            | 2                           | 1,710.95      | 2,890.95         | 24 - 76                    |
| 8     | HIMACHAL PRADESH          | 12              | 14,659.32     | 22,591.60        | 54.11            | 3                           | 6,107.21      | 10,586.37        | 15 - 111                   |
| 9     | JAMMU AND KASHMIR         | 10              | 27,408.66     | 47,277.79        | 72.49            | 7                           | 20,944.03     | 40,813.16        | 12 - 193                   |
| 10    | KARNATAKA                 | 46              | 78,727.90     | 96,951.71        | 23.15            | 6                           | 44,544.13     | 45,244.13        | 10 - 69                    |
| 11    | KERALA                    | 20              | 20,650.14     | 26,747.71        | 29.53            | 6                           | 11,313.37     | 11,420.56        | 9 - 65                     |
| 12    | MADHYA PRADESH            | 54              | 57,610.99     | 62,057.28        | 7.72             | 10                          | 16,666.98     | 17,727.08        | 2 - 96                     |
| 13    | MAHARASHTRA               | 112             | 1,69,907.76   | 1,79,607.21      | 5.71             | 23                          | 54,314.13     | 58,583.67        | 6 - 192                    |
| 14    | MANIPUR                   | 2               | 944.25        | 9,874.69         | 945.77           | 2                           | 944.25        | 9,874.69         | 44 - 108                   |
| 15    | MEGHALAYA                 | 6               | 7,108.02      | 9,025.00         | 26.97            | 3                           | 1,051.32      | 1,051.32         | 15 - 50                    |
| 16    | MIZORAM                   | 5               | 2,001.20      | 6,942.57         | 246.92           | 2                           | 988.06        | 5,929.43         | 71 - 136                   |
| 17    | NAGALAND                  | 7               | 8,126.79      | 10,276.79        | 26.46            | 4                           | 2,049.11      | 4,199.11         | 36 - 60                    |
| 18    | ODISHA                    | 66              | 72,116.99     | 79,785.64        | 10.63            | 14                          | 11,652.28     | 12,878.04        | 5 - 108                    |
| 19    | PUNJAB                    | 28              | 15,555.77     | 15,561.50        | 0.04             | 4                           | 1,512.09      | 1,512.09         | 6 - 23                     |
| 20    | RAJASTHAN                 | 62              | 44,007.10     | 46,296.19        | 5.20             | 9                           | 17,588.00     | 18,207.75        | 6 - 74                     |
| 21    | SIKKIM                    | 6               | 2,537.08      | 5,585.45         | 120.15           | 2                           | 1,648.94      | 4,638.22         | 51 - 80                    |
| 22    | TAMIL NADU                | 56              | 63,625.39     | 77,115.53        | 21.20            | 20                          | 38,846.31     | 46,683.75        | 1 - 141                    |
| 23    | TRIPURA                   | 11              | 4,400.64      | 9,067.42         | 106.05           | 3                           | 1,231.33      | 3,893.38         | 7 - 72                     |
| 24    | UTTAR PRADESH             | 83              | 1,09,253.66   | 1,12,943.92      | 3.38             | 12                          | 16,740.83     | 16,840.01        | 12 - 58                    |
| 25    | WEST BENGAL               | 53              | 56,102.34     | 71,007.29        | 26.57            | 14                          | 25,834.58     | 27,986.51        | 6 - 57                     |
| 26    | D & N HAVELI              | 1               | 6,086.08      | 5,479.75         | -9.96            | 1                           | 6,086.08      | 5,479.75         | 5 - 5                      |
| 27    | DELHI                     | 17              | 50,925.07     | 51,204.68        | 0.55             | 5                           | 3,996.12      | 4,368.91         | 5 - 27                     |
| 28    | CHHATISGARH               | 38              | 82,769.79     | 84,975.67        | 2.67             | 11                          | 49,049.07     | 50,029.69        | 10 - 93                    |
| 29    | JHARKHAND                 | 48              | 46,724.53     | 50,436.69        | 7.94             | 22                          | 25,136.25     | 25,488.39        | 5 - 166                    |
| 30    | UTTARAKHAND               | 13              | 16,833.35     | 17,673.56        | 4.99             | 5                           | 7,719.83      | 11,020.99        | 50 - 89                    |
| 31    | ANDAMAN & NICOBAR ISLANDS | 1               | 314.61        | 441.33           | 40.28            | 1                           | 314.61        | 441.33           | 21 - 21                    |
| 32    | TELANGANA                 | 35              | 24,832.84     | 27,489.74        | 10.70            | 13                          | 5,449.94      | 5,987.93         | 12 - 132                   |
| 33    | MULTI STATE               | 183             | 3,01,037.13   | 2,97,706.42      | -1.11            | 50                          | 92,255.10     | 1,27,559.86      | 3 - 261                    |
| Total |                           | 1263            | 15,53,683.89  | 17,49,427.56     | 12.60            | 297                         | 5,39,754.44   | 6,75,032.54      |                            |

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$ - Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

**TABLE-9**

| Extent of time overrun in projects with respect to latest schedule Rs.150 Crore and above |                             |                 |                      |                  |                   |                               |                      |                  |                            |
|-------------------------------------------------------------------------------------------|-----------------------------|-----------------|----------------------|------------------|-------------------|-------------------------------|----------------------|------------------|----------------------------|
| (All Cost/ Expenditure in Rs. crore)                                                      |                             |                 |                      |                  |                   |                               |                      |                  |                            |
|                                                                                           |                             |                 |                      |                  |                   | Projects with time overruns\$ |                      |                  |                            |
| Sl.No                                                                                     | Sector                      | No. of Projects | Latest Approved Cost | Anticipated Cost | Cost Overrun^ (%) | No.                           | Latest Approved Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1                                                                                         | ATOMIC ENERGY               | 3               | 29,456.00            | 29,779.00        | 1.10              | 3                             | 29,456.00            | 29,779.00        | 47 - 89                    |
| 2                                                                                         | CIVIL AVIATION              | 2               | 624.07               | 994.86           | 59.41             | 1                             | 314.61               | 441.33           | 21 - 21                    |
| 3                                                                                         | COAL                        | 92              | 88,248.46            | 88,310.36        | 0.07              | 35                            | 13,134.81            | 13,195.91        | 4 - 132                    |
| 4                                                                                         | FERTILISERS                 | 2               | 692.29               | 703.44           | 1.61              | 0                             | 0.00                 | 0.00             | -                          |
| 5                                                                                         | MINES                       | 4               | 6,773.63             | 6,773.63         | 0.00              | 0                             | 0.00                 | 0.00             | -                          |
| 6                                                                                         | STEEL                       | 34              | 57,730.46            | 57,563.17        | -0.29             | 16                            | 30,724.19            | 30,511.59        | 5 - 72                     |
| 7                                                                                         | PETROLEUM                   | 104             | 1,92,398.27          | 1,91,522.05      | -0.46             | 12                            | 11,281.66            | 12,487.26        | 1 - 74                     |
| 8                                                                                         | POWER                       | 124             | 3,73,808.24          | 3,97,302.11      | 6.29              | 44                            | 1,68,820.07          | 1,78,502.29      | 0 - 111                    |
| 9                                                                                         | HEAVY INDUSTRY              | 1               | 1,718.00             | 3,827.30         | 122.78            | 1                             | 1,718.00             | 3,827.30         | 75 - 75                    |
| 10                                                                                        | HEALTH AND FAMILY WELFARE   | 13              | 3,637.08             | 3,649.38         | 0.34              | 4                             | 819.94               | 819.94           | 6 - 7                      |
| 11                                                                                        | RAILWAYS                    | 353             | 3,63,169.43          | 4,54,173.45      | 25.06             | 39                            | 47,656.90            | 1,16,230.26      | 0 - 261                    |
| 12                                                                                        | ROAD TRANSPORT AND HIGHWAYS | 482             | 3,17,947.90          | 3,23,746.08      | 1.82              | 74                            | 64,864.93            | 68,524.01        | 5 - 116                    |
| 13                                                                                        | SHIPPING AND PORTS          | 8               | 4,131.25             | 5,085.02         | 23.09             | 2                             | 516.39               | 1,269.46         | 96 - 141                   |
| 14                                                                                        | TELECOMMUNICATIONS          | 3               | 15,863.43            | 27,093.43        | 70.79             | 1                             | 13,334.00            | 24,664.00        | 47 - 47                    |
| 15                                                                                        | URBAN DEVELOPMENT           | 36              | 1,59,215.64          | 1,58,435.24      | -0.49             | 17                            | 65,004.66            | 64,370.08        | 5 - 72                     |
| 16                                                                                        | DEFENCE PRODUCTION          | 2               | 454.00               | 469.04           | 3.31              | 0                             | 0.00                 | 0.00             | -                          |
| Total                                                                                     |                             | 1263            | 16,15,868.15         | 17,49,427.56     | 8.27              | 249                           | 4,47,646.16          | 5,44,622.43      |                            |

\$- Time overrun = Anticipated Date of Commissioning minus latest schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus latest Cost.

**TABLE-10**

| Extent of cost overrun in projects with respect to latest schedule Rs.150 Crore and above |                             |                 |                      |                  |                  |                              |                      |                  |                  |
|-------------------------------------------------------------------------------------------|-----------------------------|-----------------|----------------------|------------------|------------------|------------------------------|----------------------|------------------|------------------|
| (All Cost/ Expenditure in Rs. crore)                                                      |                             |                 |                      |                  |                  |                              |                      |                  |                  |
|                                                                                           |                             |                 |                      |                  |                  | Projects with cost overruns^ |                      |                  |                  |
| Sl.No.                                                                                    | Sector                      | No. of projects | Latest Approved Cost | Anticipated Cost | Cost overrun (%) | No.                          | Latest Approved Cost | Anticipated Cost | Cost overrun (%) |
| 1                                                                                         | ATOMIC ENERGY               | 3               | 29,456.00            | 29,779.00        | 1.10             | 1                            | 5,677.00             | 6,000.00         | 5.69             |
| 2                                                                                         | CIVIL AVIATION              | 2               | 624.07               | 994.86           | 59.41            | 2                            | 624.07               | 994.86           | 59.41            |
| 3                                                                                         | COAL                        | 92              | 88,248.46            | 88,310.36        | 0.07             | 2                            | 17,655.97            | 17,727.42        | 0.40             |
| 4                                                                                         | FERTILISERS                 | 2               | 692.29               | 703.44           | 1.61             | 1                            | 482.85               | 494.00           | 2.31             |
| 5                                                                                         | MINES                       | 4               | 6,773.63             | 6,773.63         | 0.00             | 0                            | 0.00                 | 0.00             | 0.00             |
| 6                                                                                         | STEEL                       | 34              | 57,730.46            | 57,563.17        | -0.29            | 3                            | 1,586.97             | 1,777.68         | 12.02            |
| 7                                                                                         | PETROLEUM                   | 104             | 1,92,398.27          | 1,91,522.05      | -0.46            | 9                            | 12,393.82            | 15,719.05        | 26.83            |
| 8                                                                                         | POWER                       | 124             | 3,73,808.24          | 3,97,302.11      | 6.29             | 17                           | 52,195.45            | 75,689.32        | 45.01            |
| 9                                                                                         | HEAVY INDUSTRY              | 1               | 1,718.00             | 3,827.30         | 122.78           | 1                            | 1,718.00             | 3,827.30         | 122.78           |
| 10                                                                                        | HEALTH AND FAMILY WELFARE   | 13              | 3,637.08             | 3,649.38         | 0.34             | 1                            | 196.70               | 209.00           | 6.25             |
| 11                                                                                        | RAILWAYS                    | 353             | 3,63,169.43          | 4,54,173.45      | 25.06            | 199                          | 1,17,897.02          | 2,69,398.13      | 128.50           |
| 12                                                                                        | ROAD TRANSPORT AND HIGHWAYS | 482             | 3,17,947.90          | 3,23,746.08      | 1.82             | 33                           | 23,181.71            | 29,854.53        | 28.78            |
| 13                                                                                        | SHIPPING AND PORTS          | 8               | 4,131.25             | 5,085.02         | 23.09            | 5                            | 1,219.00             | 2,172.77         | 78.24            |
| 14                                                                                        | TELECOMMUNICATIONS          | 3               | 15,863.43            | 27,093.43        | 70.79            | 1                            | 13,334.00            | 24,664.00        | 84.97            |
| 15                                                                                        | URBAN DEVELOPMENT           | 36              | 1,59,215.64          | 1,58,435.24      | -0.49            | 2                            | 662.97               | 666.80           | 0.58             |
| 16                                                                                        | DEFENCE PRODUCTION          | 2               | 454.00               | 469.04           | 3.31             | 2                            | 454.00               | 469.04           | 3.31             |
|                                                                                           |                             |                 |                      |                  |                  |                              |                      |                  |                  |
| Total                                                                                     |                             | 1263            | 16,15,868.15         | 17,49,427.56     | 8.27             | 279                          | 2,49,279.53          | 4,49,663.90      | 80.39            |

^ - Cost Overrun = Anticipated Cost minus latest Cost.

**TABLE-11**

| <u>Extent of time &amp; cost overrun in projects with respect to latest schedule</u> Rs. 150 Crore and above |                             |                 |                      |                  |                  |                                       |                      |                  |                            |
|--------------------------------------------------------------------------------------------------------------|-----------------------------|-----------------|----------------------|------------------|------------------|---------------------------------------|----------------------|------------------|----------------------------|
| (All Cost/ Expenditure in Rs. crore)                                                                         |                             |                 |                      |                  |                  |                                       |                      |                  |                            |
|                                                                                                              |                             |                 |                      |                  |                  | Projects with time\$ & cost overruns^ |                      |                  |                            |
| Sl.No.                                                                                                       | Sector                      | No. of projects | Latest Approved Cost | Anticipated Cost | Cost Overrun (%) | No.                                   | Latest Approved Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1                                                                                                            | ATOMIC ENERGY               | 3               | 29,456.00            | 29,779.00        | 1.10             | 1                                     | 5,677.00             | 6,000.00         | 89- 89                     |
| 2                                                                                                            | CIVIL AVIATION              | 2               | 624.07               | 994.86           | 59.41            | 1                                     | 314.61               | 441.33           | 21- 21                     |
| 3                                                                                                            | COAL                        | 92              | 88,248.46            | 88,310.36        | 0.07             | 1                                     | 418.97               | 489.62           | 132- 132                   |
| 4                                                                                                            | FERTILISERS                 | 2               | 692.29               | 703.44           | 1.61             | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| 5                                                                                                            | MINES                       | 4               | 6,773.63             | 6,773.63         | 0.00             | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| 6                                                                                                            | STEEL                       | 34              | 57,730.46            | 57,563.17        | -0.29            | 1                                     | 343.00               | 488.40           | 17- 17                     |
| 7                                                                                                            | PETROLEUM                   | 104             | 1,92,398.27          | 1,91,522.05      | -0.46            | 4                                     | 2,366.91             | 3,591.96         | 20- 69                     |
| 8                                                                                                            | POWER                       | 124             | 3,73,808.24          | 3,97,302.11      | 6.29             | 10                                    | 28,573.01            | 38,255.23        | 11- 111                    |
| 9                                                                                                            | HEAVY INDUSTRY              | 1               | 1,718.00             | 3,827.30         | 122.78           | 1                                     | 1,718.00             | 3,827.30         | 75- 75                     |
| 10                                                                                                           | HEALTH AND FAMILY WELFARE   | 13              | 3,637.08             | 3,649.38         | 0.34             | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| 11                                                                                                           | RAILWAYS                    | 353             | 3,63,169.43          | 4,54,173.45      | 25.06            | 27                                    | 28,348.76            | 95,916.25        | 33- 261                    |
| 12                                                                                                           | ROAD TRANSPORT AND HIGHWAYS | 482             | 3,17,947.90          | 3,23,746.08      | 1.82             | 6                                     | 5,344.71             | 9,004.30         | 22- 106                    |
| 13                                                                                                           | SHIPPING AND PORTS          | 8               | 4,131.25             | 5,085.02         | 23.09            | 2                                     | 516.39               | 1,269.46         | 96- 141                    |
| 14                                                                                                           | TELECOMMUNICATIONS          | 3               | 15,863.43            | 27,093.43        | 70.79            | 1                                     | 13,334.00            | 24,664.00        | 47- 47                     |
| 15                                                                                                           | URBAN DEVELOPMENT           | 36              | 1,59,215.64          | 1,58,435.24      | -0.49            | 1                                     | 166.97               | 170.62           | 72- 72                     |
| 16                                                                                                           | DEFENCE PRODUCTION          | 2               | 454.00               | 469.04           | 3.31             | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| Total                                                                                                        |                             | 1263            | 16,15,868.15         | 17,49,427.56     | 8.27             | 56                                    | 87,122.33            | 1,84,118.47      |                            |

\$- Time overrun = Anticipated Date of Commissioning minus latest schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus latest Cost.

**TABLE-12**

| <b>Extent of time &amp; cost overrun in projects with respect to original schedule Rs. 150 Crore and above</b> |                             |                 |                     |                     |                  |                                               |                    |                    |                            |
|----------------------------------------------------------------------------------------------------------------|-----------------------------|-----------------|---------------------|---------------------|------------------|-----------------------------------------------|--------------------|--------------------|----------------------------|
| (All Cost/ Expenditure in Rs. crore)                                                                           |                             |                 |                     |                     |                  |                                               |                    |                    |                            |
|                                                                                                                |                             |                 |                     |                     |                  | <b>Projects with time &amp; cost overruns</b> |                    |                    |                            |
| Sl.No.                                                                                                         | Sector                      | No. of projects | Original Cost       | Anticipated Cost    | Cost Overrun (%) | No.                                           | Original Cost      | Anticipated Cost   | Range of T.O.R (in months) |
| 1                                                                                                              | ATOMIC ENERGY               | 3               | 27,271.00           | 29,779.00           | 9.20             | 1                                             | 3,492.00           | 6,000.00           | 89- 89                     |
| 2                                                                                                              | CIVIL AVIATION              | 2               | 624.07              | 994.86              | 59.41            | 2                                             | 624.07             | 994.86             | 21- 80                     |
| 3                                                                                                              | COAL                        | 92              | 88,124.99           | 88,310.36           | 0.21             | 5                                             | 1,242.59           | 2,233.82           | 60- 132                    |
| 4                                                                                                              | FERTILISERS                 | 2               | 680.64              | 703.44              | 3.35             | 1                                             | 197.79             | 209.44             | 29- 29                     |
| 5                                                                                                              | MINES                       | 4               | 6,773.63            | 6,773.63            | 0.00             | 0                                             | 0.00               | 0.00               | 0- 0                       |
| 6                                                                                                              | STEEL                       | 34              | 57,349.49           | 57,563.17           | 0.37             | 2                                             | 545.61             | 715.40             | 12- 17                     |
| 7                                                                                                              | PETROLEUM                   | 104             | 1,90,142.65         | 1,91,522.05         | 0.73             | 12                                            | 19,314.96          | 24,922.58          | 9- 70                      |
| 8                                                                                                              | POWER                       | 124             | 3,39,545.24         | 3,97,302.11         | 17.01            | 37                                            | 86,966.39          | 1,24,331.29        | 5- 136                     |
| 9                                                                                                              | HEAVY INDUSTRY              | 1               | 1,718.00            | 3,827.30            | 122.78           | 1                                             | 1,718.00           | 3,827.30           | 75- 75                     |
| 10                                                                                                             | HEALTH AND FAMILY WELFARE   | 13              | 3,637.08            | 3,649.38            | 0.34             | 0                                             | 0.00               | 0.00               | 0- 0                       |
| 11                                                                                                             | RAILWAYS                    | 353             | 3,54,063.17         | 4,54,173.45         | 28.27            | 28                                            | 28,761.99          | 97,698.23          | 33- 261                    |
| 12                                                                                                             | ROAD TRANSPORT AND HIGHWAYS | 482             | 3,17,373.88         | 3,23,746.08         | 2.01             | 7                                             | 5,483.64           | 9,159.30           | 22- 106                    |
| 13                                                                                                             | SHIPPING AND PORTS          | 8               | 4,117.75            | 5,085.02            | 23.49            | 2                                             | 516.39             | 1,269.46           | 96- 141                    |
| 14                                                                                                             | TELECOMMUNICATIONS          | 3               | 15,863.43           | 27,093.43           | 70.79            | 1                                             | 13,334.00          | 24,664.00          | 47- 47                     |
| 15                                                                                                             | URBAN DEVELOPMENT           | 36              | 1,45,945.23         | 1,58,435.24         | 8.56             | 4                                             | 16,174.80          | 21,265.33          | 5- 70                      |
| 16                                                                                                             | DEFENCE PRODUCTION          | 2               | 453.64              | 469.04              | 3.39             | 0                                             | 0.00               | 0.00               | 0- 0                       |
|                                                                                                                |                             |                 |                     |                     |                  |                                               |                    |                    |                            |
| <b>Total</b>                                                                                                   |                             | <b>1263</b>     | <b>15,53,683.89</b> | <b>17,49,427.56</b> | <b>12.60</b>     | <b>103</b>                                    | <b>1,78,372.23</b> | <b>3,17,291.01</b> |                            |

\$- Time overrun = Anticipated Date of Commissioning minus original schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus original Cost.

Table-13


| State-Wise Position of Central Sector Projects costing Rs.150 Crore and above showing Both Time and Cost Overruns |                           |                 |               |                  |                   |                               |               |                  |                            |
|-------------------------------------------------------------------------------------------------------------------|---------------------------|-----------------|---------------|------------------|-------------------|-------------------------------|---------------|------------------|----------------------------|
| (All Cost/ Expenditure in Rs. crore)                                                                              |                           |                 |               |                  |                   |                               |               |                  |                            |
|                                                                                                                   |                           |                 |               |                  |                   | Projects with time overruns\$ |               |                  |                            |
| Sl.No                                                                                                             | State                     | No. of Projects | Original Cost | Anticipated cost | Cost Overrun^ (%) | No.                           | Original Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1                                                                                                                 | ANDHRA PRADESH            | 59              | 97,268.72     | 1,01,271.75      | 4.12              | 3                             | 1,241.74      | 3,280.38         | 17 - 144                   |
| 2                                                                                                                 | ARUNACHAL PRADESH         | 31              | 16,602.41     | 33,555.84        | 102.11            | 3                             | 3,209.82      | 7,672.72         | 36 - 99                    |
| 3                                                                                                                 | ASSAM                     | 50              | 33,769.60     | 47,399.82        | 40.36             | 8                             | 9,273.56      | 21,210.02        | 32 - 122                   |
| 4                                                                                                                 | BIHAR                     | 77              | 64,823.58     | 81,651.84        | 25.96             | 4                             | 27,447.25     | 37,427.37        | 11 - 98                    |
| 5                                                                                                                 | GOA                       | 9               | 4,043.51      | 4,058.91         | 0.38              | 0                             | 0.00          | 0.00             | -                          |
| 6                                                                                                                 | GUJARAT                   | 41              | 38,827.45     | 41,398.82        | 6.62              | 2                             | 1,827.34      | 3,559.49         | 63 - 84                    |
| 7                                                                                                                 | HARYANA                   | 21              | 14,081.22     | 15,967.45        | 13.40             | 1                             | 1,108.00      | 2,288.00         | 76 - 76                    |
| 8                                                                                                                 | HIMACHAL PRADESH          | 12              | 14,659.32     | 22,591.60        | 54.11             | 1                             | 3,919.59      | 8,398.75         | 111 - 111                  |
| 9                                                                                                                 | JAMMU AND KASHMIR         | 10              | 27,408.66     | 47,277.79        | 72.49             | 3                             | 7,930.45      | 27,799.58        | 12 - 193                   |
| 10                                                                                                                | KARNATAKA                 | 46              | 78,727.90     | 96,951.71        | 23.15             | 1                             | 993.00        | 1,693.00         | 69 - 69                    |
| 11                                                                                                                | KERALA                    | 20              | 20,650.14     | 26,747.71        | 29.53             | 1                             | 607.06        | 714.25           | 17 - 17                    |
| 12                                                                                                                | MADHYA PRADESH            | 54              | 57,610.99     | 62,057.28        | 7.72              | 4                             | 3,176.60      | 4,244.44         | 22 - 96                    |
| 13                                                                                                                | MAHARASHTRA               | 112             | 1,69,907.76   | 1,79,607.21      | 5.71              | 9                             | 15,706.53     | 21,470.35        | 12 - 192                   |
| 14                                                                                                                | MANIPUR                   | 2               | 944.25        | 9,874.69         | 945.77            | 1                             | 727.56        | 9,658.00         | 108 - 108                  |
| 15                                                                                                                | MEGHALAYA                 | 6               | 7,108.02      | 9,025.00         | 26.97             | 0                             | 0.00          | 0.00             | -                          |
| 16                                                                                                                | MIZORAM                   | 5               | 2,001.20      | 6,942.57         | 246.92            | 2                             | 988.06        | 5,929.43         | 71 - 136                   |
| 17                                                                                                                | NAGALAND                  | 7               | 8,126.79      | 10,276.79        | 26.46             | 1                             | 850.00        | 3,000.00         | 60 - 60                    |
| 18                                                                                                                | ODISHA                    | 66              | 72,116.99     | 79,785.64        | 10.63             | 2                             | 316.64        | 1,542.70         | 58 - 105                   |
| 19                                                                                                                | PUNJAB                    | 28              | 15,555.77     | 15,561.50        | 0.04              | 0                             | 0.00          | 0.00             | -                          |
| 20                                                                                                                | RAJASTHAN                 | 62              | 44,007.10     | 46,296.19        | 5.20              | 2                             | 1,482.93      | 2,102.68         | 57 - 63                    |
| 21                                                                                                                | SIKKIM                    | 6               | 2,537.08      | 5,585.45         | 120.15            | 2                             | 1,648.94      | 4,638.22         | 51 - 80                    |
| 22                                                                                                                | TAMIL NADU                | 56              | 63,625.39     | 77,115.53        | 21.20             | 5                             | 21,961.42     | 30,547.97        | 24 - 141                   |
| 23                                                                                                                | TRIPURA                   | 11              | 4,400.64      | 9,067.42         | 106.05            | 2                             | 1,015.95      | 3,678.00         | 12 - 72                    |
| 24                                                                                                                | UTTAR PRADESH             | 83              | 1,09,253.66   | 1,12,943.92      | 3.38              | 1                             | 195.42        | 294.60           | 58 - 58                    |
| 25                                                                                                                | WEST BENGAL               | 53              | 56,102.34     | 71,007.29        | 26.57             | 3                             | 11,432.55     | 13,584.49        | 9 - 57                     |
| 26                                                                                                                | D & N HAVELI              | 1               | 6,086.08      | 5,479.75         | -9.96             | 0                             | 0.00          | 0.00             | -                          |
| 27                                                                                                                | DELHI                     | 17              | 50,925.07     | 51,204.68        | 0.55              | 1                             | 1,219.21      | 1,592.00         | 5 - 5                      |
| 28                                                                                                                | CHHATISGARH               | 38              | 82,769.79     | 84,975.67        | 2.67              | 3                             | 2,223.98      | 3,204.60         | 40 - 93                    |
| 29                                                                                                                | JHARKHAND                 | 48              | 46,724.53     | 50,436.69        | 7.94              | 2                             | 1,161.75      | 1,513.89         | 99 - 166                   |
| 30                                                                                                                | UTTARAKHAND               | 13              | 16,833.35     | 17,673.56        | 4.99              | 3                             | 4,749.74      | 8,051.41         | 58 - 75                    |
| 31                                                                                                                | ANDAMAN & NICOBAR ISLANDS | 1               | 314.61        | 441.33           | 40.28             | 1                             | 314.61        | 441.33           | 21 - 21                    |
| 32                                                                                                                | TELANGANA                 | 35              | 24,832.84     | 27,489.74        | 10.70             | 4                             | 1,463.44      | 2,104.31         | 33 - 132                   |
| 33                                                                                                                | MULTI STATE               | 183             | 3,01,037.13   | 2,97,706.42      | -1.11             | 28                            | 50,179.09     | 85,649.03        | 5 - 261                    |
| Total                                                                                                             |                           | 1263            | 15,53,683.89  | 17,49,427.56     | 12.60             | 103                           | 1,78,372.23   | 3,17,291.01      |                            |

\$- Time overrun = Anticipated Date of Commissioning minus original schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus original Cost

TABLE-14

| EXECUTIVE SUMMARY COSTING Rs.1000 crore and above |                             |                     |                               |
|---------------------------------------------------|-----------------------------|---------------------|-------------------------------|
| Sl.No.                                            | Sector                      | Projects on Monitor | Projects Additionally Delayed |
| 1                                                 | RAILWAYS                    | 130                 | 4                             |
| 2                                                 | ROAD TRANSPORT AND HIGHWAYS | 102                 | 0                             |
| 3                                                 | POWER                       | 66                  | 5                             |
| 4                                                 | PETROLEUM                   | 42                  | 1                             |
| 5                                                 | COAL                        | 12                  | 0                             |
| 6                                                 | URBAN DEVELOPMENT           | 11                  | 0                             |
| 7                                                 | STEEL                       | 9                   | 1                             |
| 8                                                 | ATOMIC ENERGY               | 3                   | 1                             |
| 9                                                 | TELECOMMUNICATIONS          | 2                   | 1                             |
| 10                                                | MINES                       | 1                   | 0                             |
| 11                                                | HEAVY INDUSTRY              | 1                   | 0                             |
| 12                                                | SHIPPING AND PORTS          | 1                   | 0                             |
|                                                   | Total                       | 380                 | 13                            |

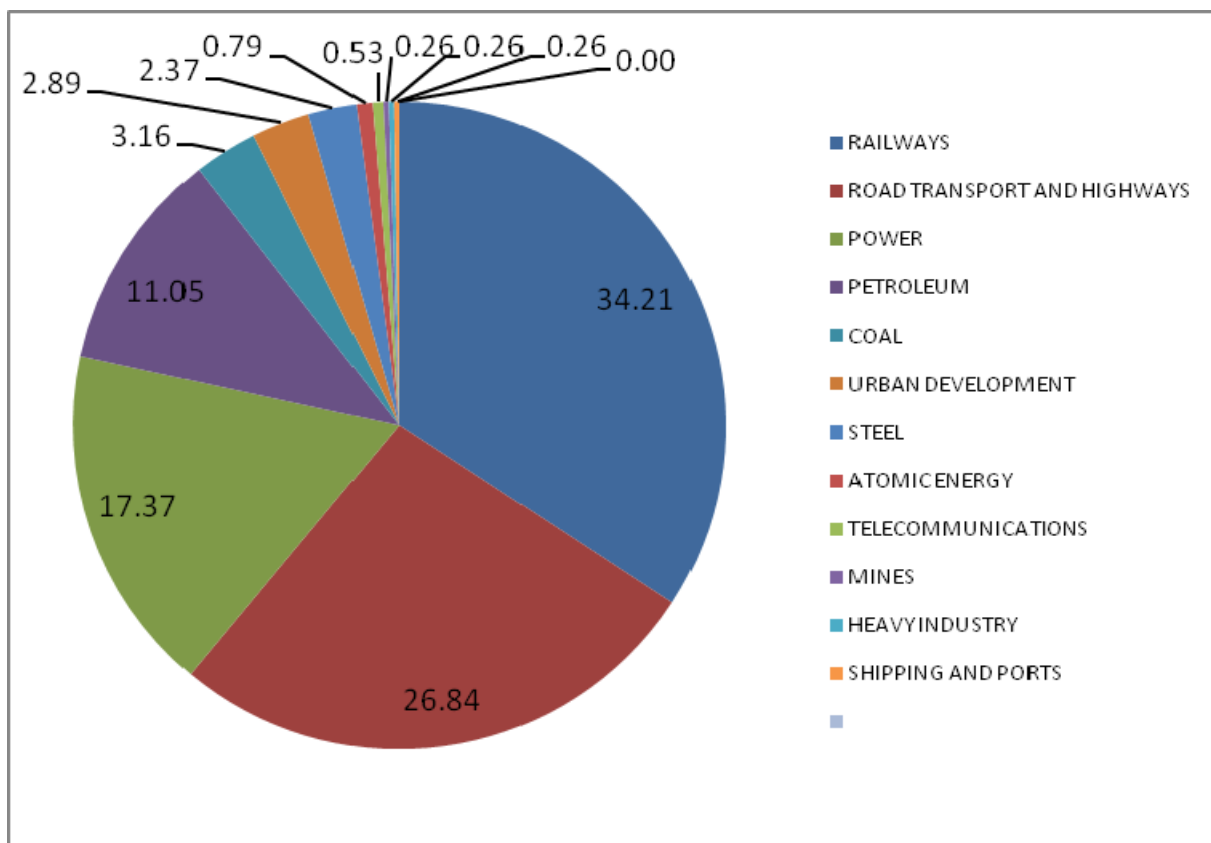

**TABLE-15**

**Projects Added / Completed / Dropped / Frozen Rs.1000 Crore and above**

|                                                          |     |
|----------------------------------------------------------|-----|
| No of Projects in Previous Month                         | 379 |
| No of Projects Completed/Dropped/Frozen in Current Month | 8   |
| No of Projects added in Current Month                    | 7   |
| No of Projects upgraded to the status of Mega Projects   | 2   |
| No of Projects in Current Month                          | 380 |

| Project status Rs. 1000 Crore and above |               |            |               |                               |               |       |
|-----------------------------------------|---------------|------------|---------------|-------------------------------|---------------|-------|
| Number of Projects                      |               |            |               |                               |               |       |
| With Respect To                         | Delayed       | Ahead      | On schedule   | Without ODC but DOC available | Without D.O.C | Total |
| Original ( Date )                       | 128 ( 33.68%) | 4 ( 1.05%) | 92 ( 24.21%)  | 48 ( 12.63%)                  | 108 (28.42%)  | 380   |
| Latest Approved ( Date)                 | 102 ( 26.84%) | 3 ( .79%)  | 121 ( 31.84%) | 45 ( 11.84%)                  | 109 (28.68%)  | 380   |

| Project cost Rs.1000 Crore and above  |                 |                 |                  |                  |                               |             |       |
|---------------------------------------|-----------------|-----------------|------------------|------------------|-------------------------------|-------------|-------|
| (All Cost/ Expenditure in Rs. crore ) |                 |                 |                  |                  |                               |             |       |
| Cost overrun                          |                 |                 |                  |                  |                               |             |       |
|                                       | No. of Projects | Sanctioned Cost | Anticipated Cost | Expenditure Cost | % cost w.r.t anticipated cost | Rs crore    | %     |
| Project with No Revision in Cost      | 320             | 10,34,125.70    | 11,36,158.22     | 4,08,889.41      | 36.00                         | 1,02,032.52 | 9.90  |
| Project with Revision in Cost         | 60              | 2,18,927.61     | 2,26,808.72      | 1,56,050.73      | 68.80                         | 7,881.11    | 3.60  |
| Total                                 | 380             | 12,53,053.31    | 13,62,966.94     | 5,64,940.14      | 41.45                         | 1,09,913.63 | 8.77  |
| Original Cost of All Projects         |                 |                 |                  |                  |                               |             |       |
| Original Cost                         | 380             | 11,96,304.11    | 13,62,966.94     | 5,64,940.14      | 41.45                         | 1,66,662.83 | 13.93 |

| Delayed Project cost Rs.1000 Crore and above            |                 |                 |                  |                  |                               |             |       |
|---------------------------------------------------------|-----------------|-----------------|------------------|------------------|-------------------------------|-------------|-------|
| (All Cost/ Expenditure in Rs. crore )                   |                 |                 |                  |                  |                               |             |       |
| Cost overrun                                            |                 |                 |                  |                  |                               |             |       |
| With Respect to                                         | No. of Projects | Sanctioned Cost | Anticipated Cost | Expenditure Cost | % cost w.r.t anticipated cost | Rs crore    | %     |
| Original (OCE)                                          | 128             | 4,71,807.20     | 6,01,071.67      | 3,77,390.73      | 62.80                         | 1,29,264.47 | 27.40 |
| Latest Approved (RCE)                                   | 102             | 3,86,522.24     | 4,79,810.38      | 2,86,076.61      | 59.60                         | 93,288.14   | 24.10 |
| Additional Delayed Project cost Rs.1000 Crore and above |                 |                 |                  |                  |                               |             |       |
| (All Cost/ Expenditure in Rs. crore )                   |                 |                 |                  |                  |                               |             |       |
| Cost overrun                                            |                 |                 |                  |                  |                               |             |       |
| With Respect to                                         | No. of Projects | Sanctioned Cost | Anticipated Cost | Expenditure Cost | % cost w.r.t anticipated cost | Rs crore    | %     |
| Latest Approved                                         | 12              | 73,535.80       | 89,589.65        | 49,265.89        | 55.00                         | 16,053.85   | 21.80 |



**TABLE-16**

| Extent of cost overrun in projects with respect to original schedule (Sector Wise) RS.1000 Crore and above |                             |                 |               |                  |                  |                             |               |                  |                  |
|------------------------------------------------------------------------------------------------------------|-----------------------------|-----------------|---------------|------------------|------------------|-----------------------------|---------------|------------------|------------------|
| (All Cost/ Expenditure in Rs. crore )                                                                      |                             |                 |               |                  |                  |                             |               |                  |                  |
|                                                                                                            |                             |                 |               |                  |                  | Projects with cost overrun^ |               |                  |                  |
| Sl.No                                                                                                      | Sector                      | No. of Projects | Original Cost | Anticipated cost | Cost overrun (%) | No.                         | Original Cost | Anticipated Cost | Cost overrun (%) |
| 1                                                                                                          | ATOMIC ENERGY               | 3               | 27,271.00     | 29,779.00        | 9.20             | 1                           | 3,492.00      | 6,000.00         | 71.82            |
| 2                                                                                                          | COAL                        | 12              | 55,807.73     | 55,808.53        | 0.00             | 1                           | 17,237.00     | 17,237.80        | 0.00             |
| 3                                                                                                          | MINES                       | 1               | 5,540.00      | 5,540.00         | 0.00             | 0                           | 0.00          | 0.00             | 0.00             |
| 4                                                                                                          | STEEL                       | 9               | 48,164.22     | 48,150.68        | -0.03            | 1                           | 768.88        | 1,113.34         | 44.80            |
| 5                                                                                                          | PETROLEUM                   | 42              | 1,65,237.15   | 1,66,989.32      | 1.06             | 9                           | 21,796.28     | 27,032.81        | 24.02            |
| 6                                                                                                          | POWER                       | 66              | 3,16,296.60   | 3,72,500.82      | 17.77            | 28                          | 98,706.62     | 1,54,910.84      | 56.94            |
| 7                                                                                                          | HEAVY INDUSTRY              | 1               | 1,718.00      | 3,827.30         | 122.78           | 1                           | 1,718.00      | 3,827.30         | 122.78           |
| 8                                                                                                          | RAILWAYS                    | 130             | 2,70,626.64   | 3,45,927.66      | 27.82            | 85                          | 83,212.97     | 2,17,733.30      | 161.66           |
| 9                                                                                                          | ROAD TRANSPORT AND HIGHWAYS | 102             | 1,48,606.06   | 1,54,042.12      | 3.66             | 15                          | 17,413.21     | 22,849.27        | 31.22            |
| 10                                                                                                         | SHIPPING AND PORTS          | 1               | 2,427.40      | 2,427.40         | 0.00             | 0                           | 0.00          | 0.00             | 0.00             |
| 11                                                                                                         | TELECOMMUNICATIONS          | 2               | 15,445.17     | 26,675.17        | 72.71            | 1                           | 13,334.00     | 24,664.00        | 84.97            |
| 12                                                                                                         | URBAN DEVELOPMENT           | 11              | 1,39,164.14   | 1,51,298.94      | 8.72             | 3                           | 22,214.21     | 34,495.01        | 55.28            |
| Total                                                                                                      |                             | 380             | 11,96,304.11  | 13,62,966.94     | 13.93            | 145                         | 2,79,893.17   | 5,09,863.67      | 82.16            |

^ - Cost Overrun = Anticipated Cost minus Original Cost

**TABLE-17**
**Extent of cost overrun in projects with respect to original schedule(State Wise) Rs.1000 Crore and above**

(All Cost/ Expenditure in Rs. crore)

|       |                   |                 |               |                  |                  | Projects with cost overrun^ |               |                  |                  |
|-------|-------------------|-----------------|---------------|------------------|------------------|-----------------------------|---------------|------------------|------------------|
| Sl.No | State             | No. of Projects | Original Cost | Anticipated Cost | Cost overrun (%) | No.                         | Original Cost | Anticipated Cost | Cost overrun (%) |
| 1     | ANDHRA PRADESH    | 16              | 82,287.82     | 84,885.89        | 3.16             | 4                           | 5,360.88      | 8,685.95         | 62.02            |
| 2     | ARUNACHAL PRADESH | 4               | 10,609.32     | 27,330.31        | 157.61           | 3                           | 9,356.22      | 26,077.21        | 178.72           |
| 3     | ASSAM             | 9               | 21,033.85     | 32,693.76        | 55.43            | 5                           | 12,723.01     | 24,469.18        | 92.32            |
| 4     | BIHAR             | 13              | 37,034.94     | 51,777.80        | 39.81            | 7                           | 28,983.86     | 43,726.72        | 50.87            |
| 5     | GUJARAT           | 10              | 23,570.79     | 26,172.48        | 11.04            | 3                           | 3,221.99      | 5,823.68         | 80.75            |
| 6     | HARYANA           | 4               | 5,634.39      | 6,814.39         | 20.94            | 1                           | 1,108.00      | 2,288.00         | 106.50           |
| 7     | HIMACHAL PRADESH  | 6               | 12,226.08     | 20,158.36        | 64.88            | 2                           | 4,966.47      | 12,898.75        | 159.72           |
| 8     | JAMMU AND KASHMIR | 10              | 27,408.66     | 47,277.79        | 72.49            | 3                           | 7,930.45      | 27,799.58        | 250.54           |
| 9     | KARNATAKA         | 22              | 67,362.06     | 84,410.34        | 25.31            | 13                          | 14,079.10     | 31,886.38        | 126.48           |
| 10    | KERALA            | 6               | 15,533.08     | 21,030.60        | 35.39            | 2                           | 1,450.00      | 6,947.52         | 379.14           |
| 11    | MADHYA PRADESH    | 15              | 38,561.17     | 42,526.03        | 10.28            | 6                           | 5,173.40      | 9,138.26         | 76.64            |
| 12    | MAHARASHTRA       | 44              | 1,42,261.61   | 1,50,501.32      | 5.79             | 17                          | 29,763.57     | 41,277.58        | 38.68            |
| 13    | MANIPUR           | 1               | 727.56        | 9,658.00         | 1227.45          | 1                           | 727.56        | 9,658.00         | 1227.45          |
| 14    | MEGHALAYA         | 2               | 5,577.50      | 7,494.48         | 34.37            | 1                           | 4,083.02      | 6,000.00         | 46.95            |
| 15    | MIZORAM           | 2               | 988.06        | 5,929.43         | 500.11           | 2                           | 988.06        | 5,929.43         | 500.11           |
| 16    | NAGALAND          | 3               | 6,420.00      | 8,570.00         | 33.49            | 1                           | 850.00        | 3,000.00         | 252.94           |
| 17    | ODISHA            | 24              | 56,413.98     | 63,001.36        | 11.68            | 6                           | 3,733.20      | 10,320.58        | 176.45           |
| 18    | PUNJAB            | 2               | 2,557.95      | 2,557.95         | 0.00             | 0                           | 0.00          | 0.00             | 0.00             |
| 19    | RAJASTHAN         | 7               | 19,624.78     | 19,956.68        | 1.69             | 1                           | 829.74        | 1,161.64         | 40.00            |
| 20    | SIKKIM            | 1               | 1,339.48      | 4,084.69         | 204.95           | 1                           | 1,339.48      | 4,084.69         | 204.95           |
| 21    | TAMIL NADU        | 14              | 45,746.76     | 56,934.45        | 24.46            | 7                           | 23,397.78     | 34,585.47        | 47.82            |
| 22    | TRIPURA           | 3               | 2,129.35      | 6,386.31         | 199.92           | 3                           | 2,129.35      | 6,386.31         | 199.92           |
| 23    | UTTAR PRADESH     | 33              | 86,307.66     | 88,855.18        | 2.95             | 7                           | 23,509.18     | 26,511.28        | 12.77            |
| 24    | WEST BENGAL       | 22              | 44,076.95     | 56,813.51        | 28.90            | 10                          | 22,275.61     | 35,012.18        | 57.18            |
| 25    | D & N HAVELI      | 1               | 6,086.08      | 5,479.75         | -9.96            | 0                           | 0.00          | 0.00             | 0.00             |
| 26    | DELHI             | 4               | 45,462.73     | 45,689.52        | 0.50             | 1                           | 1,219.21      | 1,592.00         | 30.58            |
| 27    | CHHATISGARH       | 11              | 71,673.86     | 73,381.18        | 2.38             | 3                           | 2,877.22      | 4,584.54         | 59.34            |
| 28    | JHARKHAND         | 10              | 33,188.25     | 35,781.77        | 7.81             | 3                           | 7,451.01      | 10,044.53        | 34.81            |
| 29    | UTTARAKHAND       | 6               | 14,392.36     | 14,868.59        | 3.31             | 2                           | 4,635.48      | 7,785.41         | 67.95            |
| 30    | TELANGANA         | 6               | 14,904.53     | 16,572.01        | 11.19            | 2                           | 502.99        | 2,170.47         | 331.51           |
| 31    | MULTI STATE       | 69              | 2,55,162.50   | 2,45,373.01      | -3.84            | 28                          | 55,227.33     | 1,00,018.33      | 81.10            |
| Total |                   | 380             | 11,96,304.11  | 13,62,966.94     | 13.93            | 145                         | 2,79,893.17   | 5,09,863.67      | 82.16            |

^ - Cost Overrun = Anticipated Cost minus Original Cost

**TABLE-18**

**Extent of time overrun in projects with respect to original schedule Rs. 1000 Crore and above**

(All Cost/ Expenditure in Rs. crore)

|       |                             |                 |               |                  |                               | Projects with time overruns\$ |               |                  |                            |
|-------|-----------------------------|-----------------|---------------|------------------|-------------------------------|-------------------------------|---------------|------------------|----------------------------|
| Sl.No | Sector                      | No. of Projects | Original Cost | Anticipated Cost | Cost Overrun <sup>^</sup> (%) | No.                           | Original Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1     | ATOMIC ENERGY               | 3               | 27,271.00     | 29,779.00        | 9.20                          | 3                             | 27,271.00     | 29,779.00        | 47 - 89                    |
| 2     | COAL                        | 12              | 55,807.73     | 55,808.53        | 0.00                          | 3                             | 8,192.43      | 8,192.43         | 6 - 48                     |
| 3     | MINES                       | 1               | 5,540.00      | 5,540.00         | 0.00                          | 0                             | 0.00          | 0.00             | -                          |
| 4     | STEEL                       | 9               | 48,164.22     | 48,150.68        | -0.03                         | 6                             | 40,963.49     | 40,605.49        | 5 - 55                     |
| 5     | PETROLEUM                   | 42              | 1,65,237.15   | 1,66,989.32      | 1.06                          | 17                            | 52,938.39     | 55,548.93        | 5 - 74                     |
| 6     | POWER                       | 66              | 3,16,296.60   | 3,72,500.82      | 17.77                         | 39                            | 1,89,277.08   | 2,25,161.58      | 3 - 136                    |
| 7     | HEAVY INDUSTRY              | 1               | 1,718.00      | 3,827.30         | 122.78                        | 1                             | 1,718.00      | 3,827.30         | 75 - 75                    |
| 8     | RAILWAYS                    | 130             | 2,70,626.64   | 3,45,927.66      | 27.82                         | 25                            | 39,634.09     | 1,06,496.79      | 12 - 261                   |
| 9     | ROAD TRANSPORT AND HIGHWAYS | 102             | 1,48,606.06   | 1,54,042.12      | 3.66                          | 28                            | 42,392.58     | 45,879.22        | 15 - 76                    |
| 10    | SHIPPING AND PORTS          | 1               | 2,427.40      | 2,427.40         | 0.00                          | 0                             | 0.00          | 0.00             | -                          |
| 11    | TELECOMMUNICATIONS          | 2               | 15,445.17     | 26,675.17        | 72.71                         | 1                             | 13,334.00     | 24,664.00        | 47 - 47                    |
| 12    | URBAN DEVELOPMENT           | 11              | 1,39,164.14   | 1,51,298.94      | 8.72                          | 5                             | 56,086.14     | 60,916.93        | 5 - 29                     |
| Total |                             | 380             | 11,96,304.11  | 13,62,966.94     | 13.93                         | 128                           | 4,71,807.20   | 6,01,071.67      |                            |

<sup>^</sup> - Cost Overrun = Anticipated Cost minus Original Cost

<sup>\$</sup> - Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

**TABLE-19**

**Extent of time overrun in projects with respect to original schedule(State Wise) Rs.1000 Crore and above**

(All Cost/ Expenditure in Rs. crore)

|       |                   |                 |               |                  |                               | Projects with time overruns\$ |               |                  |                            |
|-------|-------------------|-----------------|---------------|------------------|-------------------------------|-------------------------------|---------------|------------------|----------------------------|
| Sl.No | State             | No. of Projects | Original Cost | Anticipated cost | Cost Overrun <sup>^</sup> (%) | No.                           | Original Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1     | ANDHRA PRADESH    | 16              | 82,287.82     | 84,885.89        | 3.16                          | 4                             | 7,685.71      | 8,409.71         | 6 - 144                    |
| 2     | ARUNACHAL PRADESH | 4               | 10,609.32     | 27,330.31        | 157.61                        | 2                             | 3,070.89      | 7,517.72         | 55 - 99                    |
| 3     | ASSAM             | 9               | 21,033.85     | 32,693.76        | 55.43                         | 5                             | 10,888.16     | 22,328.07        | 32 - 122                   |
| 4     | BIHAR             | 13              | 37,034.94     | 51,777.80        | 39.81                         | 3                             | 27,010.57     | 36,824.93        | 11 - 98                    |
| 5     | GUJARAT           | 10              | 23,570.79     | 26,172.48        | 11.04                         | 3                             | 14,357.72     | 16,086.49        | 45 - 63                    |
| 6     | HARYANA           | 4               | 5,634.39      | 6,814.39         | 20.94                         | 1                             | 1,108.00      | 2,288.00         | 76 - 76                    |
| 7     | HIMACHAL PRADESH  | 6               | 12,226.08     | 20,158.36        | 64.88                         | 2                             | 5,836.38      | 10,315.54        | 15 - 111                   |
| 8     | JAMMU AND KASHMIR | 10              | 27,408.66     | 47,277.79        | 72.49                         | 7                             | 20,944.03     | 40,813.16        | 12 - 193                   |
| 9     | KARNATAKA         | 22              | 67,362.06     | 84,410.34        | 25.31                         | 4                             | 44,219.34     | 44,919.34        | 10 - 69                    |
| 10    | KERALA            | 6               | 15,533.08     | 21,030.60        | 35.39                         | 2                             | 9,770.08      | 9,770.08         | 9 - 29                     |
| 11    | MADHYA PRADESH    | 15              | 38,561.17     | 42,526.03        | 10.28                         | 4                             | 14,881.45     | 15,459.32        | 6 - 53                     |
| 12    | MAHARASHTRA       | 44              | 1,42,261.61   | 1,50,501.32      | 5.79                          | 14                            | 49,672.70     | 53,293.11        | 12 - 192                   |
| 13    | MANIPUR           | 1               | 727.56        | 9,658.00         | 1,227.45                      | 1                             | 727.56        | 9,658.00         | 108 - 108                  |
| 14    | MEGHALAYA         | 2               | 5,577.50      | 7,494.48         | 34.37                         | 0                             | 0.00          | 0.00             | -                          |
| 15    | MIZORAM           | 2               | 988.06        | 5,929.43         | 500.11                        | 2                             | 988.06        | 5,929.43         | 71 - 136                   |
| 16    | NAGALAND          | 3               | 6,420.00      | 8,570.00         | 33.49                         | 1                             | 850.00        | 3,000.00         | 60 - 60                    |
| 17    | ODISHA            | 24              | 56,413.98     | 63,001.36        | 11.68                         | 4                             | 8,822.27      | 9,841.74         | 10 - 58                    |
| 18    | PUNJAB            | 2               | 2,557.95      | 2,557.95         | 0.00                          | 0                             | 0.00          | 0.00             | -                          |
| 19    | RAJASTHAN         | 7               | 19,624.78     | 19,956.68        | 1.69                          | 3                             | 14,823.44     | 15,155.34        | 48 - 74                    |
| 20    | SIKKIM            | 1               | 1,339.48      | 4,084.69         | 204.95                        | 1                             | 1,339.48      | 4,084.69         | 51 - 51                    |
| 21    | TAMIL NADU        | 14              | 45,746.76     | 56,934.45        | 24.46                         | 7                             | 32,078.89     | 40,215.44        | 23 - 118                   |
| 22    | TRIPURA           | 3               | 2,129.35      | 6,386.31         | 199.92                        | 1                             | 813.34        | 3,451.00         | 72 - 72                    |
| 23    | UTTAR PRADESH     | 33              | 86,307.66     | 88,855.18        | 2.95                          | 4                             | 13,636.89     | 13,636.89        | 18 - 51                    |
| 24    | WEST BENGAL       | 22              | 44,076.95     | 56,813.51        | 28.90                         | 8                             | 22,750.71     | 24,902.64        | 6 - 57                     |
| 25    | D & N HAVELI      | 1               | 6,086.08      | 5,479.75         | -9.96                         | 1                             | 6,086.08      | 5,479.75         | 5 - 5                      |
| 26    | DELHI             | 4               | 45,462.73     | 45,689.52        | 0.50                          | 2                             | 2,613.73      | 2,986.52         | 5 - 25                     |
| 27    | CHHATISGARH       | 11              | 71,673.86     | 73,381.18        | 2.38                          | 5                             | 47,614.65     | 48,096.71        | 10 - 55                    |
| 28    | JHARKHAND         | 10              | 33,188.25     | 35,781.77        | 7.81                          | 6                             | 20,164.09     | 20,389.93        | 5 - 99                     |
| 29    | UTTARAKHAND       | 6               | 14,392.36     | 14,868.59        | 3.31                          | 3                             | 7,127.06      | 10,276.99        | 58 - 89                    |
| 30    | TELANGANA         | 6               | 14,904.53     | 16,572.01        | 11.19                         | 1                             | 1,266.60      | 1,266.60         | 18 - 18                    |
| 31    | MULTI STATE       | 69              | 2,55,162.50   | 2,45,373.01      | -3.84                         | 27                            | 80,659.32     | 1,14,674.53      | 3 - 261                    |
| Total |                   | 380             | 11,96,304.11  | 13,62,966.94     | 13.93                         | 128                           | 4,71,807.20   | 6,01,071.67      |                            |

<sup>^</sup> - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

**TABLE-20**

| Extent of time overrun in projects with respect to latest schedule Rs.1000 Crore and above |                             |                 |                      |                  |                  |                               |                      |                  |                            |
|--------------------------------------------------------------------------------------------|-----------------------------|-----------------|----------------------|------------------|------------------|-------------------------------|----------------------|------------------|----------------------------|
| (All Cost/ Expenditure in Rs. crore)                                                       |                             |                 |                      |                  |                  |                               |                      |                  |                            |
|                                                                                            |                             |                 |                      |                  |                  | Projects with time overruns\$ |                      |                  |                            |
| Sl.No                                                                                      | Sector                      | No. of Projects | Latest Approved Cost | Anticipated Cost | Cost overrun (%) | No.                           | Latest Approved Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1                                                                                          | ATOMIC ENERGY               | 3               | 29,456.00            | 29,779.00        | 1.10             | 3                             | 29,456.00            | 29,779.00        | 47 - 89                    |
| 2                                                                                          | COAL                        | 12              | 55,807.73            | 55,808.53        | 0.00             | 2                             | 2,285.32             | 2,285.32         | 6 - 48                     |
| 3                                                                                          | MINES                       | 1               | 5,540.00             | 5,540.00         | 0.00             | 0                             | 0.00                 | 0.00             | -                          |
| 4                                                                                          | STEEL                       | 9               | 48,466.31            | 48,150.68        | -0.65            | 5                             | 25,438.49            | 25,080.49        | 5 - 55                     |
| 5                                                                                          | PETROLEUM                   | 42              | 1,67,666.77          | 1,66,989.32      | -0.40            | 4                             | 7,889.71             | 8,918.36         | 23 - 74                    |
| 6                                                                                          | POWER                       | 66              | 3,49,353.13          | 3,72,500.82      | 6.63             | 25                            | 1,55,489.80          | 1,64,906.00      | 3 - 111                    |
| 7                                                                                          | HEAVY INDUSTRY              | 1               | 1,718.00             | 3,827.30         | 122.78           | 1                             | 1,718.00             | 3,827.30         | 75 - 75                    |
| 8                                                                                          | RAILWAYS                    | 130             | 2,76,483.57          | 3,45,927.66      | 25.12            | 27                            | 42,411.18            | 1,09,001.76      | 0 - 261                    |
| 9                                                                                          | ROAD TRANSPORT AND HIGHWAYS | 102             | 1,48,606.06          | 1,54,042.12      | 3.66             | 28                            | 42,392.58            | 45,879.22        | 15 - 76                    |
| 10                                                                                         | SHIPPING AND PORTS          | 1               | 2,427.40             | 2,427.40         | 0.00             | 0                             | 0.00                 | 0.00             | -                          |
| 11                                                                                         | TELECOMMUNICATIONS          | 2               | 15,445.17            | 26,675.17        | 72.71            | 1                             | 13,334.00            | 24,664.00        | 47 - 47                    |
| 12                                                                                         | URBAN DEVELOPMENT           | 11              | 1,52,083.17          | 1,51,298.94      | -0.52            | 5                             | 61,555.16            | 60,916.93        | 5 - 29                     |
| Total                                                                                      |                             | 380             | 12,53,053.31         | 13,62,966.94     | 8.77             | 101                           | 3,81,970.24          | 4,75,258.38      |                            |

\$- Time overrun = Anticipated Date of Commissioning minus latest schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus latest Cost.

**TABLE-21**

| Extent of cost overrun in projects with respect to latest schedule RS.1000 Crore and above |                             |                 |                      |                  |                  |                                          |                      |                  |                  |
|--------------------------------------------------------------------------------------------|-----------------------------|-----------------|----------------------|------------------|------------------|------------------------------------------|----------------------|------------------|------------------|
| (All Cost/ Expenditure in Rs. crore)                                                       |                             |                 |                      |                  |                  |                                          |                      |                  |                  |
|                                                                                            |                             |                 |                      |                  |                  | Projects with cost overruns <sup>^</sup> |                      |                  |                  |
| Sl.No.                                                                                     | Sector                      | No. of projects | Latest Approved Cost | Anticipated Cost | Cost overrun (%) | No.                                      | Latest Approved Cost | Anticipated Cost | Cost overrun (%) |
| 1                                                                                          | ATOMIC ENERGY               | 3               | 29,456.00            | 29,779.00        | 1.10             | 1                                        | 5,677.00             | 6,000.00         | 5.69             |
| 2                                                                                          | COAL                        | 12              | 55,807.73            | 55,808.53        | 0.00             | 1                                        | 17,237.00            | 17,237.80        | 0.00             |
| 3                                                                                          | MINES                       | 1               | 5,540.00             | 5,540.00         | 0.00             | 0                                        | 0.00                 | 0.00             | 0.00             |
| 4                                                                                          | STEEL                       | 9               | 48,466.31            | 48,150.68        | -0.65            | 1                                        | 1,070.97             | 1,113.34         | 3.96             |
| 5                                                                                          | PETROLEUM                   | 42              | 1,67,666.77          | 1,66,989.32      | -0.40            | 5                                        | 11,374.26            | 14,442.84        | 26.98            |
| 6                                                                                          | POWER                       | 66              | 3,49,353.13          | 3,72,500.82      | 6.63             | 11                                       | 49,799.02            | 72,946.71        | 46.48            |
| 7                                                                                          | HEAVY INDUSTRY              | 1               | 1,718.00             | 3,827.30         | 122.78           | 1                                        | 1,718.00             | 3,827.30         | 122.78           |
| 8                                                                                          | RAILWAYS                    | 130             | 2,76,483.57          | 3,45,927.66      | 25.12            | 78                                       | 82,004.48            | 2,08,223.86      | 153.92           |
| 9                                                                                          | ROAD TRANSPORT AND HIGHWAYS | 102             | 1,48,606.06          | 1,54,042.12      | 3.66             | 15                                       | 17,413.21            | 22,849.27        | 31.22            |
| 10                                                                                         | SHIPPING AND PORTS          | 1               | 2,427.40             | 2,427.40         | 0.00             | 0                                        | 0.00                 | 0.00             | 0.00             |
| 11                                                                                         | TELECOMMUNICATIONS          | 2               | 15,445.17            | 26,675.17        | 72.71            | 1                                        | 13,334.00            | 24,664.00        | 84.97            |
| 12                                                                                         | URBAN DEVELOPMENT           | 11              | 1,52,083.17          | 1,51,298.94      | -0.52            | 0                                        | 0.00                 | 0.00             | 0.00             |
|                                                                                            |                             |                 |                      |                  |                  |                                          |                      |                  |                  |
| Total                                                                                      |                             | 380             | 12,53,053.31         | 13,62,966.94     | 8.77             | 114                                      | 1,99,627.94          | 3,71,305.12      | 86.00            |

<sup>^</sup> - Cost Overrun = Anticipated Cost minus latest Cost.

**TABLE-22**

| Extent of time & cost overrun in projects with respect to latest schedule Rs. 1000 Crore and above |                             |                 |                      |                  |                  |                                       |                      |                  |                            |
|----------------------------------------------------------------------------------------------------|-----------------------------|-----------------|----------------------|------------------|------------------|---------------------------------------|----------------------|------------------|----------------------------|
| (All Cost/ Expenditure in Rs. crore)                                                               |                             |                 |                      |                  |                  |                                       |                      |                  |                            |
|                                                                                                    |                             |                 |                      |                  |                  | Projects with time\$ & cost overruns^ |                      |                  |                            |
| Sl.No.                                                                                             | Sector                      | No. of projects | Latest Approved Cost | Anticipated Cost | Cost Overrun (%) | No.                                   | Latest Approved Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1                                                                                                  | ATOMIC ENERGY               | 3               | 29,456.00            | 29,779.00        | 1.10             | 1                                     | 5,677.00             | 6,000.00         | 89- 89                     |
| 2                                                                                                  | COAL                        | 12              | 55,807.73            | 55,808.53        | 0.00             | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| 3                                                                                                  | MINES                       | 1               | 5,540.00             | 5,540.00         | 0.00             | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| 4                                                                                                  | STEEL                       | 9               | 48,466.31            | 48,150.68        | -0.65            | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| 5                                                                                                  | PETROLEUM                   | 42              | 1,67,666.77          | 1,66,989.32      | -0.40            | 2                                     | 1,864.35             | 2,893.00         | 32- 69                     |
| 6                                                                                                  | POWER                       | 66              | 3,49,353.13          | 3,72,500.82      | 6.63             | 7                                     | 27,615.50            | 37,031.70        | 11- 111                    |
| 7                                                                                                  | HEAVY INDUSTRY              | 1               | 1,718.00             | 3,827.30         | 122.78           | 1                                     | 1,718.00             | 3,827.30         | 75- 75                     |
| 8                                                                                                  | RAILWAYS                    | 130             | 2,76,483.57          | 3,45,927.66      | 25.12            | 19                                    | 25,099.49            | 90,675.66        | 34- 261                    |
| 9                                                                                                  | ROAD TRANSPORT AND HIGHWAYS | 102             | 1,48,606.06          | 1,54,042.12      | 3.66             | 4                                     | 4,847.10             | 8,333.74         | 22- 76                     |
| 10                                                                                                 | SHIPPING AND PORTS          | 1               | 2,427.40             | 2,427.40         | 0.00             | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| 11                                                                                                 | TELECOMMUNICATIONS          | 2               | 15,445.17            | 26,675.17        | 72.71            | 1                                     | 13,334.00            | 24,664.00        | 47- 47                     |
| 12                                                                                                 | URBAN DEVELOPMENT           | 11              | 1,52,083.17          | 1,51,298.94      | -0.52            | 0                                     | 0.00                 | 0.00             | 0- 0                       |
| Total                                                                                              |                             | 380             | 12,53,053.31         | 13,62,966.94     | 8.77             | 35                                    | 80,155.44            | 1,73,425.40      |                            |

\$- Time overrun = Anticipated Date of Commissioning minus latest schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus latest Cost.

**TABLE-23**

| Extent of time & cost overrun in projects with respect to original schedule Rs. 1000 Crore and above |                             |                 |               |                  |                  |                                       |               |                  |                            |
|------------------------------------------------------------------------------------------------------|-----------------------------|-----------------|---------------|------------------|------------------|---------------------------------------|---------------|------------------|----------------------------|
| (All Cost/ Expenditure in Rs. crore)                                                                 |                             |                 |               |                  |                  |                                       |               |                  |                            |
|                                                                                                      |                             |                 |               |                  |                  | Projects with time\$ & cost overruns^ |               |                  |                            |
| Sl.No.                                                                                               | Sector                      | No. of projects | Original Cost | Anticipated Cost | Cost Overrun (%) | No.                                   | Original Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1                                                                                                    | ATOMIC ENERGY               | 3               | 27,271.00     | 29,779.00        | 9.20             | 1                                     | 3,492.00      | 6,000.00         | 89- 89                     |
| 2                                                                                                    | COAL                        | 12              | 55,807.73     | 55,808.53        | 0.00             | 0                                     | 0.00          | 0.00             | 0- 0                       |
| 3                                                                                                    | MINES                       | 1               | 5,540.00      | 5,540.00         | 0.00             | 0                                     | 0.00          | 0.00             | 0- 0                       |
| 4                                                                                                    | STEEL                       | 9               | 48,164.22     | 48,150.68        | -0.03            | 0                                     | 0.00          | 0.00             | 0- 0                       |
| 5                                                                                                    | PETROLEUM                   | 42              | 1,65,237.15   | 1,66,989.32      | 1.06             | 7                                     | 17,692.59     | 22,455.62        | 9- 69                      |
| 6                                                                                                    | POWER                       | 66              | 3,16,296.60   | 3,72,500.82      | 17.77            | 23                                    | 81,327.32     | 1,17,211.82      | 11- 136                    |
| 7                                                                                                    | HEAVY INDUSTRY              | 1               | 1,718.00      | 3,827.30         | 122.78           | 1                                     | 1,718.00      | 3,827.30         | 75- 75                     |
| 8                                                                                                    | RAILWAYS                    | 130             | 2,70,626.64   | 3,45,927.66      | 27.82            | 20                                    | 25,594.93     | 92,457.64        | 34- 261                    |
| 9                                                                                                    | ROAD TRANSPORT AND HIGHWAYS | 102             | 1,48,606.06   | 1,54,042.12      | 3.66             | 4                                     | 4,847.10      | 8,333.74         | 22- 76                     |
| 10                                                                                                   | SHIPPING AND PORTS          | 1               | 2,427.40      | 2,427.40         | 0.00             | 0                                     | 0.00          | 0.00             | 0- 0                       |
| 11                                                                                                   | TELECOMMUNICATIONS          | 2               | 15,445.17     | 26,675.17        | 72.71            | 1                                     | 13,334.00     | 24,664.00        | 47- 47                     |
| 12                                                                                                   | URBAN DEVELOPMENT           | 11              | 1,39,164.14   | 1,51,298.94      | 8.72             | 2                                     | 15,819.21     | 20,650.00        | 5- 24                      |
|                                                                                                      |                             |                 |               |                  |                  |                                       |               |                  |                            |
| Total                                                                                                |                             | 380             | 11,96,304.11  | 13,62,966.94     | 13.93            | 59                                    | 1,63,825.15   | 2,95,600.12      |                            |

\$- Time overrun = Anticipated Date of Commissioning minus original schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus original Cost.



Table-24

| State-Wise Position of Central Sector Projects costing Rs. 1000 Crore and above showing Both Time and Cost Overruns |                   |                 |               |                  |                   |                               |               |                  |                            |
|---------------------------------------------------------------------------------------------------------------------|-------------------|-----------------|---------------|------------------|-------------------|-------------------------------|---------------|------------------|----------------------------|
| (All Cost/ Expenditure in Rs. crore)                                                                                |                   |                 |               |                  |                   |                               |               |                  |                            |
|                                                                                                                     |                   |                 |               |                  |                   | Projects with time overruns\$ |               |                  |                            |
| Sl.No                                                                                                               | State             | No. of Projects | Original Cost | Anticipated cost | Cost Overrun^ (%) | No.                           | Original Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1                                                                                                                   | ANDHRA PRADESH    | 16              | 82,287.82     | 84,885.89        | 3.16              | 1                             | 743.00        | 1,825.00         | 144 - 144                  |
| 2                                                                                                                   | ARUNACHAL PRADESH | 4               | 10,609.32     | 27,330.31        | 157.61            | 2                             | 3,070.89      | 7,517.72         | 55 - 99                    |
| 3                                                                                                                   | ASSAM             | 9               | 21,033.85     | 32,693.76        | 55.43             | 4                             | 8,423.01      | 19,949.18        | 32 - 122                   |
| 4                                                                                                                   | BIHAR             | 13              | 37,034.94     | 51,777.80        | 39.81             | 3                             | 27,010.57     | 36,824.93        | 11 - 98                    |
| 5                                                                                                                   | GUJARAT           | 10              | 23,570.79     | 26,172.48        | 11.04             | 1                             | 1,509.10      | 3,237.87         | 63 - 63                    |
| 6                                                                                                                   | HARYANA           | 4               | 5,634.39      | 6,814.39         | 20.94             | 1                             | 1,108.00      | 2,288.00         | 76 - 76                    |
| 7                                                                                                                   | HIMACHAL PRADESH  | 6               | 12,226.08     | 20,158.36        | 64.88             | 1                             | 3,919.59      | 8,398.75         | 111 - 111                  |
| 8                                                                                                                   | JAMMU AND KASHMIR | 10              | 27,408.66     | 47,277.79        | 72.49             | 3                             | 7,930.45      | 27,799.58        | 12 - 193                   |
| 9                                                                                                                   | KARNATAKA         | 22              | 67,362.06     | 84,410.34        | 25.31             | 1                             | 993.00        | 1,693.00         | 69 - 69                    |
| 10                                                                                                                  | KERALA            | 6               | 15,533.08     | 21,030.60        | 35.39             | 0                             | 0.00          | 0.00             | -                          |
| 11                                                                                                                  | MADHYA PRADESH    | 15              | 38,561.17     | 42,526.03        | 10.28             | 2                             | 2,230.00      | 2,807.87         | 22 - 53                    |
| 12                                                                                                                  | MAHARASHTRA       | 44              | 1,42,261.61   | 1,50,501.32      | 5.79              | 5                             | 14,423.33     | 19,503.64        | 12 - 192                   |
| 13                                                                                                                  | MANIPUR           | 1               | 727.56        | 9,658.00         | 1,227.45          | 1                             | 727.56        | 9,658.00         | 108 - 108                  |
| 14                                                                                                                  | MEGHALAYA         | 2               | 5,577.50      | 7,494.48         | 34.37             | 0                             | 0.00          | 0.00             | -                          |
| 15                                                                                                                  | MIZORAM           | 2               | 988.06        | 5,929.43         | 500.11            | 2                             | 988.06        | 5,929.43         | 71 - 136                   |
| 16                                                                                                                  | NAGALAND          | 3               | 6,420.00      | 8,570.00         | 33.49             | 1                             | 850.00        | 3,000.00         | 60 - 60                    |
| 17                                                                                                                  | ODISHA            | 24              | 56,413.98     | 63,001.36        | 11.68             | 1                             | 183.23        | 1,202.70         | 58 - 58                    |
| 18                                                                                                                  | PUNJAB            | 2               | 2,557.95      | 2,557.95         | 0.00              | 0                             | 0.00          | 0.00             | -                          |
| 19                                                                                                                  | RAJASTHAN         | 7               | 19,624.78     | 19,956.68        | 1.69              | 1                             | 829.74        | 1,161.64         | 57 - 57                    |
| 20                                                                                                                  | SIKKIM            | 1               | 1,339.48      | 4,084.69         | 204.95            | 1                             | 1,339.48      | 4,084.69         | 51 - 51                    |
| 21                                                                                                                  | TAMIL NADU        | 14              | 45,746.76     | 56,934.45        | 24.46             | 4                             | 21,811.42     | 29,947.97        | 24 - 118                   |
| 22                                                                                                                  | TRIPURA           | 3               | 2,129.35      | 6,386.31         | 199.92            | 1                             | 813.34        | 3,451.00         | 72 - 72                    |
| 23                                                                                                                  | UTTAR PRADESH     | 33              | 86,307.66     | 88,855.18        | 2.95              | 0                             | 0.00          | 0.00             | -                          |
| 24                                                                                                                  | WEST BENGAL       | 22              | 44,076.95     | 56,813.51        | 28.90             | 3                             | 11,432.55     | 13,584.49        | 9 - 57                     |
| 25                                                                                                                  | D & N HAVELI      | 1               | 6,086.08      | 5,479.75         | -9.96             | 0                             | 0.00          | 0.00             | -                          |
| 26                                                                                                                  | DELHI             | 4               | 45,462.73     | 45,689.52        | 0.50              | 1                             | 1,219.21      | 1,592.00         | 5 - 5                      |
| 27                                                                                                                  | CHHATISGARH       | 11              | 71,673.86     | 73,381.18        | 2.38              | 1                             | 1,746.65      | 2,228.71         | 40 - 40                    |
| 28                                                                                                                  | JHARKHAND         | 10              | 33,188.25     | 35,781.77        | 7.81              | 1                             | 900.05        | 1,125.89         | 99 - 99                    |
| 29                                                                                                                  | UTTARAKHAND       | 6               | 14,392.36     | 14,868.59        | 3.31              | 2                             | 4,635.48      | 7,785.41         | 58 - 75                    |
| 30                                                                                                                  | TELANGANA         | 6               | 14,904.53     | 16,572.01        | 11.19             | 0                             | 0.00          | 0.00             | -                          |
| 31                                                                                                                  | MULTI STATE       | 69              | 2,55,162.50   | 2,45,373.01      | -3.84             | 15                            | 44,987.44     | 79,002.65        | 20 - 261                   |
| Total                                                                                                               |                   | 380             | 11,96,304.11  | 13,62,966.94     | 13.93             | 59                            | 1,63,825.15   | 2,95,600.12      |                            |

\$- Time overrun = Anticipated Date of Commissioning minus original schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus original Cost.

**TABLE-25**

| <u>List of projects completed/dropped/Frozen during current month</u> Rs. 150 Crore and above |                                                                                                       |         |           |         |                 |         |                   |
|-----------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------|---------|-----------|---------|-----------------|---------|-------------------|
| (All Cost/ Expenditure in Rs. crore)                                                          |                                                                                                       |         |           |         |                 |         |                   |
|                                                                                               |                                                                                                       |         | Original  |         | Now anticipated |         |                   |
| Sl.No                                                                                         | Project                                                                                               | DOA     | Cost      | DOC     | Cost            | DOC     | Final Expenditure |
|                                                                                               | <u>ATOMIC ENERGY</u>                                                                                  |         |           |         |                 |         |                   |
| 1                                                                                             | KUDANKULAM APP (NPCIL) G                                                                              | 12/2001 | 13,171.00 | 12/2008 | 22,462.00       | 09/2017 | 22,340.00         |
|                                                                                               | <u>CIVIL AVIATION</u>                                                                                 |         |           |         |                 |         |                   |
| 2                                                                                             | CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) G                                            | 05/2010 | 335.61    | 05/2012 | 318.00          | 09/2017 | 305.59            |
|                                                                                               | <u>PETROLEUM</u>                                                                                      |         |           |         |                 |         |                   |
| 3                                                                                             | INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES G                          | 05/2015 | 1,714.00  | 06/2017 | 1,417.00        | 09/2017 | 1,067.89          |
| 4                                                                                             | DE-BOTTLENECKING OF SMPL G                                                                            | 12/2009 | 1,584.00  | 03/2017 | 1,584.00        | 09/2017 | 1,355.45          |
| 5                                                                                             | AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE G                                                     | 08/2011 | 586.00    | 08/2015 | 586.00          | 03/2017 | 440.20            |
| 6                                                                                             | MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) G                                                | 02/2012 | 666.00    | 11/2015 | 768.25          | 09/2017 | 606.13            |
| 7                                                                                             | INTEGRATED REFINERY EXPANSION PROJECT G                                                               | 03/2012 | 16,504.00 | 03/2017 | 16,504.00       | 09/2017 | 15,090.99         |
| 8                                                                                             | MARKETING TOP AT KORBA G                                                                              | 01/2011 | 141.86    | 09/2016 | 222.81          | 09/2017 | 174.37            |
|                                                                                               | <u>POWER</u>                                                                                          |         |           |         |                 |         |                   |
| 9                                                                                             | TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B G                   | 03/2011 | 1,585.12  | 11/2013 | 1,585.12        | 09/2017 | 1,452.46          |
| 10                                                                                            | KANDORNA AND BHANWAD WIND FARM G                                                                      | 11/2016 | 415.49    | 03/2017 | 415.50          | 09/2017 | 415.50            |
| 11                                                                                            | TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH G | 11/2011 | 2,127.51  | 07/2014 | 2,619.56        | 09/2017 | 2,582.69          |

| List of projects completed/dropped/Frozen during current month Rs. 150 Crore and above |                                                                       |         |          |         |                 |         |                   |
|----------------------------------------------------------------------------------------|-----------------------------------------------------------------------|---------|----------|---------|-----------------|---------|-------------------|
| (All Cost/ Expenditure in Rs. crore)                                                   |                                                                       |         |          |         |                 |         |                   |
|                                                                                        |                                                                       |         | Original |         | Now anticipated |         |                   |
| Sl.No                                                                                  | Project                                                               | DOA     | Cost     | DOC     | Cost            | DOC     | Final Expenditure |
| 12                                                                                     | WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH G          | 03/2012 | 9,569.76 | 06/2015 | 9,291.03        | 09/2017 | 7,311.17          |
| 13                                                                                     | TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED G | 12/2011 | 552.44   | 02/2014 | 609.44          | 09/2017 | 501.60            |
| 14                                                                                     | TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP G                | 12/2005 | 358.42   | 12/2008 | 358.42          | 09/2017 | 0.00              |
| 15                                                                                     | KBUNL-MUZAFFARPUR TPP STAGE-II-SUBSIDIARY (2X195 MW) G                | 03/2010 | 3,984.03 | 01/2013 | 3,984.03        | 09/2017 | 3,290.44          |
| 16                                                                                     | TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. G    | 08/2014 | 188.75   | 02/2017 | 188.75          | 09/2017 | 0.00              |
| 17                                                                                     | PATAN WIND FARM SITE, GUJARAT 50 MW G                                 | 10/2015 | 315.00   | 10/2016 | 311.96          | 09/2017 | 311.96            |
|                                                                                        |                                                                       |         |          |         |                 |         |                   |

**TABLE-26**

| List of projects added Rs.150 Crore and above |                                                                                                                 |         |          |         | (September 2017) |         |
|-----------------------------------------------|-----------------------------------------------------------------------------------------------------------------|---------|----------|---------|------------------|---------|
|                                               |                                                                                                                 |         | Original |         | Anticipated      |         |
| Sl.No                                         | Project                                                                                                         | DOA     | Cost     | DOC     | Cost             | DOC     |
|                                               |                                                                                                                 |         |          |         |                  |         |
|                                               | <u>PETROLEUM</u>                                                                                                |         |          |         |                  |         |
| 1                                             | INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY Central Sector Projects | 9/2016  | 208.35   | 7/2020  | 208.35           | 7/2020  |
| 2                                             | KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II Central Sector Projects                                   | 6/2009  | 2,915.00 | 12/2012 | 2,915.00         | 2/2019  |
|                                               |                                                                                                                 |         |          |         |                  |         |
|                                               | <u>POWER</u>                                                                                                    |         |          |         |                  |         |
| 3                                             | TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B Central Sector Projects                       | 4/2015  | 2,225.00 | 1/2018  | 2,225.00         | 1/2018  |
| 4                                             | TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V Central Sector Projects                         | 2/2015  | 1,750.00 | 6/2018  | 1,750.00         | 6/2018  |
| 5                                             | STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI Central Sector Projects                                    | 12/2015 | 3,654.00 | 4/2019  | 3,654.00         | 4/2019  |
| 6                                             | EASTERN REGION STRENGTHENING SCHEME- XVIII Central Sector Projects                                              | 3/2017  | 3,500.00 | 7/2020  | 3,500.00         | 7/2020  |
| 7                                             | TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM CUDDALORE AREA – PACKAGE A Central Sector Projects     | 3/2015  | 955.00   | 12/2015 | 1,364.00         | 3/2018  |
| 8                                             | TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-A Central Sector Projects                       | 4/2015  | 2,525.00 | 11/2017 | 2,525.00         | 11/2017 |
|                                               |                                                                                                                 |         |          |         |                  |         |

**TABLE-27**

**Milestones (Cumulative due & achieved) Rs. 150 Crore and above**

|                      |      |
|----------------------|------|
| Total                | 3776 |
| Achieved up to month | 2001 |


**TABLE-28**

| List of projects reporting additional delayed Rs.150 Crore and above |                                                                                                          |                  |             |              |            |            | (September 2017)  |
|----------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------|------------------|-------------|--------------|------------|------------|-------------------|
| Sl. No                                                               | Project name                                                                                             | Cost ( Rs.crore) |             | DOC reported |            |            | Delay (in months) |
|                                                                      |                                                                                                          | Original         | Anticipated | Original     | Last month | This month |                   |
|                                                                      | <u>ATOMIC ENERGY</u>                                                                                     |                  |             |              |            |            |                   |
| 1                                                                    | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)<br>BHAVNI G                                            | 3,492.00         | 6,000.00    | 09/2010      | 10/2017    | 02/2018    | 4                 |
|                                                                      | <u>COAL</u>                                                                                              |                  |             |              |            |            |                   |
| 2                                                                    | NEYVELI SOLAR POWER PROJECT 130 MW<br>NLC G                                                              | 687.28           | 687.28      | 06/2017      | 08/2017    | 10/2017    | 2                 |
| 3                                                                    | MADHUBAND NLW WASHERY<br>BCCL G                                                                          | 289.45           | 289.45      | 05/2014      | 10/2017    | 04/2018    | 6                 |
| 4                                                                    | PATHERDIH NLW WASHERY<br>BCCL G                                                                          | 269.82           | 269.82      | 04/2014      | 10/2017    | 04/2018    | 6                 |
|                                                                      | <u>STEEL</u>                                                                                             |                  |             |              |            |            |                   |
| 5                                                                    | BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS<br>RINL G                                                     | 877.73           | 877.73      | 07/2015      | 09/2017    | 10/2017    | 1                 |
| 6                                                                    | TURBO BLOWER - 5<br>RINL G                                                                               | 280.00           | 280.00      | 09/2016      | 09/2017    | 10/2017    | 1                 |
| 7                                                                    | NMDC INTEGRATED STEEL PLANT<br>NMDC G                                                                    | 15,525.00        | 15,525.00   | 05/2015      | 12/2017    | 10/2018    | 10                |
|                                                                      | <u>PETROLEUM</u>                                                                                         |                  |             |              |            |            |                   |
| 8                                                                    | SONAMURA GGS AND PIPELINE PROJECT ( PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A ONGC G | 215.38           | 215.38      | 06/2017      | 10/2017    | 01/2018    | 3                 |
| 9                                                                    | RESID UPGRADATION PROJECT<br>CPCL G                                                                      | 3,110.36         | 3,110.36    | 11/2015      | 05/2017    | 10/2017    | 5                 |
|                                                                      | <u>POWER</u>                                                                                             |                  |             |              |            |            |                   |
| 10                                                                   | EASTERN REGION STRENGTHENING SCHEME -IX<br>PGCIL G                                                       | 196.58           | 225.28      | 02/2016      | 11/2017    | 12/2017    | 1                 |
| 11                                                                   | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW)<br>PGCIL G                                        | 305.04           | 305.04      | 03/2017      | 10/2017    | 11/2017    | 1                 |
| 12                                                                   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII<br>PGCIL G                                           | 908.08           | 969.97      | 06/2016      | 09/2017    | 11/2017    | 2                 |
| 13                                                                   | STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION<br>PGCIL G                                             | 829.98           | 829.98      | 08/2016      | 10/2017    | 12/2017    | 2                 |


| List of projects reporting additional delayed Rs.150 Crore and above |                                                                                                              |                  |             |              |            | (September 2017) |                   |
|----------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------|------------------|-------------|--------------|------------|------------------|-------------------|
| Sl. No                                                               | Project name                                                                                                 | Cost ( Rs.crore) |             | DOC reported |            |                  | Delay (in months) |
|                                                                      |                                                                                                              | Original         | Anticipated | Original     | Last month | This month       |                   |
| 14                                                                   | AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B<br>PGCIL G                                          | 155.57           | 206.42      | 03/2016      | 10/2017    | 12/2017          | 2                 |
| 15                                                                   | WESTERN REGION STRENGTHENING SCHEME-V<br>PGCIL G                                                             | 477.69           | 738.48      | 09/2010      | 12/2017    | 03/2018          | 3                 |
| 16                                                                   | COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C<br>PGCIL G | 514.20           | 703.10      | 06/2015      | 12/2017    | 03/2018          | 3                 |
| 17                                                                   | TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH<br>PGCIL G         | 5,151.37         | 5,151.37    | 03/2018      | 03/2018    | 06/2018          | 3                 |
| 18                                                                   | MUNPL-MEJA TPP - JV (2X660 MW)<br>NTPC Joint Venture                                                         | 9,750.89         | 9,750.89    | 12/2016      | 03/2018    | 06/2018          | 3                 |
| 19                                                                   | GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B<br>PGCIL G                                    | 3,705.61         | 3,705.61    | 04/2018      | 04/2018    | 07/2018          | 3                 |
| 20                                                                   | ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION<br>PGCIL G                              | 198.63           | 198.63      | 09/2014      | 09/2017    | 01/2018          | 4                 |
| 21                                                                   | NPGCPL-NABINAGAR STPP - JV (3X660 MW)<br>NTPC Joint Venture                                                  | 12,964.60        | 13,731.26   | 01/2018      | 08/2018    | 12/2018          | 4                 |
| 22                                                                   | KANDORNA AND BHANWAD WIND FARM<br>THDCIL G                                                                   | 415.49           | 415.50      | 03/2017      | 03/2017    | 09/2017          | 6                 |
| 23                                                                   | TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD.<br>PGCIL G                                  | 188.75           | 188.75      | 02/2017      | 02/2017    | 09/2017          | 7                 |
| 24                                                                   | PATAN WIND FARM SITE, GUJARAT 50 MW<br>THDCIL G                                                              | 315.00           | 311.96      | 10/2016      | 10/2016    | 09/2017          | 11                |
| 25                                                                   | TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B<br>PGCIL G                 | 1,585.12         | 1,585.12    | 11/2013      | 03/2016    | 09/2017          | 18                |
| 26                                                                   | TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED<br>PGCIL G                               | 552.44           | 609.44      | 02/2014      | 03/2016    | 09/2017          | 18                |
|                                                                      |                                                                                                              |                  |             |              |            |                  |                   |
|                                                                      | <u>RAILWAYS</u>                                                                                              |                  |             |              |            |                  |                   |
| 27                                                                   | BANGURGRAM-GURIYA PATCH DOUBLING<br>NWR G                                                                    | 246.08           | 348.55      | N.A.         | 02/2019    | 03/2019          | 1                 |
| 28                                                                   | AJMER-BANGURGRAM<br>NWR G                                                                                    | 213.39           | 272.99      | N.A.         | 02/2019    | 03/2019          | 1                 |
| 29                                                                   | JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR)<br>NWR G                                   | 653.19           | 941.04      | 03/2014      | 03/2019    | 06/2019          | 3                 |
| 30                                                                   | BHOJIPUR TANAKPUR VIA PILIBHIT<br>NER G                                                                      | 195.64           | 474.30      | N.A.         | 07/2017    | 10/2017          | 3                 |
| 31                                                                   | TALCHER-BIMALAGARH(NL)(ECOR)<br>ECOR G                                                                       | 810.78           | 1,928.07    | N.A.         | 06/2022    | 12/2022          | 6                 |



## Graphical Presentation of All Projects w.r.t. Original Schedule

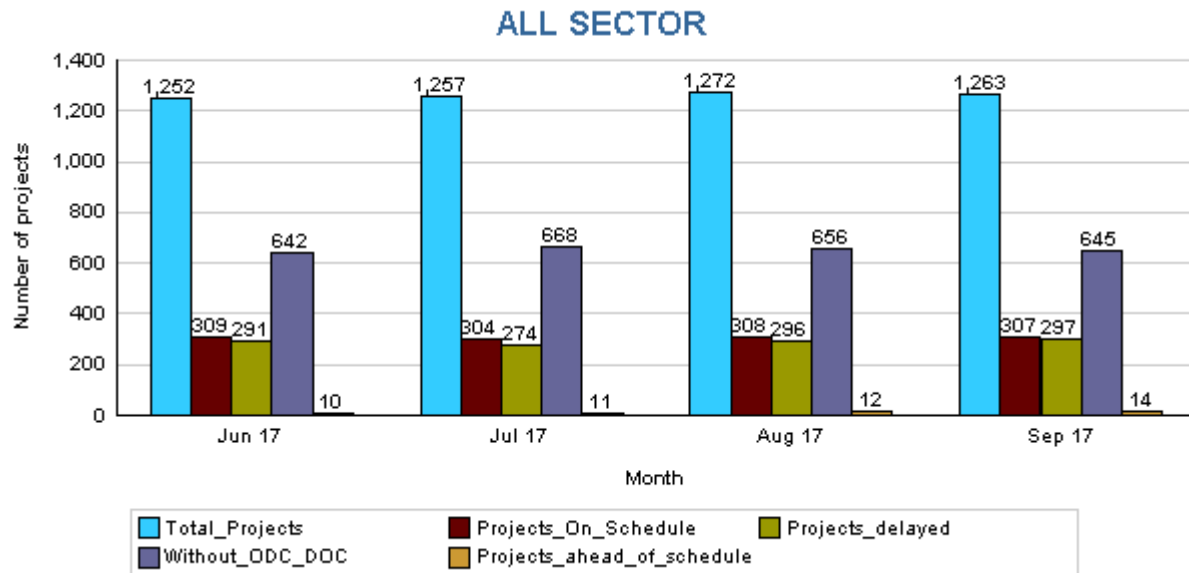

### Break-up of 297 Delayed projects in September 2017

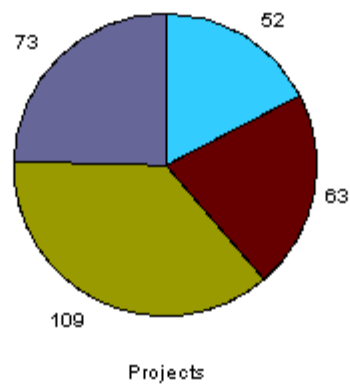


Delay in Months






# Graphical Presentation of All Projects w.r.t. Original Schedule

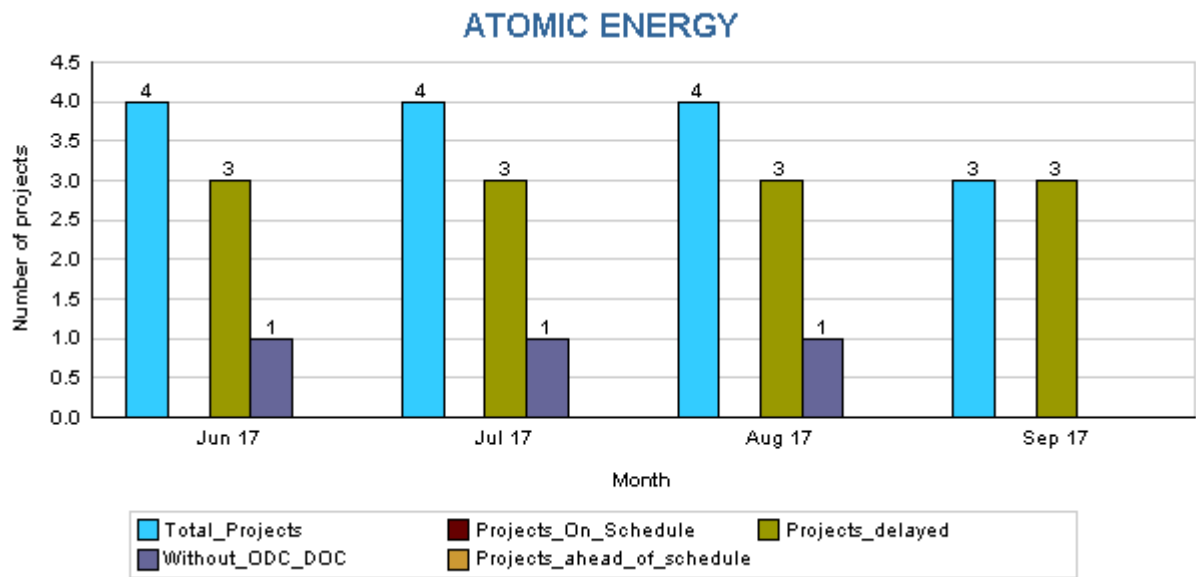


**Break-up of 3 Delayed projects in September 2017**

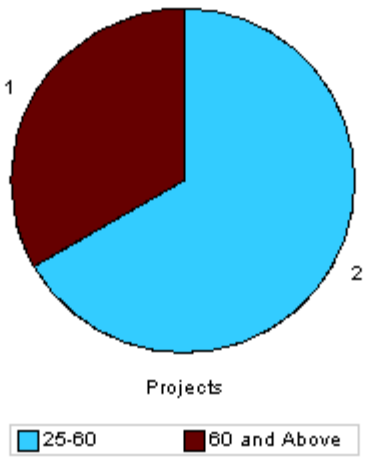


Delay in Months

# Graphical Presentation of All Projects w.r.t. Original Schedule

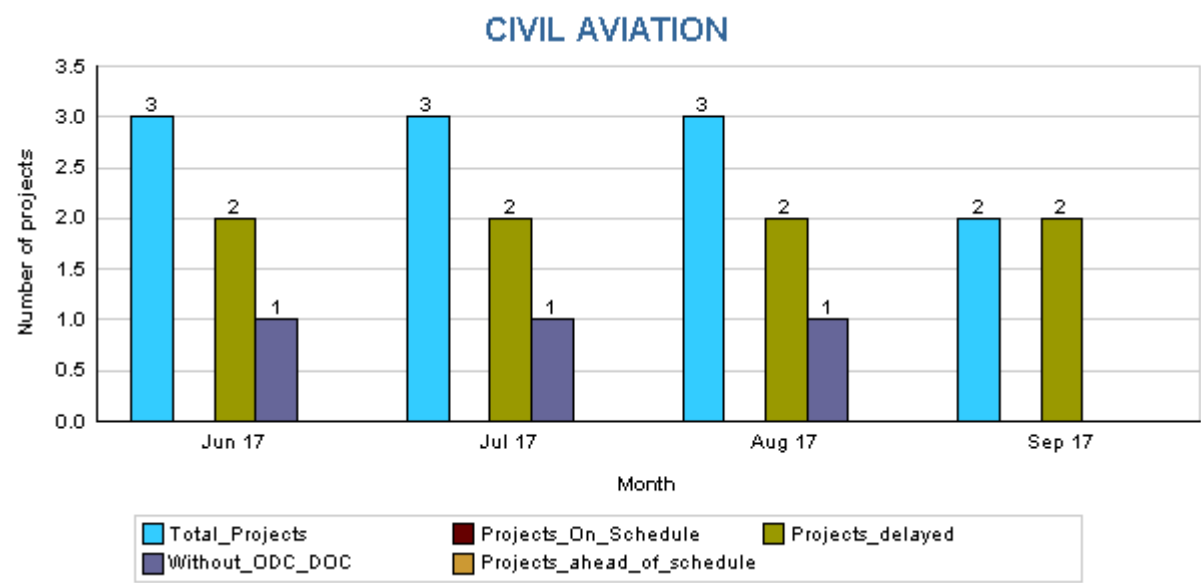


Break-up of 2 Delayed projects in September 2017

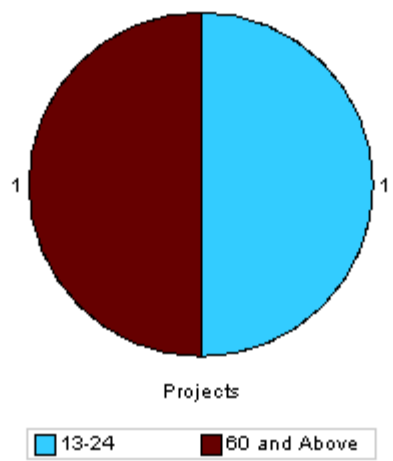


Delay in Months

# Graphical Presentation of All Projects w.r.t. Original Schedule

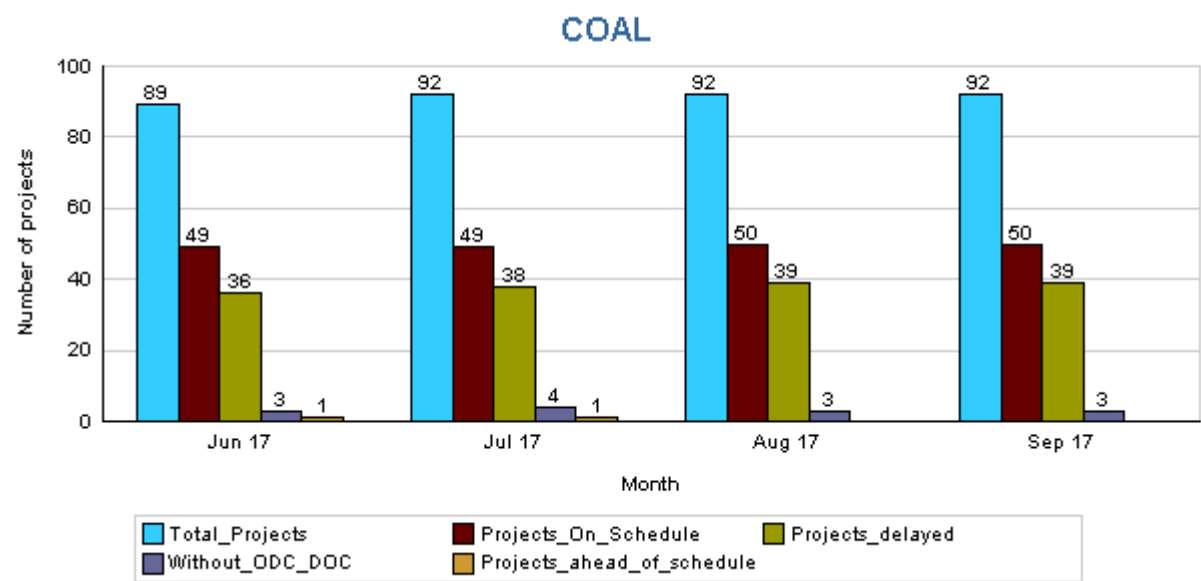


Break-up of 39 Delayed projects in September 2017

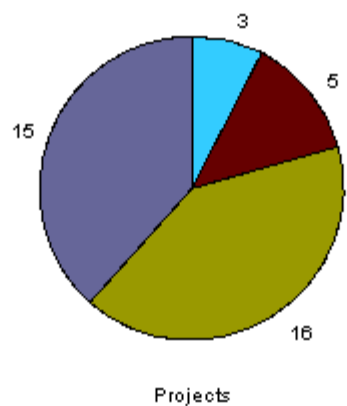


Delay in Months


# Graphical Presentation of All Projects w.r.t. Original Schedule

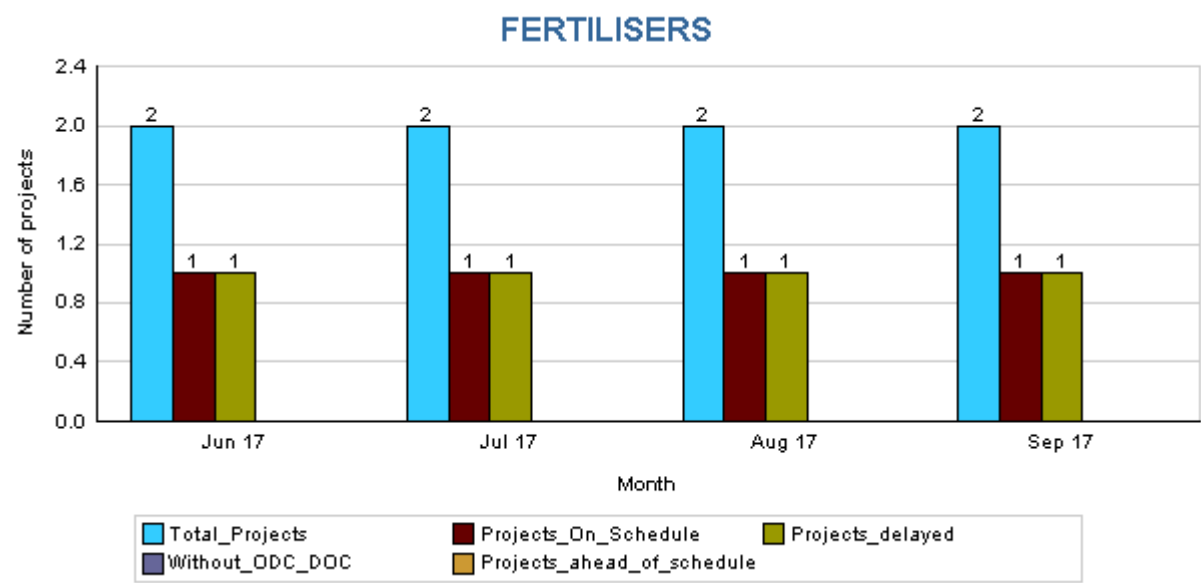


**Break-up of 1 Delayed projects in September 2017**



Delay in Months




# Graphical Presentation of All Projects w.r.t. Original Schedule

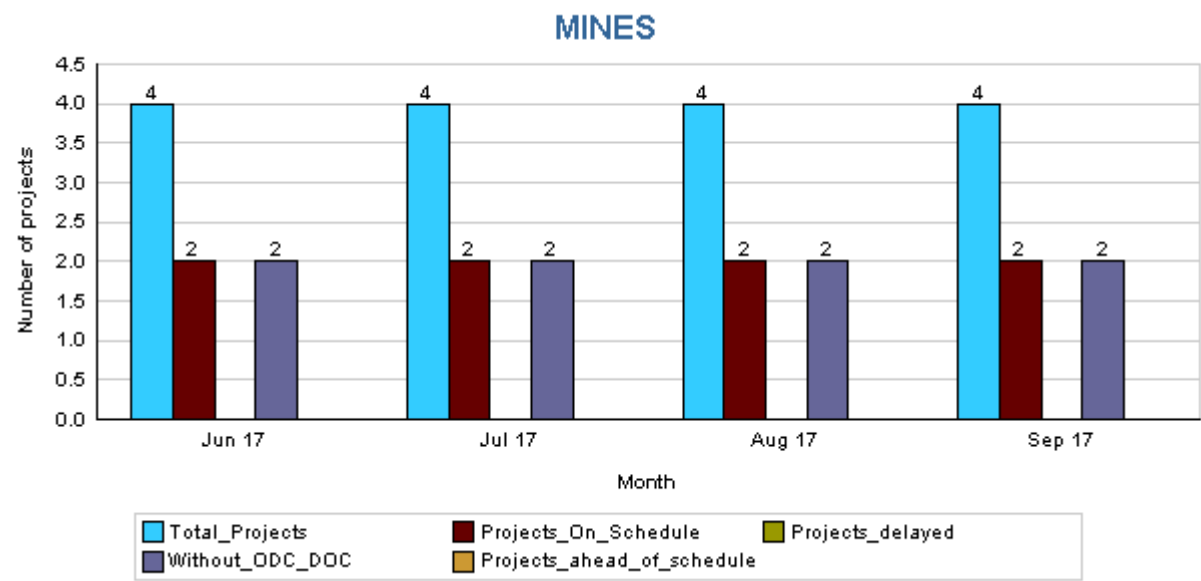


Delay in Months

## Graphical Presentation of All Projects w.r.t. Original Schedule

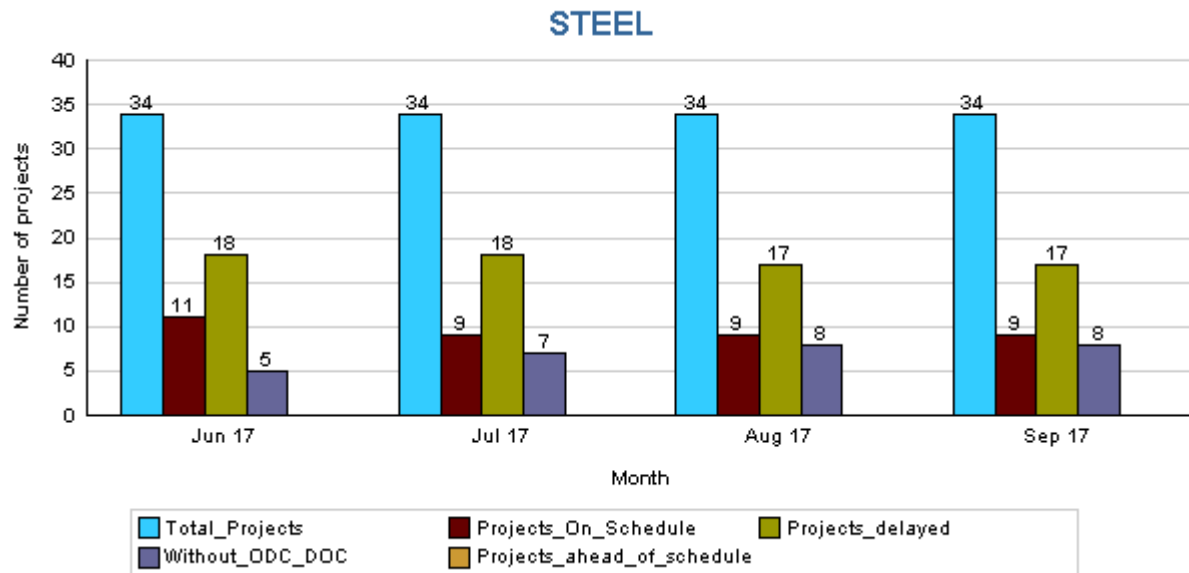


**Break-up of 17 Delayed projects in September 2017**

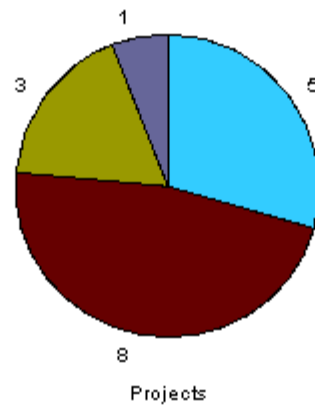


Delay in Months



## Graphical Presentation of All Projects w.r.t. Original Schedule

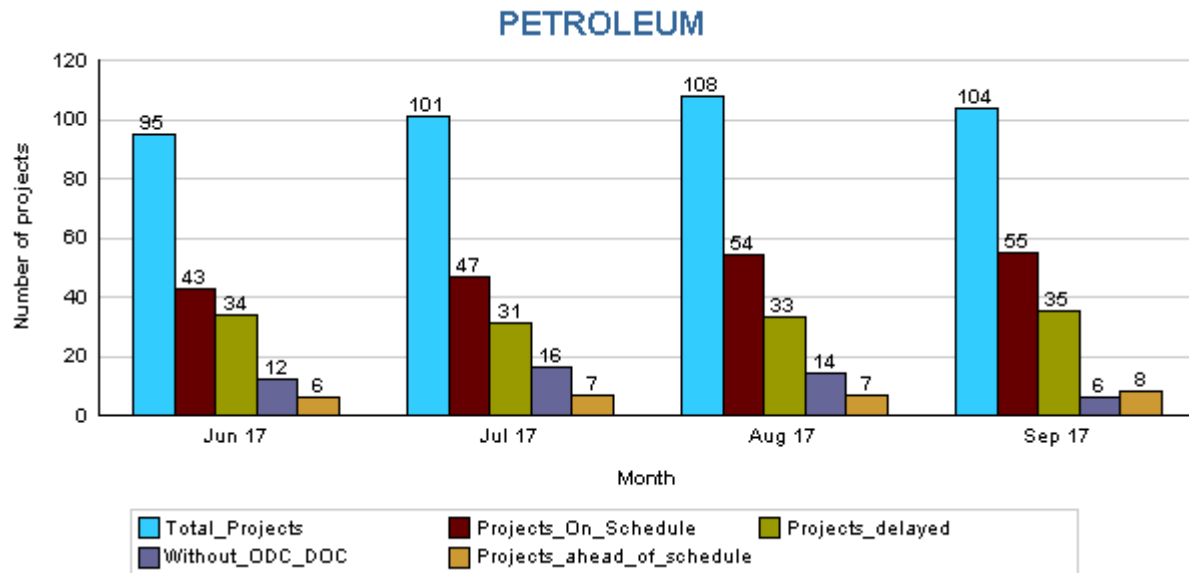


**Break-up of 35 Delayed projects in September 2017**

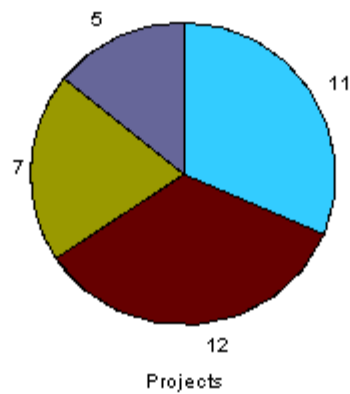


Delay in Months



# Graphical Presentation of All Projects w.r.t. Original Schedule

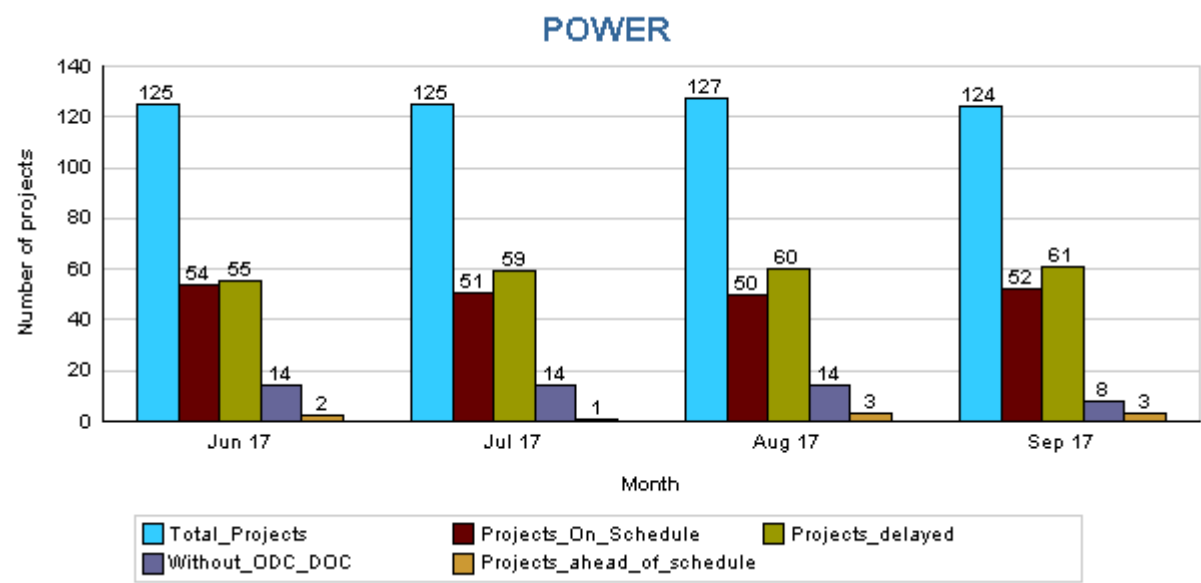

**Break-up of 61 Delayed projects in September 2017**

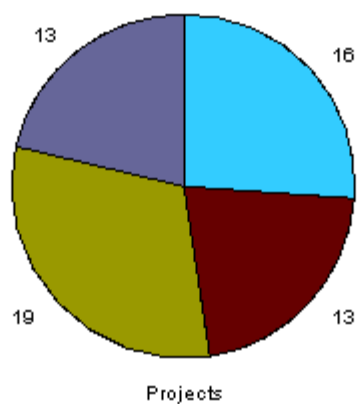


Delay in Months







# Graphical Presentation of All Projects w.r.t. Original Schedule

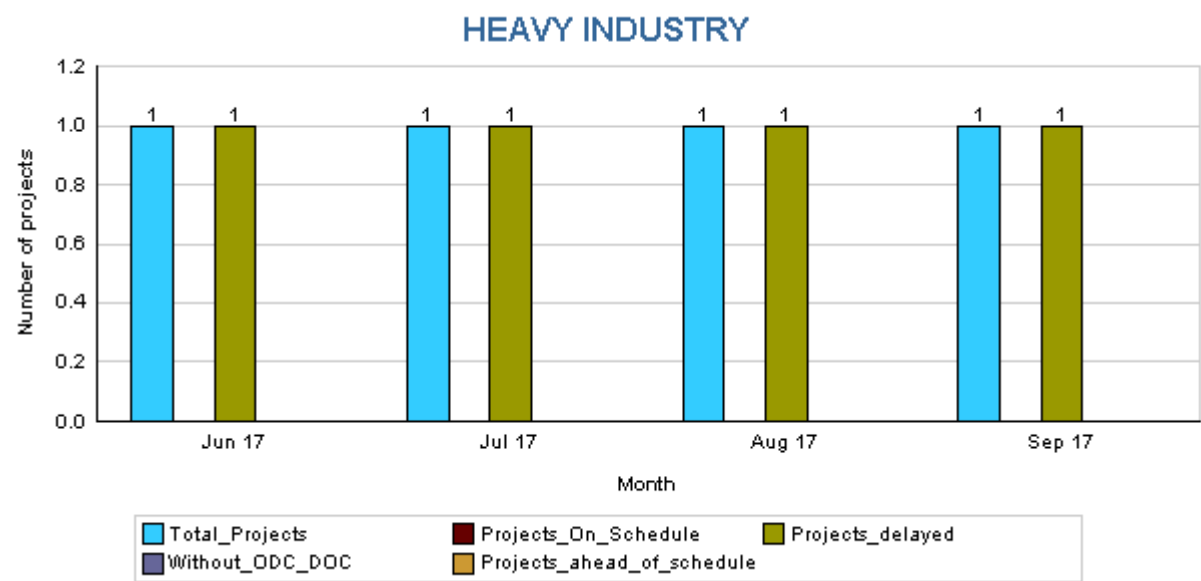


Break-up of 1 Delayed projects in September 2017




Delay in Months



# Graphical Presentation of All Projects w.r.t. Original Schedule

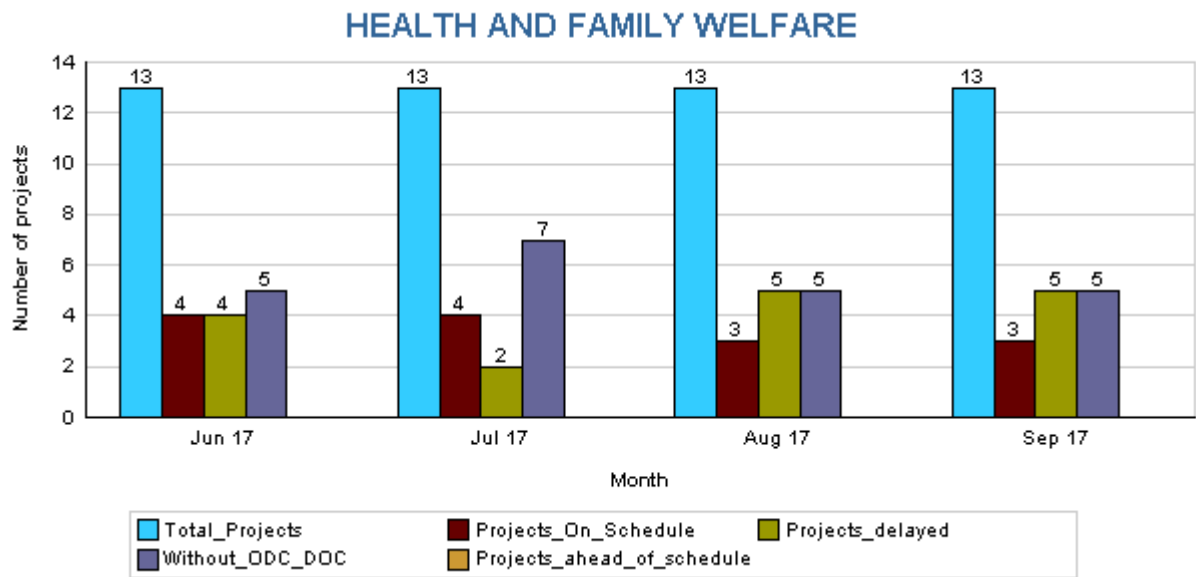


Break-up of 5 Delayed projects in September 2017

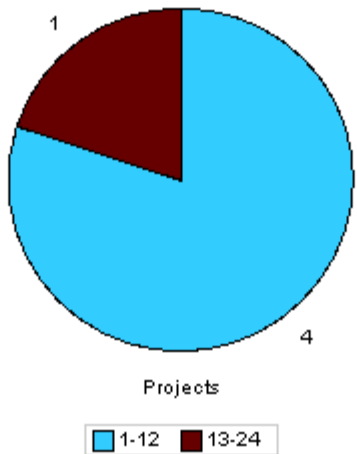


Delay in Months


# Graphical Presentation of All Projects w.r.t. Original Schedule

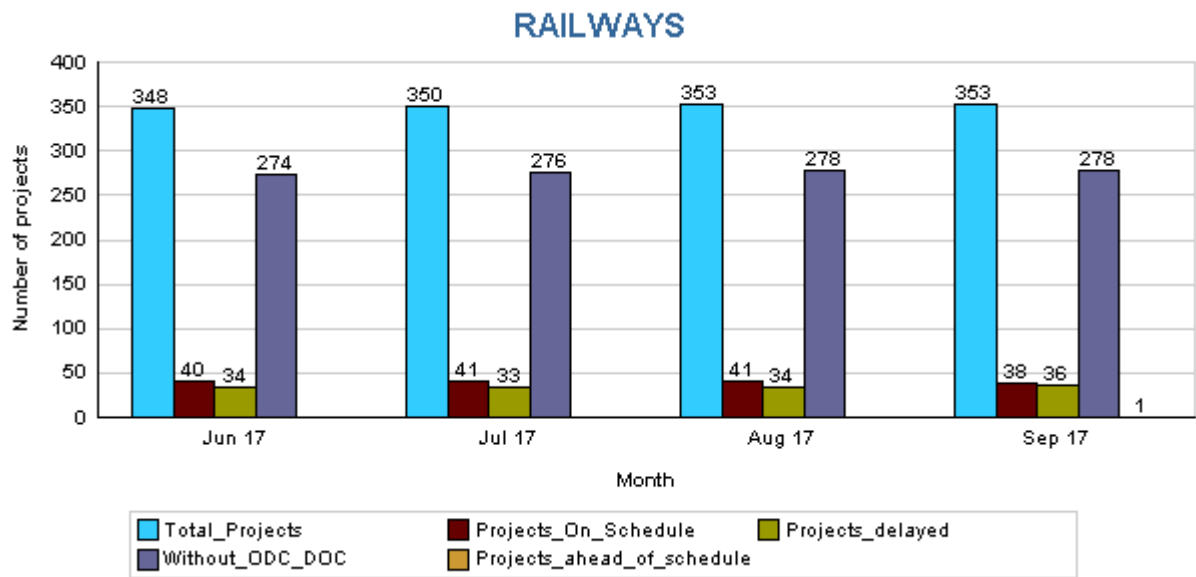


**Break-up of 36 Delayed projects in September 2017**

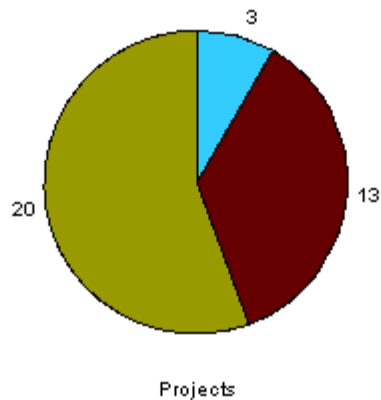


Delay in Months



# Graphical Presentation of All Projects w.r.t. Original Schedule

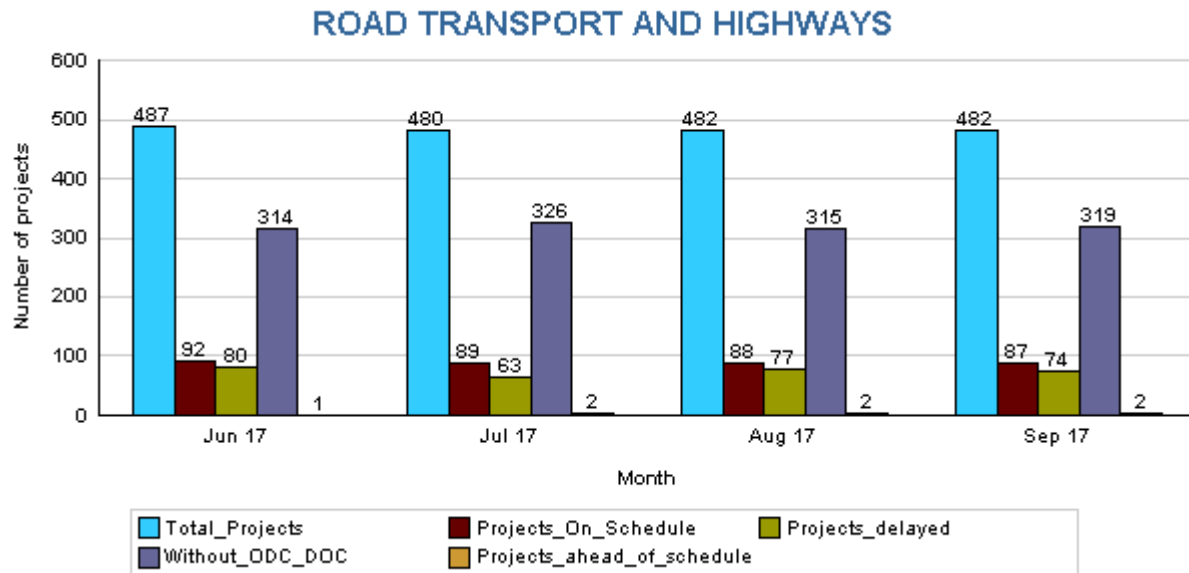


**Break-up of 74 Delayed projects in September 2017**

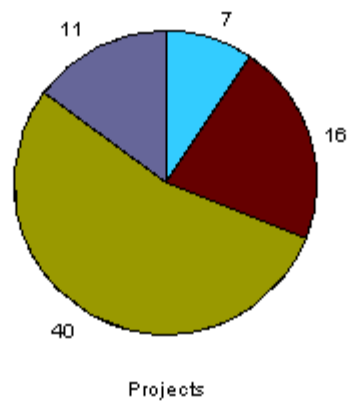


Delay in Months




# Graphical Presentation of All Projects w.r.t. Original Schedule

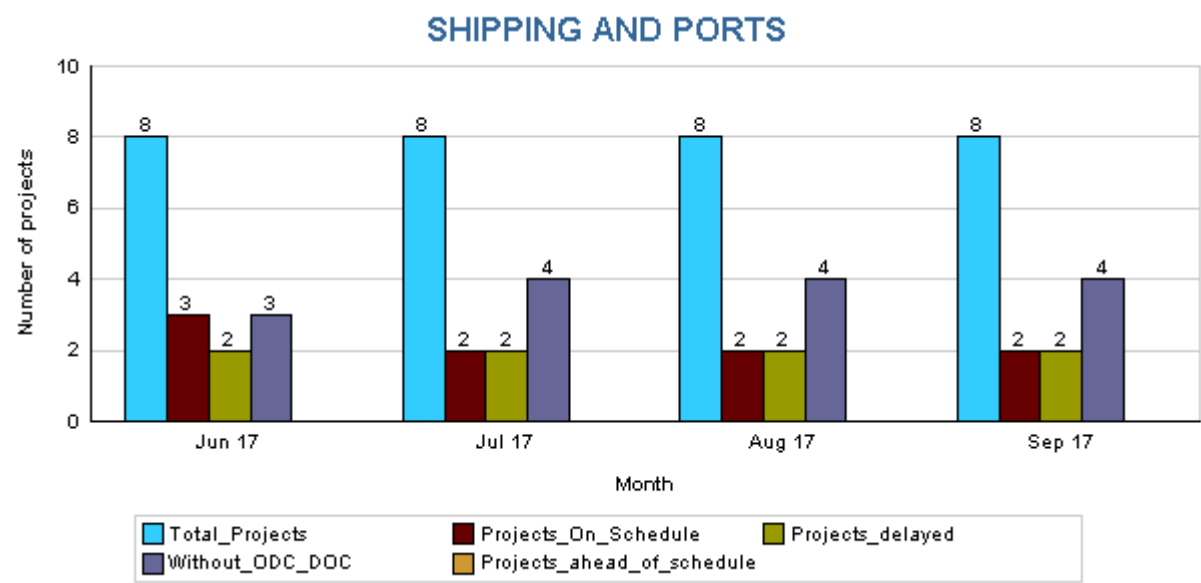


Break-up of 2 Delayed projects in September 2017

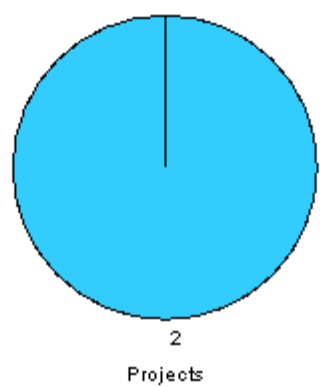


Delay in Months



# Graphical Presentation of All Projects w.r.t. Original Schedule

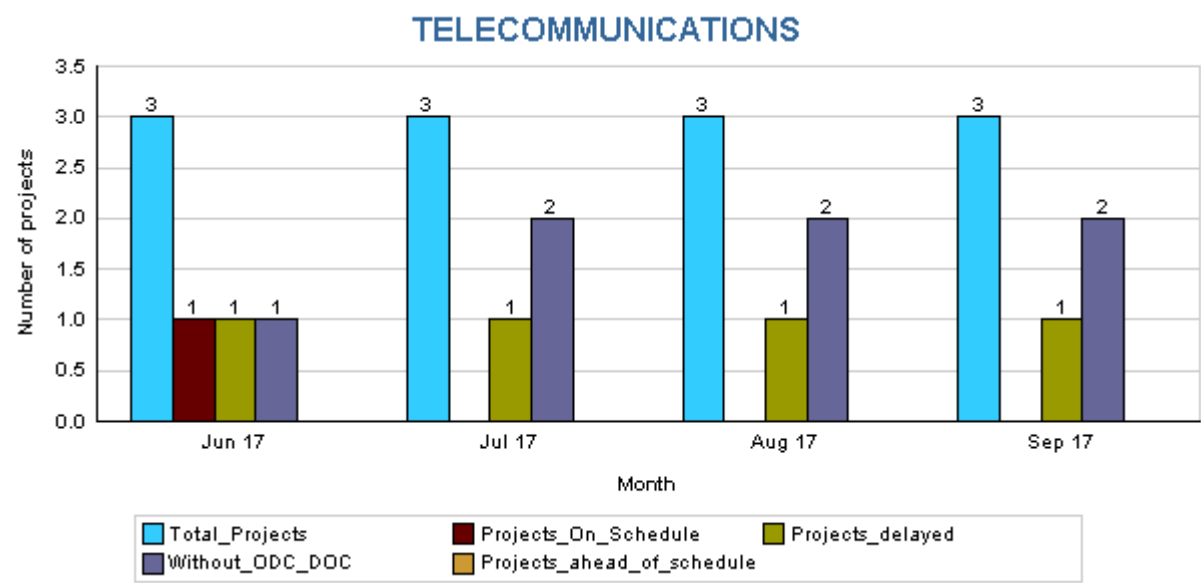


Break-up of 1 Delayed projects in September 2017




Delay in Months

## Graphical Presentation of All Projects w.r.t. Original Schedule

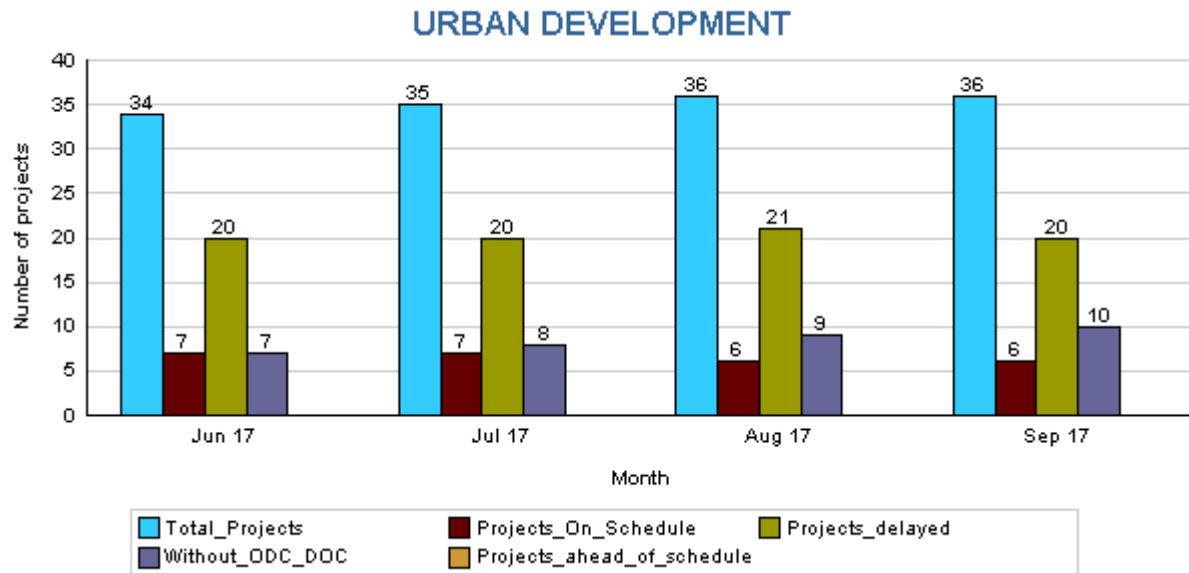


**Break-up of 20 Delayed projects in September 2017**

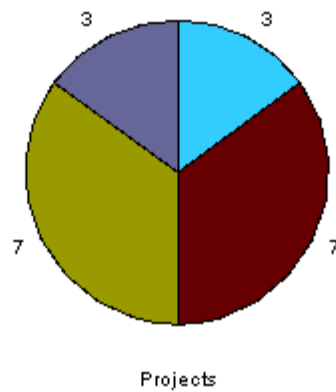

Delay in Months



# Graphical Presentation of All Projects w.r.t. Original Schedule

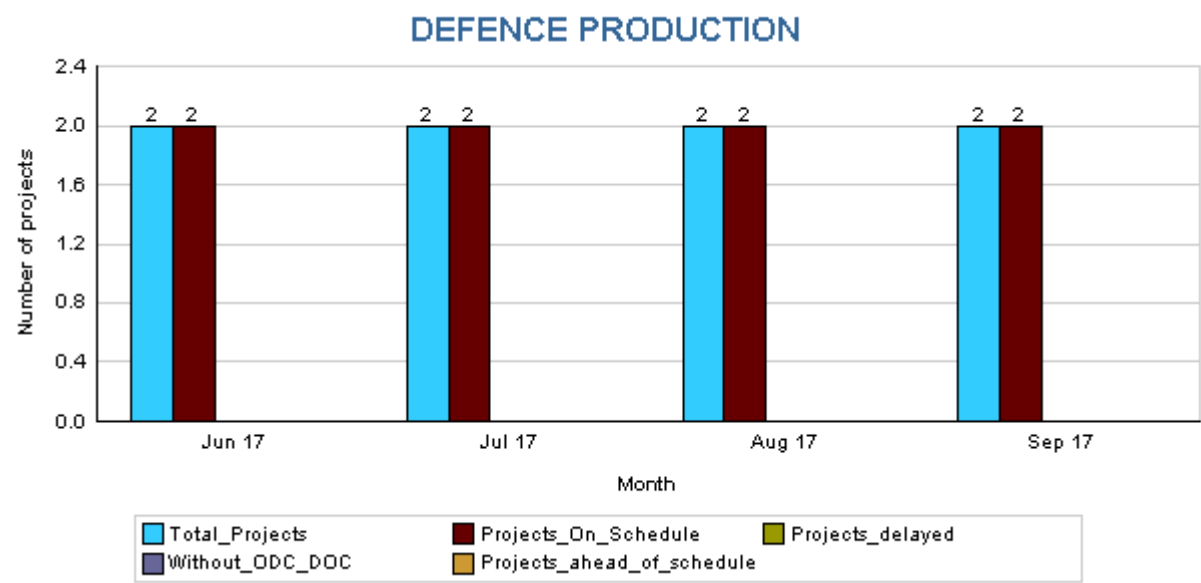

Delay in Months



**TABLE-29**

| <u>Sector wise analysis of projects</u> Rs.150 Crore and above |                    |                  |              |              |                        |
|----------------------------------------------------------------|--------------------|------------------|--------------|--------------|------------------------|
|                                                                |                    | Cost (Rs. crore) |              |              |                        |
| Sector                                                         | Number of projects | Original         | Latest       | Anticipated  | Cumulative Expenditure |
| ATOMIC ENERGY                                                  | 3                  | 27,271.00        | 294,56.00    | 29,779.00    | 24,508.27              |
| CIVIL AVIATION                                                 | 2                  | 624.07           | 6,24.07      | 994.86       | 508.89                 |
| COAL                                                           | 92                 | 88,124.99        | 882,48.46    | 88,310.36    | 21,448.64              |
| FERTILISERS                                                    | 2                  | 680.64           | 6,92.29      | 703.44       | 482.90                 |
| MINES                                                          | 4                  | 6,773.63         | 67,73.63     | 6,773.63     | 372.63                 |
| STEEL                                                          | 34                 | 57,349.49        | 577,30.46    | 57,563.17    | 39,026.87              |
| PETROLEUM                                                      | 104                | 1,90,142.65      | 1,923,98.27  | 1,91,522.05  | 52,758.11              |
| POWER                                                          | 124                | 3,39,545.24      | 3,738,08.24  | 3,97,302.11  | 2,24,764.86            |
| HEAVY INDUSTRY                                                 | 1                  | 1,718.00         | 17,18.00     | 3,827.30     | 2,289.00               |
| HEALTH AND FAMILY WELFARE                                      | 13                 | 3,637.08         | 36,37.08     | 3,649.38     | 1,792.95               |
| RAILWAYS                                                       | 353                | 3,54,063.17      | 3,631,69.43  | 4,54,173.45  | 1,30,576.24            |
| ROAD TRANSPORT AND HIGHWAYS                                    | 482                | 3,17,373.88      | 3,179,47.90  | 3,23,746.08  | 1,00,653.00            |
| SHIPPING AND PORTS                                             | 8                  | 4,117.75         | 41,31.25     | 5,085.02     | 1,875.38               |
| TELECOMMUNICATIONS                                             | 3                  | 15,863.43        | 158,63.43    | 27,093.43    | 6,913.90               |
| URBAN DEVELOPMENT                                              | 36                 | 1,45,945.23      | 1,592,15.64  | 1,58,435.24  | 71,777.57              |
| DEFENCE PRODUCTION                                             | 2                  | 453.64           | 4,54.00      | 469.04       | 52.17                  |
|                                                                |                    |                  |              |              |                        |
| Grand total                                                    | 1263               | 15,53,683.89     | 16,15,868.15 | 17,49,427.56 | 6,79,801.38            |

TABLE-30

| Detail of ongoing Projects Costing Rs.150 Crore and above. |                                                                                                                            |                  |                         |                  |                             | (All Cost/ Expenditure in Rs. Crore) |             |                                            |                             |
|------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|--------------------------------------|-------------|--------------------------------------------|-----------------------------|
|                                                            |                                                                                                                            |                  |                         |                  |                             | Date of Commissioning                |             | (September 2017)                           |                             |
| Sl.No                                                      | Project                                                                                                                    | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised                   | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1                                                          | 2                                                                                                                          | 3                | 4                       | 5                | 6                           | 7                                    | 8           | 9                                          | 10                          |
|                                                            | ATOMIC ENERGY                                                                                                              |                  |                         |                  |                             |                                      |             |                                            |                             |
| 1                                                          | KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT , G                                                     | 10/2009          | 11,459.00 -             | 11,459.00        | 10,710.00                   | 12/2015 11/2016                      | 11/2019     | 47(O) 36(R)                                | 46/70                       |
| 2                                                          | RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN , G                                        | 10/2009          | 12,320.00 -             | 12,320.00        | 8,312.00                    | 12/2016 03/2017                      | 12/2020     | 48(O) 45(R)                                | 34/68                       |
| 3                                                          | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU , G                                       | 09/2003          | 3,492.00 5,677.00       | 6,000.00         | 5,486.27                    | 09/2010 09/2016                      | 02/2018     | 89(O) 17(R)                                | 83/87                       |
|                                                            | Total                                                                                                                      |                  | 27,271.00 -             | 29,779.00        | 24,508.27                   |                                      |             |                                            | 163/225                     |
|                                                            | CIVIL AVIATION                                                                                                             |                  |                         |                  |                             |                                      |             |                                            |                             |
| 4                                                          | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT , PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS , G | 10/2013          | 314.61 -                | 441.33           | 24.13                       | 09/2018 -                            | 06/2020     | 21(O) -                                    | 0/0                         |
| 5                                                          | CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM , G                                         | 01/2009          | 309.46 -                | 553.53           | 484.76                      | 01/2011 09/2017                      | 09/2017     | 80(O) 0(R)                                 | 0/0                         |
|                                                            | Total                                                                                                                      |                  | 624.07 -                | 994.86           | 508.89                      |                                      |             |                                            | 0/0                         |
|                                                            | COAL                                                                                                                       |                  |                         |                  |                             |                                      |             |                                            |                             |
| 6                                                          | GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH , G                                                   | 06/2010          | 11,816.40 -             | 11,816.40        | 2,485.40                    | 03/2023 -                            | 03/2023     | 0(O) -                                     | 12/17                       |
| 7                                                          | KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH , G                                                        | 08/2013          | 7,612.33 -              | 7,612.33         | 1,271.99                    | 03/2023 -                            | 03/2023     | 0(O) -                                     | 3/19                        |
| 8                                                          | PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH , G                                                                      | 11/2014          | 1,624.59 -              | 1,624.59         | 5.73                        | 03/2023 -                            | 03/2023     | 0(O) -                                     | 1/11                        |
| 9                                                          | JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH , G                                                                | 09/2008          | 152.43 459.49           | 459.49           | 80.03                       | 03/2015 03/2020                      | 03/2020     | 60(O) 0(R)                                 | 2/8                         |
| 10                                                         | KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH , G                                                            | 07/2008          | 178.44 -                | 178.44           | 5.12                        | 03/2014 -                            | 03/2020     | 72(O) -                                    | 1/7                         |
| 11                                                         | MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH , G                                                          | 12/2009          | 321.50 -                | 321.50           | 198.19                      | 03/2014 -                            | 03/2018     | 48(O) -                                    | 0/3                         |
| 12                                                         | AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH , G                                                   | 11/2009          | 198.59 -                | 198.59           | 169.38                      | 03/2016 -                            | 03/2018     | 24(O) -                                    | 5/8                         |
| 13                                                         | BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH , G                                                          | 04/2012          | 258.56 -                | 258.56           | 151.94                      | 03/2016 -                            | 03/2018     | 24(O) -                                    | 3/7                         |
| 14                                                         | CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH , G                                                            | 12/2013          | 610.63 -                | 610.63           | 29.03                       | 03/2022 -                            | 03/2022     | 0(O) -                                     | 1/8                         |
| 15                                                         | BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH , G                                                                 | 05/2014          | 164.49 -                | 164.49           | 46.52                       | 03/2020 -                            | 03/2020     | 0(O) -                                     | 3/7                         |
| 16                                                         | AMERA OC RCE - [N06000123]SECL,CHHATISGARH , G                                                                             | 02/2015          | 335.97 -                | 335.97           | 49.00                       | 03/2018 -                            | 03/2018     | 0(O) -                                     | 1/6                         |
| 17                                                         | AMGAON OPENCAST PROJECT RCE - [N06000135]SECL,CHHATISGARH , G                                                              | 07/2015          | 316.10 -                | 316.10           | 34.94                       | 03/2020 -                            | 03/2020     | 0(O) -                                     | 0/5                         |
| 18                                                         | DURGAPUR OPENCAST PROJECT - [N06000136]SECL,CHHATISGARH , G                                                                | 02/2015          | 916.24 -                | 916.24           | .71                         | 03/2023 -                            | 03/2023     | 0(O) -                                     | 1/9                         |

| Detail of ongoing Projects Costing Rs.150 Crore and above. |                                                                                            |                  |                         |                  |                             | (All Cost/ Expenditure in Rs. Crore) |             |                                            |                             |
|------------------------------------------------------------|--------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|--------------------------------------|-------------|--------------------------------------------|-----------------------------|
|                                                            |                                                                                            |                  |                         |                  |                             | Date of Commissioning                |             | (September 2017)                           |                             |
| Sl.No                                                      | Project                                                                                    | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised                   | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1                                                          | 2                                                                                          | 3                | 4                       | 5                | 6                           | 7                                    | 8           | 9                                          | 10                          |
| 19                                                         | MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH , G                              | 10/2015          | 1,875.32 -              | 1,875.32         | -                           | 03/2024 -                            | 03/2024     | 0(O) -                                     | 0/3                         |
| 20                                                         | VIJAY WEST OPENCAST PROJECT - [N06000158]SECL,CHHATISGARH , G                              | 05/2017          | 976.95 -                | 976.95           | 75.96                       | 03/2026 -                            | 03/2026     | 0(O) -                                     | 0/0                         |
| 21                                                         | MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND , G                                      | 08/2008          | 706.40 -                | 706.40           | 116.67                      | 07/2012 03/2017                      | 03/2021     | 104(O) 48(R)                               | 2/3                         |
| 22                                                         | RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND , G                                            | 09/2009          | 153.82 -                | 153.82           | 126.63                      | 03/2014 -                            | 12/2017     | 45(O) -                                    | 4/6                         |
| 23                                                         | CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND , G                                   | 08/2007          | 163.51 -                | 163.51           | 93.28                       | 03/2011 -                            | 03/2020     | 108(O) -                                   | 2/2                         |
| 24                                                         | NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND , G                                 | 12/2007          | 179.87 -                | 179.87           | 97.03                       | 03/2012 -                            | 03/2019     | 84(O) -                                    | 2/2                         |
| 25                                                         | PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND , G                                      | 07/2008          | 210.98 -                | 210.98           | 206.31                      | 03/2013 -                            | 03/2018     | 60(O) -                                    | 3/3                         |
| 26                                                         | TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND , G                                         | 08/2008          | 264.68 -                | 264.68           | 153.14                      | 03/2012 -                            | 03/2019     | 84(O) -                                    | 2/3                         |
| 27                                                         | RAJRAPPA RCE OCP ( 3.0 MTY) - [N06000087]CCL,JHARKHAND , G                                 | 12/2009          | 510.85 -                | 510.85           | 341.12                      | 03/2016 -                            | 03/2018     | 24(O) -                                    | 2/3                         |
| 28                                                         | KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND , G                                          | 06/2009          | 162.46 -                | 162.46           | 80.63                       | 03/2014 -                            | 03/2019     | 60(O) -                                    | 2/2                         |
| 29                                                         | MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND , G                                | 02/2011          | 339.88 -                | 339.88           | 12.08                       | 04/2014 -                            | 10/2018     | 54(O) -                                    | 4/7                         |
| 30                                                         | MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND , G                                        | 08/2011          | 1,230.27 -              | 1,230.27         | 179.50                      | 04/2015 -                            | 04/2019     | 48(O) -                                    | 2/6                         |
| 31                                                         | AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND , G                                          | 02/2012          | 858.11 -                | 858.11           | 175.44                      | 03/2020 -                            | 03/2020     | 0(O) -                                     | 4/4                         |
| 32                                                         | NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND , G           | 02/2014          | 555.52 -                | 555.52           | 4.57                        | 03/2021 -                            | 03/2021     | 0(O) -                                     | 0/2                         |
| 33                                                         | KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND , G                                           | 08/2011          | 988.35 -                | 988.35           | 45.26                       | 04/2017 -                            | -           | -                                          | 1/3                         |
| 34                                                         | MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND , G                                      | 08/2010          | 289.45 -                | 289.45           | 151.66                      | 05/2014 -                            | 04/2018     | 47(O) -                                    | 0/8                         |
| 35                                                         | PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND , G                                      | 10/2012          | 269.82 -                | 269.82           | 150.11                      | 04/2014 -                            | 04/2018     | 48(O) -                                    | 0/10                        |
| 36                                                         | HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND , G                                         | 10/2015          | 359.69 -                | 359.69           | 7.54                        | 03/2022 -                            | 03/2022     | 0(O) -                                     | 0/21                        |
| 37                                                         | NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH , G | 10/2007          | 259.40 486.57           | 486.57           | 296.95                      | 03/2012 03/2018                      | 03/2018     | 72(O) 0(R)                                 | 1/3                         |
| 38                                                         | BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH , G                                  | 08/2015          | 1,186.64 -              | 1,186.64         | 54.40                       | 03/2023 -                            | 03/2023     | 0(O) -                                     | 3/10                        |
| 39                                                         | AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH , G                                 | 02/2015          | 481.60 -                | 481.60           | -                           | 03/2023 -                            | 03/2023     | 0(O) -                                     | 0/8                         |
| 40                                                         | RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH , G                           | 12/2014          | 357.80 -                | 357.80           | 114.37                      | 03/2021 -                            | 03/2021     | 0(O) -                                     | 1/8                         |
| 41                                                         | KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH , G                                  | 12/2014          | 371.04 -                | 371.04           | 34.53                       | 03/2021 -                            | 03/2021     | 0(O) -                                     | 1/7                         |
| 42                                                         | BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH , G                               | 07/2015          | 231.92 -                | 231.92           | -                           | 03/2022 -                            | 03/2022     | 0(O) -                                     | 1/6                         |
| 43                                                         | MALACHUA OPENCAST PROJECT - [N06000139]SECL,MADHYA PRADESH , G                             | 10/2015          | 488.33 -                | 488.33           | 1.13                        | 03/2023 -                            | 03/2023     | 0(O) -                                     | 0/4                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                             |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|-----------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                     | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                           | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 44    | AMADAND OPENCASE EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH , G     | 03/2016          | 869.44 -                | 869.44           | 109.31                      | 03/2021 -             | 03/2021     | 0(O) -                                     | 1/3                         |
| 45    | COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH , G | 07/2016          | 409.87 -                | 409.87           | 12.08                       | 03/2022 -             | 03/2022     | 0(O) -                                     | 0/0                         |
| 46    | PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA , G                      | 09/2014          | 441.82 -                | 441.82           | 174.29                      | 03/2020 -             | 03/2020     | 0(O) -                                     | 6/11                        |
| 47    | DINESH OCP - [N06000118]WCL,MAHARASHTRA , G                                 | 11/2014          | 611.16 -                | 611.16           | 360.21                      | 03/2020 -             | 03/2020     | 0(O) -                                     | 2/8                         |
| 48    | MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA , G                           | 09/2014          | 266.23 -                | 266.23           | 138.36                      | 03/2021 -             | 03/2021     | 0(O) -                                     | 6/12                        |
| 49    | GOKUL - [N06000120]WCL,MAHARASHTRA , G                                      | 11/2014          | 267.67 -                | 267.67           | 203.98                      | 03/2018 -             | 03/2018     | 0(O) -                                     | 6/7                         |
| 50    | BHANEAGAON OC - [N06000121]WCL,MAHARASHTRA , G                              | 02/2015          | 187.94 -                | 187.94           | 72.23                       | 03/2023 -             | 03/2023     | 0(O) -                                     | 6/11                        |
| 51    | NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA , G                         | 05/2015          | 295.56 -                | 295.56           | 85.80                       | 03/2019 -             | 03/2019     | 0(O) -                                     | 10/13                       |
| 52    | SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA , G                           | 06/2015          | 205.49 -                | 205.49           | 65.88                       | 03/2020 -             | 03/2020     | 0(O) -                                     | 5/10                        |
| 53    | AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA , G           | 06/2015          | 483.69 -                | 483.69           | 71.98                       | 03/2021 -             | 03/2021     | 0(O) -                                     | 2/6                         |
| 54    | AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA , G             | 08/2015          | 727.28 -                | 727.28           | 228.99                      | 03/2025 -             | 03/2025     | 0(O) -                                     | 3/13                        |
| 55    | ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA , G                             | 08/2015          | 288.90 -                | 288.90           | -                           | 03/2023 -             | 03/2023     | 0(O) -                                     | 2/10                        |
| 56    | KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA , G                       | 11/2015          | 277.65 -                | 277.65           | .13                         | 03/2021 -             | 03/2021     | 0(O) -                                     | 2/6                         |
| 57    | MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA , G  | 11/2015          | 498.42 -                | 498.42           | 7.72                        | 03/2020 -             | 03/2020     | 0(O) -                                     | 2/6                         |
| 58    | AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA , G         | 02/2016          | 198.68 -                | 198.68           | 30.32                       | 03/2019 -             | 03/2019     | 0(O) -                                     | 2/9                         |
| 59    | BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA , G                  | 02/2016          | 304.52 -                | 304.52           | 124.12                      | 03/2019 -             | 03/2019     | 0(O) -                                     | 1/8                         |
| 60    | NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE , G       | 08/2016          | 319.76 -                | 319.76           | -                           | 03/2022 -             | 03/2022     | 0(O) -                                     | 0/3                         |
| 61    | DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE , G                     | 09/2016          | 458.07 -                | 458.07           | -                           | 03/2022 -             | 03/2022     | 0(O) -                                     | 0/12                        |
| 62    | DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE , G     | 02/2017          | 328.00 -                | 328.00           | 45.31                       | 03/2021 -             | 03/2021     | 0(O) -                                     | 0/6                         |
| 63    | KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA , G             | 01/2005          | 302.96 -                | 302.96           | 329.10                      | 03/2010 -             | 03/2018     | 96(O) -                                    | 9/10                        |
| 64    | BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA , G                | 12/2007          | 490.10 -                | 490.10           | 278.34                      | 03/2017 -             | 05/2018     | 14(O) -                                    | 11/12                       |
| 65    | KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA , G                     | 12/2007          | 457.77 -                | 457.77           | 404.51                      | 03/2013 -             | 11/2018     | 68(O) -                                    | 8/9                         |
| 66    | BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA , G               | 12/2007          | 172.08 -                | 172.08           | 191.07                      | 03/2010 -             | 03/2019     | 108(O) -                                   | 3/4                         |
| 67    | ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA , G           | 08/2008          | 207.28 -                | 207.28           | 219.09                      | 03/2012 -             | 03/2019     | 84(O) -                                    | 4/5                         |
| 68    | HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA , G              | 11/2008          | 479.53 -                | 479.53           | 219.12                      | 03/2013 -             | 03/2019     | 72(O) -                                    | 5/8                         |
| 69    | BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA , G             | 05/2014          | 479.15 -                | 479.15           | 20.80                       | 03/2019 -             | 03/2019     | 0(O) -                                     | 2/9                         |

| Detail of ongoing Projects Costing Rs.150 Crore and above. |                                                                                                 |                  |                         |                  |                             | (All Cost/ Expenditure in Rs. Crore) |             |                                            |                             |
|------------------------------------------------------------|-------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|--------------------------------------|-------------|--------------------------------------------|-----------------------------|
|                                                            |                                                                                                 |                  |                         |                  |                             | Date of Commissioning                |             | (September 2017)                           |                             |
| Sl.No                                                      | Project                                                                                         | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised                   | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1                                                          | 2                                                                                               | 3                | 4                       | 5                | 6                           | 7                                    | 8           | 9                                          | 10                          |
| 70                                                         | SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA , G                                              | 05/2014          | 3,756.36<br>-           | 3,756.36         | 682.14                      | 03/2026<br>-                         | 03/2026     | 0(O)<br>-                                  | 3/15                        |
| 71                                                         | JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA , G                             | 05/2014          | 337.66<br>-             | 337.66           | 29.74                       | 03/2019<br>-                         | 03/2019     | 0(O)<br>-                                  | 3/6                         |
| 72                                                         | KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA , G                                           | 06/2014          | 289.03<br>-             | 289.03           | -                           | 03/2018<br>-                         | 03/2018     | 0(O)<br>-                                  | 2/5                         |
| 73                                                         | GARJANBAHAL OCP - [N06000117]MCL,ODISHA , G                                                     | 11/2014          | 1,375.38<br>-           | 1,375.38         | 352.44                      | 03/2021<br>-                         | 03/2021     | 0(O)<br>-                                  | 2/9                         |
| 74                                                         | HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects      | 03/2015          | 522.45<br>-             | 522.45           | 5.65                        | 09/2019<br>-                         | 09/2019     | 0(O)<br>-                                  | 0/0                         |
| 75                                                         | BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects   | 03/2015          | 513.63<br>-             | 513.63           | 167.04                      | 12/2019<br>-                         | 12/2019     | 0(O)<br>-                                  | 0/0                         |
| 76                                                         | NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU , G                     | 06/2011          | 5,907.11<br>-           | 5,907.11         | 4,763.73                    | 12/2015<br>04/2018                   | 04/2018     | 28(O)<br>0(R)                              | 16/35                       |
| 77                                                         | WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU , G                     | 04/2012          | 364.75<br>-             | 364.75           | 333.05                      | 10/2014<br>06/2017                   | 07/2017     | -                                          | 10/10                       |
| 78                                                         | EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU , G | 04/2013          | 1,458.17<br>709.06      | 709.06           | 279.07                      | 06/2015<br>09/2019                   | 09/2019     | 51(O)<br>0(R)                              | 3/7                         |
| 79                                                         | NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU , G                              | 05/2016          | 687.28<br>-             | 687.28           | 690.47                      | 06/2017<br>-                         | 10/2017     | 4(O)<br>-                                  | 0/0                         |
| 80                                                         | SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA , G                                  | 10/2006          | 249.03<br>448.86        | 448.86           | 157.97                      | 03/2012<br>-                         | 03/2019     | 84(O)<br>-                                 | 32/42                       |
| 81                                                         | KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA , G                                               | 12/2008          | 453.63<br>-             | 453.63           | 121.91                      | 12/2012<br>-                         | -           | -                                          | 11/44                       |
| 82                                                         | RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA , G                                      | 12/2009          | 418.97<br>-             | 489.62           | 477.74                      | 03/2012<br>-                         | 03/2023     | 132(O)<br>-                                | 0/2                         |
| 83                                                         | RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA , G                                                 | 03/2010          | 209.78<br>-             | 209.78           | 120.55                      | 03/2015<br>-                         | 03/2018     | 36(O)<br>-                                 | 29/31                       |
| 84                                                         | MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA , G                               | 03/2010          | 181.19<br>-             | 181.19           | 176.79                      | 03/2012<br>-                         | 03/2018     | 72(O)<br>-                                 | 5/6                         |
| 85                                                         | KISTARAM OCP - [N06000089]SCCL,TELANGANA , G                                                    | 11/2010          | 242.29<br>164.04        | 164.04           | .09                         | 03/2015<br>-                         | 03/2020     | 60(O)<br>-                                 | 0/5                         |
| 86                                                         | RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA , G                                   | 07/2011          | 162.76<br>349.28        | 349.28           | 1.31                        | 03/2015<br>-                         | 03/2020     | 60(O)<br>-                                 | 4/29                        |
| 87                                                         | JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA , G                                      | 07/2011          | 447.06<br>-             | 437.51           | 259.34                      | 03/2015<br>-                         | 03/2021     | 72(O)<br>-                                 | 5/13                        |
| 88                                                         | RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA , G                        | 06/2012          | 365.01<br>-             | 365.01           | 57.64                       | 06/2015<br>-                         | 03/2018     | 33(O)<br>-                                 | 27/36                       |
| 89                                                         | KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA , G                                   | 07/2012          | 417.33<br>417.33        | 417.33           | 43.97                       | 07/2016<br>-                         | 03/2020     | 44(O)<br>-                                 | 19/28                       |
| 90                                                         | RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA , G                                      | 11/2012          | 430.45<br>415.37        | 415.37           | 136.75                      | 03/2016<br>-                         | 03/2018     | 24(O)<br>-                                 | 33/39                       |
| 91                                                         | KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA , G                                | 05/2015          | 397.09<br>442.42        | 442.42           | 19.94                       | 03/2019<br>-                         | 03/2019     | 0(O)<br>-                                  | 6/18                        |
| 92                                                         | KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects                | 10/2015          | 426.79<br>-             | 426.79           | -                           | 03/2018<br>-                         | 03/2019     | 12(O)<br>-                                 | 0/9                         |
| 93                                                         | KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL,TELANGANA , G                                  | 12/2015          | 477.65<br>-             | 477.65           | -                           | 03/2020<br>-                         | 03/2020     | 0(O)<br>-                                  | 1/17                        |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                       |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|---------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                               | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                     | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 94    | KHADIA EXPANSION OPENCASE PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH , G                                  | 06/2011          | 1,131.28 -              | 1,131.28         | 431.09                      | 03/2018 -             | 03/2018     | 0(O) -                                     | 6/10                        |
| 95    | NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH , G                                                | 07/2016          | 17,237.00 -             | 17,237.80        | 1,116.07                    | 11/2021 -             | 11/2021     | 0(O) -                                     | 0/0                         |
| 96    | JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL,WEST BENGAL , G                                                                        | 11/2015          | 602.86 -                | 602.86           | 268.77                      | 03/2022 -             | 03/2022     | 0(O) -                                     | 6/12                        |
| 97    | SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL , G                                                                  | 08/2012          | 1,055.05 -              | 1,055.05         | 316.35                      | 03/2018 -             | 09/2018     | 6(O) -                                     | 8/15                        |
|       | Total                                                                                                                                 |                  | 88,124.99 -             | 88,310.36        | 21,448.64                   |                       |             |                                            | 399/903                     |
|       |                                                                                                                                       |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>FERTILISERS</u>                                                                                                                    |                  |                         |                  |                             |                       |             |                                            |                             |
| 98    | NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA , G                                                      | 10/2014          | 197.79 209.44           | 209.44           | 82.72                       | 11/2016 04/2019       | 04/2019     | 29(O) 0(R)                                 | 0/0                         |
| 99    | GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF,MAHARASHTRA , G                              | 02/2016          | 482.85 -                | 494.00           | 400.18                      | 12/2017 -             | 12/2017     | 0(O) -                                     | 0/1                         |
|       | Total                                                                                                                                 |                  | 680.64 -                | 703.44           | 482.90                      |                       |             |                                            | 0/1                         |
|       |                                                                                                                                       |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>MINES</u>                                                                                                                          |                  |                         |                  |                             |                       |             |                                            |                             |
| 100   | Implementation of 50.4 MW Wind Power Project at Jath, Sangli, Maharashtra - [N10000008]NALCO,MAHARASHTRA , Private                    | 12/2015          | 355.13 -                | 355.13           | 94.63                       | 11/2016 -             | -           | -                                          | 1/1                         |
| 101   | 5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA , G                                                           | 12/2014          | 5,540.00 -              | 5,540.00         | .31                         | 04/2021 -             | 04/2021     | 0(O) -                                     | 1/1                         |
| 102   | UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA , G                                                                                | 05/2016          | 534.00 -                | 534.00           | 157.34                      | 01/2020 -             | 01/2020     | 0(O) -                                     | 1/1                         |
| 103   | IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT RAJASTHAN - [N10000009]NALCO,RAJASTHAN , PPP (ANNUITY)                                  | 12/2015          | 344.50 -                | 344.50           | 120.35                      | 11/2016 -             | -           | -                                          | 1/1                         |
|       | Total                                                                                                                                 |                  | 6,773.63 -              | 6,773.63         | 372.63                      |                       |             |                                            | 4/4                         |
|       |                                                                                                                                       |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>STEEL</u>                                                                                                                          |                  |                         |                  |                             |                       |             |                                            |                             |
| 104   | 3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH , G                                                                     | 07/2011          | 974.76 -                | 974.76           | 533.93                      | 07/2016 -             | 10/2017     | 15(O) -                                    | 1/1                         |
| 105   | BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH , G                                                       | 07/2011          | 877.73 -                | 877.73           | 746.08                      | 07/2015 -             | 10/2017     | 27(O) -                                    | 2/2                         |
| 106   | REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH , G                                                           | 12/2009          | 343.00 -                | 488.40           | 225.07                      | 10/2016 -             | 03/2018     | 17(O) -                                    | 0/0                         |
| 107   | TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH , G                                                                                 | 12/2009          | 280.00 -                | 280.00           | 155.29                      | 09/2016 -             | 10/2017     | 13(O) -                                    | 1/1                         |
| 108   | CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH , G | 07/2014          | 232.00 -                | 232.00           | -                           | 01/1999 -             | -           | -                                          | 0/0                         |
| 109   | COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH , G                                                                              | 12/2011          | 2,858.00 -              | 2,500.00         | 591.35                      | 12/2017 -             | 06/2018     | 6(O) -                                     | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                     |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|-------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                             | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                   | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 110   | CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH , G                                                                          | 08/2015          | 320.66 -                | 320.66           | 15.23                       | 08/2018 -             | 08/2018     | 0(O) -                                     | 0/0                         |
| 111   | ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH , G                                                     | 07/2015          | 465.85 -                | 465.85           | 35.89                       | 07/2018 -             | 07/2018     | 0(O) -                                     | 0/0                         |
| 112   | IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR , G                                                                              | 10/2005          | 956.00 -                | 956.00           | 651.21                      | 03/2015 -             | 03/2021     | 72(O) -                                    | 0/0                         |
| 113   | EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH , G                                                                   | 08/2010          | 17,265.00 -             | 17,265.00        | 17,970.98                   | 03/2013 -             | 10/2017     | 55(O) -                                    | 35/38                       |
| 114   | DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH , G                              | 04/2014          | 188.93 -                | 188.93           | 114.49                      | 04/2015 -             | -           | -                                          | 4/5                         |
| 115   | NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH , G                                                                       | 01/2010          | 15,525.00 -             | 15,525.00        | 12,816.08                   | 05/2015 10/2018       | 10/2018     | 41(O) 0(R)                                 | 54/86                       |
| 116   | 2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]NMDC,CHHATISGARH , G                                                                   | 11/2015          | 818.00 -                | 818.00           | 25.88                       | 06/2020 -             | 06/2020     | 0(O) -                                     | 4/12                        |
| 117   | CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT , G                                 | 01/2013          | 175.00 -                | 175.00           | 1.83                        | - -                   | 12/2017     | - -                                        | 0/0                         |
| 118   | REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND , G                                                                          | 10/2013          | 245.67 -                | 245.67           | 195.66                      | 05/2016 -             | 10/2017     | 17(O) -                                    | 2/3                         |
| 119   | ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND , G                                                                        | 03/2015          | 255.19 -                | 255.19           | 156.39                      | 03/2018 -             | 03/2018     | 0(O) -                                     | 1/2                         |
| 120   | NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND , G                                                              | 03/2015          | 1,034.01 -              | 1,034.01         | 187.29                      | 10/2017 -             | 07/2018     | 9(O) -                                     | 0/2                         |
| 121   | MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND , G                                      | 05/2015          | 1,154.18 -              | 1,154.18         | 477.09                      | 12/2017 -             | 05/2018     | 5(O) -                                     | 1/2                         |
| 122   | EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND , G           | 02/2014          | 4,749.00 -              | 4,749.00         | 69.35                       | 09/2017 -             | 09/2017     | 0(O) -                                     | 0/0                         |
| 123   | CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND , G                        | 12/2007          | 253.92 253.92           | 253.92           | 193.97                      | 06/2016 -             | 03/2018     | 21(O) -                                    | 0/0                         |
| 124   | CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND , G         | 12/2007          | 200.00 -                | 200.00           | 131.15                      | 03/2018 -             | 03/2018     | 0(O) -                                     | 0/0                         |
| 125   | CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND , G                                    | 02/2014          | 787.29 -                | 787.29           | 285.30                      | 12/2016 -             | 12/2018     | 24(O) -                                    | 0/0                         |
| 126   | CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND , G                                                         | 04/2013          | 170.00 -                | 170.00           | 88.91                       | 04/2018 -             | 04/2018     | 0(O) -                                     | 0/0                         |
| 127   | REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND , G                                                         | 11/2016          | 262.87 -                | 262.87           | 35.71                       | 06/2019 -             | 06/2019     | 0(O) -                                     | 0/1                         |
| 128   | CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA , G                                            | 05/2005          | 768.88 1,070.97         | 1,113.34         | 1,085.64                    | 02/2014 -             | -           | -                                          | 0/0                         |
| 129   | CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA , G                                 | 07/2011          | 324.87 324.87           | 324.87           | 262.93                      | 12/2015 -             | -           | -                                          | 0/0                         |
| 130   | CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA , G | 04/2014          | 151.33 -                | 151.33           | 7.15                        | 09/2017 -             | 12/2018     | 15(O) -                                    | 0/0                         |



**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                                |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|----------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                                        | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                                              | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 131   | INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL, ODISHA , G                                                                                        | 04/2015          | 3,127.30 -              | 3,127.30         | 1,205.62                    | 04/2018 -             | 02/2019     | 10(O) -                                    | 1/3                         |
| 132   | CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL, RAJASTHAN , G                          | 05/2015          | 189.00 -                | 189.00           | -                           | 03/2017 -             | 08/2018     | 17(O) -                                    | 0/0                         |
| 133   | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL, TRIPURA , G                                                                  | 03/2007          | 149.73 173.00           | 175.94           | 178.65                      | 12/2015 -             | -           | -                                          | 0/0                         |
| 134   | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL, TRIPURA , G                                                                 | 12/2007          | 202.61 227.00           | 227.00           | 199.95                      | 12/2016 -             | 12/2017     | 12(O) -                                    | 0/0                         |
| 135   | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL, TRIPURA , G                                                               | 10/2011          | 175.49 206.71           | 206.71           | 141.28                      | 12/2016 -             | -           | -                                          | 0/0                         |
| 136   | FORGED WHEEL PLANT - [N12000116]RINL, UTTAR PRADESH , G                                                                                                        | 04/2014          | 1,682.85 -              | 1,682.85         | 63.22                       | 09/2018 -             | 09/2018     | 0(O) -                                     | 0/0                         |
| 137   | CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES (ITI) WEST BENG - [N12000114]HSCL, WEST BENGAL , Central Sector Projects | 08/2012          | 185.37 -                | 185.37           | 178.30                      | 03/2016 -             | -           | -                                          | 0/0                         |
|       | <b>Total</b>                                                                                                                                                   |                  | 57,349.49 -             | 57,563.17        | 39,026.87                   |                       |             |                                            | 106/158                     |
|       |                                                                                                                                                                |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <b>PETROLEUM</b>                                                                                                                                               |                  |                         |                  |                             |                       |             |                                            |                             |
| 138   | VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL, ANDHRA PRADESH , G                                                                                    | 07/2016          | 20,928.00 -             | 20,928.00        | 540.49                      | 07/2020 -             | 07/2020     | 0(O) -                                     | 0/0                         |
| 139   | VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]HPCL, ANDHRA PRADESH , G                                                      | 09/2016          | 407.00 -                | 407.00           | 27.20                       | 09/2019 -             | 09/2019     | 0(O) -                                     | 15/27                       |
| 140   | KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC, ANDHRA PRADESH , G                                                                               | 03/2016          | 34,012.00 -             | 34,012.00        | 252.02                      | 06/2020 06/2020       | 06/2020     | 0(O) 0(R)                                  | 0/0                         |
| 141   | ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL, ANDHRA PRADESH , G                                  | 01/2015          | 342.00 -                | 342.00           | -                           | 03/2021 -             | 03/2021     | 0(O) -                                     | 0/0                         |
| 142   | REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL, ANDHRA PRADESH , G                                                                        | 07/2014          | 247.00 -                | 247.00           | -                           | 03/2021 -             | 03/2021     | 0(O) -                                     | 0/0                         |
| 143   | FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC, ANDHRA PRADESH , G                                                              | 04/2017          | 420.76 -                | 420.76           | -                           | 09/2018 09/2018       | 09/2018     | 0(O) 0(R)                                  | 0/0                         |
| 144   | RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]IOCL, ARUNACHAL PRADESH , G                                                                 | 01/2016          | 247.52 -                | 247.52           | 53.32                       | 02/2019 -             | 12/2018     | -2(O) -                                    | 2/10                        |
| 145   | ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, ASSAM , G                                                                                                 | 03/2009          | 2,465.15 -              | 2,378.89         | 2,060.68                    | 03/2013 09/2018       | 09/2018     | 66(O) 0(R)                                 | 5/15                        |
| 146   | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS (WIP) - [N16000127]ONGC, ASSAM , G                                                           | 06/2010          | 202.94 341.70           | 330.35           | 2.11                        | 01/2014 11/2019       | 11/2019     | 70(O) 0(R)                                 | 0/2                         |
| 147   | INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL, ASSAM , G                                                              | 02/2014          | 163.88 -                | 163.88           | 82.45                       | 07/2016 -             | -           | -                                          | 6/6                         |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                              |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|----------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                      | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                            | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 148   | TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL, ASSAM , G                                                                                     | 03/2009          | 228.64 -                | 209.19           | 147.05                      | 12/2016 -             | 03/2018     | 15(O) -                                    | 0/0                         |
| 149   | DIESEL HYDROTREATOR - [N16000207]NRL, ASSAM , Central Sector Projects                                                                        | 07/2015          | 1,031.37 -              | 1,031.37         | 305.91                      | 01/2018 -             | 01/2018     | 0(O) -                                     | 46/61                       |
| 150   | RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]IOCL, ASSAM , G                                       | 06/2012          | 150.00 -                | 259.93           | 251.90                      | 07/2014 -             | 09/2017     | 38(O) -                                    | 6/12                        |
| 151   | DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL, ASSAM , G              | 06/2016          | 423.00 -                | 423.00           | 89.60                       | 08/2019 -             | 08/2019     | 0(O) -                                     | 2/13                        |
| 152   | INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL, ASSAM , G                                                                           | 02/2016          | 2,582.00 -              | 2,582.00         | 193.27                      | 11/2019 -             | 11/2019     | 0(O) -                                     | 0/0                         |
| 153   | PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]ONGC, ASSAM , G                                                                          | 07/2016          | 249.85 250.00           | 244.70           | -                           | 05/2020 -             | 05/2020     | 0(O) -                                     | 0/0                         |
| 154   | UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM , G                           | 09/2012          | 871.35 -                | 1,200.00         | 958.00                      | 03/2015 -             | 11/2017     | 32(O) -                                    | 0/5                         |
| 155   | FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL, BIHAR , G                                             | 07/2015          | 822.66 -                | 822.66           | 223.14                      | 11/2018 -             | 11/2018     | 0(O) -                                     | 0/0                         |
| 156   | BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]IOCL, BIHAR , G                                                        | 05/2016          | 664.00 -                | 664.00           | 137.54                      | 12/2020 -             | 02/2020     | -10(O) -                                   | 0/0                         |
| 157   | MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL, BIHAR , G                                                                                    | 09/2015          | 324.00 -                | 324.00           | 1.39                        | 06/2020 -             | 06/2020     | 0(O) -                                     | 0/0                         |
| 158   | DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC, D & N HAVELI , G                                                                                | 08/2014          | 6,086.08 -              | 5,479.75         | 2,081.12                    | 05/2019 10/2019       | 10/2019     | 5(O) 0(R)                                  | 0/0                         |
| 159   | PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC, GUJARAT , G                                                                       | 09/2011          | 202.25 -                | 160.16           | 106.98                      | 07/2016 06/2018       | 06/2018     | 23(O) 0(R)                                 | 5/12                        |
| 160   | GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC, GUJARAT , G                                                                                   | 05/2015          | 1,671.22 567.22         | 567.22           | 347.69                      | 11/2019 12/2018       | 12/2018     | -11(O) 0(R)                                | 0/0                         |
| 161   | 50 MW 10 PERSENT WIND ENERGY POWER PROJECT - [N16000208]OIL, GUJARAT , Central Sector Projects                                               | 11/2015          | 500.00 -                | 435.00           | 368.24                      | 03/2017 -             | -           | -                                          | 0/1                         |
| 162   | NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC, GUJARAT , Central Sector Projects                                                         | 11/2014          | 195.63 -                | 187.10           | 139.30                      | 09/2018 09/2018       | 09/2018     | 0(O) 0(R)                                  | 0/0                         |
| 163   | ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]GAIL, GUJARAT , G                                                                            | 07/2014          | 199.95 -                | 199.95           | 119.90                      | 03/2018 -             | 03/2018     | 0(O) -                                     | 16/22                       |
| 164   | CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL, GUJARAT , G                                                                  | 04/2016          | 327.78 -                | 200.00           | 14.44                       | 04/2018 -             | 04/2018     | 0(O) -                                     | 14/20                       |
| 165   | FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY - [N16000245]IOCL, GUJARAT , G                                              | 02/2016          | 931.00 -                | 931.00           | 383.35                      | 07/2017 -             | 02/2018     | 7(O) -                                     | 0/0                         |
| 166   | REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC, GUJARAT , G                                                                                | 02/2017          | 1,162.56 1,162.56       | 1,162.56         | 196.84                      | 03/2026 03/2026       | 03/2026     | 0(O) 0(R)                                  | 0/0                         |
| 167   | INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL, GUJARAT , Central Sector Projects | 09/2016          | 208.35 -                | 208.35           | 16.93                       | 07/2020 -             | 07/2020     | 0(O) -                                     | 0/0                         |
| 168   | CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]IOCL, HIMACHAL PRADESH , G                                              | 02/2016          | 356.00 -                | 356.00           | 64.84                       | 05/2019 -             | 12/2018     | -5(O) -                                    | 1/13                        |
| 169   | BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL, HIMACHAL PRADESH , G                                                                      | 02/2016          | 151.00 -                | 151.00           | 28.72                       | 09/2019 -             | 09/2019     | 0(O) -                                     | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                               |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|---------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                       | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                             | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 170   | RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND , G               | 04/2011          | 191.96 -                | 191.96           | 167.97                      | 05/2015<br>06/2017    | 06/2017     | -                                          | 8/12                        |
| 171   | DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND , G                                        | 12/2015          | 658.62<br>910.23        | 910.23           | 2.30                        | 03/2023<br>03/2022    | 03/2022     | -12(O)<br>0(R)                             | 0/0                         |
| 172   | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA , G                                 | 01/2006          | 993.00 -                | 1,693.00         | 1,537.84                    | 01/2012<br>-          | 10/2017     | 69(O)<br>-                                 | 0/0                         |
| 173   | GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA , Central Sector Projects                      | 02/2015          | 749.00 -                | 749.00           | 468.00                      | 02/2020<br>-          | 02/2020     | 0(O)<br>-                                  | 0/0                         |
| 174   | CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA , G | 05/2015          | 224.00<br>207.00        | 207.25           | 39.64                       | 04/2019<br>-          | 04/2019     | 0(O)<br>-                                  | 5/8                         |
| 175   | RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA , G                   | 10/2015          | 135.00<br>170.70        | 170.70           | 58.29                       | 03/2019<br>-          | 03/2019     | 0(O)<br>-                                  | 3/11                        |
| 176   | BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA , G                                                   | 09/2016          | 1,810.00<br>1,810.00    | 1,810.00         | 46.43                       | 12/2019<br>-          | 12/2019     | 0(O)<br>-                                  | 6/9                         |
| 177   | LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA , G                                                            | 10/2015          | 607.06<br>714.25        | 714.25           | 276.85                      | 10/2017<br>-          | 03/2019     | 17(O)<br>-                                 | 36/52                       |
| 178   | PALAKKAD LPG PLANT - [N16000225]BPCL,KERALA , G                                                               | 02/2015          | 184.00 -                | 184.00           | 77.07                       | 12/2017<br>-          | 12/2017     | 0(O)<br>-                                  | 0/10                        |
| 179   | PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA , G              | 11/2014          | 4,588.29<br>5,245.96    | 4,588.29         | 871.49                      | 08/2018<br>05/2019    | 05/2019     | 9(O)<br>0(R)                               | 0/20                        |
| 180   | MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA , G           | 02/2016          | 3,313.00 -              | 3,313.00         | 62.82                       | 02/2020<br>-          | 02/2020     | 0(O)<br>-                                  | 0/0                         |
| 181   | LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]BPCL,KERALA , G     | 05/2015          | 337.06 -                | 337.06           | 17.88                       | 08/2018<br>-          | 08/2018     | 0(O)<br>-                                  | 0/0                         |
| 182   | SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH , Central Sector Projects                   | 03/2009          | 181.02 -                | 173.28           | 126.94                      | 01/2017<br>03/2018    | 03/2018     | 14(O)<br>0(R)                              | 0/0                         |
| 183   | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA , G     | 03/2011          | 861.79<br>1,256.72      | 1,256.72         | 1,158.79                    | 05/2013<br>12/2017    | 12/2017     | 55(O)<br>0(R)                              | 1/5                         |
| 184   | INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA , G                                      | 12/2011          | 2,059.63 -              | 2,665.65         | 1,633.37                    | 03/2015<br>03/2018    | 03/2018     | 36(O)<br>0(R)                              | 0/17                        |
| 185   | DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA , G                                          | 03/2012          | 2,592.17 -              | 2,592.17         | 2,040.89                    | 05/2014<br>05/2018    | 05/2018     | 48(O)<br>0(R)                              | 0/21                        |
| 186   | MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA , G                                            | 06/2014          | 5,706.47<br>5,813.25    | 5,813.25         | 5,554.21                    | 05/2017<br>05/2018    | 05/2018     | 12(O)<br>0(R)                              | 7/16                        |
| 187   | MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA , G                             | 11/2014          | 6,068.80<br>6,068.80    | 5,296.93         | 4,127.27                    | 04/2019<br>03/2019    | 03/2019     | -1(O)<br>0(R)                              | 0/0                         |
| 188   | PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA , G                                             | 02/2015          | 2,899.93 -              | 2,098.43         | 1,237.43                    | 05/2017<br>05/2018    | 05/2018     | 12(O)<br>0(R)                              | 0/0                         |
| 189   | NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA , G         | 08/2015          | 2,818.88 -              | 2,818.88         | 310.71                      | 03/2019<br>05/2020    | 05/2020     | 14(O)<br>0(R)                              | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                         |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|---------------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                                 | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                                       | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 190   | ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects | 01/2015          | 4,619.94 -              | 3,961.54         | 3,386.30                    | 12/2017<br>03/2019    | 03/2019     | 15(O)<br>0(R)                              | 0/0                         |
| 191   | LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects                                | 12/2015          | 3,190.69 -              | 3,247.19         | 839.54                      | 04/2018<br>04/2018    | 04/2018     | 0(O)<br>0(R)                               | 0/0                         |
| 192   | KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA , G                                                                                    | 05/2016          | 1,945.00 -              | 1,945.00         | 17.11                       | 08/2021<br>-          | 08/2021     | 0(O)<br>-                                  | 0/0                         |
| 193   | INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA , G                              | 02/2016          | 554.00 -                | 554.00           | 24.30                       | 02/2020<br>-          | 02/2020     | 0(O)<br>-                                  | 0/0                         |
| 194   | MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA , G                                                                                       | 04/2013          | 449.58 -                | 449.58           | 95.57                       | 12/2019<br>-          | 12/2019     | 0(O)<br>-                                  | 0/0                         |
| 195   | LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]BPCL,MAHARASHTRA , G                                         | 05/2015          | 193.40 -                | 193.40           | 7.07                        | 01/2019<br>-          | 01/2019     | 0(O)<br>-                                  | 0/0                         |
| 196   | ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA , G                     | 05/2016          | 212.00 -                | 212.00           | .08                         | 01/2021<br>-          | 01/2021     | 0(O)<br>-                                  | 0/0                         |
| 197   | ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA , G                   | 05/2016          | 348.00 -                | 348.00           | .05                         | 01/2021<br>-          | 01/2021     | 0(O)<br>-                                  | 0/0                         |
| 198   | ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA , G                | 05/2016          | 261.00 -                | 261.00           | .05                         | 01/2021<br>-          | 01/2021     | 0(O)<br>-                                  | 0/0                         |
| 199   | MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA , Central Sector Projects                                                               | 09/2015          | 4,199.00 -              | 4,199.00         | 194.97                      | 03/2020<br>-          | 07/2019     | -8(O)<br>-                                 | 0/0                         |
| 200   | PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE , G                                                                               | 03/2015          | 3,957.00<br>3,561.00    | 3,397.00         | 1,311.80                    | 12/2018<br>-          | 12/2018     | 0(O)<br>-                                  | 25/39                       |
| 201   | CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE , G                                                                       | 06/2007          | 736.65 -                | 571.47           | 541.66                      | 09/2011<br>06/2019    | 06/2019     | 93(O)<br>0(R)                              | 0/0                         |
| 202   | PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE , G                                                                                       | 08/2009          | 1,793.00 -              | 1,793.00         | 1,786.89                    | 12/2016<br>-          | -           | -                                          | 7/7                         |
| 203   | DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE , G                                                                    | 04/2012          | 600.17 -                | 600.17           | 589.36                      | 12/2014<br>03/2018    | 03/2018     | 39(O)<br>0(R)                              | 0/8                         |
| 204   | PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE , G                                                                                  | 02/2011          | 913.00<br>1,330.00      | 1,330.00         | 953.98                      | 06/2018<br>-          | 06/2018     | 0(O)<br>-                                  | 0/0                         |
| 205   | URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE , G                                                                                    | 12/2009          | 309.81<br>723.40        | 723.40           | 381.64                      | 10/2014<br>03/2018    | 03/2018     | 41(O)<br>0(R)                              | 29/40                       |
| 206   | SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE , G                                 | 07/2011          | 352.56 -                | 439.03           | 126.43                      | 03/2017<br>-          | 11/2018     | 20(O)<br>-                                 | 0/0                         |
| 207   | INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE , G                                                                     | 05/2013          | 4,124.35<br>4,259.59    | 5,637.00         | 3,701.21                    | 04/2016<br>12/2017    | 12/2017     | 20(O)<br>0(R)                              | 0/3                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                     |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|-------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                             | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                   | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 208   | AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE , G | 01/2015          | 1,823.00<br>-           | 1,823.00         | 15.19                       | 12/2020<br>-          | 12/2020     | 0(O)<br>-                                  | 0/0                         |
| 209   | PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE , G                                                                        | 01/2015          | 2,321.00<br>-           | 2,321.00         | 53.61                       | 12/2020<br>-          | 08/2020     | -4(O)<br>-                                 | 0/0                         |
| 210   | JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE , G       | 02/2015          | 890.00<br>-             | 887.00           | 220.84                      | 10/2019<br>-          | 10/2019     | 0(O)<br>-                                  | 0/0                         |
| 211   | PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE , G                                                                       | 01/2015          | 690.00<br>-             | 690.00           | 133.55                      | 07/2018<br>06/2020    | 06/2020     | 23(O)<br>0(R)                              | 10/36                       |
| 212   | MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE , G                                  | 09/2016          | 1,879.00<br>-           | 1,879.00         | 168.33                      | 06/2020<br>-          | 06/2020     | 0(O)<br>-                                  | 7/24                        |
| 213   | RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]HPCL,MULTI STATE , G                       | 11/2016          | 230.00<br>-             | 230.00           | 11.46                       | 02/2019<br>-          | 02/2019     | 0(O)<br>-                                  | 5/13                        |
| 214   | PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE , G                                                | 05/2016          | 406.00<br>-             | 406.00           | .50                         | 10/2020<br>-          | 10/2020     | 0(O)<br>-                                  | 0/0                         |
| 215   | AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE , G                             | 09/2016          | 571.66<br>-             | 571.66           | -                           | 12/2019<br>-          | 12/2019     | 0(O)<br>-                                  | 0/0                         |
| 216   | LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE , G          | 07/2015          | 2,881.40<br>-           | 2,881.40         | 5.67                        | 12/2019<br>-          | 12/2019     | 0(O)<br>-                                  | 0/0                         |
| 217   | DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE , G                                                                   | 03/2017          | 2,250.00<br>-           | 2,250.00         | 3.20                        | 12/2019<br>-          | 12/2019     | 0(O)<br>-                                  | 0/0                         |
| 218   | BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE , G                                                                     | 03/2017          | 3,212.00<br>-           | 3,212.00         | .29                         | 12/2020<br>-          | 12/2020     | 0(O)<br>-                                  | 0/0                         |
| 219   | KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects                       | 06/2009          | 2,915.00<br>2,915.00    | 2,915.00         | 1,258.49                    | 12/2012<br>-          | 02/2019     | 74(O)<br>-                                 | 0/42                        |
| 220   | POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA , G                                                                | 03/2014          | 3,150.00<br>-           | 3,150.00         | 1,289.32                    | 09/2017<br>12/2018    | 12/2018     | 15(O)<br>0(R)                              | 5/6                         |
| 221   | PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA , G                                                         | 03/2014          | 238.50<br>-             | 238.50           | 167.48                      | 03/2017<br>10/2017    | 10/2017     | 7(O)<br>0(R)                               | 5/6                         |
| 222   | DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA , G                                                                          | 03/2017          | 2,253.00<br>-           | 2,253.00         | 8.12                        | 12/2019<br>-          | 12/2019     | 0(O)<br>-                                  | 0/0                         |
| 223   | INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA , G                                     | 05/2016          | 429.00<br>-             | 429.00           | 20.41                       | 01/2019<br>-          | 01/2019     | 0(O)<br>-                                  | 0/0                         |
| 224   | LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects                                                           | 12/2016          | 161.59<br>-             | 161.59           | 28.80                       | 12/2019<br>-          | 12/2019     | 0(O)<br>-                                  | 0/0                         |
| 225   | 50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN , G                                                    | 11/2011          | 310.00<br>-             | 370.00           | 17.84                       | 03/2013<br>-          | -           | -                                          | 0/24                        |
| 226   | ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU , G                                                                 | 05/2013          | 711.00<br>-             | 711.00           | 11.12                       | 06/2020<br>-          | 06/2020     | 0(O)<br>-                                  | 0/0                         |
| 227   | RESID UPGRADE PROJECT - [N16000184]CPCL,TAMIL NADU , G                                                                              | 03/2013          | 3,110.36<br>-           | 3,110.36         | 2,765.42                    | 11/2015<br>-          | 10/2017     | 23(O)<br>-                                 | 51/52                       |
| 228   | NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU , G                                | 05/2015          | 257.87<br>-             | 257.87           | 117.68                      | 11/2016<br>-          | 02/2018     | 15(O)<br>-                                 | 18/22                       |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                 |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|---------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                         | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                               | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 229   | DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]CPCL,TAMIL NADU , Central Sector Projects                             | 02/2016          | 367.11<br>-             | 367.11           | 218.14                      | 04/2017<br>-          | 11/2017     | 7(O)<br>-                                  | 20/22                       |
| 230   | ENNORE TERMINAL - [N16000224]BPCL,TAMIL NADU , G                                                                                | 08/2014          | 393.00<br>-             | 393.00           | 198.63                      | 04/2018<br>-          | 04/2018     | 0(O)<br>-                                  | 0/10                        |
| 231   | IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU , G                                                                | 11/2012          | 678.00<br>-             | 678.00           | 5.08                        | 02/2017<br>-          | -           | -                                          | 0/0                         |
| 232   | Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU , G                                    | 11/2015          | 390.52<br>-             | 390.52           | 67.52                       | 03/2019<br>-          | 04/2019     | 1(O)<br>-                                  | 0/0                         |
| 233   | ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU , G             | 05/2016          | 4,497.00<br>-           | 4,497.00         | 23.38                       | 12/2018<br>-          | 12/2018     | 0(O)<br>-                                  | 0/0                         |
| 234   | SONAMURA GGS AND PIPELINE PROJECT ( PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC,TRIPURA , G | 05/2016          | 215.38<br>-             | 215.38           | 162.34                      | 06/2017<br>01/2018    | 01/2018     | 7(O)<br>0(R)                               | 0/0                         |
| 235   | AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]GAIL,UTTAR PRADESH , G                                                            | 07/2015          | 1,427.94<br>-           | 1,427.94         | 379.02                      | 12/2018<br>-          | 12/2018     | 0(O)<br>-                                  | 11/20                       |
| 236   | SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects                                                   | 02/2017          | 160.10<br>-             | 160.10           | 20.22                       | 02/2020<br>-          | 02/2020     | 0(O)<br>-                                  | 0/0                         |
| 237   | DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL , G                               | 03/2014          | 3,076.00<br>4,190.00    | 4,190.00         | 2,097.09                    | 09/2017<br>06/2018    | 06/2018     | 9(O)<br>0(R)                               | 6/7                         |
| 238   | NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]HPCL,WEST BENGAL , G                                                            | 08/2014          | 190.45<br>-             | 190.45           | 130.15                      | 09/2017<br>03/2018    | 03/2018     | 6(O)<br>0(R)                               | 0/0                         |
| 239   | HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL , G                                                                    | 03/2015          | 694.00<br>-             | 694.00           | 183.88                      | 10/2018<br>-          | 10/2018     | 0(O)<br>-                                  | 0/0                         |
| 240   | HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL , G                                                               | 04/2016          | 1,021.00<br>-           | 1,021.00         | 6.18                        | 12/2020<br>-          | 12/2020     | 0(O)<br>-                                  | 0/0                         |
| 241   | DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL , G                                                              | 03/2017          | 1,828.00<br>-           | 1,828.00         | .54                         | 12/2020<br>-          | 12/2020     | 0(O)<br>-                                  | 0/0                         |
|       | Total                                                                                                                           |                  | 1,90,142.65<br>-        | 1,91,522.05      | 52,758.11                   |                       |             |                                            | 383/781                     |
|       |                                                                                                                                 |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <b>POWER</b>                                                                                                                    |                  |                         |                  |                             |                       |             |                                            |                             |
| 242   | SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]PGCIL,ANDHRA PRADESH , G                  | 03/2015          | 550.06<br>-             | 550.06           | 462.17                      | 03/2018<br>-          | 09/2017     | -6(O)<br>-                                 | 3/3                         |
| 243   | REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL,ANDHRA PRADESH , G                      | 01/2016          | 207.88<br>-             | 207.88           | 77.86                       | 07/2018<br>-          | 07/2018     | 0(O)<br>-                                  | 0/0                         |
| 244   | SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH , G                                                 | 09/2003          | 6,285.33<br>-           | 18,559.49        | 9,470.18                    | 09/2010<br>-          | -           | -                                          | 0/0                         |
| 245   | KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH , G                                                 | 12/2004          | 2,496.90<br>6,179.96    | 6,179.96         | 5,971.88                    | 12/2009<br>03/2018    | 03/2018     | 99(O)<br>0(R)                              | 18/30                       |
| 246   | PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH , G                                                           | 12/2008          | 573.99<br>1,337.76      | 1,337.76         | 1,499.78                    | 08/2013<br>03/2018    | 03/2018     | 55(O)<br>0(R)                              | 32/38                       |
| 247   | BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM , G                                                                    | 01/2008          | 4,375.35<br>6,749.18    | 6,749.18         | 6,797.00                    | 09/2011<br>06/2017    | 12/2017     | 75(O)<br>6(R)                              | 31/37                       |
| 248   | BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR , G                                                                             | 02/2005          | 8,692.97<br>15,095.67   | 15,095.67        | 13,727.00                   | 01/2011<br>05/2018    | 03/2019     | 98(O)<br>10(R)                             | 26/47                       |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                      |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|--------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                              | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                    | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 249   | BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR , G                                                                       | 01/2007          | 5,353.00<br>7,998.00    | 7,998.00         | 6,783.73                    | 05/2014<br>09/2017    | 06/2018     | 49(O)<br>9(R)                              | 1/18                        |
| 250   | NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture                                                        | 01/2013          | 12,964.60<br>-          | 13,731.26        | 10,084.21                   | 01/2018<br>-          | 12/2018     | 11(O)<br>-                                 | 27/31                       |
| 251   | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR , G                                         | 05/2015          | 436.68<br>-             | 602.44           | 472.27                      | 12/2016<br>-          | 12/2017     | 12(O)<br>-                                 | 8/16                        |
| 252   | ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR , G                                                    | 04/2016          | 790.13<br>-             | 790.30           | 250.26                      | 06/2019<br>-          | 06/2019     | 0(O)<br>-                                  | 0/0                         |
| 253   | SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH , G                 | 12/2011          | 1,746.65<br>2,228.71    | 2,228.71         | 1,962.81                    | 08/2014<br>12/2017    | 12/2017     | 40(O)<br>0(R)                              | 7/11                        |
| 254   | LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH , G                                              | 12/2012          | 11,846.00<br>-          | 11,846.00        | 8,605.00                    | 06/2017<br>12/2017    | 04/2018     | 10(O)<br>4(R)                              | 33/40                       |
| 255   | CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI , G                     | 03/2015          | 1,394.52<br>-           | 1,394.52         | 19.20                       | 05/2017<br>06/2019    | 06/2019     | 25(O)<br>0(R)                              | 4/9                         |
| 256   | CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI , G                     | 05/2015          | 780.33<br>-             | 780.33           | 31.99                       | 10/2018<br>-          | 10/2018     | 0(O)<br>-                                  | 0/0                         |
| 257   | TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]PGCIL,GUJARAT , G                                | 01/2016          | 244.19<br>-             | 244.19           | 108.85                      | 07/2018<br>-          | 11/2017     | -8(O)<br>-                                 | 0/0                         |
| 258   | TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT , G                                | 07/2016          | 300.94<br>-             | 300.94           | 22.11                       | 12/2018<br>-          | 12/2018     | 0(O)<br>-                                  | 0/0                         |
| 259   | WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT , G                                          | 11/2016          | 330.00<br>-             | 330.00           | 179.43                      | 11/2017<br>-          | 11/2017     | 0(O)<br>-                                  | 1/4                         |
| 260   | PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH , G                                                              | 09/2002          | 3,919.59<br>-           | 8,398.75         | 6,503.48                    | 09/2009<br>-          | 12/2018     | 111(O)<br>-                                | 2/3                         |
| 261   | KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR , G                                                                   | 01/2009          | 3,642.04<br>-           | 5,882.01         | 5,052.02                    | 01/2016<br>-          | 02/2018     | 25(O)<br>-                                 | 6/6                         |
| 262   | PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR , G                                                 | 10/2014          | 8,112.12<br>-           | 8,112.12         | -                           | 04/2020<br>-          | 05/2023     | 37(O)<br>-                                 | 0/0                         |
| 263   | TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI- LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR , G | 01/2014          | 1,788.41<br>-           | 2,352.57         | 1,154.26                    | 09/2017<br>-          | 09/2018     | 12(O)<br>-                                 | 0/0                         |
| 264   | NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND , G                                                                      | 02/2014          | 14,366.58<br>-          | 14,366.58        | 5,493.00                    | 02/2019<br>02/2020    | 02/2021     | 24(O)<br>12(R)                             | 18/20                       |
| 265   | BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND , G                                                                        | 08/2006          | 2,313.00<br>4,138.41    | 4,366.64         | 3,484.00                    | 12/2011<br>03/2016    | 02/2017     | -                                          | 14/14                       |
| 266   | PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND , G                                                                   | 10/2004          | 4,237.96<br>4,552.00    | 4,552.00         | 2,229.09                    | 10/2017<br>12/2016    | 10/2017     | 0(O)<br>10(R)                              | 0/0                         |
| 267   | KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA , G                                                                                   | 01/2012          | 15,166.19<br>-          | 15,166.19        | 14,295.00                   | 01/2017<br>07/2017    | 11/2017     | 10(O)<br>4(R)                              | 47/48                       |
| 268   | GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH , G                                                   | 03/2013          | 11,638.55<br>-          | 11,638.55        | 8,147.00                    | 09/2017<br>03/2018    | 03/2018     | 6(O)<br>0(R)                               | 31/41                       |
| 269   | KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH , G                                                                 | 03/2015          | 9,870.51<br>-           | 9,870.51         | 3,389.00                    | 09/2019<br>-          | 09/2019     | 0(O)<br>-                                  | 20/20                       |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                      |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|--------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                              | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                    | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 270   | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH , G                                         | 01/2016          | 305.04 -                | 305.04           | 156.38                      | 03/2017<br>10/2017    | 11/2017     | 8(O)<br>1(R)                               | 0/0                         |
| 271   | S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH , G   | 04/2016          | 287.99 -                | 287.99           | 73.10                       | 06/2018<br>-          | 06/2018     | 0(O)<br>-                                  | 0/0                         |
| 272   | AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects                                                        | 01/2017          | 2,104.21 -              | 2,104.21         | 40.26                       | 09/2020<br>-          | 09/2020     | 0(O)<br>-                                  | 9/16                        |
| 273   | TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL,MADHYA PRADESH , Central Sector Projects          | 02/2015          | 1,750.00 -              | 1,750.00         | 456.00                      | 06/2018<br>-          | 06/2018     | 0(O)<br>-                                  | 0/0                         |
| 274   | WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA , G                                                             | 12/2007          | 477.69<br>738.48        | 738.48           | 647.49                      | 09/2010<br>12/2017    | 03/2018     | 90(O)<br>3(R)                              | 4/8                         |
| 275   | MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA , G                                                                                 | 03/2012          | 7,921.47 -              | 7,921.47         | 5,302.00                    | 09/2016<br>03/2017    | 03/2017     | -                                          | 41/41                       |
| 276   | SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA , G                                                                                       | 03/2012          | 9,395.18 -              | 9,395.18         | 8,052.00                    | 11/2016<br>12/2017    | 04/2018     | 17(O)<br>4(R)                              | 34/36                       |
| 277   | TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]PGCIL,MAHARASHTRA , Central Sector Projects           | 04/2015          | 2,225.00<br>2,225.00    | 2,225.00         | 864.00                      | 01/2018<br>-          | 01/2018     | 0(O)<br>-                                  | 0/0                         |
| 278   | TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM , G                                                                | 07/1998          | 368.72<br>1,329.43      | 1,329.43         | 1,278.65                    | 07/2006<br>11/2017    | 11/2017     | 136(O)<br>0(R)                             | 6/13                        |
| 279   | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE , G                                        | 10/2008          | 4,824.12<br>5,071.94    | 5,071.94         | 4,475.16                    | 10/2012<br>02/2018    | 02/2018     | 64(O)<br>0(R)                              | 8/11                        |
| 280   | NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE , G                                                | 02/2009          | 11,130.19<br>13,762.80  | 13,762.80        | 12,549.95                   | 08/2013<br>12/2017    | 12/2017     | 52(O)<br>0(R)                              | 22/26                       |
| 281   | TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE , G                                      | 02/2010          | 2,144.00<br>2,932.88    | 2,932.88         | 2,564.46                    | 12/2012<br>02/2018    | 02/2018     | 62(O)<br>0(R)                              | 16/23                       |
| 282   | SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE , G                                                                    | 02/2010          | 232.34 -                | 245.00           | 238.61                      | 06/2012<br>-          | 12/2017     | 66(O)<br>-                                 | 1/4                         |
| 283   | EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE , G                                                           | 07/2010          | 1,272.80<br>1,731.10    | 1,731.10         | 1,413.61                    | 11/2012<br>12/2017    | 12/2017     | 61(O)<br>0(R)                              | 10/13                       |
| 284   | SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE , G                                                               | 10/2011          | 487.49<br>639.46        | 639.46           | 485.42                      | 06/2014<br>03/2018    | 06/2018     | 48(O)<br>3(R)                              | 10/12                       |
| 285   | SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE , G                                                      | 12/2011          | 297.33<br>346.79        | 426.29           | 357.17                      | 08/2014<br>12/2017    | 12/2017     | 40(O)<br>0(R)                              | 8/10                        |
| 286   | ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE , G                              | 03/2012          | 198.63 -                | 198.63           | 135.20                      | 09/2014<br>09/2017    | 01/2018     | 40(O)<br>4(R)                              | 0/0                         |
| 287   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE , G                                                  | 11/2011          | 723.63<br>882.13        | 882.13           | 719.42                      | 11/2014<br>06/2017    | 12/2017     | 37(O)<br>6(R)                              | 7/10                        |
| 288   | COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE , G | 03/2013          | 514.20<br>703.10        | 703.10           | 565.59                      | 06/2015<br>12/2017    | 03/2018     | 33(O)<br>3(R)                              | 7/10                        |
| 289   | COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE , G | 03/2013          | 2,514.88 -              | 2,514.88         | 1,959.67                    | 12/2015<br>12/2017    | 03/2018     | 27(O)<br>3(R)                              | 15/18                       |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                         |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                 | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                       | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 290   | EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE , G                                                                | 10/2013          | 1,364.52<br>1,891.41    | 1,891.41         | 1,151.24                    | 04/2016<br>09/2017    | 03/2018     | 23(O)<br>6(R)                              | 8/12                        |
| 291   | UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE , G                                                  | 01/2014          | 374.63<br>-             | 374.63           | 102.47                      | 04/2016<br>12/2017    | 12/2017     | 20(O)<br>0(R)                              | 0/0                         |
| 292   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE , G                                                    | 02/2014          | 539.82<br>-             | 539.82           | 386.19                      | 06/2016<br>02/2018    | 02/2018     | 20(O)<br>0(R)                              | 9/11                        |
| 293   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE , G                                                  | 02/2014          | 908.08<br>969.97        | 969.97           | 716.39                      | 06/2016<br>02/2018    | 11/2017     | 17(O)<br>-3(R)                             | 16/18                       |
| 294   | STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE , G                                                    | 05/2014          | 829.98<br>-             | 829.98           | 408.14                      | 08/2016<br>10/2017    | 12/2017     | 16(O)<br>2(R)                              | 2/4                         |
| 295   | EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE , G                                                              | 05/2014          | 522.29<br>550.18        | 550.18           | 362.94                      | 11/2016<br>11/2017    | 03/2018     | 16(O)<br>4(R)                              | 7/12                        |
| 296   | AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE , G                                             | 03/2014          | 155.57<br>206.42        | 206.42           | 131.33                      | 03/2016<br>07/2017    | 12/2017     | 21(O)<br>5(R)                              | 3/6                         |
| 297   | TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE , G            | 06/2014          | 5,151.37<br>-           | 5,151.37         | 1,474.02                    | 03/2018<br>-          | 06/2018     | 3(O)<br>-                                  | 8/12                        |
| 298   | SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE , G                                                  | 08/2014          | 288.49<br>-             | 376.09           | 219.91                      | 02/2017<br>06/2017    | 03/2018     | 13(O)<br>9(R)                              | 7/12                        |
| 299   | EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE , G                                                              | 02/2014          | 196.58<br>225.28        | 225.28           | 129.10                      | 02/2016<br>08/2017    | 12/2017     | 22(O)<br>4(R)                              | 10/17                       |
| 300   | INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE , G                                     | 12/2014          | 6,517.36<br>-           | 6,517.36         | 3,391.91                    | 04/2018<br>-          | 04/2018     | 0(O)<br>-                                  | 3/12                        |
| 301   | TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]PGCIL,MULTI STATE , G                                                 | 01/2015          | 268.80<br>340.88        | 340.88           | 160.06                      | 03/2018<br>-          | 03/2018     | 0(O)<br>-                                  | 0/3                         |
| 302   | TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE , G                                   | 01/2015          | 871.62<br>-             | 871.62           | 141.74                      | 10/2017<br>10/2017    | 06/2018     | 8(O)<br>8(R)                               | 0/5                         |
| 303   | SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE , G                                                      | 01/2015          | 203.28<br>260.03        | 260.03           | 160.70                      | 07/2017<br>-          | 12/2017     | 5(O)<br>-                                  | 3/5                         |
| 304   | ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE , G | 03/2015          | 197.40<br>-             | 197.40           | 45.02                       | 03/2018<br>-          | 03/2018     | 0(O)<br>-                                  | 0/0                         |
| 305   | INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE , G                                                           | 03/2015          | 1,071.24<br>-           | 1,071.24         | 462.18                      | 09/2017<br>-          | 04/2018     | 7(O)<br>-                                  | 0/0                         |
| 306   | GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE , G                                       | 04/2015          | 3,705.61<br>-           | 3,705.61         | 2,077.41                    | 04/2018<br>-          | 07/2018     | 3(O)<br>-                                  | 4/9                         |
| 307   | GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE , G                               | 04/2015          | 1,479.30<br>-           | 1,479.30         | 706.27                      | 04/2017<br>03/2018    | 03/2018     | 11(O)<br>0(R)                              | 2/8                         |
| 308   | GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE , G                              | 07/2015          | 2,247.37<br>-           | 2,247.37         | 619.60                      | 07/2018<br>-          | 07/2018     | 0(O)<br>-                                  | 0/0                         |
| 309   | SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE , G                                                         | 01/2016          | 1,455.47<br>-           | 1,455.47         | 471.19                      | 07/2018<br>-          | 07/2018     | 0(O)<br>-                                  | 0/0                         |



**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                         |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                 | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                       | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 310   | TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE , G | 03/2016          | 808.63 -                | 808.63           | 195.53                      | 01/2018 -             | 03/2019     | 14(O) -                                    | 0/0                         |
| 311   | EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE , G                                                               | 05/2016          | 766.21 -                | 766.21           | 12.93                       | 11/2018 -             | 11/2018     | 0(O) -                                     | 0/0                         |
| 312   | GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE , G                                      | 05/2016          | 3,519.59 -              | 3,519.59         | 369.73                      | 05/2019 -             | 05/2019     | 0(O) -                                     | 0/0                         |
| 313   | HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE , G | 05/2016          | 14,733.37 -             | 14,733.37        | 668.96                      | 11/2019 -             | 11/2019     | 0(O) -                                     | 0/0                         |
| 314   | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]PGCIL,MULTI STATE , G                | 04/2016          | 810.48 -                | 810.48           | 293.68                      | 12/2018 -             | 12/2018     | 0(O) -                                     | 0/0                         |
| 315   | EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL,MULTI STATE , G                                                              | 05/2016          | 167.01 -                | 167.01           | 30.86                       | 11/2018 -             | 11/2018     | 0(O) -                                     | 0/0                         |
| 316   | WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE , G                                                              | 07/2016          | 150.99 -                | 150.99           | 29.36                       | 07/2018 -             | 07/2018     | 0(O) -                                     | 0/0                         |
| 317   | POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL,MULTI STATE , G | 07/2016          | 333.17 -                | 333.17           | 140.83                      | 03/2019 -             | 03/2019     | 0(O) -                                     | 0/0                         |
| 318   | PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL,MULTI STATE , G                                     | 08/2016          | 431.89 -                | 431.89           | .40                         | 02/2019 -             | 02/2019     | 0(O) -                                     | 0/0                         |
| 319   | PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL,MULTI STATE , G                                                      | 08/2016          | 177.52 -                | 177.52           | 10.95                       | 02/2019 -             | 02/2019     | 0(O) -                                     | 0/0                         |
| 320   | SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE , G                                                             | 09/2016          | 562.25 -                | 562.25           | 18.56                       | 03/2019 -             | 03/2019     | 0(O) -                                     | 0/0                         |
| 321   | INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE , G           | 03/2017          | 251.60 -                | 251.60           | -                           | 06/2019 -             | 06/2019     | 0(O) -                                     | 0/0                         |
| 322   | AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]PGCIL,MULTI STATE , G                                           | 10/2016          | 167.75 -                | 167.75           | -                           | 04/2019 -             | 04/2019     | 0(O) -                                     | 0/0                         |
| 323   | S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE , G | 03/2017          | 283.72 -                | 283.72           | 7.71                        | 11/2019 -             | 11/2019     | 0(O) -                                     | 0/0                         |
| 324   | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE , G    | 10/2016          | 408.46 -                | 408.46           | 40.19                       | 01/2019 -             | 01/2019     | 0(O) -                                     | 0/0                         |
| 325   | SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE , G                | 10/2016          | 608.24 -                | 608.24           | 5.12                        | 04/2019 -             | 04/2019     | 0(O) -                                     | 0/0                         |
| 326   | WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE , G                                                            | 02/2017          | 195.05 -                | 195.05           | -                           | 02/2020 -             | 02/2020     | 0(O) -                                     | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                               |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                       | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                             | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 327   | ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE , G       | 02/2017          | 322.30<br>-             | 322.30           | 15.05                       | 02/2019<br>-          | 02/2019     | 0(O)<br>-                                  | 0/0                         |
| 328   | PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243]PGCIL,MULTI STATE , G        | 03/2017          | 162.31<br>-             | 162.31           | .62                         | 03/2019<br>-          | 03/2019     | 0(O)<br>-                                  | 0/0                         |
| 329   | EASTERN REGION STRENGTHENING SCHEME XVII( PART B) - [N18000244]PGCIL,MULTI STATE , G                                                          | 02/2017          | 235.53<br>-             | 235.53           | 5.36                        | 06/2019<br>-          | 06/2019     | 0(O)<br>-                                  | 0/0                         |
| 330   | SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE , G                                                         | 03/2017          | 379.95<br>-             | 379.95           | 19.67                       | 12/2019<br>-          | 12/2019     | 0(O)<br>-                                  | 0/0                         |
| 331   | WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL,MULTI STATE , G                                                                   | 02/2017          | 204.12<br>-             | 204.12           | 7.45                        | 09/2019<br>-          | 09/2019     | 0(O)<br>-                                  | 0/0                         |
| 332   | HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE , G       | 02/2017          | 5,070.13<br>-           | 5,070.13         | 211.75                      | 04/2020<br>-          | 04/2020     | 0(O)<br>-                                  | 0/0                         |
| 333   | SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE , G                                                     | 03/2017          | 337.75<br>-             | 337.75           | -                           | 06/2019<br>-          | 06/2019     | 0(O)<br>-                                  | 0/0                         |
| 334   | COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE , G              | 12/2014          | 4,754.42<br>-           | 4,754.42         | 361.65                      | 12/2018<br>-          | 12/2019     | 12(O)<br>-                                 | 0/0                         |
| 335   | NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE , G                         | 12/2014          | 5,111.33<br>-           | 5,111.33         | 352.58                      | 12/2018<br>-          | 12/2019     | 12(O)<br>-                                 | 0/0                         |
| 336   | TRANSMISSION SYSTEM ASSOCIATED WITH IPSPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE , Central Sector Projects  | 03/2015          | 955.00<br>1,161.00      | 1,364.00         | 1,075.00                    | 12/2015<br>-          | 03/2018     | 27(O)<br>-                                 | 0/0                         |
| 337   | TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL,MULTI STATE , Central Sector Projects       | 04/2015          | 2,525.00<br>-           | 2,525.00         | 1,217.00                    | 11/2017<br>-          | 11/2017     | 0(O)<br>-                                  | 0/0                         |
| 338   | STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects                                 | 12/2015          | 3,654.00<br>-           | 3,654.00         | 935.00                      | 04/2019<br>-          | 04/2019     | 0(O)<br>-                                  | 0/0                         |
| 339   | EASTERN REGION STRENGTHENING SCHEME-XXIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects                                            | 03/2017          | 3,500.00<br>3,500.00    | 3,500.00         | 55.00                       | 07/2020<br>-          | 07/2020     | 0(O)<br>-                                  | 0/0                         |
| 340   | TRANSMISSION SYSTEM ASSOCIATED WITH IPSPS OF NAGAPATTINAM CUDDALORE AREA - PACKAGE A - [N18000259]PGCIL,MULTI STATE , Central Sector Projects | 03/2015          | 955.00<br>1,161.00      | 1,364.00         | 515.00                      | 12/2015<br>-          | 03/2018     | 27(O)<br>-                                 | 0/0                         |
| 341   | TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-A - [N18000260]PGCIL,MULTI STATE , Central Sector Projects                    | 04/2015          | 2,525.00<br>-           | 2,525.00         | 1,215.00                    | 11/2017<br>-          | 11/2017     | 0(O)<br>-                                  | 0/0                         |
| 342   | DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA , G                                                                               | 02/2014          | 12,532.44<br>-          | 12,532.44        | 6,289.00                    | 08/2018<br>-          | 08/2018     | 0(O)<br>-                                  | 25/30                       |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                        |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|----------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                      | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 343   | PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA , G            | 04/2016          | 844.64 -                | 844.64           | 116.16                      | 04/2019 -             | 04/2019     | 0(O) -                                     | 0/0                         |
| 344   | TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN , G                                             | 07/2015          | 307.18 -                | 307.18           | 153.62                      | 11/2017 -             | 06/2018     | 7(O) -                                     | 0/0                         |
| 345   | WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC,RAJASTHAN , G                                           | 02/2015          | 302.49 302.00           | 302.49           | 270.77                      | 02/2016 -             | -           | -                                          | 1/1                         |
| 346   | TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN , G                                                | 07/2016          | 1,429.38 -              | 1,429.38         | 102.89                      | 01/2019 -             | 01/2019     | 0(O) -                                     | 0/0                         |
| 347   | KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU , G                                                                | 05/2005          | 1,779.29 2,187.32       | 2,187.32         | 1,955.61                    | 11/2008 09/2018       | 09/2018     | 118(O) 0(R)                                | 20/22                       |
| 348   | COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU , G | 09/2011          | 1,940.13 2,702.65       | 2,702.65         | 2,326.66                    | 09/2014 06/2017       | 12/2017     | 39(O) 6(R)                                 | 11/13                       |
| 349   | CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU , G                     | 01/2016          | 162.11 -                | 162.11           | 113.09                      | 05/2018 -             | 12/2017     | -5(O) -                                    | 0/0                         |
| 350   | 50 MW SOLAR POWER PROJECT - [N18000251]NHPC,TAMIL NADU , G                                                                             | 09/2017          | 287.48 -                | 287.48           | 27.51                       | 03/2018 -             | 03/2018     | 0(O) -                                     | 0/0                         |
| 351   | TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA , G                                                          | 01/2016          | 10,598.98 -             | 10,598.98        | 1,018.00                    | 07/2020 -             | 07/2020     | 0(O) -                                     | 13/18                       |
| 352   | TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA , G                                                                        | 07/2009          | 421.01 1,078.31         | 1,078.31         | 963.23                      | 07/2013 -             | -           | -                                          | 26/26                       |
| 353   | NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]PGCIL,TRIPURA , G                                                            | 05/2016          | 409.19 -                | 409.19           | 51.42                       | 05/2018 -             | 05/2018     | 0(O) -                                     | 0/0                         |
| 354   | FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH , G                                                               | 07/2013          | 3,363.12 -              | 3,363.12         | 2,244.00                    | 12/2016 -             | -           | -                                          | 28/28                       |
| 355   | TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH , G                                                                      | 09/2014          | 9,188.98 -              | 9,188.98         | 3,149.00                    | 03/2019 -             | 03/2019     | 0(O) -                                     | 19/27                       |
| 356   | DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH , G                                                                      | 05/2011          | 195.42 294.60           | 294.60           | 130.15                      | 02/2014 02/2018       | 12/2018     | 58(O) 10(R)                                | 3/5                         |
| 357   | MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture                                                         | 04/2012          | 9,750.89 -              | 9,750.89         | 6,957.91                    | 12/2016 -             | 06/2018     | 18(O) -                                    | 29/34                       |
| 358   | TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND , G                                                                 | 07/2006          | 1,657.00 2,978.86       | 3,939.11         | 2,373.15                    | 02/2016 09/2019       | 12/2020     | 58(O) 15(R)                                | 16/26                       |
| 359   | TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND , G                                                                      | 11/2006          | 2,978.48 -              | 3,846.30         | 3,300.00                    | 03/2013 06/2019       | 06/2019     | 75(O) 0(R)                                 | 3/15                        |
| 360   | VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND , G                                                         | 08/2008          | 2,491.58 -              | 2,491.58         | 1,244.96                    | 06/2013 -             | 11/2020     | 89(O) -                                    | 7/11                        |
| 361   | LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND , G                                                    | 07/2012          | 1,527.00 -              | 1,527.00         | 148.00                      | 08/2017 -             | 08/2017     | -                                          | 0/15                        |
| 362   | TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL , G | 04/2010          | 4,404.57 5,135.01       | 5,135.01         | 3,453.64                    | 01/2015 03/2018       | 03/2018     | 38(O) 0(R)                                 | 14/16                       |
| 363   | RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL , G                                                                            | 09/2014          | 1,381.84 -              | 1,381.84         | 289.00                      | 09/2019 -             | 09/2019     | 0(O) -                                     | 5/7                         |
| 364   | RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC,WEST BENGAL , G                                                            | 04/2007          | 4,122.00 8,781.30       | 9,142.58         | 8,300.00                    | 02/2011 -             | 03/2016     | -                                          | 26/26                       |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                        |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|--------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                      | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 365   | EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL , G                              | 04/2016          | 454.11 -                | 454.11           | 51.62                       | 04/2018 -             | 04/2018     | 0(O) -                                     | 0/0                         |
|       | Total                                                                                                  |                  | 3,39,545.24 -           | 3,97,302.11      | 2,24,764.86                 |                       |             |                                            | 855/1153                    |
|       |                                                                                                        |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>HEAVY INDUSTRY</u>                                                                                  |                  |                         |                  |                             |                       |             |                                            |                             |
| 366   | NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE , G | 04/2011          | 1,718.00 -              | 3,827.30         | 2,289.00                    | 09/2011 -             | 12/2017     | 75(O) -                                    | 0/0                         |
|       | Total                                                                                                  |                  | 1,718.00 -              | 3,827.30         | 2,289.00                    |                       |             |                                            | 0/0                         |
|       |                                                                                                        |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>HEALTH AND FAMILY WELFARE</u>                                                                       |                  |                         |                  |                             |                       |             |                                            |                             |
| 367   | LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM , G                                                      | 07/2012          | 175.57 -                | 175.57           | 113.50                      | 12/2014 -             | -           | -                                          | 0/0                         |
| 368   | LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI , G                                              | 02/2013          | 414.11 -                | 414.11           | 141.00                      | 11/2013 -             | -           | -                                          | 0/0                         |
| 369   | SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI , G      | 09/2013          | 444.70 -                | 444.70           | 326.30                      | 12/2015 -             | -           | -                                          | 0/0                         |
| 370   | SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI , G    | 11/2013          | 196.70 -                | 209.00           | 170.00                      | 01/2016 -             | -           | -                                          | 0/0                         |
| 371   | AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI , G                                             | 12/2013          | 204.44 -                | 204.44           | 137.00                      | 05/2017 -             | 12/2017     | 7(O) -                                     | 0/2                         |
| 372   | AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI , G                                                           | 08/2014          | 293.65 -                | 293.65           | 207.00                      | 05/2017 -             | 12/2017     | 7(O) -                                     | 0/5                         |
| 373   | CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA , G                       | 09/2014          | 505.58 -                | 505.58           | 202.00                      | 03/2018 -             | 03/2018     | 0(O) -                                     | 0/2                         |
| 374   | NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]HSCC,HARYANA , G                                    | 07/2016          | 312.99 -                | 312.99           | 120.00                      | 08/2018 -             | 08/2018     | 0(O) -                                     | 0/1                         |
| 375   | NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA , G                                            | 10/2016          | 363.99 -                | 363.99           | 6.00                        | 05/2018<br>08/2019    | 08/2019     | 15(O)<br>0(R)                              | 0/0                         |
| 376   | SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB , G                            | 07/2016          | 152.95 -                | 152.95           | 33.50                       | 02/2018 -             | 08/2018     | 6(O) -                                     | 0/1                         |
| 377   | AIIMS-RAE BARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH , G                                           | 10/2013          | 159.50 -                | 159.50           | 158.65                      | 11/2013<br>06/2017    | 06/2017     | -                                          | 0/8                         |
| 378   | CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL , G                       | 12/2014          | 168.90 -                | 168.90           | 108.00                      | 05/2017 -             | 12/2017     | 7(O) -                                     | 0/3                         |
| 379   | CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL , G                                             | 08/2016          | 244.00 -                | 244.00           | 70.00                       | 09/2018 -             | 09/2018     | 0(O) -                                     | 0/0                         |
|       | Total                                                                                                  |                  | 3,637.08 -              | 3,649.38         | 1,792.95                    |                       |             |                                            | 0/22                        |
|       |                                                                                                        |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>RAILWAYS</u>                                                                                        |                  |                         |                  |                             |                       |             |                                            |                             |
| 380   | NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH , G                                        | 03/1996          | 155.74<br>164.36        | 966.98           | 874.72                      | 02/2009 -             | 12/2017     | 106(O) -                                   | 0/0                         |
| 381   | KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH , G                                     | 12/2001          | 330.00 -                | 2,125.18         | 14.17                       | -                     | 03/2021     | -                                          | 0/0                         |
| 382   | RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH , G                                         | 04/2003          | 136.62 -                | 376.00           | -                           | 12/2007<br>03/2010    | -           | -                                          | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.** (All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                               |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|---------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                       | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                             | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 383   | OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH , G                                       | 07/2006          | 743.00 -                | 1,825.00         | -                           | 03/2008<br>06/2008    | 03/2020     | 144(O)<br>141(R)                           | 0/0                         |
| 384   | GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH , G                                                     | 04/2011          | 283.54 -                | 759.41           | .51                         | -<br>-                | -           | -                                          | 0/0                         |
| 385   | CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH , G                                                          | 04/2013          | 829.00 -                | 829.00           | .48                         | -<br>-                | -           | -                                          | 0/1                         |
| 386   | NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH , G                                                    | 04/2011          | 1,313.48 -              | 1,313.48         | 8.06                        | -<br>-                | -           | -                                          | 0/1                         |
| 387   | VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH , G                     | 03/2012          | 1,503.71 -              | 1,503.71         | 475.40                      | -<br>-                | 03/2020     | -<br>-                                     | 0/0                         |
| 388   | DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH , G                                                        | 04/2015          | 3,873.07 -              | 3,873.07         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 389   | GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH , G                                                           | 04/2016          | 4,000.00 -              | 3,631.00         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 390   | VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH , G                                                         | 04/2015          | 3,246.26 -              | 3,548.67         | 36.87                       | -<br>-                | -           | -                                          | 0/0                         |
| 391   | KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH , G                                            | 04/2015          | 2,499.71 -              | 2,499.71         | 25.30                       | 03/2021<br>-          | 03/2022     | 12(O)<br>-                                 | 0/0                         |
| 392   | MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH , G                             | 01/2013          | 387.70 -                | 387.70           | 351.00                      | 03/2018<br>-          | 03/2018     | 0(O)<br>-                                  | 0/0                         |
| 393   | MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH , G                                   | 08/2016          | 234.50 -                | 234.50           | .14                         | 03/2019<br>-          | 03/2019     | 0(O)<br>-                                  | 0/0                         |
| 394   | BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM , G                                       | 09/1997          | 1,500.00 -              | 5,000.00         | 4,793.77                    | 04/2008<br>12/2011    | 06/2018     | 122(O)<br>78(R)                            | 0/0                         |
| 395   | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM , G                    | 09/2006          | 200.00 -                | 780.00           | 425.47                      | -<br>-                | 03/2019     | -<br>-                                     | 0/0                         |
| 396   | KATAKHAL TO BHARABI - [N22000126]NFR,ASSAM , G                                                                | 04/1998          | 227.90 -                | 509.00           | 407.30                      | 12/2012<br>-          | 05/2016     | -                                          | 0/0                         |
| 397   | LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM , G             | 04/1996          | 1,676.31 -              | 7,000.00         | 7,041.41                    | 03/2009<br>-          | 03/2018     | 108(O)<br>-                                | 0/0                         |
| 398   | AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM , G                                                   | 04/2011          | 312.12 -                | 508.00           | 490.99                      | -<br>-                | 03/2019     | -<br>-                                     | 0/0                         |
| 399   | LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM , G                                               | 04/2012          | 246.07 -                | 398.93           | 103.22                      | -<br>-                | 03/2019     | -<br>-                                     | 0/0                         |
| 400   | LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR,ASSAM , G | 04/2003          | 971.22 -                | 966.27           | 834.11                      | -<br>-                | 12/2009     | -                                          | 0/0                         |
| 401   | RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR,ASSAM , G                                      | 04/2003          | 4,300.00 -              | 4,520.00         | 4,413.04                    | -<br>-                | 08/2015     | -                                          | 0/0                         |
| 402   | NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR,ASSAM , G                                                 | 04/2007          | 180.09 -                | 180.00           | 157.12                      | -<br>-                | 05/2011     | -                                          | 0/0                         |
| 403   | BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM , G                                              | 04/2015          | 2,232.32 -              | 2,232.32         | 63.56                       | -<br>-                | 03/2021     | -<br>-                                     | 0/0                         |
| 404   | DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM , G                                                              | 04/2015          | 870.96 -                | 870.96           | 18.49                       | -<br>-                | 03/2021     | -<br>-                                     | 0/0                         |
| 405   | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR , G                                          | 04/1997          | 501.69<br>335.77        | 1,043.56         | 876.49                      | 03/2012<br>-          | -           | -                                          | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                   |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|---------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                           | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                 | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 406   | KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR , G                                           | 09/2001          | 492.98 -                | 1,320.00         | 918.94                      | 12/2010 -             | -           | -                                          | 0/0                         |
| 407   | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR , G                                  | 04/1997          | 162.87 -                | 541.00           | 183.72                      | -                     | -           | -                                          | 0/0                         |
| 408   | HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR , G                                 | 04/2003          | 528.65 -                | 324.66           | 330.82                      | -                     | -           | -                                          | 0/0                         |
| 409   | KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR , G                                                  | 04/2002          | 322.95 -                | 341.41           | 320.39                      | 03/2012 -             | -           | -                                          | 0/0                         |
| 410   | DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR , G                                          | 04/2001          | 406.92 -                | 339.00           | 200.00                      | -                     | -           | -                                          | 0/0                         |
| 411   | MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR , G                                         | 04/2003          | 218.19 -                | 412.05           | 356.37                      | -                     | 03/2018     | -                                          | 0/0                         |
| 412   | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR , G                      | 04/1996          | 332.92 283.95           | 477.88           | 495.40                      | 03/2012 -             | -           | -                                          | 0/0                         |
| 413   | NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR , G               | 09/2006          | 300.00 -                | 2,145.00         | 921.25                      | -                     | 03/2020     | -                                          | 0/0                         |
| 414   | KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR , G                                         | 04/2008          | 282.92 -                | 360.00           | 3.13                        | -                     | -           | -                                          | 0/0                         |
| 415   | ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR , G                                                  | 04/2008          | 490.80 -                | 490.80           | .39                         | -                     | -           | -                                          | 0/0                         |
| 416   | NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR , G                                                   | 04/2008          | 620.57 -                | 620.57           | -                           | -                     | -           | -                                          | 0/0                         |
| 417   | GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR , G                                     | 04/2008          | 445.25 -                | 445.25           | -                           | -                     | -           | -                                          | 0/0                         |
| 418   | BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR , G                                                 | 04/2008          | 326.20 -                | 326.20           | 1.68                        | -                     | -           | -                                          | 0/0                         |
| 419   | SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR , G                                              | 04/1999          | 175.69 -                | 325.00           | 253.10                      | -                     | -           | -                                          | 0/0                         |
| 420   | CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR , G                                              | 04/2006          | 285.07 -                | 378.56           | 111.71                      | -                     | -           | -                                          | 0/0                         |
| 421   | DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR , G                                         | 04/2005          | 205.00 -                | 205.00           | 5.21                        | -                     | -           | -                                          | 0/0                         |
| 422   | MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR , G                                                | 04/2006          | 211.00 -                | 926.09           | 4.41                        | -                     | -           | -                                          | 0/0                         |
| 423   | SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR , G                            | 04/2008          | 678.62 -                | 2,393.23         | 17.17                       | -                     | -           | -                                          | 0/0                         |
| 424   | MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR , G                              | 04/2008          | 228.05 -                | 228.05           | 1.52                        | -                     | -           | -                                          | 0/0                         |
| 425   | ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR , G                                                     | 04/2008          | 304.41 -                | 304.41           | .19                         | -                     | -           | -                                          | 0/0                         |
| 426   | KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR , G                                                | 04/2008          | 192.56 -                | 192.56           | .38                         | -                     | -           | -                                          | 0/0                         |
| 427   | MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR , G                                             | 04/2008          | 281.30 -                | 281.30           | .58                         | -                     | -           | -                                          | 0/0                         |
| 428   | SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR , G | 04/2004          | 372.14 -                | 355.81           | 283.44                      | -                     | -           | -                                          | 0/0                         |
| 429   | JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR , G    | 04/2009          | 470.00 -                | 470.00           | 40.00                       | -                     | -           | -                                          | 0/0                         |
| 430   | HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR , G                                        | 04/2013          | 213.01 -                | 367.17           | 13.00                       | -                     | -           | -                                          | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.** (All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                           |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|---------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                   | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                         | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 431   | SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR , G                                                                           | 05/2015          | 380.00<br>-             | 380.00           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 432   | KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR , G                                                                   | 12/2015          | 1,200.20<br>-           | 1,200.20         | -                           | 12/2020<br>-          | 12/2020     | 0(O)<br>-                                  | 0/1                         |
| 433   | RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR , G                               | 12/2015          | 1,491.47<br>-           | 1,491.47         | -                           | 12/2020<br>-          | 12/2020     | 0(O)<br>-                                  | 1/1                         |
| 434   | MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR , G                                                                 | 01/1991          | 332.15<br>-             | 559.91           | 538.21                      | 07/2014<br>-          | -           | -                                          | 0/0                         |
| 435   | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH , G                        | 04/1995          | 304.00<br>-             | 1,195.00         | 474.51                      | 12/2012<br>-          | -           | -                                          | 0/0                         |
| 436   | SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH , G                                                     | 09/2006          | 324.90<br>-             | 516.40           | 479.68                      | 03/2010<br>-          | 12/2017     | 93(O)<br>-                                 | 0/3                         |
| 437   | KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH , G                                                           | 12/2012          | 826.57<br>-             | 1,160.83         | 452.03                      | -<br>-                | 03/2020     | -<br>-                                     | 0/1                         |
| 438   | RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH , G                                                           | 03/2007          | 758.09<br>-             | 758.09           | 632.15                      | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 439   | MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH , G                                               | 05/2014          | 207.00<br>-             | 207.00           | 142.00                      | 03/2018<br>-          | 03/2018     | 0(O)<br>-                                  | 0/0                         |
| 440   | GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI , G                                                                    | 04/1999          | 156.65<br>-             | 197.17           | 56.10                       | -<br>-                | -           | -                                          | 0/0                         |
| 441   | ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI , G                                                       | 04/2012          | 295.68<br>-             | 295.68           | 1.20                        | -<br>-                | -           | -                                          | 0/0                         |
| 442   | AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT , G                                                            | 04/2008          | 394.14<br>-             | 385.60           | 27.69                       | 03/2013<br>-          | 03/2020     | 84(O)<br>-                                 | 0/0                         |
| 443   | UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT , G                                             | 04/2008          | 1,389.62<br>-           | 1,389.62         | 1,513.78                    | 03/2014<br>-          | 12/2017     | 45(O)<br>-                                 | 0/0                         |
| 444   | BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT , G                                      | 04/2008          | 318.24<br>-             | 321.62           | 37.15                       | 03/2012<br>-          | 03/2019     | 84(O)<br>-                                 | 0/0                         |
| 445   | BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT , G                            | 04/2006          | 117.36<br>196.95        | 203.00           | 202.29                      | 03/2011<br>-          | -           | -                                          | 0/0                         |
| 446   | AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT , G                                                                        | 04/2012          | 567.18<br>-             | 975.62           | 308.42                      | -<br>-                | 03/2020     | -<br>-                                     | 0/0                         |
| 447   | DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT , G                                                                         | 04/2012          | 376.59<br>-             | 644.38           | 25.21                       | -<br>-                | 12/2020     | -<br>-                                     | 0/0                         |
| 448   | MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT , G                                                            | 04/2011          | 439.88<br>-             | 845.68           | .78                         | -<br>-                | -           | -                                          | 0/0                         |
| 449   | RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT , G | 04/1994          | 320.66<br>-             | 399.63           | -                           | -<br>-                | 03/2019     | -<br>-                                     | 0/0                         |
| 450   | PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT , G                                                                   | 04/2013          | 1,266.89<br>-           | 1,548.66         | 357.04                      | -<br>-                | 12/2020     | -<br>-                                     | 0/0                         |
| 451   | VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT , G                                                                      | 04/2011          | 446.00<br>-             | 1,037.15         | 590.60                      | -<br>-                | 03/2019     | -<br>-                                     | 0/0                         |
| 452   | VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT , G                                                                   | 04/2010          | 279.40<br>-             | 355.00           | 323.64                      | -<br>-                | -           | -                                          | 0/0                         |
| 453   | SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT , G                                                                         | 04/2015          | 1,002.39<br>-           | 1,002.39         | -                           | -<br>-                | 03/2021     | -<br>-                                     | 0/0                         |



**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                          |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|----------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                  | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                        | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 454   | MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT , G                                      | 10/2013          | 343.00 -                | 343.00           | 236.64                      | 03/2019 -             | 03/2019     | 0(O) -                                     | 0/0                         |
| 455   | JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA , G                                                         | 01/2004          | 238.56 -                | 740.00           | 722.65                      | 03/2012 -             | -           | -                                          | 0/0                         |
| 456   | ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA , G                                                           | 04/2012          | 287.00 -                | 625.00           | 4.38                        | -                     | -           | -                                          | 0/0                         |
| 457   | HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA , G                                        | 04/2013          | 400.00 -                | 400.00           | -                           | -                     | -           | -                                          | 0/0                         |
| 458   | ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA , G                                                   | 05/2015          | 400.00 -                | 400.00           | -                           | -                     | -           | -                                          | 0/0                         |
| 459   | MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA , G                                        | 12/2015          | 346.32 -                | 300.00           | 204.51                      | 03/2019 -             | 03/2019     | 0(O) -                                     | 0/0                         |
| 460   | BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH , G                                        | 04/2008          | 1,046.88 -              | 4,500.00         | 107.02                      | -                     | -           | -                                          | 0/0                         |
| 461   | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR , G                                | 03/1995          | 2,500.00 -              | 19,565.00        | 13,536.97                   | 11/2002 -             | 12/2018     | 193(O) -                                   | 0/0                         |
| 462   | MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND , G                                         | 04/1995          | 900.05 -                | 1,125.89         | 980.99                      | 12/2011 12/2010       | 03/2020     | 99(O) 111(R)                               | 0/0                         |
| 463   | RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND , G                                                  | 04/1997          | 194.07 -                | 491.33           | -                           | 06/2004 -             | -           | -                                          | 0/0                         |
| 464   | KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND , G                                                 | 04/2002          | 459.91 -                | 459.91           | 221.54                      | -                     | -           | -                                          | 0/0                         |
| 465   | GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND , G                                            | 03/1997          | 261.70 -                | 388.00           | 329.39                      | 02/2006 -             | 12/2019     | 166(O) -                                   | 0/1                         |
| 466   | TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND , G                                                  | 04/2008          | 167.73 -                | 167.73           | 207.11                      | 03/2012 -             | -           | -                                          | 0/0                         |
| 467   | DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND , G                                   | 04/2010          | 309.44 -                | 583.00           | -                           | 12/2015 -             | -           | -                                          | 0/0                         |
| 468   | MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND , G                                   | 04/2012          | 258.20 -                | 365.00           | -                           | -                     | 12/2017     | -                                          | 0/0                         |
| 469   | RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND , G                     | 04/2012          | 148.77 -                | 209.00           | -                           | 12/2016 -             | -           | -                                          | 0/0                         |
| 470   | BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND , G                                                | 03/2016          | 1,724.20 -              | 1,724.20         | -                           | 03/2021 -             | 03/2021     | 0(O) -                                     | 0/0                         |
| 471   | HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA , G                             | 02/1997          | 295.00 1,289.92         | 1,289.92         | 1,503.25                    | -                     | 01/2017     | -                                          | 0/1                         |
| 472   | HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA , G                                                      | 04/1997          | 227.00 -                | 2,135.00         | 133.87                      | -                     | -           | -                                          | 0/0                         |
| 473   | GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA , G                                                    | 02/1998          | 242.42 369.70           | 1,542.41         | 927.68                      | -                     | -           | -                                          | 0/1                         |
| 474   | BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA , G                                        | 04/1996          | 138.00 1,382.78         | 1,382.78         | 6.12                        | -                     | -           | -                                          | 0/0                         |
| 475   | RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA , G | 04/2007          | 482.00 -                | 874.57           | 985.32                      | 03/2013 -             | -           | -                                          | 0/0                         |
| 476   | TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA , G                                           | 04/2011          | 913.00 -                | 1,801.01         | 2.55                        | -                     | -           | -                                          | 0/0                         |
| 477   | MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA , G                                           | 04/2007          | 179.65 -                | 1,350.91         | 778.41                      | -                     | -           | -                                          | 0/1                         |
| 478   | BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA , G                                                       | 04/2010          | 377.93 986.30           | 986.30           | 267.65                      | -                     | -           | -                                          | 0/1                         |



| Detail of ongoing Projects Costing Rs.150 Crore and above. |                                                                                   |                  |                         |                  |                             | (All Cost/ Expenditure in Rs. Crore) |             |                                            |                             |
|------------------------------------------------------------|-----------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|--------------------------------------|-------------|--------------------------------------------|-----------------------------|
|                                                            |                                                                                   |                  |                         |                  |                             | Date of Commissioning                |             | (September 2017)                           |                             |
| Sl.No                                                      | Project                                                                           | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised                   | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1                                                          | 2                                                                                 | 3                | 4                       | 5                | 6                           | 7                                    | 8           | 9                                          | 10                          |
| 479                                                        | CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA , G | 04/2013          | 558.00<br>692.43        | 692.43           | -                           | -<br>-                               | -<br>-      | -                                          | 0/0                         |
| 480                                                        | SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA , G                                 | 04/2011          | 562.74<br>-             | 832.47           | .94                         | -<br>-                               | -<br>-      | -                                          | 0/0                         |
| 481                                                        | WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA , G                               | 04/2011          | 341.05<br>-             | 348.85           | .35                         | -<br>-                               | -<br>-      | -                                          | 0/0                         |
| 482                                                        | HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA , G                 | 04/2010          | 2,127.00<br>-           | 2,127.00         | 803.33                      | -<br>-                               | 03/2019     | -<br>-                                     | 0/1                         |
| 483                                                        | TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA , G                          | 04/2011          | 146.75<br>-             | 167.50           | .34                         | -<br>-                               | -<br>-      | -                                          | 0/0                         |
| 484                                                        | GADAG-WADI NL - [N22000299]SWR,KARNATAKA , G                                      | 04/2013          | 1,117.00<br>1,922.00    | 1,922.00         | 3.60                        | -<br>-                               | -<br>-      | -                                          | 0/0                         |
| 485                                                        | CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA , G                      | 04/2013          | 327.25<br>367.77        | 367.77           | -                           | -<br>-                               | -<br>-      | -                                          | 0/0                         |
| 486                                                        | MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA , G                                | 04/2012          | 285.57<br>279.54        | 279.54           | 2.75                        | 01/1999<br>-                         | -<br>-      | -                                          | 0/0                         |
| 487                                                        | HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA , G                  | 04/2010          | 203.40<br>203.40        | 273.84           | 281.02                      | -<br>-                               | -<br>-      | -                                          | 0/0                         |
| 488                                                        | HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA , G                                   | 03/2015          | 1,900.00<br>1,141.00    | 1,141.00         | 430.98                      | -<br>03/2020                         | -<br>-      | -                                          | 0/5                         |
| 489                                                        | ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA , G                                    | 03/2015          | 960.00<br>578.00        | 578.00           | 298.80                      | -<br>11/2015                         | 03/2020     | -<br>52(R)                                 | 0/2                         |
| 490                                                        | ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA , G                         | 10/1998          | 550.00<br>-             | 2,815.62         | 240.68                      | -<br>-                               | 01/2018     | -<br>-                                     | 0/0                         |
| 491                                                        | KUMBALAM-TURAVUR - [N22000191]SR,KERALA , G                                       | 04/2011          | 252.96<br>-             | 252.96           | 7.74                        | -<br>-                               | -<br>-      | -                                          | 0/0                         |
| 492                                                        | CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA , G                                 | 04/2006          | 191.72<br>-             | 342.85           | 360.22                      | -<br>-                               | -<br>-      | -                                          | 0/0                         |
| 493                                                        | ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA , G                                     | 04/2010          | 189.24<br>-             | 189.24           | 189.35                      | -<br>-                               | 12/2017     | -<br>-                                     | 0/0                         |
| 494                                                        | TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA , G                        | 02/2015          | 900.00<br>-             | 4,131.90         | -                           | -<br>-                               | -<br>-      | -                                          | 0/0                         |
| 495                                                        | TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA , G                           | 02/2015          | 1,000.00<br>-           | 1,000.00         | -                           | -<br>-                               | -<br>-      | -                                          | 0/0                         |
| 496                                                        | RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH , G                  | 04/2001          | 470.92<br>727.13        | 2,713.09         | 632.05                      | -<br>-                               | 03/2021     | -<br>-                                     | 0/0                         |
| 497                                                        | CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH , G               | 04/2005          | 383.79<br>-             | 1,101.16         | 194.91                      | -<br>-                               | -<br>-      | -                                          | 0/0                         |
| 498                                                        | BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH , G                 | 09/2007          | 687.20<br>-             | 950.00           | -                           | 03/2010<br>-                         | 03/2018     | 96(O)<br>-                                 | 0/0                         |
| 499                                                        | RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH , G                 | 04/2008          | 603.04<br>-             | 1,030.29         | 628.11                      | 03/2012<br>-                         | -<br>-      | -                                          | 0/0                         |
| 500                                                        | KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH , G            | 12/2015          | 1,762.94<br>-           | 1,762.94         | -                           | 12/2020<br>-                         | 12/2020     | 0(O)<br>-                                  | 1/1                         |
| 501                                                        | BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH , G                 | 04/2011          | 1,485.65<br>-           | 1,485.85         | 685.71                      | 12/2020<br>-                         | 12/2020     | 0(O)<br>-                                  | 0/0                         |
| 502                                                        | KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH , G                  | 06/2016          | 2,478.23<br>-           | 2,478.23         | -                           | 03/2022<br>-                         | 03/2022     | 0(O)<br>-                                  | 0/1                         |
| 503                                                        | KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH , G                | 08/2016          | 582.13<br>-             | 582.13           | -                           | 03/2020<br>-                         | 03/2020     | 0(O)<br>-                                  | 0/1                         |
| 504                                                        | MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH , G           | 12/2015          | 174.00<br>-             | 174.00           | 90.63                       | 03/2019<br>-                         | 03/2019     | 0(O)<br>-                                  | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                       |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                               | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                     | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 505   | AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA , G                                                               | 06/1994          | 663.01<br>668.34        | 858.97           | 694.80                      | 06/1999<br>-          | -           | -                                          | 0/0                         |
| 506   | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA , G                                   | 03/1996          | 495.44<br>1,781.98      | 1,781.98         | 663.37                      | 03/2004<br>-          | 03/2020     | 192(O)<br>-                                | 0/0                         |
| 507   | AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA , G                                                      | 02/1997          | 514.68<br>-             | 2,271.50         | 812.01                      | -<br>-                | -           | -                                          | 0/0                         |
| 508   | MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA , G                                             | 04/2008          | 5,300.00<br>-           | 7,986.04         | 2,423.55                    | 03/2014<br>-          | 03/2019     | 60(O)<br>-                                 | 0/0                         |
| 509   | RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA , G                                            | 04/2012          | 714.10<br>-             | 714.10           | 65.20                       | 04/2016<br>-          | -           | -                                          | 0/0                         |
| 510   | WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA , G                                                             | 04/2008          | 499.30<br>2,491.43      | 3,168.29         | 700.77                      | -<br>-                | 03/2023     | -<br>-                                     | 0/0                         |
| 511   | KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA , G                                                                | 04/2011          | 277.70<br>792.89        | 792.89           | 202.91                      | -<br>-                | 03/2021     | -<br>-                                     | 0/0                         |
| 512   | 3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA , G                                                     | 04/2011          | 184.06<br>-             | 199.12           | 142.22                      | -<br>-                | -           | -                                          | 0/0                         |
| 513   | WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA , G                                                          | 04/2012          | 297.85<br>540.02        | 540.02           | 118.37                      | -<br>-                | 03/2022     | -<br>-                                     | 0/0                         |
| 514   | INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA , G                                                 | 02/2016          | 9,968.00<br>-           | 9,968.00         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 515   | PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA , G                                                                   | 02/2016          | 2,425.00<br>-           | 2,425.00         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 516   | VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA , G                                                        | 02/2016          | 2,750.00<br>-           | 2,750.00         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 517   | WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA , G                                                 | 02/2015          | 630.00<br>1,272.19      | 1,272.19         | 51.81                       | -<br>-                | 03/2022     | -<br>-                                     | 0/0                         |
| 518   | ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA , G                                              | 02/2015          | 2,326.00<br>2,449.91    | 2,449.91         | 12.54                       | -<br>-                | 03/2023     | -<br>-                                     | 0/0                         |
| 519   | PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA , G                                                             | 02/2015          | 4,670.00<br>3,627.00    | 3,627.47         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 520   | DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA , G                                                               | 02/2016          | 1,876.00<br>-           | 2,081.27         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 521   | MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA , G                                                  | 02/2016          | 854.00<br>-             | 1,035.16         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 522   | WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA , G                                                    | 02/2016          | 912.00<br>637.95        | 637.95           | .36                         | -<br>-                | 03/2022     | -<br>-                                     | 0/0                         |
| 523   | DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA , G | 03/2009          | 1,514.45<br>-           | 1,514.45         | -                           | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 524   | DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA , G                                                                 | 04/2015          | 723.78<br>-             | 723.78           | .22                         | 12/2025<br>-          | 12/2025     | 0(O)<br>-                                  | 0/0                         |
| 525   | RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA , G                                              | 09/2016          | 1,273.00<br>1,908.00    | 1,908.00         | -                           | 12/2021<br>-          | 12/2021     | 0(O)<br>-                                  | 0/0                         |
| 526   | MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA , G                                            | 10/2013          | 305.00<br>-             | 305.00           | -                           | 03/2019<br>-          | 03/2019     | 0(O)<br>-                                  | 0/0                         |
| 527   | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR , G                                                      | 04/2003          | 727.56<br>-             | 9,658.00         | 5,418.63                    | 03/2011<br>-          | 03/2020     | 108(O)<br>-                                | 0/0                         |
| 528   | NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]NFR,MEGHALAYA , G                                                  | 04/2010          | 4,083.02<br>-           | 6,000.00         | 249.54                      | -<br>-                | 03/2021     | -<br>-                                     | 0/0                         |
| 529   | BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM , G                                                               | 04/2008          | 619.34<br>-             | 4,600.00         | 1,651.19                    | 04/2014<br>-          | 03/2020     | 71(O)<br>-                                 | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|--------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                        | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                              | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 530   | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE , G                                             | 04/1986          | 158.77<br>274.56        | 634.48           | 629.43                      | 03/1994<br>-          | -           | -                                          | 0/0                         |
| 531   | CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE , G                                                                    | 02/1996          | 240.00<br>-             | 579.37           | 537.02                      | -<br>-                | -           | -                                          | 0/0                         |
| 532   | GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE , G                                                                   | 02/1997          | 386.30<br>-             | 1,776.81         | 967.96                      | 03/1998<br>-          | 12/2019     | 261(O)<br>-                                | 0/0                         |
| 533   | NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE , G                                                                       | 03/1981          | 450.00<br>-             | 2,100.00         | 484.14                      | 07/2012<br>-          | -           | -                                          | 0/0                         |
| 534   | MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE , G                                                               | 04/1997          | 218.24<br>236.41        | 525.00           | 544.20                      | -<br>-                | 03/2019     | -<br>-                                     | 0/0                         |
| 535   | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE , G                                                        | 09/1998          | 247.66<br>-             | 6,093.31         | 972.82                      | 05/2008<br>-          | 03/2023     | 178(O)<br>-                                | 0/4                         |
| 536   | KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE , G                                                       | 04/1999          | 744.71<br>744.71        | 1,126.79         | 761.70                      | -<br>-                | -           | -                                          | 1/1                         |
| 537   | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE , G                                                         | 03/2002          | 625.30<br>408.76        | 876.10           | 841.57                      | 06/2007<br>-          | -           | -                                          | 0/0                         |
| 538   | QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE , G                                                | 03/1998          | 280.00<br>-             | 1,122.00         | 834.61                      | -<br>-                | -           | -                                          | 0/6                         |
| 539   | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE , G                                        | 04/2000          | 733.00<br>-             | 3,010.00         | 2,344.94                    | 12/2008<br>-          | 03/2019     | 123(O)<br>-                                | 0/0                         |
| 540   | GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE , G                                                                    | 04/1998          | 92.63<br>-              | 350.00           | 316.64                      | 02/2011<br>-          | -           | -                                          | 0/0                         |
| 541   | DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE , G                                                                 | 04/2000          | 607.09<br>-             | 973.33           | 613.71                      | 12/2012<br>12/2012    | -           | -                                          | 0/0                         |
| 542   | HATHUA-BHATNI (NL) (NER) - [220100319]NER,MULTI STATE , G                                                                      | 04/2005          | 230.03<br>-             | 718.54           | 274.67                      | -<br>-                | 05/2019     | -<br>-                                     | 0/0                         |
| 543   | ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE , G                                            | 12/2006          | 170.00<br>-             | 436.00           | 439.57                      | 03/2011<br>-          | 10/2011     | -                                          | 0/0                         |
| 544   | CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE , G                                                | 03/2007          | 243.78<br>-             | 268.78           | 96.70                       | -<br>-                | 08/2017     | -                                          | 0/0                         |
| 545   | CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE , G                                                                             | 03/2013          | 295.00<br>-             | 477.31           | 92.31                       | -<br>-                | 10/2018     | -<br>-                                     | 0/0                         |
| 546   | CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE , G                                                                          | 04/2007          | 1,347.26<br>-           | 1,347.26         | 270.58                      | -<br>-                | -           | -                                          | 0/0                         |
| 547   | DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE , G                                               | 04/2007          | 1,640.04<br>-           | 1,640.04         | 331.91                      | -<br>-                | 03/2022     | -<br>-                                     | 0/0                         |
| 548   | RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE , G                                                            | 04/2011          | 2,082.75<br>-           | 2,562.27         | 180.57                      | -<br>-                | -           | -                                          | 0/1                         |
| 549   | GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE , G                                                | 04/2011          | 1,176.09<br>-           | 3,845.60         | 1.92                        | 02/2020<br>-          | 12/2022     | 34(O)<br>-                                 | 0/0                         |
| 550   | DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE , G | 04/2010          | 622.41<br>-             | 2,030.50         | 10.34                       | 02/2019<br>-          | 12/2022     | 46(O)<br>-                                 | 0/0                         |
| 551   | DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE , G                                                    | 04/2010          | 553.63<br>-             | 1,009.00         | 7.88                        | -<br>-                | -           | -                                          | 0/0                         |
| 552   | GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE , G                                                                             | 04/2008          | 415.67<br>-             | 549.75           | 14.62                       | -<br>-                | -           | -                                          | 0/0                         |
| 553   | NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE , G                                                      | 04/2013          | 1,798.00<br>-           | 1,798.00         | -                           | -<br>-                | 03/2019     | -<br>-                                     | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                      |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|--------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                              | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                    | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 554   | CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE , G                                                                   | 04/2008          | 523.52<br>2,350.00      | 523.52           | 2.27                        | -<br>-                | -           | -                                          | 0/0                         |
| 555   | VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]RVNL,MULTI STATE , G                                                           | 04/2008          | 822.39<br>-             | 1,810.00         | 1,639.70                    | -<br>-                | 03/2018     | -<br>-                                     | 0/1                         |
| 556   | KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE , G                                                                            | 04/2007          | 270.14<br>-             | 346.15           | 253.87                      | -<br>-                | -           | -                                          | 0/0                         |
| 557   | NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE , G                                                             | 04/2010          | 242.22<br>-             | 471.00           | 50.99                       | -<br>-                | -           | -                                          | 0/0                         |
| 558   | NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE , G                                                              | 04/2010          | 241.52<br>-             | 394.28           | 148.33                      | -<br>-                | -           | -                                          | 0/0                         |
| 559   | MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE , G                                                                            | 04/2011          | 165.82<br>-             | 450.00           | 117.50                      | -<br>-                | 03/2020     | -<br>-                                     | 0/0                         |
| 560   | NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE , G   | 04/1999          | 523.17<br>-             | 1,871.00         | 1,071.96                    | -<br>-                | 03/2018     | -<br>-                                     | 0/0                         |
| 561   | MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE , G                                                                   | 04/2011          | 601.43<br>-             | 1,500.00         | 71.75                       | -<br>-                | -           | -                                          | 0/0                         |
| 562   | LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE , G | 04/1987          | 406.99<br>-             | 319.58           | 141.88                      | -<br>-                | -           | -                                          | 0/0                         |
| 563   | SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE , G                                                  | 04/2007          | 450.00<br>-             | 290.85           | 9.31                        | -<br>-                | -           | -                                          | 0/0                         |
| 564   | HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE , G                                                                     | 04/2010          | 172.03<br>-             | 260.60           | 6.42                        | -<br>-                | -           | -                                          | 0/0                         |
| 565   | PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE , G                                                                                    | 04/2013          | 915.98<br>1,130.13      | 1,130.13         | .30                         | -<br>-                | -           | -                                          | 0/0                         |
| 566   | PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE , G                                                                             | 04/2011          | 248.07<br>-             | 234.41           | 161.17                      | 03/2015<br>-          | -           | -                                          | 0/0                         |
| 567   | BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE , G                                                                              | 04/2011          | 288.35<br>-             | 238.36           | 51.31                       | -<br>-                | -           | -                                          | 0/0                         |
| 568   | PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE , G                                                                                  | 04/2011          | 261.38<br>-             | 332.14           | 87.22                       | -<br>-                | -           | -                                          | 0/0                         |
| 569   | KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE , G | 04/2001          | 923.52<br>-             | 923.52           | 227.50                      | -<br>-                | -           | -                                          | 0/0                         |
| 570   | CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE , G                     | 04/2005          | 595.91<br>-             | 595.91           | 103.62                      | -<br>-                | -           | -                                          | 0/0                         |
| 571   | KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE , G                      | 04/2010          | 174.56<br>-             | 160.97           | 56.25                       | -<br>-                | -           | -                                          | 0/0                         |
| 572   | SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE , G                                         | 04/2010          | 277.28<br>-             | 266.00           | 92.93                       | -<br>-                | -           | -                                          | 0/0                         |
| 573   | DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE , G   | 04/2010          | 296.44<br>-             | 198.88           | 15.83                       | -<br>-                | -           | -                                          | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                      |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|--------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                              | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                    | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 574   | HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE , G                                           | 04/2010          | 157.94<br>-             | 157.94           | 47.63                       | -<br>-                | 11/2018     | -<br>-                                     | 0/0                         |
| 575   | BARIARPUUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE , G                                                 | 04/2007          | 450.55<br>-             | 251.05           | 15.66                       | -<br>-                | -           | -                                          | 0/0                         |
| 576   | TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE , G                                                                        | 04/2010          | 365.17<br>-             | 365.67           | 1.37                        | -<br>-                | -           | -                                          | 0/0                         |
| 577   | HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE , G                                                                                    | 04/2011          | 267.09<br>-             | 350.78           | 98.15                       | -<br>-                | -           | -                                          | 0/0                         |
| 578   | SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE , G                                                                           | 04/2011          | 193.44<br>-             | 186.64           | 150.28                      | -<br>-                | -           | -                                          | 0/0                         |
| 579   | BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE , G                                                                          | 04/2011          | 175.80<br>-             | 173.91           | 18.54                       | -<br>-                | -           | -                                          | 0/0                         |
| 580   | PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE , G                                                    | 04/2011          | 299.60<br>-             | 269.60           | 1.11                        | 03/2017<br>-          | -           | -                                          | 0/0                         |
| 581   | NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE , G | 04/2010          | 494.54<br>-             | 369.69           | 31.99                       | -<br>-                | -           | -                                          | 0/0                         |
| 582   | SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE , G                                 | 04/2000          | 297.47<br>-             | 153.02           | 52.01                       | -<br>-                | -           | -                                          | 0/0                         |
| 583   | CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE , G | 04/2003          | 337.96<br>-             | 186.89           | 62.73                       | -<br>-                | -           | -                                          | 0/0                         |
| 584   | MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE , G  | 04/2009          | 493.96<br>-             | 681.68           | 135.79                      | -<br>-                | -           | -                                          | 0/0                         |
| 585   | KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE , G                                              | 04/2010          | 423.66<br>-             | 720.59           | 456.58                      | 03/2017<br>-          | -           | -                                          | 0/0                         |
| 586   | SANTOSHPUTR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE , G                                                | 04/2010          | 268.52<br>-             | 268.52           | 78.81                       | -<br>-                | -           | -                                          | 0/0                         |
| 587   | HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE , G         | 04/2011          | 166.89<br>-             | 166.89           | .02                         | -<br>-                | -           | -                                          | 0/0                         |
| 588   | PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE , G                                                                                    | 04/2007          | 98.74<br>-              | 381.39           | 312.12                      | -<br>-                | -           | -                                          | 0/0                         |
| 589   | PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE , G                                                                                  | 04/2006          | 96.16<br>-              | 280.00           | 268.37                      | -<br>-                | -           | -                                          | 0/0                         |
| 590   | KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE , G                                                    | 04/2012          | 1,054.35<br>-           | 2,200.00         | 85.33                       | -<br>-                | -           | -                                          | 0/0                         |
| 591   | BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE , G                                                                                 | 04/2012          | 923.23<br>-             | 923.23           | 1.11                        | -<br>-                | -           | -                                          | 0/1                         |
| 592   | DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE , G                                                                | 04/2013          | 1,239.00<br>-           | 1,239.00         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 593   | DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE , G                                                                  | 04/2007          | 336.91<br>-             | 336.91           | 143.18                      | -<br>-                | -           | -                                          | 0/0                         |

| Detail of ongoing Projects Costing Rs.150 Crore and above. |                                                                                              |                  |                         |                  |                             | (All Cost/ Expenditure in Rs. Crore) |             |                                            |                             |
|------------------------------------------------------------|----------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|--------------------------------------|-------------|--------------------------------------------|-----------------------------|
|                                                            |                                                                                              |                  |                         |                  |                             | Date of Commissioning                |             | (September 2017)                           |                             |
| Sl.No                                                      | Project                                                                                      | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised                   | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1                                                          | 2                                                                                            | 3                | 4                       | 5                | 6                           | 7                                    | 8           | 9                                          | 10                          |
| 594                                                        | SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE , G                               | 04/2013          | 296.00 -                | 466.65           | -                           | -                                    | -           | -                                          | 0/0                         |
| 595                                                        | RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE , G                                        | 04/2007          | 970.34 -                | 1,714.49         | 584.84                      | -                                    | -           | -                                          | 0/2                         |
| 596                                                        | BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE , G                                | 04/2010          | 337.49 -                | 792.01           | 1.13                        | -                                    | -           | -                                          | 0/1                         |
| 597                                                        | KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE , G              | 04/2008          | 2,050.00 -              | 2,050.00         | 200.35                      | -                                    | -           | -                                          | 0/1                         |
| 598                                                        | AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE , G  | 04/2010          | 338.54 -                | 338.54           | 212.64                      | -                                    | -           | -                                          | 0/0                         |
| 599                                                        | JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE , G                         | 04/2008          | 162.96 -                | 162.96           | 153.31                      | -                                    | -           | -                                          | 0/0                         |
| 600                                                        | YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE , G              | 04/2013          | 876.00 -                | 876.00           | -                           | -                                    | -           | -                                          | 0/0                         |
| 601                                                        | CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE , G                                          | 04/2007          | 328.14 -                | 1,540.00         | 45.20                       | -                                    | -           | -                                          | 0/0                         |
| 602                                                        | MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE , G                                            | 04/2012          | 250.93 -                | 259.23           | 8.43                        | -                                    | -           | -                                          | 0/0                         |
| 603                                                        | JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE , G                                  | 04/2007          | 313.24 -                | 554.70           | 342.00                      | 01/1999 -                            | -           | -                                          | 0/0                         |
| 604                                                        | MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE , G                                   | 04/2008          | 466.48 -                | 750.00           | -                           | 01/1999 -                            | -           | -                                          | 0/0                         |
| 605                                                        | PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE , G                                   | 05/2015          | 600.00 -                | 648.00           | .94                         | -                                    | 03/2020     | -                                          | 0/0                         |
| 606                                                        | MIRAJ-LONDA - [N22000327]SWR,MULTI STATE , G                                                 | 03/2015          | 1,830.00<br>1,190.92    | 1,190.92         | 75.57                       | -                                    | -           | -                                          | 0/0                         |
| 607                                                        | YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE , G                                         | 05/2015          | 860.43 -                | 860.43           | 285.52                      | -                                    | 03/2020     | -                                          | 0/0                         |
| 608                                                        | HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE , G                                           | 03/2015          | 1,618.00<br>1,614.59    | 1,614.59         | 434.83                      | -                                    | -           | -                                          | 0/0                         |
| 609                                                        | HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE , G                                         | 05/2015          | 720.00 -                | 678.54           | -                           | -                                    | 12/2018     | -                                          | 0/38                        |
| 610                                                        | DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects   | 10/2006          | 81,459.00 -             | 28,181.00        | -                           | -                                    | -           | -                                          | 0/0                         |
| 611                                                        | KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE , G                                            | 04/2015          | 2,063.03 -              | 2,063.03         | .14                         | -                                    | 03/2021     | -                                          | 0/0                         |
| 612                                                        | GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE , G                                | 04/2015          | 636.38 -                | 636.38           | -                           | -                                    | -           | -                                          | 0/0                         |
| 613                                                        | DUDHNOI-MENDHIPATHAR - [N22000378]NFR,MULTI STATE , G                                        | 04/1992          | 315.64 -                | 315.00           | 308.58                      | -                                    | 11/2014     | -                                          | 0/0                         |
| 614                                                        | HARMUTI-NAHARLAGUN - [N22000382]NFR,MULTI STATE , G                                          | 04/2006          | 614.54 -                | 613.00           | 549.19                      | -                                    | 03/2014     | -                                          | 0/0                         |
| 615                                                        | NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND , G | 04/2006          | 850.00 -                | 3,000.00         | 362.71                      | 03/2015 -                            | 03/2020     | 60(O)<br>-                                 | 0/0                         |
| 616                                                        | DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND , G                                               | 04/2013          | 4,274.00 -              | 4,274.00         | -                           | -                                    | 03/2020     | -                                          | 0/0                         |
| 617                                                        | KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA , G                                    | 04/1994          | 470.21 -                | 3,004.90         | 899.41                      | -                                    | 06/2021     | -                                          | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                           |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|---------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                   | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                         | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 618   | HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA , G                                                                     | 04/1996          | 301.64 -                | 1,185.64         | -                           | - 09/2009             | 03/2019     | - 114(R)                                   | 0/0                         |
| 619   | RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL, ODISHA , G                                                                   | 04/1999          | 166.16 -                | 380.00           | 370.37                      | 02/2009 02/2009       | 06/2017     | -                                          | 0/1                         |
| 620   | SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA , G                                                             | 04/1998          | 183.23 -                | 1,202.70         | 392.96                      | 02/2015 -             | 12/2019     | 58(O) -                                    | 0/0                         |
| 621   | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, ODISHA , G                                                   | 04/2000          | 133.41 207.00           | 340.00           | -                           | 03/2009 03/2009       | 12/2017     | 105(O) 105(R)                              | 1/1                         |
| 622   | TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR, ODISHA , G                                                                | 04/2005          | 810.78 -                | 1,928.07         | 466.10                      | - -                   | 12/2022     | - -                                        | 0/0                         |
| 623   | CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA , G                                                    | 04/2010          | 149.90 -                | 230.00           | 54.96                       | 03/2015 -             | -           | -                                          | 0/0                         |
| 624   | SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR, ODISHA , G                                                                  | 03/2011          | 679.27 -                | 1,579.27         | 561.78                      | - -                   | 03/2021     | - -                                        | 0/0                         |
| 625   | BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR, ODISHA , G                                                                 | 03/2013          | 858.67 -                | 843.04           | 41.36                       | - -                   | 03/2021     | - -                                        | 0/0                         |
| 626   | JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR, ODISHA , G                                                                 | 03/2006          | 201.00 -                | 230.00           | 242.28                      | - -                   | -           | -                                          | 0/0                         |
| 627   | SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA , G                                                      | 03/2012          | 155.81 -                | 238.03           | 149.99                      | - -                   | 03/2020     | - -                                        | 0/0                         |
| 628   | DELANG-PURI DOUBLING - [N22000320]ECOR, ODISHA , G                                                                        | 03/2011          | 165.16 -                | 234.71           | 224.64                      | 03/2015 -             | -           | -                                          | 0/0                         |
| 629   | JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR, ODISHA , G                                                                 | 04/2015          | 1,547.38 -              | 1,547.38         | 34.69                       | 03/2021 -             | 03/2021     | 0(O) -                                     | 0/0                         |
| 630   | KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR, ODISHA , G                                                            | 04/2015          | 2,361.74 -              | 2,361.74         | 17.49                       | 03/2021 -             | 03/2022     | 12(O) -                                    | 0/0                         |
| 631   | JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR, ODISHA , G                         | 04/2015          | 701.61 -                | 701.61           | 37.66                       | 03/2021 -             | 03/2021     | 0(O) -                                     | 0/0                         |
| 632   | BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR, ODISHA , G                                        | 04/2015          | 1,172.92 -              | 1,172.92         | 74.32                       | 03/2021 -             | 03/2020     | -12(O) -                                   | 0/0                         |
| 633   | ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER, ODISHA , G                                                        | 11/2015          | 969.83 -                | 969.83           | -                           | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/0                         |
| 634   | RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER, ODISHA , G | 04/1995          | 524.43 -                | 939.00           | -                           | 12/2021 -             | 12/2021     | 0(O) -                                     | 0/0                         |
| 635   | VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL, ODISHA , G                                                           | 01/1991          | 2,335.67 -              | 2,335.67         | 10.76                       | - -                   | 12/2024     | - -                                        | 0/0                         |
| 636   | SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL, ODISHA , G                                                            | 03/2006          | 960.18 -                | 960.18           | 704.78                      | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/0                         |
| 637   | BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA , G                                                              | 03/2009          | 942.95 -                | 942.95           | 795.83                      | 03/2019 -             | 03/2019     | 0(O) -                                     | 0/0                         |
| 638   | EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR, ODISHA , G           | 04/2016          | 5,200.00 -              | 5,200.00         | -                           | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/0                         |
| 639   | MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]JNR,PUNJAB , G       | 04/2009          | 396.04 -                | 369.00           | 186.27                      | - -                   | -           | -                                          | 0/0                         |
| 640   | QADIAN-BEAS - [N22000295]JNR,PUNJAB , G                                                                                   | 04/2011          | 205.22 -                | 205.22           | 1.59                        | - -                   | -           | -                                          | 0/0                         |



| Detail of ongoing Projects Costing Rs.150 Crore and above. |                                                                                                       |                  |                         |                  |                             | (All Cost/ Expenditure in Rs. Crore) |             |                                            |                             |
|------------------------------------------------------------|-------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|--------------------------------------|-------------|--------------------------------------------|-----------------------------|
|                                                            |                                                                                                       |                  |                         |                  |                             | Date of Commissioning                |             | (September 2017)                           |                             |
| Sl.No                                                      | Project                                                                                               | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised                   | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1                                                          | 2                                                                                                     | 3                | 4                       | 5                | 6                           | 7                                    | 8           | 9                                          | 10                          |
| 641                                                        | DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN , G                                            | 02/1997          | 410.08 -                | 780.98           | 368.96                      | - -                                  | 08/2018     | - -                                        | 0/0                         |
| 642                                                        | HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN , G                           | 04/2008          | 829.74 -                | 1,161.64         | 435.68                      | 03/2015 -                            | 12/2019     | 57(O) -                                    | 0/0                         |
| 643                                                        | JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN , G      | 04/2008          | 653.19 -                | 941.04           | 642.94                      | 03/2014 -                            | 06/2019     | 63(O) -                                    | 0/0                         |
| 644                                                        | SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN , G         | 04/2008          | 516.23 -                | 735.00           | 694.13                      | 03/2014 -                            | -           | -                                          | 0/0                         |
| 645                                                        | BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN , G                                       | 04/2012          | 246.08 -                | 348.55           | 22.76                       | - -                                  | 03/2019     | - -                                        | 0/0                         |
| 646                                                        | THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN , G                                                     | 04/2013          | 236.93 -                | 276.89           | 98.58                       | - -                                  | 10/2018     | - -                                        | 0/0                         |
| 647                                                        | AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN , G                                         | 04/2013          | 822.00 -                | 822.00           | -                           | - -                                  | -           | -                                          | 0/1                         |
| 648                                                        | PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN , G                                                          | 04/2013          | 323.00 -                | 323.00           | -                           | - -                                  | -           | -                                          | 0/0                         |
| 649                                                        | MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN , G            | 04/2013          | 456.00 -                | 855.16           | 594.34                      | - -                                  | 05/2018     | - -                                        | 0/0                         |
| 650                                                        | RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN , G | 04/2010          | 739.65 -                | 872.22           | 796.25                      | - -                                  | -           | -                                          | 0/1                         |
| 651                                                        | GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN , G                                     | 04/2011          | 239.73 -                | 257.78           | 194.32                      | - -                                  | -           | -                                          | 0/0                         |
| 652                                                        | AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN , G                                                       | 04/2011          | 213.39 -                | 272.99           | 89.27                       | - -                                  | 03/2019     | - -                                        | 0/0                         |
| 653                                                        | RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN , G                                         | 04/2012          | 288.97 335.53           | 369.08           | 160.39                      | - -                                  | 10/2018     | - -                                        | 0/0                         |
| 654                                                        | ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN , G                                                | 04/2013          | 242.09 -                | 293.68           | 120.02                      | - -                                  | 03/2019     | - -                                        | 0/0                         |
| 655                                                        | AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN , G       | 05/2015          | 873.71 -                | 873.71           | -                           | - -                                  | -           | -                                          | 0/0                         |
| 656                                                        | MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN , G                                | 01/2011          | 493.17 -                | 493.17           | 383.12                      | 03/2018 -                            | 03/2018     | 0(O) -                                     | 0/0                         |
| 657                                                        | MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]CCOI,RAJASTHAN , G                              | 04/2012          | 471.82 -                | 471.82           | 19.91                       | 03/2019 -                            | 03/2019     | 0(O) -                                     | 0/0                         |
| 658                                                        | SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM , G                                                        | 04/2008          | 1,339.48 -              | 4,084.69         | 383.92                      | 12/2015 -                            | 03/2020     | 51(O) -                                    | 0/0                         |
| 659                                                        | KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU , G                                                     | 02/1997          | 155.55 -                | 870.00           | 854.92                      | - -                                  | -           | -                                          | 0/0                         |
| 660                                                        | TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU , G                                | 09/1995          | 100.00 -                | 980.00           | 647.64                      | - -                                  | -           | -                                          | 0/0                         |
| 661                                                        | EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU , G                 | 04/2006          | 495.74 -                | 495.74           | 404.30                      | 06/2013 -                            | 03/2018     | 57(O) -                                    | 1/4                         |
| 662                                                        | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU , G        | 09/2007          | 404.19 -                | 2,072.50         | 957.24                      | - -                                  | -           | -                                          | 0/0                         |
| 663                                                        | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU , G                      | 09/2006          | 343.17 -                | 1,065.00         | 1,047.11                    | - -                                  | -           | -                                          | 0/0                         |



**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                        |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                      | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 664   | ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU , G                                                                       | 04/2008          | 446.87<br>527.37        | 527.37           | 3.34                        | -<br>01/2011          | -           | -                                          | 0/0                         |
| 665   | SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU , G            | 04/2013          | 839.00<br>-             | 1,500.00         | .61                         | -<br>-                | -           | -                                          | 0/0                         |
| 666   | CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU , G                                         | 04/1998          | 271.24<br>-             | 520.00           | 464.65                      | -<br>-                | -           | -                                          | 0/0                         |
| 667   | ERODE-PALANI - [N22000199]SR,TAMIL NADU , G                                                                            | 04/2008          | 288.57<br>-             | 603.22           | 1.63                        | -<br>-                | -           | -                                          | 0/0                         |
| 668   | MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU , G                                                                  | 04/2008          | 164.41<br>-             | 302.90           | 31.98                       | -<br>-                | -           | -                                          | 0/0                         |
| 669   | THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL,TAMIL NADU , G | 04/2011          | 190.10<br>-             | 350.00           | 282.22                      | -<br>-                | 03/2019     | -                                          | 0/0                         |
| 670   | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA , G                                                  | 12/1994          | 124.43<br>-             | 1,010.00         | 919.06                      | -<br>-                | -           | -                                          | 0/0                         |
| 671   | MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA , G                                                              | 07/1998          | 125.00<br>-             | 480.00           | 3.48                        | 07/2008<br>-          | -           | -                                          | 0/0                         |
| 672   | MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA , G                                                      | 04/2006          | 378.56<br>-             | 1,160.47         | 1.74                        | -<br>-                | 03/2022     | -                                          | 0/1                         |
| 673   | MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA , G                                  | 04/2012          | 632.68<br>-             | 816.55           | 451.81                      | 03/2016<br>-          | 12/2018     | 33(O)<br>-                                 | 0/0                         |
| 674   | MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA , G                                                                     | 04/2013          | 1,112.00<br>-           | 1,112.00         | .36                         | -<br>-                | -           | -                                          | 0/1                         |
| 675   | KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA , G                                                                   | 04/2013          | 616.08<br>-             | 616.08           | .36                         | -<br>-                | -           | -                                          | 0/1                         |
| 676   | DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA , G              | 03/2015          | 636.38<br>-             | 636.38           | 169.16                      | 03/2021<br>-          | 03/2021     | 0(O)<br>-                                  | 3/3                         |
| 677   | SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA , G                                                     | 04/2015          | 728.10<br>-             | 728.10           | 15.05                       | 12/2024<br>-          | 12/2024     | 0(O)<br>-                                  | 0/0                         |
| 678   | AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA , G                                                                | 04/2008          | 813.34<br>-             | 3,451.00         | 2,351.21                    | 03/2014<br>-          | 03/2020     | 72(O)<br>-                                 | 0/0                         |
| 679   | CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA , G                                                | 04/1999          | 895.00<br>-             | 1,857.00         | 1,487.59                    | 03/2007<br>-          | 04/2016     | -                                          | 0/0                         |
| 680   | AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA , G                                                                       | 04/2012          | 252.00<br>-             | 580.00           | -                           | -<br>-                | 07/2019     | -<br>-                                     | 2/3                         |
| 681   | KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH , G                                                      | 03/1997          | 677.97<br>1,062.36      | 1,679.13         | 1,706.54                    | -<br>-                | -           | -                                          | 0/0                         |
| 682   | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH , G                                          | 04/1999          | 108.00<br>-             | 432.72           | 446.52                      | 12/2009<br>-          | -           | -                                          | 0/0                         |
| 683   | ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH , G                                                            | 04/1997          | 120.00<br>-             | 245.39           | 210.67                      | 12/2008<br>-          | -           | -                                          | 0/0                         |
| 684   | UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH , G                                                 | 04/2006          | 325.00<br>-             | 1,581.53         | 618.19                      | 03/2010<br>-          | -           | -                                          | 0/0                         |
| 685   | ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH , G                         | 02/2008          | 171.10<br>-             | 275.08           | 141.55                      | 03/2012<br>-          | -           | -                                          | 0/0                         |
| 686   | ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH , G                                               | 03/2013          | 307.00<br>-             | 308.00           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 687   | BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH , G                                                      | 03/2008          | 195.64<br>-             | 474.30           | 398.89                      | -<br>-                | 10/2017     | -<br>-                                     | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                   |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|-------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                           | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                 | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 688   | AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH , G                                         | 03/2012          | 199.75<br>-             | 199.75           | 210.64                      | -<br>-                | 03/2018     | -<br>-                                     | 0/0                         |
| 689   | KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH , G                     | 03/2013          | 643.00<br>-             | 644.00           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 690   | MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH , G                                                    | 04/2012          | 377.44<br>-             | 377.44           | 182.85                      | -<br>-                | -           | -                                          | 0/0                         |
| 691   | FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH , G                       | 04/2013          | 654.00<br>-             | 654.00           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 692   | UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH , G                                                                 | 04/2012          | 380.00<br>-             | 380.00           | 4.12                        | -<br>-                | -           | -                                          | 0/0                         |
| 693   | GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH , G                                                    | 04/2014          | 182.92<br>-             | 197.73           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 694   | GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH , G                     | 04/1997          | 836.26<br>-             | 1,072.52         | 1,026.65                    | -<br>-                | -           | -                                          | 0/0                         |
| 695   | ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH , G                                            | 03/2015          | 1,750.00<br>-           | 1,295.42         | 19.80                       | 03/2022<br>-          | 03/2022     | 0(O)<br>-                                  | 0/0                         |
| 696   | MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH , G                                                  | 04/2015          | 524.00<br>668.00        | 668.00           | -                           | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/6                         |
| 697   | VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH , G                                        | 04/2015          | 750.55<br>-             | 750.56           | 17.25                       | 12/2024<br>-          | 12/2024     | 0(O)<br>-                                  | 0/0                         |
| 698   | LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH , G                                   | 04/2011          | 927.01<br>-             | 977.00           | 733.32                      | 03/2019<br>-          | 03/2019     | 0(O)<br>-                                  | 0/0                         |
| 699   | MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH , G                                                | 04/2015          | 1,765.90<br>-           | 1,765.90         | 26.79                       | 12/2025<br>-          | 12/2025     | 0(O)<br>-                                  | 0/0                         |
| 700   | BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH , G                                | 03/2012          | 1,183.25<br>-           | 1,183.30         | 723.70                      | 12/2020<br>-          | 12/2020     | 0(O)<br>-                                  | 0/0                         |
| 701   | RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH , G                                                     | 08/2015          | 2,436.21<br>-           | 2,436.21         | 44.89                       | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 702   | KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH , G                                            | 08/2015          | 528.57<br>-             | 528.57           | 61.44                       | 03/2018<br>-          | 03/2019     | 12(O)<br>-                                 | 0/0                         |
| 703   | KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND , G                                                        | 04/2003          | 142.45<br>-             | 228.40           | .15                         | -<br>-                | -           | -                                          | 0/0                         |
| 704   | HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND , G                                                                   | 04/2012          | 219.83<br>-             | 346.63           | 38.33                       | -<br>-                | -           | -                                          | 0/0                         |
| 705   | RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND , G                                                | 04/2011          | 4,295.30<br>-           | 1,621.60         | 167.32                      | 12/2026<br>-          | 12/2026     | 0(O)<br>-                                  | 0/0                         |
| 706   | NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL , G          | 04/1983          | 36.80<br>274.41         | 614.00           | 262.50                      | -<br>-                | -           | -                                          | 0/0                         |
| 707   | HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL , G                                                 | 04/1974          | 393.46<br>154.30        | 1,026.00         | -                           | 03/2007<br>03/2007    | -           | -                                          | 0/0                         |
| 708   | TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL , G | 03/2000          | 1,049.69<br>-           | 3,404.92         | 3,544.30                    | 12/2006<br>-          | -           | -                                          | 0/0                         |
| 709   | TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL , G                                       | 04/2000          | 1,188.91<br>-           | 1,319.33         | 757.23                      | -<br>12/2009          | 03/2019     | -<br>111(R)                                | 0/0                         |
| 710   | BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL , G                                                              | 04/2007          | 1,106.62<br>-           | 1,106.62         | 355.85                      | 12/2010<br>-          | -           | -                                          | 3/7                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                    |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                            | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                  | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 711   | TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL, G                                                                 | 03/1984          | 293.97 -                | 749.69           | -                           | 06/2005 -             | -           | -                                          | 0/0                         |
| 712   | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL, G           | 04/2010          | 2,397.72 -              | 2,397.72         | 197.20                      | 03/2016 -             | -           | -                                          | 0/0                         |
| 713   | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL, G | 04/2010          | 2,298.42 -              | 2,733.86         | 40.14                       | 03/2014 -             | -           | -                                          | 0/0                         |
| 714   | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL, G     | 04/2010          | 3,951.98 -              | 4,259.48         | 1,455.71                    | 03/2016 -             | 12/2020     | 57(O) -                                    | 0/0                         |
| 715   | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL, G                 | 04/2010          | 2,913.51 -              | 2,913.50         | 713.47                      | 03/2016 -             | 12/2018     | 33(O) -                                    | 0/0                         |
| 716   | DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL, G                                                                    | 04/2009          | 533.38 -                | 533.38           | 127.10                      | 12/2011 -             | -           | -                                          | 0/0                         |
| 717   | GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL, G                                                                          | 04/2009          | 611.03 -                | 611.03           | 146.31                      | 12/2011 -             | -           | -                                          | 0/0                         |
| 718   | PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL, G                                                                  | 04/2004          | 293.74 -                | 229.33           | 140.60                      | 12/2010 -             | -           | -                                          | 0/0                         |
| 719   | BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL, G                          | 04/1999          | 207.52 -                | 334.87           | 293.47                      | 12/2012 -             | -           | -                                          | 0/0                         |
| 720   | EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL, G                                         | 03/2013          | 4,874.58 -              | 4,874.58         | 1,881.65                    | 03/2016 -             | 06/2018     | 27(O) -                                    | 0/0                         |
| 721   | BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL, G                                                                              | 04/2010          | 267.37 -                | 434.00           | -                           | - -                   | -           | -                                          | 0/0                         |
| 722   | BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL, G                                                               | 04/2011          | 289.64 -                | 760.00           | -                           | - -                   | -           | -                                          | 0/0                         |
| 723   | TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL, WEST BENGAL, G                                                                 | 04/2010          | 171.02 -                | 250.00           | 241.47                      | 06/2013 -             | 12/2016     | -                                          | 0/0                         |
| 724   | NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL, G                                                          | 04/2010          | 221.42 -                | 380.00           | 32.48                       | - -                   | -           | -                                          | 0/0                         |
| 725   | NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL, G                                                                       | 04/2011          | 209.77 -                | 445.00           | 389.45                      | - -                   | 03/2018     | -                                          | 0/0                         |
| 726   | NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL, G                                                   | 04/2012          | 283.55 -                | 330.00           | 191.07                      | - -                   | 03/2019     | -                                          | 0/0                         |
| 727   | CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL, G                                           | 04/2009          | 573.78 -                | 268.52           | .67                         | - -                   | -           | -                                          | 0/0                         |
| 728   | BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL, G                                                                   | 04/2012          | 255.64 -                | 272.20           | .64                         | - -                   | -           | -                                          | 0/0                         |
| 729   | MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL, G                                                                        | 04/2011          | 276.69 -                | 426.00           | -                           | 01/1999 -             | -           | -                                          | 0/0                         |
| 730   | NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL, G                                  | 04/2016          | 556.31 -                | 612.00           | -                           | - -                   | -           | -                                          | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                        | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                              | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 731   | TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER, WEST BENGAL , G               | 01/1991          | 763.18 -                | 1,428.00         | -                           | 12/2021 -             | 12/2021     | 0(O) -                                     | 0/0                         |
| 732   | BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL , G                                                    | 04/1998          | 1,027.40 -              | 2,373.00         | -                           | 03/2003 -             | -           | -                                          | 0/0                         |
|       | <b>Total</b>                                                                                                                                   |                  | 3,54,063.17 -           | 4,54,173.45      | 1,30,576.24                 |                       |             |                                            | 13/110                      |
|       | <b>ROAD TRANSPORT AND HIGHWAYS</b>                                                                                                             |                  |                         |                  |                             |                       |             |                                            |                             |
| 733   | CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH , PPP (BOT)                                                   | 11/2010          | 1,585.00 -              | 1,585.00         | 2,284.33                    | 05/2013 -             | 12/2017     | 55(O) -                                    | 0/0                         |
| 734   | TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH , PPP (BOT)                                                                   | 04/2011          | 571.00 -                | 571.00           | 622.89                      | 10/2013 -             | 12/2017     | 50(O) -                                    | 0/0                         |
| 735   | SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH , PPP (BOT)                                  | 11/2011          | 1,535.00 -              | 1,535.00         | 3,093.77                    | 05/2014 -             | 06/2017     | -                                          | 0/0                         |
| 736   | REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH, ANDHRA PRADESH , EPC  | 12/2014          | 201.12 201.00           | 201.12           | -                           | 02/2015 -             | -           | -                                          | 0/4                         |
| 737   | REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION ) - [N24000263]PWD, ANDHRA PRADESH , G          | 02/2015          | 241.61 -                | 241.61           | 7.71                        | 02/2017 -             | 02/2017     | -                                          | 0/1                         |
| 738   | REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD, ANDHRA PRADESH , EPC    | 11/2014          | 297.78 330.00           | 330.00           | -                           | 02/2017 -             | 02/2017     | -                                          | 0/0                         |
| 739   | REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD, ANDHRA PRADESH , G       | 01/2014          | 361.30 200.69           | 207.40           | 44.08                       | 07/2014 -             | -           | -                                          | 0/1                         |
| 740   | REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD, ANDHRA PRADESH , EPC    | 02/2014          | 258.99 -                | 258.99           | 16.54                       | 07/2014 -             | 07/2016     | -                                          | 0/1                         |
| 741   | REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD, ANDHRA PRADESH , EPC    | 07/2014          | 251.55 -                | 251.55           | 7.74                        | 02/2015 -             | 02/2017     | -                                          | 0/1                         |
| 742   | REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD, ANDHRA PRADESH , EPC    | 03/2015          | 175.03 -                | 175.00           | -                           | - -                   | -           | -                                          | 0/1                         |
| 743   | REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD, ANDHRA PRADESH , EPC    | 02/2015          | 266.00 -                | 266.00           | -                           | - -                   | -           | -                                          | 0/4                         |
| 744   | REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735 (IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH, ANDHRA PRADESH , EPC | 07/2015          | 314.43 -                | 314.43           | -                           | - -                   | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                     |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                             | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                                   | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 745   | FOUR LANING OF 5.122 KM OF NH9 ( NEW NH 65) FROM KM 269.900 ( DESIGN CH.0 ) TO KM 275-622( DESIGN C - [N24000274]PWD,ANDHRA PRADESH , G             | 07/2015          | 333.21<br>333.21        | 333.21           | -                           | 12/2015<br>-          | 12/2016     | -                                          | 0/2                         |
| 746   | REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , EPC           | 01/2014          | 195.45<br>-             | 195.45           | -                           | 11/2014<br>-          | 11/2016     | -                                          | 0/4                         |
| 747   | REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH , EPC             | 02/2014          | 170.21<br>-             | 170.21           | 5.65                        | 11/2014<br>-          | 11/2016     | -                                          | 0/4                         |
| 748   | REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH , EPC        | 10/2015          | 480.21<br>-             | 480.21           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 749   | REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH , EPC                                | 02/2015          | 224.83<br>-             | 224.83           | -                           | 05/2015<br>-          | 05/2017     | -                                          | 2/4                         |
| 750   | REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOUT - [N24000300]PWD,ANDHRA PRADESH , EPC         | 03/2015          | 309.01<br>-             | 309.01           | -                           | 09/2015<br>-          | 08/2017     | -                                          | 0/4                         |
| 751   | REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH , EPC           | 03/2015          | 271.45<br>-             | 271.45           | -                           | 10/2015<br>-          | 10/2017     | 24(O)<br>-                                 | 0/0                         |
| 752   | FOUR LANING OF 5.122 KM OF NH9( NEW NH 65) FROM KM 269.900( DESIGN CH.0 ) - [N24000302]PWD,ANDHRA PRADESH , G                                       | 07/2015          | 333.21<br>-             | 333.21           | -                           | 12/2015<br>-          | 12/2016     | -                                          | 0/0                         |
| 753   | REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH , EPC          | 02/2014          | 417.61<br>-             | 417.61           | -                           | 06/2014<br>-          | 06/2016     | -                                          | 0/2                         |
| 754   | FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC          | 10/2015          | 333.21<br>-             | 333.21           | -                           | 11/2015<br>-          | 11/2015     | -                                          | 0/0                         |
| 755   | REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH , EPC                                                           | 02/2015          | 224.83<br>-             | 224.83           | -                           | 04/2015<br>-          | 05/2016     | -                                          | 0/0                         |
| 756   | FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH , G                                          | 01/2016          | 1,134.97<br>-           | 1,134.97         | 171.12                      | -<br>-                | 11/2018     | -<br>-                                     | 0/0                         |
| 757   | VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH , G                                                                                 | 09/2014          | 1,684.00<br>-           | 1,684.00         | 54.13                       | 02/2017<br>-          | 02/2017     | -                                          | 0/0                         |
| 758   | REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH , G                                | 03/2017          | 648.32<br>-             | 503.10           | -                           | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 759   | SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH , G                           | 03/2017          | 1,041.62<br>-           | 1,187.10         | -                           | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 760   | TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , ITEM RATE | 12/2011          | 156.63<br>276.00        | 276.00           | 132.21                      | 02/2012<br>-          | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                     |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                             | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                                   | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 761   | TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , ITEM RATE | 11/2010          | 305.49 -                | 305.49           | -                           | 03/2011 -             | -           | -                                          | 0/0                         |
| 762   | TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , ITEM RATE  | 03/2012          | 207.03 -                | 207.03           | -                           | 05/2012 -             | -           | -                                          | 0/0                         |
| 763   | 2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC    | 03/2015          | 194.11 -                | 194.11           | 30.54                       | 05/2018 -             | 05/2018     | 0(O) -                                     | 1/4                         |
| 764   | 2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , EPC                                | 10/2015          | 179.82 -                | 179.82           | 8.99                        | 01/2019 -             | 01/2019     | 0(O) -                                     | 1/4                         |
| 765   | CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC    | 07/2015          | 197.16 -                | 197.16           | 38.50                       | 10/2018 -             | 10/2018     | 0(O) -                                     | 1/4                         |
| 766   | 2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC                | 03/2015          | 394.00 -                | 394.00           | -                           | 06/2018 -             | 06/2018     | 0(O) -                                     | 0/3                         |
| 767   | FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH , ITEM RATE  | 01/2011          | 264.16 -                | 264.16           | -                           | - -                   | -           | -                                          | 0/0                         |
| 768   | TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH , ITEM RATE | 12/2009          | 165.00 -                | 165.00           | -                           | 09/2010 -             | 09/2010     | -                                          | 0/0                         |
| 769   | TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH , ITEM RATE | 12/2009          | 104.00 -                | 201.00           | -                           | 09/2010 -             | 09/2010     | -                                          | 0/0                         |
| 770   | 2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH , EPC                                   | 03/2015          | 235.08 -                | 235.08           | -                           | 05/2018 -             | 05/2018     | 0(O) -                                     | 1/4                         |
| 771   | 2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH , G     | 01/2016          | 183.65 -                | 183.65           | -                           | 11/2016 -             | 11/2016     | -                                          | 0/0                         |
| 772   | FUNDED ) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH , G      | 01/2016          | 334.22 -                | 334.22           | -                           | 06/2016 -             | 06/2016     | -                                          | 0/4                         |
| 773   | CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD( NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH , G      | 04/2016          | 245.79 -                | 245.79           | -                           | - -                   | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                        | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                              | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 774   | CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH , G  | 04/2016          | 198.00 -                | 198.00           | -                           | 10/2016 -             | 10/2016     | -                                          | 0/4                         |
| 775   | FUNDED ) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH , G | 11/2015          | 434.06 -                | 434.06           | -                           | - -                   | -           | -                                          | 0/0                         |
| 776   | CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH , G                                | 12/2016          | 138.93 155.00           | 155.00           | -                           | 01/2017 -             | 01/2020     | 36(O) -                                    | 0/0                         |
| 777   | CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH , G     | 01/2017          | 1,253.10 -              | 1,253.10         | -                           | 03/2017 -             | -           | -                                          | 0/0                         |
| 778   | TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH , G | 03/2017          | 284.09 -                | 284.09           | -                           | 04/2017 -             | -           | -                                          | 0/0                         |
| 779   | TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH , G | 02/2017          | 195.23 -                | 195.23           | -                           | 04/2017 -             | -           | -                                          | 0/0                         |
| 780   | TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH , G | 02/2017          | 203.36 -                | 203.36           | -                           | 04/2017 -             | -           | -                                          | 0/0                         |
| 781   | TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH , G  | 01/2017          | 194.66 -                | 194.66           | -                           | 04/2017 -             | -           | -                                          | 0/0                         |
| 782   | TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH , G  | 02/2017          | 168.32 -                | 168.32           | -                           | 04/2017 -             | -           | -                                          | 0/0                         |
| 783   | TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH , G  | 02/2017          | 180.57 -                | 180.57           | -                           | 04/2017 -             | -           | -                                          | 0/0                         |
| 784   | CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH , G | 02/2017          | 216.71 -                | 216.71           | -                           | 04/2017 -             | -           | -                                          | 0/0                         |
| 785   | CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH , G | 02/2017          | 167.28 -                | 167.28           | -                           | 04/2017 -             | -           | -                                          | 0/0                         |
| 786   | TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH , G  | 01/2017          | 198.22 -                | 198.22           | -                           | 04/2017 -             | -           | -                                          | 0/0                         |
| 787   | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM , G                                                             | 12/2003          | 280.00 -                | 361.00           | -                           | 02/2009 -             | 12/2017     | 106(O) -                                   | 0/0                         |
| 788   | MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM , G                                                                | 12/2003          | 199.81 -                | 385.13           | -                           | 04/2009 -             | -           | -                                          | 0/0                         |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                         |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                 | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                       | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 789   | MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM , G                                                   | 12/2003          | 167.64 -                | 167.64           | -                           | 11/2008 -             | -           | -                                          | 0/0                         |
| 790   | MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM , G                                                        | 12/2003          | 155.04 -                | 280.13           | -                           | 11/2008 -             | -           | -                                          | 0/0                         |
| 791   | MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM , G                                                          | 12/2003          | 200.00 -                | 200.00           | -                           | 04/2009 -             | 05/2017     | -                                          | 0/0                         |
| 792   | SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM , G                                                                                   | 12/2003          | 245.00 -                | 245.00           | -                           | 03/2008 -             | 05/2017     | -                                          | 0/0                         |
| 793   | NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM , G                                                                                     | 12/2003          | 225.00 -                | 225.00           | -                           | 06/2008 -             | 09/2017     | 111(O) -                                   | 0/0                         |
| 794   | NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM , G                                                                                      | 12/2003          | 208.00 -                | 208.00           | -                           | 04/2008 -             | 12/2017     | 116(O) -                                   | 0/0                         |
| 795   | DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM , G                                                                     | 12/2003          | 160.00 -                | 160.00           | -                           | 05/2008 -             | 05/2017     | -                                          | 0/0                         |
| 796   | HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM , G                                                                                 | 12/2003          | 196.00 -                | 331.23           | -                           | 07/2009 -             | -           | -                                          | 0/0                         |
| 797   | BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM , G                                                                                  | 12/2003          | 217.61 -                | 309.56           | -                           | 04/2010 -             | 03/2018     | 95(O) -                                    | 0/0                         |
| 798   | FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC    | 05/2015          | 454.89 -                | 454.89           | 22.74                       | 05/2018 -             | 05/2018     | 0(O) -                                     | 0/4                         |
| 799   | 4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC    | 06/2015          | 437.39 -                | 437.39           | 21.86                       | 06/2018 -             | 06/2018     | 0(O) -                                     | 0/4                         |
| 800   | FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC    | 06/2015          | 463.49 -                | 463.49           | 9.26                        | 06/2018 -             | 06/2018     | 0(O) -                                     | 0/4                         |
| 801   | FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC                         | 06/2016          | 829.00 -                | 829.00           | 59.85                       | 01/2019 -             | 01/2019     | 0(O) -                                     | 0/4                         |
| 802   | FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC                | 03/2015          | 168.39 -                | 168.39           | 16.84                       | 11/2018 -             | 11/2018     | 0(O) -                                     | 0/4                         |
| 803   | 4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC     | 10/2014          | 588.95 -                | 588.95           | 80.00                       | 11/2018 -             | 11/2018     | 0(O) -                                     | 0/4                         |
| 804   | 2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , EPC                     | 11/2010          | 268.08 -                | 268.08           | -                           | 05/2017 -             | 05/2017     | -                                          | 0/0                         |
| 805   | 2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , ITEM RATE   | 11/2010          | 470.20 -                | 470.20           | -                           | 02/2011 -             | 02/2011     | -                                          | 0/0                         |
| 806   | STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM , ITEM RATE | 05/2011          | 176.22 -                | 176.22           | -                           | 02/2018 -             | 02/2018     | 0(O) -                                     | 0/0                         |
| 807   | STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM , EPC        | 11/2014          | 218.31 -                | 218.31           | -                           | 02/2018 -             | 02/2018     | 0(O) -                                     | 0/0                         |
| 808   | 4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC         | 12/2015          | 225.02 -                | 159.20           | -                           | 12/2018 -             | 12/2018     | 0(O) -                                     | 0/4                         |



**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                           |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|-------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                   | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                         | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 809   | 4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC                     | 12/2015          | 223.30 -                | 223.30           | -                           | 06/2018 -             | 06/2018     | 0(O) -                                     | 0/0                         |
| 810   | 4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC                               | 01/1991          | 520.01 -                | 520.01           | -                           | -                     | -           | -                                          | 0/0                         |
| 811   | 4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC           | 12/2015          | 289.99 -                | 289.99           | -                           | 12/2018 -             | 12/2018     | 0(O) -                                     | 0/0                         |
| 812   | 4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC        | 01/2016          | 294.17 -                | 294.17           | -                           | 01/2016 -             | 01/2016     | -                                          | 0/4                         |
| 813   | 4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC        | 01/2016          | 252.00 -                | 252.00           | -                           | 01/2016 -             | 01/2016     | -                                          | 0/4                         |
| 814   | PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)                                                                                | 08/2010          | 671.30 -                | 671.30           | -                           | 02/2013 -             | 06/2018     | 64(O) -                                    | 0/0                         |
| 815   | 2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR , PPP (ANNUITY)                                                                        | 05/2011          | 351.54 -                | 351.54           | -                           | 05/2013 -             | 10/2017     | 53(O) -                                    | 0/0                         |
| 816   | 2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR , PPP (ANNUITY)                                                                 | 05/2011          | 664.00 -                | 664.00           | -                           | 02/2014 -             | -           | -                                          | 0/0                         |
| 817   | PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)                                                                | 09/2011          | 574.00 -                | 574.00           | -                           | 03/2014 -             | 09/2017     | 42(O) -                                    | 0/0                         |
| 818   | 2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR , G                                                                             | 10/2011          | 375.09 -                | 375.09           | -                           | 04/2014 -             | -           | -                                          | 0/0                         |
| 819   | 4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)                                                                       | 01/2011          | 575.00 -                | 575.00           | -                           | 07/2013 -             | 03/2018     | 56(O) -                                    | 0/0                         |
| 820   | 2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)                                                              | 05/2011          | 511.54 -                | 511.54           | -                           | 11/2013 -             | 12/2017     | 49(O) -                                    | 0/0                         |
| 821   | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , EPC       | 01/1991          | 675.00 -                | 675.00           | -                           | -                     | -           | -                                          | 0/0                         |
| 822   | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR , ITEM RATE | 01/1991          | 282.41 -                | 282.41           | 67.52                       | 08/2016 -             | 08/2016     | -                                          | 0/0                         |
| 823   | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR , ITEM RATE | 01/1991          | 358.22 -                | 358.22           | 188.71                      | 10/2016 -             | 10/2016     | -                                          | 0/0                         |
| 824   | FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR , G                                                                               | 08/2015          | 556.07 -                | 556.07           | -                           | -                     | -           | -                                          | 0/0                         |
| 825   | FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR , G                                                                   | 12/2015          | 1,041.10 -              | 1,041.10         | -                           | -                     | 04/2019     | -                                          | 0/0                         |
| 826   | FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR , G                                                                             | 08/2015          | 814.04 -                | 814.04           | -                           | -                     | -           | -                                          | 0/0                         |
| 827   | FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR , G                                                                           | 08/2015          | 322.09 -                | 322.09           | -                           | -                     | 04/2018     | -                                          | 0/0                         |
| 828   | FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR , G                                                                               | 01/1991          | 642.41 -                | 642.41           | -                           | -                     | -           | -                                          | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                   |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                           | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                 | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 829   | FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR , G                                                 | 12/2015          | 1,167.45 -              | 1,167.45         | -                           | -                     | -           | -                                          | 0/0                         |
| 830   | TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR , G                                                  | 08/2015          | 399.54 -                | 399.54           | -                           | -                     | 04/2019     | -                                          | 0/0                         |
| 831   | REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR , G                 | 01/1991          | 478.35 -                | 478.35           | -                           | -                     | -           | -                                          | 0/0                         |
| 832   | TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR , G                                                              | 08/2015          | 854.80 -                | 854.80           | -                           | -                     | 12/2017     | -                                          | 0/0                         |
| 833   | TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR , G                                                 | 08/2015          | 516.13 -                | 516.13           | -                           | -                     | 04/2018     | -                                          | 0/0                         |
| 834   | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , EPC  | 01/1991          | 154.62 -                | 154.62           | -                           | -                     | -           | -                                          | 0/0                         |
| 835   | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC  | 01/1991          | 319.68 -                | 319.68           | -                           | -                     | -           | -                                          | 0/0                         |
| 836   | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR , G | 10/2014          | 377.64 -                | 377.64           | -                           | 03/2014               | -           | -                                          | 0/0                         |
| 837   | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR , G | 10/2013          | 278.39 -                | 278.39           | -                           | 08/2014               | 08/2014     | -                                          | 0/0                         |
| 838   | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR , G | 01/2013          | 322.01 -                | 322.01           | -                           | 08/2014               | -           | -                                          | 0/0                         |
| 839   | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR , G | 11/2013          | 683.83 -                | 683.83           | -                           | 07/2016               | -           | -                                          | 0/0                         |
| 840   | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR , G  | 02/2014          | 665.50 -                | 665.50           | -                           | 07/2016               | -           | -                                          | 0/0                         |
| 841   | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR , G | 02/2016          | 178.85 -                | 178.85           | -                           | 05/2016               | -           | -                                          | 0/0                         |
| 842   | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR , G | 02/2016          | 369.77 -                | 369.77           | -                           | 06/2016               | 06/2016     | -                                          | 0/0                         |
| 843   | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR , G | 02/2016          | 553.30 -                | 553.30           | -                           | 05/2016               | -           | -                                          | 0/0                         |
| 844   | FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR , G   | 01/2014          | 1,408.85 -              | 1,408.85         | -                           | 10/2016               | -           | -                                          | 0/0                         |
| 845   | STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR , G | 03/2015          | 206.80 -                | 206.80           | -                           | 07/2016               | 10/2016     | -                                          | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                             |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|---------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                     | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                           | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 846   | CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR , G                            | 08/2015          | 288.24 -                | 288.24           | -                           | 11/2015 -             | -           | -                                          | 0/0                         |
| 847   | BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR , G                                                                | 05/2015          | 581.84 -                | 581.84           | -                           | 05/2017 -             | -           | -                                          | 0/0                         |
| 848   | REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR , G           | 08/2016          | 1,742.01 -              | 1,742.01         | -                           | 12/2016 -             | 12/2016     | -                                          | 0/0                         |
| 849   | TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR , G             | 03/2017          | 672.89 -                | 736.01           | -                           | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/0                         |
| 850   | CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR , G            | 03/2017          | 235.48 -                | 227.77           | -                           | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/0                         |
| 851   | REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH , EPC              | 10/2014          | 213.47 -                | 213.47           | -                           | 03/2015 -             | 03/2015     | -                                          | 0/0                         |
| 852   | REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 ( BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH , EPC            | 10/2014          | 298.34 -                | 298.34           | -                           | 03/2015 -             | 03/2015     | -                                          | 0/0                         |
| 853   | REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH , EPC     | 11/2014          | 262.54 -                | 262.54           | -                           | 03/2015 -             | 03/2015     | -                                          | 0/0                         |
| 854   | REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC            | 12/2015          | 291.05 -                | 291.05           | -                           | - -                   | -           | -                                          | 0/0                         |
| 855   | CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- [N24000283]PWD,CHHATISGARH , ITEM RATE | 12/2010          | 169.26 -                | 169.26           | -                           | 12/2012 -             | -           | -                                          | 0/0                         |
| 856   | REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH , EPC             | 12/2014          | 394.20 -                | 394.20           | -                           | - -                   | -           | -                                          | 0/0                         |
| 857   | REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , EPC      | 11/2015          | 485.44 -                | 485.44           | -                           | 12/2015 -             | -           | -                                          | 0/0                         |
| 858   | REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH , EPC   | 03/2015          | 422.34 -                | 422.34           | 22.25                       | - -                   | -           | -                                          | 0/0                         |
| 859   | FOUR LANING OF ORISSA/CHHATISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH , G                                                 | 02/2013          | 1,232.00 -              | 1,232.00         | -                           | 08/2015 -             | 12/2017     | 28(O) -                                    | 0/0                         |
| 860   | FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH , G                                                                           | 12/2015          | 596.67 -                | 596.67           | 67.84                       | - -                   | 05/2018     | -                                          | 0/0                         |
| 861   | FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH , G                                                                        | 12/2015          | 509.13 -                | 509.13           | 202.90                      | - -                   | 04/2018     | -                                          | 0/0                         |
| 862   | FOUR / SIX LANING OF RAIPUR - SIMGA ( PKG-1) - [N24000510]NHAI,CHHATISGARH , G                                                              | 12/2015          | 726.67 -                | 726.67           | -                           | - -                   | 04/2018     | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                     |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|-------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                             | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                   | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 863   | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-I), NEW - [N24000609]NHAI,DELHI , G                                     | 09/2015          | 771.18 -                | 771.18           | 512.31                      | - -                   | 03/2018     | - -                                        | 0/0                         |
| 864   | FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE - [N24000251]NHDP,GOA , EPC                        | 03/2015          | 297.00 -                | 297.00           | 38.33                       | - -                   | 04/2018     | - -                                        | 0/1                         |
| 865   | CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66 ) FROM KM. 26 /200 ( CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA , G     | 03/2015          | 298.33 -                | 298.33           | 16.10                       | - -                   | -           | -                                          | 0/4                         |
| 866   | CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA , EPC         | 03/2015          | 184.05 -                | 184.05           | 10.72                       | - -                   | -           | -                                          | 0/4                         |
| 867   | CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC   | 03/2015          | 280.16 -                | 280.16           | 16.06                       | - -                   | -           | -                                          | 0/4                         |
| 868   | CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC    | 10/2015          | 936.40 -                | 936.40           | -                           | - -                   | -           | -                                          | 0/0                         |
| 869   | WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC   | 12/2015          | 773.98 -                | 773.98           | -                           | - -                   | -           | -                                          | 0/0                         |
| 870   | WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA , EPC   | 12/2015          | 819.95 -                | 819.95           | -                           | - -                   | -           | -                                          | 0/0                         |
| 871   | GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT , PPP (BOT)                                          | 03/2010          | 1,509.10 -              | 3,237.87         | 3,187.19                    | 09/2012 -             | 12/2017     | 63(O) -                                    | 2/3                         |
| 872   | KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT , PPP (BOT)                                                                         | 01/2011          | 953.88 -                | 953.88           | 975.12                      | 07/2013 -             | -           | -                                          | 0/0                         |
| 873   | AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT , PPP (BOT)                                                                | 01/2013          | 2,125.24 -              | 2,125.24         | 4,659.71                    | 12/2015 -             | 07/2017     | -                                          | 0/3                         |
| 874   | VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT , G                                                                               | 03/2014          | 503.16 -                | 503.16           | 371.81                      | 08/2016 -             | -           | -                                          | 0/0                         |
| 875   | FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT , G | 05/2016          | 998.18 -                | 998.18           | -                           | - -                   | -           | -                                          | 0/0                         |
| 876   | FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT , G | 05/2016          | 834.64 -                | 834.64           | -                           | - -                   | -           | -                                          | 0/0                         |
| 877   | FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT , G | 05/2016          | 723.64 -                | 723.64           | -                           | - -                   | -           | -                                          | 0/0                         |
| 878   | FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT , G | 05/2016          | 763.08 -                | 763.08           | -                           | - -                   | -           | -                                          | 0/0                         |
| 879   | SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT , G | 05/2016          | 425.60 -                | 425.60           | -                           | - -                   | -           | -                                          | 0/0                         |
| 880   | CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT , G                                                               | 05/2016          | 364.56 -                | 364.56           | -                           | - -                   | -           | -                                          | 0/0                         |
| 881   | 4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT , G                       | 07/2016          | 829.97 -                | 829.97           | -                           | - -                   | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                    |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                            | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                  | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 882   | 2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT , G                                                | 12/2016          | 417.19 -                | 417.19           | -                           | -                     | -           | -                                          | 0/0                         |
| 883   | SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT , G      | 01/2017          | 1,251.11 -              | 1,251.11         | -                           | -                     | -           | -                                          | 0/0                         |
| 884   | 4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT , G                                        | 06/2017          | 1,958.88 -              | 1,958.88         | -                           | 06/2020 -             | 06/2020     | 0(O) -                                     | 0/0                         |
| 885   | DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)                                                              | 04/2007          | 486.00 -                | 486.00           | 481.12                      | 05/2010 -             | 08/2017     | -                                          | 0/0                         |
| 886   | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)                                                  | 05/2009          | 1,108.00 -              | 2,288.00         | 3,882.53                    | 11/2011 -             | 03/2018     | 76(O) -                                    | 0/0                         |
| 887   | ROHTAK-BAWAL - [N24000169]NHAI,HARYANA , PPP (BOT)                                                                                 | 05/2011          | 650.00 -                | 650.00           | 832.39                      | 11/2013 -             | 08/2017     | -                                          | 0/0                         |
| 888   | FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA , G                                          | 08/2015          | 723.54 -                | 723.54           | 558.12                      | 02/2018 -             | 02/2018     | 0(O) -                                     | 0/0                         |
| 889   | UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA( PKG - 2) - [N24000358]NHAI,HARYANA , G                                 | 10/2015          | 562.34 -                | 562.34           | 281.73                      | 04/2018 -             | 04/2018     | 0(O) -                                     | 0/0                         |
| 890   | 4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA , G                                                            | 12/2015          | 602.95 -                | 602.95           | 261.78                      | 06/2016 -             | 06/2018     | 24(O) -                                    | 0/0                         |
| 891   | 4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA , G                                                            | 01/2016          | 574.28 -                | 574.28           | 185.12                      | 07/2018 -             | 07/2018     | 0(O) -                                     | 0/0                         |
| 892   | 8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)                                                         | 07/2015          | 2,128.72 -              | 2,128.72         | 249.15                      | -                     | 04/2019     | -                                          | 0/0                         |
| 893   | FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA , PPP (BOT)                                                    | 07/2015          | 1,393.00 -              | 1,393.00         | 2,151.12                    | -                     | 01/2018     | -                                          | 0/0                         |
| 894   | FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA , G                                          | 11/2015          | 867.66 -                | 867.66           | 542.57                      | -                     | 05/2018     | -                                          | 0/0                         |
| 895   | UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA ( PKG - 1) - [N24000597]NHAI,HARYANA , G                                | 05/2015          | 600.85 -                | 600.85           | 234.36                      | -                     | 05/2018     | -                                          | 0/0                         |
| 896   | CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA , G                                                      | 08/2016          | 248.97 -                | 248.97           | -                           | -                     | 05/2019     | -                                          | 0/0                         |
| 897   | CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA , G | 09/2016          | 1,004.67 -              | 1,004.67         | -                           | -                     | 05/2019     | -                                          | 0/0                         |
| 898   | 4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA , G  | 03/2017          | 639.79 -                | 552.90           | -                           | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/0                         |
| 899   | FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)                   | 11/2013          | 1,916.79 -              | 1,916.79         | 1,851.95                    | 11/2016 -             | 02/2018     | 15(O) -                                    | 0/0                         |
| 900   | FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH , G                                                              | 09/2015          | 934.46 -                | 934.46           | 175.87                      | 03/2018 -             | 03/2018     | 0(O) -                                     | 0/0                         |
| 901   | 2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH , G                       | 02/2016          | 273.20 -                | 273.20           | 21.43                       | -                     | 02/2019     | -                                          | 0/0                         |
| 902   | TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH , G                           | 08/2016          | 1,583.18 -              | 1,583.18         | -                           | -                     | -           | -                                          | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                             |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|---------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                     | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                           | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 903   | FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH , G | 09/2016          | 1,273.71<br>-           | 1,273.71         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 904   | FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH , G                             | 10/2016          | 447.75<br>-             | 447.75           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 905   | 4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH , G                                                      | 06/2017          | 2,485.93<br>-           | 2,485.93         | -                           | 06/2020<br>-          | 06/2020     | 0(O)<br>-                                  | 0/0                         |
| 906   | QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)                                                | 07/2010          | 1,987.00<br>-           | 1,987.00         | -                           | 07/2015<br>-          | 03/2019     | 44(O)<br>-                                 | 0/0                         |
| 907   | NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)                                                                         | 05/2011          | 2,159.00<br>-           | 2,159.00         | -                           | 06/2015<br>-          | -           | -                                          | 0/0                         |
| 908   | JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)                                                      | 07/2010          | 1,813.76<br>-           | 1,813.76         | -                           | 07/2013<br>-          | 11/2017     | 52(O)<br>-                                 | 0/0                         |
| 909   | SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)                                                                     | 06/2011          | 1,100.70<br>-           | 1,100.70         | -                           | 06/2014<br>-          | 12/2017     | 42(O)<br>-                                 | 0/0                         |
| 910   | FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR , G                                                    | 12/2015          | 2,168.66<br>-           | 2,168.66         | -                           | 06/2019<br>-          | 06/2019     | 0(O)<br>-                                  | 0/0                         |
| 911   | FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR , G                                                   | 12/2015          | 2,136.97<br>-           | 2,136.97         | -                           | 12/2018<br>-          | 12/2018     | 0(O)<br>-                                  | 0/0                         |
| 912   | RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)                                                                         | 12/2012          | 1,479.00<br>-           | 1,479.00         | 833.65                      | 06/2015<br>-          | 12/2017     | 30(O)<br>-                                 | 0/0                         |
| 913   | TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]NHAI,JHARKHAND , G                                            | 09/2015          | 341.61<br>-             | 341.61           | 308.23                      | 09/2017<br>-          | 09/2017     | 0(O)<br>-                                  | 0/0                         |
| 914   | 4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND , G                                                        | 02/2016          | 997.15<br>-             | 997.15           | 196.95                      | -<br>-                | 03/2019     | -<br>-                                     | 0/0                         |
| 915   | TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND , G         | 07/2016          | 458.03<br>-             | 458.03           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 916   | FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND , G                                                                       | 08/2016          | 323.72<br>-             | 323.72           | 9.23                        | -<br>-                | 08/2018     | -<br>-                                     | 0/0                         |
| 917   | 4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND , G                                            | 03/2017          | 165.50<br>-             | 172.16           | -                           | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 918   | 4 LANING OF KUTCERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND , G                                   | 03/2017          | 239.68<br>-             | 235.90           | -                           | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 919   | HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA , G                                                           | 09/2010          | 946.00<br>-             | 946.00           | 818.53                      | -<br>-                | 12/2017     | -<br>-                                     | 3/3                         |
| 920   | STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , EPC     | 03/2015          | 165.67<br>-             | 165.67           | -                           | 11/2015<br>-          | 11/2017     | 24(O)<br>-                                 | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                          |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                  | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                        | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 921   | STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPUR - [N24000335]MORTH,KARNATAKA , EPC | 03/2015          | 159.12 -                | 159.12           | -                           | 11/2015 -             | 11/2017     | 24(O) -                                    | 0/0                         |
| 922   | TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 ( NEW NH NO -50) - [N24000342]NHAI,KARNATAKA , G      | 05/2015          | 709.00 -                | 709.00           | 203.50                      | 09/2017 -             | 09/2017     | 0(O) -                                     | 0/0                         |
| 923   | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC  | 01/1991          | 219.40 -                | 219.40           | -                           | 01/2018 -             | 01/2018     | 0(O) -                                     | 0/0                         |
| 924   | 4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)                                                | 05/2014          | 1,655.01 -              | 1,655.01         | 1,290.00                    | 08/2016 -             | 03/2018     | 19(O) -                                    | 0/0                         |
| 925   | FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)                                                              | 03/2015          | 1,388.00 -              | 1,388.00         | 498.00                      | - -                   | 08/2018     | - -                                        | 0/0                         |
| 926   | 4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA , G                                           | 03/2016          | 701.40 -                | 701.40           | -                           | - -                   | -           | -                                          | 0/0                         |
| 927   | 4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA , G                                             | 03/2016          | 870.00 -                | 870.00           | -                           | - -                   | -           | -                                          | 0/0                         |
| 928   | 4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA , G                                                                            | 05/2014          | 720.69 -                | 720.69           | 99.03                       | - -                   | -           | -                                          | 0/0                         |
| 929   | FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA , G                                 | 08/2016          | 1,664.20 -              | 1,664.20         | 7.25                        | - -                   | 04/2019     | - -                                        | 0/0                         |
| 930   | HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA , G                                                                       | 08/2016          | 1,167.42 -              | 1,167.42         | 24.65                       | - -                   | 03/2019     | - -                                        | 0/0                         |
| 931   | TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA , G     | 09/2016          | 950.69 -                | 950.69           | -                           | - -                   | -           | -                                          | 0/0                         |
| 932   | SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673]NHAI,KARNATAKA , G     | 03/2017          | 985.41 -                | 1,200.00         | -                           | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/0                         |
| 933   | SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA , G       | 03/2017          | 831.58 -                | 1,177.00         | -                           | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/0                         |
| 934   | SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA , G     | 03/2017          | 993.16 -                | 1,434.00         | -                           | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/0                         |
| 935   | SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)                                         | 02/2010          | 617.00 -                | 617.00           | 245.89                      | 08/2012 -             | 12/2017     | 64(O) -                                    | 0/0                         |
| 936   | CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC       | 01/2014          | 255.75 348.00           | 348.43           | .02                         | 09/2017 -             | 09/2017     | 0(O) -                                     | 0/0                         |
| 937   | CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA , EPC       | 01/2014          | 267.16 352.00           | 352.05           | .02                         | 11/2017 -             | 11/2017     | 0(O) -                                     | 0/0                         |



**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                        |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|----------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                      | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 938   | 4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA , G                                                      | 06/2015          | 845.24 -                | 845.24           | -                           | -                     | 11/2017     | -                                          | 0/0                         |
| 939   | 4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA , G      | 04/2016          | 804.97 -                | 804.97           | -                           | -                     | 06/2018     | -                                          | 0/0                         |
| 940   | INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)                                                                   | 10/2010          | 1,175.00 -              | 1,206.10         | 1,226.83                    | 04/2013 -             | 09/2017     | 53(O) -                                    | 0/0                         |
| 941   | INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)                                                                        | 11/2010          | 325.00 -                | 325.00           | 471.04                      | 05/2013 -             | 07/2017     | -                                          | 0/0                         |
| 942   | KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH , EPC                                 | 02/2015          | 377.83 -                | 377.83           | 57.42                       | 07/2017 -             | 07/2017     | -                                          | 0/0                         |
| 943   | SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)                                                    | 01/2012          | 320.48 -                | 320.48           | 189.49                      | 08/2015 -             | 09/2016     | -                                          | 0/0                         |
| 944   | BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC                  | 06/2015          | 390.51 -                | 390.51           | 43.25                       | -                     | -           | -                                          | 0/0                         |
| 945   | BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH , BOT (TOLL)                                                         | 11/2011          | 704.26 -                | 704.26           | -                           | 05/2015 -             | 05/2015     | -                                          | 0/0                         |
| 946   | BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH , BOT (TOLL)                                            | 03/2013          | 257.80 -                | 257.80           | 59.30                       | 02/2016 -             | 02/2016     | -                                          | 0/0                         |
| 947   | INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC               | 11/2013          | 497.05 -                | 497.05           | -                           | 05/2017 -             | 05/2017     | -                                          | 0/0                         |
| 948   | SHAH DOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH , EPC | 06/2015          | 532.49 -                | 532.49           | 137.08                      | 05/2017 -             | 05/2017     | -                                          | 0/0                         |
| 949   | BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)                                                    | 08/2015          | 257.80 -                | 257.00           | 12.38                       | -                     | -           | -                                          | 0/0                         |
| 950   | SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , BOT (TOLL)                                           | 11/2011          | 871.15 -                | 871.15           | 332.25                      | 09/2015 -             | 08/2016     | -                                          | 0/0                         |
| 951   | MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH , EPC                 | 06/2015          | 641.02 -                | 641.02           | 89.88                       | 12/2017 -             | 12/2017     | 0(O) -                                     | 0/0                         |
| 952   | MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , BOT (TOLL)                                         | 01/2012          | 381.86 -                | 381.86           | 252.03                      | 04/2015 -             | 04/2015     | -                                          | 0/0                         |
| 953   | BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH , BOT (TOLL)                                               | 11/2011          | 670.82 -                | 670.82           | 590.00                      | 02/2015 -             | 02/2015     | -                                          | 0/0                         |
| 954   | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH , G                                              | 03/2015          | 795.76 -                | 795.76           | 179.47                      | -                     | -           | -                                          | 0/0                         |
| 955   | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH , G                                               | 03/2015          | 794.30 -                | 794.30           | 111.83                      | -                     | -           | -                                          | 0/0                         |
| 956   | JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH , G         | 02/2015          | 327.32 -                | 327.32           | 142.73                      | 05/2017 -             | 05/2017     | -                                          | 0/0                         |
| 957   | JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC                  | 11/2015          | 628.45 -                | 628.45           | 20.74                       | 03/2018 -             | 03/2018     | 0(O) -                                     | 0/0                         |



**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                   |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|---------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                           | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                                 | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 958   | GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH , EPC                                         | 12/2015          | 927.54 -                | 927.54           | 29.17                       | 06/2018 -             | 06/2018     | 0(O) -                                     | 0/0                         |
| 959   | FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH , G                                                                          | 03/2015          | 928.83 -                | 928.83           | 1,254.37                    | - -                   | 12/2017     | - -                                        | 0/0                         |
| 960   | FOUR LANING OF GWALIOR-SHIPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)                                                                       | 05/2013          | 1,055.00 -              | 1,601.77         | 1,328.85                    | 11/2015 -             | 09/2017     | 22(O) -                                    | 0/0                         |
| 961   | FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH , G          | 06/2015          | 1,012.90 -              | 1,012.90         | 588.26                      | 03/2016 -             | 03/2019     | 36(O) -                                    | 0/0                         |
| 962   | FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH , PPP (BOT)                                                           | 01/2016          | 830.36 -                | 830.36           | 473.08                      | 07/2018 -             | 07/2018     | 0(O) -                                     | 0/0                         |
| 963   | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH , G                                                         | 03/2015          | 810.22 -                | 810.22           | 146.09                      | - -                   | -           | -                                          | 0/0                         |
| 964   | FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT) | 06/2015          | 1,583.79 -              | 1,583.79         | 560.20                      | - -                   | 01/2019     | - -                                        | 0/0                         |
| 965   | UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC                                     | 03/2015          | 511.83 -                | 511.83           | 40.87                       | 08/2017 -             | 08/2017     | -                                          | 0/0                         |
| 966   | BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH , G                                          | 08/2016          | 227.49 -                | 227.49           | 3.50                        | - -                   | 01/2019     | - -                                        | 0/0                         |
| 967   | TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA , PPP (BOT)                                                                                       | 11/2009          | 567.00 -                | 567.00           | 1,055.94                    | 11/2013 -             | -           | -                                          | 0/0                         |
| 968   | PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)                                                                                       | 10/2010          | 1,724.55 -              | 1,724.55         | 2,051.04                    | 03/2013 -             | 12/2017     | 57(O) -                                    | 0/0                         |
| 969   | PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA , G                                                                                                  | 12/2011          | 942.69 -                | 942.69           | 367.72                      | 06/2014 -             | 03/2018     | 45(O) -                                    | 0/0                         |
| 970   | WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)                                         | 05/2013          | 1,348.20 -              | 1,348.20         | 1,788.75                    | 02/2014 -             | 03/2018     | 49(O) -                                    | 2/2                         |
| 971   | REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA , G                                                  | 06/2014          | 260.39 -                | 260.39           | 87.43                       | 11/2016 -             | 11/2016     | -                                          | 0/2                         |
| 972   | CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC                  | 03/2015          | 168.30 -                | 168.30           | 13.43                       | - -                   | 10/2017     | - -                                        | 0/4                         |
| 973   | CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC            | 08/2014          | 187.79 -                | 187.79           | 57.60                       | 07/2016 -             | 07/2016     | -                                          | 0/12                        |
| 974   | REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC                                          | 01/2014          | 446.77 -                | 446.77           | 87.62                       | - -                   | 06/2017     | -                                          | 0/4                         |
| 975   | REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA , EPC                                         | 12/2013          | 220.72 -                | 220.72           | 95.02                       | 11/2016 -             | 11/2016     | -                                          | 0/4                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                 |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|-------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                         | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                               | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 976   | WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC        | 10/2015          | 289.60 -                | 289.60           | -                           | - -                   | -           | -                                          | 0/0                         |
| 977   | CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE | 12/2011          | 156.26 227.31           | 156.26           | 65.16                       | - 03/2013             | -           | -                                          | 0/0                         |
| 978   | CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA , ITEM RATE | 03/2011          | 185.82 292.22           | 185.82           | 205.97                      | - 11/2014             | 11/2014     | -                                          | 0/0                         |
| 979   | REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC       | 01/2015          | 225.81 -                | 225.81           | 6.50                        | - -                   | -           | -                                          | 0/0                         |
| 980   | 4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)                                                                | 07/2015          | 2,288.18 -              | 2,288.18         | -                           | - -                   | 05/2019     | -                                          | 0/0                         |
| 981   | CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270( D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 ( D - [N24000432]NHAI,MAHARASHTRA , G          | 09/2015          | 414.51 -                | 414.00           | 88.66                       | - -                   | 05/2018     | -                                          | 0/0                         |
| 982   | CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 ( - [N24000435]NHAI,MAHARASHTRA , G            | 10/2015          | 531.13 -                | 531.13           | -                           | - -                   | 05/2018     | -                                          | 0/0                         |
| 983   | 4 LANING OF FAGNE - MAH-GUJ BORDER ( PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC                                                                 | 07/2015          | 1,885.74 -              | 1,885.74         | -                           | - -                   | 05/2019     | -                                          | 0/0                         |
| 984   | CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 ( OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA , G                           | 10/2015          | 593.26 -                | 593.26           | -                           | - -                   | 05/2018     | -                                          | 0/0                         |
| 985   | CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA , G          | 12/2015          | 649.50 -                | 649.50           | 11.42                       | - -                   | 03/2019     | -                                          | 0/0                         |
| 986   | 6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA , G                             | 08/2015          | 505.00 -                | 505.00           | 38.08                       | - -                   | 05/2018     | -                                          | 0/0                         |
| 987   | 4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)                                                         | 01/2015          | 972.50 -                | 972.50           | 1,458.72                    | 07/2017 -             | 01/2018     | 6(O)                                       | 0/0                         |
| 988   | 4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)                                                   | 06/2014          | 923.04 -                | 923.04           | 474.52                      | 11/2016 -             | 11/2017     | 12(O)                                      | 0/0                         |
| 989   | NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA , G                                                                                             | 09/2005          | 168.00 -                | 168.00           | 279.92                      | 06/2006 -             | -           | -                                          | 0/0                         |
| 990   | FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)                                                                   | 07/2015          | 1,871.34 -              | 1,871.34         | 2,601.04                    | 01/2018 -             | 01/2018     | 0(O)                                       | 0/0                         |
| 991   | FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA , G                           | 04/2010          | 1,170.52 -              | 1,170.52         | -                           | 06/2012 -             | 03/2018     | 69(O)                                      | 0/0                         |
| 992   | REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA , G           | 01/2014          | 292.98 -                | 292.98           | 95.60                       | 11/2014 -             | 11/2014     | -                                          | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                        |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|----------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                      | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 993   | BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA , G           | 03/2016          | 197.69<br>-             | 197.69           | -                           | -<br>-                | 07/2018     | -<br>-                                     | 0/0                         |
| 994   | NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA , G                                                                           | 03/2016          | 546.00<br>-             | 546.00           | -                           | -<br>-                | 07/2019     | -<br>-                                     | 0/0                         |
| 995   | NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA , G                                                                           | 03/2016          | 591.66<br>-             | 591.66           | -                           | -<br>-                | 07/2019     | -<br>-                                     | 0/0                         |
| 996   | BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA , G            | 03/2016          | 244.00<br>-             | 244.00           | -                           | -<br>-                | 07/2018     | -<br>-                                     | 0/0                         |
| 997   | 4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA , G               | 03/2016          | 1,142.62<br>-           | 1,142.62         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 998   | 4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA , G               | 03/2016          | 1,101.58<br>-           | 1,101.58         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 999   | 4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA , G                                                 | 11/2016          | 1,071.61<br>-           | 1,071.61         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 1000  | 4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA , G                                                    | 11/2016          | 1,064.88<br>-           | 1,064.88         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 1001  | 4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA , G | 11/2016          | 400.25<br>-             | 400.25           | -                           | -<br>-                | 03/2019     | -<br>-                                     | 0/0                         |
| 1002  | 4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA , G | 11/2016          | 446.17<br>-             | 446.17           | -                           | -<br>-                | 03/2019     | -<br>-                                     | 0/0                         |
| 1003  | SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA , G | 11/2016          | 290.73<br>-             | 290.73           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 1004  | CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA , G | 01/2017          | 244.90<br>-             | 244.90           | -                           | -<br>-                | 05/2019     | -<br>-                                     | 0/0                         |
| 1005  | FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA , G                                                                | 02/2017          | 904.16<br>-             | 904.16           | -                           | 02/2020<br>-          | 02/2020     | 0(O)<br>-                                  | 0/0                         |
| 1006  | CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA , G | 03/2017          | 247.02<br>-             | 157.49           | -                           | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 1007  | 4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA , G                                             | 03/2017          | 744.64<br>-             | 982.00           | -                           | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 1008  | 4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA , G                                         | 03/2017          | 1,030.44<br>-           | 1,065.51         | -                           | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 1009  | 4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA , G                                          | 03/2017          | 988.34<br>-             | 1,043.28         | -                           | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 1010  | 4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA , G                                        | 03/2017          | 1,059.73<br>-           | 1,071.00         | -                           | 03/2017<br>-          | -           | -                                          | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                            |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|--------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                    | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                          | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1011  | DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA , G         | 03/2017          | 296.19 -                | 254.00           | -                           | 03/2020 -             | 05/2019     | -10(O) -                                   | 0/0                         |
| 1012  | 4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA , G                                            | 03/2017          | 1,098.06 -              | 1,160.64         | -                           | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/0                         |
| 1013  | JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA , PPP (ANNUITY)                                                                              | 01/2011          | 536.00 -                | 536.00           | 672.72                      | 01/2014 -             | 03/2018     | 50(O) -                                    | 0/0                         |
| 1014  | 2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA , ITEM RATE   | 12/2010          | 1,494.48 -              | 1,494.48         | -                           | 02/2011 -             | 02/2011     | -                                          | 0/0                         |
| 1015  | TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA , G                                       | 12/2015          | 479.20 -                | 479.20           | -                           | - -                   | 05/2018     | - -                                        | 0/0                         |
| 1016  | WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE   | 11/2010          | 624.41 -                | 624.41           | -                           | 03/2011 -             | -           | -                                          | 0/0                         |
| 1017  | CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE   | 08/2010          | 193.69 -                | 193.69           | -                           | 10/2010 -             | -           | -                                          | 0/0                         |
| 1018  | CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE                           | 08/2010          | 195.04 -                | 195.04           | 130.82                      | 10/2010 -             | 10/2010     | -                                          | 0/0                         |
| 1019  | GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)                                                                        | 12/2003          | 604.00 -                | 604.00           | 423.83                      | 12/2009 -             | -           | -                                          | 0/0                         |
| 1020  | SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)                                                        | 02/2009          | 1,693.75 -              | 1,693.75         | 2,675.28                    | 08/2011 -             | 09/2017     | 73(O) -                                    | 2/2                         |
| 1021  | 4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)                                                                     | 02/2011          | 2,498.76 -              | 2,498.76         | 2,489.54                    | 08/2014 -             | 12/2017     | 40(O) -                                    | 0/0                         |
| 1022  | VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)                                                          | 09/2011          | 2,848.00 -              | 2,848.00         | -                           | 03/2014 -             | 04/2018     | 49(O) -                                    | 0/0                         |
| 1023  | MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)                                                                           | 09/2011          | 754.00 -                | 754.00           | 1,101.13                    | 03/2013 -             | 11/2017     | 56(O) -                                    | 0/0                         |
| 1024  | DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)                                                              | 10/2012          | 1,928.22 -              | 1,928.22         | 2,488.00                    | 04/2015 -             | 12/2017     | 32(O) -                                    | 0/0                         |
| 1025  | WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE , EPC    | 03/2015          | 789.83 -                | 789.83           | 109.77                      | - -                   | -           | -                                          | 0/0                         |
| 1026  | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-III) - [N24000446]NHAI,MULTI STATE , G                                         | 09/2015          | 788.51 -                | 788.51           | 321.86                      | 03/2018 -             | 03/2018     | 0(O) -                                     | 0/0                         |
| 1027  | SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE , G     | 09/2016          | 1,244.10 -              | 1,244.10         | -                           | - -                   | -           | -                                          | 0/0                         |
| 1028  | WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE | 12/2010          | 1,296.00 -              | 1,296.00         | -                           | 02/2011 -             | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                       |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|---------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                               | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                     | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1029  | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND , G | 03/2016          | 373.07 -                | 373.07           | -                           | 08/2016 -             | 08/2019     | 36(O) -                                    | 0/0                         |
| 1030  | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND , G | 03/2016          | 396.52 -                | 396.52           | -                           | 08/2016 -             | 08/2019     | 36(O) -                                    | 0/0                         |
| 1031  | FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND , G | 03/2016          | 429.52 -                | 429.52           | -                           | 08/2016 -             | 08/2019     | 36(O) -                                    | 0/0                         |
| 1032  | CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND , G | 02/2017          | 507.68 -                | 507.68           | -                           | 04/2017 -             | -           | -                                          | 0/0                         |
| 1033  | PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)                                                                                 | 03/2012          | 1,410.00 -              | 1,410.00         | -                           | 09/2014 -             | -           | -                                          | 0/0                         |
| 1034  | SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)                                                    | 12/2011          | 1,047.00 -              | 1,047.00         | -                           | 06/2014 -             | 06/2017     | -                                          | 0/0                         |
| 1035  | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC  | 01/1991          | 218.63 251.92           | 218.63           | 29.27                       | 10/2017 -             | 10/2017     | 0(O) -                                     | 0/0                         |
| 1036  | IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA , EPC                                                                         | 12/2013          | 319.80 -                | 319.80           | -                           | 10/2016 -             | 10/2016     | -                                          | 0/0                         |
| 1037  | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA , G    | 01/1991          | 229.41 265.35           | 229.41           | 6.65                        | 05/2018 -             | 05/2018     | 0(O) -                                     | 0/0                         |
| 1038  | REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC    | 07/2014          | 342.05 -                | 342.05           | -                           | 01/2017 -             | 01/2017     | -                                          | 0/0                         |
| 1039  | 4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA , G                                                                        | 07/2015          | 1,282.94 -              | 1,282.94         | -                           | - -                   | -           | -                                          | 0/0                         |
| 1040  | FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA , G                                                                   | 12/2015          | 752.28 -                | 752.28           | -                           | - -                   | -           | -                                          | 0/0                         |
| 1041  | WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA , EPC        | 12/2011          | 159.39 -                | 159.39           | -                           | 11/2017 -             | 11/2017     | 0(O) -                                     | 0/0                         |
| 1042  | WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC    | 12/2011          | 191.08 -                | 191.08           | -                           | 08/2015 -             | 03/2018     | 31(O) -                                    | 0/0                         |
| 1043  | JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA , G                                                                  | 02/2016          | 1,069.65 -              | 1,069.65         | -                           | - -                   | -           | -                                          | 0/0                         |
| 1044  | DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA , G     | 09/2016          | 2,510.04 -              | 2,510.04         | -                           | - -                   | 08/2019     | -                                          | 0/0                         |
| 1045  | REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA , G     | 10/2016          | 1,008.96 -              | 1,008.96         | -                           | - -                   | -           | -                                          | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                    |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                            | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                  | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1046  | WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA , G | 03/2014          | 191.50<br>192.00        | 192.00           | -                           | 05/2016<br>-          | 06/2017     | -                                          | 0/0                         |
| 1047  | WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA , G | 01/2015          | 326.63<br>327.00        | 327.00           | -                           | 04/2018<br>-          | 04/2018     | 0(O)<br>-                                  | 0/0                         |
| 1048  | WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA , G    | 02/2015          | 239.91<br>240.00        | 240.00           | -                           | 10/2017<br>-          | 10/2017     | 0(O)<br>-                                  | 0/0                         |
| 1049  | WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA , G  | 03/2015          | 226.31<br>226.00        | 226.00           | -                           | 10/2017<br>-          | 10/2017     | 0(O)<br>-                                  | 0/0                         |
| 1050  | IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA , G  | 12/2013          | 319.80<br>320.00        | 320.00           | -                           | 05/2016<br>-          | 03/2017     | -                                          | 0/0                         |
| 1051  | REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA , G  | 07/2014          | 342.05<br>342.00        | 342.00           | -                           | 01/2017<br>-          | 08/2017     | -                                          | 0/0                         |
| 1052  | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA , G | 08/2013          | 171.96<br>172.00        | 172.00           | -                           | 06/2016<br>-          | 03/2017     | -                                          | 0/0                         |
| 1053  | WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA , G | 06/2016          | 157.30<br>157.00        | 157.00           | -                           | 06/2018<br>-          | 11/2018     | 5(O)<br>-                                  | 0/0                         |
| 1054  | WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA , G | 03/2014          | 162.51<br>163.00        | 163.00           | -                           | 05/2016<br>-          | 03/2017     | -                                          | 0/0                         |
| 1055  | REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA , G   | 03/2017          | 1,288.07<br>-           | 1,420.00         | -                           | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 1056  | REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB , EPC | 03/2015          | 435.90<br>-             | 435.90           | 31.02                       | -<br>-                | -           | -                                          | 0/0                         |
| 1057  | WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB , EPC | 01/2015          | 279.68<br>-             | 279.68           | 25.28                       | -<br>-                | -           | -                                          | 0/0                         |
| 1058  | 4-LANING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB , EPC   | 11/2014          | 463.65<br>546.00        | 463.65           | 280.16                      | -<br>-                | -           | -                                          | 0/0                         |
| 1059  | 4 LANING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB , EPC   | 11/2014          | 573.96<br>605.00        | 605.00           | 209.74                      | -<br>-                | -           | -                                          | 0/0                         |
| 1060  | JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB , G                                                                                  | 01/2014          | 523.85<br>-             | 523.85           | 248.85                      | 01/2016<br>-          | 12/2017     | 23(O)<br>-                                 | 0/0                         |
| 1061  | 4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB , EPC  | 02/2015          | 483.38<br>-             | 483.38           | 65.76                       | -<br>-                | -           | -                                          | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                    |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                            | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                  | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1062  | 4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB , EPC  | 02/2015          | 616.36<br>-             | 616.36           | 68.58                       | -<br>-                | -           | -                                          | 0/0                         |
| 1063  | 4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64( - [N24000374]PWD,PUNJAB , EPC | 02/2015          | 486.74<br>-             | 486.74           | 189.39                      | -<br>-                | -           | -                                          | 0/0                         |
| 1064  | CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15( - [N24000383]PWD,PUNJAB , EPC | 03/2015          | 312.79<br>-             | 312.79           | 17.57                       | -<br>-                | -           | -                                          | 0/0                         |
| 1065  | CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOUA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB , EPC  | 07/2014          | 319.80<br>-             | 319.80           | 102.55                      | -<br>-                | -           | -                                          | 0/0                         |
| 1066  | DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC | 12/2015          | 766.36<br>-             | 766.36           | 99.86                       | -<br>-                | -           | -                                          | 0/0                         |
| 1067  | 4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC                                  | 11/2015          | 847.02<br>-             | 847.02           | 299.81                      | -<br>-                | -           | -                                          | 0/0                         |
| 1068  | 4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC                                 | 11/2015          | 889.24<br>-             | 889.24           | 389.64                      | -<br>-                | -           | -                                          | 0/0                         |
| 1069  | DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB , EPC  | 12/2015          | 578.38<br>-             | 578.38           | 128.53                      | -<br>-                | -           | -                                          | 0/0                         |
| 1070  | IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB , G      | 09/2015          | 273.06<br>-             | 273.06           | 41.24                       | -<br>-                | 11/2017     | -<br>-                                     | 0/0                         |
| 1071  | FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB , G                                                           | 09/2014          | 479.00<br>-             | 479.00           | 401.66                      | -<br>-                | 12/2017     | -<br>-                                     | 0/0                         |
| 1072  | FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB , G                                                       | 12/2015          | 239.23<br>-             | 239.23           | 161.60                      | 12/2017<br>-          | 12/2017     | 0(O)<br>-                                  | 0/0                         |
| 1073  | FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB , G                                                                    | 10/2015          | 447.29<br>-             | 447.29           | 48.82                       | 12/2017<br>-          | 04/2019     | 16(O)<br>-                                 | 0/0                         |
| 1074  | WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , EPC | 06/2015          | 892.17<br>-             | 892.17           | 26.92                       | -<br>-                | -           | -                                          | 0/0                         |
| 1075  | WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB , EPC | 06/2015          | 899.21<br>-             | 899.21           | 25.08                       | -<br>-                | -           | -                                          | 0/0                         |
| 1076  | 4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB , G    | 08/2016          | 1,388.34<br>-           | 1,388.34         | -                           | -<br>-                | 09/2019     | -<br>-                                     | 0/0                         |
| 1077  | 4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB , G                                                                    | 08/2016          | 1,169.61<br>-           | 1,169.61         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 1078  | CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB , G   | 03/2017          | 754.54<br>-             | 756.27           | -                           | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |



**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                 |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|-------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                         | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                               | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1079  | CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN , G                                                                                   | 12/2003          | 275.00 -                | 281.31           | -                           | 02/2010 -             | -           | -                                          | 0/0                         |
| 1080  | DEOLI KOTA - [N24000148]NHAI, RAJASTHAN , PPP (BOT)                                                                                             | 01/2011          | 593.00 -                | 593.00           | -                           | 07/2013 -             | 10/2017     | 51(O) -                                    | 0/0                         |
| 1081  | 2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI, RAJASTHAN , G                                                                      | 03/2014          | 240.10 -                | 240.10           | -                           | 03/2016 -             | -           | -                                          | 0/0                         |
| 1082  | WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH, RAJASTHAN , EPC        | 10/2014          | 269.22 -                | 269.22           | 33.24                       | 01/2015 -             | -           | -                                          | 0/0                         |
| 1083  | WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH, RAJASTHAN , EPC                         | 10/2014          | 257.09 -                | 257.09           | 14.80                       | 01/2015 -             | -           | -                                          | 0/0                         |
| 1084  | REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH, RAJASTHAN , EPC                                         | 10/2013          | 278.87 -                | 278.87           | -                           | 05/2014 -             | -           | -                                          | 0/0                         |
| 1085  | REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH, RAJASTHAN , ITEM RATE | 01/1991          | 376.52 -                | 376.52           | -                           | 04/2014 -             | -           | -                                          | 0/0                         |
| 1086  | WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH, RAJASTHAN , EPC        | 02/2015          | 383.40 -                | 383.40           | 224.68                      | 03/2015 -             | -           | -                                          | 0/0                         |
| 1087  | WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH, RAJASTHAN , EPC         | 12/2015          | 621.43 -                | 621.43           | -                           | 06/2018 -             | 06/2018     | 0(O) -                                     | 0/0                         |
| 1088  | TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER ( UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI, RAJASTHAN , G           | 08/2015          | 538.08 -                | 538.08           | -                           | 02/2018 -             | 02/2018     | 0(O) -                                     | 0/0                         |
| 1089  | TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI, RAJASTHAN , G                                                            | 09/2014          | 425.19 -                | 425.19           | -                           | 09/2016 -             | 09/2017     | 12(O) -                                    | 0/0                         |
| 1090  | JAISALMER - BARMER - [N24000348]NHAI, RAJASTHAN , G                                                                                             | 08/2015          | 482.27 -                | 482.27           | -                           | 02/2018 -             | 02/2018     | 0(O) -                                     | 0/0                         |
| 1091  | TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 ( NEW NH NO -50) - [N24000352]NHAI, RAJASTHAN , G                          | 07/2015          | 455.60 -                | 455.60           | -                           | 07/2017 -             | 07/2017     | -                                          | 0/0                         |
| 1092  | PADI - DAHOD - [N24000353]NHAI, RAJASTHAN , G                                                                                                   | 11/2014          | 279.14 -                | 279.14           | -                           | 05/2017 -             | -           | -                                          | 0/0                         |
| 1093  | JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI, RAJASTHAN , G                                                                         | 10/2014          | 264.72 -                | 264.72           | -                           | 04/2017 -             | -           | -                                          | 0/0                         |
| 1094  | PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI, RAJASTHAN , G                                                   | 09/2015          | 567.51 -                | 567.51           | -                           | 03/2018 -             | 03/2018     | 0(O) -                                     | 0/0                         |
| 1095  | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH, RAJASTHAN , G          | 01/1991          | 269.26 -                | 269.26           | 212.72                      | 10/2016 -             | 10/2016     | -                                          | 0/0                         |
| 1096  | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAUJI - [N24000406]MORTH, RAJASTHAN , ITEM RATE   | 01/1991          | 208.87 223.00           | 208.87           | 206.78                      | 05/2016 -             | 05/2016     | -                                          | 0/0                         |



**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                               |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                       | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                             | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1097  | 2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN , G                                                                       | 10/2015          | 597.00 -                | 597.00           | -                           | 10/2017 -             | 04/2018     | 6(O) -                                     | 0/0                         |
| 1098  | 2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI, RAJASTHAN , PPP (BOT) | 11/2012          | 530.07 -                | 530.07           | -                           | 08/2016 -             | -           | -                                          | 0/0                         |
| 1099  | BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN , PPP (BOT)  | 08/2014          | 822.90 -                | 822.90           | -                           | 04/2018 -             | 04/2018     | 0(O) -                                     | 0/0                         |
| 1100  | NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD, RAJASTHAN , BOT (TOLL) | 09/2012          | 511.00 -                | 511.00           | -                           | 10/2013 -             | 10/2013     | -                                          | 0/0                         |
| 1101  | NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD, RAJASTHAN , BOT (TOLL)           | 09/2012          | 511.00 -                | 511.00           | -                           | 10/2013 -             | 10/2013     | -                                          | 0/0                         |
| 1102  | GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN , PPP (BOT)                                                               | 02/2008          | 1,673.70 -              | 1,673.70         | 3,145.92                    | 10/2011 -             | 12/2017     | 74(O) -                                    | 0/0                         |
| 1103  | TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI, RAJASTHAN , G                                             | 08/2015          | 275.90 -                | 275.90           | -                           | - -                   | 02/2018     | - -                                        | 0/0                         |
| 1104  | TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI, RAJASTHAN , PPP (BOT)                                                    | 06/2016          | 637.18 -                | 637.18           | -                           | 06/2019 -             | 06/2019     | 0(O) -                                     | 0/0                         |
| 1105  | FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI, RAJASTHAN , PPP (BOT)   | 06/2016          | 763.23 -                | 763.23           | -                           | 06/2019 -             | 06/2019     | 0(O) -                                     | 0/0                         |
| 1106  | FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN , G                                | 06/2016          | 649.00 -                | 649.00           | -                           | 06/2019 -             | 06/2019     | 0(O) -                                     | 0/0                         |
| 1107  | 4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN , G                                                   | 07/2016          | 688.70 -                | 688.70           | -                           | - -                   | -           | -                                          | 0/0                         |
| 1108  | TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN , G          | 07/2016          | 331.46 -                | 331.46           | -                           | - -                   | 10/2018     | - -                                        | 0/0                         |
| 1109  | 2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI, RAJASTHAN , G                                                                | 08/2016          | 320.30 -                | 320.30           | -                           | - -                   | 01/2019     | - -                                        | 0/0                         |
| 1110  | SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 ( - [N24000621]NHAI, RAJASTHAN , G         | 09/2016          | 1,239.82 -              | 1,239.82         | -                           | - -                   | -           | -                                          | 0/0                         |
| 1111  | SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI, RAJASTHAN , G         | 09/2016          | 1,100.19 -              | 1,100.19         | -                           | - -                   | -           | -                                          | 0/0                         |
| 1112  | 6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI, RAJASTHAN , G         | 12/2016          | 1,031.95 -              | 1,031.95         | -                           | - -                   | -           | -                                          | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                          |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                  | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                        | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1113  | SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN , G                                                 | 04/2017          | 894.00<br>-             | 894.00           | -                           | 04/2020<br>-          | 04/2020     | 0(O)<br>-                                  | 0/0                         |
| 1114  | CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM , G                                              | 04/2013          | 151.59<br>-             | 151.59           | -                           | 08/2013<br>-          | -           | -                                          | 0/0                         |
| 1115  | CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE                                   | 04/2013          | 166.27<br>-             | 166.27           | -                           | 08/2013<br>-          | -           | -                                          | 0/0                         |
| 1116  | CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE                                      | 01/2013          | 182.28<br>-             | 182.00           | 24.36                       | 02/2013<br>-          | -           | -                                          | 0/0                         |
| 1117  | RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects                                                 | 04/2017          | 388.00<br>-             | 447.37           | -                           | 10/2017<br>-          | 10/2017     | 0(O)<br>-                                  | 0/0                         |
| 1118  | CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU , PPP (BOT)                                          | 09/2010          | 852.00<br>-             | 852.00           | 911.86                      | 03/2013<br>-          | 06/2017     | -                                          | 0/0                         |
| 1119  | SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)                        | 09/2011          | 1,250.00<br>-           | 1,250.00         | 1,329.10                    | 12/2013<br>-          | 12/2017     | 48(O)<br>-                                 | 0/0                         |
| 1120  | DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU , G                          | 06/2011          | 600.00<br>-             | 600.00           | 319.76                      | 06/2013<br>-          | -           | -                                          | 0/0                         |
| 1121  | TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)                                          | 05/2010          | 374.00<br>-             | 374.00           | 237.00                      | 05/2013<br>-          | 12/2017     | 55(O)<br>-                                 | 0/0                         |
| 1122  | 2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)                                              | 09/2011          | 485.00<br>-             | 485.00           | 406.68                      | 08/2013<br>-          | 12/2017     | 52(O)<br>-                                 | 0/0                         |
| 1123  | 2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)                                 | 04/2012          | 624.00<br>-             | 624.00           | 350.79                      | 04/2014<br>-          | -           | -                                          | 0/0                         |
| 1124  | CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC | 03/2015          | 258.97<br>268.92        | 268.92           | -                           | 08/2015<br>-          | -           | -                                          | 0/0                         |
| 1125  | REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC | 03/2015          | 157.18<br>162.00        | 162.00           | -                           | 07/2015<br>-          | -           | -                                          | 0/0                         |
| 1126  | CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU , EPC   | 11/2015          | 154.14<br>-             | 154.14           | -                           | 08/2015<br>-          | 08/2015     | -                                          | 0/0                         |
| 1127  | FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU , G         | 05/2015          | 1,387.11<br>-           | 1,387.11         | 658.16                      | 11/2017<br>-          | 11/2017     | 0(O)<br>-                                  | 0/0                         |
| 1128  | TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU , G                                                          | 06/2015          | 563.92<br>-             | 563.92           | 95.89                       | 12/2017<br>-          | 06/2018     | 6(O)<br>-                                  | 0/0                         |
| 1129  | THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU , G                                                                        | 07/2014          | 401.11<br>-             | 401.11           | 273.89                      | 01/2017<br>-          | -           | -                                          | 0/0                         |
| 1130  | THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU , G                                                                | 11/2014          | 563.92<br>-             | 563.92           | 186.50                      | 11/2016<br>-          | 06/2018     | 19(O)<br>-                                 | 0/0                         |
| 1131  | TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)                                                                                  | 03/2007          | 516.00<br>-             | 516.00           | 761.19                      | 07/2008<br>-          | -           | -                                          | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                             |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|-------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                                     | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                                           | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1132  | FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU , G                       | 02/2016          | 707.82<br>-             | 707.82           | 129.75                      | -<br>-                | 08/2018     | -<br>-                                     | 0/0                         |
| 1133  | FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU , G                       | 02/2016          | 641.17<br>-             | 641.17           | 47.95                       | -<br>-                | 07/2018     | -<br>-                                     | 0/0                         |
| 1134  | FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU , G                       | 03/2017          | 848.45<br>-             | 848.45           | -                           | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 1135  | FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects | 03/2016          | 641.17<br>-             | 641.17           | 64.90                       | 07/2016<br>-          | 07/2018     | 24(O)<br>-                                 | 0/0                         |
| 1136  | 4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)                                                               | 04/2014          | 1,266.60<br>-           | 1,266.60         | 1,360.00                    | 09/2016<br>-          | 03/2018     | 18(O)<br>-                                 | 0/0                         |
| 1137  | REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA , EPC                        | 12/2013          | 177.18<br>-             | 177.18           | 40.51                       | 03/2016<br>-          | -           | -                                          | 3/4                         |
| 1138  | REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]PWD,TELANGANA , EPC                      | 12/2013          | 158.65<br>-             | 158.65           | 103.50                      | 03/2016<br>-          | -           | -                                          | 3/4                         |
| 1139  | YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA , EPC                          | 12/2013          | 244.08<br>-             | 244.08           | 38.32                       | 03/2016<br>-          | -           | -                                          | 1/4                         |
| 1140  | REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA , EPC                        | 01/2014          | 340.00<br>-             | 340.00           | -                           | 03/2016<br>-          | -           | -                                          | 0/2                         |
| 1141  | REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC                       | 01/2014          | 270.00<br>-             | 270.00           | 19.84                       | 03/2016<br>-          | -           | -                                          | 1/4                         |
| 1142  | REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA , EPC                       | 10/2014          | 244.30<br>-             | 156.09           | -                           | 12/2016<br>-          | 12/2016     | -                                          | 0/4                         |
| 1143  | REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA , EPC                        | 10/2014          | 295.47<br>-             | 313.27           | -                           | 02/2017<br>-          | 02/2017     | -                                          | 0/1                         |
| 1144  | EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , EPC                       | 03/2015          | 153.21<br>-             | 153.21           | -                           | 01/2017<br>-          | 01/2017     | -                                          | 0/0                         |
| 1145  | CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA , G                         | 03/2011          | 218.31<br>-             | 339.82           | 208.28                      | 12/2015<br>-          | -           | -                                          | 0/3                         |
| 1146  | FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA , G                                                                                           | 12/2015          | 1,423.96<br>-           | 1,423.96         | 454.64                      | -<br>-                | 11/2018     | -<br>-                                     | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                  |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|--------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                          | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                                | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1147  | 2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL, TRIPURA , EPC          | 10/2014          | 369.00<br>-             | 369.00           | 36.90                       | 03/2018<br>-          | 03/2018     | 0(O)<br>-                                  | 0/4                         |
| 1148  | IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL, TRIPURA , EPC           | 05/2014          | 497.89<br>-             | 497.89           | 70.47                       | 04/2017<br>-          | 04/2017     | -                                          | 0/4                         |
| 1149  | MURADABAD-BAREILY - [N24000154]NHAI, UTTAR PRADESH , PPP (BOT)                                                                                   | 04/2010          | 1,267.00<br>-           | 1,267.00         | 2,664.02                    | 06/2013<br>-          | 09/2017     | 51(O)<br>-                                 | 0/0                         |
| 1150  | GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH , PPP (BOT)                                                                             | 02/2011          | 1,141.00<br>-           | 1,141.00         | 1,948.72                    | 08/2013<br>-          | 08/2017     | -                                          | 0/0                         |
| 1151  | BAREILY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH , PPP (BOT)                                                                             | 03/2011          | 1,046.00<br>-           | 1,046.00         | 577.00                      | 09/2013<br>-          | 10/2017     | 49(O)<br>-                                 | 0/0                         |
| 1152  | 2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH , PPP (BOT)                                                            | 07/2012          | 291.36<br>-             | 291.36           | 320.46                      | 01/2014<br>-          | 12/2017     | 47(O)<br>-                                 | 0/0                         |
| 1153  | ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH , PPP (BOT)                                                                                      | 03/2013          | 1,573.00<br>-           | 1,573.00         | 1,850.00                    | 09/2015<br>-          | 10/2017     | 25(O)<br>-                                 | 0/0                         |
| 1154  | CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH, UTTAR PRADESH , EPC        | 03/2015          | 629.74<br>-             | 629.74           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 1155  | CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH, UTTAR PRADESH , EPC                        | 01/2014          | 282.41<br>-             | 282.41           | -                           | 03/2016<br>-          | 03/2016     | -                                          | 0/0                         |
| 1156  | STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH, UTTAR PRADESH , EPC              | 10/2014          | 227.74<br>-             | 227.74           | -                           | 10/2016<br>-          | 10/2016     | -                                          | 0/0                         |
| 1157  | FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH , G                                                                              | 05/2015          | 261.09<br>-             | 261.09           | 58.72                       | 05/2017<br>-          | 06/2018     | 13(O)<br>-                                 | 0/0                         |
| 1158  | 2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH , G                                        | 04/2014          | 351.34<br>-             | 351.34           | 378.36                      | 01/2016<br>-          | 11/2017     | 22(O)<br>-                                 | 0/0                         |
| 1159  | 2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH , G                                       | 09/2015          | 368.73<br>-             | 368.73           | 203.84                      | 09/2016<br>-          | 09/2017     | 12(O)<br>-                                 | 0/0                         |
| 1160  | 2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI, UTTAR PRADESH , G                                                                  | 06/2014          | 301.04<br>-             | 301.04           | 146.23                      | 01/2016<br>-          | -           | -                                          | 0/0                         |
| 1161  | 2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI, UTTAR PRADESH , G                                                          | 04/2014          | 495.78<br>-             | 495.78           | 509.65                      | 01/2016<br>-          | 11/2017     | 22(O)<br>-                                 | 0/0                         |
| 1162  | RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP, UTTAR PRADESH , EPC                         | 10/2013          | 445.89<br>-             | 445.89           | -                           | 03/2017<br>-          | 03/2017     | -                                          | 0/0                         |
| 1163  | 2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD, UTTAR PRADESH , ITEM RATE | 11/2010          | 305.49<br>-             | 305.49           | -                           | 03/2017<br>-          | 03/2017     | -                                          | 0/0                         |
| 1164  | BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP, UTTAR PRADESH , EPC                                   | 01/2014          | 397.04<br>-             | 397.04           | -                           | 10/2016<br>-          | 10/2016     | -                                          | 0/0                         |
| 1165  | ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP, UTTAR PRADESH , EPC                                               | 06/2015          | 774.57<br>-             | 774.57           | -                           | 03/2018<br>-          | 03/2018     | 0(O)<br>-                                  | 0/0                         |

# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                   |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|-----------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                           | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                 | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1166  | BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH , EPC | 10/2013          | 317.76<br>-             | 317.76           | 15.47                       | 03/2017<br>-          | 03/2017     | -                                          | 0/0                         |
| 1167  | JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH , EPC | 10/2013          | 283.45<br>-             | 283.45           | -                           | 10/2016<br>-          | 10/2016     | -                                          | 0/0                         |
| 1168  | SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH , EPC                      | 10/2013          | 493.94<br>-             | 493.94           | -                           | 03/2017<br>-          | 03/2017     | -                                          | 0/0                         |
| 1169  | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-VI) - [N24000433]NHAI,UTTAR PRADESH , G                               | 09/2015          | 768.56<br>-             | 768.56           | 512.89                      | 03/2018<br>-          | 03/2018     | 0(O)<br>-                                  | 0/0                         |
| 1170  | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-V) - [N24000436]NHAI,UTTAR PRADESH , G                                | 09/2015          | 664.53<br>-             | 664.53           | 390.38                      | 03/2018<br>-          | 03/2018     | 0(O)<br>-                                  | 0/0                         |
| 1171  | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-IV) - [N24000440]NHAI,UTTAR PRADESH , G                               | 09/2015          | 789.31<br>-             | 789.31           | 603.92                      | 03/2018<br>-          | 03/2018     | 0(O)<br>-                                  | 0/0                         |
| 1172  | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-II) - [N24000450]NHAI,UTTAR PRADESH , G                               | 09/2015          | 785.78<br>-             | 785.78           | 587.77                      | 03/2018<br>-          | 03/2018     | 0(O)<br>-                                  | 0/0                         |
| 1173  | 6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)                                                      | 07/2015          | 1,657.20<br>-           | 1,657.20         | 225.00                      | -<br>-                | 01/2019     | -<br>-                                     | 0/0                         |
| 1174  | 4-LANING OF GHAGHRA BRIDGE TO VARANSI ( PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH , G                                           | 12/2015          | 611.65<br>-             | 611.65           | 225.07                      | 06/2016<br>-          | 06/2018     | 24(O)<br>-                                 | 0/0                         |
| 1175  | FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH , G                                                 | 01/2016          | 815.28<br>-             | 815.28           | 90.98                       | 06/2018<br>-          | 06/2018     | 0(O)<br>-                                  | 0/0                         |
| 1176  | FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH , G                                                  | 01/2016          | 1,027.53<br>-           | 1,027.53         | 152.94                      | 06/2018<br>-          | 06/2018     | 0(O)<br>-                                  | 0/0                         |
| 1177  | FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH , G                                           | 06/2016          | 667.00<br>-             | 667.00           | 113.68                      | 07/2018<br>-          | 06/2018     | -1(O)<br>-                                 | 0/0                         |
| 1178  | FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH , G                                            | 12/2015          | 667.00<br>-             | 667.00           | 164.32                      | 06/2018<br>-          | 06/2018     | 0(O)<br>-                                  | 0/0                         |
| 1179  | WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC                         | 05/2013          | 164.54<br>-             | 164.54           | -                           | 08/2015<br>-          | 08/2015     | -                                          | 0/0                         |
| 1180  | WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH , EPC                    | 12/2014          | 207.88<br>-             | 207.88           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 1181  | WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH , EPC                   | 12/2014          | 207.88<br>-             | 207.88           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 1182  | MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH , G                                                                           | 01/2016          | 683.24<br>-             | 683.24           | .45                         | -<br>-                | -           | -                                          | 0/0                         |
| 1183  | DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH , G                                                | 01/2016          | 701.12<br>-             | 701.12           | -                           | -<br>-                | 05/2019     | -<br>-                                     | 0/0                         |
| 1184  | DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH , G                         | 01/2016          | 1,081.57<br>-           | 1,081.57         | -                           | -<br>-                | 06/2019     | -<br>-                                     | 0/0                         |
| 1185  | ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH , G                               | 03/2016          | 676.73<br>-             | 676.73           | 71.78                       | -<br>-                | 04/2019     | -<br>-                                     | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                           |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|-------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                   | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                         | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1186  | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH , G      | 03/2016          | 1,404.50<br>-           | 1,404.50         | 2.22                        | -<br>-                | -           | -                                          | 0/0                         |
| 1187  | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH , G | 03/2016          | 1,396.74<br>-           | 1,396.74         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 1188  | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH , G                  | 03/2016          | 1,587.49<br>-           | 1,587.49         | -                           | -<br>-                | 04/2019     | -<br>-                                     | 0/0                         |
| 1189  | FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH , G  | 03/2016          | 899.00<br>-             | 899.00           | -                           | -<br>-                | 04/2019     | -<br>-                                     | 0/0                         |
| 1190  | 4-LANNING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH , G   | 03/2016          | 1,668.00<br>-           | 1,668.00         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 1191  | 4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH , G         | 03/2016          | 1,408.00<br>-           | 1,408.00         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 1192  | 4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH , G                              | 03/2016          | 1,737.00<br>-           | 1,737.00         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 1193  | 4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH , G                                        | 08/2016          | 2,016.00<br>-           | 2,016.00         | -                           | -<br>-                | 04/2019     | -<br>-                                     | 0/0                         |
| 1194  | CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH , G  | 12/2016          | 534.55<br>-             | 534.55           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 1195  | CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH , G   | 01/2017          | 450.68<br>-             | 450.68           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 1196  | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH , G   | 03/2017          | 1,373.28<br>-           | 1,373.28         | -                           | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 1197  | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH , G  | 03/2017          | 1,184.71<br>-           | 1,310.00         | -                           | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 1198  | DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH , G  | 03/2017          | 1,989.00<br>-           | 1,989.00         | -                           | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 1199  | 6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH , G  | 03/2017          | 2,064.99<br>-           | 2,447.00         | -                           | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/0                         |
| 1200  | HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND , G                                                                    | 11/2011          | 478.51<br>-             | 478.00           | 409.17                      | 10/2013<br>-          | 12/2017     | 50(O)<br>-                                 | 0/0                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                            |                  |                          |                    |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------|--------------------------|--------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                                    | Date of Approval | Original / Revised Cost  | Anticipated Cost   | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                                          | 3                | 4                        | 5                  | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1201  | FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND , G                      | 03/2016          | 720.00<br>-              | 720.00             | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 1202  | 4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND , G                      | 03/2016          | 1,443.00<br>-            | 1,443.00           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 1203  | 4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND , G                                                         | 11/2012          | 605.84<br>-              | 605.84             | 547.57                      | -<br>-                | 07/2018     | -<br>-                                     | 0/0                         |
| 1204  | 4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)                                                                                      | 02/2011          | 1,078.84<br>-            | 1,078.84           | 2,391.07                    | 08/2013<br>-          | 12/2017     | 52(O)<br>-                                 | 0/0                         |
| 1205  | 4-LANING OF BRAHAMPPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)                                                                                  | 02/2011          | 998.79<br>-              | 998.79             | 1,930.50                    | 08/2013<br>-          | 03/2018     | 55(O)<br>-                                 | 0/0                         |
| 1206  | 6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)                                                                          | 04/2012          | 1,396.18<br>-            | 1,396.18           | 2,694.55                    | 09/2014<br>-          | 12/2017     | 39(O)<br>-                                 | 0/0                         |
| 1207  | KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL , PPP (ANNUITY)                                                                                      | 02/2012          | 702.16<br>-              | 702.16             | 490.36                      | 07/2014<br>-          | 03/2018     | 44(O)<br>-                                 | 0/0                         |
| 1208  | BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL , PPP (ANNUITY)                                                                                         | 08/2012          | 867.00<br>-              | 867.00             | 278.17                      | 02/2015<br>-          | 12/2017     | 34(O)<br>-                                 | 0/0                         |
| 1209  | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH, WEST BENGAL , G                   | 01/1991          | 322.00<br>-              | 322.00             | 56.41                       | 03/2018<br>-          | 03/2018     | 0(O)<br>-                                  | 0/0                         |
| 1210  | CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL , G                                                                                        | 10/2015          | 361.15<br>-              | 361.15             | -                           | -<br>-                | 01/2018     | -<br>-                                     | 0/0                         |
| 1211  | 4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI ( KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL , G                                              | 12/2015          | 1,083.00<br>-            | 1,083.00           | -                           | 06/2018<br>-          | 06/2018     | 0(O)<br>-                                  | 0/0                         |
| 1212  | SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)                                                                               | 04/2014          | 1,665.00<br>-            | 1,665.00           | 2,091.52                    | -<br>-                | 12/2017     | -<br>-                                     | 0/0                         |
| 1213  | CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL , G                                                                        | 03/2016          | 229.37<br>-              | 229.37             | 32.47                       | -<br>-                | 11/2018     | -<br>-                                     | 0/0                         |
| 1214  | FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL , G                    | 09/2016          | 767.03<br>-              | 767.03             | 58.27                       | -<br>-                | 08/2018     | -<br>-                                     | 0/0                         |
|       | <b>Total</b>                                                                                                                                               |                  | <b>3,17,373.88<br/>-</b> | <b>3,23,746.08</b> | <b>1,00,653.00</b>          |                       |             |                                            | <b>23/182</b>               |
|       |                                                                                                                                                            |                  |                          |                    |                             |                       |             |                                            |                             |
|       | <b>SHIPPING AND PORTS</b>                                                                                                                                  |                  |                          |                    |                             |                       |             |                                            |                             |
| 1215  | RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA , G                                                                 | 03/2007          | 245.67<br>-              | 409.83             | 350.68                      | 04/2009<br>-          | -           | -                                          | 0/0                         |
| 1216  | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA , PPP (BOT) | 01/2007          | 366.39<br>-              | 669.46             | 411.12                      | 12/2010<br>-          | 12/2018     | 96(O)<br>-                                 | 0/0                         |
| 1217  | SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, TAMIL NADU , Public Private (SPV)                                                              | 06/2005          | 2,427.40<br>-            | 2,427.40           | 831.21                      | 10/2008<br>-          | -           | -                                          | 0/0                         |



**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                        |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|----------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                      | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1218  | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU , Public Private (SPV)                  | 10/2002          | 150.00 -                | 600.00           | 139.80                      | 03/2006 -             | 12/2017     | 141(O) -                                   | 0/0                         |
| 1219  | CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]KPL,TAMIL NADU , PPP (ANNUITY)                                     | 10/2013          | 198.94 -                | 235.15           | 98.60                       | 06/2017 -             | -           | -                                          | 0/1                         |
| 1220  | CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU , PPP (ANNUITY)                                     | 02/2015          | 244.50<br>258.00        | 258.33           | .14                         | 12/2017 -             | 12/2017     | 0(O) -                                     | 0/1                         |
| 1221  | CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL,TAMIL NADU , G                                                   | 12/2014          | 274.85 -                | 274.85           | 43.83                       | 04/2017 -             | -           | -                                          | 0/1                         |
| 1222  | CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL,TAMIL NADU , G                                              | 09/2015          | 210.00 -                | 210.00           | -                           | 01/2018 -             | 01/2018     | 0(O) -                                     | 0/0                         |
|       | <b>Total</b>                                                                                                                           |                  | 4,117.75 -              | 5,085.02         | 1,875.38                    |                       |             |                                            | 0/3                         |
|       |                                                                                                                                        |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>TELECOMMUNICATIONS</u>                                                                                                              |                  |                         |                  |                             |                       |             |                                            |                             |
| 1223  | GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI , G                                                                  | 06/2016          | 418.26 -                | 418.26           | -                           | 06/2017 -             | -           | -                                          | 0/0                         |
| 1224  | NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE , G                                                                                  | 03/2012          | 13,334.00 -             | 24,664.00        | 6,660.00                    | 07/2015 -             | 06/2019     | 47(O) -                                    | 0/0                         |
| 1225  | NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE , Central Sector Projects           | 09/2014          | 2,111.17 -              | 2,011.17         | 253.90                      | 09/2014 -             | -           | -                                          | 0/70                        |
|       | <b>Total</b>                                                                                                                           |                  | 15,863.43 -             | 27,093.43        | 6,913.90                    |                       |             |                                            | 0/70                        |
|       |                                                                                                                                        |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>URBAN DEVELOPMENT</u>                                                                                                               |                  |                         |                  |                             |                       |             |                                            |                             |
| 1226  | CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH , G                       | 06/2014          | 157.84 -                | 157.84           | 100.08                      | 03/2017 -             | -           | -                                          | 0/5                         |
| 1227  | REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH , G | 08/2007          | 246.90 -                | 246.90           | -                           | - -                   | -           | -                                          | 0/0                         |
| 1228  | CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR , G                | 02/2016          | 496.18<br>496.00        | 496.18           | -                           | 06/2017 -             | -           | -                                          | 0/0                         |
| 1229  | DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI , G                                                                                      | 09/2011          | 38,585.00 -             | 38,585.00        | 30,035.84                   | 03/2016 -             | 12/2016     | -                                          | 0/0                         |
| 1230  | ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI , G            | 10/2013          | 1,219.21<br>2,230.23    | 1,592.00         | 122.50                      | 10/2019 -             | 03/2020     | 5(O) -                                     | 0/0                         |
| 1231  | CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI , G                        | 05/2012          | 405.01 -                | 405.01           | 349.54                      | 12/2014<br>07/2017    | 07/2017     | -                                          | 2/3                         |
| 1232  | CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI , G         | 07/2012          | 884.30 -                | 884.30           | 503.45                      | 12/2015<br>12/2017    | 03/2018     | 27(O)<br>3(R)                              | 0/0                         |



# Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                            |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|--------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                    | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                          | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1233  | REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI , G                                                                             | 06/2012          | 4,264.00 -              | 4,118.00         | 2,790.00                    | 11/2019 -             | 11/2019     | 0(O) -                                     | 1/7                         |
| 1234  | CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI , G               | 06/2015          | 197.33 -                | 197.33           | 3.79                        | - -                   | 04/2019     | - -                                        | 0/2                         |
| 1235  | DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH , G                                     | 11/2012          | 270.83 -                | 270.83           | 116.57                      | 11/2014 -             | 10/2018     | 47(O) -                                    | 0/0                         |
| 1236  | 2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND , G                                                   | 09/2012          | 171.86 -                | 171.86           | 38.40                       | 03/2016 -             | 12/2018     | 33(O) -                                    | 1/6                         |
| 1237  | BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA , G                                                                               | 05/2006          | 6,395.00<br>13,845.01   | 13,845.01        | 14,200.11                   | 06/2011<br>12/2015    | 04/2017     | -                                          | 3/3                         |
| 1238  | BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA , G                                                                       | 02/2014          | 26,405.14 -             | 26,405.14        | 2,391.46                    | 02/2019 -             | 03/2020     | 13(O) -                                    | 0/0                         |
| 1239  | RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA , G                                                                       | 12/2016          | 246.31 -                | 246.31           | -                           | 02/2020 -             | 02/2020     | 0(O) -                                     | 0/0                         |
| 1240  | CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA , G                                                         | 01/2010          | 165.23 -                | 165.23           | 25.91                       | 10/2012<br>04/2017    | 03/2018     | 65(O)<br>11(R)                             | 0/1                         |
| 1241  | KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA , G                                                                                      | 07/2012          | 5,181.79 -              | 5,181.79         | -                           | 07/2017 -             | 12/2019     | 29(O) -                                    | 0/0                         |
| 1242  | CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD,KERALA , G               | 07/2015          | 154.00 -                | 154.00           | 66.56                       | 11/2015 -             | 12/2017     | 25(O) -                                    | 0/0                         |
| 1243  | CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH , G                                     | 12/2012          | 188.87 -                | 188.87           | 168.98                      | 12/2015<br>12/2017    | 12/2017     | 24(O)<br>0(R)                              | 0/0                         |
| 1244  | CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]CPWD,MADHYA PRADESH , EPC | 12/2016          | 164.00 -                | 164.00           | 68.10                       | 01/2018<br>03/2018    | 03/2018     | 2(O)<br>0(R)                               | 1/10                        |
| 1245  | OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA , G                             | 02/2011          | 241.33<br>349.33        | 349.33           | 221.30                      | 03/2016<br>12/2017    | 03/2018     | 24(O)<br>3(R)                              | 0/13                        |
| 1246  | UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA , G                                       | 06/2010          | 205.00<br>166.97        | 170.62           | 146.41                      | 03/2012 -             | 03/2018     | 72(O) -                                    | 11/20                       |
| 1247  | CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA , G                              | 12/2012          | 315.00 -                | 315.00           | 302.82                      | 06/2015 -             | 09/2017     | 27(O) -                                    | 8/8                         |
| 1248  | NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA , G                                                                                       | 08/2014          | 8,680.00 -              | 8,680.00         | 1,688.81                    | 03/2018 -             | 12/2019     | 21(O) -                                    | 0/0                         |
| 1249  | MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA , G                                                               | 07/2013          | 23,136.00 -             | 23,136.00        | -                           | 01/2015 -             | -           | -                                          | 0/0                         |
| 1250  | NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects                                                | 02/2014          | 216.69 -                | 216.69           | 52.00                       | 03/2015 -             | 11/2018     | 44(O) -                                    | 0/10                        |
| 1251  | CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB , G                              | 02/2014          | 388.00 -                | 388.00           | 277.96                      | 05/2017<br>02/2018    | 02/2018     | 9(O)<br>0(R)                               | 7/12                        |
| 1252  | CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB , G                                        | 08/2016          | 294.00 -                | 294.00           | 34.90                       | 04/2019 -             | 04/2019     | 0(O) -                                     | 0/8                         |

**Detail of ongoing Projects Costing Rs.150 Crore and above.**

(All Cost/ Expenditure in Rs. Crore)

|       |                                                                                                                                                       |                  |                         |                  |                             | Date of Commissioning |             | (September 2017)                           |                             |
|-------|-------------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                                                                               | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                                                                     | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 1253  | DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN - [N28000091]CPWD, RAJASTHAN , Central Sector Projects | 08/2014          | 350.02<br>479.87        | 479.87           | 361.32                      | 03/2015<br>12/2017    | -           | -                                          | 0/0                         |
| 1254  | STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD, TAMIL NADU , G                                                                       | 04/2014          | 332.72<br>-             | 332.72           | 260.88                      | 09/2016<br>-          | 11/2017     | 14(O)<br>-                                 | 0/0                         |
| 1255  | CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU , G                                                                                    | 02/2009          | 14,600.00<br>19,058.00  | 19,058.00        | 14,784.59                   | 12/2015<br>-          | 12/2017     | 24(O)<br>-                                 | 11/24                       |
| 1256  | C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT - [N28000089]CPWD, TAMIL NADU , G                          | 12/2015          | 209.00<br>-             | 209.00           | 9.00                        | -<br>-                | -           | -                                          | 0/6                         |
| 1257  | CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL, TAMIL NADU , G                                                                                | 06/2016          | 3,770.00<br>-           | 3,770.00         | -                           | 03/2018<br>-          | 03/2018     | 0(O)<br>-                                  | 0/0                         |
| 1258  | ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD, TELANGANA , G                              | 10/2016          | 209.84<br>-             | 209.84           | .43                         | 03/2020<br>-          | 03/2020     | 0(O)<br>-                                  | 0/5                         |
| 1259  | LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL, UTTAR PRADESH , G                                                                              | 01/2016          | 6,928.00<br>6,928.00    | 6,928.00         | 2,536.77                    | 03/2019<br>-          | 03/2019     | 0(O)<br>-                                  | 0/0                         |
| 1260  | CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD, UTTARAKHAND , G                | 12/2008          | 114.26<br>266.00        | 266.00           | -                           | 12/2013<br>-          | 10/2019     | 70(O)<br>-                                 | 0/0                         |
| 1261  | CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL , G                                     | 02/2014          | 156.57<br>-             | 156.57           | 119.09                      | 08/2016<br>-          | 03/2018     | 19(O)<br>-                                 | 8/13                        |
|       | <b>Total</b>                                                                                                                                          |                  | 1,45,945.23<br>-        | 1,58,435.24      | 71,777.57                   |                       |             |                                            | 53/156                      |
|       |                                                                                                                                                       |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <b>DEFENCE PRODUCTION</b>                                                                                                                             |                  |                         |                  |                             |                       |             |                                            |                             |
| 1262  | CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL, GOA , G                                                                                                  | 12/2016          | 167.69<br>168.00        | 172.99           | 22.26                       | 05/2018<br>-          | 05/2018     | 0(O)<br>-                                  | 1/5                         |
| 1263  | CONSTRUCTION WORKS PHASE 3B - [N39000002]GSL, GOA , G                                                                                                 | 12/2016          | 285.95<br>286.00        | 296.05           | 29.91                       | 08/2020<br>-          | 08/2020     | 0(O)<br>-                                  | 1/3                         |
|       | <b>Total</b>                                                                                                                                          |                  | 453.64<br>-             | 469.04           | 52.17                       |                       |             |                                            | 2/8                         |
|       |                                                                                                                                                       |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <b>Grand Total</b>                                                                                                                                    |                  | 15,53,683.89            | 17,49,427.56     | 6,79,801.38                 |                       |             |                                            | 2001/3776                   |


## Summary of projects in the Flash Report for the month of September, 2017

### Project Implementation - Current Status:

|                                                              |      |
|--------------------------------------------------------------|------|
| Number of Projects in Previous Month                         | 1272 |
| Number of Projects completed/dropped/frozen in Current Month | 17   |
|                                                              | 0    |
| Number of Projects Added in Current Month                    | 8    |
| Number of Projects in Current Month                          | 1263 |

### Brief Analysis

**Project Status with respect to Original Schedule:** Out of 1263 projects, 14 projects are ahead of schedule, 307 projects are on schedule 297 projects are delayed. 510 projects do not have fixed dates of commissioning. 135 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

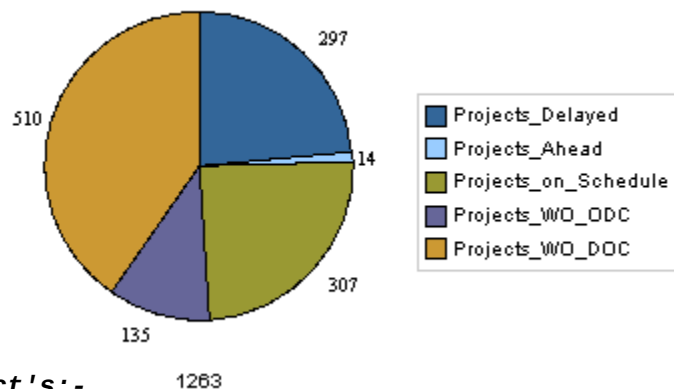


**Total No Of Project's:-**

### Investment Scenario

**Total original cost of implementation of 1263 projects when sanctioned, was of the order of Rs. 1553683.89 crore but this was subsequently revised to Rs. 1749427.56 crore implying a cost overrun of 12.6%. The expenditure incurred on these projects till September, 2017 is Rs. 679801.38 crore, which is 38.9% of the anticipated cost of the projects.**

**Figures are in Rs. Crore**

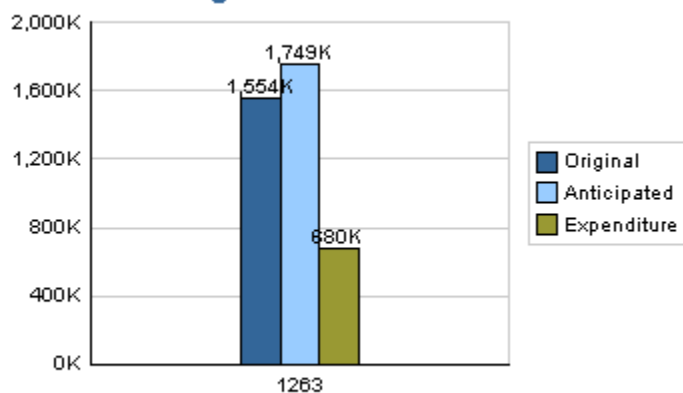

## Sector wise current status of projects on the Flash Report


### ATOMIC ENERGY

#### Current Status:

|                            |   |
|----------------------------|---|
| Number of Projects         | 3 |
| Number of Projects Delayed | 3 |

#### Brief Analysis

**Project Status with respect to Original Schedule: Out of 3 projects, 3 projects are delayed.**

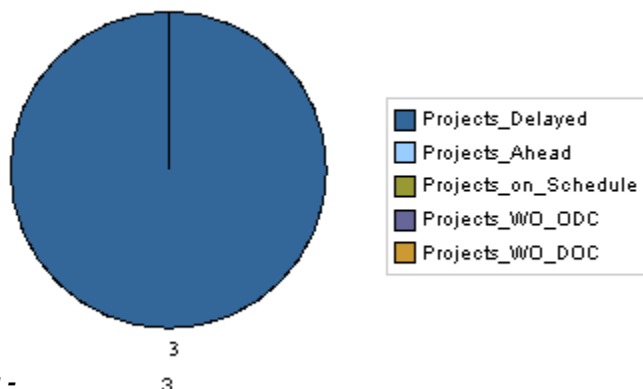


Total No Of Project's:-

#### Investment Scenario

**Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 27271 crore but this was subsequently anticipated to Rs. 29779 crore implying a cost overrun of 9.2%. The expenditure incurred on these projects till September, 2017 is Rs. 24508.27 crore, which is 82.3% of the anticipated cost of the projects.**

Figures are in Rs. Crore

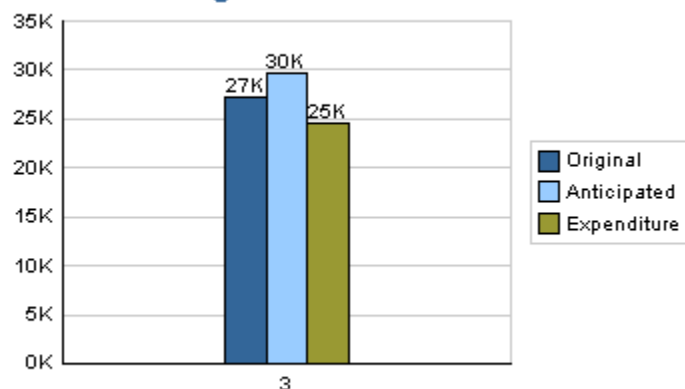

## Sector wise current status of projects on the Flash Report


### CIVIL AVIATION

#### Current Status:

|                            |   |
|----------------------------|---|
| Number of Projects         | 2 |
| Number of Projects Delayed | 2 |

#### Brief Analysis

**Project Status with respect to Original Schedule: Out of 2 projects, 2 projects are delayed.**

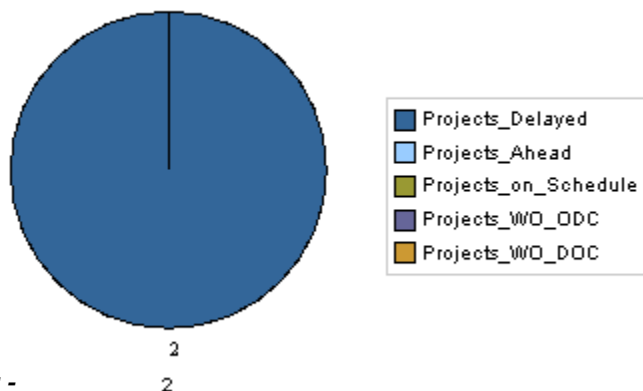


Total No Of Project's:-

#### Investment Scenario

**Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 624.07 crore but this was subsequently anticipated to Rs. 994.86 crore implying a cost overrun of 59.4%. The expenditure incurred on these projects till September, 2017 is Rs. 508.89 crore, which is 51.2% of the anticipated cost of the projects.**

Figures are in Rs. Crore

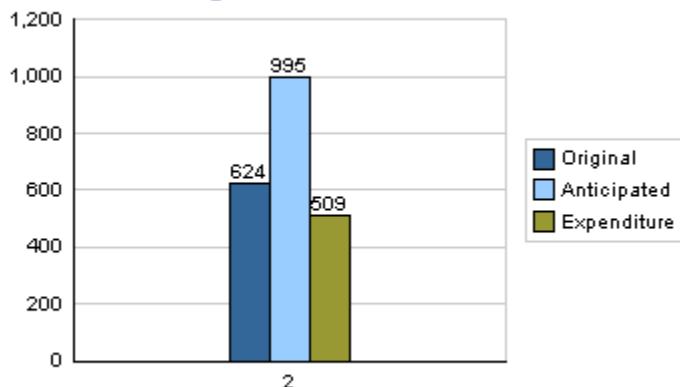

## Sector wise current status of projects on the Flash Report

### COAL


#### Current Status:

|                                |    |
|--------------------------------|----|
| Number of Projects             | 92 |
| Number of Projects On Schedule | 50 |
| Number of Projects Delayed     | 39 |

|                                                  |   |
|--------------------------------------------------|---|
| Number of Projects Without Date Of Commissioning | 3 |
|--------------------------------------------------|---|

#### Brief Analysis

**Project Status with respect to Original Schedule:** Out of 92 projects, 50 projects are on schedule 39 projects are delayed. 3 projects do not have fixed dates of commissioning.

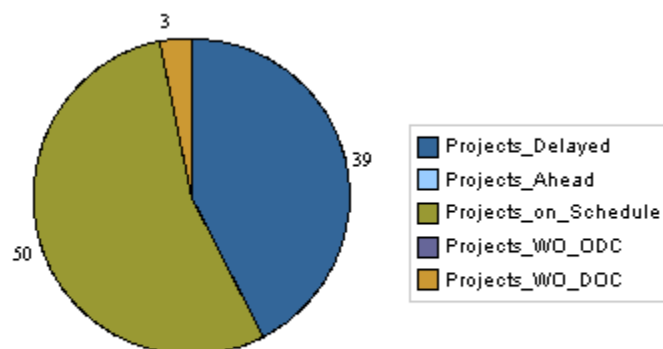


Total No Of Project's:-

92

#### Investment Scenario

**Total original cost of implementation of 92 projects when sanctioned, was of the order of Rs. 88124.99 crore but this was subsequently anticipated to Rs. 88310.36 crore implying a cost overrun of .2%. The expenditure incurred on these projects till September, 2017 is Rs. 21448.64 crore, which is 24.3% of the anticipated cost of the projects.**

Figures are in Rs. Crore

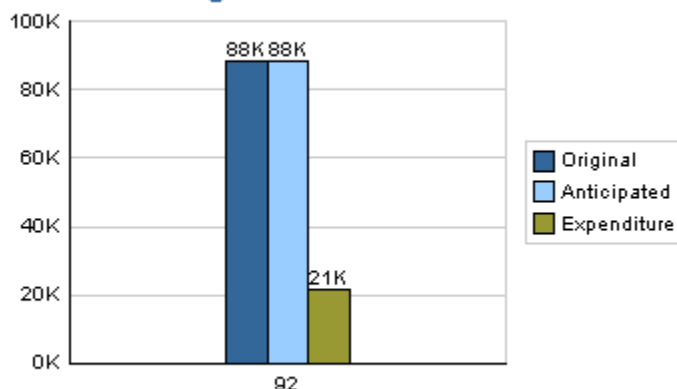

## Sector wise current status of projects on the Flash Report


### FERTILISERS

#### Current Status:

|                                |   |
|--------------------------------|---|
| Number of Projects             | 2 |
| Number of Projects On Schedule | 1 |
| Number of Projects Delayed     | 1 |

#### Brief Analysis

**Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project is delayed.**

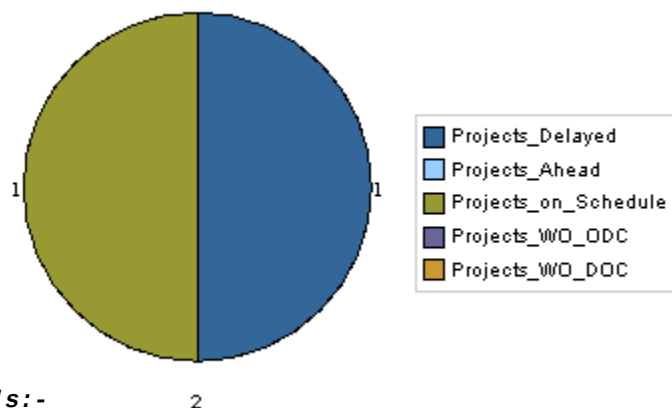


Total No Of Project's:-

#### Investment Scenario

**Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 680.64 crore but this was subsequently anticipated to Rs. 703.44 crore implying a cost overrun of 3.3%. The expenditure incurred on these projects till September, 2017 is Rs. 482.9 crore, which is 68.6% of the anticipated cost of the projects.**

Figures are in Rs. Crore

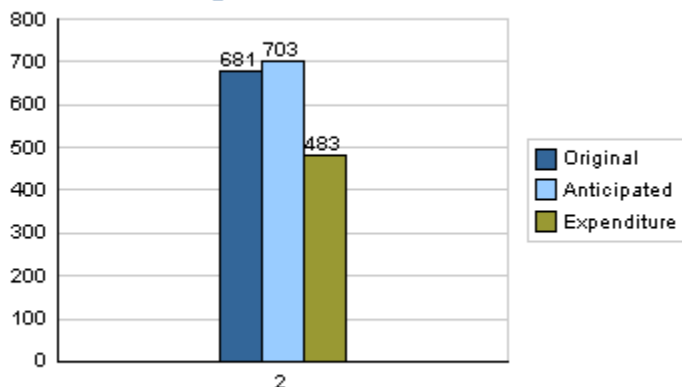

## Sector wise current status of projects on the Flash Report

### MINES


#### Current Status:

|                                |   |
|--------------------------------|---|
| Number of Projects             | 4 |
| Number of Projects On Schedule | 2 |

|                                                  |   |
|--------------------------------------------------|---|
| Number of Projects Without Date Of Commissioning | 2 |
|--------------------------------------------------|---|

#### Brief Analysis

**Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule 2 projects do not have fixed dates of commissioning.**

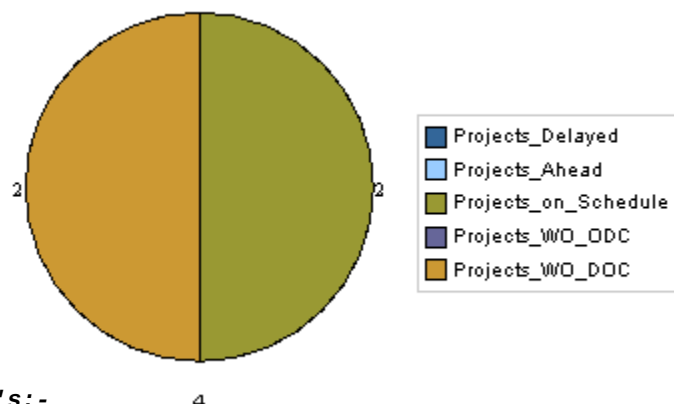


Total No Of Project's:-

4

#### Investment Scenario

**Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 6773.63 crore but this was subsequently anticipated to Rs. 6773.63 crore The expenditure incurred on these projects till September, 2017 is Rs. 372.63 crore, which is 5.5% of the anticipated cost of the projects.**

Figures are in Rs. Crore

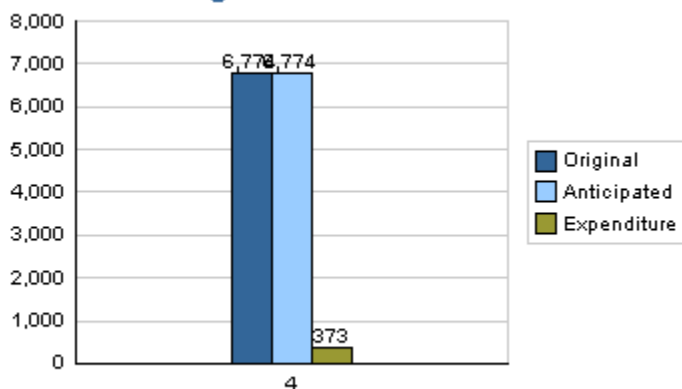



## Sector wise current status of projects on the Flash Report

### STEEL


#### Current Status:

|                                |    |
|--------------------------------|----|
| Number of Projects             | 34 |
| Number of Projects On Schedule | 9  |
| Number of Projects Delayed     | 17 |

|                                                           |   |
|-----------------------------------------------------------|---|
| Number of Projects Without Original Date of Commissioning | 1 |
| Number of Projects Without Date Of Commissioning          | 7 |

#### Brief Analysis

**Project Status with respect to Original Schedule:** Out of 34 projects, 9 projects are on schedule 17 projects are delayed. 7 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

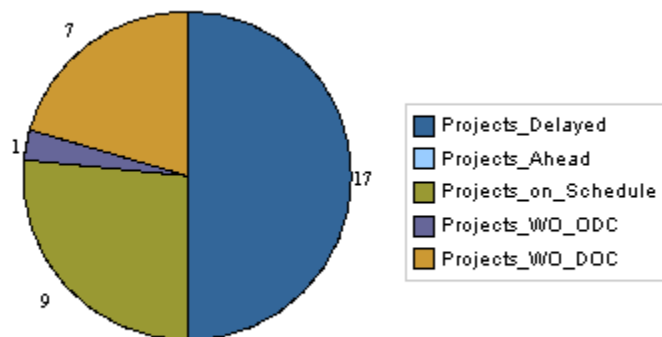


Total No Of Project's:-

34

#### Investment Scenario

**Total original cost of implementation of 34 projects when sanctioned, was of the order of Rs. 57349.49 crore but this was subsequently anticipated to Rs. 57563.17 crore implying a cost overrun of .4%. The expenditure incurred on these projects till September, 2017 is Rs. 39026.87 crore, which is 67.8% of the anticipated cost of the projects.**

Figures are in Rs. Crore

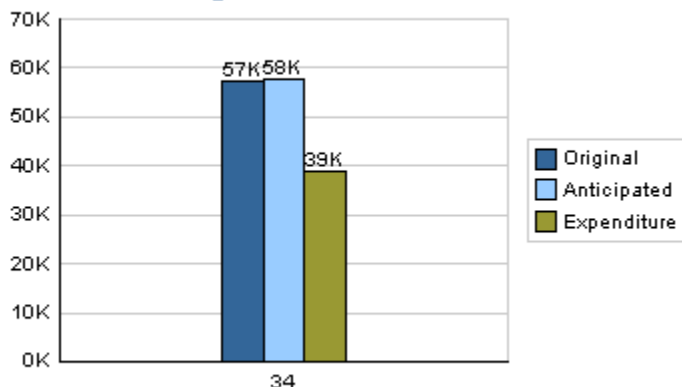

## Sector wise current status of projects on the Flash Report


### PETROLEUM

#### Current Status:

|                                                  |     |
|--------------------------------------------------|-----|
| Number of Projects                               | 104 |
| Number of Projects On Schedule                   | 55  |
| Number of Projects Delayed                       | 35  |
| Number of Projects Ahead                         | 8   |
| Number of Projects Without Date Of Commissioning | 6   |

#### Brief Analysis

Project Status with respect to Original Schedule: Out of 104 projects, 8 projects are ahead of schedule, 55 projects are on schedule 35 projects are delayed. 6 projects do not have fixed dates of commissioning.

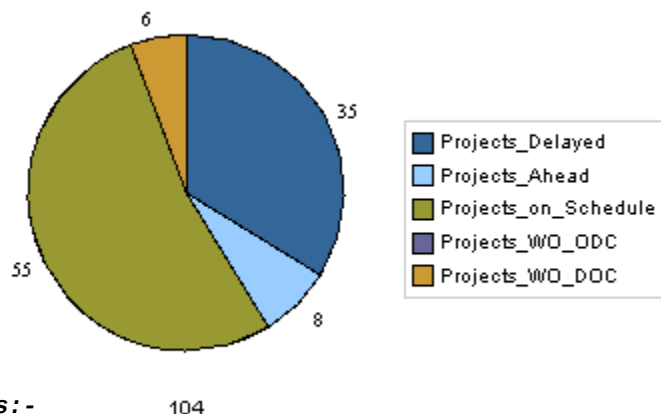


Total No Of Project's:-

#### Investment Scenario

Total original cost of implementation of 104 projects when sanctioned, was of the order of Rs. 190142.65 crore but this was subsequently anticipated to Rs. 191522.05 crore implying a cost overrun of .7%. The expenditure incurred on these projects till September, 2017 is Rs. 52758.11 crore, which is 27.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

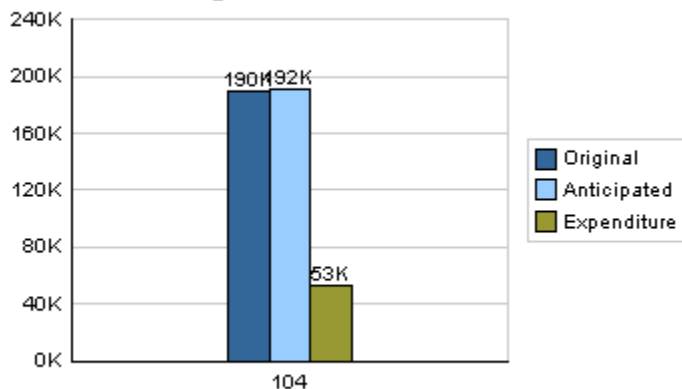

## Sector wise current status of projects on the Flash Report


### POWER

#### Current Status:

|                                                  |     |
|--------------------------------------------------|-----|
| Number of Projects                               | 124 |
| Number of Projects On Schedule                   | 52  |
| Number of Projects Delayed                       | 61  |
| Number of Projects Ahead                         | 3   |
| Number of Projects Without Date Of Commissioning | 8   |

#### Brief Analysis

Project Status with respect to Original Schedule: Out of 124 projects, 3 projects are ahead of schedule, 52 projects are on schedule 61 projects are delayed. 8 projects do not have fixed dates of commissioning.

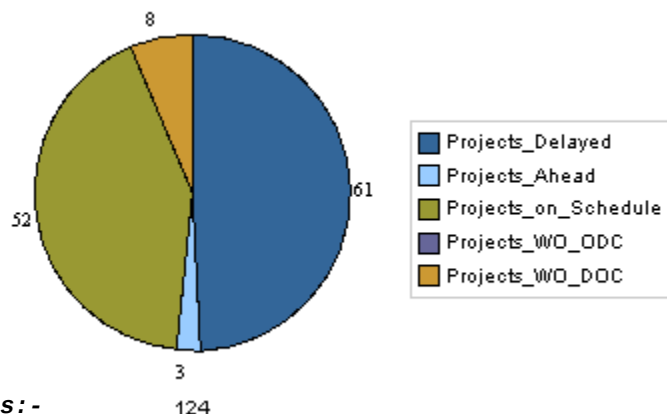


Total No Of Project's:-

#### Investment Scenario

Total original cost of implementation of 124 projects when sanctioned, was of the order of Rs. 339545.24 crore but this was subsequently anticipated to Rs. 397302.11 crore implying a cost overrun of 17%. The expenditure incurred on these projects till September, 2017 is Rs. 224764.86 crore, which is 56.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

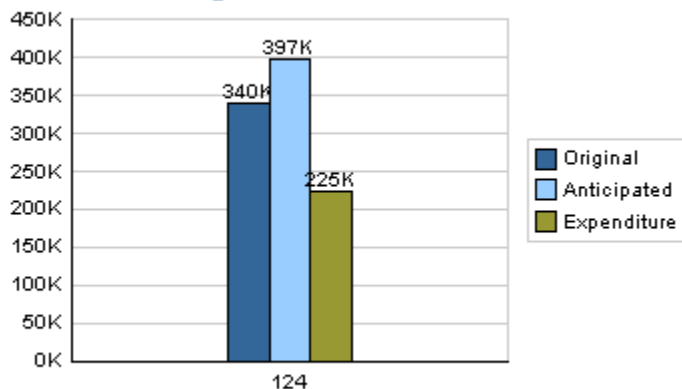

## Sector wise current status of projects on the Flash Report


### HEAVY INDUSTRY

#### Current Status:

|                            |   |
|----------------------------|---|
| Number of Projects         | 1 |
| Number of Projects Delayed | 1 |

#### Brief Analysis


**Project Status with respect to Original Schedule: Out of 1 project, 1 project is delayed.**



Total No Of Project's:-

#### Investment Scenario

**Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 1718 crore but this was subsequently anticipated to Rs. 3827.3 crore implying a cost overrun of 122.8%. The expenditure incurred on these projects till September, 2017 is Rs. 2289 crore, which is 59.8% of the anticipated cost of the projects.**

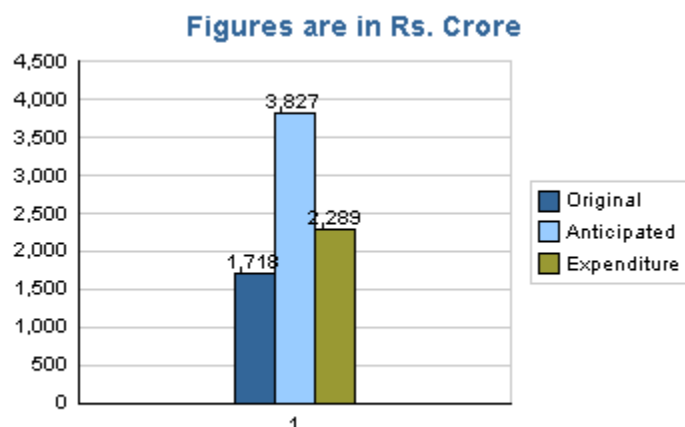

## Sector wise current status of projects on the Flash Report

### HEALTH AND FAMILY WELFARE


#### Current Status:

|                                |    |
|--------------------------------|----|
| Number of Projects             | 13 |
| Number of Projects On Schedule | 3  |
| Number of Projects Delayed     | 5  |

|                                                  |   |
|--------------------------------------------------|---|
| Number of Projects Without Date Of Commissioning | 5 |
|--------------------------------------------------|---|

#### Brief Analysis

**Project Status with respect to Original Schedule: Out of 13 projects, 3 projects are on schedule 5 projects are delayed. 5 projects do not have fixed dates of commissioning.**

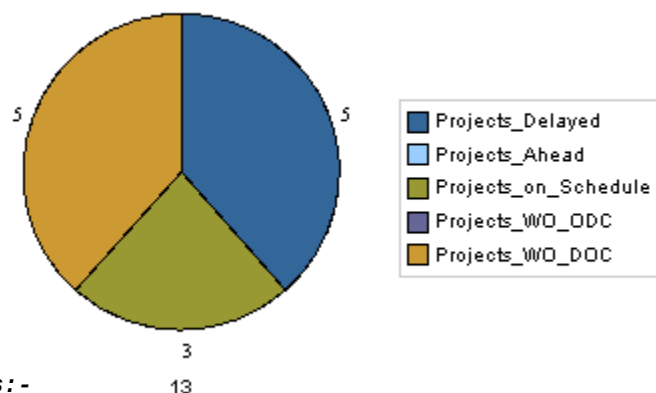


Total No Of Project's:-

#### Investment Scenario

**Total original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 3637.08 crore but this was subsequently anticipated to Rs. 3649.38 crore implying a cost overrun of .3%. The expenditure incurred on these projects till September, 2017 is Rs. 1792.95 crore, which is 49.1% of the anticipated cost of the projects.**

Figures are in Rs. Crore

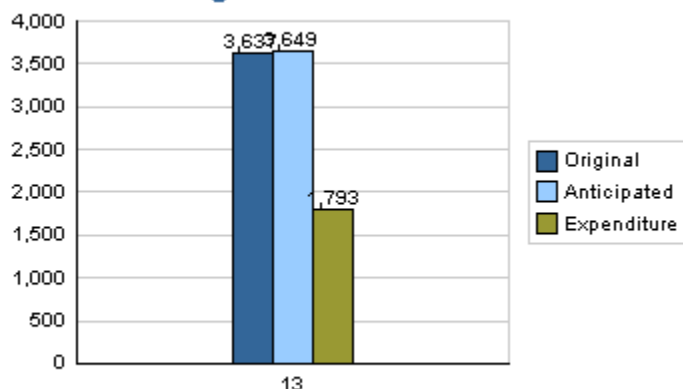

## Sector wise current status of projects on the Flash Report


### RAILWAYS

#### Current Status:

|                                                           |     |
|-----------------------------------------------------------|-----|
| Number of Projects                                        | 353 |
| Number of Projects On Schedule                            | 38  |
| Number of Projects Delayed                                | 36  |
| Number of Projects Ahead                                  | 1   |
| Number of Projects Without Original Date of Commissioning | 66  |
| Number of Projects Without Date Of Commissioning          | 212 |

#### Brief Analysis

**Project Status with respect to Original Schedule:** Out of 353 projects, 1 project is ahead of schedule, 38 projects are on schedule 36 projects are delayed. 212 projects do not have fixed dates of commissioning. 66 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

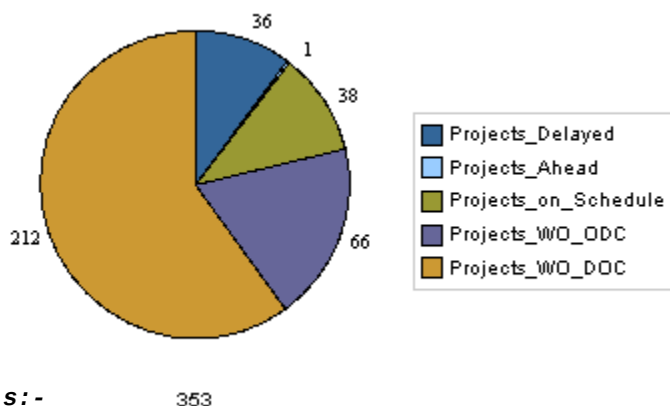


Total No Of Project's:-

#### Investment Scenario

**Total original cost of implementation of 353 projects when sanctioned, was of the order of Rs. 354063.17 crore but this was subsequently anticipated to Rs. 454173.45 crore implying a cost overrun of 28.3%. The expenditure incurred on these projects till September, 2017 is Rs. 130576.24 crore, which is 28.8% of the anticipated cost of the projects.**

Figures are in Rs. Crore

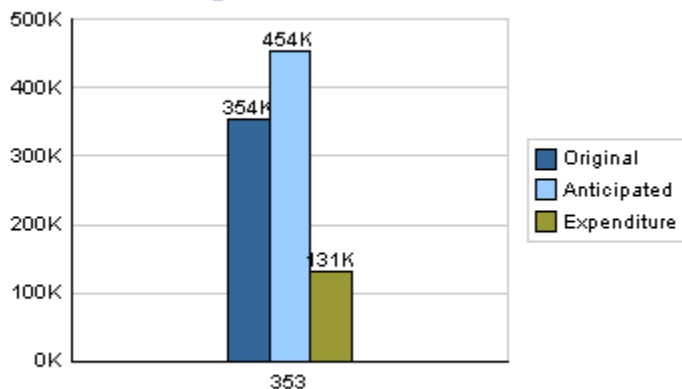

## Sector wise current status of projects on the Flash Report


### ROAD TRANSPORT AND HIGHWAYS

#### Current Status:

|                                                           |     |
|-----------------------------------------------------------|-----|
| Number of Projects                                        | 482 |
| Number of Projects On Schedule                            | 87  |
| Number of Projects Delayed                                | 74  |
| Number of Projects Ahead                                  | 2   |
| Number of Projects Without Original Date of Commissioning | 67  |
| Number of Projects Without Date Of Commissioning          | 252 |

#### Brief Analysis

**Project Status with respect to Original Schedule:** Out of 482 projects, 2 projects are ahead of schedule, 87 projects are on schedule 74 projects are delayed. 252 projects do not have fixed dates of commissioning. 67 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

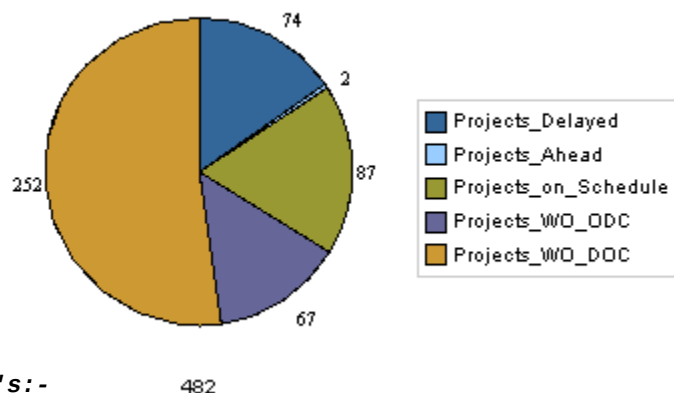


Total No Of Project's:-

482

#### Investment Scenario

**Total original cost of implementation of 482 projects when sanctioned, was of the order of Rs. 317373.88 crore but this was subsequently anticipated to Rs. 323746.08 crore implying a cost overrun of 2%. The expenditure incurred on these projects till September, 2017 is Rs. 100653 crore, which is 31.1% of the anticipated cost of the projects.**

Figures are in Rs. Crore

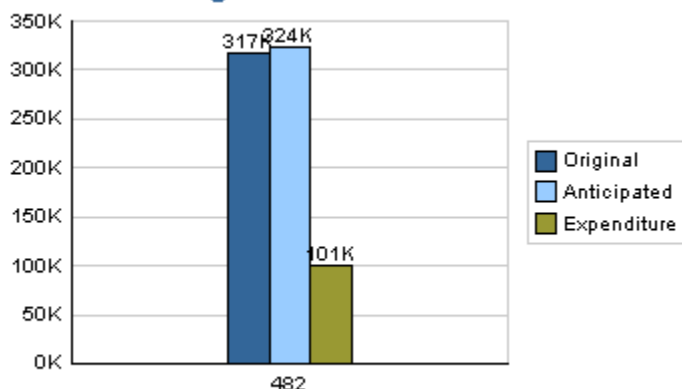

## Sector wise current status of projects on the Flash Report

### SHIPPING AND PORTS


#### Current Status:

|                                |   |
|--------------------------------|---|
| Number of Projects             | 8 |
| Number of Projects On Schedule | 2 |
| Number of Projects Delayed     | 2 |

|                                                  |   |
|--------------------------------------------------|---|
| Number of Projects Without Date Of Commissioning | 4 |
|--------------------------------------------------|---|

#### Brief Analysis

**Project Status with respect to Original Schedule: Out of 8 projects, 2 projects are on schedule 2 projects are delayed. 4 projects do not have fixed dates of commissioning.**

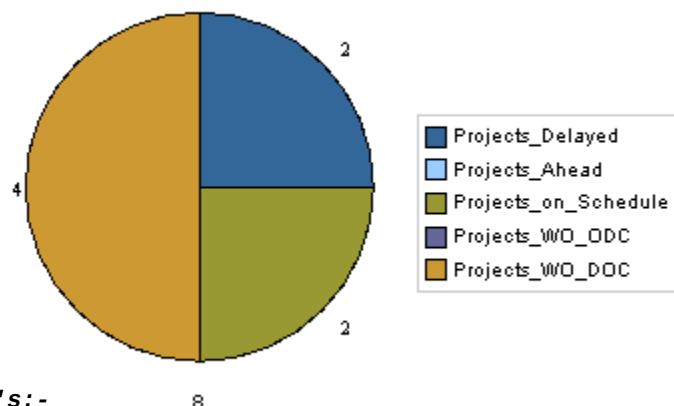


Total No Of Project's:-

#### Investment Scenario

**Total original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 4117.75 crore but this was subsequently anticipated to Rs. 5085.02 crore implying a cost overrun of 23.5%. The expenditure incurred on these projects till September, 2017 is Rs. 1875.38 crore, which is 36.9% of the anticipated cost of the projects.**

Figures are in Rs. Crore

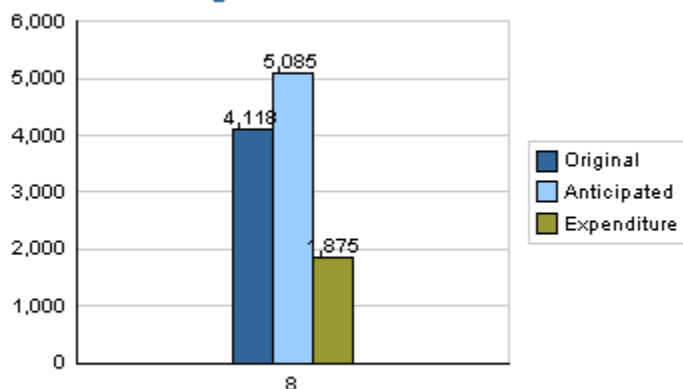



## Sector wise current status of projects on the Flash Report

### TELECOMMUNICATIONS

#### Current Status:


Number of Projects **3**

Number of Projects Delayed **1**

Number of Projects Without Date Of Commissioning **2**

#### Brief Analysis

**Project Status with respect to Original Schedule: Out of 3 projects, 1 project is delayed. 2 projects do not have fixed dates of commissioning.**

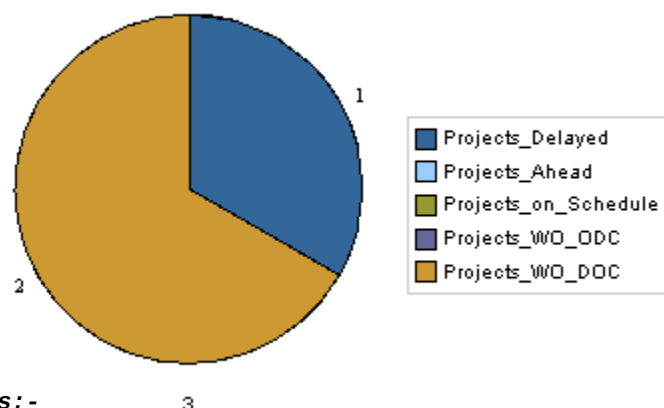


Total No Of Project's:-

#### Investment Scenario

**Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 15863.43 crore but this was subsequently anticipated to Rs. 27093.43 crore implying a cost overrun of 70.8%. The expenditure incurred on these projects till September, 2017 is Rs. 6913.9 crore, which is 25.5% of the anticipated cost of the projects.**

Figures are in Rs. Crore

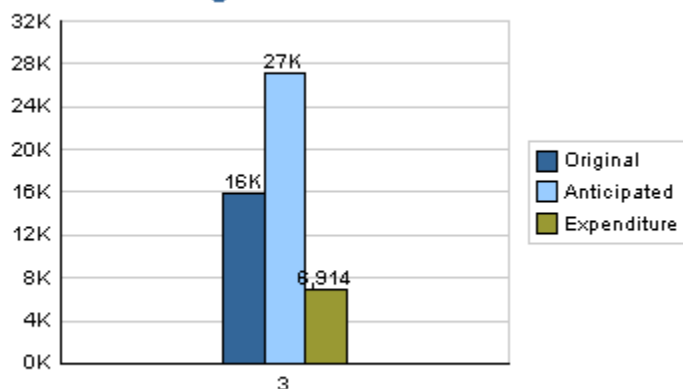

## Sector wise current status of projects on the Flash Report

### URBAN DEVELOPMENT


#### Current Status:

|                                |    |
|--------------------------------|----|
| Number of Projects             | 36 |
| Number of Projects On Schedule | 6  |
| Number of Projects Delayed     | 20 |

|                                                           |   |
|-----------------------------------------------------------|---|
| Number of Projects Without Original Date of Commissioning | 1 |
| Number of Projects Without Date Of Commissioning          | 9 |

#### Brief Analysis

**Project Status with respect to Original Schedule:** Out of 36 projects, 6 projects are on schedule 20 projects are delayed. 9 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

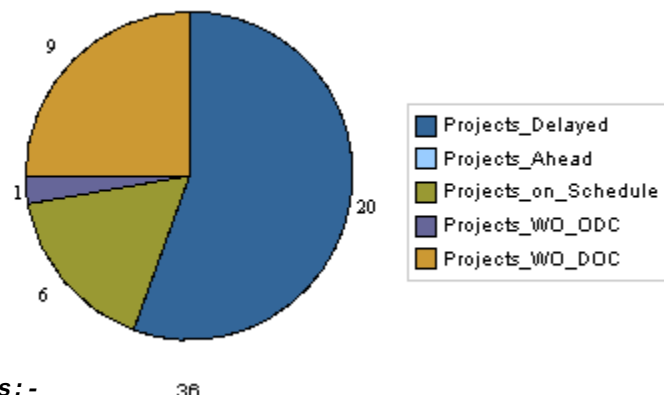


Total No Of Project's:-

#### Investment Scenario

**Total original cost of implementation of 36 projects when sanctioned, was of the order of Rs. 145945.23 crore but this was subsequently anticipated to Rs. 158435.24 crore implying a cost overrun of 8.6%. The expenditure incurred on these projects till September, 2017 is Rs. 71777.57 crore, which is 45.3% of the anticipated cost of the projects.**

Figures are in Rs. Crore

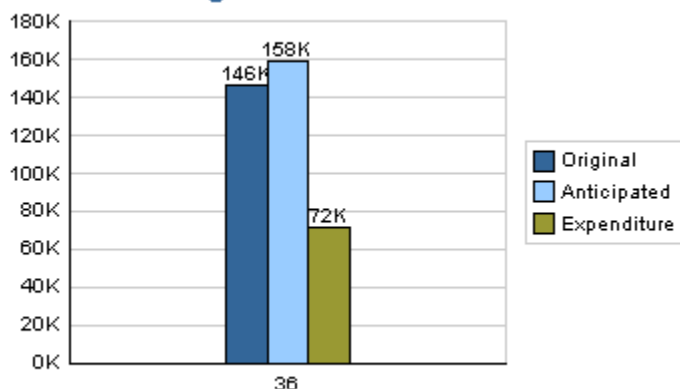

## Sector wise current status of projects on the Flash Report


### DEFENCE PRODUCTION

#### Current Status:

|                                |   |
|--------------------------------|---|
| Number of Projects             | 2 |
| Number of Projects On Schedule | 2 |

#### Brief Analysis

**Project Status with respect to Original Schedule: Out of 2 projects, 2 projects are on schedule**

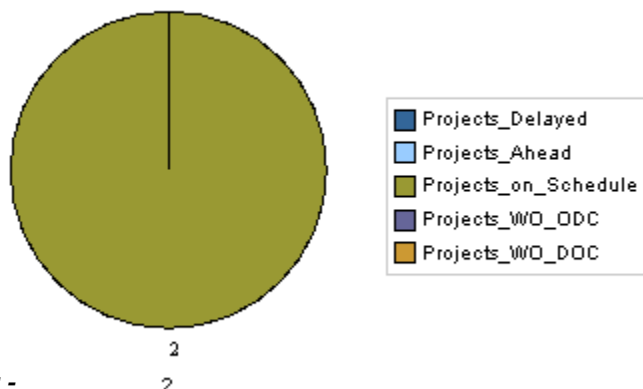


Total No Of Project's:-

#### Investment Scenario

**Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 453.64 crore but this was subsequently anticipated to Rs. 469.04 crore implying a cost overrun of 3.4%. The expenditure incurred on these projects till September, 2017 is Rs. 52.17 crore, which is 11.1% of the anticipated cost of the projects.**

Figures are in Rs. Crore

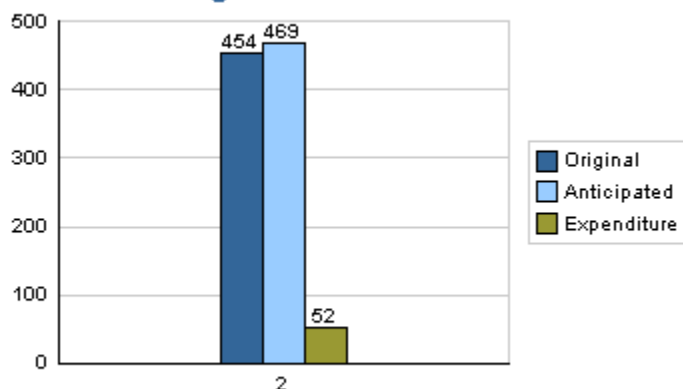

**ANNEXURE**  
**OF PROJECTS HAVING**  
**COST MORE THAN**  
**Rs 150 cr and ABOVE**

**Annexure - I**

**STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (SEPTEMBER 2017)**

(All Cost /Expenditure in Rs. crore)

| S.NO         | STATE                     | NO OF PROJECTS | COST ORIGINAL       | COST ANTICIPATED    | CUMULATIVE EXPENDITURE |
|--------------|---------------------------|----------------|---------------------|---------------------|------------------------|
| 1            | ANDAMAN & NICOBAR ISLANDS | 1              | 314.61              | 441.33              | 24.13                  |
| 2            | ANDHRA PRADESH            | 59             | 97,268.72           | 1,01,271.75         | 11,857.27              |
| 3            | ARUNACHAL PRADESH         | 31             | 16,602.41           | 33,555.84           | 17,205.4               |
| 4            | ASSAM                     | 50             | 33,769.6            | 47,399.82           | 29,960.5               |
| 5            | BIHAR                     | 77             | 64,823.58           | 81,651.84           | 38,464.48              |
| 6            | CHHATISGARH               | 38             | 82,769.79           | 84,975.67           | 48,572.54              |
| 7            | D & N HAVELI              | 1              | 6,086.08            | 5,479.75            | 2,081.12               |
| 8            | DELHI                     | 17             | 50,925.07           | 51,204.68           | 35,407.22              |
| 9            | GOA                       | 9              | 4,043.51            | 4,058.91            | 133.38                 |
| 10           | GUJARAT                   | 41             | 38,827.45           | 41,398.82           | 25,532.96              |
| 11           | HARYANA                   | 21             | 14,081.22           | 15,967.45           | 10,913.53              |
| 12           | HIMACHAL PRADESH          | 12             | 14,659.32           | 22,591.6            | 8,869.88               |
| 13           | JAMMU AND KASHMIR         | 10             | 27,408.66           | 47,277.79           | 19,743.25              |
| 14           | JHARKHAND                 | 48             | 46,724.53           | 50,436.69           | 18,263.64              |
| 15           | KARNATAKA                 | 46             | 78,727.9            | 96,951.71           | 43,753.26              |
| 16           | KERALA                    | 20             | 20,650.14           | 26,747.71           | 2,793.18               |
| 17           | MADHYA PRADESH            | 54             | 57,610.99           | 62,057.28           | 23,820.05              |
| 18           | MAHARASHTRA               | 112            | 1,69,907.76         | 1,79,607.21         | 57,223.47              |
| 19           | MANIPUR                   | 2              | 944.25              | 9,874.69            | 5,470.63               |
| 20           | MEGHALAYA                 | 6              | 7,108.02            | 9,025               | 935.41                 |
| 21           | MIZORAM                   | 5              | 2,001.2             | 6,942.57            | 3,060.66               |
| 22           | MULTI STATE               | 183            | 3,01,037.13         | 2,97,706.42         | 97,758.1               |
| 23           | NAGALAND                  | 7              | 8,126.79            | 10,276.79           | 362.71                 |
| 24           | ODISHA                    | 66             | 72,116.99           | 79,785.64           | 17,124.21              |
| 25           | PUNJAB                    | 28             | 15,555.77           | 15,561.5            | 3,396.28               |
| 26           | RAJASTHAN                 | 62             | 44,007.1            | 46,296.19           | 17,970.29              |
| 27           | SIKKIM                    | 6              | 2,537.08            | 5,585.45            | 893.04                 |
| 28           | TAMIL NADU                | 56             | 63,625.39           | 77,115.53           | 46,019.54              |
| 29           | TELANGANA                 | 35             | 24,832.84           | 27,489.74           | 6,378.54               |
| 30           | TRIPURA                   | 11             | 4,400.64            | 9,067.42            | 5,643.04               |
| 31           | UTTAR PRADESH             | 83             | 1,09,253.66         | 1,12,943.92         | 35,553.56              |
| 32           | UTTARAKHAND               | 13             | 16,833.35           | 17,673.56           | 8,248.87               |
| 33           | WEST BENGAL               | 53             | 56,102.34           | 71,007.29           | 36,367.24              |
| <b>TOTAL</b> |                           | <b>1,263</b>   | <b>15,53,683.89</b> | <b>17,49,427.56</b> | <b>6,79,801.38</b>     |

## LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(SEPTEMBER 2017)

| <b>CIVIL AVIATION</b> |                                                                                        |               |                         |                                 |                                |                                    |
|-----------------------|----------------------------------------------------------------------------------------|---------------|-------------------------|---------------------------------|--------------------------------|------------------------------------|
| <b>Sn</b>             | <b>Project</b>                                                                         | <b>Agency</b> | <b>Date of Approval</b> | <b>Cost Original (Rs.crore)</b> | <b>Cost Revised (Rs.crore)</b> | <b>Cumm Expenditure (Rs.crore)</b> |
| 1                     | CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT                                 | AAI           | 01/2009                 | 309.46                          | -                              | 484.76                             |
| <b>COAL</b>           |                                                                                        |               |                         |                                 |                                |                                    |
| <b>Sn</b>             | <b>Project</b>                                                                         | <b>Agency</b> | <b>Date of Approval</b> | <b>Cost Original (Rs.crore)</b> | <b>Cost Revised (Rs.crore)</b> | <b>Cumm Expenditure (Rs.crore)</b> |
| 2                     | KULDA OCP (MAHANADI COALFIELDS LTD)                                                    | MCL           | 01/2005                 | 302.96                          | -                              | 329.1                              |
| 3                     | BALRAM OCP EXTENSION, MCL 8.00 MTY                                                     | MCL           | 12/2007                 | 172.08                          | -                              | 191.07                             |
| 4                     | ANANTA OC EXPANSION PH-III (15.0 MTY)                                                  | MCL           | 08/2008                 | 207.28                          | -                              | 219.09                             |
| 5                     | RAMAGUNDAM OC-II EXTENSION                                                             | SCCL          | 12/2009                 | 418.97                          | -                              | 477.74                             |
| 6                     | NEYVELI SOLAR POWER PROJECT 130 MW                                                     | NLC           | 05/2016                 | 687.28                          | -                              | 690.47                             |
| <b>HEAVY INDUSTRY</b> |                                                                                        |               |                         |                                 |                                |                                    |
| <b>Sn</b>             | <b>Project</b>                                                                         | <b>Agency</b> | <b>Date of Approval</b> | <b>Cost Original (Rs.crore)</b> | <b>Cost Revised (Rs.crore)</b> | <b>Cumm Expenditure (Rs.crore)</b> |
| 7                     | NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)                     | NATIS         | 04/2011                 | 1718                            | -                              | 2289                               |
| <b>PETROLEUM</b>      |                                                                                        |               |                         |                                 |                                |                                    |
| <b>Sn</b>             | <b>Project</b>                                                                         | <b>Agency</b> | <b>Date of Approval</b> | <b>Cost Original (Rs.crore)</b> | <b>Cost Revised (Rs.crore)</b> | <b>Cumm Expenditure (Rs.crore)</b> |
| 8                     | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR                                           | ISPRL         | 01/2006                 | 993                             | -                              | 1537.84                            |
| 9                     | RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT)              | IOCL          | 06/2012                 | 150                             | -                              | 251.9                              |
| 10                    | UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE | OIL           | 09/2012                 | 871.35                          | -                              | 958                                |
| <b>POWER</b>          |                                                                                        |               |                         |                                 |                                |                                    |
| <b>Sn</b>             | <b>Project</b>                                                                         | <b>Agency</b> | <b>Date of Approval</b> | <b>Cost Original (Rs.crore)</b> | <b>Cost Revised (Rs.crore)</b> | <b>Cumm Expenditure (Rs.crore)</b> |
| 11                    | PARBATI HEP (4X200 MW) (NHPC) II                                                       | NHPC          | 09/2002                 | 3919.59                         | -                              | 6503.48                            |
| 12                    | SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)                                                | NHPC          | 09/2003                 | 6285.33                         | -                              | 9470.18                            |
| 13                    | TAPOVAN-VISHNUGAD HEP (4X130MW)                                                        | NTPC          | 11/2006                 | 2978.48                         | -                              | 3300                               |
| 14                    | KISHANGANGA HEP (3X110 MW)                                                             | NHPC          | 01/2009                 | 3642.04                         | -                              | 5052.02                            |
| 15                    | BONGAIGAON THERMAL POWER PROJECT                                                       | NTPC          | 01/2008                 | 4375.35                         | 6749.18                        | 6797                               |
| 16                    | PARE HYDRO ELECTRIC PROJECT                                                            | NEEPCO        | 12/2008                 | 573.99                          | 1337.76                        | 1499.78                            |
| 17                    | SYSTEM STRENGTHENING XII OF SR                                                         | PGCIL         | 02/2010                 | 232.34                          | -                              | 238.61                             |

## LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(SEPTEMBER 2017)

| Sn              | Project                                                            | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|-----------------|--------------------------------------------------------------------|--------|------------------|--------------------------|-------------------------|-----------------------------|
| 18              | SYTEM STRENGTHENING OF SOUTHERN REGION - XIV                       | PGCIL  | 12/2011          | 297.33                   | 346.79                  | 357.17                      |
| 19              | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT   | SJVN   | 05/2015          | 436.68                   | -                       | 472.27                      |
| <b>RAILWAYS</b> |                                                                    |        |                  |                          |                         |                             |
| Sn              | Project                                                            | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
| 20              | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)                  | NCR    | 04/1986          | 158.77                   | 274.56                  | 629.43                      |
| 21              | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)                             | SCR    | 12/1994          | 124.43                   | -                       | 919.06                      |
| 22              | AMRAVATI-NARKHER NL(CR)                                            | CR     | 06/1994          | 663.01                   | 668.34                  | 694.8                       |
| 23              | UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR                               | NR     | 03/1995          | 2500                     | -                       | 13536.97                    |
| 24              | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL | RVNL   | 04/1995          | 304                      | -                       | 474.51                      |
| 25              | CALICUT-MANGALORE (DL) (SR)                                        | SR     | 02/1996          | 240                      | -                       | 537.02                      |
| 26              | MANDARHILL-DUMKA-RAMPURHAT (NL), ER                                | ER     | 04/1995          | 900.05                   | -                       | 980.99                      |
| 27              | AHMEDNAGAR-PARLI VAIJNATH(NL) CR                                   | CR     | 02/1997          | 514.68                   | -                       | 812.01                      |
| 28              | HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR                     | SWR    | 02/1997          | 295                      | 1289.92                 | 1503.25                     |
| 29              | GONDIA-JABALPUR(GC), (SECR)                                        | SECR   | 02/1997          | 386.3                    | -                       | 967.96                      |
| 30              | NANGALDAM-TALWARA(NL), NR                                          | NR     | 03/1981          | 450                      | -                       | 484.14                      |
| 31              | KARUR-SALEM(NL), SR                                                | SR     | 02/1997          | 155.55                   | -                       | 854.92                      |
| 32              | NANDYAL-YERRAGUNTLA(NL), SCR                                       | SCR    | 03/1996          | 155.74                   | 164.36                  | 874.72                      |
| 33              | KANPUR KASGANJ MATHURA(GC) NER                                     | NER    | 03/1997          | 677.97                   | 1062.36                 | 1706.54                     |
| 34              | BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR                       | NFR    | 09/1997          | 1500                     | -                       | 4793.77                     |
| 35              | MUNEERABAD-MAHABOBNAGAR(NL), SCR                                   | SCR    | 04/1997          | 218.24                   | 236.41                  | 544.2                       |
| 36              | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)                             | WCR    | 09/1998          | 247.66                   | -                       | 972.82                      |
| 37              | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR                         | ECR    | 04/1997          | 501.69                   | 335.77                  | 876.49                      |
| 38              | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR                         | NCR    | 04/1999          | 108                      | -                       | 446.52                      |

## LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(SEPTEMBER 2017)

| Sn | Project                                                                         | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|----|---------------------------------------------------------------------------------|--------|------------------|--------------------------|-------------------------|-----------------------------|
| 39 | KATIHAR - JOGBANI (GC)(NEFR)                                                    | NFR    | 09/2001          | 492.98                   | -                       | 918.94                      |
| 40 | GULBARGA-BIDAR, SCR(NL)                                                         | SCR    | 02/1998          | 242.42                   | 369.7                   | 927.68                      |
| 41 | KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)                                         | NER    | 04/1999          | 744.71                   | 744.71                  | 761.7                       |
| 42 | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)                                           | ECR    | 04/1997          | 162.87                   | -                       | 183.72                      |
| 43 | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR                                         | NR     | 03/2002          | 625.3                    | 408.76                  | 841.57                      |
| 44 | TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)                                         | SR     | 09/1995          | 100                      | -                       | 647.64                      |
| 45 | QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)                                 | SR     | 03/1998          | 280                      | -                       | 834.61                      |
| 46 | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR                         | NFR    | 04/2000          | 733                      | -                       | 2344.94                     |
| 47 | TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) | M RTP  | 03/2000          | 1049.69                  | -                       | 3544.3                      |
| 48 | GADWAL - RAICHUR (NL), SCR                                                      | SCR    | 04/1998          | 92.63                    | -                       | 316.64                      |
| 49 | DEOGHAR - SULTANGANJ (INL), ER                                                  | ER     | 04/2000          | 607.09                   | -                       | 613.71                      |
| 50 | JIND-SONEPAT (NL), NR                                                           | NR     | 01/2004          | 238.56                   | -                       | 722.65                      |
| 51 | KHURDA ROAD-BOLANGIR(NL)ECOR                                                    | ECOR   | 04/1994          | 470.21                   | -                       | 899.41                      |
| 52 | RAJATGARH-BARANG(LD), ECR                                                       | RVNL   | 04/1999          | 166.16                   | -                       | 370.37                      |
| 53 | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)                                             | NFR    | 04/2003          | 727.56                   | -                       | 5418.63                     |
| 54 | MAHARAJGANJ-MASRAKH (NL) - NER                                                  | NER    | 04/2003          | 218.19                   | -                       | 356.37                      |
| 55 | ETAWAH-MAINPURI (NL), NCR                                                       | NCR    | 04/1997          | 120                      | -                       | 210.67                      |
| 56 | HATHUA-BHATNI (N L) (NER)                                                       | NER    | 04/2005          | 230.03                   | -                       | 274.67                      |
| 57 | SUKINDA ROAD - ANGUL (NL)(ECOR)                                                 | RVNL   | 04/1998          | 183.23                   | -                       | 392.96                      |
| 58 | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR                               | ECR    | 04/1996          | 332.92                   | 283.95                  | 495.4                       |
| 59 | GOELKERA-MANOHARPUR, (LD)(SER)                                                  | RVNL   | 03/1997          | 261.7                    | -                       | 329.39                      |
| 60 | SALKA ROAD -ANUPNAGAR LINE DOUBLING                                             | RVNL   | 09/2006          | 324.9                    | -                       | 479.68                      |
| 61 | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII' -AGASTIYAMPALLI               | SR     | 09/2007          | 404.19                   | -                       | 957.24                      |



## LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(SEPTEMBER 2017)

| Sn | Project                                                                   | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|----|---------------------------------------------------------------------------|--------|------------------|--------------------------|-------------------------|-----------------------------|
| 62 | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE                         | SR     | 09/2006          | 343.17                   | -                       | 1047.11                     |
| 63 | ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR                        | NFR    | 12/2006          | 170                      | -                       | 439.57                      |
| 64 | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR           | NFR    | 09/2006          | 200                      | -                       | 425.47                      |
| 65 | NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR                  | NFR    | 09/2006          | 300                      | -                       | 921.25                      |
| 66 | UTRATIA-ZAFRABAD, NR (LINE DOUBLING)                                      | NR     | 04/2006          | 325                      | -                       | 618.19                      |
| 67 | AGARTALA SABROOM, NL, NEFR                                                | NFR    | 04/2008          | 813.34                   | -                       | 2351.21                     |
| 68 | BHAIRABI SAIRONG, NL, NEFR                                                | NFR    | 04/2008          | 619.34                   | -                       | 1651.19                     |
| 69 | RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) | SWR    | 04/2007          | 482                      | -                       | 985.32                      |
| 70 | SURATPURA - HANUMANGARH - SRIGANGANAGAR GAUGE CONVERSION (NWR)            | NWR    | 04/2008          | 516.23                   | -                       | 694.13                      |
| 71 | TINPAHAR - SAHIBGANJ (ER)                                                 | ER     | 04/2008          | 167.73                   | -                       | 207.11                      |
| 72 | BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) | ER     | 04/1999          | 207.52                   | -                       | 293.47                      |
| 73 | RATLAM-MHOW-KHANDWA-AKOLA (GC)                                            | WR     | 04/2008          | 603.04                   | -                       | 628.11                      |
| 74 | UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR)                         | WR     | 04/2008          | 1389.62                  | -                       | 1513.78                     |
| 75 | BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)        | WR     | 04/2006          | 117.36                   | 196.95                  | 202.29                      |
| 76 | KATAKHAL TO BHAIRABI                                                      | NFR    | 04/1998          | 227.9                    | -                       | 407.3                       |
| 77 | LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT    | NFR    | 04/1996          | 1676.31                  | -                       | 7041.41                     |
| 78 | BHOJIPUR TANAKPUR VIA PILIBHIT                                            | NER    | 03/2008          | 195.64                   | -                       | 398.89                      |
| 79 | AUNRIHAR MANDUADIH GAZIPUR VARANASI UP                                    | NER    | 03/2012          | 199.75                   | -                       | 210.64                      |
| 80 | VIRAMGAM-SAMAKHIALI (DL)                                                  | WR     | 04/2011          | 446                      | -                       | 590.6                       |
| 81 | VIRAMGAM-SURENDRANAGAR (DL)                                               | WR     | 04/2010          | 279.4                    | -                       | 323.64                      |
| 82 | MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR               | NWR    | 04/2013          | 456                      | -                       | 594.34                      |
| 83 | RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)    | NWR    | 04/2010          | 739.65                   | -                       | 796.25                      |
| 84 | TAMLUK-BASULYA-SUTAHATA DOUBLING                                          | RVNL   | 04/2010          | 171.02                   | -                       | 241.47                      |

## LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(SEPTEMBER 2017)

| Sn                                 | Project                                                                                           | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|------------------------------------|---------------------------------------------------------------------------------------------------|--------|------------------|--------------------------|-------------------------|-----------------------------|
| 85                                 | SAKRI-HASANPUR ROAD (NL)                                                                          | ECOR   | 04/1999          | 175.69                   | -                       | 253.1                       |
| 86                                 | CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC                                                   | SR     | 04/1998          | 271.24                   | -                       | 464.65                      |
| 87                                 | VILLUPURAM-DINDIGUL WITH ELECTRIFICATION                                                          | RVNL   | 04/2008          | 822.39                   | -                       | 1639.7                      |
| 88                                 | CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA                                                        | NFR    | 04/1999          | 895                      | -                       | 1487.59                     |
| 89                                 | NEW COOCHBEHAR TO SAMUKTALA                                                                       | NFR    | 04/2011          | 209.77                   | -                       | 389.45                      |
| 90                                 | CHENGANNUR-CHINGAVANAM                                                                            | SR     | 04/2006          | 191.72                   | -                       | 360.22                      |
| 91                                 | ERNAKULAM-KUMBALAM                                                                                | SR     | 04/2010          | 189.24                   | -                       | 189.35                      |
| 92                                 | NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI | NFR    | 04/1999          | 523.17                   | -                       | 1071.96                     |
| 93                                 | AMBARI FALAKATA TO NEW MAYNAGURI                                                                  | NFR    | 04/2011          | 312.12                   | -                       | 490.99                      |
| 94                                 | KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC                                           | ER     | 04/2010          | 423.66                   | -                       | 456.58                      |
| 95                                 | PEN ROHA DOUBLING                                                                                 | CR     | 04/2007          | 98.74                    | -                       | 312.12                      |
| 96                                 | PANVEL PEN DOUBLING                                                                               | CR     | 04/2006          | 96.16                    | -                       | 268.37                      |
| 97                                 | MUNIRABAD (GINGERA) -RAICHUR NL                                                                   | SWR    | 04/2007          | 179.65                   | -                       | 778.41                      |
| 98                                 | JAGGAYYAPET - MELLACHERUVU                                                                        | SCR    | 04/2007          | 313.24                   | -                       | 342                         |
| 99                                 | JHARSUGUDA-RENGALI DOUBLING                                                                       | ECOR   | 03/2006          | 201                      | -                       | 242.28                      |
| 100                                | DELANG-PURI DOUBLING                                                                              | ECOR   | 03/2011          | 165.16                   | -                       | 224.64                      |
| 101                                | THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM)             | RVNL   | 04/2011          | 190.1                    | -                       | 282.22                      |
| 102                                | HOSADURGA - CHICKJAJUR (28.89 KM)                                                                 | SWR    | 04/2010          | 203.4                    | 203.4                   | 281.02                      |
| 103                                | GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM)                                        | NER    | 04/1997          | 836.26                   | -                       | 1026.65                     |
| 104                                | MUZAFFARPUR-SITAMARHI NEW LINE                                                                    | ECR    | 01/1991          | 332.15                   | -                       | 538.21                      |
| 105                                | RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS                                                     | NFR    | 04/2003          | 4300                     | -                       | 4413.04                     |
| <b>ROAD TRANSPORT AND HIGHWAYS</b> |                                                                                                   |        |                  |                          |                         |                             |
| Sn                                 | Project                                                                                           | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
| 106                                | GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA                                                            | NHAI   | 03/2010          | 1509.1                   | -                       | 3187.19                     |

## LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(SEPTEMBER 2017)

| Sn  | Project                                                                  | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|-----|--------------------------------------------------------------------------|--------|------------------|--------------------------|-------------------------|-----------------------------|
|     | PORT SECTION                                                             |        |                  |                          |                         |                             |
| 107 | SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502                                | NHAI   | 02/2009          | 1693.75                  | -                       | 2675.28                     |
| 108 | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)                              | NHAI   | 05/2009          | 1108                     | -                       | 3882.53                     |
| 109 | INDORE-JHABUA-GUJRAT/MP                                                  | NHAI   | 10/2010          | 1175                     | -                       | 1226.83                     |
| 110 | TALEGAON-AMRAVATI                                                        | NHAI   | 11/2009          | 567                      | -                       | 1055.94                     |
| 111 | CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM                   | NHAI   | 09/2010          | 852                      | -                       | 911.86                      |
| 112 | CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM                           | NHAI   | 11/2010          | 1585                     | -                       | 2284.33                     |
| 113 | MURADABAD-BAREILY                                                        | NHAI   | 04/2010          | 1267                     | -                       | 2664.02                     |
| 114 | PUNE-SATARA(NH-4)                                                        | NHAI   | 10/2010          | 1724.55                  | -                       | 2051.04                     |
| 115 | INDORE-DEWAS(NH-3)                                                       | NHAI   | 11/2010          | 325                      | -                       | 471.04                      |
| 116 | ROHTAK-BAWAL                                                             | NHAI   | 05/2011          | 650                      | -                       | 832.39                      |
| 117 | GHAZIABAD-ALIGARH NH-91                                                  | NHAI   | 02/2011          | 1141                     | -                       | 1948.72                     |
| 118 | SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 | NHAI   | 09/2011          | 1250                     | -                       | 1329.1                      |
| 119 | KANDLA - MUNDRA PORT                                                     | NHAI   | 01/2011          | 953.88                   | -                       | 975.12                      |
| 120 | TIRUPATI - TIRUTHANI - CHENNAI                                           | NHAI   | 04/2011          | 571                      | -                       | 622.89                      |
| 121 | JORBAT - BARAPANI                                                        | NHAI   | 01/2011          | 536                      | -                       | 672.72                      |
| 122 | SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547          | NHAI   | 11/2011          | 1535                     | -                       | 3093.77                     |
| 123 | MUZAFFARNAGAR-HARIDWAR                                                   | NHAI   | 09/2011          | 754                      | -                       | 1101.13                     |
| 124 | 4-LANING OF FARAKA-RAIGANJ                                               | NHAI   | 02/2011          | 1078.84                  | -                       | 2391.07                     |
| 125 | 4-LANING OF BRAHAMPORE-FARAKA                                            | NHAI   | 02/2011          | 998.79                   | -                       | 1930.5                      |
| 126 | 6-LANING OF DHANKUNI-KHARAGPUR SECTION                                   | NHAI   | 04/2012          | 1396.18                  | -                       | 2694.55                     |
| 127 | 2-LANING WITH PS RAIBAREILI TO ALLAHABAD                                 | NHAI   | 07/2012          | 291.36                   | -                       | 320.46                      |
| 128 | ETAWAH CHAKERI                                                           | NHAI   | 03/2013          | 1573                     | -                       | 1850                        |

## LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(SEPTEMBER 2017)

| Sn  | Project                                                              | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|-----|----------------------------------------------------------------------|--------|------------------|--------------------------|-------------------------|-----------------------------|
| 129 | AHMEDABAD TO VADODARA SECTION                                        | NHAI   | 01/2013          | 2125.24                  | -                       | 4659.71                     |
| 130 | DELHI AGRA APPROVED LENGTH 180.0 KM                                  | NHAI   | 10/2012          | 1928.22                  | -                       | 2488                        |
| 131 | WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50      | NHAI   | 05/2013          | 1348.2                   | -                       | 1788.75                     |
| 132 | 4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9                | NHAI   | 04/2014          | 1266.6                   | -                       | 1360                        |
| 133 | 2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 | NHAI   | 04/2014          | 351.34                   | -                       | 378.36                      |
| 134 | 2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI                   | NHAI   | 04/2014          | 495.78                   | -                       | 509.65                      |
| 135 | 4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211                        | NHAI   | 01/2015          | 972.5                    | -                       | 1458.72                     |
| 136 | NAGPUR - KONDHALI                                                    | NHAI   | 09/2005          | 168                      | -                       | 279.92                      |
| 137 | GURGAON - KOTPUTLI - JAIPUR (SIX LANE)                               | NHAI   | 02/2008          | 1673.7                   | -                       | 3145.92                     |
| 138 | FOUR LANING OF KAITHAL - RAJASTHAN BORDER                            | NHAI   | 07/2015          | 1393                     | -                       | 2151.12                     |
| 139 | FOUR LANING OF JABALPUR - LAKHNADON                                  | NHAI   | 03/2015          | 928.83                   | -                       | 1254.37                     |
| 140 | FOUR LANING OF GWALIOR-SHIVPURI                                      | NHAI   | 05/2013          | 1055                     | -                       | 1328.85                     |
| 141 | FOUR LANING OF AURANGABAD - YEDISHI                                  | NHAI   | 07/2015          | 1871.34                  | -                       | 2601.04                     |
| 142 | SIX-LANING OF BARWA ADDA-PANAGARH                                    | NHAI   | 04/2014          | 1665                     | -                       | 2091.52                     |
| 143 | TRICHY - KARUR                                                       | NHAI   | 03/2007          | 516                      | -                       | 761.19                      |

## SHIPPING AND PORTS

| Sn  | Project                                                                                              | Agency      | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|-----|------------------------------------------------------------------------------------------------------|-------------|------------------|--------------------------|-------------------------|-----------------------------|
| 144 | RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST                                        | RVNL        | 03/2007          | 245.67                   | -                       | 350.68                      |
| 145 | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB | MUMBAI PORT | 01/2007          | 366.39                   | -                       | 411.12                      |

## STEEL

| Sn  | Project                                                        | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|-----|----------------------------------------------------------------|--------|------------------|--------------------------|-------------------------|-----------------------------|
| 146 | EXPANSION OF BHILAI STEEL PLANT                                | SAIL   | 08/2010          | 17265                    | -                       | 17970.98                    |
| 147 | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V | HSCL   | 03/2007          | 149.73                   | 173                     | 178.65                      |
| 148 | CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA       | HSCL   | 05/2005          | 768.88                   | 1070.97                 | 1085.64                     |

## LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(SEPTEMBER 2017)

| Sn                       | Project                      | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
|--------------------------|------------------------------|--------|------------------|--------------------------|-------------------------|-----------------------------|
| <b>URBAN DEVELOPMENT</b> |                              |        |                  |                          |                         |                             |
| Sn                       | Project                      | Agency | Date of Approval | Cost Original (Rs.crore) | Cost Revised (Rs.crore) | Cumm Expenditure (Rs.crore) |
| 149                      | BANGALORE METRO RAIL PROJECT | M RTP  | 05/2006          | 6395                     | 13845.01                | 14200.11                    |

## Details of Projects Ahead of Schedule w.r.t. Original Schedule

### Annexure - III

| Costing Rs.150 Crore and above |                                                                                                   |                               |                                     |                              |                                    | (September 2017)                   |             |
|--------------------------------|---------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                |                                                                                                   |                               |                                     |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                           | Project                                                                                           | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                              | 2                                                                                                 | 3                             | 4                                   | 5                            | 6                                  | 7                                  | 8           |
|                                |                                                                                                   |                               |                                     |                              |                                    |                                    |             |
|                                | <u>PETROLEUM</u>                                                                                  |                               |                                     |                              |                                    |                                    |             |
| 1                              | PARADIP HYDERABAD PIPELINE<br>- [N16000194]                                                       | 1/2015                        | 2,321.00<br>-                       | 2,321.00                     | 53.61                              | 12/2020<br>-                       | 08/2020     |
|                                | Total                                                                                             |                               | 2,321.00<br>-                       | 2,321.00                     | 53.61                              |                                    |             |
|                                |                                                                                                   |                               |                                     |                              |                                    |                                    |             |
|                                | <u>POWER</u>                                                                                      |                               |                                     |                              |                                    |                                    |             |
| 2                              | SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION<br>- [N18000186]         | 3/2015                        | 550.06<br>-                         | 550.06                       | 462.17                             | 03/2018<br>-                       | 09/2017     |
|                                | Total                                                                                             |                               | 550.06<br>-                         | 550.06                       | 462.17                             |                                    |             |
|                                |                                                                                                   |                               |                                     |                              |                                    |                                    |             |
|                                | <u>PETROLEUM</u>                                                                                  |                               |                                     |                              |                                    |                                    |             |
| 3                              | MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III<br>- [N16000197]                                  | 11/2014                       | 6,068.80<br>6,068.80                | 5,296.93                     | 4,127.27                           | 04/2019<br>03/2019                 | 03/2019     |
| 4                              | GAMJI REDEVELOPMENT PROJECT<br>- [N16000202]                                                      | 5/2015                        | 1,671.22<br>567.22                  | 567.22                       | 347.69                             | 11/2019<br>12/2018                 | 12/2018     |
|                                | Total                                                                                             |                               | 7,740.02<br>-                       | 5,864.15                     | 4,474.96                           |                                    |             |
|                                |                                                                                                   |                               |                                     |                              |                                    |                                    |             |
|                                | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                |                               |                                     |                              |                                    |                                    |             |
| 5                              | FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)<br>- [N24000498]                              | 6/2016                        | 667.00<br>-                         | 667.00                       | 113.68                             | 07/2018<br>-                       | 06/2018     |
|                                | Total                                                                                             |                               | 667.00<br>-                         | 667.00                       | 113.68                             |                                    |             |
|                                |                                                                                                   |                               |                                     |                              |                                    |                                    |             |
|                                | <u>POWER</u>                                                                                      |                               |                                     |                              |                                    |                                    |             |
| 6                              | TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A)<br>- [N18000207]           | 1/2016                        | 244.19<br>-                         | 244.19                       | 108.85                             | 07/2018<br>-                       | 11/2017     |
| 7                              | CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM<br>- [N18000209] | 1/2016                        | 162.11<br>-                         | 162.11                       | 113.09                             | 05/2018<br>-                       | 12/2017     |
|                                | Total                                                                                             |                               | 406.30<br>-                         | 406.30                       | 221.94                             |                                    |             |
|                                |                                                                                                   |                               |                                     |                              |                                    |                                    |             |
|                                | <u>PETROLEUM</u>                                                                                  |                               |                                     |                              |                                    |                                    |             |
| 8                              | RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH<br>- [N16000216]                            | 1/2016                        | 247.52<br>-                         | 247.52                       | 53.32                              | 02/2019<br>-                       | 12/2018     |
|                                | Total                                                                                             |                               | 247.52<br>-                         | 247.52                       | 53.32                              |                                    |             |
|                                |                                                                                                   |                               |                                     |                              |                                    |                                    |             |

## Details of Projects Ahead of Schedule w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                               |                               |                                     |                              |                                    | (September 2017)                   |             |
|--------------------------------|---------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                |                                                                                                               |                               |                                     |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                           | Project                                                                                                       | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                              | 2                                                                                                             | 3                             | 4                                   | 5                            | 6                                  | 7                                  | 8           |
|                                | <u>RAILWAYS</u>                                                                                               |                               |                                     |                              |                                    |                                    |             |
| 9                              | BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.<br>- [N22000381                                          | 4/2015                        | 1,172.92<br>-                       | 1,172.92                     | 74.32                              | 03/2021<br>-                       | 03/2020     |
|                                | Total                                                                                                         |                               | 1,172.92<br>-                       | 1,172.92                     | 74.32                              |                                    |             |
|                                |                                                                                                               |                               |                                     |                              |                                    |                                    |             |
|                                | <u>PETROLEUM</u>                                                                                              |                               |                                     |                              |                                    |                                    |             |
| 10                             | CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP<br>- [N16000226                                       | 2/2016                        | 356.00<br>-                         | 356.00                       | 64.84                              | 05/2019<br>-                       | 12/2018     |
| 11                             | DEVELOPMENT PLAN OF CBM - BOKARO BLOCK<br>- [N16000239                                                        | 12/2015                       | 658.62<br>910.23                    | 910.23                       | 2.30                               | 03/2023<br>03/2022                 | 03/2022     |
| 12                             | BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL<br>- [N16000252                                      | 5/2016                        | 664.00<br>-                         | 664.00                       | 137.54                             | 12/2020<br>-                       | 02/2020     |
|                                | Total                                                                                                         |                               | 1,678.62<br>-                       | 1,930.23                     | 204.68                             |                                    |             |
|                                |                                                                                                               |                               |                                     |                              |                                    |                                    |             |
|                                | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                            |                               |                                     |                              |                                    |                                    |             |
| 13                             | DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660 | 3/2017                        | 296.19<br>-                         | 254.00                       | -                                  | 03/2020<br>-                       | 05/2019     |
|                                | Total                                                                                                         |                               | 296.19<br>-                         | 254.00                       | .00                                |                                    |             |
|                                |                                                                                                               |                               |                                     |                              |                                    |                                    |             |
|                                | <u>PETROLEUM</u>                                                                                              |                               |                                     |                              |                                    |                                    |             |
| 14                             | MUMBAI REFINERY EXPANSION PROJECT<br>- [N16000281                                                             | 9/2015                        | 4,199.00                            | 4,199.00                     | 194.97                             | 03/2020<br>-                       | 07/2019     |
|                                | Total                                                                                                         |                               | 4,199.00<br>-                       | 4,199.00                     | 194.97                             |                                    |             |
|                                |                                                                                                               |                               |                                     |                              |                                    |                                    |             |
|                                | Grand Total                                                                                                   |                               | 19,278.63                           | 17,612.18                    | 5,853.65                           |                                    |             |

## Details of On Schedule Projects w.r.t. Original Schedule

### Annexure - IV

| Costing Rs.150 Crore and above |                                                                                    |                               |                                    |                              |                                    | (September 2017)                   |             |
|--------------------------------|------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                |                                                                                    |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                           | Project                                                                            | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                              | 2                                                                                  | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
|                                | <u>COAL</u>                                                                        |                               |                                    |                              |                                    |                                    |             |
| 1                              | AMADAND OPENCAST EXPANSION PROJECT<br>- [N06000148]                                | 3/2016                        | 869.44<br>-                        | 869.44                       | 109.31                             | 03/2021<br>-                       | 03/2021     |
| 2                              | ADASA UG TO OC<br>- [N06000133]                                                    | 8/2015                        | 288.90<br>-                        | 288.90                       | -                                  | 03/2023<br>-                       | 03/2023     |
| 3                              | MALACHUA OPENCAST PROJECT<br>- [N06000139]                                         | 10/2015                       | 488.33<br>-                        | 488.33                       | 1.13                               | 03/2023<br>-                       | 03/2023     |
| 4                              | BHATADI EXPANSION OC MINE<br>- [N06000150]                                         | 2/2016                        | 304.52<br>-                        | 304.52                       | 124.12                             | 03/2019<br>-                       | 03/2019     |
| 5                              | GARJANBAHAL OCP<br>- [N06000117]                                                   | 11/2014                       | 1,375.38<br>-                      | 1,375.38                     | 352.44                             | 03/2021<br>-                       | 03/2021     |
| 6                              | AMALGAMATED YEKONA-I YEKONA-II<br>- [N06000132]                                    | 8/2015                        | 727.28<br>-                        | 727.28                       | 228.99                             | 03/2025<br>-                       | 03/2025     |
| 7                              | KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL)<br>- [N06000091] | 6/2011                        | 1,131.28<br>-                      | 1,131.28                     | 431.09                             | 03/2018<br>-                       | 03/2018     |
| 8                              | KANCHAN OC EXPANSION<br>- [N06000125]                                              | 12/2014                       | 371.04<br>-                        | 371.04                       | 34.53                              | 03/2021<br>-                       | 03/2021     |
| 9                              | SIARMAL OCP (40.00MTY)<br>- [N06000113]                                            | 5/2014                        | 3,756.36<br>-                      | 3,756.36                     | 682.14                             | 03/2026<br>-                       | 03/2026     |
| 10                             | HURA - C OC (3 MTY)<br>- [N06000143]                                               | 10/2015                       | 359.69<br>-                        | 359.69                       | 7.54                               | 03/2022<br>-                       | 03/2022     |
| 11                             | MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE<br>- [N06000142]                         | 11/2015                       | 498.42<br>-                        | 498.42                       | 7.72                               | 03/2020<br>-                       | 03/2020     |
| 12                             | SINGHORI OC MINE<br>- [N06000130]                                                  | 6/2015                        | 205.49<br>-                        | 205.49                       | 65.88                              | 03/2020<br>-                       | 03/2020     |
| 13                             | JHANJRA COMBINED PR(3.50 MTY)<br>- [N06000020]                                     | 11/2015                       | 602.86<br>-                        | 602.86                       | 268.77                             | 03/2022<br>-                       | 03/2022     |
| 14                             | PENGANGA OCP(REVISED)<br>- [N06000066]                                             | 9/2014                        | 441.82<br>-                        | 441.82                       | 174.29                             | 03/2020<br>-                       | 03/2020     |
| 15                             | VIJAY WEST OPENCAST PROJECT<br>- [N06000158]                                       | 5/2017                        | 976.95<br>-                        | 976.95                       | 75.96                              | 03/2026<br>-                       | 03/2026     |
| 16                             | DHANKASA UG (1.00 MTY)<br>- [N06000155]                                            | 9/2016                        | 458.07<br>-                        | 458.07                       | -                                  | 03/2022<br>-                       | 03/2022     |
| 17                             | KUSMUNDA EXPN.OCP(SECL)(15-50)MTY<br>- [N06000008]                                 | 8/2013                        | 7,612.33<br>-                      | 7,612.33                     | 1,271.99                           | 03/2023<br>-                       | 03/2023     |
| 18                             | RAJNAGAR OCP RPR (1.70 MTY)<br>- [N06000124]                                       | 12/2014                       | 357.80<br>-                        | 357.80                       | 114.37                             | 03/2021<br>-                       | 03/2021     |
| 19                             | BIJARI OC RCE (1.50 MTY)<br>- [N06000111]                                          | 5/2014                        | 164.49<br>-                        | 164.49                       | 46.52                              | 03/2020<br>-                       | 03/2020     |
| 20                             | CHHAL OC SEAM -III (6.00 MTY)<br>- [N06000104]                                     | 12/2013                       | 610.63<br>-                        | 610.63                       | 29.03                              | 03/2022<br>-                       | 03/2022     |
| 21                             | BHANEGAON OC<br>- [N06000121]                                                      | 2/2015                        | 187.94<br>-                        | 187.94                       | 72.23                              | 03/2023<br>-                       | 03/2023     |
| 22                             | MADANNAGAR OPENCAST PROJECT<br>- [N06000140]                                       | 10/2015                       | 1,875.32<br>-                      | 1,875.32                     | -                                  | 03/2024<br>-                       | 03/2024     |



## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                      |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
|--------------------------------|----------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
| S.No                           | Project                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                              | 2                                                                    | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 23                             | AMRAPALI OC(12MTY)<br>- [N06000103]                                  | 2/2012                        | 858.11<br>-                        | 858.11                       | 175.44                             | 03/2020<br>-                       | 03/2020     |
| 24                             | GOKUL<br>- [N06000120]                                               | 11/2014                       | 267.67<br>-                        | 267.67                       | 203.98                             | 03/2018<br>-                       | 03/2018     |
| 25                             | BATURA OCP (2.0 MTY)<br>- [N06000049]                                | 8/2015                        | 1,186.64<br>-                      | 1,186.64                     | 54.40                              | 03/2023<br>-                       | 03/2023     |
| 26                             | BASUNDHARA (WEST) OC EXTN(7.00 MTY)<br>- [N06000112]                 | 5/2014                        | 479.15<br>-                        | 479.15                       | 20.80                              | 03/2019<br>-                       | 03/2019     |
| 27                             | KAKATIYAKHANI OPENCAST-2 PROJECT<br>- [N06000129]                    | 5/2015                        | 397.09<br>-                        | 442.42                       | 19.94                              | 03/2019<br>-                       | 03/2019     |
| 28                             | HADLA LIGNITE MINE PROJECT(1.90 MTPA)<br>- [N06000144]               | 3/2015                        | 522.45<br>-                        | 522.45                       | 5.65                               | 09/2019<br>-                       | 09/2019     |
| 29                             | DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)<br>- [N06000157]              | 2/2017                        | 328.00<br>-                        | 328.00                       | 45.31                              | 03/2021<br>-                       | 03/2021     |
| 30                             | DINESH OCP<br>- [N06000118]                                          | 11/2014                       | 611.16<br>-                        | 611.16                       | 360.21                             | 03/2020<br>-                       | 03/2020     |
| 31                             | NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW<br>- [N06000152] | 7/2016                        | 17,237.00<br>-                     | 17,237.80                    | 1,116.07                           | 11/2021<br>-                       | 11/2021     |
| 32                             | DURGAPUR OPENCAST PROJECT<br>- [N06000136]                           | 2/2015                        | 916.24<br>-                        | 916.24                       | 0.71                               | 03/2023<br>-                       | 03/2023     |
| 33                             | KULDA EXPN OC. (5.00 MTY)<br>- [N06000115]                           | 6/2014                        | 289.03<br>-                        | 289.03                       | -                                  | 03/2018<br>-                       | 03/2018     |
| 34                             | NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)<br>- [N06000106]    | 2/2014                        | 555.52<br>-                        | 555.52                       | 4.57                               | 03/2021<br>-                       | 03/2021     |
| 35                             | BATURA HIGHWALL PROJECT<br>- [N06000134]                             | 7/2015                        | 231.92<br>-                        | 231.92                       | -                                  | 03/2022<br>-                       | 03/2022     |
| 36                             | NEW MAJRI UG TO OC<br>- [N06000128]                                  | 5/2015                        | 295.56<br>-                        | 295.56                       | 85.80                              | 03/2019<br>-                       | 03/2019     |
| 37                             | AMALGAMATED GONDEGAON GHATROHAN OC<br>- [N06000149]                  | 2/2016                        | 198.68<br>-                        | 198.68                       | 30.32                              | 03/2019<br>-                       | 03/2019     |
| 38                             | COAL PROJECT NAME JAMUNIA UG (0.84 MTY)<br>- [N06000153]             | 7/2016                        | 409.87<br>-                        | 409.87                       | 12.08                              | 03/2022<br>-                       | 03/2022     |
| 39                             | GEVRA EXPANSION OCP (SECL) (35-70) MTY<br>- [060100093]              | 6/2010                        | 11,816.40<br>-                     | 11,816.40                    | 2,485.40                           | 03/2023<br>-                       | 03/2023     |
| 40                             | KAMPTEE DEEP OC MINE<br>- [N06000141]                                | 11/2015                       | 277.65<br>-                        | 277.65                       | 0.13                               | 03/2021<br>-                       | 03/2021     |
| 41                             | PELMA OCP(15.00MTY)<br>- [N06000045]                                 | 11/2014                       | 1,624.59<br>-                      | 1,624.59                     | 5.73                               | 03/2023<br>-                       | 03/2023     |
| 42                             | JAGANNATH RE-ORGANISATION OC.(6.00 MTY)<br>- [N06000114]             | 5/2014                        | 337.66<br>-                        | 337.66                       | 29.74                              | 03/2019<br>-                       | 03/2019     |
| 43                             | BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)<br>- [N06000145]            | 3/2015                        | 513.63<br>-                        | 513.63                       | 167.04                             | 12/2019<br>-                       | 12/2019     |
| 44                             | AMRITDHARA OC PROJECT<br>- [N06000122]                               | 2/2015                        | 481.60<br>-                        | 481.60                       | -                                  | 03/2023<br>-                       | 03/2023     |
| 45                             | AMALGAMATED PAUNI-II III OC MINE<br>- [N06000131]                    | 6/2015                        | 483.69<br>-                        | 483.69                       | 71.98                              | 03/2021<br>-                       | 03/2021     |
| 46                             | AMGAON OPENCAST PROJECT RCE<br>- [N06000135]                         | 7/2015                        | 316.10<br>-                        | 316.10                       | 34.94                              | 03/2020<br>-                       | 03/2020     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                             |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
|--------------------------------|-------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
| S.No                           | Project                                                                                                     | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                              | 2                                                                                                           | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 47                             | MAKARDHOKRA I OC<br>- [N06000119]                                                                           | 9/2014                        | 266.23<br>-                        | 266.23                       | 138.36                             | 03/2021<br>-                       | 03/2021     |
| 48                             | KALYANIKHANI 6 INCLINE PROJECT<br>- [N06000147]                                                             | 12/2015                       | 477.65<br>-                        | 477.65                       | -                                  | 03/2020<br>-                       | 03/2020     |
| 49                             | NILJAI EXPANSION (DEEP) OC (3.5 MTY)<br>- [N06000154]                                                       | 8/2016                        | 319.76<br>-                        | 319.76                       | -                                  | 03/2022<br>-                       | 03/2022     |
| 50                             | AMERA OC RCE<br>- [N06000123]                                                                               | 2/2015                        | 335.97<br>-                        | 335.97                       | 49.00                              | 03/2018<br>-                       | 03/2018     |
|                                | Total                                                                                                       |                               | 65,699.36<br>-                     | 65,745.49                    | 9,215.65                           |                                    |             |
|                                |                                                                                                             |                               |                                    |                              |                                    |                                    |             |
|                                | <u>DEFENCE PRODUCTION</u>                                                                                   |                               |                                    |                              |                                    |                                    |             |
| 51                             | CONSTRUCTION WORKS PHASE 3B<br>- [N39000002]                                                                | 12/2016                       | 285.95<br>286.00                   | 296.05                       | 29.91                              | 08/2020<br>-                       | 08/2020     |
| 52                             | CONSTRUCTION WORKS PHASE 4<br>- [N39000001]                                                                 | 12/2016                       | 167.69<br>168.00                   | 172.99                       | 22.26                              | 05/2018<br>-                       | 05/2018     |
|                                | Total                                                                                                       |                               | 453.64<br>-                        | 469.04                       | 52.17                              |                                    |             |
|                                |                                                                                                             |                               |                                    |                              |                                    |                                    |             |
|                                | <u>FERTILISERS</u>                                                                                          |                               |                                    |                              |                                    |                                    |             |
| 53                             | GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL.<br>- [N08000010]                    | 2/2016                        | 482.85<br>-                        | 494.00                       | 400.18                             | 12/2017<br>-                       | 12/2017     |
|                                | Total                                                                                                       |                               | 482.85<br>-                        | 494.00                       | 400.18                             |                                    |             |
|                                |                                                                                                             |                               |                                    |                              |                                    |                                    |             |
|                                | <u>HEALTH AND FAMILY WELFARE</u>                                                                            |                               |                                    |                              |                                    |                                    |             |
| 54                             | CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR<br>- [N21000011]                                         | 9/2014                        | 505.58<br>-                        | 505.58                       | 202.00                             | 03/2018<br>-                       | 03/2018     |
| 55                             | NCI AIIMS JHAJJAR RESIDENTIAL HARYANA<br>- [N21000014]                                                      | 7/2016                        | 312.99<br>-                        | 312.99                       | 120.00                             | 08/2018<br>-                       | 08/2018     |
| 56                             | CNCI KOLKATA WEST BENGAL<br>- [N21000015]                                                                   | 8/2016                        | 244.00<br>-                        | 244.00                       | 70.00                              | 09/2018<br>-                       | 09/2018     |
|                                | Total                                                                                                       |                               | 1,062.57<br>-                      | 1,062.57                     | 392.00                             |                                    |             |
|                                |                                                                                                             |                               |                                    |                              |                                    |                                    |             |
|                                | <u>MINES</u>                                                                                                |                               |                                    |                              |                                    |                                    |             |
| 57                             | UTKAL D AND E COAL BLOCK<br>- [N10000011]                                                                   | 5/2016                        | 534.00<br>-                        | 534.00                       | 157.34                             | 01/2020<br>-                       | 01/2020     |
| 58                             | 5TH STREAM ALUMINA REFINERY EXPANSION PROJECT<br>- [N10000010]                                              | 12/2014                       | 5,540.00<br>-                      | 5,540.00                     | 0.31                               | 04/2021<br>-                       | 04/2021     |
|                                | Total                                                                                                       |                               | 6,074.00<br>-                      | 6,074.00                     | 157.65                             |                                    |             |
|                                |                                                                                                             |                               |                                    |                              |                                    |                                    |             |
|                                | <u>PETROLEUM</u>                                                                                            |                               |                                    |                              |                                    |                                    |             |
| 59                             | JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE<br>- [N16000195] | 2/2015                        | 890.00<br>-                        | 887.00                       | 220.84                             | 10/2019<br>-                       | 10/2019     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                      |                               |                                    |                              |                                    | (September 2017)                   |             |
|--------------------------------|----------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                |                                                                                                                      |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                           | Project                                                                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                              | 2                                                                                                                    | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 60                             | CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE<br>- [N16000233]                                                        | 4/2016                        | 327.78<br>-                        | 200.00                       | 14.44                              | 04/2018<br>-                       | 04/2018     |
| 61                             | LAYING OF VIJAI PUR-AURAIYA PIPELINE SECTION OF VIJAI PUR-AURAIYA-PHULPUR PIPELINE PROJECT<br>[N16000271]            | 7/2015                        | 2,881.40<br>-                      | 2,881.40                     | 5.67                               | 12/2019<br>-                       | 12/2019     |
| 62                             | DIESEL HYDROTREATOR<br>- [N16000207]                                                                                 | 7/2015                        | 1,031.37<br>-                      | 1,031.37                     | 305.91                             | 01/2018<br>-                       | 01/2018     |
| 63                             | LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS<br>- [N16000213]                                    | 12/2015                       | 3,190.69<br>-                      | 3,247.19                     | 839.54                             | 04/2018<br>04/2018                 | 04/2018     |
| 64                             | SITARGANJ LPG PROJECT<br>- [N16000282]                                                                               | 2/2017                        | 160.10<br>-                        | 160.10                       | 20.22                              | 02/2020<br>-                       | 02/2020     |
| 65                             | LPG BP PROJECT KHORDHA<br>- [N16000283]                                                                              | 12/2016                       | 161.59<br>-                        | 161.59                       | 28.80                              | 12/2019<br>-                       | 12/2019     |
| 66                             | INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY<br>[N16000284]               | 9/2016                        | 208.35<br>-                        | 208.35                       | 16.93                              | 07/2020<br>-                       | 07/2020     |
| 67                             | NAWAGAM-KOYALI PIPELINE PROJECT<br>- [N16000211]                                                                     | 11/2014                       | 195.63<br>-                        | 187.10                       | 139.30                             | 09/2018<br>09/2018                 | 09/2018     |
| 68                             | GAIL GAS LTD BENGALURU CGD PROJECT<br>- [N16000210]                                                                  | 2/2015                        | 749.00<br>-                        | 749.00                       | 468.00                             | 02/2020<br>-                       | 02/2020     |
| 69                             | ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE<br>[N16000269]               | 1/2015                        | 342.00<br>-                        | 342.00                       | -                                  | 03/2021<br>-                       | 03/2021     |
| 70                             | MOTIHARI AMLEKHGANJ PIPELINE<br>- [N16000254]                                                                        | 9/2015                        | 324.00<br>-                        | 324.00                       | 1.39                               | 06/2020<br>-                       | 06/2020     |
| 71                             | ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE<br>- [N16000268] | 5/2016                        | 348.00<br>-                        | 348.00                       | 0.05                               | 01/2021<br>-                       | 01/2021     |
| 72                             | PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I<br>- [N16000072]                                                             | 3/2015                        | 3,957.00<br>-                      | 3,397.00                     | 1,311.80                           | 12/2018<br>-                       | 12/2018     |
| 73                             | HALDIA BARAUNI PRODUCT PIPELINE<br>- [N16000251]                                                                     | 4/2016                        | 1,021.00<br>-                      | 1,021.00                     | 6.18                               | 12/2020<br>-                       | 12/2020     |
| 74                             | PARADIP HALDIA DURGAPUR LPG PIPELINE<br>- [N16000148]                                                                | 2/2011                        | 913.00<br>-                        | 1,330.00                     | 953.98                             | 06/2018<br>-                       | 06/2018     |
| 75                             | INDMAX PROJECT AT BONGAIGAON REFINERY<br>- [N16000243]                                                               | 2/2016                        | 2,582.00<br>-                      | 2,582.00                     | 193.27                             | 11/2019<br>-                       | 11/2019     |
| 76                             | KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT<br>- [N16000247]                                                          | 3/2016                        | 34,012.00<br>-                     | 34,012.00                    | 252.02                             | 06/2020<br>06/2020                 | 06/2020     |
| 77                             | REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM<br>- [N16000270]                                                   | 7/2014                        | 247.00<br>-                        | 247.00                       | -                                  | 03/2021<br>-                       | 03/2021     |
| 78                             | AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR<br>- [N16000193]   | 1/2015                        | 1,823.00<br>-                      | 1,823.00                     | 15.19                              | 12/2020<br>-                       | 12/2020     |
| 79                             | INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY<br>[N16000260]              | 2/2016                        | 554.00<br>-                        | 554.00                       | 24.30                              | 02/2020<br>-                       | 02/2020     |
| 80                             | MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY<br>- [N16000263]                              | 2/2016                        | 3,313.00<br>-                      | 3,313.00                     | 62.82                              | 02/2020<br>-                       | 02/2020     |
| 81                             | KOYALI AHMEDNAGAR SOLAPUR PIPELINE<br>- [N16000249]                                                                  | 5/2016                        | 1,945.00<br>-                      | 1,945.00                     | 17.11                              | 08/2021<br>-                       | 08/2021     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                         |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
|--------------------------------|-------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
| S.No                           | Project                                                                                                                 | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                              | 2                                                                                                                       | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 82                             | DHAMRA-ANGUL PIPELINE PROJECT<br>- [N16000272]                                                                          | 3/2017                        | 2,253.00<br>-                      | 2,253.00                     | 8.12                               | 12/2019<br>-                       | 12/2019     |
| 83                             | BSVI UPGRADATION<br>- [N16000257]                                                                                       | 9/2016                        | 1,810.00<br>1,810.00               | 1,810.00                     | 46.43                              | 12/2019<br>-                       | 12/2019     |
| 84                             | CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU<br>- [N16000255]                                     | 5/2015                        | 224.00<br>207.00                   | 207.25                       | 39.64                              | 04/2019<br>-                       | 04/2019     |
| 85                             | FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG<br>- [N16000280]                                            | 4/2017                        | 420.76<br>-                        | 420.76                       | -                                  | 09/2018<br>09/2018                 | 09/2018     |
| 86                             | MMPL PIPELINE REROUTING PROJECT<br>- [N16000261]                                                                        | 4/2013                        | 449.58<br>-                        | 449.58                       | 95.57                              | 12/2019<br>-                       | 12/2019     |
| 87                             | DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT<br>- [N16000236]     | 6/2016                        | 423.00<br>-                        | 423.00                       | 89.60                              | 08/2019<br>-                       | 08/2019     |
| 88                             | ADDITIONAL FACILITIES AT MANMAD FOR COVERION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE<br>- [N16000267]       | 5/2016                        | 212.00<br>-                        | 212.00                       | 0.08                               | 01/2021<br>-                       | 01/2021     |
| 89                             | ANKLESHWAR BARODA PIPELINE PROJECT<br>- [N16000232]                                                                     | 7/2014                        | 199.95<br>-                        | 199.95                       | 119.90                             | 03/2018<br>-                       | 03/2018     |
| 90                             | LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY<br>- [N16000264]                           | 5/2015                        | 337.06<br>-                        | 337.06                       | 17.88                              | 08/2018<br>-                       | 08/2018     |
| 91                             | ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE<br>- [N16000253]                     | 5/2016                        | 4,497.00<br>-                      | 4,497.00                     | 23.38                              | 12/2018<br>-                       | 12/2018     |
| 92                             | BOKARO-ANGUL PIPELINE PROJECT<br>- [N16000274]                                                                          | 3/2017                        | 3,212.00<br>-                      | 3,212.00                     | 0.29                               | 12/2020<br>-                       | 12/2020     |
| 93                             | FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY<br>- [N16000248]                                    | 7/2015                        | 822.66<br>-                        | 822.66                       | 223.14                             | 11/2018<br>-                       | 11/2018     |
| 94                             | PIPELINE NETWORK PROJECT GELEKI, ASSAM<br>- [N16000278]                                                                 | 7/2016                        | 249.85<br>250.00                   | 244.70                       | -                                  | 05/2020<br>-                       | 05/2020     |
| 95                             | VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT<br>- [N16000237]                                    | 9/2016                        | 407.00<br>-                        | 407.00                       | 27.20                              | 09/2019<br>-                       | 09/2019     |
| 96                             | MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION<br>- [N16000238]                                       | 9/2016                        | 1,879.00<br>-                      | 1,879.00                     | 168.33                             | 06/2020<br>-                       | 06/2020     |
| 97                             | VISAKH REFINERY MODERNISATION PROJECT<br>- [N16000235]                                                                  | 7/2016                        | 20,928.00<br>-                     | 20,928.00                    | 540.49                             | 07/2020<br>-                       | 07/2020     |
| 98                             | PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)<br>- [N16000258]                                                    | 5/2016                        | 406.00<br>-                        | 406.00                       | 0.50                               | 10/2020<br>-                       | 10/2020     |
| 99                             | BRANCH PIPELINE OF PAJPL TO UNA<br>- [N16000250]                                                                        | 2/2016                        | 151.00<br>-                        | 151.00                       | 28.72                              | 09/2019<br>-                       | 09/2019     |
| 100                            | ENNORE TERMINAL<br>- [N16000224]                                                                                        | 8/2014                        | 393.00<br>-                        | 393.00                       | 198.63                             | 04/2018<br>-                       | 04/2018     |
| 101                            | ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE<br>- [N16000276] | 5/2016                        | 261.00<br>-                        | 261.00                       | 0.05                               | 01/2021<br>-                       | 01/2021     |
| 102                            | DOBHI-DURGAPUR PIPELINE PROJECT<br>- [N16000273]                                                                        | 3/2017                        | 2,250.00<br>-                      | 2,250.00                     | 3.20                               | 12/2019<br>-                       | 12/2019     |
| 103                            | PALAKKAD LPG PLANT<br>- [N16000225]                                                                                     | 2/2015                        | 184.00<br>-                        | 184.00                       | 77.07                              | 12/2017<br>-                       | 12/2017     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                       |                               |                                    |                              |                                    | (September 2017)                   |             |
|--------------------------------|-----------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                |                                                                                                                       |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                           | Project                                                                                                               | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                              | 2                                                                                                                     | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 104                            | DURGAPUR-HALDIA PIPELINE PROJECT<br>- [N16000275]                                                                     | 3/2017                        | 1,828.00<br>-                      | 1,828.00                     | 0.54                               | 12/2020<br>-                       | 12/2020     |
| 105                            | REDEVELOPMENT OF SANTHAL FIELD<br>- [N16000279]                                                                       | 2/2017                        | 1,162.56<br>-                      | 1,162.56                     | 196.84                             | 03/2026<br>03/2026                 | 03/2026     |
| 106                            | ENNORE-TRICHY-MADURAI LPG PIPELINE<br>- [N16000162]                                                                   | 5/2013                        | 711.00<br>-                        | 711.00                       | 11.12                              | 06/2020<br>-                       | 06/2020     |
| 107                            | HALDIA LPG IMPORT FACILITY<br>- [N16000223]                                                                           | 3/2015                        | 694.00<br>-                        | 694.00                       | 183.88                             | 10/2018<br>-                       | 10/2018     |
| 108                            | LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY<br>- [N16000262]                        | 5/2015                        | 193.40<br>-                        | 193.40                       | 7.07                               | 01/2019<br>-                       | 01/2019     |
| 109                            | AURAIYA PHULPUR PIPELINE PROJECT<br>- [N16000231]                                                                     | 7/2015                        | 1,427.94<br>-                      | 1,427.94                     | 379.02                             | 12/2018<br>-                       | 12/2018     |
| 110                            | RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE<br>- [N16000256]                                                     | 10/2015                       | 135.00<br>171.00                   | 170.70                       | 58.29                              | 03/2019<br>-                       | 03/2019     |
| 111                            | RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA)<br>[N16000242]                            | 11/2016                       | 230.00<br>-                        | 230.00                       | 11.46                              | 02/2019<br>-                       | 02/2019     |
| 112                            | AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II<br>[N16000259]                                 | 9/2016                        | 571.66<br>-                        | 571.66                       | -                                  | 12/2019<br>-                       | 12/2019     |
| 113                            | INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY<br>- [N16000277]                                   | 5/2016                        | 429.00<br>-                        | 429.00                       | 20.41                              | 01/2019<br>-                       | 01/2019     |
|                                | Total                                                                                                                 |                               | 1,10,529.33<br>-                   | 1,10,317.32                  | 7,474.61                           |                                    |             |
|                                |                                                                                                                       |                               |                                    |                              |                                    |                                    |             |
|                                | <u>POWER</u>                                                                                                          |                               |                                    |                              |                                    |                                    |             |
| 114                            | 50 MW SOLAR POWER PROJECT<br>- [N18000251]                                                                            | 9/2017                        | 287.48<br>-                        | 287.48                       | 27.51                              | 03/2018<br>-                       | 03/2018     |
| 115                            | HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR<br>- [N18000247] | 2/2017                        | 5,070.13<br>-                      | 5,070.13                     | 211.75                             | 04/2020<br>-                       | 04/2020     |
| 116                            | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)<br>- [N18000239]    | 10/2016                       | 408.46<br>-                        | 408.46                       | 40.19                              | 01/2019<br>-                       | 01/2019     |
| 117                            | GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C<br>- [N18000200]                              | 7/2015                        | 2,247.37<br>-                      | 2,247.37                     | 619.60                             | 07/2018<br>-                       | 07/2018     |
| 118                            | SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI<br>[N18000240]                  | 10/2016                       | 608.24<br>-                        | 608.24                       | 5.12                               | 04/2019<br>-                       | 04/2019     |
| 119                            | SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII<br>- [N18000245]                                                   | 3/2017                        | 379.95<br>-                        | 379.95                       | 19.67                              | 12/2019<br>-                       | 12/2019     |
| 120                            | ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/<br>- [N18000242] | 2/2017                        | 322.30<br>-                        | 322.30                       | 15.05                              | 02/2019<br>-                       | 02/2019     |
| 121                            | EASTERN REGION STRENGTHENING SCHEME XVII( PART B)<br>- [N18000244]                                                    | 2/2017                        | 235.53<br>-                        | 235.53                       | 5.36                               | 06/2019<br>-                       | 06/2019     |
| 122                            | EASTERN REGION STRENGTHENING SCHEME XIV<br>- [N18000224]                                                              | 5/2016                        | 167.01<br>-                        | 167.01                       | 30.86                              | 11/2018<br>-                       | 11/2018     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                             |                               |                                    |                              |                                    | (September 2017)                   |             |
|--------------------------------|-------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                |                                                                                                             |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                           | Project                                                                                                     | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                              | 2                                                                                                           | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 123                            | AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION<br>- [N18000237]                                 | 10/2016                       | 167.75<br>-                        | 167.75                       | -                                  | 04/2019<br>-                       | 04/2019     |
| 124                            | PAKRI BARWADIH COAL MINING PROJECT<br>- [N18000225]                                                         | 10/2004                       | 4,237.96<br>4,238.00               | 4,552.00                     | 2,229.09                           | 10/2017<br>12/2016                 | 10/2017     |
| 125                            | TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A)<br>- [N18000254]             | 4/2015                        | 2,525.00<br>-                      | 2,525.00                     | 1,217.00                           | 11/2017<br>-                       | 11/2017     |
| 126                            | STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI<br>- [N18000257]                                       | 12/2015                       | 3,654.00<br>-                      | 3,654.00                     | 935.00                             | 04/2019<br>-                       | 04/2019     |
| 127                            | AMELIA COAL MINE<br>- [N18000252]                                                                           | 1/2017                        | 2,104.21<br>-                      | 2,104.21                     | 40.26                              | 09/2020<br>-                       | 09/2020     |
| 128                            | TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B<br>- [N18000255]                          | 4/2015                        | 2,225.00<br>2,225.00               | 2,225.00                     | 864.00                             | 01/2018<br>-                       | 01/2018     |
| 129                            | TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-A<br>- [N18000260]                          | 4/2015                        | 2,525.00<br>-                      | 2,525.00                     | 1,215.00                           | 11/2017<br>-                       | 11/2017     |
| 130                            | EASTERN REGION STRENGTHENING SCHEME-XVIII<br>- [N18000258]                                                  | 3/2017                        | 3,500.00<br>3,500.00               | 3,500.00                     | 55.00                              | 07/2020<br>-                       | 07/2020     |
| 131                            | TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V<br>- [N18000256]                            | 2/2015                        | 1,750.00<br>-                      | 1,750.00                     | 456.00                             | 06/2018<br>-                       | 06/2018     |
| 132                            | NORTH EASTERN REGION STRENGTHENING SCHEME IV<br>- [N18000216]                                               | 5/2016                        | 409.19<br>-                        | 409.19                       | 51.42                              | 05/2018<br>-                       | 05/2018     |
| 133                            | PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION<br>- [N18000231]                           | 8/2016                        | 431.89<br>-                        | 431.89                       | 0.40                               | 02/2019<br>-                       | 02/2019     |
| 134                            | WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT)<br>[N18000235]                                | 11/2016                       | 330.00<br>-                        | 330.00                       | 179.43                             | 11/2017<br>-                       | 11/2017     |
| 135                            | TANDA TPP STAGE-II (2X660 MW)<br>- [N18000175]                                                              | 9/2014                        | 9,188.98<br>-                      | 9,188.98                     | 3,149.00                           | 03/2019<br>-                       | 03/2019     |
| 136                            | REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS<br>- [N18000210]                       | 1/2016                        | 207.88<br>-                        | 207.88                       | 77.86                              | 07/2018<br>-                       | 07/2018     |
| 137                            | TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP<br>- [N18000180]                                       | 1/2015                        | 268.80<br>-                        | 340.88                       | 160.06                             | 03/2018<br>-                       | 03/2018     |
| 138                            | RAMMAM-III HEPP (3X40 MW)<br>- [N18000178]                                                                  | 9/2014                        | 1,381.84<br>-                      | 1,381.84                     | 289.00                             | 09/2019<br>-                       | 09/2019     |
| 139                            | INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION<br>- [N18000236] | 3/2017                        | 251.60<br>-                        | 251.60                       | -                                  | 06/2019<br>-                       | 06/2019     |
| 140                            | TELANGANA SUPER THERMAL POWER PROJECT PHASE I<br>- [N18000212]                                              | 1/2016                        | 10,598.98<br>-                     | 10,598.98                    | 1,018.00                           | 07/2020<br>-                       | 07/2020     |
| 141                            | PROVISION OF SERIES REACTORS IN NORTHERN REGION<br>- [N18000232]                                            | 8/2016                        | 177.52<br>-                        | 177.52                       | 10.95                              | 02/2019<br>-                       | 02/2019     |
| 142                            | SOUTHERN REGION STRENGTHENING SCHEME-XXI<br>- [N18000233]                                                   | 9/2016                        | 562.25<br>-                        | 562.25                       | 18.56                              | 03/2019<br>-                       | 03/2019     |
| 143                            | TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN<br>- [N18000227]                                     | 7/2016                        | 1,429.38<br>-                      | 1,429.38                     | 102.89                             | 01/2019<br>-                       | 01/2019     |
| 144                            | EASTERN REGION STRENGTHENING SCHEME-XV<br>- [N18000214]                                                     | 4/2016                        | 454.11<br>-                        | 454.11                       | 51.62                              | 04/2018<br>-                       | 04/2018     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                    |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
| S.No                           | Project                                                                                                            | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                              | 2                                                                                                                  | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 145                            | S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]         | 4/2016                        | 287.99 -                           | 287.99                       | 73.10                              | 06/2018 -                          | 06/2018     |
| 146                            | WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]                                                             | 2/2017                        | 204.12 -                           | 204.12                       | 7.45                               | 09/2019 -                          | 09/2019     |
| 147                            | KHARGONE STPP STAGE I (1320 MW) - [N18000205]                                                                      | 3/2015                        | 9,870.51 -                         | 9,870.51                     | 3,389.00                           | 09/2019 -                          | 09/2019     |
| 148                            | ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]                                                 | 4/2016                        | 790.13 -                           | 790.30                       | 250.26                             | 06/2019 -                          | 06/2019     |
| 149                            | EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]                                                               | 5/2016                        | 766.21 -                           | 766.21                       | 12.93                              | 11/2018 -                          | 11/2018     |
| 150                            | SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]                                               | 3/2017                        | 337.75 -                           | 337.75                       | -                                  | 06/2019 -                          | 06/2019     |
| 151                            | CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]                  | 5/2015                        | 780.33 -                           | 780.33                       | 31.99                              | 10/2018 -                          | 10/2018     |
| 152                            | ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184] | 3/2015                        | 197.40 -                           | 197.40                       | 45.02                              | 03/2018 -                          | 03/2018     |
| 153                            | DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]                                                                   | 2/2014                        | 12,532.44 -                        | 12,532.44                    | 6,289.00                           | 08/2018 -                          | 08/2018     |
| 154                            | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]                | 4/2016                        | 810.48 -                           | 810.48                       | 293.68                             | 12/2018 -                          | 12/2018     |
| 155                            | S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238] | 3/2017                        | 283.72 -                           | 283.72                       | 7.71                               | 11/2019 -                          | 11/2019     |
| 156                            | GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]                                      | 5/2016                        | 3,519.59 -                         | 3,519.59                     | 369.73                             | 05/2019 -                          | 05/2019     |
| 157                            | TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]                               | 7/2016                        | 300.94 -                           | 300.94                       | 22.11                              | 12/2018 -                          | 12/2018     |
| 158                            | PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243]  | 3/2017                        | 162.31 -                           | 162.31                       | 0.62                               | 03/2019 -                          | 03/2019     |
| 159                            | PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]        | 4/2016                        | 844.64 -                           | 844.64                       | 116.16                             | 04/2019 -                          | 04/2019     |
| 160                            | WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]                                                            | 2/2017                        | 195.05 -                           | 195.05                       | -                                  | 02/2020 -                          | 02/2020     |
| 161                            | WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]                                                              | 7/2016                        | 150.99 -                           | 150.99                       | 29.36                              | 07/2018 -                          | 07/2018     |
| 162                            | POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230] | 7/2016                        | 333.17 -                           | 333.17                       | 140.83                             | 03/2019 -                          | 03/2019     |
| 163                            | INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]                                     | 12/2014                       | 6,517.36 -                         | 6,517.36                     | 3,391.91                           | 04/2018 -                          | 04/2018     |
| 164                            | HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219] | 5/2016                        | 14,733.37 -                        | 14,733.37                    | 668.96                             | 11/2019 -                          | 11/2019     |
| 165                            | SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]                                                         | 1/2016                        | 1,455.47 -                         | 1,455.47                     | 471.19                             | 07/2018 -                          | 07/2018     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                    |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
| S.No                           | Project                                                                                                            | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                              | 2                                                                                                                  | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
|                                | Total                                                                                                              |                               | 1,13,181.78 -                      | 1,13,568.07                  | 28,706.66                          |                                    |             |
|                                | <u>RAILWAYS</u>                                                                                                    |                               |                                    |                              |                                    |                                    |             |
| 166                            | MATHURA-PLWAL 4TH LINE (80KM)<br>- [N22000372]                                                                     | 4/2015                        | 524.00<br>668.00                   | 668.00                       | -                                  | 03/2020<br>-                       | 03/2020     |
| 167                            | TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM<br>18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI -<br>[N22000397] | 1/1991                        | 763.18 -                           | 1,428.00                     | -                                  | 12/2021<br>-                       | 12/2021     |
| 168                            | RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING<br>INCLUDING GANGA BRIDGE - [N22000350]                                  | 12/2015                       | 1,491.47 -                         | 1,491.47                     | -                                  | 12/2020<br>-                       | 12/2020     |
| 169                            | BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION<br>- [N22000413]                                                    | 3/2012                        | 1,183.25 -                         | 1,183.30                     | 723.70                             | 12/2020<br>-                       | 12/2020     |
| 170                            | KIUL - GAYA DOUBLING PROJECT<br>- [N22000349]                                                                      | 12/2015                       | 1,200.20 -                         | 1,200.20                     | -                                  | 12/2020<br>-                       | 12/2020     |
| 171                            | MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR<br>- [N22000425]                                                         | 5/2014                        | 207.00 -                           | 207.00                       | 142.00                             | 03/2018<br>-                       | 03/2018     |
| 172                            | RAIPUR - TITLAGARH - DOUBLING<br>- [N22000411]                                                                     | 3/2007                        | 758.09 -                           | 758.09                       | 632.15                             | 03/2020<br>-                       | 03/2020     |
| 173                            | KATNI - SINGRAULI DOUBLING PROJECT<br>- [N22000351]                                                                | 12/2015                       | 1,762.94 -                         | 1,762.94                     | -                                  | 12/2020<br>-                       | 12/2020     |
| 174                            | RAJNANDGAON - NAGPUR - 3RD LINE (SECR)<br>- [N22000420]                                                            | 9/2016                        | 1,273.00<br>1,908.00               | 1,908.00                     | -                                  | 12/2021<br>-                       | 12/2021     |
| 175                            | MULTI MODAL LOGISTICS TRANSPORT AT MIHAN<br>- [N22000422]                                                          | 10/2013                       | 305.00 -                           | 305.00                       | -                                  | 03/2019<br>-                       | 03/2019     |
| 176                            | BONDAMUNDA RANCHI DOUBLING<br>- [N22000396]                                                                        | 3/2016                        | 1,724.20 -                         | 1,724.20                     | -                                  | 03/2021<br>-                       | 03/2021     |
| 177                            | MULTI MODAL LOGISTICS PARK AT VARNAMA<br>- [N22000428]                                                             | 10/2013                       | 343.00 -                           | 343.00                       | 236.64                             | 03/2019<br>-                       | 03/2019     |
| 178                            | RAMNA - SINGRAULI DOUBLING<br>- [N22000417]                                                                        | 8/2015                        | 2,436.21 -                         | 2,436.21                     | 44.89                              | 03/2020<br>-                       | 03/2020     |
| 179                            | SAMBALPUR - TITLAGARH - DOUBLING<br>- [N22000410]                                                                  | 3/2006                        | 960.18 -                           | 960.18                       | 704.78                             | 03/2020<br>-                       | 03/2020     |
| 180                            | MULTI MODAL LOGISTICS PARK AT KAKINADA<br>- [N22000431]                                                            | 8/2016                        | 234.50 -                           | 234.50                       | 0.14                               | 03/2019<br>-                       | 03/2019     |
| 181                            | JAGADALPUR-KORAPUT DOUBLING<br>- [N22000376]                                                                       | 4/2015                        | 1,547.38 -                         | 1,547.38                     | 34.69                              | 03/2021<br>-                       | 03/2021     |
| 182                            | MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM<br>- [N22000424]                                                      | 1/2013                        | 387.70 -                           | 387.70                       | 351.00                             | 03/2018<br>-                       | 03/2018     |
| 183                            | ROSA-SITAPUR CANTT-BURHWAL DOUBLING<br>- [N22000347]                                                               | 3/2015                        | 1,750.00 -                         | 1,295.42                     | 19.80                              | 03/2022<br>-                       | 03/2022     |
| 184                            | JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD<br>3RD AND 4TH LINE - [N22000380]                               | 4/2015                        | 701.61 -                           | 701.61                       | 37.66                              | 03/2021<br>-                       | 03/2021     |
| 185                            | LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC<br>- [N22000404]                                                       | 4/2011                        | 927.01 -                           | 977.00                       | 733.32                             | 03/2019<br>-                       | 03/2019     |
| 186                            | MULTI MODAL LOGISTICS PARK AT SWARUPGANJ<br>- [N22000423]                                                          | 4/2012                        | 471.82 -                           | 471.82                       | 19.91                              | 03/2019<br>-                       | 03/2019     |



## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                          |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
| S.No                           | Project                                                                                                                  | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                              | 2                                                                                                                        | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 187                            | SECUNDERABAD-MAHABUBNAGAR DOUBLING<br>- [N22000403]                                                                      | 4/2015                        | 728.10<br>-                        | 728.10                       | 15.05                              | 12/2024<br>-                       | 12/2024     |
| 188                            | BINA - KOTA DOUBLING WITH RE<br>- [N22000414]                                                                            | 4/2011                        | 1,485.65<br>-                      | 1,485.85                     | 685.71                             | 12/2020<br>-                       | 12/2020     |
| 189                            | ROURKELA JHARSUGUDA THIRD LINE 101 KM<br>- [N22000395]                                                                   | 11/2015                       | 969.83<br>-                        | 969.83                       | -                                  | 03/2020<br>-                       | 03/2020     |
| 190                            | DIGHI PORT NEW LINE<br>- [N22000408]                                                                                     | 4/2015                        | 723.78<br>-                        | 723.78                       | 0.22                               | 12/2025<br>-                       | 12/2025     |
| 191                            | DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM<br>OF SOUTH CENTRAL RAILWAY - [N22000394]                                | 3/2015                        | 636.38<br>-                        | 636.38                       | 169.16                             | 03/2021<br>-                       | 03/2021     |
| 192                            | MULTI MODAL LOGISTICS PARK AT TIHI<br>- [N22000427]                                                                      | 12/2015                       | 174.00<br>-                        | 174.00                       | 90.63                              | 03/2019<br>-                       | 03/2019     |
| 193                            | KATNI-BINA 3RD LINE (263 KM)<br>- [N22000415]                                                                            | 6/2016                        | 2,478.23<br>-                      | 2,478.23                     | -                                  | 03/2022<br>-                       | 03/2022     |
| 194                            | KATNI GRADE SEPARATOR/BYE PASS<br>- [N22000416]                                                                          | 8/2016                        | 582.13<br>-                        | 582.13                       | -                                  | 03/2020<br>-                       | 03/2020     |
| 195                            | MULTI MODAL LOGISTICS PARK AT BARHI<br>- [N22000426]                                                                     | 12/2015                       | 346.32<br>-                        | 300.00                       | 204.51                             | 03/2019<br>-                       | 03/2019     |
| 196                            | DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-<br>GUNTAKAL -ELECTRIFICATION (641.37 KM) -<br>[N22000407]                 | 3/2009                        | 1,514.45<br>-                      | 1,514.45                     | -                                  | 03/2020<br>-                       | 03/2020     |
| 197                            | BANASPANI- JAKHPURA - DOUBLING<br>- [N22000412]                                                                          | 3/2009                        | 942.95<br>-                        | 942.95                       | 795.83                             | 03/2019<br>-                       | 03/2019     |
| 198                            | RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION<br>FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO -<br>[N22000398]         | 4/1995                        | 524.43<br>-                        | 939.00                       | -                                  | 12/2021<br>-                       | 12/2021     |
| 199                            | EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL<br>TRANSPORTATION IN ODISHA FOR MCRL -<br>[N22000418]                    | 4/2016                        | 5,200.00<br>-                      | 5,200.00                     | -                                  | 03/2020<br>-                       | 03/2020     |
| 200                            | VARANASI-MODHOSINGH-ALLAHABAD DOUBLING<br>- [N22000401]                                                                  | 4/2015                        | 750.55<br>-                        | 750.56                       | 17.25                              | 12/2024<br>-                       | 12/2024     |
| 201                            | RISHIKESH - KARNAPRAYAG NEW LINE<br>- [N22000406]                                                                        | 4/2011                        | 4,295.30<br>-                      | 1,621.60                     | 167.32                             | 12/2026<br>-                       | 12/2026     |
| 202                            | MULTI MODAL LOGISTICS PARK AT KATHUWAS<br>- [N22000421]                                                                  | 1/2011                        | 493.17<br>-                        | 493.17                       | 383.12                             | 03/2018<br>-                       | 03/2018     |
| 203                            | MAU-GHAZIPUR-TARIGHAT NEW LINE<br>- [N22000405]                                                                          | 4/2015                        | 1,765.90<br>-                      | 1,765.90                     | 26.79                              | 12/2025<br>-                       | 12/2025     |
|                                | Total                                                                                                                    |                               | 44,562.91<br>-                     | 43,296.95                    | 6,236.27                           |                                    |             |
|                                |                                                                                                                          |                               |                                    |                              |                                    |                                    |             |
|                                | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                       |                               |                                    |                              |                                    |                                    |             |
| 204                            | TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-<br>SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020<br>(DESIGN - [N24000665] | 3/2017                        | 672.89<br>-                        | 736.01                       | -                                  | 03/2020<br>-                       | 03/2020     |
| 205                            | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I)<br>FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 -<br>[N24000653]  | 3/2017                        | 1,373.28<br>-                      | 1,373.28                     | -                                  | 03/2020<br>-                       | 03/2020     |
| 206                            | STRENGTHENING AND CONSTRUCTION OF PAVED<br>SHOULDERS INCLUDING REHABILITATION/REPAIRING OF<br>BRIDGES FROM - [N24000409] | 5/2011                        | 176.22<br>-                        | 176.22                       | -                                  | 02/2018<br>-                       | 02/2018     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                        |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
|--------------------------------|------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
| S.No                           | Project                                                                                                                | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                              | 2                                                                                                                      | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 207                            | RHENOK-RORATHANG-PAKYONG ON NH 717A<br>- [N24000695]                                                                   | 4/2017                        | 388.00<br>-                        | 447.37                       | -                                  | 10/2017<br>-                       | 10/2017     |
| 208                            | JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400<br>- [N24000475]                        | 11/2015                       | 628.45<br>-                        | 628.45                       | 20.74                              | 03/2018<br>-                       | 03/2018     |
| 209                            | STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ -<br>[N24000411]   | 11/2014                       | 218.31<br>-                        | 218.31                       | -                                  | 02/2018<br>-                       | 02/2018     |
| 210                            | FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52<br>- [N24000321]                       | 6/2016                        | 829.00<br>-                        | 829.00                       | 59.85                              | 01/2019<br>-                       | 01/2019     |
| 211                            | WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH<br>- [N24000333]   | 12/2015                       | 621.43<br>-                        | 621.43                       | -                                  | 06/2018<br>-                       | 06/2018     |
| 212                            | CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH -<br>[N24000326]  | 7/2015                        | 197.16<br>-                        | 197.16                       | 38.50                              | 10/2018<br>-                       | 10/2018     |
| 213                            | 2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S -<br>[N24000328]  | 10/2014                       | 369.00<br>-                        | 369.00                       | 36.90                              | 03/2018<br>-                       | 03/2018     |
| 214                            | MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A<br>- [N24000410]                       | 6/2015                        | 641.02<br>-                        | 641.02                       | 89.88                              | 12/2017<br>-                       | 12/2017     |
| 215                            | CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]     | 1/2014                        | 255.75<br>348.00                   | 348.43                       | 0.02                               | 09/2017<br>-                       | 09/2017     |
| 216                            | 4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. -<br>[N24000438]       | 12/2015                       | 289.99<br>-                        | 289.99                       | -                                  | 12/2018<br>-                       | 12/2018     |
| 217                            | 4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL -<br>[N24000323]   | 10/2014                       | 588.95<br>-                        | 588.95                       | 80.00                              | 11/2018<br>-                       | 11/2018     |
| 218                            | 2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH<br>- [N24000327]              | 3/2015                        | 394.00<br>-                        | 394.00                       | -                                  | 06/2018<br>-                       | 06/2018     |
| 219                            | CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]     | 1/2014                        | 267.16<br>352.00                   | 352.05                       | 0.02                               | 11/2017<br>-                       | 11/2017     |
| 220                            | FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 -<br>[N24000320] | 6/2015                        | 463.49<br>-                        | 463.49                       | 9.26                               | 06/2018<br>-                       | 06/2018     |
| 221                            | GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93<br>- [N24000478]                                    | 12/2015                       | 927.54<br>-                        | 927.54                       | 29.17                              | 06/2018<br>-                       | 06/2018     |
| 222                            | 2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS<br>- [N24000325]                              | 10/2015                       | 179.82<br>-                        | 179.82                       | 8.99                               | 01/2019<br>-                       | 01/2019     |
| 223                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB -<br>[N24000376]  | 1/1991                        | 219.40<br>-                        | 219.40                       | -                                  | 01/2018<br>-                       | 01/2018     |
| 224                            | FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A<br>- [N24000322]              | 3/2015                        | 168.39<br>-                        | 168.39                       | 16.84                              | 11/2018<br>-                       | 11/2018     |
| 225                            | FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM -<br>[N24000305]  | 5/2015                        | 454.89<br>-                        | 454.89                       | 22.74                              | 05/2018<br>-                       | 05/2018     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                   |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
|--------------------------------|-------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
| S.No                           | Project                                                                                                           | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                              | 2                                                                                                                 | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 226                            | 4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319 | 6/2015                        | 437.39 -                           | 437.39                       | 21.86                              | 06/2018 -                          | 06/2018     |
| 227                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379 | 1/1991                        | 218.63 -                           | 218.63                       | 29.27                              | 10/2017 -                          | 10/2017     |
| 228                            | WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523     | 12/2011                       | 159.39 -                           | 159.39                       | -                                  | 11/2017 -                          | 11/2017     |
| 229                            | 2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421                                | 3/2015                        | 235.08 -                           | 235.08                       | -                                  | 05/2018 -                          | 05/2018     |
| 230                            | 4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429      | 12/2015                       | 225.02 -                           | 159.20                       | -                                  | 12/2018 -                          | 12/2018     |
| 231                            | 2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324 | 3/2015                        | 194.11 -                           | 194.11                       | 30.54                              | 05/2018 -                          | 05/2018     |
| 232                            | 4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430                | 12/2015                       | 223.30 -                           | 223.30                       | -                                  | 06/2018 -                          | 06/2018     |
| 233                            | ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393                                          | 6/2015                        | 774.57 -                           | 774.57                       | -                                  | 03/2018 -                          | 03/2018     |
| 234                            | FOUR LANING OF AURANGABAD - YEDISHI - [N24000508                                                                  | 7/2015                        | 1,871.34 -                         | 1,871.34                     | 2,601.04                           | 01/2018 -                          | 01/2018     |
| 235                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397 | 1/1991                        | 322.00 -                           | 322.00                       | 56.41                              | 03/2018 -                          | 03/2018     |
| 236                            | SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691                                             | 4/2017                        | 894.00 -                           | 894.00                       | -                                  | 04/2020 -                          | 04/2020     |
| 237                            | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-VI) - [N24000433                                      | 9/2015                        | 768.56 -                           | 768.56                       | 512.89                             | 03/2018 -                          | 03/2018     |
| 238                            | REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671  | 3/2017                        | 1,288.07 -                         | 1,420.00                     | -                                  | 03/2020 -                          | 03/2020     |
| 239                            | WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642  | 3/2015                        | 226.31 226.00                      | 226.00                       | -                                  | 10/2017 -                          | 10/2017     |
| 240                            | FOUR LANNING OF VIKRAVANDI-SETHIAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652  | 3/2017                        | 848.45 -                           | 848.45                       | -                                  | 03/2020 -                          | 03/2020     |
| 241                            | 4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656                                             | 3/2017                        | 744.64 -                           | 982.00                       | -                                  | 03/2020 -                          | 03/2020     |
| 242                            | WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640  | 1/2015                        | 326.63 327.00                      | 327.00                       | -                                  | 04/2018 -                          | 04/2018     |
| 243                            | 4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692                                                      | 6/2017                        | 2,485.93 -                         | 2,485.93                     | -                                  | 06/2020 -                          | 06/2020     |
| 244                            | CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662 | 3/2017                        | 754.54 -                           | 756.27                       | -                                  | 03/2020 -                          | 03/2020     |
| 245                            | 4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670                           | 3/2017                        | 239.68 -                           | 235.90                       | -                                  | 03/2020 -                          | 03/2020     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                    |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
| S.No                           | Project                                                                                                            | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                              | 2                                                                                                                  | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 246                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414  | 1/1991                        | 229.41 -                           | 229.41                       | 6.65                               | 05/2018 -                          | 05/2018     |
| 247                            | 4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693                                         | 6/2017                        | 1,958.88 -                         | 1,958.88                     | -                                  | 06/2020 -                          | 06/2020     |
| 248                            | SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668                  | 3/2017                        | 1,041.62 -                         | 1,187.10                     | -                                  | 03/2020 -                          | 03/2020     |
| 249                            | FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484                                                       | 12/2015                       | 239.23 -                           | 239.23                       | 161.60                             | 12/2017 -                          | 12/2017     |
| 250                            | SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O) - [N24000675 | 3/2017                        | 993.16 -                           | 1,434.00                     | -                                  | 03/2020 -                          | 03/2020     |
| 251                            | FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493                                                          | 1/2016                        | 1,027.53 -                         | 1,027.53                     | 152.94                             | 06/2018 -                          | 06/2018     |
| 252                            | 4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448                                                             | 1/2016                        | 574.28 -                           | 574.28                       | 185.12                             | 07/2018 -                          | 07/2018     |
| 253                            | TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23 - [N24000343                                       | 9/2015                        | 341.61 -                           | 341.61                       | 308.23                             | 09/2017 -                          | 09/2017     |
| 254                            | 4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI ( KM 0.00 TO KM . 83.785) - [N24000463                            | 12/2015                       | 1,083.00 -                         | 1,083.00                     | -                                  | 06/2018 -                          | 06/2018     |
| 255                            | TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 ( NEW NH NO - 50) - [N24000342  | 5/2015                        | 709.00 -                           | 709.00                       | 203.50                             | 09/2017 -                          | 09/2017     |
| 256                            | FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471                                                      | 12/2015                       | 2,168.66 -                         | 2,168.66                     | -                                  | 06/2019 -                          | 06/2019     |
| 257                            | CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655  | 3/2017                        | 247.02 -                           | 157.49                       | -                                  | 03/2020 -                          | 03/2020     |
| 258                            | SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673  | 3/2017                        | 985.41 -                           | 1,200.00                     | -                                  | 03/2020 -                          | 03/2020     |
| 259                            | FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651                                                                 | 2/2017                        | 904.16 -                           | 904.16                       | -                                  | 02/2020 -                          | 02/2020     |
| 260                            | FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491                                                         | 1/2016                        | 815.28 -                           | 815.28                       | 90.98                              | 06/2018 -                          | 06/2018     |
| 261                            | JAISALMER - BARMER - [N24000348                                                                                    | 8/2015                        | 482.27 -                           | 482.27                       | -                                  | 02/2018 -                          | 02/2018     |
| 262                            | DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663  | 3/2017                        | 1,989.00 -                         | 1,989.00                     | -                                  | 03/2020 -                          | 03/2020     |
| 263                            | 4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664   | 3/2017                        | 639.79 -                           | 552.90                       | -                                  | 03/2020 -                          | 03/2020     |
| 264                            | PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357                                         | 9/2015                        | 567.51 -                           | 567.51                       | -                                  | 03/2018 -                          | 03/2018     |
| 265                            | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654  | 3/2017                        | 1,184.71 -                         | 1,310.00                     | -                                  | 03/2020 -                          | 03/2020     |
| 266                            | 4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658                                           | 3/2017                        | 988.34 -                           | 1,043.28                     | -                                  | 03/2020 -                          | 03/2020     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                   |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
|--------------------------------|-------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
| S.No                           | Project                                                                                                           | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                              | 2                                                                                                                 | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 267                            | FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589                        | 6/2016                        | 649.00 -                           | 649.00                       | -                                  | 06/2019 -                          | 06/2019     |
| 268                            | 4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661                                        | 3/2017                        | 1,098.06 -                         | 1,160.64                     | -                                  | 03/2020 -                          | 03/2020     |
| 269                            | FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587   | 6/2016                        | 763.23 -                           | 763.23                       | -                                  | 06/2019 -                          | 06/2019     |
| 270                            | TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586                                                     | 6/2016                        | 637.18 -                           | 637.18                       | -                                  | 06/2019 -                          | 06/2019     |
| 271                            | FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500                                                           | 1/2016                        | 830.36 -                           | 830.36                       | 473.08                             | 07/2018 -                          | 07/2018     |
| 272                            | BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445  | 8/2014                        | 822.90 -                           | 822.90                       | -                                  | 04/2018 -                          | 04/2018     |
| 273                            | 4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657                                         | 3/2017                        | 1,030.44 -                         | 1,065.51                     | -                                  | 03/2020 -                          | 03/2020     |
| 274                            | REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667                      | 3/2017                        | 648.32 -                           | 503.10                       | -                                  | 03/2020 -                          | 03/2020     |
| 275                            | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-V) - [N24000436                                       | 9/2015                        | 664.53 -                           | 664.53                       | 390.38                             | 03/2018 -                          | 03/2018     |
| 276                            | FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488                                                    | 12/2015                       | 2,136.97 -                         | 2,136.97                     | -                                  | 12/2018 -                          | 12/2018     |
| 277                            | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-III) - [N24000446                                     | 9/2015                        | 788.51 -                           | 788.51                       | 321.86                             | 03/2018 -                          | 03/2018     |
| 278                            | TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER ( UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337 | 8/2015                        | 538.08 -                           | 538.08                       | -                                  | 02/2018 -                          | 02/2018     |
| 279                            | FOUR LANING OF PARWANOO -SOLAN - [N24000479                                                                       | 9/2015                        | 934.46 -                           | 934.46                       | 175.87                             | 03/2018 -                          | 03/2018     |
| 280                            | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-II) - [N24000450                                      | 9/2015                        | 785.78 -                           | 785.78                       | 587.77                             | 03/2018 -                          | 03/2018     |
| 281                            | FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347                                          | 8/2015                        | 723.54 -                           | 723.54                       | 558.12                             | 02/2018 -                          | 02/2018     |
| 282                            | SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674   | 3/2017                        | 831.58 -                           | 1,177.00                     | -                                  | 03/2020 -                          | 03/2020     |
| 283                            | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-IV) - [N24000440                                      | 9/2015                        | 789.31 -                           | 789.31                       | 603.92                             | 03/2018 -                          | 03/2018     |
| 284                            | FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349      | 5/2015                        | 1,387.11 -                         | 1,387.11                     | 658.16                             | 11/2017 -                          | 11/2017     |
| 285                            | 6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672 | 3/2017                        | 2,064.99 -                         | 2,447.00                     | -                                  | 03/2020 -                          | 03/2020     |
| 286                            | 4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669                                     | 3/2017                        | 165.50 -                           | 172.16                       | -                                  | 03/2020 -                          | 03/2020     |
| 287                            | CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666 | 3/2017                        | 235.48 -                           | 227.77                       | -                                  | 03/2020 -                          | 03/2020     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
|--------------------------------|----------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
| S.No                           | Project                                                                                                        | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                              | 2                                                                                                              | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 288                            | UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA( PKG - 2) - [N24000358                             | 10/2015                       | 562.34 -                           | 562.34                       | 281.73                             | 04/2018 -                          | 04/2018     |
| 289                            | FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499                                                | 12/2015                       | 667.00 -                           | 667.00                       | 164.32                             | 06/2018 -                          | 06/2018     |
| 290                            | WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641 | 2/2015                        | 239.91 240.00                      | 240.00                       | -                                  | 10/2017 -                          | 10/2017     |
|                                | Total                                                                                                          |                               | 62,726.23 -                        | 64,811.39                    | 8,989.15                           |                                    |             |
|                                |                                                                                                                |                               |                                    |                              |                                    |                                    |             |
|                                | <u>SHIPPING AND PORTS</u>                                                                                      |                               |                                    |                              |                                    |                                    |             |
| 291                            | CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068                                         | 9/2015                        | 210.00 -                           | 210.00                       | -                                  | 01/2018 -                          | 01/2018     |
| 292                            | CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066                                            | 2/2015                        | 244.50 258.00                      | 258.33                       | 0.14                               | 12/2017 -                          | 12/2017     |
|                                | Total                                                                                                          |                               | 454.50 -                           | 468.33                       | .14                                |                                    |             |
|                                |                                                                                                                |                               |                                    |                              |                                    |                                    |             |
|                                | <u>STEEL</u>                                                                                                   |                               |                                    |                              |                                    |                                    |             |
| 293                            | EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097         | 2/2014                        | 4,749.00 -                         | 4,749.00                     | 69.35                              | 09/2017 -                          | 09/2017     |
| 294                            | CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110       | 12/2007                       | 200.00 -                           | 200.00                       | 131.15                             | 03/2018 -                          | 03/2018     |
| 295                            | REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118                                                       | 11/2016                       | 262.87 -                           | 262.87                       | 35.71                              | 06/2019 -                          | 06/2019     |
| 296                            | ALTERNATE GAS NETWORK AT BSL - [N12000093                                                                      | 3/2015                        | 255.19 -                           | 255.19                       | 156.39                             | 03/2018 -                          | 03/2018     |
| 297                            | CENTRAL DISPATCH YARD - [N12000119                                                                             | 8/2015                        | 320.66 -                           | 320.66                       | 15.23                              | 08/2018 -                          | 08/2018     |
| 298                            | ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120                                                        | 7/2015                        | 465.85 -                           | 465.85                       | 35.89                              | 07/2018 -                          | 07/2018     |
| 299                            | FORGED WHEEL PLANT - [N12000116                                                                                | 4/2014                        | 1,682.85 -                         | 1,682.85                     | 63.22                              | 09/2018 -                          | 09/2018     |
| 300                            | 2 MTPA PELLET PLANT AT NAGARNAR - [N12000115                                                                   | 11/2015                       | 818.00 -                           | 818.00                       | 25.88                              | 06/2020 -                          | 06/2020     |
| 301                            | CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112                                                       | 4/2013                        | 170.00 -                           | 170.00                       | 88.91                              | 04/2018 -                          | 04/2018     |
|                                | Total                                                                                                          |                               | 8,924.42 -                         | 8,924.42                     | 621.73                             |                                    |             |
|                                |                                                                                                                |                               |                                    |                              |                                    |                                    |             |
|                                | <u>URBAN DEVELOPMENT</u>                                                                                       |                               |                                    |                              |                                    |                                    |             |
| 302                            | RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103                                                              | 12/2016                       | 246.31 -                           | 246.31                       | -                                  | 02/2020 -                          | 02/2020     |
| 303                            | ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098           | 10/2016                       | 209.84 -                           | 209.84                       | 0.43                               | 03/2020 -                          | 03/2020     |

## Details of On Schedule Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                         |                               |                                    |                              |                                    | (September 2017)                   |             |
|--------------------------------|-----------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|
|                                |                                                                                         |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |
| S.No                           | Project                                                                                 | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original/ Revised                  | Anticipated |
| 1                              | 2                                                                                       | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           |
| 304                            | CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB<br>- [N28000102] | 8/2016                        | 294.00<br>-                        | 294.00                       | 34.90                              | 04/2019<br>-                       | 04/2019     |
| 305                            | REDEVELOPMENT OF EAST KIDWAI NAGAR<br>- [N28000080]                                     | 6/2012                        | 4,264.00<br>-                      | 4,118.00                     | 2,790.00                           | 11/2019<br>-                       | 11/2019     |
| 306                            | CHENNAI METRO RAIL LTD (PHASE 1 EXT)<br>- [N28000097]                                   | 6/2016                        | 3,770.00<br>-                      | 3,770.00                     | -                                  | 03/2018<br>-                       | 03/2018     |
| 307                            | LUCKNOW METRO RAIL CORPORATION LTD<br>- [N28000094]                                     | 1/2016                        | 6,928.00<br>6,928.00               | 6,928.00                     | 2,536.77                           | 03/2019<br>-                       | 03/2019     |
|                                | Total                                                                                   |                               | 15,712.15<br>-                     | 15,566.15                    | 5,362.10                           |                                    |             |
|                                |                                                                                         |                               |                                    |                              |                                    |                                    |             |
|                                | Grand Total                                                                             |                               | 4,29,863.74                        | 4,30,797.73                  | 67,608.31                          |                                    |             |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

### Annexure - V

| (September 2017) |                                                                                          |                                  |                                      |                                |                                       |             |                   |
|------------------|------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                  |                                                                                          |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No             | Project                                                                                  | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1                | 2                                                                                        | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
|                  |                                                                                          |                                  |                                      |                                |                                       |             |                   |
|                  | <u>ATOMIC ENERGY</u>                                                                     |                                  |                                      |                                |                                       |             |                   |
| 1                | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)<br>- [020100044                        | 09/2003                          | 3,492.00<br>-                        | 6,000.00                       | 09/2010<br>-                          | 02/2018     | 71.82             |
|                  | Total                                                                                    |                                  | 3,492.00<br>-                        | 6,000.00                       |                                       |             |                   |
|                  |                                                                                          |                                  |                                      |                                |                                       |             |                   |
|                  | <u>CIVIL AVIATION</u>                                                                    |                                  |                                      |                                |                                       |             |                   |
| 2                | CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT<br>[N04000050                     | 01/2009                          | 309.46<br>-                          | 553.53                         | 01/2011<br>-                          | 09/2017     | 78.87             |
| 3                | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR<br>[N04000073 | 10/2013                          | 314.61<br>-                          | 441.33                         | 09/2018<br>-                          | 06/2020     | 40.28             |
|                  | Total                                                                                    |                                  | 624.07<br>-                          | 994.86                         |                                       |             |                   |
|                  |                                                                                          |                                  |                                      |                                |                                       |             |                   |
|                  | <u>COAL</u>                                                                              |                                  |                                      |                                |                                       |             |                   |
| 4                | JAGANNATHPOR OCP(3.00MTY)<br>- [N06000075                                                | 09/2008                          | 152.43<br>-                          | 459.49                         | 03/2015<br>-                          | 03/2020     | 201.44            |
| 5                | NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI<br>- [N06000033                   | 10/2007                          | 259.40<br>-                          | 486.57                         | 03/2012<br>-                          | 03/2018     | 87.58             |
| 6                | RAMAGUNDAM OC-II EXTENSION<br>- [N06000078                                               | 12/2009                          | 418.97<br>-                          | 489.62                         | 03/2012<br>-                          | 03/2023     | 16.86             |
| 7                | SHANTIKHANI LONGWALL PROJ-SCCL<br>- [N06000017                                           | 10/2006                          | 249.03<br>-                          | 448.86                         | 03/2012<br>-                          | 03/2019     | 80.24             |
| 8                | KAKATIYAKHANI OPENCAST-2 PROJECT<br>- [N06000129                                         | 05/2015                          | 397.09<br>-                          | 442.42                         | 03/2019<br>-                          | 03/2019     | 11.42             |
| 9                | RCE OF INDARAM OCP(1.20 MTPA)<br>- [N06000093                                            | 07/2011                          | 162.76<br>-                          | 349.28                         | 03/2015<br>-                          | 03/2020     | 114.60            |
| 10               | NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW<br>- [N06000152                      | 07/2016                          | 17,237.00<br>-                       | 17,237.80                      | 11/2021<br>-                          | 11/2021     | .00               |
|                  | Total                                                                                    |                                  | 18,876.68<br>-                       | 19,914.04                      |                                       |             |                   |
|                  |                                                                                          |                                  |                                      |                                |                                       |             |                   |
|                  | <u>DEFENCE PRODUCTION</u>                                                                |                                  |                                      |                                |                                       |             |                   |
| 11               | CONSTRUCTION WORKS PHASE 4<br>- [N39000001                                               | 12/2016                          | 167.69<br>168.00                     | 172.99                         | 05/2018<br>-                          | 05/2018     | 3.16              |
| 12               | CONSTRUCTION WORKS PHASE 3B<br>- [N39000002                                              | 12/2016                          | 285.95<br>286.00                     | 296.05                         | 08/2020<br>-                          | 08/2020     | 3.53              |
|                  | Total                                                                                    |                                  | 453.64<br>-                          | 469.04                         |                                       |             |                   |
|                  |                                                                                          |                                  |                                      |                                |                                       |             |                   |



## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (September 2017) |                                                                                                         |                                  |                                      |                                |                                       |             |                   |
|------------------|---------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                  |                                                                                                         |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No             | Project                                                                                                 | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1                | 2                                                                                                       | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
|                  | <u>FERTILISERS</u>                                                                                      |                                  |                                      |                                |                                       |             |                   |
| 13               | NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY<br>- [N08000009]                                        | 10/2014                          | 197.79<br>-                          | 209.44                         | 11/2016<br>-                          | 04/2019     | 5.89              |
| 14               | GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL.<br>[N08000010]                  | 02/2016                          | 482.85<br>-                          | 494.00                         | 12/2017<br>-                          | 12/2017     | 2.31              |
|                  | Total                                                                                                   |                                  | 680.64<br>-                          | 703.44                         |                                       |             |                   |
|                  |                                                                                                         |                                  |                                      |                                |                                       |             |                   |
|                  | <u>HEALTH AND FAMILY WELFARE</u>                                                                        |                                  |                                      |                                |                                       |             |                   |
| 15               | SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK<br>[N21000005]                  | 11/2013                          | 196.70<br>-                          | 209.00                         | 01/2016<br>-                          | -           | 6.25              |
|                  | Total                                                                                                   |                                  | 196.70<br>-                          | 209.00                         |                                       |             |                   |
|                  |                                                                                                         |                                  |                                      |                                |                                       |             |                   |
|                  | <u>HEAVY INDUSTRY</u>                                                                                   |                                  |                                      |                                |                                       |             |                   |
| 16               | NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)<br>- [N20000001]                    | 04/2011                          | 1,718.00<br>-                        | 3,827.30                       | 09/2011<br>-                          | 12/2017     | 122.78            |
|                  | Total                                                                                                   |                                  | 1,718.00<br>-                        | 3,827.30                       |                                       |             |                   |
|                  |                                                                                                         |                                  |                                      |                                |                                       |             |                   |
|                  | <u>PETROLEUM</u>                                                                                        |                                  |                                      |                                |                                       |             |                   |
| 17               | SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN<br>- [N16000167] | 07/2011                          | 352.56<br>-                          | 439.03                         | 03/2017<br>-                          | 11/2018     | 24.53             |
| 18               | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR<br>- [N16000169]                                           | 01/2006                          | 993.00<br>-                          | 1,693.00                       | 01/2012<br>-                          | 10/2017     | 70.49             |
| 19               | LPG TERMINAL AT KOCHI<br>- [N16000171]                                                                  | 10/2015                          | 607.06<br>-                          | 714.25                         | 10/2017<br>-                          | 03/2019     | 17.66             |
| 20               | INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS<br>- [N16000172]                                      | 05/2013                          | 4,124.35<br>-                        | 5,637.00                       | 04/2016<br>-                          | 12/2017     | 36.68             |
| 21               | DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY<br>- [N16000175]                        | 03/2014                          | 3,076.00<br>-                        | 4,190.00                       | 09/2017<br>-                          | 06/2018     | 36.22             |
| 22               | MH NORTH REDEVELOPMENT PHASE III<br>- [N16000188]                                                       | 06/2014                          | 5,706.47<br>-                        | 5,813.25                       | 05/2017<br>-                          | 05/2018     | 1.87              |
| 23               | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)<br>[N16000127]                   | 06/2010                          | 202.94<br>-                          | 330.35                         | 01/2014<br>-                          | 11/2019     | 62.78             |
| 24               | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)<br>[N16000128]                  | 03/2011                          | 861.79<br>-                          | 1,256.72                       | 05/2013<br>-                          | 12/2017     | 45.83             |
| 25               | INTEGRATED DEVELOPMENT OF B-127 FIELDS<br>- [N16000131]                                                 | 12/2011                          | 2,059.63<br>-                        | 2,665.65                       | 03/2015<br>-                          | 03/2018     | 29.42             |
| 26               | PARADIP HALDIA DURGAPUR LPG PIPELINE<br>- [N16000148]                                                   | 02/2011                          | 913.00<br>-                          | 1,330.00                       | 06/2018<br>-                          | 06/2018     | 45.67             |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (September 2017) |                                                                                                                         |                                  |                                      |                                |                                       |             |                   |
|------------------|-------------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                  |                                                                                                                         |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No             | Project                                                                                                                 | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1                | 2                                                                                                                       | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 27               | URAN CHAKAN SHIKRAPUR LPG PIPELINE<br>- [N16000155]                                                                     | 12/2009                          | 309.81<br>-                          | 723.40                         | 10/2014<br>-                          | 03/2018     | 133.50            |
| 28               | UPGRADATION OF CRUDE OIL PUMP STATIONS OF<br>NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE<br>- [N18000148]              | 09/2012                          | 871.35<br>-                          | 1,200.00                       | 03/2015<br>-                          | 11/2017     | 37.72             |
| 29               | 50 MW CAPACITY WIND POWER PROJECT UNDER<br>PHASE II - [N16000209]                                                       | 11/2011                          | 310.00<br>-                          | 370.00                         | 03/2013<br>-                          | -           | 19.35             |
| 30               | LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI<br>HIGH AND HEERA FIELDS -<br>[N16000213]                                    | 12/2015                          | 3,190.69<br>-                        | 3,247.19                       | 04/2018<br>-                          | 04/2018     | 1.77              |
| 31               | RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI<br>MARKETING TERMINAL PROJECT) -<br>[N16000217]                           | 06/2012                          | 150.00<br>-                          | 259.93                         | 07/2014<br>-                          | 09/2017     | 73.29             |
| 32               | DEVELOPMENT PLAN OF CBM - BOKARO BLOCK<br>- [N16000239]                                                                 | 12/2015                          | 658.62<br>-                          | 910.23                         | 03/2023<br>-                          | 03/2022     | 38.20             |
| 33               | RAILWAY SIDING PROJECT FOR EVACUATION OF<br>PETCOKE - [N16000256]                                                       | 10/2015                          | 135.00<br>171.00                     | 170.70                         | 03/2019<br>-                          | 03/2019     | 26.44             |
|                  | Total                                                                                                                   |                                  | 24,522.27<br>-                       | 30,950.70                      |                                       |             |                   |
|                  |                                                                                                                         |                                  |                                      |                                |                                       |             |                   |
|                  | <u>POWER</u>                                                                                                            |                                  |                                      |                                |                                       |             |                   |
| 34               | PARBATI HEP (4X200 MW) (NHPC) II<br>- [180100210]                                                                       | 09/2002                          | 3,919.59<br>-                        | 8,398.75                       | 09/2009<br>-                          | 12/2018     | 114.28            |
| 35               | SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)<br>- [180100221]                                                                | 09/2003                          | 6,285.33<br>-                        | 18,559.49                      | 09/2010<br>-                          | -           | 195.28            |
| 36               | WESTERN REGION STRENGTHENING SCHEME-V<br>- [N18000035]                                                                  | 12/2007                          | 477.69<br>-                          | 738.48                         | 09/2010<br>-                          | 03/2018     | 54.59             |
| 37               | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA<br>POWER PROJECT - [N18000061]                                             | 10/2008                          | 4,824.12<br>-                        | 5,071.94                       | 10/2012<br>-                          | 02/2018     | 5.14              |
| 38               | TRANSMISSION SYSTEM FOR DEVELOPMENT OF<br>POOLING STN. IN NR PART OF WEST BENGAL AND<br>TRANSFER OF POWER - [N18000077] | 04/2010                          | 4,404.57<br>-                        | 5,135.01                       | 01/2015<br>-                          | 03/2018     | 16.58             |
| 39               | NORTH- EAST NORTH WESTERN INTERCONNECTOR I<br>PROJECT - [N18000066]                                                     | 02/2009                          | 11,130.19<br>-                       | 13,762.80                      | 08/2013<br>-                          | 12/2017     | 23.65             |
| 40               | TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA<br>GBPP and BPTS. - [N18000080]                                           | 02/2010                          | 2,144.00<br>-                        | 2,932.88                       | 12/2012<br>-                          | 02/2018     | 36.79             |
| 41               | EASTERN REGION STRENGTHENING SCHEME-V<br>- [N18000155]                                                                  | 10/2013                          | 1,364.52<br>-                        | 1,891.41                       | 04/2016<br>-                          | 03/2018     | 38.61             |
| 42               | NORTHERN REGION SYSTEM STRENGTHENING SCHEME<br>- XXXII - [N18000159]                                                    | 02/2014                          | 908.08<br>-                          | 969.97                         | 06/2016<br>-                          | 11/2017     | 6.82              |
| 43               | EASTERN REGION STRENGTHENING SCHEME-XII<br>- [N18000164]                                                                | 05/2014                          | 522.29<br>-                          | 550.18                         | 11/2016<br>-                          | 03/2018     | 5.34              |
| 44               | AUGMENTATION OF TRANSFORMERS IN NORTHERN<br>REGION - PART B - [N18000165]                                               | 03/2014                          | 155.57<br>-                          | 206.42                         | 03/2016<br>-                          | 12/2017     | 32.69             |
| 45               | TAPOVAN-VISHNUGAD HEP (4X130MW)<br>- [N18000014]                                                                        | 11/2006                          | 2,978.48<br>-                        | 3,846.30                       | 03/2013<br>-                          | 06/2019     | 29.14             |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (September 2017) |                                                                                                                    |                                  |                                      |                                |                                       |             |                   |
|------------------|--------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                  |                                                                                                                    |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No             | Project                                                                                                            | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1                | 2                                                                                                                  | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 46               | BONGAIGAON THERMAL POWER PROJECT<br>- [N18000041]                                                                  | 01/2008                          | 4,375.35<br>-                        | 6,749.18                       | 09/2011<br>-                          | 12/2017     | 54.25             |
| 47               | SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID<br>[N18000169]                                                 | 08/2014                          | 288.49<br>-                          | 376.09                         | 02/2017<br>-                          | 03/2018     | 30.37             |
| 48               | EASTERN REGION STRENGTHENING SCHEME -IX<br>- [N18000171]                                                           | 02/2014                          | 196.58<br>-                          | 225.28                         | 02/2016<br>-                          | 12/2017     | 14.60             |
| 49               | TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP<br>[N18000180]                                                | 01/2015                          | 268.80<br>-                          | 340.88                         | 03/2018<br>-                          | 03/2018     | 26.82             |
| 50               | SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII<br>- [N18000182]                                                   | 01/2015                          | 203.28<br>-                          | 260.03                         | 07/2017<br>-                          | 12/2017     | 27.92             |
| 51               | EASTERN REGION STRENGTHENING SCHEME-III<br>- [N18000100]                                                           | 07/2010                          | 1,272.80<br>-                        | 1,731.10                       | 11/2012<br>-                          | 12/2017     | 36.01             |
| 52               | SYSTEM STRENGTHENING XII OF SR<br>- [N18000085]                                                                    | 02/2010                          | 232.34<br>-                          | 245.00                         | 06/2012<br>-                          | 12/2017     | 5.45              |
| 53               | DHUKWAN SMALL HYDRO PROJECT<br>- [N18000189]                                                                       | 05/2011                          | 195.42<br>-                          | 294.60                         | 02/2014<br>-                          | 12/2018     | 50.75             |
| 54               | BRBCL-NABINAGAR TPP- JV (4X250 MW)<br>- [N18000190]                                                                | 01/2007                          | 5,353.00<br>-                        | 7,998.00                       | 05/2014<br>-                          | 06/2018     | 49.41             |
| 55               | NPGCPL-NABINAGAR STPP - JV (3X660 MW)<br>- [N18000192]                                                             | 01/2013                          | 12,964.60<br>-                       | 13,731.26                      | 01/2018<br>-                          | 12/2018     | 5.91              |
| 56               | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT<br>[N18000194]                                    | 05/2015                          | 436.68<br>-                          | 602.44                         | 12/2016<br>-                          | 12/2017     | 37.96             |
| 57               | BOKARO THERMAL POWER STATION-A<br>- [N18000199]                                                                    | 08/2006                          | 2,313.00<br>4,139.00                 | 4,366.64                       | 12/2011<br>-                          | 02/2017     | 88.79             |
| 58               | RAGHUNATHPUR THERMAL POWER STATION PHASE-I<br>- [N18000202]                                                        | 04/2007                          | 4,122.00<br>8,781.00                 | 9,142.58                       | 02/2011<br>-                          | 03/2016     | 121.80            |
| 59               | KAMENG HYDROELECTRIC PROJECT (NEEPCO)<br>- [180100239]                                                             | 12/2004                          | 2,496.90<br>-                        | 6,179.96                       | 12/2009<br>06/2016                    | 03/2018     | 147.51            |
| 60               | COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103] | 09/2011                          | 1,940.13<br>-                        | 2,702.65                       | 09/2014<br>-                          | 12/2017     | 39.30             |
| 61               | TEHRI PUMPED STORAGE PLANT(1000MW)<br>- [N18000010]                                                                | 07/2006                          | 1,657.00<br>-                        | 3,939.11                       | 02/2016<br>-                          | 12/2020     | 137.73            |
| 62               | SYTEM STRENGTHENING XIII OF SR GRID<br>- [N18000109]                                                               | 10/2011                          | 487.49<br>-                          | 639.46                         | 06/2014<br>-                          | 06/2018     | 31.17             |
| 63               | PARE HYDRO ELECTRIC PROJECT<br>- [N18000045]                                                                       | 12/2008                          | 573.99<br>-                          | 1,337.76                       | 08/2013<br>-                          | 03/2018     | 133.06            |
| 64               | SYTEM STRENGTHENING OF SOUTHERN REGION - XIV<br>- [N18000115]                                                      | 12/2011                          | 297.33<br>-                          | 426.29                         | 08/2014<br>-                          | 12/2017     | 43.37             |
| 65               | SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH<br>- [N18000116]                 | 12/2011                          | 1,746.65<br>-                        | 2,228.71                       | 08/2014<br>-                          | 12/2017     | 27.60             |
| 66               | KISHANGANGA HEP (3X110 MW)<br>- [N18000031]                                                                        | 01/2009                          | 3,642.04<br>-                        | 5,882.01                       | 01/2016<br>-                          | 02/2018     | 61.50             |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (September 2017) |                                                                                                                       |                                  |                                      |                                |                                       |             |                   |
|------------------|-----------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                  |                                                                                                                       |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No             | Project                                                                                                               | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1                | 2                                                                                                                     | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 67               | KUNADANKULAM APP TRANS SYSTEM (PGCIL)<br>- [180100258]                                                                | 05/2005                          | 1,779.29<br>-                        | 2,187.32                       | 11/2008<br>-                          | 09/2018     | 22.93             |
| 68               | BARH STPP(3X660MW) NTPC<br>- [180100242]                                                                              | 02/2005                          | 8,692.97<br>-                        | 15,095.67                      | 01/2011<br>-                          | 03/2019     | 73.65             |
| 69               | TUIRIAL HYDRO ELECTRIC PROJECT (60MW)<br>- [N18000119]                                                                | 07/1998                          | 368.72<br>-                          | 1,329.43                       | 07/2006<br>02/2015                    | 11/2017     | 260.55            |
| 70               | TRIPURA GAS BASED POWER PROJECT<br>- [N18000071]                                                                      | 07/2009                          | 421.01<br>-                          | 1,078.31                       | 07/2013<br>-                          | -           | 156.12            |
| 71               | NORTHERN REGION SYSTEM STRENGTHENING<br>SCHEME-XXIV<br>- [N18000128]                                                  | 11/2011                          | 723.63<br>-                          | 882.13                         | 11/2014<br>-                          | 12/2017     | 21.90             |
| 72               | COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND<br>NCC POWER PROJECTS IN SRIKAKULAM AREA A.P.<br>PART- C - [N18000143] | 03/2013                          | 514.20<br>-                          | 703.10                         | 06/2015<br>-                          | 03/2018     | 36.74             |
| 73               | TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG<br>(SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT<br>- [N18000215]        | 01/2014                          | 1,788.41<br>-                        | 2,352.57                       | 09/2017<br>-                          | 09/2018     | 31.55             |
| 74               | ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-<br>II TIPS<br>- [N18000222]                                             | 04/2016                          | 790.13<br>-                          | 790.30                         | 06/2019<br>-                          | 06/2019     | .02               |
| 75               | PAKRI BARWADIH COAL MINING PROJECT<br>- [N18000225]                                                                   | 10/2004                          | 4,237.96<br>4,238.00                 | 4,552.00                       | 10/2017<br>-                          | 10/2017     | 7.41              |
| 76               | TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF<br>NAGAPATTINAM/ CUDDALORE AREA PACKAGE A<br>- [N18000253]                | 03/2015                          | 955.00<br>-                          | 1,364.00                       | 12/2015<br>-                          | 03/2018     | 42.83             |
| 77               | TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF<br>NAGAPATTINAM CUDDALORE AREA – PACKAGE A<br>- [N18000259]               | 03/2015                          | 955.00<br>1,161.00                   | 1,364.00                       | 12/2015<br>-                          | 03/2018     | 42.83             |
|                  | Total                                                                                                                 |                                  | 1,05,404.62<br>-                     | 1,63,161.49                    |                                       |             |                   |
|                  |                                                                                                                       |                                  |                                      |                                |                                       |             |                   |
|                  | <u>RAILWAYS</u>                                                                                                       |                                  |                                      |                                |                                       |             |                   |
| 78               | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL,<br>(NCR)<br>- [220100007]                                                 | 04/1986                          | 158.77<br>274.56                     | 634.48                         | 03/1994<br>-                          | -           | 299.62            |
| 79               | NEW BG RLY LINE FROM EKLAKHI-BALURGHAT<br>INCLUDING GAZOLE-ITAHAR(NL),NEFR<br>[220100135]                             | 04/1983                          | 36.80<br>274.41                      | 614.00                         | -<br>-                                | -           | 1,568.48          |
| 80               | CALICUT-MANGALORE (DL) (SR)<br>- [220100151]                                                                          | 02/1996                          | 240.00<br>-                          | 579.37                         | -<br>-                                | -           | 141.40            |
| 81               | KARUR-SALEM(NL),SR<br>- [220100191]                                                                                   | 02/1997                          | 155.55<br>-                          | 870.00                         | -<br>-                                | -           | 459.31            |
| 82               | KATIHAR - JOGBANI (GC)(NEFR)<br>- [220100247]                                                                         | 09/2001                          | 492.98<br>-                          | 1,320.00                       | 12/2010<br>-                          | -           | 167.76            |
| 83               | GULBARGA-BIDAR,SCR(NL)<br>- [220100254]                                                                               | 02/1998                          | 242.42<br>369.70                     | 1,542.41                       | -<br>05/2009                          | -           | 536.26            |
| 84               | QUILON-TIRUNELVELI-TENKASI-<br>VIRUDHUNAGAR(SR)(GC)<br>[220100263]                                                    | 03/1998                          | 280.00<br>-                          | 1,122.00                       | -<br>-                                | -           | 300.71            |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (September 2017) |                                                                                                     |                                  |                                      |                                |                                       |             |                   |
|------------------|-----------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                  |                                                                                                     |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No             | Project                                                                                             | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1                | 2                                                                                                   | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 85               | KOTLPALLI-NARASAPUR (NL) (SCR)<br>- [220100265                                                      | 12/2001                          | 330.00<br>-                          | 2,125.18                       | -<br>-                                | 03/2021     | 543.99            |
| 86               | TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-<br>NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)<br>- [220100268 | 03/2000                          | 1,049.69<br>-                        | 3,404.92                       | 12/2006<br>-                          | -           | 224.37            |
| 87               | GADWAL - RAICHUR (NL), SCR<br>- [220100270                                                          | 04/1998                          | 92.63<br>-                           | 350.00                         | 02/2011<br>-                          | -           | 277.85            |
| 88               | TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER<br>- [220100272                                         | 04/2000                          | 1,188.91<br>-                        | 1,319.33                       | -<br>12/2009                          | 03/2019     | 10.97             |
| 89               | DEOGHAR - SULTANGANJ (INL), ER<br>- [220100273                                                      | 04/2000                          | 607.09<br>-                          | 973.33                         | 12/2012<br>12/2012                    | -           | 60.33             |
| 90               | JIND-SONEPAT (NL),NR<br>- [220100280                                                                | 01/2004                          | 238.56<br>-                          | 740.00                         | 03/2012<br>-                          | -           | 210.19            |
| 91               | HARIDASPUR-PARADEEP(NL)<br>- [220100285                                                             | 04/1996                          | 301.64<br>-                          | 1,185.64                       | -<br>09/2009                          | 03/2019     | 293.06            |
| 92               | RAMGANJMUUNDI-BHOPAL (NL),WCR<br>- [220100314                                                       | 04/2001                          | 470.92<br>727.13                     | 2,713.09                       | -<br>-                                | 03/2021     | 476.13            |
| 93               | MAHARAJGANJ-MASRAKH (NL) - NER<br>- [220100316                                                      | 04/2003                          | 218.19<br>-                          | 412.05                         | -<br>-                                | 03/2018     | 88.85             |
| 94               | KICHHA-KHATIMA (NL) - NER<br>- [220100317                                                           | 04/2003                          | 142.45<br>-                          | 228.40                         | -<br>-                                | -           | 60.34             |
| 95               | ETAWAH-MAINPURI (NL),NCR<br>- [220100318                                                            | 04/1997                          | 120.00<br>-                          | 245.39                         | 12/2008<br>-                          | -           | 104.49            |
| 96               | HATHUA-BHATNI (N L) (NER)<br>- [220100319                                                           | 04/2005                          | 230.03<br>-                          | 718.54                         | -<br>-                                | 05/2019     | 212.37            |
| 97               | CHHINDWARA - NAGPUR (GC)(SECR)<br>- [220100324                                                      | 04/2005                          | 383.79<br>-                          | 1,101.16                       | -<br>-                                | -           | 186.92            |
| 98               | SUKINDA ROAD - ANGUL (NL)(ECOR)<br>- [220100325                                                     | 04/1998                          | 183.23<br>-                          | 1,202.70                       | 02/2015<br>-                          | 12/2019     | 556.39            |
| 99               | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)<br>- [220100327                                           | 04/2000                          | 133.41<br>207.00                     | 340.00                         | 03/2009<br>03/2009                    | 12/2017     | 154.85            |
| 100              | TALCHER-BIMALAGARH(NL)(ECOR)<br>- [220100328                                                        | 04/2005                          | 810.78<br>-                          | 1,928.07                       | -<br>-                                | 12/2022     | 137.80            |
| 101              | RAICHUR-GUNTAKAL(DL)(SCR)<br>- [220100329                                                           | 04/2003                          | 136.62<br>-                          | 376.00                         | 12/2007<br>03/2010                    | -           | 175.22            |
| 102              | GOELKERA-MANOHARPUR,(LD)(SER)<br>- [N22000045                                                       | 03/1997                          | 261.70<br>-                          | 388.00                         | 02/2006<br>-                          | 12/2019     | 48.26             |
| 103              | BHOPAL BINA 3D LINE DOUBLING<br>- [N22000077                                                        | 09/2007                          | 687.20<br>-                          | 950.00                         | 03/2010<br>-                          | 03/2018     | 38.24             |
| 104              | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU<br>'POND' AGASTIYAMPALLI<br>[N22000079                     | 09/2007                          | 404.19<br>-                          | 2,072.50                       | -<br>-                                | -           | 412.75            |
| 105              | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND<br>COIMBATORE<br>- [N22000080                                | 09/2006                          | 343.17<br>-                          | 1,065.00                       | -<br>-                                | -           | 210.34            |
| 106              | ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR<br>AND G'BAD-MEERUT<br>- [N22000094                     | 02/2008                          | 171.10<br>-                          | 275.08                         | 03/2012<br>-                          | -           | 60.77             |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (September 2017) |                                                                                                                         |                                  |                                      |                                |                                       |             |                      |
|------------------|-------------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|----------------------|
|                  |                                                                                                                         |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                      |
| S.No             | Project                                                                                                                 | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated<br>Cost (Rs.crore) | Original/<br>Revised                  | Anticipated | Cost Overruns<br>(%) |
| 1                | 2                                                                                                                       | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                    |
| 107              | BHAIRABI SAIRONG, NL, NEFR<br>- [N22000100]                                                                             | 04/2008                          | 619.34<br>-                          | 4,600.00                       | 04/2014<br>-                          | 03/2020     | 642.73               |
| 108              | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN<br>ECR<br>- [N22000002]                                                   | 04/1996                          | 332.92<br>283.95                     | 477.88                         | 03/2012<br>-                          | -           | 43.54                |
| 109              | MANOHARABAD-KOTHPALL NEW LINE(SCR)<br>- [N22000032]                                                                     | 04/2006                          | 378.56<br>-                          | 1,160.47                       | -<br>-                                | 03/2022     | 206.55               |
| 110              | OBULAVARIPALLE-KRISHNAPATNAM(RVNL)<br>- [N22000049]                                                                     | 07/2006                          | 743.00<br>-                          | 1,825.00                       | 03/2008<br>06/2008                    | 03/2020     | 145.63               |
| 111              | JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE<br>CONVERSION (NWR)<br>- [N22000113]                                   | 04/2008                          | 653.19<br>-                          | 941.04                         | 03/2014<br>-                          | 06/2019     | 44.07                |
| 112              | RATLAM-MHOW-KHANDWA-AKOLA (GC)<br>- [N22000120]                                                                         | 04/2008                          | 603.04<br>-                          | 1,030.29                       | 03/2012<br>-                          | -           | 70.85                |
| 113              | BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG<br>COACHES POH PER MONTH (WR)<br>- [N22000125]                                  | 04/2006                          | 117.36<br>196.95                     | 203.00                         | 03/2011<br>-                          | -           | 72.97                |
| 114              | KATAKHAL TO BHAIRABI<br>- [N22000126]                                                                                   | 04/1998                          | 227.90<br>-                          | 509.00                         | 12/2012<br>-                          | 05/2016     | 123.34               |
| 115              | WARDHA-NANDED MAHARASHTRA<br>- [N22000231]                                                                              | 04/2008                          | 499.30<br>-                          | 3,168.29                       | -<br>-                                | 03/2023     | 534.55               |
| 116              | KALYAN-KASARA 3RD LINE<br>- [N22000233]                                                                                 | 04/2011                          | 277.70<br>-                          | 792.89                         | -<br>-                                | 03/2021     | 185.52               |
| 117              | TARAKESHWAR-MAGRA NEW BG LINE<br>- [N22000235]                                                                          | 04/2010                          | 365.17<br>-                          | 365.67                         | -<br>-                                | -           | .14                  |
| 118              | HANSDIHA-GODDA NL<br>- [N22000236]                                                                                      | 04/2011                          | 267.09<br>-                          | 350.78                         | -<br>-                                | -           | 31.33                |
| 119              | MAGRAHAT-DIAMOND HARBOUR WITH MM<br>SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND<br>HATBOUR - BAHRAHAT-KULPI NL - [N22000243] | 04/2009                          | 493.96<br>-                          | 681.68                         | -<br>-                                | -           | 38.00                |
| 120              | KATWA-PATULI DOUBLING WITH NEW MM FOR<br>AHMEDPUR-KATWA GC<br>- [N22000245]                                             | 04/2010                          | 423.66<br>-                          | 720.59                         | 03/2017<br>-                          | -           | 70.09                |
| 121              | 3RD LINE BETWEEN BHUSAWAL-JALGAON<br>- [N22000247]                                                                      | 04/2011                          | 184.06<br>-                          | 199.12                         | -<br>-                                | -           | 8.18                 |
| 122              | WARDHA-SEWAGRAM NGP 3RD LINE<br>- [N22000250]                                                                           | 04/2012                          | 297.85<br>-                          | 540.02                         | -<br>-                                | 03/2022     | 81.31                |
| 123              | PEN ROHA DOUBLING<br>- [N22000254]                                                                                      | 04/2007                          | 98.74<br>-                           | 381.39                         | -<br>-                                | -           | 286.26               |
| 124              | PANVEL PEN DOUBLING<br>- [N22000255]                                                                                    | 04/2006                          | 96.16<br>-                           | 280.00                         | -<br>-                                | -           | 191.18               |
| 125              | TUMKUR-CHITRADURGA-DAVENGERE NL<br>- [N22000256]                                                                        | 04/2011                          | 913.00<br>-                          | 1,801.01                       | -<br>-                                | -           | 97.26                |
| 126              | MUNIRABAD (GINGERA) -RAICHUR NL<br>- [N22000257]                                                                        | 04/2007                          | 179.65<br>-                          | 1,350.91                       | -<br>-                                | -           | 651.97               |
| 127              | BAGALKOT-KUDACHI NL<br>- [N22000258]                                                                                    | 04/2010                          | 377.93<br>-                          | 986.30                         | -<br>-                                | -           | 160.97               |
| 128              | KAZIPET-VIJAYAWADA 3RD LINE WITH<br>ELECTRIFICATION<br>- [N22000261]                                                    | 04/2012                          | 1,054.35<br>-                        | 2,200.00                       | -<br>-                                | -           | 108.66               |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (September 2017) |                                                                     |                                  |                                      |                                |                                       |             |                   |
|------------------|---------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                  |                                                                     |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No             | Project                                                             | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1                | 2                                                                   | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 129              | GUDUR-DURGARAJAPATNAM<br>- [N22000265]                              | 04/2011                          | 283.54<br>-                          | 759.41                         | -<br>-                                | -           | 167.83            |
| 130              | GRADE SEPERATOR AT DAYABASTI<br>- [N22000269]                       | 04/1999                          | 156.65<br>-                          | 197.17                         | -<br>-                                | -           | 25.87             |
| 131              | ROHTAK-MEHAM HANSI<br>- [N22000272]                                 | 04/2012                          | 287.00<br>-                          | 625.00                         | -<br>-                                | -           | 117.77            |
| 132              | BHANUPALI-BILASPUR BERI NL<br>- [N22000273]                         | 04/2008                          | 1,046.88<br>-                        | 4,500.00                       | -<br>-                                | -           | 329.85            |
| 133              | CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI<br>NILAYAM NL - [N22000276] | 04/2013                          | 558.00<br>-                          | 692.43                         | -<br>-                                | -           | 24.09             |
| 134              | SRINIVASA-PURA-MADANAPALLI NL<br>- [N22000277]                      | 04/2013                          | 296.00<br>-                          | 466.65                         | -<br>-                                | -           | 57.65             |
| 135              | SHIMOGA-HARIHAR NL<br>- [N22000278]                                 | 04/2011                          | 562.74<br>-                          | 832.47                         | -<br>-                                | -           | 47.93             |
| 136              | RAYADURGA-TUMKUR NL<br>- [N22000279]                                | 04/2007                          | 970.34<br>-                          | 1,714.49                       | -<br>-                                | -           | 76.69             |
| 137              | WHITE FIELD-KOLAR NL<br>- [N22000280]                               | 04/2011                          | 341.05<br>-                          | 348.85                         | -<br>-                                | -           | 2.29              |
| 138              | BHADRACHALAM ROAD-SATTUPALLI<br>- [N22000287]                       | 04/2010                          | 337.49<br>-                          | 792.01                         | -<br>-                                | -           | 134.68            |
| 139              | HARIDWAR-LAKSAR<br>- [N22000289]                                    | 04/2012                          | 219.83<br>-                          | 346.63                         | -<br>-                                | -           | 57.68             |
| 140              | CHANDIGARH-BADDI NL<br>- [N22000296]                                | 04/2007                          | 328.14<br>-                          | 1,540.00                       | -<br>-                                | -           | 369.31            |
| 141              | TORANAGALLU-RANJITPURA DL<br>- [N22000298]                          | 04/2011                          | 146.75<br>-                          | 167.50                         | -<br>-                                | -           | 14.14             |
| 142              | GADAG-WADI NL<br>- [N22000299]                                      | 04/2013                          | 1,117.00<br>-                        | 1,922.00                       | -<br>-                                | -           | 72.07             |
| 143              | CHIKBALLA-PUR-GOWRIBIDANUR NL<br>- [N22000300]                      | 04/2013                          | 327.25<br>-                          | 367.77                         | -<br>-                                | -           | 12.38             |
| 144              | MONIGRAM- NIMTITA<br>- [N22000301]                                  | 04/2012                          | 250.93<br>-                          | 259.23                         | -<br>-                                | -           | 3.31              |
| 145              | BAZAR SAU -AZIMGANJ JN. DOUBLING<br>- [N22000302]                   | 04/2012                          | 255.64<br>-                          | 272.20                         | -<br>-                                | -           | 6.48              |
| 146              | JAGGAYYAPET - MELLACHERUVU<br>- [N22000304]                         | 04/2007                          | 313.24<br>-                          | 554.70                         | 01/1999<br>-                          | -           | 77.08             |
| 147              | MM FROM BURAMARA-CHAKULIA<br>- [N22000305]                          | 04/2008                          | 466.48<br>-                          | 750.00                         | 01/1999<br>-                          | -           | 60.78             |
| 148              | MM FROM PANSKURA-GHATAL NL<br>- [N22000309]                         | 04/2011                          | 276.69<br>-                          | 426.00                         | 01/1999<br>-                          | -           | 53.96             |
| 149              | AHMEDNAGAR-PARLI VAIJNATH(NL) CR<br>- [220100181]                   | 02/1997                          | 514.68<br>-                          | 2,271.50                       | -<br>-                                | -           | 341.34            |
| 150              | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE<br>LINE(MTP) - [220100164]  | 03/1996                          | 495.44<br>-                          | 1,781.98                       | 03/2004<br>-                          | 03/2020     | 259.68            |
| 151              | MANDARHILL-DUMKA-RAMPURHAT (NL),ER<br>- [220100168]                 | 04/1995                          | 900.05<br>-                          | 1,125.89                       | 12/2011<br>12/2010                    | 03/2020     | 25.09             |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (September 2017) |                                                                                          |                               |                                   |                             |                                    |             |                   |
|------------------|------------------------------------------------------------------------------------------|-------------------------------|-----------------------------------|-----------------------------|------------------------------------|-------------|-------------------|
|                  |                                                                                          |                               |                                   |                             | Date of Commissioning (Month/Year) |             |                   |
| S.No             | Project                                                                                  | Date of Approval (Month/Year) | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised                  | Anticipated | Cost Overruns (%) |
| 1                | 2                                                                                        | 3                             | 4                                 | 5                           | 6                                  | 7           | 8                 |
| 152              | BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR<br>- [220100201]                            | 09/1997                       | 1,500.00<br>-                     | 5,000.00                    | 04/2008<br>12/2011                 | 06/2018     | 233.33            |
| 153              | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)<br>- [220100232]                                  | 09/1998                       | 247.66<br>-                       | 6,093.31                    | 05/2008<br>-                       | 03/2023     | 2,360.35          |
| 154              | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR<br>- [220100240]                              | 04/1997                       | 501.69<br>335.77                  | 1,043.56                    | 03/2012<br>-                       | -           | 108.01            |
| 155              | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR<br>- [220100243]                              | 04/1999                       | 108.00<br>-                       | 432.72                      | 12/2009<br>-                       | -           | 300.67            |
| 156              | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)<br>- [220100257]                                   | 04/1997                       | 162.87<br>-                       | 541.00                      | -<br>-                             | -           | 232.17            |
| 157              | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR<br>- [220100266]                 | 04/2000                       | 733.00<br>-                       | 3,010.00                    | 12/2008<br>-                       | 03/2019     | 310.64            |
| 158              | KHURDA ROAD-BOLANGIR(NL)ECOR<br>- [220100284]                                            | 04/1994                       | 470.21<br>-                       | 3,004.90                    | -<br>-                             | 06/2021     | 539.05            |
| 159              | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)<br>- [220100288]                                     | 04/2003                       | 727.56<br>-                       | 9,658.00                    | 03/2011<br>-                       | 03/2020     | 1,227.45          |
| 160              | KOSI BRIDGE (NL), ECR<br>- [220100304]                                                   | 04/2002                       | 322.95<br>-                       | 341.41                      | 03/2012<br>-                       | -           | 5.72              |
| 161              | ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR<br>- [N22000082]                      | 12/2006                       | 170.00<br>-                       | 436.00                      | 03/2011<br>-                       | 10/2011     | 156.47            |
| 162              | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR<br>- [N22000086]         | 09/2006                       | 200.00<br>-                       | 780.00                      | -<br>-                             | 03/2019     | 290.00            |
| 163              | NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR<br>[N22000087]                  | 09/2006                       | 300.00<br>-                       | 2,145.00                    | -<br>-                             | 03/2020     | 615.00            |
| 164              | NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)<br>[N22000124]            | 04/2006                       | 850.00<br>-                       | 3,000.00                    | 03/2015<br>-                       | 03/2020     | 252.94            |
| 165              | MUMBAI URBAN TRANSPORT PROJECT PHASE-II<br>- [N22000092]                                 | 04/2008                       | 5,300.00<br>-                     | 7,986.04                    | 03/2014<br>-                       | 03/2019     | 50.68             |
| 166              | BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)<br>[N22000119] | 04/1999                       | 207.52<br>-                       | 334.87                      | 12/2012<br>-                       | -           | 61.37             |
| 167              | LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT<br>[N22000127]    | 04/1996                       | 1,676.31<br>-                     | 7,000.00                    | 03/2009<br>-                       | 03/2018     | 317.58            |
| 168              | AGARTALA SABROOM, NL, NEFR<br>- [N22000099]                                              | 04/2008                       | 813.34<br>-                       | 3,451.00                    | 03/2014<br>-                       | 03/2020     | 324.30            |
| 169              | KISHANGANJ JALALGARH, NL, NEFR<br>- [N22000101]                                          | 04/2008                       | 282.92<br>-                       | 360.00                      | -<br>-                             | -           | 27.24             |
| 170              | SEVOK RANGPO, NEFR<br>- [N22000102]                                                      | 04/2008                       | 1,339.48<br>-                     | 4,084.69                    | 12/2015<br>-                       | 03/2020     | 204.95            |
| 171              | KANPUR KASGANJ MATHURA(GC) NER<br>- [220100197]                                          | 03/1997                       | 677.97<br>1,062.36                | 1,679.13                    | -<br>-                             | -           | 147.67            |
| 172              | KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)<br>- [220100256]                                 | 04/1999                       | 744.71<br>-                       | 1,126.79                    | -<br>-                             | -           | 51.31             |



## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (September 2017) |                                                                                                                     |                                  |                                      |                                |                                       |             |                   |
|------------------|---------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                  |                                                                                                                     |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No             | Project                                                                                                             | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1                | 2                                                                                                                   | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 173              | DAUSA-GANGAPUR CITY(NL),NWR<br>- [220100184                                                                         | 02/1997                          | 410.08<br>-                          | 780.98                         | -<br>-                                | 08/2018     | 90.45             |
| 174              | SURATPURA - HANUMANGARH - SRIGANGANAGAR<br>GUAGE CONVERSION (NWR)<br>[N22000114                                     | 04/2008                          | 516.23<br>-                          | 735.00                         | 03/2014<br>-                          | -           | 42.38             |
| 175              | NANGALDAM-TALWARA(NL),NR<br>- [220100188                                                                            | 03/1981                          | 450.00<br>-                          | 2,100.00                       | 07/2012<br>-                          | -           | 366.67            |
| 176              | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR<br>- [220100133                                                                 | 03/1995                          | 2,500.00<br>-                        | 19,565.00                      | 11/2002<br>-                          | 12/2018     | 682.60            |
| 177              | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR<br>- [220100258                                                              | 03/2002                          | 625.30<br>408.76                     | 876.10                         | 06/2007<br>-                          | -           | 40.11             |
| 178              | UTRATIA-ZAFRABAD, NR (LINE DOUBLING)<br>- [N22000088                                                                | 04/2006                          | 325.00<br>-                          | 1,581.53                       | 03/2010<br>-                          | -           | 386.62            |
| 179              | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-<br>JAGDALPUR),NL,RVNL - [220100149                                   | 04/1995                          | 304.00<br>-                          | 1,195.00                       | 12/2012<br>-                          | -           | 293.09            |
| 180              | RAJATGARH-BARANG(LD),ECOR<br>- [220100286                                                                           | 04/1999                          | 166.16<br>-                          | 380.00                         | 02/2009<br>02/2009                    | 06/2017     | 128.70            |
| 181              | SALKA ROAD -ANUPNAGAR LINE DOUBLING<br>- [N22000075                                                                 | 09/2006                          | 324.90<br>-                          | 516.40                         | 03/2010<br>-                          | 12/2017     | 58.94             |
| 182              | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY<br>FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT<br>(MTP) - [N22000110     | 04/2010                          | 3,951.98<br>-                        | 4,259.48                       | 03/2016<br>-                          | 12/2020     | 7.78              |
| 183              | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY<br>FROM BARANAGAR TO BARRACKPORE AND<br>DAKSHINESHWAR (MTP) - [N22000109 | 04/2010                          | 2,298.42<br>-                        | 2,733.86                       | 03/2014<br>-                          | -           | 18.95             |
| 184              | NANDYAL-YERRAGUNTLA(NL),SCR<br>- [220100192                                                                         | 03/1996                          | 155.74<br>164.36                     | 966.98                         | 02/2009<br>-                          | 12/2017     | 520.89            |
| 185              | MUNEERABAD-MAHABOBNAGAR(NL),SCR<br>- [220100205                                                                     | 04/1997                          | 218.24<br>236.41                     | 525.00                         | -<br>-                                | 03/2019     | 140.56            |
| 186              | MACHERLA-NALGONDA(NL)(SCR)<br>- [220100220                                                                          | 07/1998                          | 125.00<br>-                          | 480.00                         | 07/2008<br>-                          | -           | 284.00            |
| 187              | GONDIA-JABALPUR(GC),(SECR)<br>- [220100186                                                                          | 02/1997                          | 386.30<br>-                          | 1,776.81                       | 03/1998<br>-                          | 12/2019     | 359.96            |
| 188              | HOWRAH-AMTA-CHAMPADANGA NL (SER)<br>- [220100208                                                                    | 04/1974                          | 393.46<br>154.30                     | 1,026.00                       | 03/2007<br>03/2007                    | -           | 160.76            |
| 189              | TAMLUK DIGHA,LINE DOUBLING (SER)<br>- [N22000097                                                                    | 03/1984                          | 293.97<br>-                          | 749.69                         | 06/2005<br>-                          | -           | 155.02            |
| 190              | RANCHI-LOHARDAGA(GC),SER<br>- [220100214                                                                            | 04/1997                          | 194.07<br>-                          | 491.33                         | 06/2004<br>-                          | -           | 153.17            |
| 191              | HUBLI-ANKOLA(NL),SWR<br>- [220100193                                                                                | 04/1997                          | 227.00<br>-                          | 2,135.00                       | -<br>-                                | -           | 840.53            |
| 192              | GONDA GORAKHPUR LOOP WITH ANAND NAGAR<br>NAUTANWA GC (260 KM)<br>[N22000345                                         | 04/1997                          | 836.26<br>-                          | 1,072.52                       | -<br>-                                | -           | 28.25             |
| 193              | HASSAN-BANGALORE VIA SHRAVANA-<br>BELGOLA(NL),SWR<br>[220100183                                                     | 02/1997                          | 295.00<br>-                          | 1,289.92                       | -<br>-                                | 01/2017     | 337.26            |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (September 2017) |                                                                                                          |                                  |                                      |                                |                                       |                 |                         |
|------------------|----------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-----------------|-------------------------|
|                  |                                                                                                          |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |                 |                         |
| S.No             | Project                                                                                                  | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated<br>Cost (Rs.crore) | Original/<br>Revised                  | Antici<br>Pated | Cost<br>Overruns<br>(%) |
| 1                | 2                                                                                                        | 3                                | 4                                    | 5                              | 6                                     | 7               | 8                       |
| 194              | BANGLORE - SATYAMANGALAM (NL)(SWR)<br>- [220100274                                                       | 04/1996                          | 138.00<br>-                          | 1,382.78                       | -<br>-                                | -               | 902.01                  |
| 195              | RAMANAGRAM-MYSORE DOUBLING WITH<br>ELECTRIFICATION OF KENGESII- MUSORE (SWR)<br>- [N22000107             | 04/2007                          | 482.00<br>-                          | 874.57                         | 03/2013<br>-                          | -               | 81.45                   |
| 196              | TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)<br>- [220100262                                                  | 09/1995                          | 100.00<br>-                          | 980.00                         | -<br>-                                | -               | 880.00                  |
| 197              | BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO<br>VAYOR (WR) - [N22000123                                 | 04/2008                          | 318.24<br>-                          | 321.62                         | 03/2012<br>-                          | 03/2019         | 1.06                    |
| 198              | SAMBALPUR-TALCHER DOUBLING<br>- [N22000315                                                               | 03/2011                          | 679.27<br>-                          | 1,579.27                       | -<br>-                                | 03/2021         | 132.50                  |
| 199              | JHARSUGUDA-RENGALI DOUBLING<br>- [N22000317                                                              | 03/2006                          | 201.00<br>-                          | 230.00                         | -<br>-                                | -               | 14.43                   |
| 200              | KIRANDUL - JAGDALPUR DOUBLING<br>- [N22000318                                                            | 12/2012                          | 826.57<br>-                          | 1,160.83                       | -<br>-                                | 03/2020         | 40.44                   |
| 201              | SAMBALPUR - ANGUL RLY. ELECTRIFICATION<br>- [N22000319                                                   | 03/2012                          | 155.81<br>-                          | 238.03                         | -<br>-                                | 03/2020         | 52.77                   |
| 202              | DELANG-PURI DOUBLING<br>- [N22000320                                                                     | 03/2011                          | 165.16<br>-                          | 234.71                         | 03/2015<br>-                          | -               | 42.11                   |
| 203              | GHAZIPUR - AUNRIHAR (40 KM)<br>- [N22000321                                                              | 04/2014                          | 182.92<br>-                          | 197.73                         | -<br>-                                | -               | 8.10                    |
| 204              | THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH<br>BYE-PASS LINE BEFORE PONMALAI (1.13 KM)<br>- [N22000322 | 04/2011                          | 190.10<br>-                          | 350.00                         | -<br>-                                | 03/2019         | 84.11                   |
| 205              | RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM)<br>JHARKHAND - [N22000323                                    | 04/2012                          | 148.77<br>-                          | 209.00                         | 12/2016<br>-                          | -               | 40.49                   |
| 206              | HOSADURGA - CHICKJAJUR (28.89 KM)<br>- [N22000324                                                        | 04/2010                          | 203.40<br>-                          | 273.84                         | -<br>-                                | -               | 34.63                   |
| 207              | PHULERA - DIGANA DOUBLING<br>- [N22000326                                                                | 05/2015                          | 600.00<br>-                          | 648.00                         | -<br>-                                | 03/2020         | 8.00                    |
| 208              | HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)<br>- [N22000112                                             | 04/2008                          | 829.74<br>-                          | 1,161.64                       | 03/2015<br>-                          | 12/2019         | 40.00                   |
| 209              | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)<br>- [220100106                                                   | 12/1994                          | 124.43<br>-                          | 1,010.00                       | -<br>-                                | -               | 711.70                  |
| 210              | AMRAVATI-NARKHER NL(CR)<br>- [220100118                                                                  | 06/1994                          | 663.01<br>175.30                     | 858.97                         | 06/1999<br>-                          | -               | 29.56                   |
| 211              | ANGAMALI-SABARIMALA (N.L.)(SR)<br>- [220100252                                                           | 10/1998                          | 550.00<br>-                          | 2,815.62                       | -<br>-                                | 01/2018         | 411.93                  |
| 212              | ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP<br>- [N22000130                                                    | 03/2013                          | 307.00<br>-                          | 308.00                         | -<br>-                                | -               | .33                     |
| 213              | CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ<br>UP - [N22000131                                           | 03/2007                          | 243.78<br>-                          | 268.78                         | -<br>-                                | 08/2017         | 10.26                   |
| 214              | BHOJIPUR TANAKPUR VIA PILIBHIT<br>- [N22000132                                                           | 03/2008                          | 195.64<br>-                          | 474.30                         | -<br>-                                | 10/2017         | 142.44                  |
| 215              | CHHAPRA-BALLIA UP<br>- [N22000134                                                                        | 03/2013                          | 295.00<br>-                          | 477.31                         | -<br>-                                | 10/2018         | 61.80                   |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (September 2017) |                                                                                                                    |                                  |                                      |                                |                                       |                 |                         |
|------------------|--------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-----------------|-------------------------|
|                  |                                                                                                                    |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |                 |                         |
| S.No             | Project                                                                                                            | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated<br>Cost (Rs.crore) | Original/<br>Revised                  | Antici<br>Pated | Cost<br>Overruns<br>(%) |
| 1                | 2                                                                                                                  | 3                                | 4                                    | 5                              | 6                                     | 7               | 8                       |
| 216              | KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI<br>NAUGARH UP<br>- [N22000136]                                     | 03/2013                          | 643.00<br>-                          | 644.00                         | -<br>-                                | -               | .16                     |
| 217              | BANGURGRAM-GURIYA PATCH DOUBLING<br>- [N22000137]                                                                  | 04/2012                          | 246.08<br>-                          | 348.55                         | -<br>-                                | 03/2019         | 41.64                   |
| 218              | AHMEDABAD-BOTAD (GC)<br>- [N22000140]                                                                              | 04/2012                          | 567.18<br>-                          | 975.62                         | -<br>-                                | 03/2020         | 72.01                   |
| 219              | DHASA-JETALSAR (GC)<br>- [N22000141]                                                                               | 04/2012                          | 376.59<br>-                          | 644.38                         | -<br>-                                | 12/2020         | 71.11                   |
| 220              | MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)<br>- [N22000142]                                                                | 04/2011                          | 439.88<br>-                          | 845.68                         | -<br>-                                | -               | 92.25                   |
| 221              | RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW<br>MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR<br>(GC) - [N22000143]  | 04/1994                          | 320.66<br>-                          | 399.63                         | -<br>-                                | 03/2019         | 24.63                   |
| 222              | PALANPUR-SAMAKHAYALI (DL)<br>- [N22000144]                                                                         | 04/2013                          | 1,266.89<br>-                        | 1,548.66                       | -<br>-                                | 12/2020         | 22.24                   |
| 223              | VIRAMGAM-SAMAKHIALI (DL)<br>- [N22000145]                                                                          | 04/2011                          | 446.00<br>-                          | 1,037.15                       | -<br>-                                | 03/2019         | 132.54                  |
| 224              | VIRAMGAM-SURENDRANAGAR (DL)<br>- [N22000146]                                                                       | 04/2010                          | 279.40<br>-                          | 355.00                         | -<br>-                                | -               | 27.06                   |
| 225              | RATLAM-DUNGARPUR VIA BANSWARA (NL)<br>- [N22000147]                                                                | 04/2011                          | 2,082.75<br>-                        | 2,562.27                       | -<br>-                                | -               | 23.02                   |
| 226              | GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA<br>(GC) - [N22000148]                                                    | 04/2011                          | 1,176.09<br>-                        | 3,845.60                       | 02/2020<br>-                          | 12/2022         | 226.98                  |
| 227              | THIYAT HAMIRA-SANU<br>- [N22000149]                                                                                | 04/2013                          | 236.93<br>-                          | 276.89                         | -<br>-                                | 10/2018         | 16.87                   |
| 228              | MAVLI JUNCTION-BARI SADRI, MM OF AJMER-<br>CHITTSURGARH-UDAIPUR<br>[N22000152]                                     | 04/2013                          | 456.00<br>-                          | 855.16                         | -<br>-                                | 05/2018         | 87.54                   |
| 229              | RATANGARH-SARDARSAHAR (MM OF SADULPUR-<br>BIKANER AND RATANGARH-DEGANA GC)<br>- [N22000153]                        | 04/2010                          | 739.65<br>-                          | 872.22                         | -<br>-                                | -               | 17.92                   |
| 230              | GURIYA-MARWAR AND KARJODA-PALANPUR<br>- [N22000154]                                                                | 04/2011                          | 239.73<br>-                          | 257.78                         | -<br>-                                | -               | 7.53                    |
| 231              | AJMER-BANGURGRAM<br>- [N22000155]                                                                                  | 04/2011                          | 213.39<br>-                          | 272.99                         | -<br>-                                | 03/2019         | 27.93                   |
| 232              | RANI-MARWAR JN. PATCH DOUBLING<br>- [N22000156]                                                                    | 04/2012                          | 288.97<br>-                          | 369.08                         | -<br>-                                | 10/2018         | 27.72                   |
| 233              | ALWAR-BANDIKUI DOUBLING<br>- [N22000157]                                                                           | 04/2013                          | 242.09<br>-                          | 293.68                         | -<br>-                                | 03/2019         | 21.31                   |
| 234              | DHOLPUR-SIRMUTTRA WITH EXTENSION TO<br>GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-<br>BANSI PAHARPUR - [N22000158] | 04/2010                          | 622.41<br>-                          | 2,030.50                       | 02/2019<br>-                          | 12/2022         | 226.23                  |
| 235              | BOWAICHANDI-ARAMBAGH<br>- [N22000159]                                                                              | 04/2010                          | 267.37<br>-                          | 434.00                         | -<br>-                                | -               | 62.32                   |
| 236              | DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA<br>- [N22000160]                                                        | 04/2010                          | 553.63<br>-                          | 1,009.00                       | -<br>-                                | -               | 82.25                   |
| 237              | BHADUTOLA-JHARGRAM VIA LALGARH (NL)<br>- [N22000161]                                                               | 04/2011                          | 289.64<br>-                          | 760.00                         | -<br>-                                | -               | 162.39                  |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (September 2017) |                                                                                                  |                                  |                                      |                                |                                       |             |                   |
|------------------|--------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                  |                                                                                                  |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No             | Project                                                                                          | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1                | 2                                                                                                | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 238              | CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION<br>- [N22000162]                                       | 04/2010                          | 149.90<br>-                          | 230.00                         | 03/2015<br>-                          | -           | 53.44             |
| 239              | TAMLUK-BASULYA-SUTAHATA DOUBLING<br>- [N22000163]                                                | 04/2010                          | 171.02<br>-                          | 250.00                         | 06/2013<br>-                          | 12/2016     | 46.18             |
| 240              | DANGOAPOLI-RAJGHARSWAN 3RD LINE DOUBLING<br>- [N22000164]                                        | 04/2010                          | 309.44<br>-                          | 583.00                         | 12/2015<br>-                          | -           | 88.40             |
| 241              | MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING<br>- [N22000165]                                         | 04/2012                          | 258.20<br>-                          | 365.00                         | -                                     | 12/2017     | 41.36             |
| 242              | GAYA-CHATRA (NL)<br>- [N22000169]                                                                | 04/2008                          | 415.67<br>-                          | 549.75                         | -                                     | -           | 32.26             |
| 243              | SAKRI-HASANPUR ROAD (NL)<br>- [N22000171]                                                        | 04/1999                          | 175.69<br>-                          | 325.00                         | -                                     | -           | 84.98             |
| 244              | CHHAPRA-MUZAFFARPUR (NL)<br>- [N22000172]                                                        | 04/2006                          | 285.07<br>-                          | 378.56                         | -                                     | -           | 32.80             |
| 245              | MOTIHARI-SITAMARHI (NL)<br>- [N22000174]                                                         | 04/2006                          | 211.00<br>-                          | 926.09                         | -                                     | -           | 338.91            |
| 246              | SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)<br>- [N22000175]                                     | 04/2008                          | 678.62<br>-                          | 2,393.23                       | -                                     | -           | 252.66            |
| 247              | HAJIPUR-RAMDAYALUNAGAR DOUBLING<br>- [N22000182]                                                 | 04/2013                          | 213.01<br>-                          | 367.17                         | -                                     | -           | 72.37             |
| 248              | ATTIPPATTU PUTTUR<br>- [N22000184]                                                               | 04/2008                          | 446.87<br>-                          | 527.37                         | -                                     | -           | 18.01             |
| 249              | SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO<br>IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR<br>- [N22000186] | 04/2013                          | 839.00<br>-                          | 1,500.00                       | -                                     | -           | 78.78             |
| 250              | CHENNAI BEACH-TAMBARAM-CHENGALPATTU<br>SUBURBAN GC<br>- [N22000188]                              | 04/1998                          | 271.24<br>-                          | 520.00                         | -                                     | -           | 91.71             |
| 251              | VILLUPURAM-DINDIGUL WITH ELECTRIFICATION<br>- [N22000189]                                        | 04/2008                          | 822.39<br>-                          | 1,810.00                       | -                                     | 03/2018     | 120.09            |
| 252              | KURUPPANTHARA-CHINGAVANAM<br>- [N22000190]                                                       | 04/2007                          | 270.14<br>-                          | 346.15                         | -                                     | -           | 28.14             |
| 253              | NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR<br>- [N22000193]                                        | 04/2010                          | 221.42<br>-                          | 380.00                         | -                                     | -           | 71.62             |
| 254              | CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA<br>- [N22000194]                                      | 04/1999                          | 895.00<br>-                          | 1,857.00                       | 03/2007<br>-                          | 04/2016     | 107.49            |
| 255              | AGARTALA-AKHAURA NL<br>- [N22000195]                                                             | 04/2012                          | 252.00<br>-                          | 580.00                         | -                                     | 07/2019     | 130.16            |
| 256              | NEW COOCHBEHAR TO SAMUKTALA<br>- [N22000197]                                                     | 04/2011                          | 209.77<br>-                          | 445.00                         | -                                     | 03/2018     | 112.14            |
| 257              | NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING<br>PROJECT<br>- [N22000198]                              | 04/2012                          | 283.55<br>-                          | 330.00                         | -                                     | 03/2019     | 16.38             |
| 258              | ERODE-PALANI<br>- [N22000199]                                                                    | 04/2008                          | 288.57<br>-                          | 603.22                         | -                                     | -           | 109.04            |
| 259              | MADURAI-BODINAYAKKANUR<br>- [N22000201]                                                          | 04/2008                          | 164.41<br>-                          | 302.90                         | -                                     | -           | 84.23             |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (September 2017) |                                                                                                                       |                                  |                                      |                                |                                       |             |                   |
|------------------|-----------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                  |                                                                                                                       |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No             | Project                                                                                                               | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1                | 2                                                                                                                     | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 260              | CHENGANNUR-CHINGAVANAM<br>- [N22000203]                                                                               | 04/2006                          | 191.72<br>-                          | 342.85                         | -<br>-                                | -           | 78.83             |
| 261              | NEW BG LINE FROM BYRNIHAT TO SHILLONG<br>- [N22000205]                                                                | 04/2010                          | 4,083.02<br>-                        | 6,000.00                       | -<br>-                                | 03/2021     | 46.95             |
| 262              | NEW BG LINE FROM BALURGHAT TO HILLY NFR<br>- [N22000206]                                                              | 04/2010                          | 242.22<br>-                          | 471.00                         | -<br>-                                | -           | 94.45             |
| 263              | NEW BG LINE FROM JAGBANI TO BIRATNAGAR<br>- [N22000207]                                                               | 04/2010                          | 241.52<br>-                          | 394.28                         | -<br>-                                | -           | 63.25             |
| 264              | MURKONGSELEK-PASIGHAT NL<br>- [N22000208]                                                                             | 04/2011                          | 165.82<br>-                          | 450.00                         | -<br>-                                | 03/2020     | 171.38            |
| 265              | NEW JALPAIGURI SILIGURI NEW BONGAIGAON<br>INCLUDING BR LINE AND MM CHALSA NAXAL<br>RAJABHATKHOWA JAINTI - [N22000209] | 04/1999                          | 523.17<br>-                          | 1,871.00                       | -<br>-                                | 03/2018     | 257.63            |
| 266              | AMBARI FALAKATA TO NEW MAYNAGURI<br>- [N22000210]                                                                     | 04/2011                          | 312.12<br>-                          | 508.00                         | -<br>-                                | 03/2019     | 62.76             |
| 267              | LUMDING-HOJAI PATCH DOUBLING PROJECT<br>- [N22000211]                                                                 | 04/2012                          | 246.07<br>-                          | 398.93                         | -<br>-                                | 03/2019     | 62.12             |
| 268              | MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II<br>HYDERABAD - [N22000213]                                                | 04/2012                          | 632.68<br>-                          | 816.55                         | 03/2016<br>-                          | 12/2018     | 29.06             |
| 269              | MADURAI-TUTICORIN VIA ARUPPUKOTTAI<br>- [N22000215]                                                                   | 04/2011                          | 601.43<br>-                          | 1,500.00                       | -<br>-                                | -           | 149.41            |
| 270              | HANSNABAD-HINGALGANJ NEW BG LINE<br>- [N22000218]                                                                     | 04/2010                          | 172.03<br>-                          | 260.60                         | -<br>-                                | -           | 51.49             |
| 271              | PIRPAINTI-JASIDIH<br>- [N22000219]                                                                                    | 04/2013                          | 915.98<br>-                          | 1,130.13                       | -<br>-                                | -           | 23.38             |
| 272              | PIRPAINTI-BHAGALPUR<br>- [N22000222]                                                                                  | 04/2011                          | 261.38<br>-                          | 332.14                         | -<br>-                                | -           | 27.07             |
| 273              | WARDHA-BALHARSHAH - 3RD LINE (132 KM)<br>- [N22000356]                                                                | 02/2015                          | 630.00<br>-                          | 1,272.19                       | -<br>-                                | 03/2022     | 101.93            |
| 274              | ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)<br>- [N22000358]                                                             | 02/2015                          | 2,326.00<br>-                        | 2,449.91                       | -<br>-                                | 03/2023     | 5.33              |
| 275              | DAUND - MANMAD (236 KM)<br>- [N22000360]                                                                              | 02/2016                          | 1,876.00<br>-                        | 2,081.27                       | -<br>-                                | -           | 10.94             |
| 276              | MANMAD - JALGAON - 3RD LINE (160 KM)<br>- [N22000361]                                                                 | 02/2016                          | 854.00<br>-                          | 1,035.16                       | -<br>-                                | -           | 21.21             |
| 277              | VIJAYAWADA-GUDUR<br>- [N22000369]                                                                                     | 04/2015                          | 3,246.26<br>-                        | 3,548.67                       | -<br>-                                | -           | 9.32              |
| 278              | MATHURA-PLWAL 4TH LINE (80KM)<br>- [N22000372]                                                                        | 04/2015                          | 524.00<br>668.00                     | 668.00                         | 03/2020<br>-                          | 03/2020     | 27.48             |
| 279              | MUZAFFARPUR-SITAMARHI NEW LINE<br>- [N22000374]                                                                       | 01/1991                          | 332.15<br>-                          | 559.91                         | 07/2014<br>-                          | -           | 68.57             |
| 280              | RANGIA-MURKONGSELEK ALONG WITH LINKED<br>FINGERS - [N22000386]                                                        | 04/2003                          | 4,300.00<br>-                        | 4,520.00                       | -<br>-                                | 08/2015     | 5.12              |
| 281              | NEW MAYNAGURI-GUMANIHAT-DOUBLING OF<br>REMAINING PORTION (51.65 KM)<br>- [N22000390]                                  | 04/2016                          | 556.31<br>-                          | 612.00                         | -<br>-                                | -           | 10.01             |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (September 2017) |                                                                                                                         |                                  |                                      |                                |                                       |             |                   |
|------------------|-------------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                  |                                                                                                                         |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No             | Project                                                                                                                 | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1                | 2                                                                                                                       | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 282              | TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN<br>NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM<br>NADAKUMAR BOLAI - [N22000397       | 01/1991                          | 763.18<br>-                          | 1,428.00                       | 12/2021<br>-                          | 12/2021     | 87.11             |
| 283              | RUPSA BANGRIPOSI 90 KM WITH MM FOR<br>UPGRADATION FROM RUPSA BURAMARA AND<br>EXTENSION OF LINE FRO - [N22000398         | 04/1995                          | 524.43<br>-                          | 939.00                         | 12/2021<br>-                          | 12/2021     | 79.05             |
| 284              | TRIVANDRUM-KANYAKUMARI DOUBLING<br>- [N22000399                                                                         | 02/2015                          | 900.00<br>-                          | 4,131.90                       | -<br>-                                | -           | 359.10            |
| 285              | VARANASI-MODHOSINGH-ALLAHABAD DOUBLING<br>- [N22000401                                                                  | 04/2015                          | 750.55<br>-                          | 750.56                         | 12/2024<br>-                          | 12/2024     | .00               |
| 286              | BANKURA DAMODAR VALLEY RLY LINE 96 KM GC<br>WITH 6MMS FOR NL - [N22000402                                               | 04/1998                          | 1,027.40<br>-                        | 2,373.00                       | 03/2003<br>-                          | -           | 130.97            |
| 287              | LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC<br>- [N22000404                                                             | 04/2011                          | 927.01<br>-                          | 977.00                         | 03/2019<br>-                          | 03/2019     | 5.39              |
| 288              | BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION<br>- [N22000413                                                          | 03/2012                          | 1,183.25<br>-                        | 1,183.30                       | 12/2020<br>-                          | 12/2020     | .00               |
| 289              | BINA - KOTA DOUBLING WITH RE<br>- [N22000414                                                                            | 04/2011                          | 1,485.65<br>-                        | 1,485.85                       | 12/2020<br>-                          | 12/2020     | .01               |
| 290              | RAJNANDGAON - NAGPUR - 3RD LINE (SECR)<br>- [N22000420                                                                  | 09/2016                          | 1,273.00<br>1,908.00                 | 1,908.00                       | 12/2021<br>-                          | 12/2021     | 49.88             |
|                  | Total                                                                                                                   |                                  | 1,21,595.36<br>-                     | 2,83,482.35                    |                                       |             |                   |
|                  |                                                                                                                         |                                  |                                      |                                |                                       |             |                   |
|                  | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                      |                                  |                                      |                                |                                       |             |                   |
| 291              | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO<br>KM.140.700 - [240106277                                                  | 12/2003                          | 280.00<br>-                          | 361.00                         | 02/2009<br>-                          | 12/2017     | 28.93             |
| 292              | MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000<br>- [240106278                                                     | 12/2003                          | 199.81<br>-                          | 385.13                         | 04/2009<br>-                          | -           | 92.75             |
| 293              | MAIBANG TO LUMDING (AS-24), KM.111.000 TO<br>KM.126.450 - [240106280                                                    | 12/2003                          | 155.04<br>-                          | 280.13                         | 11/2008<br>-                          | -           | 80.68             |
| 294              | HARANGAJO TO MAIBANG, NH-54<br>- [N24000062                                                                             | 12/2003                          | 196.00<br>-                          | 331.23                         | 07/2009<br>-                          | -           | 68.99             |
| 295              | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)<br>- [N24000133                                                             | 05/2009                          | 1,108.00<br>-                        | 2,288.00                       | 11/2011<br>-                          | 03/2018     | 106.50            |
| 296              | 4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN<br>TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-<br>52) FROM - [N24000292 | 11/2014                          | 573.96<br>605.00                     | 605.00                         | -<br>-                                | -           | 5.41              |
| 297              | TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B)<br>(42.50 KM) IN ARUNACHAL PRADESH UNDER<br>ARUNACHAL PRA - [N24000307 | 12/2011                          | 156.63<br>276.00                     | 276.00                         | 02/2012<br>-                          | -           | 76.21             |
| 298              | CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO<br>203/0 INCLUDING RECONSTRUCTION AND WIDENING OF<br>CULVERT - [N24000316 | 03/2015                          | 258.97<br>-                          | 268.92                         | 08/2015<br>-                          | -           | 3.84              |
| 299              | REHABILITATION AND UPGRADATION OF NH 226 E<br>FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS<br>ON EPC MO - [N24000317 | 03/2015                          | 157.18<br>162.00                     | 162.00                         | 07/2015<br>-                          | -           | 3.07              |
| 300              | BRAHMPUTRA BRIDGE,NH NO-31<br>- [N24000063                                                                              | 12/2003                          | 217.61<br>-                          | 309.56                         | 04/2010<br>-                          | 03/2018     | 42.25             |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (September 2017) |                                                                                                                    |                                  |                                      |                                |                                       |             |                   |
|------------------|--------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                  |                                                                                                                    |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No             | Project                                                                                                            | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1                | 2                                                                                                                  | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 301              | CHAMBAL BRIDGE, NH-76 (RJ-5)<br>- [N24000068]                                                                      | 12/2003                          | 275.00<br>-                          | 281.31                         | 02/2010<br>-                          | -           | 2.29              |
| 302              | GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION<br>- [N24000125]                                               | 03/2010                          | 1,509.10<br>-                        | 3,237.87                       | 09/2012<br>-                          | 12/2017     | 114.56            |
| 303              | INDORE-JHABUA-GUJRAT/MP<br>- [N24000136]                                                                           | 10/2010                          | 1,175.00<br>-                        | 1,206.10                       | 04/2013<br>-                          | 09/2017     | 2.65              |
| 304              | REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]  | 10/2014                          | 295.47<br>-                          | 313.27                         | 02/2017<br>-                          | 02/2017     | 6.02              |
| 305              | CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249] | 03/2011                          | 218.31<br>-                          | 339.82                         | 12/2015<br>-                          | -           | 55.66             |
| 306              | CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260] | 01/2014                          | 255.75<br>348.00                     | 348.43                         | 09/2017<br>-                          | 09/2017     | 36.24             |
| 307              | CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261] | 01/2014                          | 267.16<br>352.00                     | 352.05                         | 11/2017<br>-                          | 11/2017     | 31.78             |
| 308              | REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265] | 11/2014                          | 297.78<br>330.00                     | 330.00                         | 02/2017<br>-                          | 02/2017     | 10.82             |
| 309              | TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420] | 12/2009                          | 104.00<br>-                          | 201.00                         | 09/2010<br>-                          | 09/2010     | 93.27             |
| 310              | FOUR LANING OF GWALIOR-SHIVPURI<br>- [N24000494]                                                                   | 05/2013                          | 1,055.00<br>-                        | 1,601.77                       | 11/2015<br>-                          | 09/2017     | 51.83             |
| 311              | WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639] | 03/2014                          | 191.50<br>192.00                     | 192.00                         | 05/2016<br>-                          | 06/2017     | .26               |
| 312              | WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]  | 01/2015                          | 326.63<br>327.00                     | 327.00                         | 04/2018<br>-                          | 04/2018     | .11               |
| 313              | WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]    | 02/2015                          | 239.91<br>240.00                     | 240.00                         | 10/2017<br>-                          | 10/2017     | .04               |
| 314              | IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]  | 12/2013                          | 319.80<br>320.00                     | 320.00                         | 05/2016<br>-                          | 03/2017     | .06               |
| 315              | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645] | 08/2013                          | 171.96<br>172.00                     | 172.00                         | 06/2016<br>-                          | 03/2017     | .02               |
| 316              | WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647] | 03/2014                          | 162.51<br>163.00                     | 163.00                         | 05/2016<br>-                          | 03/2017     | .30               |
| 317              | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654] | 03/2017                          | 1,184.71<br>-                        | 1,310.00                       | 03/2020<br>-                          | 03/2020     | 10.58             |
| 318              | 4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)<br>- [N24000656]                                          | 03/2017                          | 744.64<br>-                          | 982.00                         | 03/2020<br>-                          | 03/2020     | 31.88             |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (September 2017) |                                                                                                                    |                                  |                                      |                                |                                       |             |                   |
|------------------|--------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                  |                                                                                                                    |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No             | Project                                                                                                            | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1                | 2                                                                                                                  | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 319              | 4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)<br>- [N24000657]                                      | 03/2017                          | 1,030.44<br>-                        | 1,065.51                       | 03/2020<br>-                          | 03/2020     | 3.40              |
| 320              | 4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)<br>- [N24000658]                                       | 03/2017                          | 988.34<br>-                          | 1,043.28                       | 03/2020<br>-                          | 03/2020     | 5.56              |
| 321              | 4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)<br>- [N24000659]                                     | 03/2017                          | 1,059.73<br>-                        | 1,071.00                       | 03/2017<br>-                          | -           | 1.06              |
| 322              | 4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)<br>- [N24000661]                                     | 03/2017                          | 1,098.06<br>-                        | 1,160.64                       | 03/2020<br>-                          | 03/2020     | 5.70              |
| 323              | CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662] | 03/2017                          | 754.54<br>-                          | 756.27                         | 03/2020<br>-                          | 03/2020     | .23               |
| 324              | TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]  | 03/2017                          | 672.89<br>-                          | 736.01                         | 03/2020<br>-                          | 03/2020     | 9.38              |
| 325              | SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000<br>- [N24000668]              | 03/2017                          | 1,041.62<br>-                        | 1,187.10                       | 03/2020<br>-                          | 03/2020     | 13.97             |
| 326              | 4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00)<br>- [N24000669]                                  | 03/2017                          | 165.50<br>-                          | 172.16                         | 03/2020<br>-                          | 03/2020     | 4.02              |
| 327              | REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]  | 03/2017                          | 1,288.07<br>-                        | 1,420.00                       | 03/2020<br>-                          | 03/2020     | 10.24             |
| 328              | 6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672] | 03/2017                          | 2,064.99<br>-                        | 2,447.00                       | 03/2020<br>-                          | 03/2020     | 18.50             |
| 329              | SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673] | 03/2017                          | 985.41<br>-                          | 1,200.00                       | 03/2020<br>-                          | 03/2020     | 21.78             |
| 330              | SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]   | 03/2017                          | 831.58<br>-                          | 1,177.00                       | 03/2020<br>-                          | 03/2020     | 41.54             |
| 331              | SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675] | 03/2017                          | 993.16<br>-                          | 1,434.00                       | 03/2020<br>-                          | 03/2020     | 44.39             |
| 332              | CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120<br>- [N24000676]                             | 12/2016                          | 138.93<br>155.00                     | 155.00                         | 01/2017<br>-                          | 01/2020     | 11.57             |
| 333              | RHENOK-RORATHANG-PAKYONG ON NH 717A<br>- [N24000695]                                                               | 04/2017                          | 388.00<br>-                          | 447.37                         | 10/2017<br>-                          | 10/2017     | 15.30             |
|                  | Total                                                                                                              |                                  | 25,598.69<br>-                       | 32,656.93                      |                                       |             |                   |
|                  |                                                                                                                    |                                  |                                      |                                |                                       |             |                   |
|                  | <u>SHIPPING AND PORTS</u>                                                                                          |                                  |                                      |                                |                                       |             |                   |
| 334              | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)<br>- [N25000035]                                       | 10/2002                          | 150.00<br>-                          | 600.00                         | 03/2006<br>-                          | 12/2017     | 300.00            |
| 335              | CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED<br>- [N25000065]                                            | 10/2013                          | 198.94<br>-                          | 235.15                         | 06/2017<br>-                          | -           | 18.20             |



## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (September 2017) |                                                                                                                    |                                  |                                      |                                |                                       |             |                   |
|------------------|--------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|
|                  |                                                                                                                    |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                   |
| S.No             | Project                                                                                                            | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/ Revised                     | Anticipated | Cost Overruns (%) |
| 1                | 2                                                                                                                  | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                 |
| 336              | CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED<br>- [N25000066]                                            | 02/2015                          | 244.50<br>258.00                     | 258.33                         | 12/2017<br>-                          | 12/2017     | 5.66              |
| 337              | RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST<br>- [N25000059]                                     | 03/2007                          | 245.67<br>-                          | 409.83                         | 04/2009<br>-                          | -           | 66.82             |
| 338              | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063] | 01/2007                          | 366.39<br>-                          | 669.46                         | 12/2010<br>-                          | 12/2018     | 82.72             |
|                  | Total                                                                                                              |                                  | 1,205.50<br>-                        | 2,172.77                       |                                       |             |                   |
|                  |                                                                                                                    |                                  |                                      |                                |                                       |             |                   |
|                  | <u>STEEL</u>                                                                                                       |                                  |                                      |                                |                                       |             |                   |
| 339              | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI<br>- [N12000099]                                   | 12/2007                          | 202.61<br>227.00                     | 227.00                         | 12/2016<br>-                          | 12/2017     | 12.04             |
| 340              | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII<br>- [N12000100]                                 | 10/2011                          | 175.49<br>206.71                     | 206.71                         | 12/2016<br>-                          | -           | 17.79             |
| 341              | CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA<br>- [N12000101]                                          | 05/2005                          | 768.88<br>1,070.97                   | 1,113.34                       | 02/2014<br>-                          | -           | 44.80             |
| 342              | REVAMPING OF SINTER MACHINES - 1 AND 2<br>- [N12000091]                                                            | 12/2009                          | 343.00<br>-                          | 488.40                         | 10/2016<br>-                          | 03/2018     | 42.39             |
| 343              | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V<br>- [N12000098]                                    | 03/2007                          | 149.73<br>173.00                     | 175.94                         | 12/2015<br>-                          | -           | 17.50             |
|                  | Total                                                                                                              |                                  | 1,639.71<br>-                        | 2,211.39                       |                                       |             |                   |
|                  |                                                                                                                    |                                  |                                      |                                |                                       |             |                   |
|                  | <u>TELECOMMUNICATIONS</u>                                                                                          |                                  |                                      |                                |                                       |             |                   |
| 344              | NETWORK FOR SPECTRUM<br>- [N26000101]                                                                              | 03/2012                          | 13,334.00<br>-                       | 24,664.00                      | 07/2015<br>-                          | 06/2019     | 84.97             |
|                  | Total                                                                                                              |                                  | 13,334.00<br>-                       | 24,664.00                      |                                       |             |                   |
|                  |                                                                                                                    |                                  |                                      |                                |                                       |             |                   |
|                  | <u>URBAN DEVELOPMENT</u>                                                                                           |                                  |                                      |                                |                                       |             |                   |
| 345              | BANGALORE METRO RAIL PROJECT<br>- [N28000008]                                                                      | 05/2006                          | 6,395.00<br>-                        | 13,845.01                      | 06/2011<br>-                          | 04/2017     | 116.50            |
| 346              | OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA<br>- [N28000068]                      | 02/2011                          | 241.33<br>-                          | 349.33                         | 03/2016<br>-                          | 03/2018     | 44.75             |
| 347              | ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI<br>- [N28000071]   | 10/2013                          | 1,219.21<br>-                        | 1,592.00                       | 10/2019<br>-                          | 03/2020     | 30.58             |
| 348              | CHENNAI METRO RAIL LTD (PHASE 1)<br>- [N28000084]                                                                  | 02/2009                          | 14,600.00<br>-                       | 19,058.00                      | 12/2015<br>-                          | 12/2017     | 30.53             |

## Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

| (September 2017) |                                                                                                                  |                                  |                                      |                                |                                       |             |                      |
|------------------|------------------------------------------------------------------------------------------------------------------|----------------------------------|--------------------------------------|--------------------------------|---------------------------------------|-------------|----------------------|
|                  |                                                                                                                  |                                  |                                      |                                | Date of Commissioning<br>(Month/Year) |             |                      |
| S.No             | Project                                                                                                          | Date of Approval<br>(Month/Year) | Original / Revised<br>Cost(Rs crore) | Anticipated Cost<br>(Rs.crore) | Original/<br>Revised                  | Anticipated | Cost Overruns<br>(%) |
| 1                | 2                                                                                                                | 3                                | 4                                    | 5                              | 6                                     | 7           | 8                    |
| 349              | DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091         | 08/2014                          | 350.02<br>-                          | 479.87                         | 03/2015<br>-                          | -           | 37.10                |
| 350              | CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101 | 12/2008                          | 114.26<br>266.00                     | 266.00                         | 12/2013<br>-                          | 10/2019     | 132.80               |
|                  | Total                                                                                                            |                                  | 22,919.82<br>-                       | 35,590.21                      |                                       |             |                      |
|                  |                                                                                                                  |                                  |                                      |                                |                                       |             |                      |
|                  | Grand Total                                                                                                      |                                  | 3,42,261.70                          | 6,07,007.52                    |                                       |             |                      |

## Details of Delayed Projects w.r.t. Original Schedule

### Annexure - VI

| Costing Rs.150 Crore and above (September 2017) |                                                                                                                        |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
|-------------------------------------------------|------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                                 |                                                                                                                        |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  |                                                                  |
| S.No                                            | Project                                                                                                                | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) | Reasons for Delay (As Reported by Project Implementing Agencies) |
| 1                                               | 2                                                                                                                      | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
|                                                 | <u>ATOMIC ENERGY</u>                                                                                                   |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 1                                               | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU                                      | 09/2003                       | 3,492.00<br>5,677.00               | 6,000.00                     | 5,486.27                           | 09/2010<br>09/2016                 | 02/2018     | 89                    | 71.82            |                                                                  |
| 2                                               | KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT                                                    | 10/2009                       | 11,459.00<br>-                     | 11,459.00                    | 10,710.00                          | 12/2015<br>11/2016                 | 11/2019     | 47                    | 0                |                                                                  |
| 3                                               | RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN                                      | 10/2009                       | 12,320.00<br>-                     | 12,320.00                    | 8,312.00                           | 12/2016<br>03/2017                 | 12/2020     | 48                    | 0                |                                                                  |
|                                                 | Total                                                                                                                  |                               | 27,271.00<br>-                     | 29,779.00                    | 24,508.27                          |                                    |             |                       |                  |                                                                  |
|                                                 | <u>CIVIL AVIATION</u>                                                                                                  |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 4                                               | CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM                                        | 01/2009                       | 309.46<br>-                        | 553.53                       | 484.76                             | 01/2011<br>09/2017                 | 09/2017     | 80                    | 78.87            | long rainy season                                                |
| 5                                               | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS | 10/2013                       | 314.61<br>-                        | 441.33                       | 24.13                              | 09/2018<br>-                       | 06/2020     | 21                    | 40.28            |                                                                  |
|                                                 | Total                                                                                                                  |                               | 624.07<br>-                        | 994.86                       | 508.89                             |                                    |             |                       |                  |                                                                  |
|                                                 | <u>COAL</u>                                                                                                            |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                  |
| 6                                               | NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC, TAMIL NADU                                                        | 05/2016                       | 687.28<br>-                        | 687.28                       | 690.47                             | 06/2017<br>-                       | 10/2017     | 4                     | 0                |                                                                  |
| 7                                               | RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND                                                                           | 09/2009                       | 153.82<br>-                        | 153.82                       | 126.63                             | 03/2014<br>-                       | 12/2017     | 45                    | 0                |                                                                  |
| 8                                               | KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA                                                           | 01/2005                       | 302.96<br>-                        | 302.96                       | 329.10                             | 03/2010<br>-                       | 03/2018     | 96                    | 0                |                                                                  |
| 9                                               | NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, MADHYA PRADESH                                | 10/2007                       | 259.40<br>486.57                   | 486.57                       | 296.95                             | 03/2012<br>03/2018                 | 03/2018     | 72                    | 87.58            | forest clearance                                                 |
| 10                                              | RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA                                                                           | 03/2010                       | 209.78<br>-                        | 209.78                       | 120.55                             | 03/2015<br>-                       | 03/2018     | 36                    | 0                |                                                                  |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                         |                               |                                    |                              |                                    | (September 2017)                   |             |                       |                  |                                                                                                                                                              |
|--------------------------------|-------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------|
|                                |                                                                         |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies)                                                                                             |
| S.No                           | Project                                                                 | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                                                                                                              |
| 1                              | 2                                                                       | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                                                                                                                           |
| 11                             | MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA           | 03/2010                       | 181.19 -                           | 181.19                       | 176.79                             | 03/2012 -                          | 03/2018     | 72                    | 0                |                                                                                                                                                              |
| 12                             | MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH           | 12/2009                       | 321.50 -                           | 321.50                       | 198.19                             | 03/2014 -                          | 03/2018     | 48                    | 0                |                                                                                                                                                              |
| 13                             | AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH    | 11/2009                       | 198.59 -                           | 198.59                       | 169.38                             | 03/2016 -                          | 03/2018     | 24                    | 0                |                                                                                                                                                              |
| 14                             | PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND                       | 07/2008                       | 210.98 -                           | 210.98                       | 206.31                             | 03/2013 -                          | 03/2018     | 60                    | 0                |                                                                                                                                                              |
| 15                             | RAJRAPPA RCE OCP ( 3.0 MTY) - [N06000087]CCL,JHARKHAND                  | 12/2009                       | 510.85 -                           | 510.85                       | 341.12                             | 03/2016 -                          | 03/2018     | 24                    | 0                |                                                                                                                                                              |
| 16                             | BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,CHHATISGARH            | 04/2012                       | 258.56 -                           | 258.56                       | 151.94                             | 03/2016 -                          | 03/2018     | 24                    | 0                |                                                                                                                                                              |
| 17                             | RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL,TELANGANA   | 06/2012                       | 365.01 -                           | 365.01                       | 57.64                              | 06/2015 -                          | 03/2018     | 33                    | 0                |                                                                                                                                                              |
| 18                             | RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA                  | 11/2012                       | 430.45<br>415.37                   | 415.37                       | 136.75                             | 03/2016 -                          | 03/2018     | 24                    | -3.5             |                                                                                                                                                              |
| 19                             | NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU | 06/2011                       | 5,907.11 -                         | 5,907.11                     | 4,763.73                           | 12/2015<br>04/2018                 | 04/2018     | 28                    | 0                |                                                                                                                                                              |
| 20                             | MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND                       | 08/2010                       | 289.45 -                           | 289.45                       | 151.66                             | 05/2014 -                          | 04/2018     | 47                    | 0                |                                                                                                                                                              |
| 21                             | PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND                       | 10/2012                       | 269.82 -                           | 269.82                       | 150.11                             | 04/2014 -                          | 04/2018     | 48                    | 0                |                                                                                                                                                              |
| 22                             | BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA                | 12/2007                       | 490.10 -                           | 490.10                       | 278.34                             | 03/2017 -                          | 05/2018     | 14                    | 0                |                                                                                                                                                              |
| 23                             | SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL       | 08/2012                       | 1,055.05 -                         | 1,055.05                     | 316.35                             | 03/2018 -                          | 09/2018     | 6                     | 0                | Rehabilitation of PAFs: Process of R&R activity delayed due to disputes among villagers for selection of rehab site and resistance by villagers in shifting. |
| 24                             | MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND                 | 02/2011                       | 339.88 -                           | 339.88                       | 12.08                              | 04/2014 -                          | 10/2018     | 54                    | 0                |                                                                                                                                                              |
| 25                             | KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA                     | 12/2007                       | 457.77 -                           | 457.77                       | 404.51                             | 03/2013 -                          | 11/2018     | 68                    | 0                |                                                                                                                                                              |
| 26                             | SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA              | 10/2006                       | 249.03<br>448.86                   | 448.86                       | 157.97                             | 03/2012 -                          | 03/2019     | 84                    | 80.24            |                                                                                                                                                              |
| 27                             | BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA               | 12/2007                       | 172.08 -                           | 172.08                       | 191.07                             | 03/2010 -                          | 03/2019     | 108                   | 0                |                                                                                                                                                              |

### Details of Delayed Projects w.r.t. Original Schedule

[illegible]

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                           |                                  |                                       |                                 |                                       | (September 2017)                      |             |                          |                     |                                                                     |
|--------------------------------|-----------------------------------------------------------------------------------------------------------|----------------------------------|---------------------------------------|---------------------------------|---------------------------------------|---------------------------------------|-------------|--------------------------|---------------------|---------------------------------------------------------------------|
|                                |                                                                                                           |                                  |                                       |                                 |                                       | Date of Commissioning<br>(Month/Year) |             |                          |                     | Reasons for Delay<br>(As Reported by Project Implementing Agencies) |
| S.No                           | Project                                                                                                   | Date of Approval<br>(Month/Year) | Original/ Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs. crore) | Cumulative Expenditure<br>(Rs. crore) | Original / Revised                    | Anticipated | Time Overrun<br>(Months) | Cost Overrun<br>(%) |                                                                     |
| 1                              | 2                                                                                                         | 3                                | 4                                     | 5                               | 6                                     | 7                                     | 8           | 9                        | 10                  | 11                                                                  |
|                                | <u>FERTILISERS</u>                                                                                        |                                  |                                       |                                 |                                       |                                       |             |                          |                     |                                                                     |
| 45                             | NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA                              | 10/2014                          | 197.79<br>209.44                      | 209.44                          | 82.72                                 | 11/2016<br>04/2019                    | 04/2019     | 29                       | 5.89                |                                                                     |
|                                | Total                                                                                                     |                                  | 197.79<br>-                           | 209.44                          | 82.72                                 |                                       |             |                          |                     |                                                                     |
|                                | <u>STEEL</u>                                                                                              |                                  |                                       |                                 |                                       |                                       |             |                          |                     |                                                                     |
| 46                             | EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH                                             | 08/2010                          | 17,265.00<br>-                        | 17,265.00                       | 17,970.98                             | 03/2013<br>-                          | 10/2017     | 55                       | 0                   |                                                                     |
| 47                             | REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND                                                    | 10/2013                          | 245.67<br>-                           | 245.67                          | 195.66                                | 05/2016<br>-                          | 10/2017     | 17                       | 0                   |                                                                     |
| 48                             | 3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH                                             | 07/2011                          | 974.76<br>-                           | 974.76                          | 533.93                                | 07/2016<br>-                          | 10/2017     | 15                       | 0                   |                                                                     |
| 49                             | BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH                               | 07/2011                          | 877.73<br>-                           | 877.73                          | 746.08                                | 07/2015<br>-                          | 10/2017     | 27                       | 0                   |                                                                     |
| 50                             | TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH                                                         | 12/2009                          | 280.00<br>-                           | 280.00                          | 155.29                                | 09/2016<br>-                          | 10/2017     | 13                       | 0                   |                                                                     |
| 51                             | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA                 | 12/2007                          | 202.61<br>227.00                      | 227.00                          | 199.95                                | 12/2016<br>-                          | 12/2017     | 12                       | 12.04               |                                                                     |
| 52                             | REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH                                   | 12/2009                          | 343.00<br>-                           | 488.40                          | 225.07                                | 10/2016<br>-                          | 03/2018     | 17                       | 42.39               |                                                                     |
| 53                             | CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY- JHARKHAND - [N12000109]HSCL,JHARKHAND | 12/2007                          | 253.92<br>253.92                      | 253.92                          | 193.97                                | 06/2016<br>-                          | 03/2018     | 21                       | 0                   |                                                                     |
| 54                             | MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND                | 05/2015                          | 1,154.18<br>-                         | 1,154.18                        | 477.09                                | 12/2017<br>-                          | 05/2018     | 5                        | 0                   |                                                                     |
| 55                             | COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH                                                      | 12/2011                          | 2,858.00<br>-                         | 2,500.00                        | 591.35                                | 12/2017<br>-                          | 06/2018     | 6                        | -12.53              |                                                                     |
| 56                             | NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND                                        | 03/2015                          | 1,034.01<br>-                         | 1,034.01                        | 187.29                                | 10/2017<br>-                          | 07/2018     | 9                        | 0                   |                                                                     |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                                     |                                  |                                       |                                 |                                       | (September 2017)                      |             |                          |                     |                                                                     |
|--------------------------------|-------------------------------------------------------------------------------------------------------------------------------------|----------------------------------|---------------------------------------|---------------------------------|---------------------------------------|---------------------------------------|-------------|--------------------------|---------------------|---------------------------------------------------------------------|
|                                |                                                                                                                                     |                                  |                                       |                                 |                                       | Date of Commissioning<br>(Month/Year) |             |                          |                     | Reasons for Delay<br>(As Reported by Project Implementing Agencies) |
| S.No                           | Project                                                                                                                             | Date of Approval<br>(Month/Year) | Original/ Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs. crore) | Cumulative Expenditure<br>(Rs. crore) | Original / Revised                    | Anticipated | Time Overrun<br>(Months) | Cost Overrun<br>(%) |                                                                     |
| 1                              | 2                                                                                                                                   | 3                                | 4                                     | 5                               | 6                                     | 7                                     | 8           | 9                        | 10                  | 11                                                                  |
| 57                             | CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL, RAJASTHAN   | 05/2015                          | 189.00 -                              | 189.00                          | -                                     | 03/2017 -                             | 08/2018     | 17                       | 0                   |                                                                     |
| 58                             | NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH                                                                          | 01/2010                          | 15,525.00 -                           | 15,525.00                       | 12,816.08                             | 05/2015<br>10/2018                    | 10/2018     | 41                       | 0                   |                                                                     |
| 59                             | CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL, MEGHALAYA | 04/2014                          | 151.33 -                              | 151.33                          | 7.15                                  | 09/2017 -                             | 12/2018     | 15                       | 0                   |                                                                     |
| 60                             | CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL, JHARKHAND                                       | 02/2014                          | 787.29 -                              | 787.29                          | 285.30                                | 12/2016 -                             | 12/2018     | 24                       | 0                   |                                                                     |
| 61                             | INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL, ODISHA                                                                 | 04/2015                          | 3,127.30 -                            | 3,127.30                        | 1,205.62                              | 04/2018 -                             | 02/2019     | 10                       | 0                   |                                                                     |
| 62                             | IRRIGATION WORK OF BAGMATI - [N12000108]HSCL, BIHAR                                                                                 | 10/2005                          | 956.00 -                              | 956.00                          | 651.21                                | 03/2015 -                             | 03/2021     | 72                       | 0                   |                                                                     |
|                                | Total                                                                                                                               |                                  | 46,224.80 -                           | 46,036.59                       | 36,442.02                             |                                       |             |                          |                     |                                                                     |
|                                |                                                                                                                                     |                                  |                                       |                                 |                                       |                                       |             |                          |                     |                                                                     |
|                                | <u>PETROLEUM</u>                                                                                                                    |                                  |                                       |                                 |                                       |                                       |             |                          |                     |                                                                     |
| 63                             | RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]IOCL, ASSAM                                  | 06/2012                          | 150.00 -                              | 259.93                          | 251.90                                | 07/2014 -                             | 09/2017     | 38                       | 73.29               |                                                                     |
| 64                             | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL, KARNATAKA                                                          | 01/2006                          | 993.00 -                              | 1,693.00                        | 1,537.84                              | 01/2012 -                             | 10/2017     | 69                       | 70.49               |                                                                     |
| 65                             | RESID UPGRADATION PROJECT - [N16000184]CPCL, TAMIL NADU                                                                             | 03/2013                          | 3,110.36 -                            | 3,110.36                        | 2,765.42                              | 11/2015 -                             | 10/2017     | 23                       | 0                   |                                                                     |
| 66                             | PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL, ODISHA                                                            | 03/2014                          | 238.50 -                              | 238.50                          | 167.48                                | 03/2017<br>10/2017                    | 10/2017     | 7                        | 0                   |                                                                     |
| 67                             | DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]CPCL, TAMIL NADU                                                          | 02/2016                          | 367.11 -                              | 367.11                          | 218.14                                | 04/2017 -                             | 11/2017     | 7                        | 0                   |                                                                     |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                              |                                  |                                       |                                 |                                       | (September 2017)                      |             |                          |                     |                                                                     |
|--------------------------------|------------------------------------------------------------------------------------------------------------------------------|----------------------------------|---------------------------------------|---------------------------------|---------------------------------------|---------------------------------------|-------------|--------------------------|---------------------|---------------------------------------------------------------------|
|                                |                                                                                                                              |                                  |                                       |                                 |                                       | Date of Commissioning<br>(Month/Year) |             |                          |                     | Reasons for Delay<br>(As Reported by Project Implementing Agencies) |
| S.No                           | Project                                                                                                                      | Date of Approval<br>(Month/Year) | Original/ Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs. crore) | Cumulative Expenditure<br>(Rs. crore) | Original / Revised                    | Anticipated | Time Overrun<br>(Months) | Cost Overrun<br>(%) |                                                                     |
| 1                              | 2                                                                                                                            | 3                                | 4                                     | 5                               | 6                                     | 7                                     | 8           | 9                        | 10                  | 11                                                                  |
| 68                             | UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM               | 09/2012                          | 871.35 -                              | 1,200.00                        | 958.00                                | 03/2015 -                             | 11/2017     | 32                       | 37.72               |                                                                     |
| 69                             | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA                       | 03/2011                          | 861.79<br>1,256.72                    | 1,256.72                        | 1,158.79                              | 05/2013<br>12/2017                    | 12/2017     | 55                       | 45.83               |                                                                     |
| 70                             | INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC, MULTI STATE                                             | 05/2013                          | 4,124.35<br>4,259.59                  | 5,637.00                        | 3,701.21                              | 04/2016<br>12/2017                    | 12/2017     | 20                       | 36.68               |                                                                     |
| 71                             | SONAMURA GGS AND PIPELINE PROJECT ( PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC, TRIPURA | 05/2016                          | 215.38 -                              | 215.38                          | 162.34                                | 06/2017<br>01/2018                    | 01/2018     | 7                        | 0                   |                                                                     |
| 72                             | NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL, TAMIL NADU                            | 05/2015                          | 257.87 -                              | 257.87                          | 117.68                                | 11/2016 -                             | 02/2018     | 15                       | 0                   |                                                                     |
| 73                             | FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY - [N16000245]IOCL, GUJARAT                                  | 02/2016                          | 931.00 -                              | 931.00                          | 383.35                                | 07/2017 -                             | 02/2018     | 7                        | 0                   |                                                                     |
| 74                             | INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC, MAHARASHTRA                                                        | 12/2011                          | 2,059.63 -                            | 2,665.65                        | 1,633.37                              | 03/2015<br>03/2018                    | 03/2018     | 36                       | 29.42               |                                                                     |
| 75                             | DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC, MULTI STATE                                            | 04/2012                          | 600.17 -                              | 600.17                          | 589.36                                | 12/2014<br>03/2018                    | 03/2018     | 39                       | 0                   |                                                                     |
| 76                             | URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL, MULTI STATE                                                            | 12/2009                          | 309.81<br>723.40                      | 723.40                          | 381.64                                | 10/2014<br>03/2018                    | 03/2018     | 41                       | 133.5               |                                                                     |
| 77                             | TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL, ASSAM                                                                         | 03/2009                          | 228.64 -                              | 209.19                          | 147.05                                | 12/2016 -                             | 03/2018     | 15                       | -8.51               |                                                                     |
| 78                             | SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC, MADHYA PRADESH                                                           | 03/2009                          | 181.02 -                              | 173.28                          | 126.94                                | 01/2017<br>03/2018                    | 03/2018     | 14                       | -4.28               |                                                                     |
| 79                             | NEW 250 TMTPL LPG PLANT AT PANAGARH - [N16000222]HPCL, WEST BENGAL                                                           | 08/2014                          | 190.45 -                              | 190.45                          | 130.15                                | 09/2017<br>03/2018                    | 03/2018     | 6                        | 0                   |                                                                     |
| 80                             | DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC, MAHARASHTRA                                                            | 03/2012                          | 2,592.17 -                            | 2,592.17                        | 2,040.89                              | 05/2014<br>05/2018                    | 05/2018     | 48                       | 0                   |                                                                     |



## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                               |                                  |                                       |                                 |                                       | (September 2017)                      |             |                          |                     |                                                                     |
|--------------------------------|-------------------------------------------------------------------------------------------------------------------------------|----------------------------------|---------------------------------------|---------------------------------|---------------------------------------|---------------------------------------|-------------|--------------------------|---------------------|---------------------------------------------------------------------|
|                                |                                                                                                                               |                                  |                                       |                                 |                                       | Date of Commissioning<br>(Month/Year) |             |                          |                     | Reasons for Delay<br>(As Reported by Project Implementing Agencies) |
| S.No                           | Project                                                                                                                       | Date of Approval<br>(Month/Year) | Original/ Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs. crore) | Cumulative Expenditure<br>(Rs. crore) | Original / Revised                    | Anticipated | Time Overrun<br>(Months) | Cost Overrun<br>(%) |                                                                     |
| 1                              | 2                                                                                                                             | 3                                | 4                                     | 5                               | 6                                     | 7                                     | 8           | 9                        | 10                  | 11                                                                  |
| 81                             | MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA                                                                | 06/2014                          | 5,706.47<br>5,813.25                  | 5,813.25                        | 5,554.21                              | 05/2017<br>05/2018                    | 05/2018     | 12                       | 1.87                |                                                                     |
| 82                             | PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA                                                                 | 02/2015                          | 2,899.93<br>-                         | 2,098.43                        | 1,237.43                              | 05/2017<br>05/2018                    | 05/2018     | 12                       | -27.64              |                                                                     |
| 83                             | PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT                                                             | 09/2011                          | 202.25<br>-                           | 160.16                          | 106.98                                | 07/2016<br>06/2018                    | 06/2018     | 23                       | -20.81              |                                                                     |
| 84                             | DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL                                 | 03/2014                          | 3,076.00<br>4,190.00                  | 4,190.00                        | 2,097.09                              | 09/2017<br>06/2018                    | 06/2018     | 9                        | 36.22               |                                                                     |
| 85                             | ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM                                                                     | 03/2009                          | 2,465.15<br>-                         | 2,378.89                        | 2,060.68                              | 03/2013<br>09/2018                    | 09/2018     | 66                       | -3.5                |                                                                     |
| 86                             | SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE           | 07/2011                          | 352.56<br>-                           | 439.03                          | 126.43                                | 03/2017<br>-                          | 11/2018     | 20                       | 24.53               |                                                                     |
| 87                             | POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA                                                              | 03/2014                          | 3,150.00<br>-                         | 3,150.00                        | 1,289.32                              | 09/2017<br>12/2018                    | 12/2018     | 15                       | 0                   |                                                                     |
| 88                             | KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE                                           | 06/2009                          | 2,915.00<br>2,915.00                  | 2,915.00                        | 1,258.49                              | 12/2012<br>-                          | 02/2019     | 74                       | 0                   |                                                                     |
| 89                             | LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA                                                                                | 10/2015                          | 607.06<br>714.25                      | 714.25                          | 276.85                                | 10/2017<br>-                          | 03/2019     | 17                       | 17.66               |                                                                     |
| 90                             | ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA | 01/2015                          | 4,619.94<br>-                         | 3,961.54                        | 3,386.30                              | 12/2017<br>03/2019                    | 03/2019     | 15                       | -14.25              |                                                                     |
| 91                             | Field Development Plan of Madanam NGLP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU                                      | 11/2015                          | 390.52<br>-                           | 390.52                          | 67.52                                 | 03/2019<br>-                          | 04/2019     | 1                        | 0                   |                                                                     |
| 92                             | PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA                                  | 11/2014                          | 4,588.29<br>5,245.96                  | 4,588.29                        | 871.49                                | 08/2018<br>05/2019                    | 05/2019     | 9                        | 0                   |                                                                     |
| 93                             | CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE                                                 | 06/2007                          | 736.65<br>-                           | 571.47                          | 541.66                                | 09/2011<br>06/2019                    | 06/2019     | 93                       | -22.42              |                                                                     |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                   |                               |                                    |                              |                                    | (September 2017)                   |             |                       |                  |                                                                                                                                                                                                      |
|--------------------------------|---------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
|                                |                                                                                                   |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies)                                                                                                                                     |
| S.No                           | Project                                                                                           | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                                                                                                                                                      |
| 1                              | 2                                                                                                 | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                                                                                                                                                                   |
| 94                             | DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI                                          | 08/2014                       | 6,086.08 -                         | 5,479.75                     | 2,081.12                           | 05/2019<br>10/2019                 | 10/2019     | 5                     | -9.96            |                                                                                                                                                                                                      |
| 95                             | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM    | 06/2010                       | 202.94<br>341.70                   | 330.35                       | 2.11                               | 01/2014<br>11/2019                 | 11/2019     | 70                    | 62.78            |                                                                                                                                                                                                      |
| 96                             | NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA | 08/2015                       | 2,818.88 -                         | 2,818.88                     | 310.71                             | 03/2019<br>05/2020                 | 05/2020     | 14                    | 0                |                                                                                                                                                                                                      |
| 97                             | PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE                                         | 01/2015                       | 690.00 -                           | 690.00                       | 133.55                             | 07/2018<br>06/2020                 | 06/2020     | 23                    | 0                |                                                                                                                                                                                                      |
|                                | Total                                                                                             |                               | 59,790.32 -                        | 63,010.99                    | 37,873.49                          |                                    |             |                       |                  |                                                                                                                                                                                                      |
|                                |                                                                                                   |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                                                                                                      |
|                                | <u>POWER</u>                                                                                      |                               |                                    |                              |                                    |                                    |             |                       |                  |                                                                                                                                                                                                      |
| 98                             | TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM                                 | 07/1998                       | 368.72<br>1,329.43                 | 1,329.43                     | 1,278.65                           | 07/2006<br>11/2017                 | 11/2017     | 136                   | 260.55           |                                                                                                                                                                                                      |
| 99                             | KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA                                                    | 01/2012                       | 15,166.19 -                        | 15,166.19                    | 14,295.00                          | 01/2017<br>07/2017                 | 11/2017     | 10                    | 0                |                                                                                                                                                                                                      |
| 100                            | NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE                | 02/2014                       | 908.08<br>969.97                   | 969.97                       | 716.39                             | 06/2016<br>02/2018                 | 11/2017     | 17                    | 6.82             | Project completed except ICT at Parbati PS, held up due to non-availability of shut down. Non-availability of down-stream line by HPSEB at Parbati PS shall, however, affect commissioning.          |
| 101                            | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH          | 01/2016                       | 305.04 -                           | 305.04                       | 156.38                             | 03/2017<br>10/2017                 | 11/2017     | 8                     | 0                | Work slowed-down to match Gen. project (Gen. project ant. by Nov'17).                                                                                                                                |
| 102                            | BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM                                          | 01/2008                       | 4,375.35<br>6,749.18               | 6,749.18                     | 6,797.00                           | 09/2011<br>06/2017                 | 12/2017     | 75                    | 54.25            |                                                                                                                                                                                                      |
| 103                            | NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE                 | 02/2009                       | 11,130.19<br>13,762.80             | 13,762.80                    | 12,549.95                          | 08/2013<br>12/2017                 | 12/2017     | 52                    | 23.65            | Balance lines (linked to Gen. Proj.) to be completed matching with Generation Project. Kaneng HEP scheduled in Dec'17 and & Lower Subhansiri HEP is schedule uncertain.(agitation against big dams). |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                                    |                                  |                                       |                                 |                                       | (September 2017)                      |             |                          |                     |                                                                                                                                                                 |
|--------------------------------|------------------------------------------------------------------------------------------------------------------------------------|----------------------------------|---------------------------------------|---------------------------------|---------------------------------------|---------------------------------------|-------------|--------------------------|---------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------|
|                                |                                                                                                                                    |                                  |                                       |                                 |                                       | Date of Commissioning<br>(Month/Year) |             |                          |                     | Reasons for Delay<br>(As Reported by Project Implementing Agencies)                                                                                             |
| S.No                           | Project                                                                                                                            | Date of Approval<br>(Month/Year) | Original/ Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs. crore) | Cumulative Expenditure<br>(Rs. crore) | Original / Revised                    | Anticipated | Time Overrun<br>(Months) | Cost Overrun<br>(%) |                                                                                                                                                                 |
| 1                              | 2                                                                                                                                  | 3                                | 4                                     | 5                               | 6                                     | 7                                     | 8           | 9                        | 10                  | 11                                                                                                                                                              |
| 104                            | SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE                                                                      | 02/2010                          | 232.34<br>-                           | 245.00                          | 238.61                                | 06/2012<br>-                          | 12/2017     | 66                       | 5.45                | (Completion subject to resolution of issue by Nov'17).                                                                                                          |
| 105                            | EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE                                                             | 07/2010                          | 1,272.80<br>1,731.10                  | 1,731.10                        | 1,413.61                              | 11/2012<br>12/2017                    | 12/2017     | 61                       | 36.01               | Down stream 220KV line of state at Daltonganj required matching with readiness of Sasaram - Daltonganj line & Daltonganj sub station anticipated by Dec'17.     |
| 106                            | COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU | 09/2011                          | 1,940.13<br>2,702.65                  | 2,702.65                        | 2,326.66                              | 09/2014<br>06/2017                    | 12/2017     | 39                       | 39.3                | Balance line affected due to severe ROW problem                                                                                                                 |
| 107                            | SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE                                                        | 12/2011                          | 297.33<br>346.79                      | 426.29                          | 357.17                                | 08/2014<br>12/2017                    | 12/2017     | 40                       | 43.37               | Implementation affected due to severe ROW problem in Bengaluru area                                                                                             |
| 108                            | SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH                   | 12/2011                          | 1,746.65<br>2,228.71                  | 2,228.71                        | 1,962.81                              | 08/2014<br>12/2017                    | 12/2017     | 40                       | 27.6                | Implementation of Kudus (Padghe) S/stn. & associated down stream lines being executed by MSETCL. Critical for commissioning of balance lines under the project. |
| 109                            | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE                                                    | 11/2011                          | 723.63<br>882.13                      | 882.13                          | 719.42                                | 11/2014<br>06/2017                    | 12/2017     | 37                       | 21.9                | Implementation affected due to severe ROW                                                                                                                       |
| 110                            | UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE                                                 | 01/2014                          | 374.63<br>-                           | 374.63                          | 102.47                                | 04/2016<br>12/2017                    | 12/2017     | 20                       | 0                   |                                                                                                                                                                 |
| 111                            | STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE                                                   | 05/2014                          | 829.98<br>-                           | 829.98                          | 408.14                                | 08/2016<br>10/2017                    | 12/2017     | 16                       | 0                   | Implementation of balance work affected due to disturbance in J&K.                                                                                              |
| 112                            | AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE                                            | 03/2014                          | 155.57<br>206.42                      | 206.42                          | 131.33                                | 03/2016<br>07/2017                    | 12/2017     | 21                       | 32.69               | Implementation of balance affected due to delay in equipment supply(Off-shore) & non-readiness of down stream line by State Govt. at Hamirpur.                  |
| 113                            | EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE                                                             | 02/2014                          | 196.58<br>225.28                      | 225.28                          | 129.10                                | 02/2016<br>08/2017                    | 12/2017     | 22                       | 14.6                | Implementation affected due to delay in manufacturing of Reactors by Vendor.                                                                                    |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                     |                                  |                                       |                                 |                                       | (September 2017)                      |             |                          |                     |                                                                                                                                                                      |
|--------------------------------|-----------------------------------------------------------------------------------------------------|----------------------------------|---------------------------------------|---------------------------------|---------------------------------------|---------------------------------------|-------------|--------------------------|---------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------|
|                                |                                                                                                     |                                  |                                       |                                 |                                       | Date of Commissioning<br>(Month/Year) |             |                          |                     | Reasons for Delay<br>(As Reported by Project Implementing Agencies)                                                                                                  |
| S.No                           | Project                                                                                             | Date of Approval<br>(Month/Year) | Original/ Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs. crore) | Cumulative Expenditure<br>(Rs. crore) | Original / Revised                    | Anticipated | Time Overrun<br>(Months) | Cost Overrun<br>(%) |                                                                                                                                                                      |
| 1                              | 2                                                                                                   | 3                                | 4                                     | 5                               | 6                                     | 7                                     | 8           | 9                        | 10                  | 11                                                                                                                                                                   |
| 114                            | SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE                      | 01/2015                          | 203.28<br>260.03                      | 260.03                          | 160.70                                | 07/2017<br>-                          | 12/2017     | 5                        | 27.92               |                                                                                                                                                                      |
| 115                            | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR            | 05/2015                          | 436.68<br>-                           | 602.44                          | 472.27                                | 12/2016<br>-                          | 12/2017     | 12                       | 37.96               |                                                                                                                                                                      |
| 116                            | ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE | 03/2012                          | 198.63<br>-                           | 198.63                          | 135.20                                | 09/2014<br>09/2017                    | 01/2018     | 40                       | 0                   | having ROW issues. Stringing affected due to non-readiness of TL for taking-up OPGW installation.                                                                    |
| 117                            | KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR                                      | 01/2009                          | 3,642.04<br>-                         | 5,882.01                        | 5,052.02                              | 01/2016<br>-                          | 02/2018     | 25                       | 61.5                |                                                                                                                                                                      |
| 118                            | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE           | 10/2008                          | 4,824.12<br>5,071.94                  | 5,071.94                        | 4,475.16                              | 10/2012<br>02/2018                    | 02/2018     | 64                       | 5.14                | ROW problem also being encountered, apart from poor performance by executing agency necessitating termination & re-awarding fresh contracts.                         |
| 119                            | TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE         | 02/2010                          | 2,144.00<br>2,932.88                  | 2,932.88                        | 2,564.46                              | 12/2012<br>02/2018                    | 02/2018     | 62                       | 36.79               | due to local disturbances & geographical constraints. 01 line in Arunachal Pradesh (Tezu-Namsai line) affected due to compensation issues & land ownership disputes. |
| 120                            | NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE                    | 02/2014                          | 539.82<br>-                           | 539.82                          | 386.19                                | 06/2016<br>02/2018                    | 02/2018     | 20                       | 0                   | Implementation affected due to severe ROW problem at singrauli end. Work also affected due to poor performance by executing agency.                                  |
| 121                            | KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH                         | 12/2004                          | 2,496.90<br>6,179.96                  | 6,179.96                        | 5,971.88                              | 12/2009<br>03/2018                    | 03/2018     | 99                       | 147.51              |                                                                                                                                                                      |
| 122                            | WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA                                | 12/2007                          | 477.69<br>738.48                      | 738.48                          | 647.49                                | 09/2010<br>12/2017                    | 03/2018     | 90                       | 54.59               | Severe ROW problem in                                                                                                                                                |
| 123                            | PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH                                   | 12/2008                          | 573.99<br>1,337.76                    | 1,337.76                        | 1,499.78                              | 08/2013<br>03/2018                    | 03/2018     | 55                       | 133.06              |                                                                                                                                                                      |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                                     |                                  |                                       |                                 |                                       | (September 2017)                      |             |                          |                     |                                                                                                                                                                                                                     |
|--------------------------------|-------------------------------------------------------------------------------------------------------------------------------------|----------------------------------|---------------------------------------|---------------------------------|---------------------------------------|---------------------------------------|-------------|--------------------------|---------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
|                                |                                                                                                                                     |                                  |                                       |                                 |                                       | Date of Commissioning<br>(Month/Year) |             |                          |                     | Reasons for Delay<br>(As Reported by Project Implementing Agencies)                                                                                                                                                 |
| S.No                           | Project                                                                                                                             | Date of Approval<br>(Month/Year) | Original/ Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs. crore) | Cumulative Expenditure<br>(Rs. crore) | Original / Revised                    | Anticipated | Time Overrun<br>(Months) | Cost Overrun<br>(%) |                                                                                                                                                                                                                     |
| 1                              | 2                                                                                                                                   | 3                                | 4                                     | 5                               | 6                                     | 7                                     | 8           | 9                        | 10                  | 11                                                                                                                                                                                                                  |
| 124                            | TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL, WEST BENGAL | 04/2010                          | 4,404.57<br>5,135.01                  | 5,135.01                        | 3,453.64                              | 01/2015<br>03/2018                    | 03/2018     | 38                       | 16.58               | Gen. Proj.(Punatsangchu-I HEP in Bhutan) getting delayed                                                                                                                                                            |
| 125                            | COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL, MULTI STATE   | 03/2013                          | 514.20<br>703.10                      | 703.10                          | 565.59                                | 06/2015<br>12/2017                    | 03/2018     | 33                       | 36.74               | .                                                                                                                                                                                                                   |
| 126                            | COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL, MULTI STATE   | 03/2013                          | 2,514.88<br>-                         | 2,514.88                        | 1,959.67                              | 12/2015<br>12/2017                    | 03/2018     | 27                       | 0                   | Implementation affected due to severe ROW problem & huge forest involvement. forest clearance stage-I for Chattisgarh issued in Jul'17 & working permission awaited. Working permission received in Odisha portion. |
| 127                            | GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC, MADHYA PRADESH                                                     | 03/2013                          | 11,638.55<br>-                        | 11,638.55                       | 8,147.00                              | 09/2017<br>03/2018                    | 03/2018     | 6                        | 0                   |                                                                                                                                                                                                                     |
| 128                            | EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL, MULTI STATE                                                               | 10/2013                          | 1,364.52<br>1,891.41                  | 1,891.41                        | 1,151.24                              | 04/2016<br>09/2017                    | 03/2018     | 23                       | 38.61               | Implementation affected due to severe ROW.                                                                                                                                                                          |
| 129                            | EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL, MULTI STATE                                                             | 05/2014                          | 522.29<br>550.18                      | 550.18                          | 362.94                                | 11/2016<br>11/2017                    | 03/2018     | 16                       | 5.34                | due to delay in supply of transformers due to testing issues and other transportation constraints.                                                                                                                  |
| 130                            | SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL, MULTI STATE                                                 | 08/2014                          | 288.49<br>-                           | 376.09                          | 219.91                                | 02/2017<br>06/2017                    | 03/2018     | 13                       | 30.37               |                                                                                                                                                                                                                     |
| 131                            | GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL, MULTI STATE                              | 04/2015                          | 1,479.30<br>-                         | 1,479.30                        | 706.27                                | 04/2017<br>03/2018                    | 03/2018     | 11                       | 0                   | Work has been slowed-down to match with Generation (ant. by Mar'18). Severe ROW problem in Ajmer – Ajmer line. Matter already taken up with State Govt.                                                             |
| 132                            | TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL, MULTI STATE                  | 03/2015                          | 955.00<br>1,161.00                    | 1,364.00                        | 1,075.00                              | 12/2015<br>-                          | 03/2018     | 27                       | 42.83               |                                                                                                                                                                                                                     |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                          |                                  |                                          |                                 |                                       | (September 2017)                      |             |                          |                     |                                                                                                                              |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------|----------------------------------|------------------------------------------|---------------------------------|---------------------------------------|---------------------------------------|-------------|--------------------------|---------------------|------------------------------------------------------------------------------------------------------------------------------|
|                                |                                                                                                                          |                                  |                                          |                                 |                                       | Date of Commissioning<br>(Month/Year) |             |                          |                     | Reasons for Delay<br>(As Reported by Project Implementing Agencies)                                                          |
| S.No                           | Project                                                                                                                  | Date of Approval<br>(Month/Year) | Original/<br>Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs. crore) | Cumulative Expenditure<br>(Rs. crore) | Original /<br>Revised                 | Anticipated | Time Overrun<br>(Months) | Cost Overrun<br>(%) |                                                                                                                              |
| 1                              | 2                                                                                                                        | 3                                | 4                                        | 5                               | 6                                     | 7                                     | 8           | 9                        | 10                  | 11                                                                                                                           |
| 133                            | TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM CUDDALORE AREA – PACKAGE A - [N18000259]PGCIL,MULTI STATE       | 03/2015                          | 955.00<br>1,161.00                       | 1,364.00                        | 515.00                                | 12/2015<br>-                          | 03/2018     | 27                       | 42.83               |                                                                                                                              |
| 134                            | SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA                                                                               | 03/2012                          | 9,395.18<br>-                            | 9,395.18                        | 8,052.00                              | 11/2016<br>12/2017                    | 04/2018     | 17                       | 0                   |                                                                                                                              |
| 135                            | LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATTISGARH                                     | 12/2012                          | 11,846.00<br>-                           | 11,846.00                       | 8,605.00                              | 06/2017<br>12/2017                    | 04/2018     | 10                       | 0                   |                                                                                                                              |
| 136                            | INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE                                                | 03/2015                          | 1,071.24<br>-                            | 1,071.24                        | 462.18                                | 09/2017<br>-                          | 04/2018     | 7                        | 0                   |                                                                                                                              |
| 137                            | SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE                                                      | 10/2011                          | 487.49<br>639.46                         | 639.46                          | 485.42                                | 06/2014<br>03/2018                    | 06/2018     | 48                       | 31.17               | to severe ROW problem.                                                                                                       |
| 138                            | TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE | 06/2014                          | 5,151.37<br>-                            | 5,151.37                        | 1,474.02                              | 03/2018<br>-                          | 06/2018     | 3                        | 0                   | Completion likely to be delay due to delay in off-shore supply.                                                              |
| 139                            | TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE                        | 01/2015                          | 871.62<br>-                              | 871.62                          | 141.74                                | 10/2017<br>10/2017                    | 06/2018     | 8                        | 0                   | Gen. project delayed. Work on ATS are being slowed-down to extent possible to match with Generation (ant. by Sep'19).        |
| 140                            | BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR                                                               | 01/2007                          | 5,353.00<br>7,998.00                     | 7,998.00                        | 6,783.73                              | 05/2014<br>09/2017                    | 06/2018     | 49                       | 49.41               |                                                                                                                              |
| 141                            | MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH                                                           | 04/2012                          | 9,750.89<br>-                            | 9,750.89                        | 6,957.91                              | 12/2016<br>-                          | 06/2018     | 18                       | 0                   |                                                                                                                              |
| 142                            | TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN                                   | 07/2015                          | 307.18<br>-                              | 307.18                          | 153.62                                | 11/2017<br>-                          | 06/2018     | 7                        | 0                   | Generation project ant. in 2019-20/beyond. Work slowed-down to extent possible to match the generation.                      |
| 143                            | GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE                            | 04/2015                          | 3,705.61<br>-                            | 3,705.61                        | 2,077.41                              | 04/2018<br>-                          | 07/2018     | 3                        | 0                   | Implementation affected due to severe ROW problem & forest clearance (awaited). Generation project delayed (ant. by Jul'18). |
| 144                            | KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU                                                      | 05/2005                          | 1,779.29<br>2,187.32                     | 2,187.32                        | 1,955.61                              | 11/2008<br>09/2018                    | 09/2018     | 118                      | 22.93               | affected due to severe ROW problem (long pending).                                                                           |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                                     |                                  |                                       |                                 |                                       | (September 2017)                      |             |                          |                     |                                                                                                                             |
|--------------------------------|-------------------------------------------------------------------------------------------------------------------------------------|----------------------------------|---------------------------------------|---------------------------------|---------------------------------------|---------------------------------------|-------------|--------------------------|---------------------|-----------------------------------------------------------------------------------------------------------------------------|
|                                |                                                                                                                                     |                                  |                                       |                                 |                                       | Date of Commissioning<br>(Month/Year) |             |                          |                     | Reasons for Delay<br>(As Reported by Project Implementing Agencies)                                                         |
| S.No                           | Project                                                                                                                             | Date of Approval<br>(Month/Year) | Original/ Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs. crore) | Cumulative Expenditure<br>(Rs. crore) | Original / Revised                    | Anticipated | Time Overrun<br>(Months) | Cost Overrun<br>(%) |                                                                                                                             |
| 1                              | 2                                                                                                                                   | 3                                | 4                                     | 5                               | 6                                     | 7                                     | 8           | 9                        | 10                  | 11                                                                                                                          |
| 145                            | TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR    | 01/2014                          | 1,788.41 -                            | 2,352.57                        | 1,154.26                              | 09/2017 -                             | 09/2018     | 12                       | 31.55               | Implementation affected due to delay in land acquisition of Kargil S/s.                                                     |
| 146                            | PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH                                                                 | 09/2002                          | 3,919.59 -                            | 8,398.75                        | 6,503.48                              | 09/2009 -                             | 12/2018     | 111                      | 114.28              |                                                                                                                             |
| 147                            | DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH                                                                       | 05/2011                          | 195.42<br>294.60                      | 294.60                          | 130.15                                | 02/2014<br>02/2018                    | 12/2018     | 58                       | 50.75               | Ind stage forest clearance for Power Evacuation Arrangement.                                                                |
| 148                            | NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR                                                                       | 01/2013                          | 12,964.60 -                           | 13,731.26                       | 10,084.21                             | 01/2018 -                             | 12/2018     | 11                       | 5.91                |                                                                                                                             |
| 149                            | BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR                                                                                     | 02/2005                          | 8,692.97<br>15,095.67                 | 15,095.67                       | 13,727.00                             | 01/2011<br>05/2018                    | 03/2019     | 98                       | 73.65               |                                                                                                                             |
| 150                            | TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE | 03/2016                          | 808.63 -                              | 808.63                          | 195.53                                | 01/2018 -                             | 03/2019     | 14                       | 0                   | Implementation affected due to forest (Tiger reserve) clearance..                                                           |
| 151                            | TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND                                                                       | 11/2006                          | 2,978.48 -                            | 3,846.30                        | 3,300.00                              | 03/2013<br>06/2019                    | 06/2019     | 75                       | 29.14               |                                                                                                                             |
| 152                            | CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI                        | 03/2015                          | 1,394.52 -                            | 1,394.52                        | 19.20                                 | 05/2017<br>06/2019                    | 06/2019     | 25                       | 0                   | Implementation affected due to delayed in land acquisition (land hand over for Dwarka-I S/s in Aug'16 & Rajghat in Dec'16). |
| 153                            | COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE        | 12/2014                          | 4,754.42 -                            | 4,754.42                        | 361.65                                | 12/2018 -                             | 12/2019     | 12                       | 0                   | Award have been delayed due to poor response & high prices quoted by bidders.                                               |
| 154                            | NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE                   | 12/2014                          | 5,111.33 -                            | 5,111.33                        | 352.58                                | 12/2018 -                             | 12/2019     | 12                       | 0                   | Land for 05 nos. distribution Sub station yet to be handed over.                                                            |
| 155                            | VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND                                                          | 08/2008                          | 2,491.58 -                            | 2,491.58                        | 1,244.96                              | 06/2013 -                             | 11/2020     | 89                       | 0                   | Reasons pending with state government: .                                                                                    |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                    |                                  |                                       |                                 |                                       | (September 2017)                      |             |                          |                     |                                                                                                                                                                                                                                                 |
|--------------------------------|----------------------------------------------------------------------------------------------------|----------------------------------|---------------------------------------|---------------------------------|---------------------------------------|---------------------------------------|-------------|--------------------------|---------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
|                                |                                                                                                    |                                  |                                       |                                 |                                       | Date of Commissioning<br>(Month/Year) |             |                          |                     | Reasons for Delay<br>(As Reported by Project Implementing Agencies)                                                                                                                                                                             |
| S.No                           | Project                                                                                            | Date of Approval<br>(Month/Year) | Original/ Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs. crore) | Cumulative Expenditure<br>(Rs. crore) | Original / Revised                    | Anticipated | Time Overrun<br>(Months) | Cost Overrun<br>(%) |                                                                                                                                                                                                                                                 |
| 1                              | 2                                                                                                  | 3                                | 4                                     | 5                               | 6                                     | 7                                     | 8           | 9                        | 10                  | 11                                                                                                                                                                                                                                              |
| 156                            | TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND                                 | 07/2006                          | 1,657.00<br>2,978.86                  | 3,939.11                        | 2,373.15                              | 02/2016<br>09/2019                    | 12/2020     | 58                       | 137.73              | Law and order problem Dharna at crusher plant area has again been started by locals since 05.10.17.                                                                                                                                             |
| 157                            | NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND                                        | 02/2014                          | 14,366.58<br>-                        | 14,366.58                       | 5,493.00                              | 02/2019<br>02/2020                    | 02/2021     | 24                       | 0                   |                                                                                                                                                                                                                                                 |
| 158                            | PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR                   | 10/2014                          | 8,112.12<br>-                         | 8,112.12                        | -                                     | 04/2020<br>-                          | 05/2023     | 37                       | 0                   |                                                                                                                                                                                                                                                 |
|                                | Total                                                                                              |                                  | 1,99,151.68<br>-                      | 2,36,516.58                     | 1,65,191.91                           |                                       |             |                          |                     |                                                                                                                                                                                                                                                 |
|                                |                                                                                                    |                                  |                                       |                                 |                                       |                                       |             |                          |                     |                                                                                                                                                                                                                                                 |
|                                | <u>HEAVY INDUSTRY</u>                                                                              |                                  |                                       |                                 |                                       |                                       |             |                          |                     |                                                                                                                                                                                                                                                 |
| 159                            | NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE | 04/2011                          | 1,718.00<br>-                         | 3,827.30                        | 2,289.00                              | 09/2011<br>-                          | 12/2017     | 75                       | 122.78              |                                                                                                                                                                                                                                                 |
|                                | Total                                                                                              |                                  | 1,718.00<br>-                         | 3,827.30                        | 2,289.00                              |                                       |             |                          |                     |                                                                                                                                                                                                                                                 |
|                                |                                                                                                    |                                  |                                       |                                 |                                       |                                       |             |                          |                     |                                                                                                                                                                                                                                                 |
|                                | <u>HEALTH AND FAMILY WELFARE</u>                                                                   |                                  |                                       |                                 |                                       |                                       |             |                          |                     |                                                                                                                                                                                                                                                 |
| 160                            | AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI                                             | 12/2013                          | 204.44<br>-                           | 204.44                          | 137.00                                | 05/2017<br>-                          | 12/2017     | 7                        | 0                   |                                                                                                                                                                                                                                                 |
| 161                            | AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI                                                           | 08/2014                          | 293.65<br>-                           | 293.65                          | 207.00                                | 05/2017<br>-                          | 12/2017     | 7                        | 0                   |                                                                                                                                                                                                                                                 |
| 162                            | CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL                       | 12/2014                          | 168.90<br>-                           | 168.90                          | 108.00                                | 05/2017<br>-                          | 12/2017     | 7                        | 0                   | Slow progress on account of labor and material constraints created by the localized unions /goons                                                                                                                                               |
| 163                            | SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB                            | 07/2016                          | 152.95<br>-                           | 152.95                          | 33.50                                 | 02/2018<br>-                          | 08/2018     | 6                        | 0                   | Progress impacted due to shortage of construction/Building material due to Punjab Govt. Notification banning the mining /querying of aggregate and sand since 18.03.2017, Delay in submission/Mobilization of structural drawings by the agency |
| 164                            | NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA                                            | 10/2016                          | 363.99<br>-                           | 363.99                          | 6.00                                  | 05/2018<br>08/2019                    | 08/2019     | 15                       | 0                   |                                                                                                                                                                                                                                                 |
|                                | Total                                                                                              |                                  | 1,183.93<br>-                         | 1,183.93                        | 491.50                                |                                       |             |                          |                     |                                                                                                                                                                                                                                                 |



## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                |                                  |                                       |                                 |                                       | (September 2017)                      |             |                          |                     |                                                                     |
|--------------------------------|----------------------------------------------------------------------------------------------------------------|----------------------------------|---------------------------------------|---------------------------------|---------------------------------------|---------------------------------------|-------------|--------------------------|---------------------|---------------------------------------------------------------------|
|                                |                                                                                                                |                                  |                                       |                                 |                                       | Date of Commissioning<br>(Month/Year) |             |                          |                     | Reasons for Delay<br>(As Reported by Project Implementing Agencies) |
| S.No                           | Project                                                                                                        | Date of Approval<br>(Month/Year) | Original/ Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs. crore) | Cumulative Expenditure<br>(Rs. crore) | Original / Revised                    | Anticipated | Time Overrun<br>(Months) | Cost Overrun<br>(%) |                                                                     |
| 1                              | 2                                                                                                              | 3                                | 4                                     | 5                               | 6                                     | 7                                     | 8           | 9                        | 10                  | 11                                                                  |
|                                | <u>RAILWAYS</u>                                                                                                |                                  |                                       |                                 |                                       |                                       |             |                          |                     |                                                                     |
| 165                            | NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH                                                    | 03/1996                          | 155.74<br>164.36                      | 966.98                          | 874.72                                | 02/2009<br>-                          | 12/2017     | 106                      | 520.89              |                                                                     |
| 166                            | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA                                             | 04/2000                          | 133.41<br>207.00                      | 340.00                          | -                                     | 03/2009<br>03/2009                    | 12/2017     | 105                      | 154.85              |                                                                     |
| 167                            | SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH                                              | 09/2006                          | 324.90<br>-                           | 516.40                          | 479.68                                | 03/2010<br>-                          | 12/2017     | 93                       | 58.94               |                                                                     |
| 168                            | UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT                                      | 04/2008                          | 1,389.62<br>-                         | 1,389.62                        | 1,513.78                              | 03/2014<br>-                          | 12/2017     | 45                       | 0                   |                                                                     |
| 169                            | EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU                              | 04/2006                          | 495.74<br>-                           | 495.74                          | 404.30                                | 06/2013<br>-                          | 03/2018     | 57                       | 0                   |                                                                     |
| 170                            | BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH                                                  | 09/2007                          | 687.20<br>-                           | 950.00                          | -                                     | 03/2010<br>-                          | 03/2018     | 96                       | 38.24               |                                                                     |
| 171                            | LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM                  | 04/1996                          | 1,676.31<br>-                         | 7,000.00                        | 7,041.41                              | 03/2009<br>-                          | 03/2018     | 108                      | 317.58              |                                                                     |
| 172                            | BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM                                            | 09/1997                          | 1,500.00<br>-                         | 5,000.00                        | 4,793.77                              | 04/2008<br>12/2011                    | 06/2018     | 122                      | 233.33              |                                                                     |
| 173                            | EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL                         | 03/2013                          | 4,874.58<br>-                         | 4,874.58                        | 1,881.65                              | 03/2016<br>-                          | 06/2018     | 27                       | 0                   |                                                                     |
| 174                            | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR                                          | 03/1995                          | 2,500.00<br>-                         | 19,565.00                       | 13,536.97                             | 11/2002<br>-                          | 12/2018     | 193                      | 682.6               |                                                                     |
| 175                            | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL | 04/2010                          | 2,913.51<br>-                         | 2,913.50                        | 713.47                                | 03/2016<br>-                          | 12/2018     | 33                       | 0                   |                                                                     |
| 176                            | MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA                              | 04/2012                          | 632.68<br>-                           | 816.55                          | 451.81                                | 03/2016<br>-                          | 12/2018     | 33                       | 29.06               |                                                                     |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                               |                                  |                                       |                                 |                                       | (September 2017)                      |             |                          |                     |                                                                     |
|--------------------------------|-----------------------------------------------------------------------------------------------|----------------------------------|---------------------------------------|---------------------------------|---------------------------------------|---------------------------------------|-------------|--------------------------|---------------------|---------------------------------------------------------------------|
|                                |                                                                                               |                                  |                                       |                                 |                                       | Date of Commissioning<br>(Month/Year) |             |                          |                     | Reasons for Delay<br>(As Reported by Project Implementing Agencies) |
| S.No                           | Project                                                                                       | Date of Approval<br>(Month/Year) | Original/ Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs. crore) | Cumulative Expenditure<br>(Rs. crore) | Original / Revised                    | Anticipated | Time Overrun<br>(Months) | Cost Overrun<br>(%) |                                                                     |
| 1                              | 2                                                                                             | 3                                | 4                                     | 5                               | 6                                     | 7                                     | 8           | 9                        | 10                  | 11                                                                  |
| 177                            | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE         | 04/2000                          | 733.00<br>-                           | 3,010.00                        | 2,344.94                              | 12/2008<br>-                          | 03/2019     | 123                      | 310.64              |                                                                     |
| 178                            | MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA                        | 04/2008                          | 5,300.00<br>-                         | 7,986.04                        | 2,423.55                              | 03/2014<br>-                          | 03/2019     | 60                       | 50.68               |                                                                     |
| 179                            | BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT             | 04/2008                          | 318.24<br>-                           | 321.62                          | 37.15                                 | 03/2012<br>-                          | 03/2019     | 84                       | 1.06                |                                                                     |
| 180                            | KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH                           | 08/2015                          | 528.57<br>-                           | 528.57                          | 61.44                                 | 03/2018<br>-                          | 03/2019     | 12                       | 0                   |                                                                     |
| 181                            | JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]NWR, RAJASTHAN | 04/2008                          | 653.19<br>-                           | 941.04                          | 642.94                                | 03/2014<br>-                          | 06/2019     | 63                       | 44.07               |                                                                     |
| 182                            | GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE                                     | 02/1997                          | 386.30<br>-                           | 1,776.81                        | 967.96                                | 03/1998<br>-                          | 12/2019     | 261                      | 359.96              |                                                                     |
| 183                            | SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA                                     | 04/1998                          | 183.23<br>-                           | 1,202.70                        | 392.96                                | 02/2015<br>-                          | 12/2019     | 58                       | 556.39              |                                                                     |
| 184                            | GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL, JHARKHAND                                    | 03/1997                          | 261.70<br>-                           | 388.00                          | 329.39                                | 02/2006<br>-                          | 12/2019     | 166                      | 48.26               |                                                                     |
| 185                            | HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN                      | 04/2008                          | 829.74<br>-                           | 1,161.64                        | 435.68                                | 03/2015<br>-                          | 12/2019     | 57                       | 40                  |                                                                     |
| 186                            | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA              | 03/1996                          | 495.44<br>1,781.98                    | 1,781.98                        | 663.37                                | 03/2004<br>-                          | 03/2020     | 192                      | 259.68              |                                                                     |
| 187                            | MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER, JHARKHAND                                 | 04/1995                          | 900.05<br>-                           | 1,125.89                        | 980.99                                | 12/2011<br>12/2010                    | 03/2020     | 99                       | 25.09               |                                                                     |
| 188                            | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR                                 | 04/2003                          | 727.56<br>-                           | 9,658.00                        | 5,418.63                              | 03/2011<br>-                          | 03/2020     | 108                      | 1227.45             |                                                                     |
| 189                            | OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH                          | 07/2006                          | 743.00<br>-                           | 1,825.00                        | -                                     | 03/2008<br>06/2008                    | 03/2020     | 144                      | 145.63              |                                                                     |
| 190                            | AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA                                          | 04/2008                          | 813.34<br>-                           | 3,451.00                        | 2,351.21                              | 03/2014<br>-                          | 03/2020     | 72                       | 324.3               |                                                                     |
| 191                            | BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM                                          | 04/2008                          | 619.34<br>-                           | 4,600.00                        | 1,651.19                              | 04/2014<br>-                          | 03/2020     | 71                       | 642.73              |                                                                     |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                             |                                  |                                       |                                 |                                       | (September 2017)                      |             |                          |                     |                                                                     |
|--------------------------------|-----------------------------------------------------------------------------------------------------------------------------|----------------------------------|---------------------------------------|---------------------------------|---------------------------------------|---------------------------------------|-------------|--------------------------|---------------------|---------------------------------------------------------------------|
|                                |                                                                                                                             |                                  |                                       |                                 |                                       | Date of Commissioning<br>(Month/Year) |             |                          |                     | Reasons for Delay<br>(As Reported by Project Implementing Agencies) |
| S.No                           | Project                                                                                                                     | Date of Approval<br>(Month/Year) | Original/ Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs. crore) | Cumulative Expenditure<br>(Rs. crore) | Original / Revised                    | Anticipated | Time Overrun<br>(Months) | Cost Overrun<br>(%) |                                                                     |
| 1                              | 2                                                                                                                           | 3                                | 4                                     | 5                               | 6                                     | 7                                     | 8           | 9                        | 10                  | 11                                                                  |
| 192                            | SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM                                                                                  | 04/2008                          | 1,339.48 -                            | 4,084.69                        | 383.92                                | 12/2015 -                             | 03/2020     | 51                       | 204.95              |                                                                     |
| 193                            | AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT                                                                  | 04/2008                          | 394.14 -                              | 385.60                          | 27.69                                 | 03/2013 -                             | 03/2020     | 84                       | -2.17               |                                                                     |
| 194                            | NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND                                    | 04/2006                          | 850.00 -                              | 3,000.00                        | 362.71                                | 03/2015 -                             | 03/2020     | 60                       | 252.94              |                                                                     |
| 195                            | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL | 04/2010                          | 3,951.98 -                            | 4,259.48                        | 1,455.71                              | 03/2016 -                             | 12/2020     | 57                       | 7.78                |                                                                     |
| 196                            | KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH                                                              | 04/2015                          | 2,499.71 -                            | 2,499.71                        | 25.30                                 | 03/2021 -                             | 03/2022     | 12                       | 0                   |                                                                     |
| 197                            | KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA                                                                   | 04/2015                          | 2,361.74 -                            | 2,361.74                        | 17.49                                 | 03/2021 -                             | 03/2022     | 12                       | 0                   |                                                                     |
| 198                            | GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE                                                 | 04/2011                          | 1,176.09 -                            | 3,845.60                        | 1.92                                  | 02/2020 -                             | 12/2022     | 34                       | 226.98              |                                                                     |
| 199                            | DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE  | 04/2010                          | 622.41 -                              | 2,030.50                        | 10.34                                 | 02/2019 -                             | 12/2022     | 46                       | 226.23              |                                                                     |
| 200                            | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE                                                         | 09/1998                          | 247.66 -                              | 6,093.31                        | 972.82                                | 05/2008 -                             | 03/2023     | 178                      | 2360.35             |                                                                     |
|                                | Total                                                                                                                       |                                  | 44,219.60 -                           | 1,13,147.29                     | 53,650.86                             |                                       |             |                          |                     |                                                                     |
|                                |                                                                                                                             |                                  |                                       |                                 |                                       |                                       |             |                          |                     |                                                                     |
|                                | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                          |                                  |                                       |                                 |                                       |                                       |             |                          |                     |                                                                     |
| 201                            | NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM                                                                             | 12/2003                          | 225.00 -                              | 225.00                          | -                                     | 06/2008 -                             | 09/2017     | 111                      | 0                   |                                                                     |
| 202                            | SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE                                                     | 02/2009                          | 1,693.75 -                            | 1,693.75                        | 2,675.28                              | 08/2011 -                             | 09/2017     | 73                       | 0                   |                                                                     |
| 203                            | INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH                                                                    | 10/2010                          | 1,175.00 -                            | 1,206.10                        | 1,226.83                              | 04/2013 -                             | 09/2017     | 53                       | 2.65                |                                                                     |
| 204                            | MURADABAD-BAREILLY - [N24000154]NHAI,UTTAR PRADESH                                                                          | 04/2010                          | 1,267.00 -                            | 1,267.00                        | 2,664.02                              | 06/2013 -                             | 09/2017     | 51                       | 0                   |                                                                     |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                                       |                                  |                                       |                                 |                                       | (September 2017)                      |             |                          |                     |                                                                     |
|--------------------------------|---------------------------------------------------------------------------------------------------------------------------------------|----------------------------------|---------------------------------------|---------------------------------|---------------------------------------|---------------------------------------|-------------|--------------------------|---------------------|---------------------------------------------------------------------|
|                                |                                                                                                                                       |                                  |                                       |                                 |                                       | Date of Commissioning<br>(Month/Year) |             |                          |                     | Reasons for Delay<br>(As Reported by Project Implementing Agencies) |
| S.No                           | Project                                                                                                                               | Date of Approval<br>(Month/Year) | Original/ Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs. crore) | Cumulative Expenditure<br>(Rs. crore) | Original / Revised                    | Anticipated | Time Overrun<br>(Months) | Cost Overrun<br>(%) |                                                                     |
| 1                              | 2                                                                                                                                     | 3                                | 4                                     | 5                               | 6                                     | 7                                     | 8           | 9                        | 10                  | 11                                                                  |
| 205                            | PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR                                                                       | 09/2011                          | 574.00 -                              | 574.00                          | -                                     | 03/2014 -                             | 09/2017     | 42                       | 0                   |                                                                     |
| 206                            | TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI, RAJASTHAN                                                      | 09/2014                          | 425.19 -                              | 425.19                          | -                                     | 09/2016 -                             | 09/2017     | 12                       | 0                   |                                                                     |
| 207                            | 2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH                                | 09/2015                          | 368.73 -                              | 368.73                          | 203.84                                | 09/2016 -                             | 09/2017     | 12                       | 0                   |                                                                     |
| 208                            | FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI, MADHYA PRADESH                                                                     | 05/2013                          | 1,055.00 -                            | 1,601.77                        | 1,328.85                              | 11/2015 -                             | 09/2017     | 22                       | 51.83               |                                                                     |
| 209                            | DEOLI KOTA - [N24000148]NHAI, RAJASTHAN                                                                                               | 01/2011                          | 593.00 -                              | 593.00                          | -                                     | 07/2013 -                             | 10/2017     | 51                       | 0                   |                                                                     |
| 210                            | 2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR                                                                                   | 05/2011                          | 351.54 -                              | 351.54                          | -                                     | 05/2013 -                             | 10/2017     | 53                       | 0                   |                                                                     |
| 211                            | BAREILLY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH                                                                             | 03/2011                          | 1,046.00 -                            | 1,046.00                        | 577.00                                | 09/2013 -                             | 10/2017     | 49                       | 0                   |                                                                     |
| 212                            | ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH                                                                                       | 03/2013                          | 1,573.00 -                            | 1,573.00                        | 1,850.00                              | 09/2015 -                             | 10/2017     | 25                       | 0                   |                                                                     |
| 213                            | REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD, ANDHRA PRADESH | 03/2015                          | 271.45 -                              | 271.45                          | -                                     | 10/2015 -                             | 10/2017     | 24                       | 0                   |                                                                     |
| 214                            | JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR                                                               | 07/2010                          | 1,813.76 -                            | 1,813.76                        | -                                     | 07/2013 -                             | 11/2017     | 52                       | 0                   |                                                                     |
| 215                            | MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE                                                                                 | 09/2011                          | 754.00 -                              | 754.00                          | 1,101.13                              | 03/2013 -                             | 11/2017     | 56                       | 0                   |                                                                     |
| 216                            | STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH, KARNATAKA    | 03/2015                          | 165.67 -                              | 165.67                          | -                                     | 11/2015 -                             | 11/2017     | 24                       | 0                   |                                                                     |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                                    |                                  |                                       |                                 |                                       | (September 2017)                      |             |                          |                     |                                                                     |
|--------------------------------|------------------------------------------------------------------------------------------------------------------------------------|----------------------------------|---------------------------------------|---------------------------------|---------------------------------------|---------------------------------------|-------------|--------------------------|---------------------|---------------------------------------------------------------------|
|                                |                                                                                                                                    |                                  |                                       |                                 |                                       | Date of Commissioning<br>(Month/Year) |             |                          |                     | Reasons for Delay<br>(As Reported by Project Implementing Agencies) |
| S.No                           | Project                                                                                                                            | Date of Approval<br>(Month/Year) | Original/ Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs. crore) | Cumulative Expenditure<br>(Rs. crore) | Original / Revised                    | Anticipated | Time Overrun<br>(Months) | Cost Overrun<br>(%) |                                                                     |
| 1                              | 2                                                                                                                                  | 3                                | 4                                     | 5                               | 6                                     | 7                                     | 8           | 9                        | 10                  | 11                                                                  |
| 217                            | STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPUR - [N24000335]MORTH,KARNATAKA | 03/2015                          | 159.12 -                              | 159.12                          | -                                     | 11/2015 -                             | 11/2017     | 24                       | 0                   |                                                                     |
| 218                            | 2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH                               | 04/2014                          | 351.34 -                              | 351.34                          | 378.36                                | 01/2016 -                             | 11/2017     | 22                       | 0                   |                                                                     |
| 219                            | 2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH                                                 | 04/2014                          | 495.78 -                              | 495.78                          | 509.65                                | 01/2016 -                             | 11/2017     | 22                       | 0                   |                                                                     |
| 220                            | 4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA                                                  | 06/2014                          | 923.04 -                              | 923.04                          | 474.52                                | 11/2016 -                             | 11/2017     | 12                       | 0                   |                                                                     |
| 221                            | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM                                                     | 12/2003                          | 280.00 -                              | 361.00                          | -                                     | 02/2009 -                             | 12/2017     | 106                      | 28.93               |                                                                     |
| 222                            | NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM                                                                                     | 12/2003                          | 208.00 -                              | 208.00                          | -                                     | 04/2008 -                             | 12/2017     | 116                      | 0                   |                                                                     |
| 223                            | GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT                                                      | 03/2010                          | 1,509.10 -                            | 3,237.87                        | 3,187.19                              | 09/2012 -                             | 12/2017     | 63                       | 114.56              |                                                                     |
| 224                            | CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH                                                    | 11/2010                          | 1,585.00 -                            | 1,585.00                        | 2,284.33                              | 05/2013 -                             | 12/2017     | 55                       | 0                   |                                                                     |
| 225                            | SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA                                               | 02/2010                          | 617.00 -                              | 617.00                          | 245.89                                | 08/2012 -                             | 12/2017     | 64                       | 0                   |                                                                     |
| 226                            | 4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE                                                                             | 02/2011                          | 2,498.76 -                            | 2,498.76                        | 2,489.54                              | 08/2014 -                             | 12/2017     | 40                       | 0                   |                                                                     |
| 227                            | PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA                                                                                    | 10/2010                          | 1,724.55 -                            | 1,724.55                        | 2,051.04                              | 03/2013 -                             | 12/2017     | 57                       | 0                   |                                                                     |
| 228                            | SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU                               | 09/2011                          | 1,250.00 -                            | 1,250.00                        | 1,329.10                              | 12/2013 -                             | 12/2017     | 48                       | 0                   |                                                                     |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                         |                                  |                                       |                                 |                                       | (September 2017)                      |             |                          |                     |                                                                     |
|--------------------------------|-----------------------------------------------------------------------------------------|----------------------------------|---------------------------------------|---------------------------------|---------------------------------------|---------------------------------------|-------------|--------------------------|---------------------|---------------------------------------------------------------------|
|                                |                                                                                         |                                  |                                       |                                 |                                       | Date of Commissioning<br>(Month/Year) |             |                          |                     | Reasons for Delay<br>(As Reported by Project Implementing Agencies) |
| S.No                           | Project                                                                                 | Date of Approval<br>(Month/Year) | Original/ Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs. crore) | Cumulative Expenditure<br>(Rs. crore) | Original / Revised                    | Anticipated | Time Overrun<br>(Months) | Cost Overrun<br>(%) |                                                                     |
| 1                              | 2                                                                                       | 3                                | 4                                     | 5                               | 6                                     | 7                                     | 8           | 9                        | 10                  | 11                                                                  |
| 229                            | TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU         | 05/2010                          | 374.00 -                              | 374.00                          | 237.00                                | 05/2013 -                             | 12/2017     | 55                       | 0                   |                                                                     |
| 230                            | 2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU             | 09/2011                          | 485.00 -                              | 485.00                          | 406.68                                | 08/2013 -                             | 12/2017     | 52                       | 0                   |                                                                     |
| 231                            | TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH                         | 04/2011                          | 571.00 -                              | 571.00                          | 622.89                                | 10/2013 -                             | 12/2017     | 50                       | 0                   |                                                                     |
| 232                            | 2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR                             | 05/2011                          | 511.54 -                              | 511.54                          | -                                     | 11/2013 -                             | 12/2017     | 49                       | 0                   |                                                                     |
| 233                            | SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR                                 | 06/2011                          | 1,100.70 -                            | 1,100.70                        | -                                     | 06/2014 -                             | 12/2017     | 42                       | 0                   |                                                                     |
| 234                            | 4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL                               | 02/2011                          | 1,078.84 -                            | 1,078.84                        | 2,391.07                              | 08/2013 -                             | 12/2017     | 52                       | 0                   |                                                                     |
| 235                            | 6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL                   | 04/2012                          | 1,396.18 -                            | 1,396.18                        | 2,694.55                              | 09/2014 -                             | 12/2017     | 39                       | 0                   |                                                                     |
| 236                            | 2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH                | 07/2012                          | 291.36 -                              | 291.36                          | 320.46                                | 01/2014 -                             | 12/2017     | 47                       | 0                   |                                                                     |
| 237                            | HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND                      | 11/2011                          | 478.51 -                              | 478.00                          | 409.17                                | 10/2013 -                             | 12/2017     | 50                       | -11                 |                                                                     |
| 238                            | RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND                                     | 12/2012                          | 1,479.00 -                            | 1,479.00                        | 833.65                                | 06/2015 -                             | 12/2017     | 30                       | 0                   |                                                                     |
| 239                            | DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE                       | 10/2012                          | 1,928.22 -                            | 1,928.22                        | 2,488.00                              | 04/2015 -                             | 12/2017     | 32                       | 0                   |                                                                     |
| 240                            | BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL                                      | 08/2012                          | 867.00 -                              | 867.00                          | 278.17                                | 02/2015 -                             | 12/2017     | 34                       | 0                   |                                                                     |
| 241                            | JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB                                           | 01/2014                          | 523.85 -                              | 523.85                          | 248.85                                | 01/2016 -                             | 12/2017     | 23                       | 0                   |                                                                     |
| 242                            | GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN                      | 02/2008                          | 1,673.70 -                            | 1,673.70                        | 3,145.92                              | 10/2011 -                             | 12/2017     | 74                       | 0                   |                                                                     |
| 243                            | FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH | 02/2013                          | 1,232.00 -                            | 1,232.00                        | -                                     | 08/2015 -                             | 12/2017     | 28                       | 0                   |                                                                     |
| 244                            | 4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA             | 01/2015                          | 972.50 -                              | 972.50                          | 1,458.72                              | 07/2017 -                             | 01/2018     | 6                        | 0                   |                                                                     |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                                |                                  |                                          |                                 |                                       | (September 2017)                      |             |                          |                     |                                                                     |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------|----------------------------------|------------------------------------------|---------------------------------|---------------------------------------|---------------------------------------|-------------|--------------------------|---------------------|---------------------------------------------------------------------|
|                                |                                                                                                                                |                                  |                                          |                                 |                                       | Date of Commissioning<br>(Month/Year) |             |                          |                     | Reasons for Delay<br>(As Reported by Project Implementing Agencies) |
| S.No                           | Project                                                                                                                        | Date of Approval<br>(Month/Year) | Original/<br>Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs. crore) | Cumulative Expenditure<br>(Rs. crore) | Original /<br>Revised                 | Anticipated | Time Overrun<br>(Months) | Cost Overrun<br>(%) |                                                                     |
| 1                              | 2                                                                                                                              | 3                                | 4                                        | 5                               | 6                                     | 7                                     | 8           | 9                        | 10                  | 11                                                                  |
| 245                            | FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH                         | 11/2013                          | 1,916.79 -                               | 1,916.79                        | 1,851.95                              | 11/2016 -                             | 02/2018     | 15                       | 0                   |                                                                     |
| 246                            | BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM                                                                           | 12/2003                          | 217.61 -                                 | 309.56                          | -                                     | 04/2010 -                             | 03/2018     | 95                       | 42.25               |                                                                     |
| 247                            | PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA                                                        | 05/2009                          | 1,108.00 -                               | 2,288.00                        | 3,882.53                              | 11/2011 -                             | 03/2018     | 76                       | 106.5               |                                                                     |
| 248                            | JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA                                                                                 | 01/2011                          | 536.00 -                                 | 536.00                          | 672.72                                | 01/2014 -                             | 03/2018     | 50                       | 0                   |                                                                     |
| 249                            | 4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR                                                                           | 01/2011                          | 575.00 -                                 | 575.00                          | -                                     | 07/2013 -                             | 03/2018     | 56                       | 0                   |                                                                     |
| 250                            | 4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL                                                                   | 02/2011                          | 998.79 -                                 | 998.79                          | 1,930.50                              | 08/2013 -                             | 03/2018     | 55                       | 0                   |                                                                     |
| 251                            | KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL                                                                          | 02/2012                          | 702.16 -                                 | 702.16                          | 490.36                                | 07/2014 -                             | 03/2018     | 44                       | 0                   |                                                                     |
| 252                            | PANVEL-INDAPUR - [N24000216]NHAI, MAHARASHTRA                                                                                  | 12/2011                          | 942.69 -                                 | 942.69                          | 367.72                                | 06/2014 -                             | 03/2018     | 45                       | 0                   |                                                                     |
| 253                            | WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA                                 | 05/2013                          | 1,348.20 -                               | 1,348.20                        | 1,788.75                              | 02/2014 -                             | 03/2018     | 49                       | 0                   |                                                                     |
| 254                            | 4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA                                             | 04/2014                          | 1,266.60 -                               | 1,266.60                        | 1,360.00                              | 09/2016 -                             | 03/2018     | 18                       | 0                   |                                                                     |
| 255                            | 4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI, KARNATAKA                                                 | 05/2014                          | 1,655.01 -                               | 1,655.01                        | 1,290.00                              | 08/2016 -                             | 03/2018     | 19                       | 0                   |                                                                     |
| 256                            | FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA             | 04/2010                          | 1,170.52 -                               | 1,170.52                        | -                                     | 06/2012 -                             | 03/2018     | 69                       | 0                   |                                                                     |
| 257                            | WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA) - [N24000527]PWD, ODISHA | 12/2011                          | 191.08 -                                 | 191.08                          | -                                     | 08/2015 -                             | 03/2018     | 31                       | 0                   |                                                                     |
| 258                            | VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE                                                         | 09/2011                          | 2,848.00 -                               | 2,848.00                        | -                                     | 03/2014 -                             | 04/2018     | 49                       | 0                   |                                                                     |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                                      |                               |                                    |                              |                                    | (September 2017)                   |             |                       |                  |                                                                  |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------|------------------|------------------------------------------------------------------|
|                                |                                                                                                                                      |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                       |                  | Reasons for Delay (As Reported by Project Implementing Agencies) |
| S.No                           | Project                                                                                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Time Overrun (Months) | Cost Overrun (%) |                                                                  |
| 1                              | 2                                                                                                                                    | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                     | 10               | 11                                                               |
| 259                            | 2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN                                                                   | 10/2015                       | 597.00 -                           | 597.00                       | -                                  | 10/2017 -                          | 04/2018     | 6                     | 0                |                                                                  |
| 260                            | PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR                                                                                           | 08/2010                       | 671.30 -                           | 671.30                       | -                                  | 02/2013 -                          | 06/2018     | 64                    | 0                |                                                                  |
| 261                            | TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU                                                          | 06/2015                       | 563.92 -                           | 563.92                       | 95.89                              | 12/2017 -                          | 06/2018     | 6                     | 0                |                                                                  |
| 262                            | FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH                                                                       | 05/2015                       | 261.09 -                           | 261.09                       | 58.72                              | 05/2017 -                          | 06/2018     | 13                    | 0                |                                                                  |
| 263                            | THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU                                                                | 11/2014                       | 563.92 -                           | 563.92                       | 186.50                             | 11/2016 -                          | 06/2018     | 19                    | 0                |                                                                  |
| 264                            | 4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA                                                                  | 12/2015                       | 602.95 -                           | 602.95                       | 261.78                             | 06/2016 -                          | 06/2018     | 24                    | 0                |                                                                  |
| 265                            | 4-LANING OF GHAGHRA BRIDGE TO VARANSI ( PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH                                                  | 12/2015                       | 611.65 -                           | 611.65                       | 225.07                             | 06/2016 -                          | 06/2018     | 24                    | 0                |                                                                  |
| 266                            | FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU    | 03/2016                       | 641.17 -                           | 641.17                       | 64.90                              | 07/2016 -                          | 07/2018     | 24                    | 0                |                                                                  |
| 267                            | WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA       | 06/2016                       | 157.30<br>157.00                   | 157.00                       | -                                  | 06/2018 -                          | 11/2018     | 5                     | -19              |                                                                  |
| 268                            | QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR                                                         | 07/2010                       | 1,987.00 -                         | 1,987.00                     | -                                  | 07/2015 -                          | 03/2019     | 44                    | 0                |                                                                  |
| 269                            | FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH | 06/2015                       | 1,012.90 -                         | 1,012.90                     | 588.26                             | 03/2016 -                          | 03/2019     | 36                    | 0                |                                                                  |
| 270                            | FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB                                                                          | 10/2015                       | 447.29 -                           | 447.29                       | 48.82                              | 12/2017 -                          | 04/2019     | 16                    | 0                |                                                                  |
| 271                            | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND    | 03/2016                       | 373.07 -                           | 373.07                       | -                                  | 08/2016 -                          | 08/2019     | 36                    | 0                |                                                                  |



## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                                               |                                  |                                       |                                 |                                       | (September 2017)                      |             |                          |                     |                                                                     |
|--------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------|---------------------------------------|---------------------------------|---------------------------------------|---------------------------------------|-------------|--------------------------|---------------------|---------------------------------------------------------------------|
|                                |                                                                                                                                               |                                  |                                       |                                 |                                       | Date of Commissioning<br>(Month/Year) |             |                          |                     | Reasons for Delay<br>(As Reported by Project Implementing Agencies) |
| S.No                           | Project                                                                                                                                       | Date of Approval<br>(Month/Year) | Original/ Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs. crore) | Cumulative Expenditure<br>(Rs. crore) | Original / Revised                    | Anticipated | Time Overrun<br>(Months) | Cost Overrun<br>(%) |                                                                     |
| 1                              | 2                                                                                                                                             | 3                                | 4                                     | 5                               | 6                                     | 7                                     | 8           | 9                        | 10                  | 11                                                                  |
| 272                            | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND             | 03/2016                          | 396.52 -                              | 396.52                          | -                                     | 08/2016 -                             | 08/2019     | 36                       | 0                   |                                                                     |
| 273                            | FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND             | 03/2016                          | 429.52 -                              | 429.52                          | -                                     | 08/2016 -                             | 08/2019     | 36                       | 0                   |                                                                     |
| 274                            | CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH                                   | 12/2016                          | 138.93<br>155.00                      | 155.00                          | -                                     | 01/2017 -                             | 01/2020     | 36                       | 11.57               |                                                                     |
|                                | Total                                                                                                                                         |                                  | 64,849.16 -                           | 68,524.01                       | 55,276.17                             |                                       |             |                          |                     |                                                                     |
|                                |                                                                                                                                               |                                  |                                       |                                 |                                       |                                       |             |                          |                     |                                                                     |
|                                | <u>SHIPPING AND PORTS</u>                                                                                                                     |                                  |                                       |                                 |                                       |                                       |             |                          |                     |                                                                     |
| 275                            | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU                                                | 10/2002                          | 150.00 -                              | 600.00                          | 139.80                                | 03/2006 -                             | 12/2017     | 141                      | 300                 |                                                                     |
| 276                            | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA | 01/2007                          | 366.39 -                              | 669.46                          | 411.12                                | 12/2010 -                             | 12/2018     | 96                       | 82.72               |                                                                     |
|                                | Total                                                                                                                                         |                                  | 516.39 -                              | 1,269.46                        | 550.92                                |                                       |             |                          |                     |                                                                     |
|                                |                                                                                                                                               |                                  |                                       |                                 |                                       |                                       |             |                          |                     |                                                                     |
|                                | <u>TELECOMMUNICATIONS</u>                                                                                                                     |                                  |                                       |                                 |                                       |                                       |             |                          |                     |                                                                     |
| 277                            | NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE                                                                                             | 03/2012                          | 13,334.00 -                           | 24,664.00                       | 6,660.00                              | 07/2015 -                             | 06/2019     | 47                       | 84.97               |                                                                     |
|                                | Total                                                                                                                                         |                                  | 13,334.00 -                           | 24,664.00                       | 6,660.00                              |                                       |             |                          |                     |                                                                     |
|                                |                                                                                                                                               |                                  |                                       |                                 |                                       |                                       |             |                          |                     |                                                                     |
|                                | <u>URBAN DEVELOPMENT</u>                                                                                                                      |                                  |                                       |                                 |                                       |                                       |             |                          |                     |                                                                     |
| 278                            | CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA                                     | 12/2012                          | 315.00 -                              | 315.00                          | 302.82                                | 06/2015 -                             | 09/2017     | 27                       | 0                   |                                                                     |
| 279                            | STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU                                                                    | 04/2014                          | 332.72 -                              | 332.72                          | 260.88                                | 09/2016 -                             | 11/2017     | 14                       | 0                   |                                                                     |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                                      |                                  |                                       |                                 |                                       | (September 2017)                      |             |                          |                     |                                                                     |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|----------------------------------|---------------------------------------|---------------------------------|---------------------------------------|---------------------------------------|-------------|--------------------------|---------------------|---------------------------------------------------------------------|
|                                |                                                                                                                                      |                                  |                                       |                                 |                                       | Date of Commissioning<br>(Month/Year) |             |                          |                     | Reasons for Delay<br>(As Reported by Project Implementing Agencies) |
| S.No                           | Project                                                                                                                              | Date of Approval<br>(Month/Year) | Original/ Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs. crore) | Cumulative Expenditure<br>(Rs. crore) | Original / Revised                    | Anticipated | Time Overrun<br>(Months) | Cost Overrun<br>(%) |                                                                     |
| 1                              | 2                                                                                                                                    | 3                                | 4                                     | 5                               | 6                                     | 7                                     | 8           | 9                        | 10                  | 11                                                                  |
| 280                            | CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH                                   | 12/2012                          | 188.87 -                              | 188.87                          | 168.98                                | 12/2015<br>12/2017                    | 12/2017     | 24                       | 0                   |                                                                     |
| 281                            | CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU                                                                        | 02/2009                          | 14,600.00<br>19,058.00                | 19,058.00                       | 14,784.59                             | 12/2015<br>-                          | 12/2017     | 24                       | 30.53               |                                                                     |
| 282                            | CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD,KERALA             | 07/2015                          | 154.00 -                              | 154.00                          | 66.56                                 | 11/2015<br>-                          | 12/2017     | 25                       | 0                   |                                                                     |
| 283                            | CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB                            | 02/2014                          | 388.00 -                              | 388.00                          | 277.96                                | 05/2017<br>02/2018                    | 02/2018     | 9                        | 0                   |                                                                     |
| 284                            | CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL                         | 02/2014                          | 156.57 -                              | 156.57                          | 119.09                                | 08/2016<br>-                          | 03/2018     | 19                       | 0                   |                                                                     |
| 285                            | OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA                           | 02/2011                          | 241.33<br>349.33                      | 349.33                          | 221.30                                | 03/2016<br>12/2017                    | 03/2018     | 24                       | 44.75               |                                                                     |
| 286                            | UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA                                    | 06/2010                          | 205.00<br>166.97                      | 170.62                          | 146.41                                | 03/2012<br>-                          | 03/2018     | 72                       | -16.77              |                                                                     |
| 287                            | CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA                                                       | 01/2010                          | 165.23 -                              | 165.23                          | 25.91                                 | 10/2012<br>04/2017                    | 03/2018     | 65                       | 0                   |                                                                     |
| 288                            | CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI           | 07/2012                          | 884.30 -                              | 884.30                          | 503.45                                | 12/2015<br>12/2017                    | 03/2018     | 27                       | 0                   |                                                                     |
| 289                            | CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]CPWD,MADHYA PRADESH | 12/2016                          | 164.00 -                              | 164.00                          | 68.10                                 | 01/2018<br>03/2018                    | 03/2018     | 2                        | 0                   |                                                                     |

## Details of Delayed Projects w.r.t. Original Schedule

| Costing Rs.150 Crore and above |                                                                                                                                   |                                  |                                       |                                 |                                       | (September 2017)                      |             |                          |                     |                                                                     |
|--------------------------------|-----------------------------------------------------------------------------------------------------------------------------------|----------------------------------|---------------------------------------|---------------------------------|---------------------------------------|---------------------------------------|-------------|--------------------------|---------------------|---------------------------------------------------------------------|
|                                |                                                                                                                                   |                                  |                                       |                                 |                                       | Date of Commissioning<br>(Month/Year) |             |                          |                     | Reasons for Delay<br>(As Reported by Project Implementing Agencies) |
| S.No                           | Project                                                                                                                           | Date of Approval<br>(Month/Year) | Original/ Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs. crore) | Cumulative Expenditure<br>(Rs. crore) | Original / Revised                    | Anticipated | Time Overrun<br>(Months) | Cost Overrun<br>(%) |                                                                     |
| 1                              | 2                                                                                                                                 | 3                                | 4                                     | 5                               | 6                                     | 7                                     | 8           | 9                        | 10                  | 11                                                                  |
| 290                            | DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH                                | 11/2012                          | 270.83 -                              | 270.83                          | 116.57                                | 11/2014 -                             | 10/2018     | 47                       | 0                   |                                                                     |
| 291                            | NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR                                                                 | 02/2014                          | 216.69 -                              | 216.69                          | 52.00                                 | 03/2015 -                             | 11/2018     | 44                       | 0                   |                                                                     |
| 292                            | 2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND                                              | 09/2012                          | 171.86 -                              | 171.86                          | 38.40                                 | 03/2016 -                             | 12/2018     | 33                       | 0                   |                                                                     |
| 293                            | CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND | 12/2008                          | 114.26<br>266.00                      | 266.00                          | -                                     | 12/2013 -                             | 10/2019     | 70                       | 132.8               |                                                                     |
| 294                            | KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA                                                                                | 07/2012                          | 5,181.79 -                            | 5,181.79                        | -                                     | 07/2017 -                             | 12/2019     | 29                       | 0                   |                                                                     |
| 295                            | NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA                                                                                  | 08/2014                          | 8,680.00 -                            | 8,680.00                        | 1,688.81                              | 03/2018 -                             | 12/2019     | 21                       | 0                   |                                                                     |
| 296                            | BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA                                                                 | 02/2014                          | 26,405.14 -                           | 26,405.14                       | 2,391.46                              | 02/2019 -                             | 03/2020     | 13                       | 0                   | land acquisition                                                    |
| 297                            | ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI           | 10/2013                          | 1,219.21<br>2,230.23                  | 1,592.00                        | 122.50                                | 10/2019 -                             | 03/2020     | 5                        | 30.58               |                                                                     |
|                                | Total                                                                                                                             |                                  | 60,054.80 -                           | 65,110.95                       | 21,355.79                             |                                       |             |                          |                     |                                                                     |
|                                |                                                                                                                                   |                                  |                                       |                                 |                                       |                                       |             |                          |                     |                                                                     |
|                                | Grand Total                                                                                                                       |                                  | 5,39,754.44                           | 6,75,032.54                     | 4,16,614.31                           |                                       |             |                          |                     |                                                                     |

# Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

| (September 2017) |                                                                                             |                               |                                     |                             |                                    |             |                   |                     |
|------------------|---------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|-----------------------------|------------------------------------|-------------|-------------------|---------------------|
|                  |                                                                                             |                               |                                     |                             | Date of Commissioning (Month/Year) |             |                   |                     |
| Sl.No            | Project                                                                                     | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised                 | Anticipated | Cost Overruns (%) | T.O.R.s (in months) |
| 1                | 2                                                                                           | 3                             | 4                                   | 5                           | 6                                  | 7           | 8                 | 9                   |
|                  |                                                                                             |                               |                                     |                             |                                    |             |                   |                     |
|                  | <u>ATOMIC ENERGY</u>                                                                        |                               |                                     |                             |                                    |             |                   |                     |
| 1                | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)<br>- [020100044]                          | 09/2003                       | 3,492.00<br>-                       | 6,000.00                    | 09/2010<br>-                       | 02/2018     | 71.82             | 89                  |
|                  | Total                                                                                       |                               | 3,492.00<br>-                       | 6,000.00                    |                                    |             |                   |                     |
|                  |                                                                                             |                               |                                     |                             |                                    |             |                   |                     |
|                  | <u>CIVIL AVIATION</u>                                                                       |                               |                                     |                             |                                    |             |                   |                     |
| 2                | CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT<br>- [N04000050]                     | 01/2009                       | 309.46<br>-                         | 553.53                      | 01/2011<br>-                       | 09/2017     | 78.87             | 80                  |
| 3                | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR<br>- [N04000073] | 10/2013                       | 314.61<br>-                         | 441.33                      | 09/2018<br>-                       | 06/2020     | 40.28             | 21                  |
|                  | Total                                                                                       |                               | 624.07<br>-                         | 994.86                      |                                    |             |                   |                     |
|                  |                                                                                             |                               |                                     |                             |                                    |             |                   |                     |
|                  | <u>COAL</u>                                                                                 |                               |                                     |                             |                                    |             |                   |                     |
| 4                | JAGANNATHPOR OCP(3.00MTY)<br>- [N06000075]                                                  | 09/2008                       | 152.43<br>-                         | 459.49                      | 03/2015<br>-                       | 03/2020     | 201.44            | 60                  |
| 5                | RCE OF INDARAM OCP(1.20 MTPA)<br>- [N06000093]                                              | 07/2011                       | 162.76<br>-                         | 349.28                      | 03/2015<br>-                       | 03/2020     | 114.60            | 60                  |
| 6                | SHANTIKHANI LONGWALL PROJ-SCCL<br>- [N06000017]                                             | 10/2006                       | 249.03<br>-                         | 448.86                      | 03/2012<br>-                       | 03/2019     | 80.24             | 84                  |
| 7                | NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI<br>[N06000033]                       | 10/2007                       | 259.40<br>-                         | 486.57                      | 03/2012<br>-                       | 03/2018     | 87.58             | 72                  |
| 8                | RAMAGUNDAM OC-II EXTENSION<br>- [N06000078]                                                 | 12/2009                       | 418.97<br>-                         | 489.62                      | 03/2012<br>-                       | 03/2023     | 16.86             | 132                 |
|                  | Total                                                                                       |                               | 1,242.59<br>-                       | 2,233.82                    |                                    |             |                   |                     |
|                  |                                                                                             |                               |                                     |                             |                                    |             |                   |                     |
|                  | <u>FERTILISERS</u>                                                                          |                               |                                     |                             |                                    |             |                   |                     |
| 9                | NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY<br>[N08000009]                              | 10/2014                       | 197.79<br>-                         | 209.44                      | 11/2016<br>-                       | 04/2019     | 5.89              | 29                  |
|                  | Total                                                                                       |                               | 197.79<br>-                         | 209.44                      |                                    |             |                   |                     |
|                  |                                                                                             |                               |                                     |                             |                                    |             |                   |                     |
|                  | <u>HEAVY INDUSTRY</u>                                                                       |                               |                                     |                             |                                    |             |                   |                     |
| 10               | NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIPI)<br>- [N20000001]        | 04/2011                       | 1,718.00<br>-                       | 3,827.30                    | 09/2011<br>-                       | 12/2017     | 122.78            | 75                  |
|                  | Total                                                                                       |                               | 1,718.00<br>-                       | 3,827.30                    |                                    |             |                   |                     |

## Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2017)

|       |                                                                                                     |                               |                                     |                             | Date of Commissioning (Month/Year) |             |                   |                     |
|-------|-----------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|-----------------------------|------------------------------------|-------------|-------------------|---------------------|
| Sl.No | Project                                                                                             | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised                 | Anticipated | Cost Overruns (%) | T.O.R.s (in months) |
| 1     | 2                                                                                                   | 3                             | 4                                   | 5                           | 6                                  | 7           | 8                 | 9                   |
|       |                                                                                                     |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>PETROLEUM</u>                                                                                    |                               |                                     |                             |                                    |             |                   |                     |
| 11    | RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217              | 06/2012                       | 150.00 -                            | 259.93                      | 07/2014 -                          | 09/2017     | 73.29             | 38                  |
| 12    | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127                 | 06/2010                       | 202.94 -                            | 330.35                      | 01/2014 -                          | 11/2019     | 62.78             | 70                  |
| 13    | URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155                                                     | 12/2009                       | 309.81 -                            | 723.40                      | 10/2014 -                          | 03/2018     | 133.50            | 41                  |
| 14    | SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167 | 07/2011                       | 352.56 -                            | 439.03                      | 03/2017 -                          | 11/2018     | 24.53             | 20                  |
| 15    | LPG TERMINAL AT KOCHI - [N16000171                                                                  | 10/2015                       | 607.06 -                            | 714.25                      | 10/2017 -                          | 03/2019     | 17.66             | 17                  |
| 16    | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128                | 03/2011                       | 861.79 -                            | 1,256.72                    | 05/2013 -                          | 12/2017     | 45.83             | 55                  |
| 17    | UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148 | 09/2012                       | 871.35 -                            | 1,200.00                    | 03/2015 -                          | 11/2017     | 37.72             | 32                  |
| 18    | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169                                           | 01/2006                       | 993.00 -                            | 1,693.00                    | 01/2012 -                          | 10/2017     | 70.49             | 69                  |
| 19    | INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131                                                 | 12/2011                       | 2,059.63 -                          | 2,665.65                    | 03/2015 -                          | 03/2018     | 29.42             | 36                  |
| 20    | DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175                        | 03/2014                       | 3,076.00 -                          | 4,190.00                    | 09/2017 -                          | 06/2018     | 36.22             | 9                   |
| 21    | INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172                                      | 05/2013                       | 4,124.35 -                          | 5,637.00                    | 04/2016 -                          | 12/2017     | 36.68             | 20                  |
| 22    | MH NORTH REDEVELOPMENT PHASE III - [N16000188                                                       | 06/2014                       | 5,706.47 -                          | 5,813.25                    | 05/2017 -                          | 05/2018     | 1.87              | 12                  |
|       | Total                                                                                               |                               | 19,314.96 -                         | 24,922.58                   |                                    |             |                   |                     |
|       |                                                                                                     |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>POWER</u>                                                                                        |                               |                                     |                             |                                    |             |                   |                     |
| 23    | AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165                               | 03/2014                       | 155.57 -                            | 206.42                      | 03/2016 -                          | 12/2017     | 32.69             | 21                  |
| 24    | DHUKWAN SMALL HYDRO PROJECT - [N18000189                                                            | 05/2011                       | 195.42 -                            | 294.60                      | 02/2014 -                          | 12/2018     | 50.75             | 58                  |
| 25    | EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171                                                | 02/2014                       | 196.58 -                            | 225.28                      | 02/2016 -                          | 12/2017     | 14.60             | 22                  |
| 26    | SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182                                        | 01/2015                       | 203.28 -                            | 260.03                      | 07/2017 -                          | 12/2017     | 27.92             | 5                   |
| 27    | SYSTEM STRENGTHENING XII OF SR - [N18000085                                                         | 02/2010                       | 232.34 -                            | 245.00                      | 06/2012 -                          | 12/2017     | 5.45              | 66                  |

## Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2017)

|       |                                                                                                                    |                               |                                     |                             | Date of Commissioning (Month/Year) |             |                   |                     |
|-------|--------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|-----------------------------|------------------------------------|-------------|-------------------|---------------------|
| Sl.No | Project                                                                                                            | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised                 | Anticipated | Cost Overruns (%) | T.O.R.s (in months) |
| 1     | 2                                                                                                                  | 3                             | 4                                   | 5                           | 6                                  | 7           | 8                 | 9                   |
| 28    | SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID<br>- [N18000169]                                               | 08/2014                       | 288.49<br>-                         | 376.09                      | 02/2017<br>-                       | 03/2018     | 30.37             | 13                  |
| 29    | SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV<br>- [N18000115]                                                     | 12/2011                       | 297.33<br>-                         | 426.29                      | 08/2014<br>-                       | 12/2017     | 43.37             | 40                  |
| 30    | TUIRIAL HYDRO ELECTRIC PROJECT (60MW)<br>- [N18000119]                                                             | 07/1998                       | 368.72<br>-                         | 1,329.43                    | 07/2006<br>02/2015                 | 11/2017     | 260.55            | 136                 |
| 31    | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT<br>- [N18000194]                                  | 05/2015                       | 436.68<br>-                         | 602.44                      | 12/2016<br>-                       | 12/2017     | 37.96             | 12                  |
| 32    | WESTERN REGION STRENGTHENING SCHEME-V<br>- [N18000035]                                                             | 12/2007                       | 477.69<br>-                         | 738.48                      | 09/2010<br>-                       | 03/2018     | 54.59             | 90                  |
| 33    | SYSTEM STRENGTHENING XIII OF SR GRID<br>- [N18000109]                                                              | 10/2011                       | 487.49<br>-                         | 639.46                      | 06/2014<br>-                       | 06/2018     | 31.17             | 48                  |
| 34    | COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C<br>- [N18000143] | 03/2013                       | 514.20<br>-                         | 703.10                      | 06/2015<br>-                       | 03/2018     | 36.74             | 33                  |
| 35    | EASTERN REGION STRENGTHENING SCHEME-XII<br>- [N18000164]                                                           | 05/2014                       | 522.29<br>-                         | 550.18                      | 11/2016<br>-                       | 03/2018     | 5.34              | 16                  |
| 36    | PARE HYDRO ELECTRIC PROJECT<br>- [N18000045]                                                                       | 12/2008                       | 573.99<br>-                         | 1,337.76                    | 08/2013<br>-                       | 03/2018     | 133.06            | 55                  |
| 37    | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV<br>- [N18000128]                                                  | 11/2011                       | 723.63<br>-                         | 882.13                      | 11/2014<br>-                       | 12/2017     | 21.90             | 37                  |
| 38    | NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII<br>- [N18000159]                                               | 02/2014                       | 908.08<br>-                         | 969.97                      | 06/2016<br>-                       | 11/2017     | 6.82              | 17                  |
| 39    | TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A<br>- [N18000253]                | 03/2015                       | 955.00<br>-                         | 1,364.00                    | 12/2015<br>-                       | 03/2018     | 42.83             | 27                  |
| 40    | TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM CUDDALORE AREA - PACKAGE A<br>- [N18000259]               | 03/2015                       | 955.00<br>1,161.00                  | 1,364.00                    | 12/2015<br>-                       | 03/2018     | 42.83             | 27                  |
| 41    | EASTERN REGION STRENGTHENING SCHEME-III<br>- [N18000100]                                                           | 07/2010                       | 1,272.80<br>-                       | 1,731.10                    | 11/2012<br>-                       | 12/2017     | 36.01             | 61                  |
| 42    | EASTERN REGION STRENGTHENING SCHEME-V<br>- [N18000155]                                                             | 10/2013                       | 1,364.52<br>-                       | 1,891.41                    | 04/2016<br>-                       | 03/2018     | 38.61             | 23                  |
| 43    | TEHRI PUMPED STORAGE PLANT(1000MW)<br>- [N18000010]                                                                | 07/2006                       | 1,657.00<br>-                       | 3,939.11                    | 02/2016<br>-                       | 12/2020     | 137.73            | 58                  |
| 44    | SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH<br>- [N18000116]                 | 12/2011                       | 1,746.65<br>-                       | 2,228.71                    | 08/2014<br>-                       | 12/2017     | 27.60             | 40                  |
| 45    | KUNADANKULAM APP TRANS SYSTEM (PGCIL)<br>- [180100258]                                                             | 05/2005                       | 1,779.29<br>-                       | 2,187.32                    | 11/2008<br>-                       | 09/2018     | 22.93             | 118                 |
| 46    | TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT<br>- [N18000215]        | 01/2014                       | 1,788.41<br>-                       | 2,352.57                    | 09/2017<br>-                       | 09/2018     | 31.55             | 12                  |
| 47    | COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103] | 09/2011                       | 1,940.13<br>-                       | 2,702.65                    | 09/2014<br>-                       | 12/2017     | 39.30             | 39                  |

## Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2017)

|       |                                                                                                                   |                               |                                     |                             | Date of Commissioning (Month/Year) |             |                   |                     |
|-------|-------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|-----------------------------|------------------------------------|-------------|-------------------|---------------------|
| Sl.No | Project                                                                                                           | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised                 | Anticipated | Cost Overruns (%) | T.O.R.s (in months) |
| 1     | 2                                                                                                                 | 3                             | 4                                   | 5                           | 6                                  | 7           | 8                 | 9                   |
| 48    | TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.<br>- [N18000080]                                     | 02/2010                       | 2,144.00<br>-                       | 2,932.88                    | 12/2012<br>-                       | 02/2018     | 36.79             | 62                  |
| 49    | KAMENG HYDROELECTRIC PROJECT (NEEPCO)<br>- [180100239]                                                            | 12/2004                       | 2,496.90<br>-                       | 6,179.96                    | 12/2009<br>06/2016                 | 03/2018     | 147.51            | 99                  |
| 50    | TAPOVAN-VISHNUGAD HEP (4X130MW)<br>- [N18000014]                                                                  | 11/2006                       | 2,978.48<br>-                       | 3,846.30                    | 03/2013<br>-                       | 06/2019     | 29.14             | 75                  |
| 51    | KISHANGANGA HEP (3X110 MW)<br>- [N18000031]                                                                       | 01/2009                       | 3,642.04<br>-                       | 5,882.01                    | 01/2016<br>-                       | 02/2018     | 61.50             | 25                  |
| 52    | PARBATI HEP (4X200 MW) (NHPC) II<br>- [180100210]                                                                 | 09/2002                       | 3,919.59<br>-                       | 8,398.75                    | 09/2009<br>-                       | 12/2018     | 114.28            | 111                 |
| 53    | BONGAIGAON THERMAL POWER PROJECT<br>- [N18000041]                                                                 | 01/2008                       | 4,375.35<br>-                       | 6,749.18                    | 09/2011<br>-                       | 12/2017     | 54.25             | 75                  |
| 54    | TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077] | 04/2010                       | 4,404.57<br>-                       | 5,135.01                    | 01/2015<br>-                       | 03/2018     | 16.58             | 38                  |
| 55    | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT<br>- [N18000061]                                       | 10/2008                       | 4,824.12<br>-                       | 5,071.94                    | 10/2012<br>-                       | 02/2018     | 5.14              | 64                  |
| 56    | BRBCL-NABINAGAR TPP- JV (4X250 MW)<br>- [N18000190]                                                               | 01/2007                       | 5,353.00<br>-                       | 7,998.00                    | 05/2014<br>-                       | 06/2018     | 49.41             | 49                  |
| 57    | BARH STPP(3X660MW) NTPC<br>- [180100242]                                                                          | 02/2005                       | 8,692.97<br>-                       | 15,095.67                   | 01/2011<br>-                       | 03/2019     | 73.65             | 98                  |
| 58    | NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT<br>- [N18000066]                                               | 02/2009                       | 11,130.19<br>-                      | 13,762.80                   | 08/2013<br>-                       | 12/2017     | 23.65             | 52                  |
| 59    | NPCCPL-NABINAGAR STPP - JV (3X660 MW)<br>- [N18000192]                                                            | 01/2013                       | 12,964.60<br>-                      | 13,731.26                   | 01/2018<br>-                       | 12/2018     | 5.91              | 11                  |
|       | Total                                                                                                             |                               | 86,966.39<br>-                      | 1,24,331.29                 |                                    |             |                   |                     |
|       |                                                                                                                   |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>RAILWAYS</u>                                                                                                   |                               |                                     |                             |                                    |             |                   |                     |
| 60    | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)<br>- [220100327]                                                        | 04/2000                       | 133.41<br>207.00                    | 340.00                      | 03/2009<br>03/2009                 | 12/2017     | 154.85            | 105                 |
| 61    | NANDYAL-YERRAGUNTLA(NL),SCR<br>- [220100192]                                                                      | 03/1996                       | 155.74<br>164.36                    | 966.98                      | 02/2009<br>-                       | 12/2017     | 520.89            | 106                 |
| 62    | SUKINDA ROAD - ANGUL (NL)(ECOR)<br>- [220100325]                                                                  | 04/1998                       | 183.23<br>-                         | 1,202.70                    | 02/2015<br>-                       | 12/2019     | 556.39            | 58                  |
| 63    | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)<br>- [220100232]                                                           | 09/1998                       | 247.66<br>-                         | 6,093.31                    | 05/2008<br>-                       | 03/2023     | 2,360.35          | 178                 |
| 64    | GOELKERA-MANOHARPUR,(LD)(SER)<br>- [N22000045]                                                                    | 03/1997                       | 261.70<br>-                         | 388.00                      | 02/2006<br>-                       | 12/2019     | 48.26             | 166                 |
| 65    | BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)<br>- [N22000123]                                         | 04/2008                       | 318.24<br>-                         | 321.62                      | 03/2012<br>-                       | 03/2019     | 1.06              | 84                  |
| 66    | SALKA ROAD -ANUPNAGAR LINE DOUBLING<br>- [N22000075]                                                              | 09/2006                       | 324.90<br>-                         | 516.40                      | 03/2010<br>-                       | 12/2017     | 58.94             | 93                  |
| 67    | GONDIA-JABALPUR(GC),(SECR)<br>- [220100186]                                                                       | 02/1997                       | 386.30<br>-                         | 1,776.81                    | 03/1998<br>-                       | 12/2019     | 359.96            | 261                 |

## Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2017)

|       |                                                                                                             |                               |                                     |                             | Date of Commissioning (Month/Year) |             |                   |                     |
|-------|-------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|-----------------------------|------------------------------------|-------------|-------------------|---------------------|
| Sl.No | Project                                                                                                     | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised                 | Anticipated | Cost Overruns (%) | T.O.R.s (in months) |
| 1     | 2                                                                                                           | 3                             | 4                                   | 5                           | 6                                  | 7           | 8                 | 9                   |
| 68    | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [N220100164]                                            | 03/1996                       | 495.44 -                            | 1,781.98                    | 03/2004 -                          | 03/2020     | 259.68            | 192                 |
| 69    | BHAIRABI SAIRONG, NL, NEFR - [N22000100]                                                                    | 04/2008                       | 619.34 -                            | 4,600.00                    | 04/2014 -                          | 03/2020     | 642.73            | 71                  |
| 70    | DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158] | 04/2010                       | 622.41 -                            | 2,030.50                    | 02/2019 -                          | 12/2022     | 226.23            | 46                  |
| 71    | MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]                                         | 04/2012                       | 632.68 -                            | 816.55                      | 03/2016 -                          | 12/2018     | 29.06             | 33                  |
| 72    | JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]                             | 04/2008                       | 653.19 -                            | 941.04                      | 03/2014 -                          | 06/2019     | 44.07             | 63                  |
| 73    | BHOPAL BINA 3D LINE DOUBLING - [N22000077]                                                                  | 09/2007                       | 687.20 -                            | 950.00                      | 03/2010 -                          | 03/2018     | 38.24             | 96                  |
| 74    | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]                                                           | 04/2003                       | 727.56 -                            | 9,658.00                    | 03/2011 -                          | 03/2020     | 1,227.45          | 108                 |
| 75    | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]                                        | 04/2000                       | 733.00 -                            | 3,010.00                    | 12/2008 -                          | 03/2019     | 310.64            | 123                 |
| 76    | OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]                                                            | 07/2006                       | 743.00 -                            | 1,825.00                    | 03/2008<br>06/2008                 | 03/2020     | 145.63            | 144                 |
| 77    | AGARTALA SABROOM, NL, NEFR - [N22000099]                                                                    | 04/2008                       | 813.34 -                            | 3,451.00                    | 03/2014 -                          | 03/2020     | 324.30            | 72                  |
| 78    | HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]                                                  | 04/2008                       | 829.74 -                            | 1,161.64                    | 03/2015 -                          | 12/2019     | 40.00             | 57                  |
| 79    | NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]                                | 04/2006                       | 850.00 -                            | 3,000.00                    | 03/2015 -                          | 03/2020     | 252.94            | 60                  |
| 80    | MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]                                                            | 04/1995                       | 900.05 -                            | 1,125.89                    | 12/2011<br>12/2010                 | 03/2020     | 25.09             | 99                  |
| 81    | GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]                                                | 04/2011                       | 1,176.09 -                          | 3,845.60                    | 02/2020 -                          | 12/2022     | 226.98            | 34                  |
| 82    | SEVOK RANGPO, NEFR - [N22000102]                                                                            | 04/2008                       | 1,339.48 -                          | 4,084.69                    | 12/2015 -                          | 03/2020     | 204.95            | 51                  |
| 83    | BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]                                                  | 09/1997                       | 1,500.00 -                          | 5,000.00                    | 04/2008<br>12/2011                 | 06/2018     | 233.33            | 122                 |
| 84    | LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]                        | 04/1996                       | 1,676.31 -                          | 7,000.00                    | 03/2009 -                          | 03/2018     | 317.58            | 108                 |
| 85    | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]                                                           | 03/1995                       | 2,500.00 -                          | 19,565.00                   | 11/2002 -                          | 12/2018     | 682.60            | 193                 |
| 86    | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]  | 04/2010                       | 3,951.98 -                          | 4,259.48                    | 03/2016 -                          | 12/2020     | 7.78              | 57                  |
| 87    | MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]                                                       | 04/2008                       | 5,300.00 -                          | 7,986.04                    | 03/2014 -                          | 03/2019     | 50.68             | 60                  |
|       | Total                                                                                                       |                               | 28,761.99 -                         | 97,698.23                   |                                    |             |                   |                     |



## Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2017)

|       |                                                                                                                    |                               |                                     |                             | Date of Commissioning (Month/Year) |             |                   |                     |
|-------|--------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|-----------------------------|------------------------------------|-------------|-------------------|---------------------|
| Sl.No | Project                                                                                                            | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised                 | Anticipated | Cost Overruns (%) | T.O.R.s (in months) |
| 1     | 2                                                                                                                  | 3                             | 4                                   | 5                           | 6                                  | 7           | 8                 | 9                   |
|       |                                                                                                                    |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                 |                               |                                     |                             |                                    |             |                   |                     |
| 88    | CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]                                | 12/2016                       | 138.93<br>155.00                    | 155.00                      | 01/2017<br>-                       | 01/2020     | 11.57             | 36                  |
| 89    | BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]                                                                          | 12/2003                       | 217.61<br>-                         | 309.56                      | 04/2010<br>-                       | 03/2018     | 42.25             | 95                  |
| 90    | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]                                               | 12/2003                       | 280.00<br>-                         | 361.00                      | 02/2009<br>-                       | 12/2017     | 28.93             | 106                 |
| 91    | FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]                                                                      | 05/2013                       | 1,055.00<br>-                       | 1,601.77                    | 11/2015<br>-                       | 09/2017     | 51.83             | 22                  |
| 92    | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]                                                          | 05/2009                       | 1,108.00<br>-                       | 2,288.00                    | 11/2011<br>-                       | 03/2018     | 106.50            | 76                  |
| 93    | INDORE-JHABUA-GUJRAT/MP - [N24000136]                                                                              | 10/2010                       | 1,175.00<br>-                       | 1,206.10                    | 04/2013<br>-                       | 09/2017     | 2.65              | 53                  |
| 94    | GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]                                                  | 03/2010                       | 1,509.10<br>-                       | 3,237.87                    | 09/2012<br>-                       | 12/2017     | 114.56            | 63                  |
|       | Total                                                                                                              |                               | 5,483.64<br>-                       | 9,159.30                    |                                    |             |                   |                     |
|       |                                                                                                                    |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>SHIPPING AND PORTS</u>                                                                                          |                               |                                     |                             |                                    |             |                   |                     |
| 95    | ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]                                         | 10/2002                       | 150.00<br>-                         | 600.00                      | 03/2006<br>-                       | 12/2017     | 300.00            | 141                 |
| 96    | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063] | 01/2007                       | 366.39<br>-                         | 669.46                      | 12/2010<br>-                       | 12/2018     | 82.72             | 96                  |
|       | Total                                                                                                              |                               | 516.39<br>-                         | 1,269.46                    |                                    |             |                   |                     |
|       |                                                                                                                    |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>STEEL</u>                                                                                                       |                               |                                     |                             |                                    |             |                   |                     |
| 97    | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]                                      | 12/2007                       | 202.61<br>227.00                    | 227.00                      | 12/2016<br>-                       | 12/2017     | 12.04             | 12                  |
| 98    | REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]                                                               | 12/2009                       | 343.00<br>-                         | 488.40                      | 10/2016<br>-                       | 03/2018     | 42.39             | 17                  |
|       | Total                                                                                                              |                               | 545.61<br>-                         | 715.40                      |                                    |             |                   |                     |
|       |                                                                                                                    |                               |                                     |                             |                                    |             |                   |                     |
|       | <u>TELECOMMUNICATIONS</u>                                                                                          |                               |                                     |                             |                                    |             |                   |                     |
| 99    | NETWORK FOR SPECTRUM - [N26000101]                                                                                 | 03/2012                       | 13,334.00<br>-                      | 24,664.00                   | 07/2015<br>-                       | 06/2019     | 84.97             | 47                  |
|       | Total                                                                                                              |                               | 13,334.00<br>-                      | 24,664.00                   |                                    |             |                   |                     |
|       |                                                                                                                    |                               |                                     |                             |                                    |             |                   |                     |

## Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2017)

|       |                                                                                                                  |                                  |                                        |                                | Date of Commissioning<br>(Month/Year) |             |                   |                     |
|-------|------------------------------------------------------------------------------------------------------------------|----------------------------------|----------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|---------------------|
| Sl.No | Project                                                                                                          | Date of Approval<br>(Month/Year) | Original / Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs.crore) | Original / Revised                    | Anticipated | Cost Overruns (%) | T.O.R.s (in months) |
| 1     | 2                                                                                                                | 3                                | 4                                      | 5                              | 6                                     | 7           | 8                 | 9                   |
|       | <u>URBAN DEVELOPMENT</u>                                                                                         |                                  |                                        |                                |                                       |             |                   |                     |
| 100   | CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101 | 12/2008                          | 114.26<br>266.00                       | 266.00                         | 12/2013<br>-                          | 10/2019     | 132.80            | 70                  |
| 101   | OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068                        | 02/2011                          | 241.33<br>-                            | 349.33                         | 03/2016<br>-                          | 03/2018     | 44.75             | 24                  |
| 102   | ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071     | 10/2013                          | 1,219.21<br>-                          | 1,592.00                       | 10/2019<br>-                          | 03/2020     | 30.58             | 5                   |
| 103   | CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084                                                                    | 02/2009                          | 14,600.00<br>-                         | 19,058.00                      | 12/2015<br>-                          | 12/2017     | 30.53             | 24                  |
|       | Total                                                                                                            |                                  | 16,174.80<br>-                         | 21,265.33                      |                                       |             |                   |                     |
|       |                                                                                                                  |                                  |                                        |                                |                                       |             |                   |                     |
|       | Grand Total                                                                                                      |                                  | 1,78,372.23                            | 3,17,291.01                    |                                       |             |                   |                     |

## Details of Projects Without Date of Commissioning

### Annexure - VIII

| Costing Rs.150 Crore and above |                                                                                                                                    |                               |                                     |                                    | (September 2017) |
|--------------------------------|------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|------------------|
|                                |                                                                                                                                    |                               |                                     | Date of Commissioning (Month/Year) |                  |
| Sl.No                          | Project                                                                                                                            | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated      |
| 1                              | 2                                                                                                                                  | 3                             | 4                                   | 5                                  | 6                |
|                                | <u>COAL</u>                                                                                                                        |                               |                                     |                                    |                  |
| 1                              | WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU                                                            | 04/2012                       | 364.75 -                            | 10/2014<br>06/2017                 | 07/2017          |
| 2                              | KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA                                                                                      | 12/2008                       | 453.63 -                            | 12/2012 -                          | -                |
| 3                              | KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND                                                                                       | 08/2011                       | 988.35 -                            | 04/2017 -                          | -                |
|                                | Total                                                                                                                              |                               | 1,806.73 -                          |                                    |                  |
|                                | <u>MINES</u>                                                                                                                       |                               |                                     |                                    |                  |
| 4                              | Implementation of 50.4 MW Wind Power Project at Jath, Sangli, Maharashtra - [N10000008]NALCO,MAHARASHTRA                           | 12/2015                       | 355.13 -                            | 11/2016 -                          | -                |
| 5                              | IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT RAJASTHAN - [N10000009]NALCO,RAJASTHAN                                               | 12/2015                       | 344.50 -                            | 11/2016 -                          | -                |
|                                | Total                                                                                                                              |                               | 699.63 -                            |                                    |                  |
|                                | <u>STEEL</u>                                                                                                                       |                               |                                     |                                    |                  |
| 6                              | DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH                                 | 04/2014                       | 188.93 -                            | 04/2015 -                          | -                |
| 7                              | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA                                           | 03/2007                       | 149.73<br>173.00                    | 12/2015 -                          | -                |
| 8                              | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA                                        | 10/2011                       | 175.49<br>206.71                    | 12/2016 -                          | -                |
| 9                              | CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA                                               | 05/2005                       | 768.88<br>1,070.97                  | 02/2014 -                          | -                |
| 10                             | CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA                                    | 07/2011                       | 324.87<br>324.87                    | 12/2015 -                          | -                |
| 11                             | CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH   | 07/2014                       | 232.00 -                            | 01/1999 -                          | -                |
| 12                             | CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL | 08/2012                       | 185.37 -                            | 03/2016 -                          | -                |
|                                | Total                                                                                                                              |                               | 2,025.27 -                          |                                    |                  |
|                                | <u>PETROLEUM</u>                                                                                                                   |                               |                                     |                                    |                  |
| 13                             | RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND                                        | 04/2011                       | 191.96 -                            | 05/2015<br>06/2017                 | 06/2017          |
| 14                             | PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE                                                                      | 08/2009                       | 1,793.00 -                          | 12/2016 -                          | -                |
| 15                             | INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL,ASSAM                                       | 02/2014                       | 163.88 -                            | 07/2016 -                          | -                |

## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                           |                               |                                     | (September 2017)                   |             |
|--------------------------------|-----------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
|                                |                                                                                                           |                               |                                     | Date of Commissioning (Month/Year) |             |
| Sl.No                          | Project                                                                                                   | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1                              | 2                                                                                                         | 3                             | 4                                   | 5                                  | 6           |
| 16                             | 50 MW 10 PERSENT WIND ENERGY POWER PROJECT - [N16000208]OIL,GUJARAT                                       | 11/2015                       | 500.00<br>-                         | 03/2017<br>-                       | -           |
| 17                             | 50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN                              | 11/2011                       | 310.00<br>-                         | 03/2013<br>-                       | -           |
| 18                             | IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU                                              | 11/2012                       | 678.00<br>-                         | 02/2017<br>-                       | -           |
|                                | Total                                                                                                     |                               | 3,636.84<br>-                       |                                    |             |
|                                |                                                                                                           |                               |                                     |                                    |             |
|                                | <u>POWER</u>                                                                                              |                               |                                     |                                    |             |
| 19                             | RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC,WEST BENGAL                                   | 04/2007                       | 4,122.00<br>8,781.30                | 02/2011<br>-                       | 03/2016     |
| 20                             | BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND                                                 | 08/2006                       | 2,313.00<br>4,138.41                | 12/2011<br>03/2016                 | 02/2017     |
| 21                             | MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA                                                          | 03/2012                       | 7,921.47<br>-                       | 09/2016<br>03/2017                 | 03/2017     |
| 22                             | LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND                           | 07/2012                       | 1,527.00<br>-                       | 08/2017<br>-                       | 08/2017     |
| 23                             | SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH                               | 09/2003                       | 6,285.33<br>-                       | 09/2010<br>-                       | -           |
| 24                             | TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA                                               | 07/2009                       | 421.01<br>1,078.31                  | 07/2013<br>-                       | -           |
| 25                             | FGUTPP, UNCHAHAIR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH                                     | 07/2013                       | 3,363.12<br>-                       | 12/2016<br>-                       | -           |
| 26                             | WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC,RAJASTHAN                  | 02/2015                       | 302.49<br>302.00                    | 02/2016<br>-                       | -           |
|                                | Total                                                                                                     |                               | 26,255.42<br>-                      |                                    |             |
|                                |                                                                                                           |                               |                                     |                                    |             |
|                                | <u>HEALTH AND FAMILY WELFARE</u>                                                                          |                               |                                     |                                    |             |
| 27                             | AIIMS-RAE BARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH                                                  | 10/2013                       | 159.50<br>-                         | 11/2013<br>06/2017                 | 06/2017     |
| 28                             | LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI                                                     | 02/2013                       | 414.11<br>-                         | 11/2013<br>-                       | -           |
| 29                             | SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI             | 09/2013                       | 444.70<br>-                         | 12/2015<br>-                       | -           |
| 30                             | SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI           | 11/2013                       | 196.70<br>-                         | 01/2016<br>-                       | -           |
| 31                             | LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM                                                             | 07/2012                       | 175.57<br>-                         | 12/2014<br>-                       | -           |
|                                | Total                                                                                                     |                               | 1,390.58<br>-                       |                                    |             |
|                                |                                                                                                           |                               |                                     |                                    |             |
|                                | <u>RAILWAYS</u>                                                                                           |                               |                                     |                                    |             |
| 32                             | LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR,ASSAM | 04/2003                       | 971.22<br>-                         | -<br>-                             | 12/2009     |
| 33                             | NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR,ASSAM                                                 | 04/2007                       | 180.09<br>-                         | -<br>-                             | 05/2011     |
| 34                             | ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE                           | 12/2006                       | 170.00<br>-                         | 03/2011<br>-                       | 10/2011     |

## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                       |                               |                                     |                                    | (September 2017) |
|--------------------------------|-------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|------------------|
|                                |                                                                                                       |                               |                                     | Date of Commissioning (Month/Year) |                  |
| Sl.No                          | Project                                                                                               | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated      |
| 1                              | 2                                                                                                     | 3                             | 4                                   | 5                                  | 6                |
| 35                             | HARMUTI-NAHARLAGUN - [N22000382]NFR,MULTI STATE                                                       | 04/2006                       | 614.54<br>-                         | -<br>-                             | 03/2014          |
| 36                             | DUDHNOI-MENDHIPATHAR - [N22000378]NFR,MULTI STATE                                                     | 04/1992                       | 315.64<br>-                         | -<br>-                             | 11/2014          |
| 37                             | RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR,ASSAM                                  | 04/2003                       | 4,300.00<br>-                       | -<br>-                             | 08/2015          |
| 38                             | CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA                                   | 04/1999                       | 895.00<br>-                         | 03/2007<br>-                       | 04/2016          |
| 39                             | KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM                                                           | 04/1998                       | 227.90<br>-                         | 12/2012<br>-                       | 05/2016          |
| 40                             | TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL, WEST BENGAL                                       | 04/2010                       | 171.02<br>-                         | 06/2013<br>-                       | 12/2016          |
| 41                             | HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA                              | 02/1997                       | 295.00<br>1,289.92                  | -<br>-                             | 01/2017          |
| 42                             | RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA                                                    | 04/1999                       | 166.16<br>-                         | 02/2009<br>02/2009                 | 06/2017          |
| 43                             | CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE                           | 03/2007                       | 243.78<br>-                         | -<br>-                             | 08/2017          |
| 44                             | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE                        | 04/1986                       | 158.77<br>274.56                    | 03/1994<br>-                       | -                |
| 45                             | PEDAPALI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA                                      | 12/1994                       | 124.43<br>-                         | -<br>-                             | -                |
| 46                             | AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA                                                   | 06/1994                       | 663.01<br>668.34                    | 06/1999<br>-                       | -                |
| 47                             | NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL | 04/1983                       | 36.80<br>274.41                     | -<br>-                             | -                |
| 48                             | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL, CHHATISGARH       | 04/1995                       | 304.00<br>-                         | 12/2012<br>-                       | -                |
| 49                             | CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE                                               | 02/1996                       | 240.00<br>-                         | -<br>-                             | -                |
| 50                             | AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA                                          | 02/1997                       | 514.68<br>-                         | -<br>-                             | -                |
| 51                             | NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE                                                  | 03/1981                       | 450.00<br>-                         | 07/2012<br>-                       | -                |
| 52                             | KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU                                                         | 02/1997                       | 155.55<br>-                         | -<br>-                             | -                |
| 53                             | HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA                                                       | 04/1997                       | 227.00<br>-                         | -<br>-                             | -                |
| 54                             | KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH                                         | 03/1997                       | 677.97<br>1,062.36                  | -<br>-                             | -                |
| 55                             | HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL                                        | 04/1974                       | 393.46<br>154.30                    | 03/2007<br>03/2007                 | -                |
| 56                             | RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND                                                   | 04/1997                       | 194.07<br>-                         | 06/2004<br>-                       | -                |
| 57                             | MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA                                                 | 07/1998                       | 125.00<br>-                         | 07/2008<br>-                       | -                |
| 58                             | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR                                      | 04/1997                       | 501.69<br>335.77                    | 03/2012<br>-                       | -                |
| 59                             | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH                             | 04/1999                       | 108.00<br>-                         | 12/2009<br>-                       | -                |

## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                                |                               |                                     | (September 2017)                   |             |
|--------------------------------|----------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
|                                |                                                                                                                |                               |                                     | Date of Commissioning (Month/Year) |             |
| Sl.No                          | Project                                                                                                        | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1                              | 2                                                                                                              | 3                             | 4                                   | 5                                  | 6           |
| 60                             | KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR                                                            | 09/2001                       | 492.98<br>-                         | 12/2010<br>-                       | -           |
| 61                             | GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA                                                              | 02/1998                       | 242.42<br>369.70                    | -<br>05/2009                       | -           |
| 62                             | KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE                                           | 04/1999                       | 744.71<br>744.71                    | -<br>-                             | -           |
| 63                             | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR                                                   | 04/1997                       | 162.87<br>-                         | -<br>-                             | -           |
| 64                             | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE                                             | 03/2002                       | 625.30<br>408.76                    | 06/2007<br>-                       | -           |
| 65                             | TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU                                             | 09/1995                       | 100.00<br>-                         | -<br>-                             | -           |
| 66                             | QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE                                    | 03/1998                       | 280.00<br>-                         | -<br>-                             | -           |
| 67                             | TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL | 03/2000                       | 1,049.69<br>-                       | 12/2006<br>-                       | -           |
| 68                             | GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE                                                        | 04/1998                       | 92.63<br>-                          | 02/2011<br>-                       | -           |
| 69                             | DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE                                                     | 04/2000                       | 607.09<br>-                         | 12/2012<br>12/2012                 | -           |
| 70                             | BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA                                                  | 04/1996                       | 138.00<br>1,382.78                  | -<br>-                             | -           |
| 71                             | JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA                                                                   | 01/2004                       | 238.56<br>-                         | 03/2012<br>-                       | -           |
| 72                             | HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR                                                  | 04/2003                       | 528.65<br>-                         | -<br>-                             | -           |
| 73                             | KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR                                                                   | 04/2002                       | 322.95<br>-                         | 03/2012<br>-                       | -           |
| 74                             | KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND                                                           | 04/2002                       | 459.91<br>-                         | -<br>-                             | -           |
| 75                             | DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR                                                           | 04/2001                       | 406.92<br>-                         | -<br>-                             | -           |
| 76                             | KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND                                                         | 04/2003                       | 142.45<br>-                         | -<br>-                             | -           |
| 77                             | ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH                                                        | 04/1997                       | 120.00<br>-                         | 12/2008<br>-                       | -           |
| 78                             | CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH                                                | 04/2005                       | 383.79<br>-                         | -<br>-                             | -           |
| 79                             | RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH                                                     | 04/2003                       | 136.62<br>-                         | 12/2007<br>03/2010                 | -           |
| 80                             | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR                                       | 04/1996                       | 332.92<br>283.95                    | 03/2012<br>-                       | -           |
| 81                             | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU                    | 09/2007                       | 404.19<br>-                         | -<br>-                             | -           |
| 82                             | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU                                   | 09/2006                       | 343.17<br>-                         | -<br>-                             | -           |
| 83                             | UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH                                             | 04/2006                       | 325.00<br>-                         | 03/2010<br>-                       | -           |
| 84                             | BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL                                                              | 04/2007                       | 1,106.62<br>-                       | 12/2010<br>-                       | -           |

## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                                                |                               |                                     |                                    | (September 2017) |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|------------------|
|                                |                                                                                                                                |                               |                                     | Date of Commissioning (Month/Year) |                  |
| Sl.No                          | Project                                                                                                                        | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated      |
| 1                              | 2                                                                                                                              | 3                             | 4                                   | 5                                  | 6                |
| 85                             | ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH                                     | 02/2008                       | 171.10<br>-                         | 03/2012<br>-                       | -                |
| 86                             | TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL                                                                  | 03/1984                       | 293.97<br>-                         | 06/2005<br>-                       | -                |
| 87                             | KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR                                                                          | 04/2008                       | 282.92<br>-                         | -<br>-                             | -                |
| 88                             | RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA                           | 04/2007                       | 482.00<br>-                         | 03/2013<br>-                       | -                |
| 89                             | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL,WEST BENGAL           | 04/2010                       | 2,397.72<br>-                       | 03/2016<br>-                       | -                |
| 90                             | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL | 04/2010                       | 2,298.42<br>-                       | 03/2014<br>-                       | -                |
| 91                             | SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN                                      | 04/2008                       | 516.23<br>-                         | 03/2014<br>-                       | -                |
| 92                             | TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND                                                                            | 04/2008                       | 167.73<br>-                         | 03/2012<br>-                       | -                |
| 93                             | DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL                                                                    | 04/2009                       | 533.38<br>-                         | 12/2011<br>-                       | -                |
| 94                             | GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL                                                                          | 04/2009                       | 611.03<br>-                         | 12/2011<br>-                       | -                |
| 95                             | PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL                                                                  | 04/2004                       | 293.74<br>-                         | 12/2010<br>-                       | -                |
| 96                             | BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL                          | 04/1999                       | 207.52<br>-                         | 12/2012<br>-                       | -                |
| 97                             | RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH                                                                  | 04/2008                       | 603.04<br>-                         | 03/2012<br>-                       | -                |
| 98                             | BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT                                     | 04/2006                       | 117.36<br>196.95                    | 03/2011<br>-                       | -                |
| 99                             | ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH                                                           | 03/2013                       | 307.00<br>-                         | -<br>-                             | -                |
| 100                            | KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH                                      | 03/2013                       | 643.00<br>-                         | -<br>-                             | -                |
| 101                            | CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE                                                                              | 04/2007                       | 1,347.26<br>-                       | -<br>-                             | -                |
| 102                            | MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT                                                                     | 04/2011                       | 439.88<br>-                         | -<br>-                             | -                |
| 103                            | VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT                                                                            | 04/2010                       | 279.40<br>-                         | -<br>-                             | -                |
| 104                            | RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE                                                                | 04/2011                       | 2,082.75<br>-                       | -<br>-                             | -                |
| 105                            | AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN                                                                      | 04/2013                       | 822.00<br>-                         | -<br>-                             | -                |
| 106                            | PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN                                                                                       | 04/2013                       | 323.00<br>-                         | -<br>-                             | -                |
| 107                            | RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN                              | 04/2010                       | 739.65<br>-                         | -<br>-                             | -                |
| 108                            | GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN                                                                  | 04/2011                       | 239.73<br>-                         | -<br>-                             | -                |

## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                         |                               |                                     | (September 2017)                   |             |
|--------------------------------|---------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
|                                |                                                                                                         |                               |                                     | Date of Commissioning (Month/Year) |             |
| Sl.No                          | Project                                                                                                 | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1                              | 2                                                                                                       | 3                             | 4                                   | 5                                  | 6           |
| 109                            | BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL                                                       | 04/2010                       | 267.37<br>-                         | -<br>-                             | -           |
| 110                            | DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE                                 | 04/2010                       | 553.63<br>-                         | -<br>-                             | -           |
| 111                            | BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL                                        | 04/2011                       | 289.64<br>-                         | -<br>-                             | -           |
| 112                            | CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA                                       | 04/2010                       | 149.90<br>-                         | 03/2015<br>-                       | -           |
| 113                            | DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND                                     | 04/2010                       | 309.44<br>-                         | 12/2015<br>-                       | -           |
| 114                            | ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR                                                            | 04/2008                       | 490.80<br>-                         | -<br>-                             | -           |
| 115                            | NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR                                                             | 04/2008                       | 620.57<br>-                         | -<br>-                             | -           |
| 116                            | GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR                                               | 04/2008                       | 445.25<br>-                         | -<br>-                             | -           |
| 117                            | GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE                                                          | 04/2008                       | 415.67<br>-                         | -<br>-                             | -           |
| 118                            | BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR                                                           | 04/2008                       | 326.20<br>-                         | -<br>-                             | -           |
| 119                            | SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR                                                        | 04/1999                       | 175.69<br>-                         | -<br>-                             | -           |
| 120                            | CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR                                                        | 04/2006                       | 285.07<br>-                         | -<br>-                             | -           |
| 121                            | DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR                                                   | 04/2005                       | 205.00<br>-                         | -<br>-                             | -           |
| 122                            | MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR                                                          | 04/2006                       | 211.00<br>-                         | -<br>-                             | -           |
| 123                            | SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR                                      | 04/2008                       | 678.62<br>-                         | -<br>-                             | -           |
| 124                            | MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR                                        | 04/2008                       | 228.05<br>-                         | -<br>-                             | -           |
| 125                            | ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR                                                               | 04/2008                       | 304.41<br>-                         | -<br>-                             | -           |
| 126                            | KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR                                                          | 04/2008                       | 192.56<br>-                         | -<br>-                             | -           |
| 127                            | MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR                                                       | 04/2008                       | 281.30<br>-                         | -<br>-                             | -           |
| 128                            | SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR           | 04/2004                       | 372.14<br>-                         | -<br>-                             | -           |
| 129                            | JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR              | 04/2009                       | 470.00<br>-                         | -<br>-                             | -           |
| 130                            | HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR                                                  | 04/2013                       | 213.01<br>-                         | -<br>-                             | -           |
| 131                            | ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU                                                            | 04/2008                       | 446.87<br>527.37                    | -<br>01/2011                       | -           |
| 132                            | CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE                                          | 04/2008                       | 523.52<br>2,350.00                  | -<br>-                             | -           |
| 133                            | SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU | 04/2013                       | 839.00<br>-                         | -<br>-                             | -           |



## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                                                  |                               |                                     | (September 2017)                   |             |
|--------------------------------|----------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
|                                |                                                                                                                                  |                               |                                     | Date of Commissioning (Month/Year) |             |
| Sl.No                          | Project                                                                                                                          | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1                              | 2                                                                                                                                | 3                             | 4                                   | 5                                  | 6           |
| 134                            | CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU                                                       | 04/1998                       | 271.24<br>-                         | -<br>-                             | -           |
| 135                            | KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE                                                                            | 04/2007                       | 270.14<br>-                         | -<br>-                             | -           |
| 136                            | KUMBALAM-TURAVUR - [N22000191]SR,KERALA                                                                                          | 04/2011                       | 252.96<br>-                         | -<br>-                             | -           |
| 137                            | NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL                                                            | 04/2010                       | 221.42<br>-                         | -<br>-                             | -           |
| 138                            | ERODE-PALANI - [N22000199]SR,TAMIL NADU                                                                                          | 04/2008                       | 288.57<br>-                         | -<br>-                             | -           |
| 139                            | MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU                                                                                | 04/2008                       | 164.41<br>-                         | -<br>-                             | -           |
| 140                            | CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA                                                                                    | 04/2006                       | 191.72<br>-                         | -<br>-                             | -           |
| 141                            | NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE                                                             | 04/2010                       | 242.22<br>-                         | -<br>-                             | -           |
| 142                            | NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE                                                              | 04/2010                       | 241.52<br>-                         | -<br>-                             | -           |
| 143                            | CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL                                            | 04/2009                       | 573.78<br>-                         | -<br>-                             | -           |
| 144                            | RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA                                                           | 04/2012                       | 714.10<br>-                         | 04/2016<br>-                       | -           |
| 145                            | MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE                                                                   | 04/2011                       | 601.43<br>-                         | -<br>-                             | -           |
| 146                            | LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE | 04/1987                       | 406.99<br>-                         | -<br>-                             | -           |
| 147                            | SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE                                                  | 04/2007                       | 450.00<br>-                         | -<br>-                             | -           |
| 148                            | HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE                                                                     | 04/2010                       | 172.03<br>-                         | -<br>-                             | -           |
| 149                            | PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE                                                                                    | 04/2013                       | 915.98<br>1,130.13                  | -<br>-                             | -           |
| 150                            | PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE                                                                             | 04/2011                       | 248.07<br>-                         | 03/2015<br>-                       | -           |
| 151                            | BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE                                                                              | 04/2011                       | 288.35<br>-                         | -<br>-                             | -           |
| 152                            | PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE                                                                                  | 04/2011                       | 261.38<br>-                         | -<br>-                             | -           |
| 153                            | KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE | 04/2001                       | 923.52<br>-                         | -<br>-                             | -           |
| 154                            | CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE                     | 04/2005                       | 595.91<br>-                         | -<br>-                             | -           |
| 155                            | KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE                      | 04/2010                       | 174.56<br>-                         | -<br>-                             | -           |
| 156                            | SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRACHAKIA NL - [N22000228]ER,MULTI STATE                                          | 04/2010                       | 277.28<br>-                         | -<br>-                             | -           |

## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                                                  |                               |                                     | (September 2017)                   |             |
|--------------------------------|----------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
|                                |                                                                                                                                  |                               |                                     | Date of Commissioning (Month/Year) |             |
| Sl.No                          | Project                                                                                                                          | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1                              | 2                                                                                                                                | 3                             | 4                                   | 5                                  | 6           |
| 157                            | DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE   | 04/2010                       | 296.44<br>-                         | -<br>-                             | -           |
| 158                            | BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE                                                 | 04/2007                       | 450.55<br>-                         | -<br>-                             | -           |
| 159                            | TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE                                                                        | 04/2010                       | 365.17<br>-                         | -<br>-                             | -           |
| 160                            | HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE                                                                                    | 04/2011                       | 267.09<br>-                         | -<br>-                             | -           |
| 161                            | SAINTIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE                                                                            | 04/2011                       | 193.44<br>-                         | -<br>-                             | -           |
| 162                            | BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE                                                                          | 04/2011                       | 175.80<br>-                         | -<br>-                             | -           |
| 163                            | PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE                                                    | 04/2011                       | 299.60<br>-                         | 03/2017<br>-                       | -           |
| 164                            | NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE | 04/2010                       | 494.54<br>-                         | -<br>-                             | -           |
| 165                            | SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE                                 | 04/2000                       | 297.47<br>-                         | -<br>-                             | -           |
| 166                            | CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE | 04/2003                       | 337.96<br>-                         | -<br>-                             | -           |
| 167                            | MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE  | 04/2009                       | 493.96<br>-                         | -<br>-                             | -           |
| 168                            | KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE                                              | 04/2010                       | 423.66<br>-                         | 03/2017<br>-                       | -           |
| 169                            | 3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA                                                                    | 04/2011                       | 184.06<br>-                         | -<br>-                             | -           |
| 170                            | SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE                                                 | 04/2010                       | 268.52<br>-                         | -<br>-                             | -           |
| 171                            | HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE         | 04/2011                       | 166.89<br>-                         | -<br>-                             | -           |
| 172                            | PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE                                                                                    | 04/2007                       | 98.74<br>-                          | -<br>-                             | -           |
| 173                            | PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE                                                                                  | 04/2006                       | 96.16<br>-                          | -<br>-                             | -           |
| 174                            | TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA                                                                       | 04/2011                       | 913.00<br>-                         | -<br>-                             | -           |
| 175                            | MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA                                                                       | 04/2007                       | 179.65<br>-                         | -<br>-                             | -           |
| 176                            | BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA                                                                                   | 04/2010                       | 377.93<br>986.30                    | -<br>-                             | -           |
| 177                            | MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA                                                                                   | 04/2013                       | 1,112.00<br>-                       | -<br>-                             | -           |
| 178                            | KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE                                                    | 04/2012                       | 1,054.35<br>-                       | -<br>-                             | -           |
| 179                            | BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE                                                                                 | 04/2012                       | 923.23<br>-                         | -<br>-                             | -           |

## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                                 |                               |                                     | (September 2017)                   |             |
|--------------------------------|-----------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
|                                |                                                                                                                 |                               |                                     | Date of Commissioning (Month/Year) |             |
| Sl.No                          | Project                                                                                                         | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1                              | 2                                                                                                               | 3                             | 4                                   | 5                                  | 6           |
| 180                            | GUDUR-DURGARA JAPATNAM - [N22000265]SCR, ANDHRA PRADESH                                                         | 04/2011                       | 283.54<br>-                         | -<br>-                             | -           |
| 181                            | MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR, UTTAR PRADESH                                                     | 04/2012                       | 377.44<br>-                         | -<br>-                             | -           |
| 182                            | MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR, PUNJAB | 04/2009                       | 396.04<br>-                         | -<br>-                             | -           |
| 183                            | GRADE SEPARATOR AT DAYABASTI - [N22000269]NR, DELHI                                                             | 04/1999                       | 156.65<br>-                         | -<br>-                             | -           |
| 184                            | FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR, UTTAR PRADESH                        | 04/2013                       | 654.00<br>-                         | -<br>-                             | -           |
| 185                            | DELHI-SOHNANUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR, MULTI STATE                                               | 04/2013                       | 1,239.00<br>-                       | -<br>-                             | -           |
| 186                            | ROHTAK-MEHAM HANSI - [N22000272]NR, HARYANA                                                                     | 04/2012                       | 287.00<br>-                         | -<br>-                             | -           |
| 187                            | BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL, HIMACHAL PRADESH                                                  | 04/2008                       | 1,046.88<br>-                       | -<br>-                             | -           |
| 188                            | DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR, MULTI STATE                                                | 04/2007                       | 336.91<br>-                         | -<br>-                             | -           |
| 189                            | CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR, KARNATAKA                                  | 04/2013                       | 558.00<br>692.43                    | -<br>-                             | -           |
| 190                            | SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR, MULTI STATE                                                     | 04/2013                       | 296.00<br>-                         | -<br>-                             | -           |
| 191                            | SHIMOGA-HARIHAR NL - [N22000278]SWR, KARNATAKA                                                                  | 04/2011                       | 562.74<br>-                         | -<br>-                             | -           |
| 192                            | RAYADURGA-TUMKUR NL - [N22000279]RVNL, MULTI STATE                                                              | 04/2007                       | 970.34<br>-                         | -<br>-                             | -           |
| 193                            | WHITE FIELD-KOLAR NL - [N22000280]SWR, KARNATAKA                                                                | 04/2011                       | 341.05<br>-                         | -<br>-                             | -           |
| 194                            | ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR, DELHI                                                | 04/2012                       | 295.68<br>-                         | -<br>-                             | -           |
| 195                            | CUMBUM-PRODDATUR - [N22000282]SCR, ANDHRA PRADESH                                                               | 04/2013                       | 829.00<br>-                         | -<br>-                             | -           |
| 196                            | NADIKUDE-SRI KALAHASTI - [N22000286]SCR, ANDHRA PRADESH                                                         | 04/2011                       | 1,313.48<br>-                       | -<br>-                             | -           |
| 197                            | BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR, MULTI STATE                                                      | 04/2010                       | 337.49<br>-                         | -<br>-                             | -           |
| 198                            | KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR, MULTI STATE                                    | 04/2008                       | 2,050.00<br>-                       | -<br>-                             | -           |
| 199                            | HARIDWAR-LAKSAR - [N22000289]NR, UTTARAKHAND                                                                    | 04/2012                       | 219.83<br>-                         | -<br>-                             | -           |
| 200                            | AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR, MULTI STATE                        | 04/2010                       | 338.54<br>-                         | -<br>-                             | -           |
| 201                            | JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR, MULTI STATE                                               | 04/2008                       | 162.96<br>-                         | -<br>-                             | -           |
| 202                            | HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR, HARYANA                                                  | 04/2013                       | 400.00<br>-                         | -<br>-                             | -           |
| 203                            | YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR, MULTI STATE                                    | 04/2013                       | 876.00<br>-                         | -<br>-                             | -           |
| 204                            | UNCHAHAH-AMETHI - [N22000294]NR, UTTAR PRADESH                                                                  | 04/2012                       | 380.00<br>-                         | -<br>-                             | -           |

## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                             |                               |                                     | (September 2017)                   |             |
|--------------------------------|---------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
|                                |                                                                                             |                               |                                     | Date of Commissioning (Month/Year) |             |
| Sl.No                          | Project                                                                                     | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1                              | 2                                                                                           | 3                             | 4                                   | 5                                  | 6           |
| 205                            | QADIAN-BEAS - [N22000295]NR,PUNJAB                                                          | 04/2011                       | 205.22<br>-                         | -<br>-                             | -           |
| 206                            | CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE                                             | 04/2007                       | 328.14<br>-                         | -<br>-                             | -           |
| 207                            | TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA                                        | 04/2011                       | 146.75<br>-                         | -<br>-                             | -           |
| 208                            | GADAG-WADI NL - [N22000299]SWR,KARNATAKA                                                    | 04/2013                       | 1,117.00<br>1,922.00                | -<br>-                             | -           |
| 209                            | CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA                                    | 04/2013                       | 327.25<br>367.77                    | -<br>-                             | -           |
| 210                            | MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE                                               | 04/2012                       | 250.93<br>-                         | -<br>-                             | -           |
| 211                            | BAZAR SAU - AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL                               | 04/2012                       | 255.64<br>-                         | -<br>-                             | -           |
| 212                            | JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE                                     | 04/2007                       | 313.24<br>-                         | 01/1999<br>-                       | -           |
| 213                            | MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE                                      | 04/2008                       | 466.48<br>-                         | 01/1999<br>-                       | -           |
| 214                            | MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA                                              | 04/2012                       | 285.57<br>279.54                    | 01/1999<br>-                       | -           |
| 215                            | MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL                                     | 04/2011                       | 276.69<br>-                         | 01/1999<br>-                       | -           |
| 216                            | JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA                                        | 03/2006                       | 201.00<br>-                         | -<br>-                             | -           |
| 217                            | DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA                                               | 03/2011                       | 165.16<br>-                         | 03/2015<br>-                       | -           |
| 218                            | GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH                                  | 04/2014                       | 182.92<br>-                         | -<br>-                             | -           |
| 219                            | RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND            | 04/2012                       | 148.77<br>-                         | 12/2016<br>-                       | -           |
| 220                            | HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA                                | 04/2010                       | 203.40<br>203.40                    | -<br>-                             | -           |
| 221                            | MIRAJ-LONDA - [N22000327]SWR,MULTI STATE                                                    | 03/2015                       | 1,830.00<br>1,190.92                | -<br>-                             | -           |
| 222                            | SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR                                                 | 05/2015                       | 380.00<br>-                         | -<br>-                             | -           |
| 223                            | AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN | 05/2015                       | 873.71<br>-                         | -<br>-                             | -           |
| 224                            | ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA                                          | 05/2015                       | 400.00<br>-                         | -<br>-                             | -           |
| 225                            | HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE                                              | 03/2015                       | 1,618.00<br>1,614.59                | -<br>-                             | -           |
| 226                            | GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH   | 04/1997                       | 836.26<br>-                         | -<br>-                             | -           |
| 227                            | DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE                            | 10/2006                       | 81,459.00<br>-                      | -<br>-                             | -           |
| 228                            | INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA                           | 02/2016                       | 9,968.00<br>-                       | -<br>-                             | -           |
| 229                            | PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA                                             | 02/2016                       | 2,425.00<br>-                       | -<br>-                             | -           |

## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                                                         |                               |                                     | (September 2017)                   |             |
|--------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
|                                |                                                                                                                                         |                               |                                     | Date of Commissioning (Month/Year) |             |
| Sl.No                          | Project                                                                                                                                 | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1                              | 2                                                                                                                                       | 3                             | 4                                   | 5                                  | 6           |
| 230                            | VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA                                                                             | 02/2016                       | 2,750.00<br>-                       | -<br>-                             | -           |
| 231                            | PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA                                                                                   | 02/2015                       | 4,670.00<br>3,627.00                | -<br>-                             | -           |
| 232                            | DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA                                                                                     | 02/2016                       | 1,876.00<br>-                       | -<br>-                             | -           |
| 233                            | MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA                                                                        | 02/2016                       | 854.00<br>-                         | -<br>-                             | -           |
| 234                            | KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA                                                                                        | 04/2013                       | 616.08<br>-                         | -<br>-                             | -           |
| 235                            | DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH                                                                                      | 04/2015                       | 3,873.07<br>-                       | -<br>-                             | -           |
| 236                            | GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH                                                                                         | 04/2016                       | 4,000.00<br>-                       | -<br>-                             | -           |
| 237                            | VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH                                                                                       | 04/2015                       | 3,246.26<br>-                       | -<br>-                             | -           |
| 238                            | GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE                                                                               | 04/2015                       | 636.38<br>-                         | -<br>-                             | -           |
| 239                            | MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]JECR,BIHAR                                                                                  | 01/1991                       | 332.15<br>-                         | 07/2014<br>-                       | -           |
| 240                            | NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL                                           | 04/2016                       | 556.31<br>-                         | -<br>-                             | -           |
| 241                            | TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA                                                                                  | 02/2015                       | 900.00<br>-                         | -<br>-                             | -           |
| 242                            | TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA                                                                                     | 02/2015                       | 1,000.00<br>-                       | -<br>-                             | -           |
| 243                            | BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL                                                  | 04/1998                       | 1,027.40<br>-                       | 03/2003<br>-                       | -           |
|                                | Total                                                                                                                                   |                               | 2,12,634.90<br>-                    |                                    |             |
|                                |                                                                                                                                         |                               |                                     |                                    |             |
|                                | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                                      |                               |                                     |                                    |             |
| 244                            | TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH | 12/2009                       | 165.00<br>-                         | 09/2010<br>-                       | 09/2010     |
| 245                            | TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH | 12/2009                       | 104.00<br>-                         | 09/2010<br>-                       | 09/2010     |
| 246                            | CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM                                    | 08/2010                       | 195.04<br>-                         | 10/2010<br>-                       | 10/2010     |
| 247                            | 2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA            | 12/2010                       | 1,494.48<br>-                       | 02/2011<br>-                       | 02/2011     |
| 248                            | 2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM               | 11/2010                       | 470.20<br>-                         | 02/2011<br>-                       | 02/2011     |
| 249                            | NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN         | 09/2012                       | 511.00<br>-                         | 10/2013<br>-                       | 10/2013     |

## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                                                      |                               |                                     |                                    | (September 2017) |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|------------------|
|                                |                                                                                                                                      |                               |                                     | Date of Commissioning (Month/Year) |                  |
| Sl.No                          | Project                                                                                                                              | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated      |
| 1                              | 2                                                                                                                                    | 3                             | 4                                   | 5                                  | 6                |
| 250                            | NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN                | 09/2012                       | 511.00<br>-                         | 10/2013<br>-                       | 10/2013          |
| 251                            | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR        | 10/2013                       | 278.39<br>-                         | 08/2014<br>-                       | 08/2014          |
| 252                            | CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA  | 03/2011                       | 185.82<br>292.22                    | -<br>11/2014                       | 11/2014          |
| 253                            | REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA    | 01/2014                       | 292.98<br>-                         | 11/2014<br>-                       | 11/2014          |
| 254                            | BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH                                                          | 11/2011                       | 670.82<br>-                         | 02/2015<br>-                       | 02/2015          |
| 255                            | REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH             | 10/2014                       | 213.47<br>-                         | 03/2015<br>-                       | 03/2015          |
| 256                            | REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 ( BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH           | 10/2014                       | 298.34<br>-                         | 03/2015<br>-                       | 03/2015          |
| 257                            | REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH    | 11/2014                       | 262.54<br>-                         | 03/2015<br>-                       | 03/2015          |
| 258                            | MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH                                                    | 01/2012                       | 381.86<br>-                         | 04/2015<br>-                       | 04/2015          |
| 259                            | BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH                                                                    | 11/2011                       | 704.26<br>-                         | 05/2015<br>-                       | 05/2015          |
| 260                            | CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU    | 11/2015                       | 154.14<br>-                         | 08/2015<br>-                       | 08/2015          |
| 261                            | WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH                                  | 05/2013                       | 164.54<br>-                         | 08/2015<br>-                       | 08/2015          |
| 262                            | FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH | 10/2015                       | 333.21<br>-                         | 11/2015<br>-                       | 11/2015          |
| 263                            | 4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM         | 01/2016                       | 294.17<br>-                         | 01/2016<br>-                       | 01/2016          |
| 264                            | 4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM         | 01/2016                       | 252.00<br>-                         | 01/2016<br>-                       | 01/2016          |
| 265                            | BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH                                                       | 03/2013                       | 257.80<br>-                         | 02/2016<br>-                       | 02/2016          |
| 266                            | CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH                   | 01/2014                       | 282.41<br>-                         | 03/2016<br>-                       | 03/2016          |
| 267                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN     | 01/1991                       | 208.87<br>223.00                    | 05/2016<br>-                       | 05/2016          |
| 268                            | REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH                                                  | 02/2015                       | 224.83<br>-                         | 04/2015<br>-                       | 05/2016          |

## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                                                            |                               |                                     | (September 2017)                   |             |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
|                                |                                                                                                                                            |                               |                                     | Date of Commissioning (Month/Year) |             |
| Sl.No                          | Project                                                                                                                                    | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1                              | 2                                                                                                                                          | 3                             | 4                                   | 5                                  | 6           |
| 269                            | REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH       | 02/2014                       | 417.61 -                            | 06/2014 -                          | 06/2016     |
| 270                            | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR              | 02/2016                       | 369.77 -                            | 06/2016 -                          | 06/2016     |
| 271                            | FUNDED ) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH | 01/2016                       | 334.22 -                            | 06/2016 -                          | 06/2016     |
| 272                            | CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA           | 08/2014                       | 187.79 -                            | 07/2016 -                          | 07/2016     |
| 273                            | REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH       | 02/2014                       | 258.99 -                            | 07/2014 -                          | 07/2016     |
| 274                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR              | 01/1991                       | 282.41 -                            | 08/2016 -                          | 08/2016     |
| 275                            | SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH                                                            | 11/2011                       | 871.15 -                            | 09/2015 -                          | 08/2016     |
| 276                            | SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH                                                                     | 01/2012                       | 320.48 -                            | 08/2015 -                          | 09/2016     |
| 277                            | STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH               | 10/2014                       | 227.74 -                            | 10/2016 -                          | 10/2016     |
| 278                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN          | 01/1991                       | 269.26 -                            | 10/2016 -                          | 10/2016     |
| 279                            | BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH                                    | 01/2014                       | 397.04 -                            | 10/2016 -                          | 10/2016     |
| 280                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR              | 01/1991                       | 358.22 -                            | 10/2016 -                          | 10/2016     |
| 281                            | JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH                | 10/2013                       | 283.45 -                            | 10/2016 -                          | 10/2016     |
| 282                            | IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA                                                                                    | 12/2013                       | 319.80 -                            | 10/2016 -                          | 10/2016     |
| 283                            | STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR              | 03/2015                       | 206.80 -                            | 07/2016 -                          | 10/2016     |
| 284                            | CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH  | 04/2016                       | 198.00 -                            | 10/2016 -                          | 10/2016     |
| 285                            | REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA                                               | 06/2014                       | 260.39 -                            | 11/2016 -                          | 11/2016     |
| 286                            | REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA                                        | 12/2013                       | 220.72 -                            | 11/2016 -                          | 11/2016     |
| 287                            | REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH        | 01/2014                       | 195.45 -                            | 11/2014 -                          | 11/2016     |

## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                                                            |                               |                                     | (September 2017)                   |             |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
|                                |                                                                                                                                            |                               |                                     | Date of Commissioning (Month/Year) |             |
| Sl.No                          | Project                                                                                                                                    | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1                              | 2                                                                                                                                          | 3                             | 4                                   | 5                                  | 6           |
| 288                            | REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH          | 02/2014                       | 170.21 -                            | 11/2014 -                          | 11/2016     |
| 289                            | 2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH | 01/2016                       | 183.65 -                            | 11/2016 -                          | 11/2016     |
| 290                            | REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA            | 10/2014                       | 244.30 -                            | 12/2016 -                          | 12/2016     |
| 291                            | FOUR LANING OF 5.122 KM OF NH9 ( NEW NH 65) FROM KM 269.900 ( DESIGN CH0.0 ) TO KM 275-622( DESIGN C - [N24000274]PWD,ANDHRA PRADESH       | 07/2015                       | 333.21 333.21                       | 12/2015 -                          | 12/2016     |
| 292                            | FOUR LANING OF 5.122 KM OF NH9( NEW NH 65) FROM KM 269.900( DESIGN CH0.0 ) - [N24000302]PWD,ANDHRA PRADESH                                 | 07/2015                       | 333.21 -                            | 12/2015 -                          | 12/2016     |
| 293                            | REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR              | 08/2016                       | 1,742.01 -                          | 12/2016 -                          | 12/2016     |
| 294                            | EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA            | 03/2015                       | 153.21 -                            | 01/2017 -                          | 01/2017     |
| 295                            | REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA               | 07/2014                       | 342.05 -                            | 01/2017 -                          | 01/2017     |
| 296                            | REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA             | 10/2014                       | 295.47 -                            | 02/2017 -                          | 02/2017     |
| 297                            | REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION ) - [N24000263]PWD,ANDHRA PRADESH           | 02/2015                       | 241.61 -                            | 02/2017 -                          | 02/2017     |
| 298                            | REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH       | 11/2014                       | 297.78 330.00                       | 02/2017 -                          | 02/2017     |
| 299                            | REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH       | 07/2014                       | 251.55 -                            | 02/2015 -                          | 02/2017     |
| 300                            | VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH                                                                            | 09/2014                       | 1,684.00 -                          | 02/2017 -                          | 02/2017     |
| 301                            | RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH                          | 10/2013                       | 445.89 -                            | 03/2017 -                          | 03/2017     |
| 302                            | 2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH         | 11/2010                       | 305.49 -                            | 03/2017 -                          | 03/2017     |
| 303                            | BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH                | 10/2013                       | 317.76 -                            | 03/2017 -                          | 03/2017     |
| 304                            | SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH                                     | 10/2013                       | 493.94 -                            | 03/2017 -                          | 03/2017     |
| 305                            | IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA              | 12/2013                       | 319.80 320.00                       | 05/2016 -                          | 03/2017     |



## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                                                 |                               |                                     | (September 2017)                   |             |
|--------------------------------|---------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
|                                |                                                                                                                                 |                               |                                     | Date of Commissioning (Month/Year) |             |
| Sl.No                          | Project                                                                                                                         | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1                              | 2                                                                                                                               | 3                             | 4                                   | 5                                  | 6           |
| 306                            | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA  | 08/2013                       | 171.96<br>172.00                    | 06/2016<br>-                       | 03/2017     |
| 307                            | WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA  | 03/2014                       | 162.51<br>163.00                    | 05/2016<br>-                       | 03/2017     |
| 308                            | IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA | 05/2014                       | 497.89<br>-                         | 04/2017<br>-                       | 04/2017     |
| 309                            | MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM                                                      | 12/2003                       | 200.00<br>-                         | 04/2009<br>-                       | 05/2017     |
| 310                            | SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM                                                                               | 12/2003                       | 245.00<br>-                         | 03/2008<br>-                       | 05/2017     |
| 311                            | DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM                                                                 | 12/2003                       | 160.00<br>-                         | 05/2008<br>-                       | 05/2017     |
| 312                            | REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH                  | 02/2015                       | 224.83<br>-                         | 05/2015<br>-                       | 05/2017     |
| 313                            | INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH              | 11/2013                       | 497.05<br>-                         | 05/2017<br>-                       | 05/2017     |
| 314                            | 2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM                   | 11/2010                       | 268.08<br>-                         | 05/2017<br>-                       | 05/2017     |
| 315                            | SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH | 06/2015                       | 532.49<br>-                         | 05/2017<br>-                       | 05/2017     |
| 316                            | JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH      | 02/2015                       | 327.32<br>-                         | 05/2017<br>-                       | 05/2017     |
| 317                            | CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU                                             | 09/2010                       | 852.00<br>-                         | 03/2013<br>-                       | 06/2017     |
| 318                            | SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH                                | 11/2011                       | 1,535.00<br>-                       | 05/2014<br>-                       | 06/2017     |
| 319                            | SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA                                                          | 12/2011                       | 1,047.00<br>-                       | 06/2014<br>-                       | 06/2017     |
| 320                            | REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA                              | 01/2014                       | 446.77<br>-                         | -<br>-                             | 06/2017     |
| 321                            | WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA  | 03/2014                       | 191.50<br>192.00                    | 05/2016<br>-                       | 06/2017     |
| 322                            | INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH                                                                             | 11/2010                       | 325.00<br>-                         | 05/2013<br>-                       | 07/2017     |
| 323                            | AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT                                                                         | 01/2013                       | 2,125.24<br>-                       | 12/2015<br>-                       | 07/2017     |
| 324                            | KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH                                | 02/2015                       | 377.83<br>-                         | 07/2017<br>-                       | 07/2017     |
| 325                            | TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 ( NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN               | 07/2015                       | 455.60<br>-                         | 07/2017<br>-                       | 07/2017     |
| 326                            | DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA                                                                       | 04/2007                       | 486.00<br>-                         | 05/2010<br>-                       | 08/2017     |

## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                                                     |                               |                                     | (September 2017)                   |             |
|--------------------------------|-------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
|                                |                                                                                                                                     |                               |                                     | Date of Commissioning (Month/Year) |             |
| Sl.No                          | Project                                                                                                                             | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1                              | 2                                                                                                                                   | 3                             | 4                                   | 5                                  | 6           |
| 327                            | ROHTAK-BAWAL - [N24000169]NHAI,HARYANA                                                                                              | 05/2011                       | 650.00<br>-                         | 11/2013<br>-                       | 08/2017     |
| 328                            | GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH                                                                             | 02/2011                       | 1,141.00<br>-                       | 08/2013<br>-                       | 08/2017     |
| 329                            | REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH | 03/2015                       | 309.01<br>-                         | 09/2015<br>-                       | 08/2017     |
| 330                            | UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH                             | 03/2015                       | 511.83<br>-                         | 08/2017<br>-                       | 08/2017     |
| 331                            | REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA       | 07/2014                       | 342.05<br>342.00                    | 01/2017<br>-                       | 08/2017     |
| 332                            | MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM                                                         | 12/2003                       | 199.81<br>-                         | 04/2009<br>-                       | -           |
| 333                            | MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM                                                   | 12/2003                       | 167.64<br>-                         | 11/2008<br>-                       | -           |
| 334                            | MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM                                                        | 12/2003                       | 155.04<br>-                         | 11/2008<br>-                       | -           |
| 335                            | HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM                                                                                 | 12/2003                       | 196.00<br>-                         | 07/2009<br>-                       | -           |
| 336                            | CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN                                                                            | 12/2003                       | 275.00<br>-                         | 02/2010<br>-                       | -           |
| 337                            | GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE                                                                                 | 12/2003                       | 604.00<br>-                         | 12/2009<br>-                       | -           |
| 338                            | TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA                                                                                     | 11/2009                       | 567.00<br>-                         | 11/2013<br>-                       | -           |
| 339                            | NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR                                                                                 | 05/2011                       | 2,159.00<br>-                       | 06/2015<br>-                       | -           |
| 340                            | DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU                          | 06/2011                       | 600.00<br>-                         | 06/2013<br>-                       | -           |
| 341                            | KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT                                                                                      | 01/2011                       | 953.88<br>-                         | 07/2013<br>-                       | -           |
| 342                            | 2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR                                                                           | 05/2011                       | 664.00<br>-                         | 02/2014<br>-                       | -           |
| 343                            | 2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR                                                                           | 10/2011                       | 375.09<br>-                         | 04/2014<br>-                       | -           |
| 344                            | PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA                                                                                           | 03/2012                       | 1,410.00<br>-                       | 09/2014<br>-                       | -           |
| 345                            | 2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHHT 170 KM) - [N24000213]NHAI,TAMIL NADU                                            | 04/2012                       | 624.00<br>-                         | 04/2014<br>-                       | -           |
| 346                            | 2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN                                                               | 03/2014                       | 240.10<br>-                         | 03/2016<br>-                       | -           |
| 347                            | REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA      | 12/2013                       | 177.18<br>-                         | 03/2016<br>-                       | -           |
| 348                            | REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPPLY SECTIO - [N24000242]PWD,TELANGANA     | 12/2013                       | 158.65<br>-                         | 03/2016<br>-                       | -           |
| 349                            | YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH - 222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA       | 12/2013                       | 244.08<br>-                         | 03/2016<br>-                       | -           |

## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                                                        |                               |                                     |                                    | (September 2017) |
|--------------------------------|----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|------------------|
|                                |                                                                                                                                        |                               |                                     | Date of Commissioning (Month/Year) |                  |
| Sl.No                          | Project                                                                                                                                | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated      |
| 1                              | 2                                                                                                                                      | 3                             | 4                                   | 5                                  | 6                |
| 350                            | REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA         | 01/2014                       | 340.00 -                            | 03/2016 -                          | -                |
| 351                            | REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA        | 01/2014                       | 270.00 -                            | 03/2016 -                          | -                |
| 352                            | CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA        | 03/2011                       | 218.31 -                            | 12/2015 -                          | -                |
| 353                            | CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66 ) FROM KM. 26 /200 ( CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA            | 03/2015                       | 298.33 -                            | - -                                | -                |
| 354                            | CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA                  | 03/2015                       | 184.05 -                            | - -                                | -                |
| 355                            | CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA            | 03/2015                       | 280.16 -                            | - -                                | -                |
| 356                            | REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH | 12/2014                       | 201.12 201.00                       | 02/2015 -                          | -                |
| 357                            | REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH    | 01/2014                       | 361.30 200.69                       | 07/2014 -                          | -                |
| 358                            | REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH   | 03/2015                       | 175.03 -                            | - -                                | -                |
| 359                            | REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH   | 02/2015                       | 266.00 -                            | - -                                | -                |
| 360                            | REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH | 07/2015                       | 314.43 -                            | - -                                | -                |
| 361                            | WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA     | 10/2015                       | 289.60 -                            | - -                                | -                |
| 362                            | CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA    | 12/2011                       | 156.26 227.31                       | - 03/2013                          | -                |
| 363                            | CONSTRUCTION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH     | 12/2010                       | 169.26 -                            | 12/2012 -                          | -                |
| 364                            | REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH              | 12/2014                       | 394.20 -                            | - -                                | -                |
| 365                            | REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH       | 11/2015                       | 485.44 -                            | 12/2015 -                          | -                |
| 366                            | REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH    | 03/2015                       | 422.34 -                            | - -                                | -                |
| 367                            | REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB           | 03/2015                       | 435.90 -                            | - -                                | -                |

## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                                                         |                               |                                     | (September 2017)                   |             |
|--------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
|                                |                                                                                                                                         |                               |                                     | Date of Commissioning (Month/Year) |             |
| Sl.No                          | Project                                                                                                                                 | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1                              | 2                                                                                                                                       | 3                             | 4                                   | 5                                  | 6           |
| 368                            | WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB            | 01/2015                       | 279.68<br>-                         | -<br>-                             | -           |
| 369                            | 4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB             | 11/2014                       | 463.65<br>546.00                    | -<br>-                             | -           |
| 370                            | 4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB             | 11/2014                       | 573.96<br>605.00                    | -<br>-                             | -           |
| 371                            | REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH  | 10/2015                       | 480.21<br>-                         | -<br>-                             | -           |
| 372                            | WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN       | 10/2014                       | 269.22<br>-                         | 01/2015<br>-                       | -           |
| 373                            | WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN                        | 10/2014                       | 257.09<br>-                         | 01/2015<br>-                       | -           |
| 374                            | REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN                                        | 10/2013                       | 278.87<br>-                         | 05/2014<br>-                       | -           |
| 375                            | REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN       | 01/1991                       | 376.52<br>-                         | 04/2014<br>-                       | -           |
| 376                            | WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN       | 02/2015                       | 383.40<br>-                         | 03/2015<br>-                       | -           |
| 377                            | WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM            | 11/2010                       | 624.41<br>-                         | 03/2011<br>-                       | -           |
| 378                            | TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH | 12/2011                       | 156.63<br>276.00                    | 02/2012<br>-                       | -           |
| 379                            | CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM            | 08/2010                       | 193.69<br>-                         | 10/2010<br>-                       | -           |
| 380                            | TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH | 11/2010                       | 305.49<br>-                         | 03/2011<br>-                       | -           |
| 381                            | TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH | 03/2012                       | 207.03<br>-                         | 05/2012<br>-                       | -           |
| 382                            | CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM                                                 | 04/2013                       | 151.59<br>-                         | 08/2013<br>-                       | -           |
| 383                            | CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM                                              | 04/2013                       | 166.27<br>-                         | 08/2013<br>-                       | -           |
| 384                            | CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM                                                 | 01/2013                       | 182.28<br>-                         | 02/2013<br>-                       | -           |
| 385                            | WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND          | 12/2010                       | 1,296.00<br>-                       | 02/2011<br>-                       | -           |
| 386                            | CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU      | 03/2015                       | 258.97<br>268.92                    | 08/2015<br>-                       | -           |

## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                                                        |                               |                                     |                                    | (September 2017) |
|--------------------------------|----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|------------------|
|                                |                                                                                                                                        |                               |                                     | Date of Commissioning (Month/Year) |                  |
| Sl.No                          | Project                                                                                                                                | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated      |
| 1                              | 2                                                                                                                                      | 3                             | 4                                   | 5                                  | 6                |
| 387                            | REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU     | 03/2015                       | 157.18<br>162.00                    | 07/2015<br>-                       | -                |
| 388                            | CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH     | 03/2015                       | 629.74<br>-                         | -<br>-                             | -                |
| 389                            | REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA    | 01/2015                       | 225.81<br>-                         | -<br>-                             | -                |
| 390                            | PADI - DAHOD - [N24000353]NHAI,RAJASTHAN                                                                                               | 11/2014                       | 279.14<br>-                         | 05/2017<br>-                       | -                |
| 391                            | JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN                                                                     | 10/2014                       | 264.72<br>-                         | 04/2017<br>-                       | -                |
| 392                            | THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU                                                                          | 07/2014                       | 401.11<br>-                         | 01/2017<br>-                       | -                |
| 393                            | 2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH                                                             | 06/2014                       | 301.04<br>-                         | 01/2016<br>-                       | -                |
| 394                            | 4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB            | 02/2015                       | 483.38<br>-                         | -<br>-                             | -                |
| 395                            | 4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB            | 02/2015                       | 616.36<br>-                         | -<br>-                             | -                |
| 396                            | 4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64( - [N24000374]PWD,PUNJAB           | 02/2015                       | 486.74<br>-                         | -<br>-                             | -                |
| 397                            | BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH                        | 06/2015                       | 390.51<br>-                         | -<br>-                             | -                |
| 398                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR          | 01/1991                       | 675.00<br>-                         | -<br>-                             | -                |
| 399                            | CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15( - [N24000383]PWD,PUNJAB           | 03/2015                       | 312.79<br>-                         | -<br>-                             | -                |
| 400                            | CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB           | 07/2014                       | 319.80<br>-                         | -<br>-                             | -                |
| 401                            | DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB           | 12/2015                       | 766.36<br>-                         | -<br>-                             | -                |
| 402                            | FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH | 01/2011                       | 264.16<br>-                         | -<br>-                             | -                |
| 403                            | 4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB                                            | 11/2015                       | 847.02<br>-                         | -<br>-                             | -                |
| 404                            | 4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB                                           | 11/2015                       | 889.24<br>-                         | -<br>-                             | -                |
| 405                            | BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH                                                                 | 08/2015                       | 257.80<br>-                         | -<br>-                             | -                |
| 406                            | DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB            | 12/2015                       | 578.38<br>-                         | -<br>-                             | -                |

## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                                                   |                               |                                     | (September 2017)                   |             |
|--------------------------------|-----------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
|                                |                                                                                                                                   |                               |                                     | Date of Commissioning (Month/Year) |             |
| Sl.No                          | Project                                                                                                                           | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1                              | 2                                                                                                                                 | 3                             | 4                                   | 5                                  | 6           |
| 407                            | WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE | 03/2015                       | 789.83<br>-                         | -<br>-                             | -           |
| 408                            | 2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN  | 11/2012                       | 530.07<br>-                         | 08/2016<br>-                       | -           |
| 409                            | 4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA                                                                        | 07/2015                       | 1,282.94<br>-                       | -<br>-                             | -           |
| 410                            | 4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM                             | 01/1991                       | 520.01<br>-                         | -<br>-                             | -           |
| 411                            | CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA        | 10/2015                       | 936.40<br>-                         | -<br>-                             | -           |
| 412                            | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH                                             | 03/2015                       | 795.76<br>-                         | -<br>-                             | -           |
| 413                            | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH                                              | 03/2015                       | 794.30<br>-                         | -<br>-                             | -           |
| 414                            | NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA                                                                                   | 09/2005                       | 168.00<br>-                         | 06/2006<br>-                       | -           |
| 415                            | FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR                                                                           | 08/2015                       | 556.07<br>-                         | -<br>-                             | -           |
| 416                            | FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR                                                                         | 08/2015                       | 814.04<br>-                         | -<br>-                             | -           |
| 417                            | FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA                                                                   | 12/2015                       | 752.28<br>-                         | -<br>-                             | -           |
| 418                            | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH                                             | 03/2015                       | 810.22<br>-                         | -<br>-                             | -           |
| 419                            | FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR                                                                           | 01/1991                       | 642.41<br>-                         | -<br>-                             | -           |
| 420                            | FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR                                                     | 12/2015                       | 1,167.45<br>-                       | -<br>-                             | -           |
| 421                            | WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH                          | 12/2014                       | 207.88<br>-                         | -<br>-                             | -           |
| 422                            | WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA       | 12/2015                       | 773.98<br>-                         | -<br>-                             | -           |
| 423                            | WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA       | 12/2015                       | 819.95<br>-                         | -<br>-                             | -           |
| 424                            | REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR                     | 01/1991                       | 478.35<br>-                         | -<br>-                             | -           |
| 425                            | WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB      | 06/2015                       | 892.17<br>-                         | -<br>-                             | -           |
| 426                            | WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB      | 06/2015                       | 899.21<br>-                         | -<br>-                             | -           |
| 427                            | TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU                                                                                       | 03/2007                       | 516.00<br>-                         | 07/2008<br>-                       | -           |
| 428                            | WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH                         | 12/2014                       | 207.88<br>-                         | -<br>-                             | -           |

## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                                                          |                               |                                     |                                    | (September 2017) |
|--------------------------------|------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|------------------|
|                                |                                                                                                                                          |                               |                                     | Date of Commissioning (Month/Year) |                  |
| Sl.No                          | Project                                                                                                                                  | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated      |
| 1                              | 2                                                                                                                                        | 3                             | 4                                   | 5                                  | 6                |
| 429                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40 - [N24000530]PWD,BIHAR              | 01/1991                       | 154.62<br>-                         | -<br>-                             | -                |
| 430                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR               | 01/1991                       | 319.68<br>-                         | -<br>-                             | -                |
| 431                            | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR            | 10/2014                       | 377.64<br>-                         | 03/2014<br>-                       | -                |
| 432                            | MEERUT-BULANDSHAHR - [N24000539]NHAI,UTTAR PRADESH                                                                                       | 01/2016                       | 683.24<br>-                         | -<br>-                             | -                |
| 433                            | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH         | 03/2016                       | 1,404.50<br>-                       | -<br>-                             | -                |
| 434                            | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH | 03/2016                       | 1,396.74<br>-                       | -<br>-                             | -                |
| 435                            | JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA                                                                         | 02/2016                       | 1,069.65<br>-                       | -<br>-                             | -                |
| 436                            | 4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA                                               | 03/2016                       | 701.40<br>-                         | -<br>-                             | -                |
| 437                            | 4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA                                                 | 03/2016                       | 870.00<br>-                         | -<br>-                             | -                |
| 438                            | FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND        | 03/2016                       | 720.00<br>-                         | -<br>-                             | -                |
| 439                            | 4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND        | 03/2016                       | 1,443.00<br>-                       | -<br>-                             | -                |
| 440                            | 4-LANNING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH     | 03/2016                       | 1,668.00<br>-                       | -<br>-                             | -                |
| 441                            | 4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH            | 03/2016                       | 1,408.00<br>-                       | -<br>-                             | -                |
| 442                            | 4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH                                 | 03/2016                       | 1,737.00<br>-                       | -<br>-                             | -                |
| 443                            | FOUR LANNING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT          | 05/2016                       | 998.18<br>-                         | -<br>-                             | -                |
| 444                            | FOUR LANNING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT          | 05/2016                       | 834.64<br>-                         | -<br>-                             | -                |
| 445                            | FOUR LANNING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT          | 05/2016                       | 723.64<br>-                         | -<br>-                             | -                |
| 446                            | FOUR LANNING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT          | 05/2016                       | 763.08<br>-                         | -<br>-                             | -                |
| 447                            | SIX-LANNING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT          | 05/2016                       | 425.60<br>-                         | -<br>-                             | -                |



## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                                                            |                               |                                     |                                    | (September 2017) |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|------------------|
|                                |                                                                                                                                            |                               |                                     | Date of Commissioning (Month/Year) |                  |
| Sl.No                          | Project                                                                                                                                    | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated      |
| 1                              | 2                                                                                                                                          | 3                             | 4                                   | 5                                  | 6                |
| 448                            | CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT                                                                           | 05/2016                       | 364.56<br>-                         | -<br>-                             | -                |
| 449                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR              | 01/2013                       | 322.01<br>-                         | 08/2014<br>-                       | -                |
| 450                            | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR              | 11/2013                       | 683.83<br>-                         | 07/2016<br>-                       | -                |
| 451                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR               | 02/2014                       | 665.50<br>-                         | 07/2016<br>-                       | -                |
| 452                            | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR              | 02/2016                       | 178.85<br>-                         | 05/2016<br>-                       | -                |
| 453                            | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR              | 02/2016                       | 553.30<br>-                         | 05/2016<br>-                       | -                |
| 454                            | FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR                | 01/2014                       | 1,408.85<br>-                       | 10/2016<br>-                       | -                |
| 455                            | CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR                               | 08/2015                       | 288.24<br>-                         | 11/2015<br>-                       | -                |
| 456                            | 4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA                       | 03/2016                       | 1,142.62<br>-                       | -<br>-                             | -                |
| 457                            | 4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA                       | 03/2016                       | 1,101.58<br>-                       | -<br>-                             | -                |
| 458                            | BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR                                                                    | 05/2015                       | 581.84<br>-                         | 05/2017<br>-                       | -                |
| 459                            | 4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN                                                     | 07/2016                       | 688.70<br>-                         | -<br>-                             | -                |
| 460                            | 4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT                                   | 07/2016                       | 829.97<br>-                         | -<br>-                             | -                |
| 461                            | TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND            | 07/2016                       | 458.03<br>-                         | -<br>-                             | -                |
| 462                            | 4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA                                                                                  | 05/2014                       | 720.69<br>-                         | -<br>-                             | -                |
| 463                            | 4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB                                                                                | 08/2016                       | 1,169.61<br>-                       | -<br>-                             | -                |
| 464                            | TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH                                       | 08/2016                       | 1,583.18<br>-                       | -<br>-                             | -                |
| 465                            | FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH    | 09/2016                       | 1,273.71<br>-                       | -<br>-                             | -                |
| 466                            | CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD( NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH | 04/2016                       | 245.79<br>-                         | -<br>-                             | -                |
| 467                            | FUNDED ) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH | 11/2015                       | 434.06<br>-                         | -<br>-                             | -                |



## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                                                            |                               |                                     | (September 2017)                   |             |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
|                                |                                                                                                                                            |                               |                                     | Date of Commissioning (Month/Year) |             |
| Sl.No                          | Project                                                                                                                                    | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1                              | 2                                                                                                                                          | 3                             | 4                                   | 5                                  | 6           |
| 468                            | SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN            | 09/2016                       | 1,239.82<br>-                       | -<br>-                             | -           |
| 469                            | TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA           | 09/2016                       | 950.69<br>-                         | -<br>-                             | -           |
| 470                            | SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN           | 09/2016                       | 1,100.19<br>-                       | -<br>-                             | -           |
| 471                            | SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE         | 09/2016                       | 1,244.10<br>-                       | -<br>-                             | -           |
| 472                            | 4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA                                                         | 11/2016                       | 1,071.61<br>-                       | -<br>-                             | -           |
| 473                            | 4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA                                                            | 11/2016                       | 1,064.88<br>-                       | -<br>-                             | -           |
| 474                            | SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA         | 11/2016                       | 290.73<br>-                         | -<br>-                             | -           |
| 475                            | REHABILITATION AND UPGRADE TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA                  | 10/2016                       | 1,008.96<br>-                       | -<br>-                             | -           |
| 476                            | FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH                                | 10/2016                       | 447.75<br>-                         | -<br>-                             | -           |
| 477                            | 2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT                                                            | 12/2016                       | 417.19<br>-                         | -<br>-                             | -           |
| 478                            | 6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN           | 12/2016                       | 1,031.95<br>-                       | -<br>-                             | -           |
| 479                            | CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH       | 12/2016                       | 534.55<br>-                         | -<br>-                             | -           |
| 480                            | CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH        | 01/2017                       | 450.68<br>-                         | -<br>-                             | -           |
| 481                            | SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT                  | 01/2017                       | 1,251.11<br>-                       | -<br>-                             | -           |
| 482                            | 4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA                                                | 03/2017                       | 1,059.73<br>-                       | 03/2017<br>-                       | -           |
| 483                            | CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH     | 01/2017                       | 1,253.10<br>-                       | 03/2017<br>-                       | -           |
| 484                            | TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH | 03/2017                       | 284.09<br>-                         | 04/2017<br>-                       | -           |
| 485                            | TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH | 02/2017                       | 195.23<br>-                         | 04/2017<br>-                       | -           |
| 486                            | TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH | 02/2017                       | 203.36<br>-                         | 04/2017<br>-                       | -           |

## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                                                            |                               |                                     | (September 2017)                   |             |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|-------------|
|                                |                                                                                                                                            |                               |                                     | Date of Commissioning (Month/Year) |             |
| Sl.No                          | Project                                                                                                                                    | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated |
| 1                              | 2                                                                                                                                          | 3                             | 4                                   | 5                                  | 6           |
| 487                            | TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH  | 01/2017                       | 194.66<br>-                         | 04/2017<br>-                       | -           |
| 488                            | TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH  | 02/2017                       | 168.32<br>-                         | 04/2017<br>-                       | -           |
| 489                            | TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH  | 02/2017                       | 180.57<br>-                         | 04/2017<br>-                       | -           |
| 490                            | CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH | 02/2017                       | 216.71<br>-                         | 04/2017<br>-                       | -           |
| 491                            | CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH | 02/2017                       | 167.28<br>-                         | 04/2017<br>-                       | -           |
| 492                            | CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND          | 02/2017                       | 507.68<br>-                         | 04/2017<br>-                       | -           |
| 493                            | TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH  | 01/2017                       | 198.22<br>-                         | 04/2017<br>-                       | -           |
| 494                            | REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH                 | 12/2015                       | 291.05<br>-                         | -<br>-                             | -           |
| 495                            | VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT                                                                                           | 03/2014                       | 503.16<br>-                         | 08/2016<br>-                       | -           |
|                                | Total                                                                                                                                      |                               | 1,33,488.10<br>-                    |                                    |             |
|                                |                                                                                                                                            |                               |                                     |                                    |             |
|                                | <u>SHIPPING AND PORTS</u>                                                                                                                  |                               |                                     |                                    |             |
| 496                            | SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU                                                                      | 06/2005                       | 2,427.40<br>-                       | 10/2008<br>-                       | -           |
| 497                            | RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA                                                     | 03/2007                       | 245.67<br>-                         | 04/2009<br>-                       | -           |
| 498                            | CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]KPL,TAMIL NADU                                                         | 10/2013                       | 198.94<br>-                         | 06/2017<br>-                       | -           |
| 499                            | CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL,TAMIL NADU                                                           | 12/2014                       | 274.85<br>-                         | 04/2017<br>-                       | -           |
|                                | Total                                                                                                                                      |                               | 3,146.86<br>-                       |                                    |             |
|                                |                                                                                                                                            |                               |                                     |                                    |             |
|                                | <u>TELECOMMUNICATIONS</u>                                                                                                                  |                               |                                     |                                    |             |
| 500                            | NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE                                         | 09/2014                       | 2,111.17<br>-                       | 09/2014<br>-                       | -           |
| 501                            | GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI                                                                          | 06/2016                       | 418.26<br>-                         | 06/2017<br>-                       | -           |
|                                | Total                                                                                                                                      |                               | 2,529.43<br>-                       |                                    |             |
|                                |                                                                                                                                            |                               |                                     |                                    |             |
|                                | <u>URBAN DEVELOPMENT</u>                                                                                                                   |                               |                                     |                                    |             |

## Details of Projects Without Date of Commissioning

| Costing Rs.150 Crore and above |                                                                                                                                    |                               |                                     |                                    | (September 2017) |
|--------------------------------|------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|------------------------------------|------------------|
|                                |                                                                                                                                    |                               |                                     | Date of Commissioning (Month/Year) |                  |
| Sl.No                          | Project                                                                                                                            | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Original / Revised                 | Anticipated      |
| 1                              | 2                                                                                                                                  | 3                             | 4                                   | 5                                  | 6                |
| 502                            | DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI                                                                                      | 09/2011                       | 38,585.00<br>-                      | 03/2016<br>-                       | 12/2016          |
| 503                            | BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA                                                                           | 05/2006                       | 6,395.00<br>13,845.01               | 06/2011<br>12/2015                 | 04/2017          |
| 504                            | CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI                        | 05/2012                       | 405.01<br>-                         | 12/2014<br>07/2017                 | 07/2017          |
| 505                            | CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH                       | 06/2014                       | 157.84<br>-                         | 03/2017<br>-                       | -                |
| 506                            | REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH | 08/2007                       | 246.90<br>-                         | -<br>-                             | -                |
| 507                            | MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA                                                           | 07/2013                       | 23,136.00<br>-                      | 01/2015<br>-                       | -                |
| 508                            | C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT - [N28000089]CPWD,TAMIL NADU            | 12/2015                       | 209.00<br>-                         | -<br>-                             | -                |
| 509                            | DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN            | 08/2014                       | 350.02<br>479.87                    | 03/2015<br>12/2017                 | -                |
| 510                            | CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR                | 02/2016                       | 496.18<br>496.00                    | 06/2017<br>-                       | -                |
|                                | Total                                                                                                                              |                               | 69,980.95<br>-                      |                                    |                  |
|                                |                                                                                                                                    |                               |                                     |                                    |                  |
|                                | Grand Total                                                                                                                        |                               | 4,57,594.71                         |                                    |                  |

## Details of Projects Without Original Date of Commissioning

Annexure - IX

| Costing Rs.150 Crore and above |                                                                                                                                 |                               |                                    |                              |                                    | (September 2017)                   |             |                                   |                            |
|--------------------------------|---------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------------------|----------------------------|
|                                |                                                                                                                                 |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                                   |                            |
| Sl.No                          | Project                                                                                                                         | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
| 1                              | 2                                                                                                                               | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                                 | 10                         |
|                                | <u>STEEL</u>                                                                                                                    |                               |                                    |                              |                                    |                                    |             |                                   |                            |
| 1                              | CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL, GUJARAT                                | 01/2013                       | 175.00 -                           | 175.00                       | 1.83                               | - -                                | 12/2017     | -                                 | 0/0                        |
|                                | Total                                                                                                                           |                               | 175.00 -                           | 175.00                       | 1.83                               |                                    |             |                                   | 0/0                        |
|                                | <u>RAILWAYS</u>                                                                                                                 |                               |                                    |                              |                                    |                                    |             |                                   |                            |
| 2                              | BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH                                                                  | 03/2008                       | 195.64 -                           | 474.30                       | 398.89                             | - -                                | 10/2017     | -                                 | 0/0                        |
| 3                              | MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND                                                             | 04/2012                       | 258.20 -                           | 365.00                       | -                                  | - -                                | 12/2017     | -                                 | 0/0                        |
| 4                              | ERNAKULAM-KUMBALAM - [N22000204]SR, KERALA                                                                                      | 04/2010                       | 189.24 -                           | 189.24                       | 189.35                             | - -                                | 12/2017     | -                                 | 0/0                        |
| 5                              | ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, KERALA                                                                          | 10/1998                       | 550.00 -                           | 2,815.62                     | 240.68                             | - -                                | 01/2018     | -                                 | 0/0                        |
| 6                              | MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR                                                                          | 04/2003                       | 218.19 -                           | 412.05                       | 356.37                             | - -                                | 03/2018     | -                                 | 0/0                        |
| 7                              | AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER, UTTAR PRADESH                                                          | 03/2012                       | 199.75 -                           | 199.75                       | 210.64                             | - -                                | 03/2018     | -                                 | 0/0                        |
| 8                              | VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]RVNL, MULTI STATE                                                         | 04/2008                       | 822.39 -                           | 1,810.00                     | 1,639.70                           | - -                                | 03/2018     | -                                 | 0/1                        |
| 9                              | NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL                                                                       | 04/2011                       | 209.77 -                           | 445.00                       | 389.45                             | - -                                | 03/2018     | -                                 | 0/0                        |
| 10                             | NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE | 04/1999                       | 523.17 -                           | 1,871.00                     | 1,071.96                           | - -                                | 03/2018     | -                                 | 0/0                        |
| 11                             | MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR, RAJASTHAN                                         | 04/2013                       | 456.00 -                           | 855.16                       | 594.34                             | - -                                | 05/2018     | -                                 | 0/0                        |
| 12                             | DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR, RAJASTHAN                                                                         | 02/1997                       | 410.08 -                           | 780.98                       | 368.96                             | - -                                | 08/2018     | -                                 | 0/0                        |
| 13                             | CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE                                                                                 | 03/2013                       | 295.00 -                           | 477.31                       | 92.31                              | - -                                | 10/2018     | -                                 | 0/0                        |
| 14                             | THIYAT HAMIRA-SANU - [N22000149]NWR, RAJASTHAN                                                                                  | 04/2013                       | 236.93 -                           | 276.89                       | 98.58                              | - -                                | 10/2018     | -                                 | 0/0                        |
| 15                             | RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR, RAJASTHAN                                                                      | 04/2012                       | 288.97 335.53                      | 369.08                       | 160.39                             | - -                                | 10/2018     | -                                 | 0/0                        |

## Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above

(September 2017)

|       |                                                                                                                       |                                  |                                          |                                    |                                          | Date of Commissioning<br>(Month/Year) |             |                                         |                                  |
|-------|-----------------------------------------------------------------------------------------------------------------------|----------------------------------|------------------------------------------|------------------------------------|------------------------------------------|---------------------------------------|-------------|-----------------------------------------|----------------------------------|
| Sl.No | Project                                                                                                               | Date of Approval<br>(Month/Year) | Original/<br>Revised Cost<br>(Rs. crore) | Anticipated<br>Cost<br>(Rs. crore) | Cumulative<br>Expenditure<br>(Rs. crore) | Original<br>/ Revised                 | Anticipated | Delay w.r.t.<br>Original<br>(in months) | Milestones<br>Achieved/<br>Total |
| 1     | 2                                                                                                                     | 3                                | 4                                        | 5                                  | 6                                        | 7                                     | 8           | 9                                       | 10                               |
| 16    | HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE                                | 04/2010                          | 157.94<br>-                              | 157.94                             | 47.63                                    | -<br>-                                | 11/2018     | -                                       | 0/0                              |
| 17    | HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE                                                                      | 05/2015                          | 720.00<br>-                              | 678.54                             | -                                        | -<br>-                                | 12/2018     | -                                       | 0/38                             |
| 18    | MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE                                                          | 04/1997                          | 218.24<br>236.41                         | 525.00                             | 544.20                                   | -<br>-                                | 03/2019     | -                                       | 0/0                              |
| 19    | TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL                                               | 04/2000                          | 1,188.91<br>-                            | 1,319.33                           | 757.23                                   | -<br>12/2009                          | 03/2019     | 111(R1)                                 | 0/0                              |
| 20    | HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA                                                                      | 04/1996                          | 301.64<br>-                              | 1,185.64                           | -                                        | -<br>09/2009                          | 03/2019     | 114(R1)                                 | 0/0                              |
| 21    | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM                                | 09/2006                          | 200.00<br>-                              | 780.00                             | 425.47                                   | -<br>-                                | 03/2019     | -                                       | 0/0                              |
| 22    | BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN                                                           | 04/2012                          | 246.08<br>-                              | 348.55                             | 22.76                                    | -<br>-                                | 03/2019     | -                                       | 0/0                              |
| 23    | RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT | 04/1994                          | 320.66<br>-                              | 399.63                             | -                                        | -<br>-                                | 03/2019     | -                                       | 0/0                              |
| 24    | VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT                                                                      | 04/2011                          | 446.00<br>-                              | 1,037.15                           | 590.60                                   | -<br>-                                | 03/2019     | -                                       | 0/0                              |
| 25    | AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN                                                                           | 04/2011                          | 213.39<br>-                              | 272.99                             | 89.27                                    | -<br>-                                | 03/2019     | -                                       | 0/0                              |
| 26    | ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN                                                                    | 04/2013                          | 242.09<br>-                              | 293.68                             | 120.02                                   | -<br>-                                | 03/2019     | -                                       | 0/0                              |
| 27    | NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE                                                 | 04/2013                          | 1,798.00<br>-                            | 1,798.00                           | -                                        | -<br>-                                | 03/2019     | -                                       | 0/0                              |
| 28    | NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL                                          | 04/2012                          | 283.55<br>-                              | 330.00                             | 191.07                                   | -<br>-                                | 03/2019     | -                                       | 0/0                              |
| 29    | AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM                                                               | 04/2011                          | 312.12<br>-                              | 508.00                             | 490.99                                   | -<br>-                                | 03/2019     | -                                       | 0/0                              |
| 30    | LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM                                                           | 04/2012                          | 246.07<br>-                              | 398.93                             | 103.22                                   | -<br>-                                | 03/2019     | -                                       | 0/0                              |
| 31    | HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA                                                         | 04/2010                          | 2,127.00<br>-                            | 2,127.00                           | 803.33                                   | -<br>-                                | 03/2019     | -                                       | 0/1                              |
| 32    | THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL,TAMIL NADU    | 04/2011                          | 190.10<br>-                              | 350.00                             | 282.22                                   | -<br>-                                | 03/2019     | -                                       | 0/0                              |
| 33    | HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE                                                                | 04/2005                          | 230.03<br>-                              | 718.54                             | 274.67                                   | -<br>-                                | 05/2019     | -                                       | 0/0                              |
| 34    | AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA                                                                          | 04/2012                          | 252.00<br>-                              | 580.00                             | -                                        | -<br>-                                | 07/2019     | -                                       | 2/3                              |
| 35    | NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR                                       | 09/2006                          | 300.00<br>-                              | 2,145.00                           | 921.25                                   | -<br>-                                | 03/2020     | -                                       | 0/0                              |

## Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above (September 2017)

|       |                                                                                       |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                                   |                            |
|-------|---------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------------------|----------------------------|
| Sl.No | Project                                                                               | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
| 1     | 2                                                                                     | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                                 | 10                         |
| 36    | AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT                                        | 04/2012                       | 567.18 -                           | 975.62                       | 308.42                             | - -                                | 03/2020     | -                                 | 0/0                        |
| 37    | DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND                                            | 04/2013                       | 4,274.00 -                         | 4,274.00                     | -                                  | - -                                | 03/2020     | -                                 | 0/0                        |
| 38    | MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE                                 | 04/2011                       | 165.82 -                           | 450.00                       | 117.50                             | - -                                | 03/2020     | -                                 | 0/0                        |
| 39    | VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH | 03/2012                       | 1,503.71 -                         | 1,503.71                     | 475.40                             | - -                                | 03/2020     | -                                 | 0/0                        |
| 40    | KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH                           | 12/2012                       | 826.57 -                           | 1,160.83                     | 452.03                             | - -                                | 03/2020     | -                                 | 1/1                        |
| 41    | SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA                       | 03/2012                       | 155.81 -                           | 238.03                       | 149.99                             | - -                                | 03/2020     | -                                 | 0/0                        |
| 42    | PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE                                | 05/2015                       | 600.00 -                           | 648.00                       | .94                                | - -                                | 03/2020     | -                                 | 0/0                        |
| 43    | YELAHANKA-PENKONDA - [N22000328]SWR,MULTI STATE                                       | 05/2015                       | 860.43 -                           | 860.43                       | 285.52                             | - -                                | 03/2020     | -                                 | 0/0                        |
| 44    | ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA                                            | 03/2015                       | 960.00 578.00                      | 578.00                       | 298.80                             | - 11/2015                          | 03/2020     | 52(R3)                            | 0/2                        |
| 45    | DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT                                         | 04/2012                       | 376.59 -                           | 644.38                       | 25.21                              | - -                                | 12/2020     | -                                 | 0/0                        |
| 46    | PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT                                   | 04/2013                       | 1,266.89 -                         | 1,548.66                     | 357.04                             | - -                                | 12/2020     | -                                 | 0/0                        |
| 47    | KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH                        | 12/2001                       | 330.00 -                           | 2,125.18                     | 14.17                              | - -                                | 03/2021     | -                                 | 0/0                        |
| 48    | RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH                          | 04/2001                       | 470.92 727.13                      | 2,713.09                     | 632.05                             | - -                                | 03/2021     | -                                 | 0/0                        |
| 49    | NEW BG LINE FROM BYRNHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA                       | 04/2010                       | 4,083.02 -                         | 6,000.00                     | 249.54                             | - -                                | 03/2021     | -                                 | 0/0                        |
| 50    | KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA                                    | 04/2011                       | 277.70 792.89                      | 792.89                       | 202.91                             | - -                                | 03/2021     | -                                 | 0/0                        |
| 51    | SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA                                   | 03/2011                       | 679.27 -                           | 1,579.27                     | 561.78                             | - -                                | 03/2021     | -                                 | 0/0                        |
| 52    | BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA                                  | 03/2013                       | 858.67 -                           | 843.04                       | 41.36                              | - -                                | 03/2021     | -                                 | 0/0                        |
| 53    | KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE                                         | 04/2015                       | 2,063.03 -                         | 2,063.03                     | .14                                | - -                                | 03/2021     | -                                 | 0/0                        |
| 54    | BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM                          | 04/2015                       | 2,232.32 -                         | 2,232.32                     | 63.56                              | - -                                | 03/2021     | -                                 | 0/0                        |
| 55    | DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM                                          | 04/2015                       | 870.96 -                           | 870.96                       | 18.49                              | - -                                | 03/2021     | -                                 | 0/0                        |
| 56    | SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT                                         | 04/2015                       | 1,002.39 -                         | 1,002.39                     | -                                  | - -                                | 03/2021     | -                                 | 0/0                        |
| 57    | KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA                                 | 04/1994                       | 470.21 -                           | 3,004.90                     | 899.41                             | - -                                | 06/2021     | -                                 | 0/0                        |

## Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above (September 2017)

|       |                                                                                                                            |                                  |                                          |                                    |                                          | Date of Commissioning<br>(Month/Year) |                 |                                         |                                          |
|-------|----------------------------------------------------------------------------------------------------------------------------|----------------------------------|------------------------------------------|------------------------------------|------------------------------------------|---------------------------------------|-----------------|-----------------------------------------|------------------------------------------|
| Sl.No | Project                                                                                                                    | Date of Approval<br>(Month/Year) | Original/<br>Revised Cost<br>(Rs. crore) | Anticipated<br>Cost<br>(Rs. crore) | Cumulative<br>Expenditure<br>(Rs. crore) | Original<br>/<br>Revised              | Antici<br>Pated | Delay w.r.t.<br>Original<br>(in months) | Milesto<br>nes<br>Achiev<br>ed/<br>Total |
| 1     | 2                                                                                                                          | 3                                | 4                                        | 5                                  | 6                                        | 7                                     | 8               | 9                                       | 10                                       |
| 58    | MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA                                                              | 04/2006                          | 378.56<br>-                              | 1,160.47                           | 1.74                                     | -<br>-                                | 03/2022         | -                                       | 0/1                                      |
| 59    | DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE                                               | 04/2007                          | 1,640.04<br>-                            | 1,640.04                           | 331.91                                   | -<br>-                                | 03/2022         | -                                       | 0/0                                      |
| 60    | WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA                                                                   | 04/2012                          | 297.85<br>540.02                         | 540.02                             | 118.37                                   | -<br>-                                | 03/2022         | -                                       | 0/0                                      |
| 61    | WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA                                                          | 02/2015                          | 630.00<br>1,272.19                       | 1,272.19                           | 51.81                                    | -<br>-                                | 03/2022         | -                                       | 0/0                                      |
| 62    | WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA                                                             | 02/2016                          | 912.00<br>637.95                         | 637.95                             | .36                                      | -<br>-                                | 03/2022         | -                                       | 0/0                                      |
| 63    | TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA                                                                      | 04/2005                          | 810.78<br>-                              | 1,928.07                           | 466.10                                   | -<br>-                                | 12/2022         | -                                       | 0/0                                      |
| 64    | WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA                                                                      | 04/2008                          | 499.30<br>2,491.43                       | 3,168.29                           | 700.77                                   | -<br>-                                | 03/2023         | -                                       | 0/0                                      |
| 65    | ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA                                                       | 02/2015                          | 2,326.00<br>2,449.91                     | 2,449.91                           | 12.54                                    | -<br>-                                | 03/2023         | -                                       | 0/0                                      |
| 66    | VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA                                                                | 01/1991                          | 2,335.67<br>-                            | 2,335.67                           | 10.76                                    | -<br>-                                | 12/2024         | -                                       | 0/0                                      |
| 67    | HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA                                                                                | 03/2015                          | 1,900.00<br>1,141.00                     | 1,141.00                           | 430.98                                   | -<br>03/2020                          | -               | -                                       | 0/5                                      |
|       | Total                                                                                                                      |                                  | 51,472.84<br>-                           | 79,677.64                          | 18,755.15                                |                                       |                 |                                         | 3/52                                     |
|       |                                                                                                                            |                                  |                                          |                                    |                                          |                                       |                 |                                         |                                          |
|       | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                         |                                  |                                          |                                    |                                          |                                       |                 |                                         |                                          |
| 68    | CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA | 03/2015                          | 168.30<br>-                              | 168.30                             | 13.43                                    | -<br>-                                | 10/2017         | -                                       | 0/4                                      |
| 69    | 4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA                                              | 06/2015                          | 845.24<br>-                              | 845.24                             | -                                        | -<br>-                                | 11/2017         | -                                       | 0/0                                      |
| 70    | IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB  | 09/2015                          | 273.06<br>-                              | 273.06                             | 41.24                                    | -<br>-                                | 11/2017         | -                                       | 0/0                                      |
| 71    | HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA                                              | 09/2010                          | 946.00<br>-                              | 946.00                             | 818.53                                   | -<br>-                                | 12/2017         | -                                       | 3/3                                      |
| 72    | FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB                                                       | 09/2014                          | 479.00<br>-                              | 479.00                             | 401.66                                   | -<br>-                                | 12/2017         | -                                       | 0/0                                      |
| 73    | FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH                                                       | 03/2015                          | 928.83<br>-                              | 928.83                             | 1,254.37                                 | -<br>-                                | 12/2017         | -                                       | 0/0                                      |
| 74    | SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL                                                            | 04/2014                          | 1,665.00<br>-                            | 1,665.00                           | 2,091.52                                 | -<br>-                                | 12/2017         | -                                       | 0/0                                      |
| 75    | TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI,BIHAR                                                          | 08/2015                          | 854.80<br>-                              | 854.80                             | -                                        | -<br>-                                | 12/2017         | -                                       | 0/0                                      |

## Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above (September 2017)

|       |                                                                                                                                     |                                  |                                          |                                    |                                          | Date of Commissioning<br>(Month/Year) |             |                                         |                                  |
|-------|-------------------------------------------------------------------------------------------------------------------------------------|----------------------------------|------------------------------------------|------------------------------------|------------------------------------------|---------------------------------------|-------------|-----------------------------------------|----------------------------------|
| Sl.No | Project                                                                                                                             | Date of Approval<br>(Month/Year) | Original/<br>Revised Cost<br>(Rs. crore) | Anticipated<br>Cost<br>(Rs. crore) | Cumulative<br>Expenditure<br>(Rs. crore) | Original<br>/ Revised                 | Anticipated | Delay w.r.t.<br>Original<br>(in months) | Milestones<br>Achieved/<br>Total |
| 1     | 2                                                                                                                                   | 3                                | 4                                        | 5                                  | 6                                        | 7                                     | 8           | 9                                       | 10                               |
| 76    | CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL                                                                     | 10/2015                          | 361.15<br>-                              | 361.15                             | -                                        | -<br>-                                | 01/2018     | -                                       | 0/0                              |
| 77    | FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI, HARYANA                                                                | 07/2015                          | 1,393.00<br>-                            | 1,393.00                           | 2,151.12                                 | -<br>-                                | 01/2018     | -                                       | 0/0                              |
| 78    | TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI, RAJASTHAN                                       | 08/2015                          | 275.90<br>-                              | 275.90                             | -                                        | -<br>-                                | 02/2018     | -                                       | 0/0                              |
| 79    | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-I)_NEW - [N24000609]NHAI, DELHI                                         | 09/2015                          | 771.18<br>-                              | 771.18                             | 512.31                                   | -<br>-                                | 03/2018     | -                                       | 0/0                              |
| 80    | FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP, GOA                              | 03/2015                          | 297.00<br>-                              | 297.00                             | 38.33                                    | -<br>-                                | 04/2018     | -                                       | 0/1                              |
| 81    | FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI, BIHAR                                                                        | 08/2015                          | 322.09<br>-                              | 322.09                             | -                                        | -<br>-                                | 04/2018     | -                                       | 0/0                              |
| 82    | FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI, CHHATISGARH                                                                   | 12/2015                          | 509.13<br>-                              | 509.13                             | 202.90                                   | -<br>-                                | 04/2018     | -                                       | 0/0                              |
| 83    | FOUR / SIX LANING OF RAIPUR - SIMGA ( PKG-1) - [N24000510]NHAI, CHHATISGARH                                                         | 12/2015                          | 726.67<br>-                              | 726.67                             | -                                        | -<br>-                                | 04/2018     | -                                       | 0/0                              |
| 84    | TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR                                                     | 08/2015                          | 516.13<br>-                              | 516.13                             | -                                        | -<br>-                                | 04/2018     | -                                       | 0/0                              |
| 85    | CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270( D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 ( D - [N24000432]NHAI, MAHARASHTRA | 09/2015                          | 414.51<br>-                              | 414.00                             | 88.66                                    | -<br>-                                | 05/2018     | -                                       | 0/0                              |
| 86    | CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 ( - [N24000435]NHAI, MAHARASHTRA   | 10/2015                          | 531.13<br>-                              | 531.13                             | -                                        | -<br>-                                | 05/2018     | -                                       | 0/0                              |
| 87    | CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 ( OLD SH -54) PKG-2 - [N24000441]NHAI, MAHARASHTRA                  | 10/2015                          | 593.26<br>-                              | 593.26                             | -                                        | -<br>-                                | 05/2018     | -                                       | 0/0                              |
| 88    | 6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI, MAHARASHTRA                    | 08/2015                          | 505.00<br>-                              | 505.00                             | 38.08                                    | -<br>-                                | 05/2018     | -                                       | 0/0                              |
| 89    | FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI, HARYANA                                              | 11/2015                          | 867.66<br>-                              | 867.66                             | 542.57                                   | -<br>-                                | 05/2018     | -                                       | 0/0                              |
| 90    | FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI, CHHATISGARH                                                                      | 12/2015                          | 596.67<br>-                              | 596.67                             | 67.84                                    | -<br>-                                | 05/2018     | -                                       | 0/0                              |
| 91    | TWO LANING WITH PS OF JOWAI - MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA                                  | 12/2015                          | 479.20<br>-                              | 479.20                             | -                                        | -<br>-                                | 05/2018     | -                                       | 0/0                              |
| 92    | UP/HARYANA BORDER - YAMUNA NAGAR - SAHA- BARWALA - PANCHKULA ( PKG - 1) - [N24000597]NHAI, HARYANA                                  | 05/2015                          | 600.85<br>-                              | 600.85                             | 234.36                                   | -<br>-                                | 05/2018     | -                                       | 0/0                              |



## Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above

(September 2017)

|       |                                                                                                                                       |                                  |                                          |                                    |                                          | Date of Commissioning<br>(Month/Year) |             |                                         |                                  |
|-------|---------------------------------------------------------------------------------------------------------------------------------------|----------------------------------|------------------------------------------|------------------------------------|------------------------------------------|---------------------------------------|-------------|-----------------------------------------|----------------------------------|
| Sl.No | Project                                                                                                                               | Date of Approval<br>(Month/Year) | Original/<br>Revised Cost<br>(Rs. crore) | Anticipated<br>Cost<br>(Rs. crore) | Cumulative<br>Expenditure<br>(Rs. crore) | Original<br>/ Revised                 | Anticipated | Delay w.r.t.<br>Original<br>(in months) | Milestones<br>Achieved/<br>Total |
| 1     | 2                                                                                                                                     | 3                                | 4                                        | 5                                  | 6                                        | 7                                     | 8           | 9                                       | 10                               |
| 93    | 4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA         | 04/2016                          | 804.97<br>-                              | 804.97                             | -                                        | -<br>-                                | 06/2018     | -                                       | 0/0                              |
| 94    | BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA               | 03/2016                          | 197.69<br>-                              | 197.69                             | -                                        | -<br>-                                | 07/2018     | -                                       | 0/0                              |
| 95    | FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU     | 02/2016                          | 641.17<br>-                              | 641.17                             | 47.95                                    | -<br>-                                | 07/2018     | -                                       | 0/0                              |
| 96    | BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA                | 03/2016                          | 244.00<br>-                              | 244.00                             | -                                        | -<br>-                                | 07/2018     | -                                       | 0/0                              |
| 97    | 4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND                                        | 11/2012                          | 605.84<br>-                              | 605.84                             | 547.57                                   | -<br>-                                | 07/2018     | -                                       | 0/0                              |
| 98    | FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA                                                                       | 03/2015                          | 1,388.00<br>-                            | 1,388.00                           | 498.00                                   | -<br>-                                | 08/2018     | -                                       | 0/0                              |
| 99    | FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU     | 02/2016                          | 707.82<br>-                              | 707.82                             | 129.75                                   | -<br>-                                | 08/2018     | -                                       | 0/0                              |
| 100   | FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND                                                                     | 08/2016                          | 323.72<br>-                              | 323.72                             | 9.23                                     | -<br>-                                | 08/2018     | -                                       | 0/0                              |
| 101   | FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL    | 09/2016                          | 767.03<br>-                              | 767.03                             | 58.27                                    | -<br>-                                | 08/2018     | -                                       | 0/0                              |
| 102   | TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN       | 07/2016                          | 331.46<br>-                              | 331.46                             | -                                        | -<br>-                                | 10/2018     | -                                       | 0/0                              |
| 103   | FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA                                                                         | 12/2015                          | 1,423.96<br>-                            | 1,423.96                           | 454.64                                   | -<br>-                                | 11/2018     | -                                       | 0/0                              |
| 104   | FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH                                | 01/2016                          | 1,134.97<br>-                            | 1,134.97                           | 171.12                                   | -<br>-                                | 11/2018     | -                                       | 0/0                              |
| 105   | CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL                                                        | 03/2016                          | 229.37<br>-                              | 229.37                             | 32.47                                    | -<br>-                                | 11/2018     | -                                       | 0/0                              |
| 106   | 6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH                                                                      | 07/2015                          | 1,657.20<br>-                            | 1,657.20                           | 225.00                                   | -<br>-                                | 01/2019     | -                                       | 0/0                              |
| 107   | FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH | 06/2015                          | 1,583.79<br>-                            | 1,583.79                           | 560.20                                   | -<br>-                                | 01/2019     | -                                       | 0/0                              |

## Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above (September 2017)

|       |                                                                                                                                      |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                                   |                            |
|-------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------------------|----------------------------|
| Sl.No | Project                                                                                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
| 1     | 2                                                                                                                                    | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                                 | 10                         |
| 108   | 2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN                                                            | 08/2016                       | 320.30 -                           | 320.30                       | -                                  | - -                                | 01/2019     | -                                 | 0/0                        |
| 109   | BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH                                 | 08/2016                       | 227.49 -                           | 227.49                       | 3.50                               | - -                                | 01/2019     | -                                 | 0/0                        |
| 110   | 2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH                             | 02/2016                       | 273.20 -                           | 273.20                       | 21.43                              | - -                                | 02/2019     | -                                 | 0/0                        |
| 111   | CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA   | 12/2015                       | 649.50 -                           | 649.50                       | 11.42                              | - -                                | 03/2019     | -                                 | 0/0                        |
| 112   | 4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND                                                     | 02/2016                       | 997.15 -                           | 997.15                       | 196.95                             | - -                                | 03/2019     | -                                 | 0/0                        |
| 113   | HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA                                                                       | 08/2016                       | 1,167.42 -                         | 1,167.42                     | 24.65                              | - -                                | 03/2019     | -                                 | 0/0                        |
| 114   | 4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA   | 11/2016                       | 400.25 -                           | 400.25                       | -                                  | - -                                | 03/2019     | -                                 | 0/0                        |
| 115   | 4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA   | 11/2016                       | 446.17 -                           | 446.17                       | -                                  | - -                                | 03/2019     | -                                 | 0/0                        |
| 116   | 8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA                                                                       | 07/2015                       | 2,128.72 -                         | 2,128.72                     | 249.15                             | - -                                | 04/2019     | -                                 | 0/0                        |
| 117   | FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR                                                                  | 12/2015                       | 1,041.10 -                         | 1,041.10                     | -                                  | - -                                | 04/2019     | -                                 | 0/0                        |
| 118   | TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR                                                        | 08/2015                       | 399.54 -                           | 399.54                       | -                                  | - -                                | 04/2019     | -                                 | 0/0                        |
| 119   | ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH                                      | 03/2016                       | 676.73 -                           | 676.73                       | 71.78                              | - -                                | 04/2019     | -                                 | 0/0                        |
| 120   | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH                 | 03/2016                       | 1,587.49 -                         | 1,587.49                     | -                                  | - -                                | 04/2019     | -                                 | 0/0                        |
| 121   | FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH | 03/2016                       | 899.00 -                           | 899.00                       | -                                  | - -                                | 04/2019     | -                                 | 0/0                        |
| 122   | 4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH                                       | 08/2016                       | 2,016.00 -                         | 2,016.00                     | -                                  | - -                                | 04/2019     | -                                 | 0/0                        |
| 123   | FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA                                 | 08/2016                       | 1,664.20 -                         | 1,664.20                     | 7.25                               | - -                                | 04/2019     | -                                 | 0/0                        |

## **Details of Projects Without Original Date of Commissioning**

**Costing Rs.150 Crore and above**

**(September 2017)**

|       |                                                                                                                                    |                               |                                    |                              |                                    | Date of Commissioning (Month/Year) |             |                                   |                            |
|-------|------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------|------------------------------------|------------------------------------|-------------|-----------------------------------|----------------------------|
| Sl.No | Project                                                                                                                            | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised                 | Anticipated | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
| 1     | 2                                                                                                                                  | 3                             | 4                                  | 5                            | 6                                  | 7                                  | 8           | 9                                 | 10                         |
| 124   | 4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA                                                               | 07/2015                       | 2,288.18 -                         | 2,288.18                     | -                                  | -                                  | 05/2019     | -                                 | 0/0                        |
| 125   | 4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA                                                           | 07/2015                       | 1,885.74 -                         | 1,885.74                     | -                                  | -                                  | 05/2019     | -                                 | 0/0                        |
| 126   | DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH                                                     | 01/2016                       | 701.12 -                           | 701.12                       | -                                  | -                                  | 05/2019     | -                                 | 0/0                        |
| 127   | CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA                                                          | 08/2016                       | 248.97 -                           | 248.97                       | -                                  | -                                  | 05/2019     | -                                 | 0/0                        |
| 128   | CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA     | 09/2016                       | 1,004.67 -                         | 1,004.67                     | -                                  | -                                  | 05/2019     | -                                 | 0/0                        |
| 129   | CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA | 01/2017                       | 244.90 -                           | 244.90                       | -                                  | -                                  | 05/2019     | -                                 | 0/0                        |
| 130   | DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH                              | 01/2016                       | 1,081.57 -                         | 1,081.57                     | -                                  | -                                  | 06/2019     | -                                 | 0/0                        |
| 131   | NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA                                                                           | 03/2016                       | 546.00 -                           | 546.00                       | -                                  | -                                  | 07/2019     | -                                 | 0/0                        |
| 132   | NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA                                                                           | 03/2016                       | 591.66 -                           | 591.66                       | -                                  | -                                  | 07/2019     | -                                 | 0/0                        |
| 133   | DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA      | 09/2016                       | 2,510.04 -                         | 2,510.04                     | -                                  | -                                  | 08/2019     | -                                 | 0/0                        |
| 134   | 4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB        | 08/2016                       | 1,388.34 -                         | 1,388.34                     | -                                  | -                                  | 09/2019     | -                                 | 0/0                        |
|       | <b>Total</b>                                                                                                                       |                               | 55,347.20 -                        | 55,346.69                    | 11,817.25                          |                                    |             |                                   | 3/8                        |
|       |                                                                                                                                    |                               |                                    |                              |                                    |                                    |             |                                   |                            |
|       | <b>URBAN DEVELOPMENT</b>                                                                                                           |                               |                                    |                              |                                    |                                    |             |                                   |                            |
| 135   | CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI           | 06/2015                       | 197.33 -                           | 197.33                       | 3.79                               | -                                  | 04/2019     | -                                 | 0/2                        |
|       | <b>Total</b>                                                                                                                       |                               | 197.33 -                           | 197.33                       | 3.79                               |                                    |             |                                   | 0/2                        |
|       |                                                                                                                                    |                               |                                    |                              |                                    |                                    |             |                                   |                            |
|       | <b>Grand Total</b>                                                                                                                 |                               | 1,07,192.37                        | 1,35,396.66                  | 30,578.02                          |                                    |             |                                   | 6/62                       |

## Details of Projects Without Milestones w.r.t. Original Schedule

**Annexure - X**

| Costing Rs.150 Crore and Above |                                                                                                                       |                                  |                                             | (September 2017)                      |             |                                  |
|--------------------------------|-----------------------------------------------------------------------------------------------------------------------|----------------------------------|---------------------------------------------|---------------------------------------|-------------|----------------------------------|
| Sl.No                          | Project                                                                                                               | Date of Approval<br>(Month/Year) | Original/<br>Revised<br>Cost<br>(Rs. crore) | Date of Commissioning<br>(Month/Year) |             | Milestones<br>Achieved/<br>Total |
|                                |                                                                                                                       |                                  |                                             | Original /<br>Revised                 | Anticipated |                                  |
| 1                              | 2                                                                                                                     | 3                                | 4                                           | 5                                     | 6           | 7                                |
|                                |                                                                                                                       |                                  |                                             |                                       |             |                                  |
|                                | <u>CIVIL AVIATION</u>                                                                                                 |                                  |                                             |                                       |             |                                  |
| 1                              | CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM                                        | 01/2009                          | 309.46<br>-                                 | 01/2011<br>09/2017                    | 09/2017     | 0/0                              |
| 2                              | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS | 10/2013                          | 314.61<br>-                                 | 09/2018<br>-                          | 06/2020     | 0/0                              |
|                                | Total                                                                                                                 |                                  | 624.07<br>-                                 |                                       |             | 0/0                              |
|                                |                                                                                                                       |                                  |                                             |                                       |             |                                  |
|                                | <u>COAL</u>                                                                                                           |                                  |                                             |                                       |             |                                  |
| 3                              | NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU                                                        | 05/2016                          | 687.28<br>-                                 | 06/2017<br>-                          | 10/2017     | 0/0                              |
| 4                              | HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN                                                      | 03/2015                          | 522.45<br>-                                 | 09/2019<br>-                          | 09/2019     | 0/0                              |
| 5                              | BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN                                                   | 03/2015                          | 513.63<br>-                                 | 12/2019<br>-                          | 12/2019     | 0/0                              |
| 6                              | NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH                                    | 07/2016                          | 17,237.00<br>-                              | 11/2021<br>-                          | 11/2021     | 0/0                              |
| 7                              | COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH                                               | 07/2016                          | 409.87<br>-                                 | 03/2022<br>-                          | 03/2022     | 0/0                              |
| 8                              | VIJAY WEST OPENCAST PROJECT - [N06000158]SECL,CHHATISGARH                                                             | 05/2017                          | 976.95<br>-                                 | 03/2026<br>-                          | 03/2026     | 0/0                              |
|                                | Total                                                                                                                 |                                  | 20,347.18<br>-                              |                                       |             | 0/0                              |
|                                |                                                                                                                       |                                  |                                             |                                       |             |                                  |
|                                | <u>FERTILISERS</u>                                                                                                    |                                  |                                             |                                       |             |                                  |
| 9                              | NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA                                          | 10/2014                          | 197.79<br>209.44                            | 11/2016<br>04/2019                    | 04/2019     | 0/0                              |
|                                | Total                                                                                                                 |                                  | 197.79<br>-                                 |                                       |             | 0/0                              |
|                                |                                                                                                                       |                                  |                                             |                                       |             |                                  |
|                                | <u>STEEL</u>                                                                                                          |                                  |                                             |                                       |             |                                  |
| 10                             | EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND | 02/2014                          | 4,749.00<br>-                               | 09/2017<br>-                          | 09/2017     | 0/0                              |
| 11                             | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA                             | 12/2007                          | 202.61<br>227.00                            | 12/2016<br>-                          | 12/2017     | 0/0                              |
| 12                             | CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT                       | 01/2013                          | 175.00<br>-                                 | -<br>-                                | 12/2017     | 0/0                              |
| 13                             | REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH                                               | 12/2009                          | 343.00<br>-                                 | 10/2016<br>-                          | 03/2018     | 0/0                              |
| 14                             | CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND              | 12/2007                          | 253.92<br>253.92                            | 06/2016<br>-                          | 03/2018     | 0/0                              |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                    |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                            | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                    |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                  | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 15                             | CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND            | 12/2007                       | 200.00<br>-                        | 03/2018<br>-                       | 03/2018     | 0/0                        |
| 16                             | CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND                                                            | 04/2013                       | 170.00<br>-                        | 04/2018<br>-                       | 04/2018     | 0/0                        |
| 17                             | COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH                                                                               | 12/2011                       | 2,858.00<br>-                      | 12/2017<br>-                       | 06/2018     | 0/0                        |
| 18                             | ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH                                                        | 07/2015                       | 465.85<br>-                        | 07/2018<br>-                       | 07/2018     | 0/0                        |
| 19                             | CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN   | 05/2015                       | 189.00<br>-                        | 03/2017<br>-                       | 08/2018     | 0/0                        |
| 20                             | CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH                                                                             | 08/2015                       | 320.66<br>-                        | 08/2018<br>-                       | 08/2018     | 0/0                        |
| 21                             | FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH                                                                                 | 04/2014                       | 1,682.85<br>-                      | 09/2018<br>-                       | 09/2018     | 0/0                        |
| 22                             | CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA   | 04/2014                       | 151.33<br>-                        | 09/2017<br>-                       | 12/2018     | 0/0                        |
| 23                             | CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND                                       | 02/2014                       | 787.29<br>-                        | 12/2016<br>-                       | 12/2018     | 0/0                        |
| 24                             | IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR                                                                                 | 10/2005                       | 956.00<br>-                        | 03/2015<br>-                       | 03/2021     | 0/0                        |
| 25                             | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA                                           | 03/2007                       | 149.73<br>173.00                   | 12/2015<br>-                       | -           | 0/0                        |
| 26                             | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA                                        | 10/2011                       | 175.49<br>206.71                   | 12/2016<br>-                       | -           | 0/0                        |
| 27                             | CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA                                               | 05/2005                       | 768.88<br>1,070.97                 | 02/2014<br>-                       | -           | 0/0                        |
| 28                             | CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA                                    | 07/2011                       | 324.87<br>324.87                   | 12/2015<br>-                       | -           | 0/0                        |
| 29                             | CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH  | 07/2014                       | 232.00<br>-                        | 01/1999<br>-                       | -           | 0/0                        |
| 30                             | CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL | 08/2012                       | 185.37<br>-                        | 03/2016<br>-                       | -           | 0/0                        |
|                                | <b>Total</b>                                                                                                                       |                               | <b>15,340.85</b><br>-              |                                    |             | <b>0/0</b>                 |
|                                |                                                                                                                                    |                               |                                    |                                    |             |                            |
|                                | <b>PETROLEUM</b>                                                                                                                   |                               |                                    |                                    |             |                            |
| 31                             | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA                                                          | 01/2006                       | 993.00<br>-                        | 01/2012<br>-                       | 10/2017     | 0/0                        |
| 32                             | SONAMURA GGS AND PIPELINE PROJECT ( PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC,TRIPURA        | 05/2016                       | 215.38<br>-                        | 06/2017<br>01/2018                 | 01/2018     | 0/0                        |
| 33                             | FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY - [N16000245]IOCL,GUJARAT                                         | 02/2016                       | 931.00<br>-                        | 07/2017<br>-                       | 02/2018     | 0/0                        |
| 34                             | TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM                                                                                | 03/2009                       | 228.64<br>-                        | 12/2016<br>-                       | 03/2018     | 0/0                        |
| 35                             | SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH                                                                  | 03/2009                       | 181.02<br>-                        | 01/2017<br>03/2018                 | 03/2018     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                        | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                              | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 36                             | NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]HPCL, WEST BENGAL                                                              | 08/2014                       | 190.45 -                           | 09/2017<br>03/2018                 | 03/2018     | 0/0                        |
| 37                             | LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC, MAHARASHTRA                                | 12/2015                       | 3,190.69 -                         | 04/2018<br>04/2018                 | 04/2018     | 0/0                        |
| 38                             | PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC, MAHARASHTRA                                                                 | 02/2015                       | 2,899.93 -                         | 05/2017<br>05/2018                 | 05/2018     | 0/0                        |
| 39                             | PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL, MULTI STATE                                                            | 02/2011                       | 913.00<br>1,330.00                 | 06/2018<br>-                       | 06/2018     | 0/0                        |
| 40                             | LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]BPCL, KERALA                         | 05/2015                       | 337.06 -                           | 08/2018<br>-                       | 08/2018     | 0/0                        |
| 41                             | NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC, GUJARAT                                                                     | 11/2014                       | 195.63 -                           | 09/2018<br>09/2018                 | 09/2018     | 0/0                        |
| 42                             | FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC, ANDHRA PRADESH                                  | 04/2017                       | 420.76 -                           | 09/2018<br>09/2018                 | 09/2018     | 0/0                        |
| 43                             | HALDIA LPG IMPORT FACILITY - [N16000223]BPCL, WEST BENGAL                                                                      | 03/2015                       | 694.00 -                           | 10/2018<br>-                       | 10/2018     | 0/0                        |
| 44                             | SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL, MULTI STATE           | 07/2011                       | 352.56 -                           | 03/2017<br>-                       | 11/2018     | 0/0                        |
| 45                             | FUEL QUALITY UPGRADE (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL, BIHAR                                       | 07/2015                       | 822.66 -                           | 11/2018<br>-                       | 11/2018     | 0/0                        |
| 46                             | GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC, GUJARAT                                                                         | 05/2015                       | 1,671.22<br>567.22                 | 11/2019<br>12/2018                 | 12/2018     | 0/0                        |
| 47                             | ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL, TAMIL NADU               | 05/2016                       | 4,497.00 -                         | 12/2018<br>-                       | 12/2018     | 0/0                        |
| 48                             | LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]BPCL, MAHARASHTRA                   | 05/2015                       | 193.40 -                           | 01/2019<br>-                       | 01/2019     | 0/0                        |
| 49                             | INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL, ODISHA                                   | 05/2016                       | 429.00 -                           | 01/2019<br>-                       | 01/2019     | 0/0                        |
| 50                             | MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC, MAHARASHTRA                                                 | 11/2014                       | 6,068.80<br>6,068.80               | 04/2019<br>03/2019                 | 03/2019     | 0/0                        |
| 51                             | ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC, MAHARASHTRA | 01/2015                       | 4,619.94 -                         | 12/2017<br>03/2019                 | 03/2019     | 0/0                        |
| 52                             | Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC, TAMIL NADU                                      | 11/2015                       | 390.52 -                           | 03/2019<br>-                       | 04/2019     | 0/0                        |
| 53                             | CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, MULTI STATE                                                 | 06/2007                       | 736.65 -                           | 09/2011<br>06/2019                 | 06/2019     | 0/0                        |
| 54                             | MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL, MAHARASHTRA                                                               | 09/2015                       | 4,199.00 -                         | 03/2020<br>-                       | 07/2019     | 0/0                        |
| 55                             | BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL, HIMACHAL PRADESH                                                            | 02/2016                       | 151.00 -                           | 09/2019<br>-                       | 09/2019     | 0/0                        |
| 56                             | JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL, MULTI STATE     | 02/2015                       | 890.00 -                           | 10/2019<br>-                       | 10/2019     | 0/0                        |
| 57                             | DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC, D & N HAVELI                                                                      | 08/2014                       | 6,086.08 -                         | 05/2019<br>10/2019                 | 10/2019     | 0/0                        |
| 58                             | INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL, ASSAM                                                                 | 02/2016                       | 2,582.00 -                         | 11/2019<br>-                       | 11/2019     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                 |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|---------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                         | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                 |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                               | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 59                             | AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE                             | 09/2016                       | 571.66<br>-                        | 12/2019<br>-                       | 12/2019     | 0/0                        |
| 60                             | MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA                                                                   | 04/2013                       | 449.58<br>-                        | 12/2019<br>-                       | 12/2019     | 0/0                        |
| 61                             | LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE          | 07/2015                       | 2,881.40<br>-                      | 12/2019<br>-                       | 12/2019     | 0/0                        |
| 62                             | DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA                                                                          | 03/2017                       | 2,253.00<br>-                      | 12/2019<br>-                       | 12/2019     | 0/0                        |
| 63                             | DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE                                                                   | 03/2017                       | 2,250.00<br>-                      | 12/2019<br>-                       | 12/2019     | 0/0                        |
| 64                             | LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA                                                                                 | 12/2016                       | 161.59<br>-                        | 12/2019<br>-                       | 12/2019     | 0/0                        |
| 65                             | GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA                                                                  | 02/2015                       | 749.00<br>-                        | 02/2020<br>-                       | 02/2020     | 0/0                        |
| 66                             | BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]IOCL,BIHAR                                                | 05/2016                       | 664.00<br>-                        | 12/2020<br>-                       | 02/2020     | 0/0                        |
| 67                             | INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA          | 02/2016                       | 554.00<br>-                        | 02/2020<br>-                       | 02/2020     | 0/0                        |
| 68                             | MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA                                 | 02/2016                       | 3,313.00<br>-                      | 02/2020<br>-                       | 02/2020     | 0/0                        |
| 69                             | SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND                                                                             | 02/2017                       | 160.10<br>-                        | 02/2020<br>-                       | 02/2020     | 0/0                        |
| 70                             | NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA                               | 08/2015                       | 2,818.88<br>-                      | 03/2019<br>05/2020                 | 05/2020     | 0/0                        |
| 71                             | PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]ONGC,ASSAM                                                                  | 07/2016                       | 249.85<br>250.00                   | 05/2020<br>-                       | 05/2020     | 0/0                        |
| 72                             | ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU                                                                 | 05/2013                       | 711.00<br>-                        | 06/2020<br>-                       | 06/2020     | 0/0                        |
| 73                             | KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH                                                     | 03/2016                       | 34,012.00<br>-                     | 06/2020<br>06/2020                 | 06/2020     | 0/0                        |
| 74                             | MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL,BIHAR                                                                            | 09/2015                       | 324.00<br>-                        | 06/2020<br>-                       | 06/2020     | 0/0                        |
| 75                             | VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH                                                          | 07/2016                       | 20,928.00<br>-                     | 07/2020<br>-                       | 07/2020     | 0/0                        |
| 76                             | INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL,GUJARAT               | 09/2016                       | 208.35<br>-                        | 07/2020<br>-                       | 07/2020     | 0/0                        |
| 77                             | PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE                                                                        | 01/2015                       | 2,321.00<br>-                      | 12/2020<br>-                       | 08/2020     | 0/0                        |
| 78                             | PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE                                                | 05/2016                       | 406.00<br>-                        | 10/2020<br>-                       | 10/2020     | 0/0                        |
| 79                             | AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE | 01/2015                       | 1,823.00<br>-                      | 12/2020<br>-                       | 12/2020     | 0/0                        |
| 80                             | HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL                                                                   | 04/2016                       | 1,021.00<br>-                      | 12/2020<br>-                       | 12/2020     | 0/0                        |
| 81                             | BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE                                                                     | 03/2017                       | 3,212.00<br>-                      | 12/2020<br>-                       | 12/2020     | 0/0                        |
| 82                             | DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL                                                                  | 03/2017                       | 1,828.00<br>-                      | 12/2020<br>-                       | 12/2020     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                      |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                      |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                    | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 83                             | ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA      | 05/2016                       | 212.00<br>-                        | 01/2021<br>-                       | 01/2021     | 0/0                        |
| 84                             | ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA    | 05/2016                       | 348.00<br>-                        | 01/2021<br>-                       | 01/2021     | 0/0                        |
| 85                             | ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA | 05/2016                       | 261.00<br>-                        | 01/2021<br>-                       | 01/2021     | 0/0                        |
| 86                             | ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH             | 01/2015                       | 342.00<br>-                        | 03/2021<br>-                       | 03/2021     | 0/0                        |
| 87                             | REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH                                                   | 07/2014                       | 247.00<br>-                        | 03/2021<br>-                       | 03/2021     | 0/0                        |
| 88                             | KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA                                                                     | 05/2016                       | 1,945.00<br>-                      | 08/2021<br>-                       | 08/2021     | 0/0                        |
| 89                             | DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND                                                                   | 12/2015                       | 658.62<br>910.23                   | 03/2023<br>03/2022                 | 03/2022     | 0/0                        |
| 90                             | REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT                                                                             | 02/2017                       | 1,162.56<br>1,162.56               | 03/2026<br>03/2026                 | 03/2026     | 0/0                        |
| 91                             | IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU                                                                         | 11/2012                       | 678.00<br>-                        | 02/2017<br>-                       | -           | 0/0                        |
|                                | Total                                                                                                                                |                               | 1,34,804.98<br>-                   |                                    |             | 0/0                        |
|                                |                                                                                                                                      |                               |                                    |                                    |             |                            |
|                                | <u>POWER</u>                                                                                                                         |                               |                                    |                                    |             |                            |
| 92                             | PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND                                                                       | 10/2004                       | 4,237.96<br>4,552.00               | 10/2017<br>12/2016                 | 10/2017     | 0/0                        |
| 93                             | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH                                             | 01/2016                       | 305.04<br>-                        | 03/2017<br>10/2017                 | 11/2017     | 0/0                        |
| 94                             | TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]PGCIL,GUJARAT                                    | 01/2016                       | 244.19<br>-                        | 07/2018<br>-                       | 11/2017     | 0/0                        |
| 95                             | TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL,MULTI STATE                        | 04/2015                       | 2,525.00<br>-                      | 11/2017<br>-                       | 11/2017     | 0/0                        |
| 96                             | TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-A - [N18000260]PGCIL,MULTI STATE                                     | 04/2015                       | 2,525.00<br>-                      | 11/2017<br>-                       | 11/2017     | 0/0                        |
| 97                             | UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE                                                   | 01/2014                       | 374.63<br>-                        | 04/2016<br>12/2017                 | 12/2017     | 0/0                        |
| 98                             | CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU                       | 01/2016                       | 162.11<br>-                        | 05/2018<br>-                       | 12/2017     | 0/0                        |
| 99                             | ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE                                  | 03/2012                       | 198.63<br>-                        | 09/2014<br>09/2017                 | 01/2018     | 0/0                        |
| 100                            | TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]PGCIL,MAHARASHTRA                                     | 04/2015                       | 2,225.00<br>2,225.00               | 01/2018<br>-                       | 01/2018     | 0/0                        |
| 101                            | ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE  | 03/2015                       | 197.40<br>-                        | 03/2018<br>-                       | 03/2018     | 0/0                        |
| 102                            | 50 MW SOLAR POWER PROJECT - [N18000251]NHPC,TAMIL NADU                                                                               | 09/2017                       | 287.48<br>-                        | 03/2018<br>-                       | 03/2018     | 0/0                        |
| 103                            | TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE                    | 03/2015                       | 955.00<br>1,161.00                 | 12/2015<br>-                       | 03/2018     | 0/0                        |



## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                     |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|-------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                             | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                     |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                   | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 104                            | TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM CUDDALORE AREA – PACKAGE A - [N18000259]PGCIL,MULTI STATE                  | 03/2015                       | 955.00<br>1,161.00                 | 12/2015<br>-                       | 03/2018     | 0/0                        |
| 105                            | INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE                                                           | 03/2015                       | 1,071.24<br>-                      | 09/2017<br>-                       | 04/2018     | 0/0                        |
| 106                            | EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL                                                               | 04/2016                       | 454.11<br>-                        | 04/2018<br>-                       | 04/2018     | 0/0                        |
| 107                            | NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]PGCIL,TRIPURA                                                             | 05/2016                       | 409.19<br>-                        | 05/2018<br>-                       | 05/2018     | 0/0                        |
| 108                            | TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN                                              | 07/2015                       | 307.18<br>-                        | 11/2017<br>-                       | 06/2018     | 0/0                        |
| 109                            | S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH      | 04/2016                       | 287.99<br>-                        | 06/2018<br>-                       | 06/2018     | 0/0                        |
| 110                            | TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL,MADHYA PRADESH                                   | 02/2015                       | 1,750.00<br>-                      | 06/2018<br>-                       | 06/2018     | 0/0                        |
| 111                            | GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE                              | 07/2015                       | 2,247.37<br>-                      | 07/2018<br>-                       | 07/2018     | 0/0                        |
| 112                            | SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE                                                         | 01/2016                       | 1,455.47<br>-                      | 07/2018<br>-                       | 07/2018     | 0/0                        |
| 113                            | REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL,ANDHRA PRADESH                              | 01/2016                       | 207.88<br>-                        | 07/2018<br>-                       | 07/2018     | 0/0                        |
| 114                            | WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE                                                              | 07/2016                       | 150.99<br>-                        | 07/2018<br>-                       | 07/2018     | 0/0                        |
| 115                            | TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS-KARGIL-KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR      | 01/2014                       | 1,788.41<br>-                      | 09/2017<br>-                       | 09/2018     | 0/0                        |
| 116                            | CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI                        | 05/2015                       | 780.33<br>-                        | 10/2018<br>-                       | 10/2018     | 0/0                        |
| 117                            | EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE                                                               | 05/2016                       | 766.21<br>-                        | 11/2018<br>-                       | 11/2018     | 0/0                        |
| 118                            | EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL,MULTI STATE                                                              | 05/2016                       | 167.01<br>-                        | 11/2018<br>-                       | 11/2018     | 0/0                        |
| 119                            | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]PGCIL,MULTI STATE                | 04/2016                       | 810.48<br>-                        | 12/2018<br>-                       | 12/2018     | 0/0                        |
| 120                            | TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT                                   | 07/2016                       | 300.94<br>-                        | 12/2018<br>-                       | 12/2018     | 0/0                        |
| 121                            | TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJASTHAN - [N18000227]PGCIL,RAJASTHAN                                                 | 07/2016                       | 1,429.38<br>-                      | 01/2019<br>-                       | 01/2019     | 0/0                        |
| 122                            | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE    | 10/2016                       | 408.46<br>-                        | 01/2019<br>-                       | 01/2019     | 0/0                        |
| 123                            | PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL,MULTI STATE                                     | 08/2016                       | 431.89<br>-                        | 02/2019<br>-                       | 02/2019     | 0/0                        |
| 124                            | PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL,MULTI STATE                                                      | 08/2016                       | 177.52<br>-                        | 02/2019<br>-                       | 02/2019     | 0/0                        |
| 125                            | ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE | 02/2017                       | 322.30<br>-                        | 02/2019<br>-                       | 02/2019     | 0/0                        |
| 126                            | TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE | 03/2016                       | 808.63<br>-                        | 01/2018<br>-                       | 03/2019     | 0/0                        |
| 127                            | POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL,MULTI STATE | 07/2016                       | 333.17<br>-                        | 03/2019<br>-                       | 03/2019     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                     |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|-------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                             | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                     |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                   | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 128                            | SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE                                                             | 09/2016                       | 562.25<br>-                        | 03/2019<br>-                       | 03/2019     | 0/0                        |
| 129                            | PG WORK ASSOCIATED WITH TCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243]PGCIL,MULTI STATE   | 03/2017                       | 162.31<br>-                        | 03/2019<br>-                       | 03/2019     | 0/0                        |
| 130                            | PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA             | 04/2016                       | 844.64<br>-                        | 04/2019<br>-                       | 04/2019     | 0/0                        |
| 131                            | AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]PGCIL,MULTI STATE                                           | 10/2016                       | 167.75<br>-                        | 04/2019<br>-                       | 04/2019     | 0/0                        |
| 132                            | SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE                | 10/2016                       | 608.24<br>-                        | 04/2019<br>-                       | 04/2019     | 0/0                        |
| 133                            | STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE                                                 | 12/2015                       | 3,654.00<br>-                      | 04/2019<br>-                       | 04/2019     | 0/0                        |
| 134                            | GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE                                      | 05/2016                       | 3,519.59<br>-                      | 05/2019<br>-                       | 05/2019     | 0/0                        |
| 135                            | ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR                                                       | 04/2016                       | 790.13<br>-                        | 06/2019<br>-                       | 06/2019     | 0/0                        |
| 136                            | INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE           | 03/2017                       | 251.60<br>-                        | 06/2019<br>-                       | 06/2019     | 0/0                        |
| 137                            | EASTERN REGION STRENGTHENING SCHEME XVII( PART B) - [N18000244]PGCIL,MULTI STATE                                                    | 02/2017                       | 235.53<br>-                        | 06/2019<br>-                       | 06/2019     | 0/0                        |
| 138                            | SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE                                               | 03/2017                       | 337.75<br>-                        | 06/2019<br>-                       | 06/2019     | 0/0                        |
| 139                            | WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL,MULTI STATE                                                             | 02/2017                       | 204.12<br>-                        | 09/2019<br>-                       | 09/2019     | 0/0                        |
| 140                            | HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE | 05/2016                       | 14,733.37<br>-                     | 11/2019<br>-                       | 11/2019     | 0/0                        |
| 141                            | S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE | 03/2017                       | 283.72<br>-                        | 11/2019<br>-                       | 11/2019     | 0/0                        |
| 142                            | SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE                                                   | 03/2017                       | 379.95<br>-                        | 12/2019<br>-                       | 12/2019     | 0/0                        |
| 143                            | COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE        | 12/2014                       | 4,754.42<br>-                      | 12/2018<br>-                       | 12/2019     | 0/0                        |
| 144                            | NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE                   | 12/2014                       | 5,111.33<br>-                      | 12/2018<br>-                       | 12/2019     | 0/0                        |
| 145                            | WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE                                                            | 02/2017                       | 195.05<br>-                        | 02/2020<br>-                       | 02/2020     | 0/0                        |
| 146                            | HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE | 02/2017                       | 5,070.13<br>-                      | 04/2020<br>-                       | 04/2020     | 0/0                        |
| 147                            | EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE                                                            | 03/2017                       | 3,500.00<br>3,500.00               | 07/2020<br>-                       | 07/2020     | 0/0                        |
| 148                            | PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR                                                    | 10/2014                       | 8,112.12<br>-                      | 04/2020<br>-                       | 05/2023     | 0/0                        |
| 149                            | SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH                                                         | 09/2003                       | 6,285.33<br>-                      | 09/2010<br>-                       | -           | 0/0                        |
|                                | Total                                                                                                                               |                               | 91,821.92<br>-                     |                                    |             | 0/0                        |
|                                |                                                                                                                                     |                               |                                    |                                    |             |                            |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                            |                               |                                    | (September 2017)                   |         |                            |
|--------------------------------|------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|---------|----------------------------|
| SI.No                          | Project                                                                                                    | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |         | Milestones Achieved/ Total |
| 1                              | 2                                                                                                          | 3                             | 4                                  | 5                                  | 6       | 7                          |
|                                | <u>HEAVY INDUSTRY</u>                                                                                      |                               |                                    |                                    |         |                            |
| 150                            | NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]NATIS,MULTI STATE          | 04/2011                       | 1,718.00 -                         | 09/2011 -                          | 12/2017 | 0/0                        |
|                                | Total                                                                                                      |                               | 1,718.00 -                         |                                    |         | 0/0                        |
|                                |                                                                                                            |                               |                                    |                                    |         |                            |
|                                | <u>HEALTH AND FAMILY WELFARE</u>                                                                           |                               |                                    |                                    |         |                            |
| 151                            | CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL                                                    | 08/2016                       | 244.00 -                           | 09/2018 -                          | 09/2018 | 0/0                        |
| 152                            | NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC, MEGHALAYA                                                   | 10/2016                       | 363.99 -                           | 05/2018<br>08/2019                 | 08/2019 | 0/0                        |
| 153                            | LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC, DELHI                                                     | 02/2013                       | 414.11 -                           | 11/2013 -                          | -       | 0/0                        |
| 154                            | SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC, DELHI             | 09/2013                       | 444.70 -                           | 12/2015 -                          | -       | 0/0                        |
| 155                            | SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC, DELHI           | 11/2013                       | 196.70 -                           | 01/2016 -                          | -       | 0/0                        |
| 156                            | LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC, ASSAM                                                             | 07/2012                       | 175.57 -                           | 12/2014 -                          | -       | 0/0                        |
|                                | Total                                                                                                      |                               | 1,839.07 -                         |                                    |         | 0/0                        |
|                                |                                                                                                            |                               |                                    |                                    |         |                            |
|                                | <u>RAILWAYS</u>                                                                                            |                               |                                    |                                    |         |                            |
| 157                            | LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR, ASSAM | 04/2003                       | 971.22 -                           | - -                                | 12/2009 | 0/0                        |
| 158                            | NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR, ASSAM                                                 | 04/2007                       | 180.09 -                           | - -                                | 05/2011 | 0/0                        |
| 159                            | ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR, MULTI STATE                           | 12/2006                       | 170.00 -                           | 03/2011 -                          | 10/2011 | 0/0                        |
| 160                            | HARMUTI-NAHARLAGUN - [N22000382]NFR, MULTI STATE                                                           | 04/2006                       | 614.54 -                           | - -                                | 03/2014 | 0/0                        |
| 161                            | DUDHNOI-MENDHIPATHAR - [N22000378]NFR, MULTI STATE                                                         | 04/1992                       | 315.64 -                           | - -                                | 11/2014 | 0/0                        |
| 162                            | RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR, ASSAM                                      | 04/2003                       | 4,300.00 -                         | - -                                | 08/2015 | 0/0                        |
| 163                            | CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA                                       | 04/1999                       | 895.00 -                           | 03/2007 -                          | 04/2016 | 0/0                        |
| 164                            | KATAKHAL TO BHAIRABI - [N22000126]NFR, ASSAM                                                               | 04/1998                       | 227.90 -                           | 12/2012 -                          | 05/2016 | 0/0                        |
| 165                            | TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL, WEST BENGAL                                            | 04/2010                       | 171.02 -                           | 06/2013 -                          | 12/2016 | 0/0                        |
| 166                            | CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER, MULTI STATE                               | 03/2007                       | 243.78 -                           | - -                                | 08/2017 | 0/0                        |
| 167                            | BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH                                             | 03/2008                       | 195.64 -                           | - -                                | 10/2017 | 0/0                        |
| 168                            | NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, ANDHRA PRADESH                                             | 03/1996                       | 155.74<br>164.36                   | 02/2009 -                          | 12/2017 | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                        | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                              | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 169                            | UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT                                                      | 04/2008                       | 1,389.62 -                         | 03/2014 -                          | 12/2017     | 0/0                        |
| 170                            | MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND                                                             | 04/2012                       | 258.20 -                           | - -                                | 12/2017     | 0/0                        |
| 171                            | ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA                                                                                      | 04/2010                       | 189.24 -                           | - -                                | 12/2017     | 0/0                        |
| 172                            | ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA                                                                          | 10/1998                       | 550.00 -                           | - -                                | 01/2018     | 0/0                        |
| 173                            | MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR                                                                          | 04/2003                       | 218.19 -                           | - -                                | 03/2018     | 0/0                        |
| 174                            | BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH                                                                  | 09/2007                       | 687.20 -                           | 03/2010 -                          | 03/2018     | 0/0                        |
| 175                            | LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM                                  | 04/1996                       | 1,676.31 -                         | 03/2009 -                          | 03/2018     | 0/0                        |
| 176                            | AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH                                                          | 03/2012                       | 199.75 -                           | - -                                | 03/2018     | 0/0                        |
| 177                            | NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL                                                                       | 04/2011                       | 209.77 -                           | - -                                | 03/2018     | 0/0                        |
| 178                            | NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE | 04/1999                       | 523.17 -                           | - -                                | 03/2018     | 0/0                        |
| 179                            | MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN                                                             | 01/2011                       | 493.17 -                           | 03/2018 -                          | 03/2018     | 0/0                        |
| 180                            | MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH                                                  | 01/2013                       | 387.70 -                           | 03/2018 -                          | 03/2018     | 0/0                        |
| 181                            | MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH                                                        | 05/2014                       | 207.00 -                           | 03/2018 -                          | 03/2018     | 0/0                        |
| 182                            | MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN                                        | 04/2013                       | 456.00 -                           | - -                                | 05/2018     | 0/0                        |
| 183                            | BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM                                                            | 09/1997                       | 1,500.00 -                         | 04/2008 12/2011                    | 06/2018     | 0/0                        |
| 184                            | EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL                                        | 03/2013                       | 4,874.58 -                         | 03/2016 -                          | 06/2018     | 0/0                        |
| 185                            | DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN                                                                         | 02/1997                       | 410.08 -                           | - -                                | 08/2018     | 0/0                        |
| 186                            | CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE                                                                                 | 03/2013                       | 295.00 -                           | - -                                | 10/2018     | 0/0                        |
| 187                            | THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN                                                                                  | 04/2013                       | 236.93 -                           | - -                                | 10/2018     | 0/0                        |
| 188                            | RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN                                                                      | 04/2012                       | 288.97 335.53                      | - -                                | 10/2018     | 0/0                        |
| 189                            | HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE                                         | 04/2010                       | 157.94 -                           | - -                                | 11/2018     | 0/0                        |
| 190                            | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR                                                          | 03/1995                       | 2,500.00 -                         | 11/2002 -                          | 12/2018     | 0/0                        |
| 191                            | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL                | 04/2010                       | 2,913.51 -                         | 03/2016 -                          | 12/2018     | 0/0                        |
| 192                            | MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA                                              | 04/2012                       | 632.68 -                           | 03/2016 -                          | 12/2018     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                         |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|-------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                 | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                         |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                       | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 193                            | MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE                                                          | 04/1997                       | 218.24<br>236.41                   | -<br>-                             | 03/2019     | 0/0                        |
| 194                            | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE                                   | 04/2000                       | 733.00<br>-                        | 12/2008<br>-                       | 03/2019     | 0/0                        |
| 195                            | TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL                                                | 04/2000                       | 1,188.91<br>-                      | -<br>12/2009                       | 03/2019     | 0/0                        |
| 196                            | HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA                                                                       | 04/1996                       | 301.64<br>-                        | -<br>09/2009                       | 03/2019     | 0/0                        |
| 197                            | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM                                 | 09/2006                       | 200.00<br>-                        | -<br>-                             | 03/2019     | 0/0                        |
| 198                            | MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA                                                  | 04/2008                       | 5,300.00<br>-                      | 03/2014<br>-                       | 03/2019     | 0/0                        |
| 199                            | BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT                                       | 04/2008                       | 318.24<br>-                        | 03/2012<br>-                       | 03/2019     | 0/0                        |
| 200                            | BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR, RAJASTHAN                                                            | 04/2012                       | 246.08<br>-                        | -<br>-                             | 03/2019     | 0/0                        |
| 201                            | RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR, GUJARAT | 04/1994                       | 320.66<br>-                        | -<br>-                             | 03/2019     | 0/0                        |
| 202                            | VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR, GUJARAT                                                                       | 04/2011                       | 446.00<br>-                        | -<br>-                             | 03/2019     | 0/0                        |
| 203                            | AJMER-BANGURGRAM - [N22000155]NWR, RAJASTHAN                                                                            | 04/2011                       | 213.39<br>-                        | -<br>-                             | 03/2019     | 0/0                        |
| 204                            | ALWAR-BANDIKUI DOUBLING - [N22000157]NWR, RAJASTHAN                                                                     | 04/2013                       | 242.09<br>-                        | -<br>-                             | 03/2019     | 0/0                        |
| 205                            | NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE                                                  | 04/2013                       | 1,798.00<br>-                      | -<br>-                             | 03/2019     | 0/0                        |
| 206                            | NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL                                           | 04/2012                       | 283.55<br>-                        | -<br>-                             | 03/2019     | 0/0                        |
| 207                            | AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM                                                                | 04/2011                       | 312.12<br>-                        | -<br>-                             | 03/2019     | 0/0                        |
| 208                            | LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR, ASSAM                                                            | 04/2012                       | 246.07<br>-                        | -<br>-                             | 03/2019     | 0/0                        |
| 209                            | THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL, TAMIL NADU     | 04/2011                       | 190.10<br>-                        | -<br>-                             | 03/2019     | 0/0                        |
| 210                            | LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL, UTTAR PRADESH                                            | 04/2011                       | 927.01<br>-                        | 03/2019<br>-                       | 03/2019     | 0/0                        |
| 211                            | BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA                                                                | 03/2009                       | 942.95<br>-                        | 03/2019<br>-                       | 03/2019     | 0/0                        |
| 212                            | KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH                                                     | 08/2015                       | 528.57<br>-                        | 03/2018<br>-                       | 03/2019     | 0/0                        |
| 213                            | MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI, MAHARASHTRA                                                 | 10/2013                       | 305.00<br>-                        | 03/2019<br>-                       | 03/2019     | 0/0                        |
| 214                            | MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]CCOI, RAJASTHAN                                                   | 04/2012                       | 471.82<br>-                        | 03/2019<br>-                       | 03/2019     | 0/0                        |
| 215                            | MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI, HARYANA                                                          | 12/2015                       | 346.32<br>-                        | 03/2019<br>-                       | 03/2019     | 0/0                        |
| 216                            | MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI, MADHYA PRADESH                                                    | 12/2015                       | 174.00<br>-                        | 03/2019<br>-                       | 03/2019     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                               |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|-----------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                       | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                               |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                             | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 217                            | MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI, GUJARAT                              | 10/2013                       | 343.00<br>-                        | 03/2019<br>-                       | 03/2019     | 0/0                        |
| 218                            | MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI, ANDHRA PRADESH                      | 08/2016                       | 234.50<br>-                        | 03/2019<br>-                       | 03/2019     | 0/0                        |
| 219                            | HATHUA-BHATNI (N L) (NER) - [220100319]NER, MULTI STATE                                       | 04/2005                       | 230.03<br>-                        | -<br>-                             | 05/2019     | 0/0                        |
| 220                            | JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]NWR, RAJASTHAN | 04/2008                       | 653.19<br>-                        | 03/2014<br>-                       | 06/2019     | 0/0                        |
| 221                            | GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE                                     | 02/1997                       | 386.30<br>-                        | 03/1998<br>-                       | 12/2019     | 0/0                        |
| 222                            | SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA                                     | 04/1998                       | 183.23<br>-                        | 02/2015<br>-                       | 12/2019     | 0/0                        |
| 223                            | HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR) - [N22000112]NWR, RAJASTHAN                      | 04/2008                       | 829.74<br>-                        | 03/2015<br>-                       | 12/2019     | 0/0                        |
| 224                            | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA              | 03/1996                       | 495.44<br>1,781.98                 | 03/2004<br>-                       | 03/2020     | 0/0                        |
| 225                            | MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, JHARKHAND                                | 04/1995                       | 900.05<br>-                        | 12/2011<br>12/2010                 | 03/2020     | 0/0                        |
| 226                            | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR                                 | 04/2003                       | 727.56<br>-                        | 03/2011<br>-                       | 03/2020     | 0/0                        |
| 227                            | OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH                          | 07/2006                       | 743.00<br>-                        | 03/2008<br>06/2008                 | 03/2020     | 0/0                        |
| 228                            | NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR              | 09/2006                       | 300.00<br>-                        | -<br>-                             | 03/2020     | 0/0                        |
| 229                            | AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA                                          | 04/2008                       | 813.34<br>-                        | 03/2014<br>-                       | 03/2020     | 0/0                        |
| 230                            | BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM                                          | 04/2008                       | 619.34<br>-                        | 04/2014<br>-                       | 03/2020     | 0/0                        |
| 231                            | SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM                                                   | 04/2008                       | 1,339.48<br>-                      | 12/2015<br>-                       | 03/2020     | 0/0                        |
| 232                            | AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT                                   | 04/2008                       | 394.14<br>-                        | 03/2013<br>-                       | 03/2020     | 0/0                        |
| 233                            | NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND     | 04/2006                       | 850.00<br>-                        | 03/2015<br>-                       | 03/2020     | 0/0                        |
| 234                            | AHMEDABAD-BOTAD (GC) - [N22000140]RVNL, GUJARAT                                               | 04/2012                       | 567.18<br>-                        | -<br>-                             | 03/2020     | 0/0                        |
| 235                            | DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND                                                   | 04/2013                       | 4,274.00<br>-                      | -<br>-                             | 03/2020     | 0/0                        |
| 236                            | MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE                                        | 04/2011                       | 165.82<br>-                        | -<br>-                             | 03/2020     | 0/0                        |
| 237                            | VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH        | 03/2012                       | 1,503.71<br>-                      | -<br>-                             | 03/2020     | 0/0                        |
| 238                            | SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA                              | 03/2012                       | 155.81<br>-                        | -<br>-                             | 03/2020     | 0/0                        |
| 239                            | PHULERA - DIGANA DOUBLING - [N22000326]NWR, MULTI STATE                                       | 05/2015                       | 600.00<br>-                        | -<br>-                             | 03/2020     | 0/0                        |
| 240                            | YELAHANKA-PENUKONDA - [N22000328]SWR, MULTI STATE                                             | 05/2015                       | 860.43<br>-                        | -<br>-                             | 03/2020     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                            |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|----------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                    | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                            |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                          | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 241                            | BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA                                              | 04/2015                       | 1,172.92 -                         | 03/2021 -                          | 03/2020     | 0/0                        |
| 242                            | ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA                                                              | 11/2015                       | 969.83 -                           | 03/2020 -                          | 03/2020     | 0/0                        |
| 243                            | DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA         | 03/2009                       | 1,514.45 -                         | 03/2020 -                          | 03/2020     | 0/0                        |
| 244                            | SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA                                                                  | 03/2006                       | 960.18 -                           | 03/2020 -                          | 03/2020     | 0/0                        |
| 245                            | RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH                                                                | 03/2007                       | 758.09 -                           | 03/2020 -                          | 03/2020     | 0/0                        |
| 246                            | RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH                                                                  | 08/2015                       | 2,436.21 -                         | 03/2020 -                          | 03/2020     | 0/0                        |
| 247                            | EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA                 | 04/2016                       | 5,200.00 -                         | 03/2020 -                          | 03/2020     | 0/0                        |
| 248                            | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL | 04/2010                       | 3,951.98 -                         | 03/2016 -                          | 12/2020     | 0/0                        |
| 249                            | DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT                                                                              | 04/2012                       | 376.59 -                           | -                                  | 12/2020     | 0/0                        |
| 250                            | PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT                                                                        | 04/2013                       | 1,266.89 -                         | -                                  | 12/2020     | 0/0                        |
| 251                            | BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH                                             | 03/2012                       | 1,183.25 -                         | 12/2020 -                          | 12/2020     | 0/0                        |
| 252                            | BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH                                                              | 04/2011                       | 1,485.65 -                         | 12/2020 -                          | 12/2020     | 0/0                        |
| 253                            | KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH                                                             | 12/2001                       | 330.00 -                           | -                                  | 03/2021     | 0/0                        |
| 254                            | RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH                                                               | 04/2001                       | 470.92 727.13                      | -                                  | 03/2021     | 0/0                        |
| 255                            | NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA                                                           | 04/2010                       | 4,083.02 -                         | -                                  | 03/2021     | 0/0                        |
| 256                            | KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA                                                                         | 04/2011                       | 277.70 792.89                      | -                                  | 03/2021     | 0/0                        |
| 257                            | SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA                                                                        | 03/2011                       | 679.27 -                           | -                                  | 03/2021     | 0/0                        |
| 258                            | BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA                                                                       | 03/2013                       | 858.67 -                           | -                                  | 03/2021     | 0/0                        |
| 259                            | KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE                                                                              | 04/2015                       | 2,063.03 -                         | -                                  | 03/2021     | 0/0                        |
| 260                            | JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA                                                                        | 04/2015                       | 1,547.38 -                         | 03/2021 -                          | 03/2021     | 0/0                        |
| 261                            | JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA                               | 04/2015                       | 701.61 -                           | 03/2021 -                          | 03/2021     | 0/0                        |
| 262                            | BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM                                                               | 04/2015                       | 2,232.32 -                         | -                                  | 03/2021     | 0/0                        |
| 263                            | DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM                                                                               | 04/2015                       | 870.96 -                           | -                                  | 03/2021     | 0/0                        |
| 264                            | SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT                                                                              | 04/2015                       | 1,002.39 -                         | -                                  | 03/2021     | 0/0                        |



## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                              |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                      | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                              |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                            | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 265                            | BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND                                                                        | 03/2016                       | 1,724.20<br>-                      | 03/2021<br>-                       | 03/2021     | 0/0                        |
| 266                            | KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA                                                                        | 04/1994                       | 470.21<br>-                        | -<br>-                             | 06/2021     | 0/0                        |
| 267                            | TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER, WEST BENGAL | 01/1991                       | 763.18<br>-                        | 12/2021<br>-                       | 12/2021     | 0/0                        |
| 268                            | RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA         | 04/1995                       | 524.43<br>-                        | 12/2021<br>-                       | 12/2021     | 0/0                        |
| 269                            | RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA                                                         | 09/2016                       | 1,273.00<br>1,908.00               | 12/2021<br>-                       | 12/2021     | 0/0                        |
| 270                            | DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE                                                 | 04/2007                       | 1,640.04<br>-                      | -<br>-                             | 03/2022     | 0/0                        |
| 271                            | WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA                                                                     | 04/2012                       | 297.85<br>540.02                   | -<br>-                             | 03/2022     | 0/0                        |
| 272                            | ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH                                                           | 03/2015                       | 1,750.00<br>-                      | 03/2022<br>-                       | 03/2022     | 0/0                        |
| 273                            | WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA                                                            | 02/2015                       | 630.00<br>1,272.19                 | -<br>-                             | 03/2022     | 0/0                        |
| 274                            | WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA                                                               | 02/2016                       | 912.00<br>637.95                   | -<br>-                             | 03/2022     | 0/0                        |
| 275                            | KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH                                                               | 04/2015                       | 2,499.71<br>-                      | 03/2021<br>-                       | 03/2022     | 0/0                        |
| 276                            | KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA                                                                    | 04/2015                       | 2,361.74<br>-                      | 03/2021<br>-                       | 03/2022     | 0/0                        |
| 277                            | TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA                                                                        | 04/2005                       | 810.78<br>-                        | -<br>-                             | 12/2022     | 0/0                        |
| 278                            | GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE                                                  | 04/2011                       | 1,176.09<br>-                      | 02/2020<br>-                       | 12/2022     | 0/0                        |
| 279                            | DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE   | 04/2010                       | 622.41<br>-                        | 02/2019<br>-                       | 12/2022     | 0/0                        |
| 280                            | WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA                                                                        | 04/2008                       | 499.30<br>2,491.43                 | -<br>-                             | 03/2023     | 0/0                        |
| 281                            | ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA                                                         | 02/2015                       | 2,326.00<br>2,449.91               | -<br>-                             | 03/2023     | 0/0                        |
| 282                            | VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH                                                       | 04/2015                       | 750.55<br>-                        | 12/2024<br>-                       | 12/2024     | 0/0                        |
| 283                            | SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA                                                               | 04/2015                       | 728.10<br>-                        | 12/2024<br>-                       | 12/2024     | 0/0                        |
| 284                            | VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA                                                                   | 01/1991                       | 2,335.67<br>-                      | -<br>-                             | 12/2024     | 0/0                        |
| 285                            | MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH                                                               | 04/2015                       | 1,765.90<br>-                      | 12/2025<br>-                       | 12/2025     | 0/0                        |
| 286                            | DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA                                                                            | 04/2015                       | 723.78<br>-                        | 12/2025<br>-                       | 12/2025     | 0/0                        |
| 287                            | RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND                                                               | 04/2011                       | 4,295.30<br>-                      | 12/2026<br>-                       | 12/2026     | 0/0                        |
| 288                            | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE                                               | 04/1986                       | 158.77<br>274.56                   | 03/1994<br>-                       | -           | 0/0                        |



## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                              |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|--------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                      | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                              |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                            | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 289                            | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA                                            | 12/1994                       | 124.43<br>-                        | -<br>-                             | -           | 0/0                        |
| 290                            | AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA                                                          | 06/1994                       | 663.01<br>668.34                   | 06/1999<br>-                       | -           | 0/0                        |
| 291                            | NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL         | 04/1983                       | 36.80<br>274.41                    | -<br>-                             | -           | 0/0                        |
| 292                            | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH               | 04/1995                       | 304.00<br>-                        | 12/2012<br>-                       | -           | 0/0                        |
| 293                            | CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE                                                      | 02/1996                       | 240.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 294                            | AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA                                                 | 02/1997                       | 514.68<br>-                        | -<br>-                             | -           | 0/0                        |
| 295                            | NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE                                                         | 03/1981                       | 450.00<br>-                        | 07/2012<br>-                       | -           | 0/0                        |
| 296                            | KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU                                                                | 02/1997                       | 155.55<br>-                        | -<br>-                             | -           | 0/0                        |
| 297                            | HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA                                                              | 04/1997                       | 227.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 298                            | KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH                                                | 03/1997                       | 677.97<br>1,062.36                 | -<br>-                             | -           | 0/0                        |
| 299                            | HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL                                                | 04/1974                       | 393.46<br>154.30                   | 03/2007<br>03/2007                 | -           | 0/0                        |
| 300                            | RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND                                                          | 04/1997                       | 194.07<br>-                        | 06/2004<br>-                       | -           | 0/0                        |
| 301                            | MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA                                                        | 07/1998                       | 125.00<br>-                        | 07/2008<br>-                       | -           | 0/0                        |
| 302                            | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR                                             | 04/1997                       | 501.69<br>335.77                   | 03/2012<br>-                       | -           | 0/0                        |
| 303                            | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH                                    | 04/1999                       | 108.00<br>-                        | 12/2009<br>-                       | -           | 0/0                        |
| 304                            | KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR                                                          | 09/2001                       | 492.98<br>-                        | 12/2010<br>-                       | -           | 0/0                        |
| 305                            | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR                                                 | 04/1997                       | 162.87<br>-                        | -<br>-                             | -           | 0/0                        |
| 306                            | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE                                           | 03/2002                       | 625.30<br>408.76                   | 06/2007<br>-                       | -           | 0/0                        |
| 307                            | TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU                                           | 09/1995                       | 100.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 308                            | TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MTP,WEST BENGAL | 03/2000                       | 1,049.69<br>-                      | 12/2006<br>-                       | -           | 0/0                        |
| 309                            | GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE                                                      | 04/1998                       | 92.63<br>-                         | 02/2011<br>-                       | -           | 0/0                        |
| 310                            | DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE                                                   | 04/2000                       | 607.09<br>-                        | 12/2012<br>12/2012                 | -           | 0/0                        |
| 311                            | BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA                                                | 04/1996                       | 138.00<br>1,382.78                 | -<br>-                             | -           | 0/0                        |
| 312                            | JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA                                                                 | 01/2004                       | 238.56<br>-                        | 03/2012<br>-                       | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                 |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|---------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                         | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                 |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                               | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 313                            | HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR                                                                   | 04/2003                       | 528.65<br>-                        | -<br>-                             | -           | 0/0                        |
| 314                            | KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR                                                                                    | 04/2002                       | 322.95<br>-                        | 03/2012<br>-                       | -           | 0/0                        |
| 315                            | KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND                                                                            | 04/2002                       | 459.91<br>-                        | -<br>-                             | -           | 0/0                        |
| 316                            | DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR                                                                            | 04/2001                       | 406.92<br>-                        | -<br>-                             | -           | 0/0                        |
| 317                            | KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND                                                                          | 04/2003                       | 142.45<br>-                        | -<br>-                             | -           | 0/0                        |
| 318                            | ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH                                                                         | 04/1997                       | 120.00<br>-                        | 12/2008<br>-                       | -           | 0/0                        |
| 319                            | CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH                                                                 | 04/2005                       | 383.79<br>-                        | -<br>-                             | -           | 0/0                        |
| 320                            | RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH                                                                      | 04/2003                       | 136.62<br>-                        | 12/2007<br>03/2010                 | -           | 0/0                        |
| 321                            | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR                                                        | 04/1996                       | 332.92<br>283.95                   | 03/2012<br>-                       | -           | 0/0                        |
| 322                            | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU                                      | 09/2007                       | 404.19<br>-                        | -<br>-                             | -           | 0/0                        |
| 323                            | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU                                                    | 09/2006                       | 343.17<br>-                        | -<br>-                             | -           | 0/0                        |
| 324                            | UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH                                                              | 04/2006                       | 325.00<br>-                        | 03/2010<br>-                       | -           | 0/0                        |
| 325                            | ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH                                      | 02/2008                       | 171.10<br>-                        | 03/2012<br>-                       | -           | 0/0                        |
| 326                            | TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL                                                                   | 03/1984                       | 293.97<br>-                        | 06/2005<br>-                       | -           | 0/0                        |
| 327                            | KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR                                                                           | 04/2008                       | 282.92<br>-                        | -<br>-                             | -           | 0/0                        |
| 328                            | RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA                             | 04/2007                       | 482.00<br>-                        | 03/2013<br>-                       | -           | 0/0                        |
| 329                            | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL           | 04/2010                       | 2,397.72<br>-                      | 03/2016<br>-                       | -           | 0/0                        |
| 330                            | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL | 04/2010                       | 2,298.42<br>-                      | 03/2014<br>-                       | -           | 0/0                        |
| 331                            | SURATPURA - HANUMANGARH - SRIGANGANAGAR GAUGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN                                       | 04/2008                       | 516.23<br>-                        | 03/2014<br>-                       | -           | 0/0                        |
| 332                            | TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND                                                                             | 04/2008                       | 167.73<br>-                        | 03/2012<br>-                       | -           | 0/0                        |
| 333                            | DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL                                                                    | 04/2009                       | 533.38<br>-                        | 12/2011<br>-                       | -           | 0/0                        |
| 334                            | GHUTIASARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL                                                                           | 04/2009                       | 611.03<br>-                        | 12/2011<br>-                       | -           | 0/0                        |
| 335                            | PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL                                                                  | 04/2004                       | 293.74<br>-                        | 12/2010<br>-                       | -           | 0/0                        |
| 336                            | BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL                          | 04/1999                       | 207.52<br>-                        | 12/2012<br>-                       | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                            |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|--------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                    | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                            |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                          | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 337                            | RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH                              | 04/2008                       | 603.04<br>-                        | 03/2012<br>-                       | -           | 0/0                        |
| 338                            | BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT | 04/2006                       | 117.36<br>196.95                   | 03/2011<br>-                       | -           | 0/0                        |
| 339                            | ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH                       | 03/2013                       | 307.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 340                            | KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH  | 03/2013                       | 643.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 341                            | CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE                                          | 04/2007                       | 1,347.26<br>-                      | -<br>-                             | -           | 0/0                        |
| 342                            | MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT                                 | 04/2011                       | 439.88<br>-                        | -<br>-                             | -           | 0/0                        |
| 343                            | VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT                                        | 04/2010                       | 279.40<br>-                        | -<br>-                             | -           | 0/0                        |
| 344                            | PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN                                                   | 04/2013                       | 323.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 345                            | GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN                              | 04/2011                       | 239.73<br>-                        | -<br>-                             | -           | 0/0                        |
| 346                            | BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL                                          | 04/2010                       | 267.37<br>-                        | -<br>-                             | -           | 0/0                        |
| 347                            | DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE                    | 04/2010                       | 553.63<br>-                        | -<br>-                             | -           | 0/0                        |
| 348                            | BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL                           | 04/2011                       | 289.64<br>-                        | -<br>-                             | -           | 0/0                        |
| 349                            | CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA                          | 04/2010                       | 149.90<br>-                        | 03/2015<br>-                       | -           | 0/0                        |
| 350                            | DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND                         | 04/2010                       | 309.44<br>-                        | 12/2015<br>-                       | -           | 0/0                        |
| 351                            | ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR                                               | 04/2008                       | 490.80<br>-                        | -<br>-                             | -           | 0/0                        |
| 352                            | NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR                                                | 04/2008                       | 620.57<br>-                        | -<br>-                             | -           | 0/0                        |
| 353                            | GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR                                  | 04/2008                       | 445.25<br>-                        | -<br>-                             | -           | 0/0                        |
| 354                            | GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE                                             | 04/2008                       | 415.67<br>-                        | -<br>-                             | -           | 0/0                        |
| 355                            | BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR                                              | 04/2008                       | 326.20<br>-                        | -<br>-                             | -           | 0/0                        |
| 356                            | SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR                                           | 04/1999                       | 175.69<br>-                        | -<br>-                             | -           | 0/0                        |
| 357                            | CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR                                           | 04/2006                       | 285.07<br>-                        | -<br>-                             | -           | 0/0                        |
| 358                            | DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR                                      | 04/2005                       | 205.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 359                            | MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR                                             | 04/2006                       | 211.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 360                            | SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR                         | 04/2008                       | 678.62<br>-                        | -<br>-                             | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                  |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|----------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                          | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                  |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 361                            | MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR                                                                 | 04/2008                       | 228.05<br>-                        | -<br>-                             | -           | 0/0                        |
| 362                            | ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR                                                                                        | 04/2008                       | 304.41<br>-                        | -<br>-                             | -           | 0/0                        |
| 363                            | KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR                                                                                   | 04/2008                       | 192.56<br>-                        | -<br>-                             | -           | 0/0                        |
| 364                            | MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR                                                                                | 04/2008                       | 281.30<br>-                        | -<br>-                             | -           | 0/0                        |
| 365                            | SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR                                    | 04/2004                       | 372.14<br>-                        | -<br>-                             | -           | 0/0                        |
| 366                            | JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR                                       | 04/2009                       | 470.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 367                            | HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR                                                                           | 04/2013                       | 213.01<br>-                        | -<br>-                             | -           | 0/0                        |
| 368                            | ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU                                                                                     | 04/2008                       | 446.87<br>527.37                   | -<br>01/2011                       | -           | 0/0                        |
| 369                            | CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE                                                                   | 04/2008                       | 523.52<br>2,350.00                 | -<br>-                             | -           | 0/0                        |
| 370                            | SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU                          | 04/2013                       | 839.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 371                            | CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU                                                       | 04/1998                       | 271.24<br>-                        | -<br>-                             | -           | 0/0                        |
| 372                            | KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE                                                                            | 04/2007                       | 270.14<br>-                        | -<br>-                             | -           | 0/0                        |
| 373                            | KUMBALAM-TURAVUR - [N22000191]SR,KERALA                                                                                          | 04/2011                       | 252.96<br>-                        | -<br>-                             | -           | 0/0                        |
| 374                            | NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL                                                            | 04/2010                       | 221.42<br>-                        | -<br>-                             | -           | 0/0                        |
| 375                            | ERODE-PALANI - [N22000199]SR,TAMIL NADU                                                                                          | 04/2008                       | 288.57<br>-                        | -<br>-                             | -           | 0/0                        |
| 376                            | MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU                                                                                | 04/2008                       | 164.41<br>-                        | -<br>-                             | -           | 0/0                        |
| 377                            | CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA                                                                                    | 04/2006                       | 191.72<br>-                        | -<br>-                             | -           | 0/0                        |
| 378                            | NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE                                                             | 04/2010                       | 242.22<br>-                        | -<br>-                             | -           | 0/0                        |
| 379                            | NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE                                                              | 04/2010                       | 241.52<br>-                        | -<br>-                             | -           | 0/0                        |
| 380                            | CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHUPUR - [N22000212]MRTP, WEST BENGAL                                            | 04/2009                       | 573.78<br>-                        | -<br>-                             | -           | 0/0                        |
| 381                            | RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA                                                          | 04/2012                       | 714.10<br>-                        | 04/2016<br>-                       | -           | 0/0                        |
| 382                            | MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE                                                                  | 04/2011                       | 601.43<br>-                        | -<br>-                             | -           | 0/0                        |
| 383                            | LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE | 04/1987                       | 406.99<br>-                        | -<br>-                             | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                  |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|----------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                          | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                  |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 384                            | SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE                                                  | 04/2007                       | 450.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 385                            | HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE                                                                     | 04/2010                       | 172.03<br>-                        | -<br>-                             | -           | 0/0                        |
| 386                            | PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE                                                                                    | 04/2013                       | 915.98<br>1,130.13                 | -<br>-                             | -           | 0/0                        |
| 387                            | PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE                                                                             | 04/2011                       | 248.07<br>-                        | 03/2015<br>-                       | -           | 0/0                        |
| 388                            | BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE                                                                              | 04/2011                       | 288.35<br>-                        | -<br>-                             | -           | 0/0                        |
| 389                            | PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE                                                                                  | 04/2011                       | 261.38<br>-                        | -<br>-                             | -           | 0/0                        |
| 390                            | KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE | 04/2001                       | 923.52<br>-                        | -<br>-                             | -           | 0/0                        |
| 391                            | CHINPAI- SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE                    | 04/2005                       | 595.91<br>-                        | -<br>-                             | -           | 0/0                        |
| 392                            | KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE                      | 04/2010                       | 174.56<br>-                        | -<br>-                             | -           | 0/0                        |
| 393                            | SONDALIA-CHAMPAPUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE                                           | 04/2010                       | 277.28<br>-                        | -<br>-                             | -           | 0/0                        |
| 394                            | DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE   | 04/2010                       | 296.44<br>-                        | -<br>-                             | -           | 0/0                        |
| 395                            | BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE                                                | 04/2007                       | 450.55<br>-                        | -<br>-                             | -           | 0/0                        |
| 396                            | TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE                                                                        | 04/2010                       | 365.17<br>-                        | -<br>-                             | -           | 0/0                        |
| 397                            | HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE                                                                                    | 04/2011                       | 267.09<br>-                        | -<br>-                             | -           | 0/0                        |
| 398                            | SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE                                                                           | 04/2011                       | 193.44<br>-                        | -<br>-                             | -           | 0/0                        |
| 399                            | BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE                                                                          | 04/2011                       | 175.80<br>-                        | -<br>-                             | -           | 0/0                        |
| 400                            | PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE                                                    | 04/2011                       | 299.60<br>-                        | 03/2017<br>-                       | -           | 0/0                        |
| 401                            | NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE | 04/2010                       | 494.54<br>-                        | -<br>-                             | -           | 0/0                        |
| 402                            | SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE                                 | 04/2000                       | 297.47<br>-                        | -<br>-                             | -           | 0/0                        |
| 403                            | CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE | 04/2003                       | 337.96<br>-                        | -<br>-                             | -           | 0/0                        |
| 404                            | MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE  | 04/2009                       | 493.96<br>-                        | -<br>-                             | -           | 0/0                        |
| 405                            | KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE                                              | 04/2010                       | 423.66<br>-                        | 03/2017<br>-                       | -           | 0/0                        |
| 406                            | 3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA                                                                    | 04/2011                       | 184.06<br>-                        | -<br>-                             | -           | 0/0                        |
| 407                            | SANTOSHAPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE                                                | 04/2010                       | 268.52<br>-                        | -<br>-                             | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                          |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                  | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                          |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                        | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 408                            | HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE | 04/2011                       | 166.89<br>-                        | -<br>-                             | -           | 0/0                        |
| 409                            | PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE                                                                            | 04/2007                       | 98.74<br>-                         | -<br>-                             | -           | 0/0                        |
| 410                            | PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE                                                                          | 04/2006                       | 96.16<br>-                         | -<br>-                             | -           | 0/0                        |
| 411                            | TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA                                                               | 04/2011                       | 913.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 412                            | KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE                                            | 04/2012                       | 1,054.35<br>-                      | -<br>-                             | -           | 0/0                        |
| 413                            | GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH                                                                    | 04/2011                       | 283.54<br>-                        | -<br>-                             | -           | 0/0                        |
| 414                            | MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH                                                               | 04/2012                       | 377.44<br>-                        | -<br>-                             | -           | 0/0                        |
| 415                            | MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB            | 04/2009                       | 396.04<br>-                        | -<br>-                             | -           | 0/0                        |
| 416                            | GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI                                                                       | 04/1999                       | 156.65<br>-                        | -<br>-                             | -           | 0/0                        |
| 417                            | FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH                                  | 04/2013                       | 654.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 418                            | DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE                                                        | 04/2013                       | 1,239.00<br>-                      | -<br>-                             | -           | 0/0                        |
| 419                            | ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA                                                                               | 04/2012                       | 287.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 420                            | BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH                                                            | 04/2008                       | 1,046.88<br>-                      | -<br>-                             | -           | 0/0                        |
| 421                            | DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE                                                          | 04/2007                       | 336.91<br>-                        | -<br>-                             | -           | 0/0                        |
| 422                            | CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA                                            | 04/2013                       | 558.00<br>692.43                   | -<br>-                             | -           | 0/0                        |
| 423                            | SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE                                                               | 04/2013                       | 296.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 424                            | SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA                                                                            | 04/2011                       | 562.74<br>-                        | -<br>-                             | -           | 0/0                        |
| 425                            | WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA                                                                          | 04/2011                       | 341.05<br>-                        | -<br>-                             | -           | 0/0                        |
| 426                            | ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI                                                          | 04/2012                       | 295.68<br>-                        | -<br>-                             | -           | 0/0                        |
| 427                            | HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND                                                                              | 04/2012                       | 219.83<br>-                        | -<br>-                             | -           | 0/0                        |
| 428                            | AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE                                  | 04/2010                       | 338.54<br>-                        | -<br>-                             | -           | 0/0                        |
| 429                            | JAKHAL-MANSAB DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE                                                        | 04/2008                       | 162.96<br>-                        | -<br>-                             | -           | 0/0                        |
| 430                            | HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA                                                            | 04/2013                       | 400.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 431                            | YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE                                              | 04/2013                       | 876.00<br>-                        | -<br>-                             | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                             |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|---------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                     | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                             |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                           | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 432                            | UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH                                               | 04/2012                       | 380.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 433                            | QADIAN-BEAS - [N22000295]NR,PUNJAB                                                          | 04/2011                       | 205.22<br>-                        | -<br>-                             | -           | 0/0                        |
| 434                            | CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE                                             | 04/2007                       | 328.14<br>-                        | -<br>-                             | -           | 0/0                        |
| 435                            | TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA                                        | 04/2011                       | 146.75<br>-                        | -<br>-                             | -           | 0/0                        |
| 436                            | GADAG-WADI NL - [N22000299]SWR,KARNATAKA                                                    | 04/2013                       | 1,117.00<br>1,922.00               | -<br>-                             | -           | 0/0                        |
| 437                            | CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA                                    | 04/2013                       | 327.25<br>367.77                   | -<br>-                             | -           | 0/0                        |
| 438                            | MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE                                               | 04/2012                       | 250.93<br>-                        | -<br>-                             | -           | 0/0                        |
| 439                            | BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL                                | 04/2012                       | 255.64<br>-                        | -<br>-                             | -           | 0/0                        |
| 440                            | JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE                                     | 04/2007                       | 313.24<br>-                        | 01/1999<br>-                       | -           | 0/0                        |
| 441                            | MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE                                      | 04/2008                       | 466.48<br>-                        | 01/1999<br>-                       | -           | 0/0                        |
| 442                            | MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA                                              | 04/2012                       | 285.57<br>279.54                   | 01/1999<br>-                       | -           | 0/0                        |
| 443                            | MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL                                     | 04/2011                       | 276.69<br>-                        | 01/1999<br>-                       | -           | 0/0                        |
| 444                            | JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA                                        | 03/2006                       | 201.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 445                            | DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA                                               | 03/2011                       | 165.16<br>-                        | 03/2015<br>-                       | -           | 0/0                        |
| 446                            | GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH                                  | 04/2014                       | 182.92<br>-                        | -<br>-                             | -           | 0/0                        |
| 447                            | RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND            | 04/2012                       | 148.77<br>-                        | 12/2016<br>-                       | -           | 0/0                        |
| 448                            | HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA                               | 04/2010                       | 203.40<br>203.40                   | -<br>-                             | -           | 0/0                        |
| 449                            | MIRAJ-LONDA - [N22000327]SWR,MULTI STATE                                                    | 03/2015                       | 1,830.00<br>1,190.92               | -<br>-                             | -           | 0/0                        |
| 450                            | SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR                                                 | 05/2015                       | 380.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 451                            | AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN | 05/2015                       | 873.71<br>-                        | -<br>-                             | -           | 0/0                        |
| 452                            | ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA                                          | 05/2015                       | 400.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 453                            | HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE                                              | 03/2015                       | 1,618.00<br>1,614.59               | -<br>-                             | -           | 0/0                        |
| 454                            | GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH   | 04/1997                       | 836.26<br>-                        | -<br>-                             | -           | 0/0                        |
| 455                            | DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE                            | 10/2006                       | 81,459.00<br>-                     | -<br>-                             | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                         |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                                 | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                         |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                       | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 456                            | INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA                                                                       | 02/2016                       | 9,968.00<br>-                      | -<br>-                             | -           | 0/0                        |
| 457                            | PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA                                                                                         | 02/2016                       | 2,425.00<br>-                      | -<br>-                             | -           | 0/0                        |
| 458                            | VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA                                                                             | 02/2016                       | 2,750.00<br>-                      | -<br>-                             | -           | 0/0                        |
| 459                            | PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA                                                                                   | 02/2015                       | 4,670.00<br>3,627.00               | -<br>-                             | -           | 0/0                        |
| 460                            | DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA                                                                                     | 02/2016                       | 1,876.00<br>-                      | -<br>-                             | -           | 0/0                        |
| 461                            | MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA                                                                        | 02/2016                       | 854.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 462                            | DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH                                                                                      | 04/2015                       | 3,873.07<br>-                      | -<br>-                             | -           | 0/0                        |
| 463                            | GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH                                                                                         | 04/2016                       | 4,000.00<br>-                      | -<br>-                             | -           | 0/0                        |
| 464                            | VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH                                                                                       | 04/2015                       | 3,246.26<br>-                      | -<br>-                             | -           | 0/0                        |
| 465                            | GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE                                                                               | 04/2015                       | 636.38<br>-                        | -<br>-                             | -           | 0/0                        |
| 466                            | MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR                                                                                   | 01/1991                       | 332.15<br>-                        | 07/2014<br>-                       | -           | 0/0                        |
| 467                            | NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL                                           | 04/2016                       | 556.31<br>-                        | -<br>-                             | -           | 0/0                        |
| 468                            | TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA                                                                                  | 02/2015                       | 900.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 469                            | TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA                                                                                     | 02/2015                       | 1,000.00<br>-                      | -<br>-                             | -           | 0/0                        |
| 470                            | BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL                                                  | 04/1998                       | 1,027.40<br>-                      | 03/2003<br>-                       | -           | 0/0                        |
|                                | <b>Total</b>                                                                                                                            |                               | 3,207,49.38<br>-                   |                                    |             | 0/0                        |
|                                |                                                                                                                                         |                               |                                    |                                    |             |                            |
|                                | <b>ROAD TRANSPORT AND HIGHWAYS</b>                                                                                                      |                               |                                    |                                    |             |                            |
| 471                            | TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH | 12/2009                       | 165.00<br>-                        | 09/2010<br>-                       | 09/2010     | 0/0                        |
| 472                            | TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH | 12/2009                       | 104.00<br>-                        | 09/2010<br>-                       | 09/2010     | 0/0                        |
| 473                            | CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM                                    | 08/2010                       | 195.04<br>-                        | 10/2010<br>-                       | 10/2010     | 0/0                        |
| 474                            | 2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA            | 12/2010                       | 1,494.48<br>-                      | 02/2011<br>-                       | 02/2011     | 0/0                        |
| 475                            | 2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM               | 11/2010                       | 470.20<br>-                        | 02/2011<br>-                       | 02/2011     | 0/0                        |
| 476                            | NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN         | 09/2012                       | 511.00<br>-                        | 10/2013<br>-                       | 10/2013     | 0/0                        |



## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                      |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                      |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                    | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 477                            | NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN                | 09/2012                       | 511.00 -                           | 10/2013 -                          | 10/2013     | 0/0                        |
| 478                            | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR        | 10/2013                       | 278.39 -                           | 08/2014 -                          | 08/2014     | 0/0                        |
| 479                            | CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA  | 03/2011                       | 185.82<br>292.22                   | -<br>11/2014                       | 11/2014     | 0/0                        |
| 480                            | REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA    | 01/2014                       | 292.98 -                           | 11/2014 -                          | 11/2014     | 0/0                        |
| 481                            | BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH                                                          | 11/2011                       | 670.82 -                           | 02/2015 -                          | 02/2015     | 0/0                        |
| 482                            | REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH             | 10/2014                       | 213.47 -                           | 03/2015 -                          | 03/2015     | 0/0                        |
| 483                            | REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 ( BEDMA-DAHAKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH           | 10/2014                       | 298.34 -                           | 03/2015 -                          | 03/2015     | 0/0                        |
| 484                            | REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHAKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH    | 11/2014                       | 262.54 -                           | 03/2015 -                          | 03/2015     | 0/0                        |
| 485                            | MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH                                                    | 01/2012                       | 381.86 -                           | 04/2015 -                          | 04/2015     | 0/0                        |
| 486                            | BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH                                                                    | 11/2011                       | 704.26 -                           | 05/2015 -                          | 05/2015     | 0/0                        |
| 487                            | CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU    | 11/2015                       | 154.14 -                           | 08/2015 -                          | 08/2015     | 0/0                        |
| 488                            | WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH                                  | 05/2013                       | 164.54 -                           | 08/2015 -                          | 08/2015     | 0/0                        |
| 489                            | FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH | 10/2015                       | 333.21 -                           | 11/2015 -                          | 11/2015     | 0/0                        |
| 490                            | BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH                                                       | 03/2013                       | 257.80 -                           | 02/2016 -                          | 02/2016     | 0/0                        |
| 491                            | CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH                   | 01/2014                       | 282.41 -                           | 03/2016 -                          | 03/2016     | 0/0                        |
| 492                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN     | 01/1991                       | 208.87<br>223.00                   | 05/2016 -                          | 05/2016     | 0/0                        |
| 493                            | REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH                                                  | 02/2015                       | 224.83 -                           | 04/2015 -                          | 05/2016     | 0/0                        |
| 494                            | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR        | 02/2016                       | 369.77 -                           | 06/2016 -                          | 06/2016     | 0/0                        |
| 495                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR        | 01/1991                       | 282.41 -                           | 08/2016 -                          | 08/2016     | 0/0                        |
| 496                            | SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH                                                      | 11/2011                       | 871.15 -                           | 09/2015 -                          | 08/2016     | 0/0                        |
| 497                            | SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH                                                               | 01/2012                       | 320.48 -                           | 08/2015 -                          | 09/2016     | 0/0                        |
| 498                            | STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH         | 10/2014                       | 227.74 -                           | 10/2016 -                          | 10/2016     | 0/0                        |
| 499                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN    | 01/1991                       | 269.26 -                           | 10/2016 -                          | 10/2016     | 0/0                        |
| 500                            | BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH                              | 01/2014                       | 397.04 -                           | 10/2016 -                          | 10/2016     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                             |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                                     | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                             |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                           | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 501                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR               | 01/1991                       | 358.22<br>-                        | 10/2016<br>-                       | 10/2016     | 0/0                        |
| 502                            | JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH                 | 10/2013                       | 283.45<br>-                        | 10/2016<br>-                       | 10/2016     | 0/0                        |
| 503                            | IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA                                                                                     | 12/2013                       | 319.80<br>-                        | 10/2016<br>-                       | 10/2016     | 0/0                        |
| 504                            | STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV - [N24000580]MORTH,BIHAR              | 03/2015                       | 206.80<br>-                        | 07/2016<br>-                       | 10/2016     | 0/0                        |
| 505                            | 2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH | 01/2016                       | 183.65<br>-                        | 11/2016<br>-                       | 11/2016     | 0/0                        |
| 506                            | FOUR LANING OF 5.122 KM OF NH9( NEW NH 65) FROM KM 269.900( DESIGN CH0.0 ) - [N24000302]PWD,ANDHRA PRADESH                                  | 07/2015                       | 333.21<br>-                        | 12/2015<br>-                       | 12/2016     | 0/0                        |
| 507                            | REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR               | 08/2016                       | 1,742.01<br>-                      | 12/2016<br>-                       | 12/2016     | 0/0                        |
| 508                            | EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA             | 03/2015                       | 153.21<br>-                        | 01/2017<br>-                       | 01/2017     | 0/0                        |
| 509                            | REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA                | 07/2014                       | 342.05<br>-                        | 01/2017<br>-                       | 01/2017     | 0/0                        |
| 510                            | REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH        | 11/2014                       | 297.78<br>330.00                   | 02/2017<br>-                       | 02/2017     | 0/0                        |
| 511                            | VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH                                                                             | 09/2014                       | 1,684.00<br>-                      | 02/2017<br>-                       | 02/2017     | 0/0                        |
| 512                            | RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH                           | 10/2013                       | 445.89<br>-                        | 03/2017<br>-                       | 03/2017     | 0/0                        |
| 513                            | 2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH         | 11/2010                       | 305.49<br>-                        | 03/2017<br>-                       | 03/2017     | 0/0                        |
| 514                            | BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH                 | 10/2013                       | 317.76<br>-                        | 03/2017<br>-                       | 03/2017     | 0/0                        |
| 515                            | SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH                                      | 10/2013                       | 493.94<br>-                        | 03/2017<br>-                       | 03/2017     | 0/0                        |
| 516                            | IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA               | 12/2013                       | 319.80<br>320.00                   | 05/2016<br>-                       | 03/2017     | 0/0                        |
| 517                            | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA              | 08/2013                       | 171.96<br>172.00                   | 06/2016<br>-                       | 03/2017     | 0/0                        |
| 518                            | WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA              | 03/2014                       | 162.51<br>163.00                   | 05/2016<br>-                       | 03/2017     | 0/0                        |
| 519                            | MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM                                                                  | 12/2003                       | 200.00<br>-                        | 04/2009<br>-                       | 05/2017     | 0/0                        |
| 520                            | SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM                                                                                           | 12/2003                       | 245.00<br>-                        | 03/2008<br>-                       | 05/2017     | 0/0                        |
| 521                            | DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM                                                                             | 12/2003                       | 160.00<br>-                        | 05/2008<br>-                       | 05/2017     | 0/0                        |
| 522                            | INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH                          | 11/2013                       | 497.05<br>-                        | 05/2017<br>-                       | 05/2017     | 0/0                        |
| 523                            | 2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM                               | 11/2010                       | 268.08<br>-                        | 05/2017<br>-                       | 05/2017     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                 |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|---------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                         | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                 |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                               | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 524                            | SHAHDOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH | 06/2015                       | 532.49<br>-                        | 05/2017<br>-                       | 05/2017     | 0/0                        |
| 525                            | JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH      | 02/2015                       | 327.32<br>-                        | 05/2017<br>-                       | 05/2017     | 0/0                        |
| 526                            | CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU                                             | 09/2010                       | 852.00<br>-                        | 03/2013<br>-                       | 06/2017     | 0/0                        |
| 527                            | SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH                                | 11/2011                       | 1,535.00<br>-                      | 05/2014<br>-                       | 06/2017     | 0/0                        |
| 528                            | SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA                                                          | 12/2011                       | 1,047.00<br>-                      | 06/2014<br>-                       | 06/2017     | 0/0                        |
| 529                            | WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA  | 03/2014                       | 191.50<br>192.00                   | 05/2016<br>-                       | 06/2017     | 0/0                        |
| 530                            | INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH                                                                             | 11/2010                       | 325.00<br>-                        | 05/2013<br>-                       | 07/2017     | 0/0                        |
| 531                            | KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH                                | 02/2015                       | 377.83<br>-                        | 07/2017<br>-                       | 07/2017     | 0/0                        |
| 532                            | TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 ( NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN               | 07/2015                       | 455.60<br>-                        | 07/2017<br>-                       | 07/2017     | 0/0                        |
| 533                            | DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA                                                                       | 04/2007                       | 486.00<br>-                        | 05/2010<br>-                       | 08/2017     | 0/0                        |
| 534                            | ROHTAK-BAWAL - [N24000169]NHAI,HARYANA                                                                                          | 05/2011                       | 650.00<br>-                        | 11/2013<br>-                       | 08/2017     | 0/0                        |
| 535                            | GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH                                                                         | 02/2011                       | 1,141.00<br>-                      | 08/2013<br>-                       | 08/2017     | 0/0                        |
| 536                            | UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH                         | 03/2015                       | 511.83<br>-                        | 08/2017<br>-                       | 08/2017     | 0/0                        |
| 537                            | REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA   | 07/2014                       | 342.05<br>342.00                   | 01/2017<br>-                       | 08/2017     | 0/0                        |
| 538                            | NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM                                                                                 | 12/2003                       | 225.00<br>-                        | 06/2008<br>-                       | 09/2017     | 0/0                        |
| 539                            | INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH                                                                        | 10/2010                       | 1,175.00<br>-                      | 04/2013<br>-                       | 09/2017     | 0/0                        |
| 540                            | MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH                                                                               | 04/2010                       | 1,267.00<br>-                      | 06/2013<br>-                       | 09/2017     | 0/0                        |
| 541                            | PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR                                                                   | 09/2011                       | 574.00<br>-                        | 03/2014<br>-                       | 09/2017     | 0/0                        |
| 542                            | CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA    | 01/2014                       | 255.75<br>348.00                   | 09/2017<br>-                       | 09/2017     | 0/0                        |
| 543                            | TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 ( NEW NH NO -50) - [N24000342]NHAI,KARNATAKA | 05/2015                       | 709.00<br>-                        | 09/2017<br>-                       | 09/2017     | 0/0                        |
| 544                            | TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23 - [N24000343]NHAI,JHARKHAND                                     | 09/2015                       | 341.61<br>-                        | 09/2017<br>-                       | 09/2017     | 0/0                        |
| 545                            | TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN                                                 | 09/2014                       | 425.19<br>-                        | 09/2016<br>-                       | 09/2017     | 0/0                        |
| 546                            | 2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH                           | 09/2015                       | 368.73<br>-                        | 09/2016<br>-                       | 09/2017     | 0/0                        |
| 547                            | FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH                                                                | 05/2013                       | 1,055.00<br>-                      | 11/2015<br>-                       | 09/2017     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                       |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|---------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                               | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                       |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                     | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 548                            | DEOLI KOTA - [N24000148]NHAI, RAJASTHAN                                                                                               | 01/2011                       | 593.00<br>-                        | 07/2013<br>-                       | 10/2017     | 0/0                        |
| 549                            | 2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR                                                                                   | 05/2011                       | 351.54<br>-                        | 05/2013<br>-                       | 10/2017     | 0/0                        |
| 550                            | BAREILY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH                                                                              | 03/2011                       | 1,046.00<br>-                      | 09/2013<br>-                       | 10/2017     | 0/0                        |
| 551                            | ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH                                                                                       | 03/2013                       | 1,573.00<br>-                      | 09/2015<br>-                       | 10/2017     | 0/0                        |
| 552                            | REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD, ANDHRA PRADESH | 03/2015                       | 271.45<br>-                        | 10/2015<br>-                       | 10/2017     | 0/0                        |
| 553                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAP - [N24000379]MORTH, ODISHA       | 01/1991                       | 218.63<br>251.92                   | 10/2017<br>-                       | 10/2017     | 0/0                        |
| 554                            | WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH, ODISHA          | 02/2015                       | 239.91<br>240.00                   | 10/2017<br>-                       | 10/2017     | 0/0                        |
| 555                            | WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH, ODISHA        | 03/2015                       | 226.31<br>226.00                   | 10/2017<br>-                       | 10/2017     | 0/0                        |
| 556                            | RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL, SIKKIM                                                                       | 04/2017                       | 388.00<br>-                        | 10/2017<br>-                       | 10/2017     | 0/0                        |
| 557                            | JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR                                                               | 07/2010                       | 1,813.76<br>-                      | 07/2013<br>-                       | 11/2017     | 0/0                        |
| 558                            | MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE                                                                                 | 09/2011                       | 754.00<br>-                        | 03/2013<br>-                       | 11/2017     | 0/0                        |
| 559                            | CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD, KERALA         | 01/2014                       | 267.16<br>352.00                   | 11/2017<br>-                       | 11/2017     | 0/0                        |
| 560                            | STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH, KARNATAKA    | 03/2015                       | 165.67<br>-                        | 11/2015<br>-                       | 11/2017     | 0/0                        |
| 561                            | STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH, KARNATAKA    | 03/2015                       | 159.12<br>-                        | 11/2015<br>-                       | 11/2017     | 0/0                        |
| 562                            | FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI, TAMIL NADU         | 05/2015                       | 1,387.11<br>-                      | 11/2017<br>-                       | 11/2017     | 0/0                        |
| 563                            | 2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH                                 | 04/2014                       | 351.34<br>-                        | 01/2016<br>-                       | 11/2017     | 0/0                        |
| 564                            | 2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI, UTTAR PRADESH                                                   | 04/2014                       | 495.78<br>-                        | 01/2016<br>-                       | 11/2017     | 0/0                        |
| 565                            | 4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA                                                    | 06/2014                       | 923.04<br>-                        | 11/2016<br>-                       | 11/2017     | 0/0                        |
| 566                            | 4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI, KERALA                                                        | 06/2015                       | 845.24<br>-                        | -<br>-                             | 11/2017     | 0/0                        |
| 567                            | IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI, PUNJAB            | 09/2015                       | 273.06<br>-                        | -<br>-                             | 11/2017     | 0/0                        |
| 568                            | WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD, ODISHA             | 12/2011                       | 159.39<br>-                        | 11/2017<br>-                       | 11/2017     | 0/0                        |
| 569                            | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM                                                       | 12/2003                       | 280.00<br>-                        | 02/2009<br>-                       | 12/2017     | 0/0                        |
| 570                            | NALBARI T BIJNI (AS-7) - [N24000048]NHAI, ASSAM                                                                                       | 12/2003                       | 208.00<br>-                        | 04/2008<br>-                       | 12/2017     | 0/0                        |
| 571                            | CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH                                                      | 11/2010                       | 1,585.00<br>-                      | 05/2013<br>-                       | 12/2017     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                  |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                          | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                  |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 572                            | SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA                             | 02/2010                       | 617.00<br>-                        | 08/2012<br>-                       | 12/2017     | 0/0                        |
| 573                            | 4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE                                                           | 02/2011                       | 2,498.76<br>-                      | 08/2014<br>-                       | 12/2017     | 0/0                        |
| 574                            | PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA                                                                  | 10/2010                       | 1,724.55<br>-                      | 03/2013<br>-                       | 12/2017     | 0/0                        |
| 575                            | SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU            | 09/2011                       | 1,250.00<br>-                      | 12/2013<br>-                       | 12/2017     | 0/0                        |
| 576                            | TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU                                  | 05/2010                       | 374.00<br>-                        | 05/2013<br>-                       | 12/2017     | 0/0                        |
| 577                            | 2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU                                      | 09/2011                       | 485.00<br>-                        | 08/2013<br>-                       | 12/2017     | 0/0                        |
| 578                            | TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH                                                  | 04/2011                       | 571.00<br>-                        | 10/2013<br>-                       | 12/2017     | 0/0                        |
| 579                            | 2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR                                                      | 05/2011                       | 511.54<br>-                        | 11/2013<br>-                       | 12/2017     | 0/0                        |
| 580                            | SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR                                                          | 06/2011                       | 1,100.70<br>-                      | 06/2014<br>-                       | 12/2017     | 0/0                        |
| 581                            | 4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL                                                         | 02/2011                       | 1,078.84<br>-                      | 08/2013<br>-                       | 12/2017     | 0/0                        |
| 582                            | 6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL                                             | 04/2012                       | 1,396.18<br>-                      | 09/2014<br>-                       | 12/2017     | 0/0                        |
| 583                            | 2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH                                         | 07/2012                       | 291.36<br>-                        | 01/2014<br>-                       | 12/2017     | 0/0                        |
| 584                            | HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND                                               | 11/2011                       | 478.51<br>-                        | 10/2013<br>-                       | 12/2017     | 0/0                        |
| 585                            | RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND                                                              | 12/2012                       | 1,479.00<br>-                      | 06/2015<br>-                       | 12/2017     | 0/0                        |
| 586                            | DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE                                                | 10/2012                       | 1,928.22<br>-                      | 04/2015<br>-                       | 12/2017     | 0/0                        |
| 587                            | BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL                                                                | 08/2012                       | 867.00<br>-                        | 02/2015<br>-                       | 12/2017     | 0/0                        |
| 588                            | JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB                                                                    | 01/2014                       | 523.85<br>-                        | 01/2016<br>-                       | 12/2017     | 0/0                        |
| 589                            | MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH | 06/2015                       | 641.02<br>-                        | 12/2017<br>-                       | 12/2017     | 0/0                        |
| 590                            | GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN                                               | 02/2008                       | 1,673.70<br>-                      | 10/2011<br>-                       | 12/2017     | 0/0                        |
| 591                            | FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH                          | 02/2013                       | 1,232.00<br>-                      | 08/2015<br>-                       | 12/2017     | 0/0                        |
| 592                            | FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB                                             | 09/2014                       | 479.00<br>-                        | -<br>-                             | 12/2017     | 0/0                        |
| 593                            | FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB                                         | 12/2015                       | 239.23<br>-                        | 12/2017<br>-                       | 12/2017     | 0/0                        |
| 594                            | FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH                                             | 03/2015                       | 928.83<br>-                        | -<br>-                             | 12/2017     | 0/0                        |
| 595                            | SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL                                                  | 04/2014                       | 1,665.00<br>-                      | -<br>-                             | 12/2017     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                      |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                      |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                    | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 596                            | TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR                                                                     | 08/2015                       | 854.80<br>-                        | -<br>-                             | 12/2017     | 0/0                        |
| 597                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA    | 01/1991                       | 219.40<br>-                        | 01/2018<br>-                       | 01/2018     | 0/0                        |
| 598                            | CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL                                                                      | 10/2015                       | 361.15<br>-                        | -<br>-                             | 01/2018     | 0/0                        |
| 599                            | 4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA                                                         | 01/2015                       | 972.50<br>-                        | 07/2017<br>-                       | 01/2018     | 0/0                        |
| 600                            | FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA                                                                  | 07/2015                       | 1,393.00<br>-                      | -<br>-                             | 01/2018     | 0/0                        |
| 601                            | FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI, MAHARASHTRA                                                                   | 07/2015                       | 1,871.34<br>-                      | 01/2018<br>-                       | 01/2018     | 0/0                        |
| 602                            | FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH                                | 11/2013                       | 1,916.79<br>-                      | 11/2016<br>-                       | 02/2018     | 0/0                        |
| 603                            | TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER ( UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI, RAJASTHAN    | 08/2015                       | 538.08<br>-                        | 02/2018<br>-                       | 02/2018     | 0/0                        |
| 604                            | FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE - I - [N24000347]NHAI,HARYANA                                               | 08/2015                       | 723.54<br>-                        | 02/2018<br>-                       | 02/2018     | 0/0                        |
| 605                            | JAISALMER - BARMER - [N24000348]NHAI, RAJASTHAN                                                                                      | 08/2015                       | 482.27<br>-                        | 02/2018<br>-                       | 02/2018     | 0/0                        |
| 606                            | STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD, ASSAM         | 05/2011                       | 176.22<br>-                        | 02/2018<br>-                       | 02/2018     | 0/0                        |
| 607                            | STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD, ASSAM          | 11/2014                       | 218.31<br>-                        | 02/2018<br>-                       | 02/2018     | 0/0                        |
| 608                            | TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI, RAJASTHAN                                         | 08/2015                       | 275.90<br>-                        | -<br>-                             | 02/2018     | 0/0                        |
| 609                            | BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM                                                                                 | 12/2003                       | 217.61<br>-                        | 04/2010<br>-                       | 03/2018     | 0/0                        |
| 610                            | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA                                                                | 05/2009                       | 1,108.00<br>-                      | 11/2011<br>-                       | 03/2018     | 0/0                        |
| 611                            | JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA                                                                                       | 01/2011                       | 536.00<br>-                        | 01/2014<br>-                       | 03/2018     | 0/0                        |
| 612                            | 4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR                                                                                  | 01/2011                       | 575.00<br>-                        | 07/2013<br>-                       | 03/2018     | 0/0                        |
| 613                            | 4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL                                                                         | 02/2011                       | 998.79<br>-                        | 08/2013<br>-                       | 03/2018     | 0/0                        |
| 614                            | KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL                                                                                | 02/2012                       | 702.16<br>-                        | 07/2014<br>-                       | 03/2018     | 0/0                        |
| 615                            | PANVEL-INDAPUR - [N24000216]NHAI, MAHARASHTRA                                                                                        | 12/2011                       | 942.69<br>-                        | 06/2014<br>-                       | 03/2018     | 0/0                        |
| 616                            | 4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA                                                   | 04/2014                       | 1,266.60<br>-                      | 09/2016<br>-                       | 03/2018     | 0/0                        |
| 617                            | PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI, RAJASTHAN                                            | 09/2015                       | 567.51<br>-                        | 03/2018<br>-                       | 03/2018     | 0/0                        |
| 618                            | ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP, UTTAR PRADESH                                         | 06/2015                       | 774.57<br>-                        | 03/2018<br>-                       | 03/2018     | 0/0                        |
| 619                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH, WEST BENGAL | 01/1991                       | 322.00<br>-                        | 03/2018<br>-                       | 03/2018     | 0/0                        |



## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                    |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                            | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                    |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                  | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 620                            | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-VI) - [N24000433]NHAI,UTTAR PRADESH                                    | 09/2015                       | 768.56<br>-                        | 03/2018<br>-                       | 03/2018     | 0/0                        |
| 621                            | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-V) - [N24000436]NHAI,UTTAR PRADESH                                     | 09/2015                       | 664.53<br>-                        | 03/2018<br>-                       | 03/2018     | 0/0                        |
| 622                            | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-IV) - [N24000440]NHAI,UTTAR PRADESH                                    | 09/2015                       | 789.31<br>-                        | 03/2018<br>-                       | 03/2018     | 0/0                        |
| 623                            | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-III) - [N24000446]NHAI,MULTI STATE                                     | 09/2015                       | 788.51<br>-                        | 03/2018<br>-                       | 03/2018     | 0/0                        |
| 624                            | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-II) - [N24000450]NHAI,UTTAR PRADESH                                    | 09/2015                       | 785.78<br>-                        | 03/2018<br>-                       | 03/2018     | 0/0                        |
| 625                            | 4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA                                                      | 05/2014                       | 1,655.01<br>-                      | 08/2016<br>-                       | 03/2018     | 0/0                        |
| 626                            | JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH                    | 11/2015                       | 628.45<br>-                        | 03/2018<br>-                       | 03/2018     | 0/0                        |
| 627                            | FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH                                                                  | 09/2015                       | 934.46<br>-                        | 03/2018<br>-                       | 03/2018     | 0/0                        |
| 628                            | FOUR LANING FROM MPMHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA                    | 04/2010                       | 1,170.52<br>-                      | 06/2012<br>-                       | 03/2018     | 0/0                        |
| 629                            | WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA       | 12/2011                       | 191.08<br>-                        | 08/2015<br>-                       | 03/2018     | 0/0                        |
| 630                            | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-I)_NEW - [N24000609]NHAI,DELHI                                         | 09/2015                       | 771.18<br>-                        | -<br>-                             | 03/2018     | 0/0                        |
| 631                            | VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE                                                              | 09/2011                       | 2,848.00<br>-                      | 03/2014<br>-                       | 04/2018     | 0/0                        |
| 632                            | UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA( PKG - 2) - [N24000358]NHAI,HARYANA                                    | 10/2015                       | 562.34<br>-                        | 04/2018<br>-                       | 04/2018     | 0/0                        |
| 633                            | 2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN                                                                 | 10/2015                       | 597.00<br>-                        | 10/2017<br>-                       | 04/2018     | 0/0                        |
| 634                            | BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN    | 08/2014                       | 822.90<br>-                        | 04/2018<br>-                       | 04/2018     | 0/0                        |
| 635                            | FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR                                                                        | 08/2015                       | 322.09<br>-                        | -<br>-                             | 04/2018     | 0/0                        |
| 636                            | FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH                                                                   | 12/2015                       | 509.13<br>-                        | -<br>-                             | 04/2018     | 0/0                        |
| 637                            | FOUR / SIX LANING OF RAIPUR - SIMGA ( PKG-1) - [N24000510]NHAI,CHHATISGARH                                                         | 12/2015                       | 726.67<br>-                        | -<br>-                             | 04/2018     | 0/0                        |
| 638                            | TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR                                                      | 08/2015                       | 516.13<br>-                        | -<br>-                             | 04/2018     | 0/0                        |
| 639                            | WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA     | 01/2015                       | 326.63<br>327.00                   | 04/2018<br>-                       | 04/2018     | 0/0                        |
| 640                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA     | 01/1991                       | 229.41<br>265.35                   | 05/2018<br>-                       | 05/2018     | 0/0                        |
| 641                            | CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270( D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 ( D - [N24000432]NHAI,MAHARASHTRA | 09/2015                       | 414.51<br>-                        | -<br>-                             | 05/2018     | 0/0                        |
| 642                            | CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 ( - [N24000435]NHAI,MAHARASHTRA   | 10/2015                       | 531.13<br>-                        | -<br>-                             | 05/2018     | 0/0                        |
| 643                            | CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 ( OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA                  | 10/2015                       | 593.26<br>-                        | -<br>-                             | 05/2018     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                   |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|-----------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                           | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                   |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                 | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 644                            | 6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA                   | 08/2015                       | 505.00<br>-                        | -<br>-                             | 05/2018     | 0/0                        |
| 645                            | FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA                                             | 11/2015                       | 867.66<br>-                        | -<br>-                             | 05/2018     | 0/0                        |
| 646                            | FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH                                                                     | 12/2015                       | 596.67<br>-                        | -<br>-                             | 05/2018     | 0/0                        |
| 647                            | TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA                                  | 12/2015                       | 479.20<br>-                        | -<br>-                             | 05/2018     | 0/0                        |
| 648                            | UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA ( PKG - 1) - [N24000597]NHAI,HARYANA                                  | 05/2015                       | 600.85<br>-                        | -<br>-                             | 05/2018     | 0/0                        |
| 649                            | PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR                                                                                        | 08/2010                       | 671.30<br>-                        | 02/2013<br>-                       | 06/2018     | 0/0                        |
| 650                            | WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN  | 12/2015                       | 621.43<br>-                        | 06/2018<br>-                       | 06/2018     | 0/0                        |
| 651                            | TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU                                                       | 06/2015                       | 563.92<br>-                        | 12/2017<br>-                       | 06/2018     | 0/0                        |
| 652                            | FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH                                                                    | 05/2015                       | 261.09<br>-                        | 05/2017<br>-                       | 06/2018     | 0/0                        |
| 653                            | THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU                                                             | 11/2014                       | 563.92<br>-                        | 11/2016<br>-                       | 06/2018     | 0/0                        |
| 654                            | 4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM                   | 12/2015                       | 223.30<br>-                        | 06/2018<br>-                       | 06/2018     | 0/0                        |
| 655                            | 4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA                                                               | 12/2015                       | 602.95<br>-                        | 06/2016<br>-                       | 06/2018     | 0/0                        |
| 656                            | 4-LANING OF GHAGHRA BRIDGE TO VARANSI ( PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH                                               | 12/2015                       | 611.65<br>-                        | 06/2016<br>-                       | 06/2018     | 0/0                        |
| 657                            | 4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI ( KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL                          | 12/2015                       | 1,083.00<br>-                      | 06/2018<br>-                       | 06/2018     | 0/0                        |
| 658                            | GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH                               | 12/2015                       | 927.54<br>-                        | 06/2018<br>-                       | 06/2018     | 0/0                        |
| 659                            | FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH                                                     | 01/2016                       | 815.28<br>-                        | 06/2018<br>-                       | 06/2018     | 0/0                        |
| 660                            | FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH                                                      | 01/2016                       | 1,027.53<br>-                      | 06/2018<br>-                       | 06/2018     | 0/0                        |
| 661                            | FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH                                               | 06/2016                       | 667.00<br>-                        | 07/2018<br>-                       | 06/2018     | 0/0                        |
| 662                            | FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH                                                | 12/2015                       | 667.00<br>-                        | 06/2018<br>-                       | 06/2018     | 0/0                        |
| 663                            | 4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA     | 04/2016                       | 804.97<br>-                        | -<br>-                             | 06/2018     | 0/0                        |
| 664                            | 4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA                                                               | 01/2016                       | 574.28<br>-                        | 07/2018<br>-                       | 07/2018     | 0/0                        |
| 665                            | FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH                                                       | 01/2016                       | 830.36<br>-                        | 07/2018<br>-                       | 07/2018     | 0/0                        |
| 666                            | BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA           | 03/2016                       | 197.69<br>-                        | -<br>-                             | 07/2018     | 0/0                        |
| 667                            | FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU | 02/2016                       | 641.17<br>-                        | -<br>-                             | 07/2018     | 0/0                        |



## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                       |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|---------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                               | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                       |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                     | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 668                            | BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA                | 03/2016                       | 244.00<br>-                        | -<br>-                             | 07/2018     | 0/0                        |
| 669                            | 4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND                                        | 11/2012                       | 605.84<br>-                        | -<br>-                             | 07/2018     | 0/0                        |
| 670                            | FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU     | 03/2016                       | 641.17<br>-                        | 07/2016<br>-                       | 07/2018     | 0/0                        |
| 671                            | FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA                                                                       | 03/2015                       | 1,388.00<br>-                      | -<br>-                             | 08/2018     | 0/0                        |
| 672                            | FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU     | 02/2016                       | 707.82<br>-                        | -<br>-                             | 08/2018     | 0/0                        |
| 673                            | FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND                                                                     | 08/2016                       | 323.72<br>-                        | -<br>-                             | 08/2018     | 0/0                        |
| 674                            | FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL    | 09/2016                       | 767.03<br>-                        | -<br>-                             | 08/2018     | 0/0                        |
| 675                            | TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN       | 07/2016                       | 331.46<br>-                        | -<br>-                             | 10/2018     | 0/0                        |
| 676                            | FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA                                                                         | 12/2015                       | 1,423.96<br>-                      | -<br>-                             | 11/2018     | 0/0                        |
| 677                            | FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH                                | 01/2016                       | 1,134.97<br>-                      | -<br>-                             | 11/2018     | 0/0                        |
| 678                            | CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL                                                        | 03/2016                       | 229.37<br>-                        | -<br>-                             | 11/2018     | 0/0                        |
| 679                            | WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA        | 06/2016                       | 157.30<br>157.00                   | 06/2018<br>-                       | 11/2018     | 0/0                        |
| 680                            | 4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHAI,ASSAM               | 12/2015                       | 289.99<br>-                        | 12/2018<br>-                       | 12/2018     | 0/0                        |
| 681                            | FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR                                                 | 12/2015                       | 2,136.97<br>-                      | 12/2018<br>-                       | 12/2018     | 0/0                        |
| 682                            | 6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH                                                                      | 07/2015                       | 1,657.20<br>-                      | -<br>-                             | 01/2019     | 0/0                        |
| 683                            | FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH | 06/2015                       | 1,583.79<br>-                      | -<br>-                             | 01/2019     | 0/0                        |
| 684                            | 2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN                                                             | 08/2016                       | 320.30<br>-                        | -<br>-                             | 01/2019     | 0/0                        |
| 685                            | BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH                                  | 08/2016                       | 227.49<br>-                        | -<br>-                             | 01/2019     | 0/0                        |
| 686                            | 2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH                              | 02/2016                       | 273.20<br>-                        | -<br>-                             | 02/2019     | 0/0                        |
| 687                            | QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR                                                          | 07/2010                       | 1,987.00<br>-                      | 07/2015<br>-                       | 03/2019     | 0/0                        |
| 688                            | CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA    | 12/2015                       | 649.50<br>-                        | -<br>-                             | 03/2019     | 0/0                        |
| 689                            | FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH  | 06/2015                       | 1,012.90<br>-                      | 03/2016<br>-                       | 03/2019     | 0/0                        |
| 690                            | 4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND                                                      | 02/2016                       | 997.15<br>-                        | -<br>-                             | 03/2019     | 0/0                        |
| 691                            | HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA                                                                        | 08/2016                       | 1,167.42<br>-                      | -<br>-                             | 03/2019     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                      |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                      |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                    | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 692                            | 4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA   | 11/2016                       | 400.25<br>-                        | -<br>-                             | 03/2019     | 0/0                        |
| 693                            | 4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA   | 11/2016                       | 446.17<br>-                        | -<br>-                             | 03/2019     | 0/0                        |
| 694                            | 8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA                                                                       | 07/2015                       | 2,128.72<br>-                      | -<br>-                             | 04/2019     | 0/0                        |
| 695                            | FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR                                                                  | 12/2015                       | 1,041.10<br>-                      | -<br>-                             | 04/2019     | 0/0                        |
| 696                            | FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB                                                                          | 10/2015                       | 447.29<br>-                        | 12/2017<br>-                       | 04/2019     | 0/0                        |
| 697                            | TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR                                                        | 08/2015                       | 399.54<br>-                        | -<br>-                             | 04/2019     | 0/0                        |
| 698                            | ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH                                      | 03/2016                       | 676.73<br>-                        | -<br>-                             | 04/2019     | 0/0                        |
| 699                            | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH                 | 03/2016                       | 1,587.49<br>-                      | -<br>-                             | 04/2019     | 0/0                        |
| 700                            | FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH | 03/2016                       | 899.00<br>-                        | -<br>-                             | 04/2019     | 0/0                        |
| 701                            | 4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH                                       | 08/2016                       | 2,016.00<br>-                      | -<br>-                             | 04/2019     | 0/0                        |
| 702                            | FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA                                 | 08/2016                       | 1,664.20<br>-                      | -<br>-                             | 04/2019     | 0/0                        |
| 703                            | 4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA                                                                 | 07/2015                       | 2,288.18<br>-                      | -<br>-                             | 05/2019     | 0/0                        |
| 704                            | 4 LANING OF FAGNE - MAH-GUJ BORDER ( PKG-3) - [N24000439]NHAI,MAHARASHTRA                                                            | 07/2015                       | 1,885.74<br>-                      | -<br>-                             | 05/2019     | 0/0                        |
| 705                            | DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH                                                       | 01/2016                       | 701.12<br>-                        | -<br>-                             | 05/2019     | 0/0                        |
| 706                            | CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA                                                            | 08/2016                       | 248.97<br>-                        | -<br>-                             | 05/2019     | 0/0                        |
| 707                            | CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA       | 09/2016                       | 1,004.67<br>-                      | -<br>-                             | 05/2019     | 0/0                        |
| 708                            | CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA   | 01/2017                       | 244.90<br>-                        | -<br>-                             | 05/2019     | 0/0                        |
| 709                            | DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA       | 03/2017                       | 296.19<br>-                        | 03/2020<br>-                       | 05/2019     | 0/0                        |
| 710                            | FOUR LANING OF RAMBAN - BANIHAI SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR                                                 | 12/2015                       | 2,168.66<br>-                      | 06/2019<br>-                       | 06/2019     | 0/0                        |
| 711                            | DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH                                | 01/2016                       | 1,081.57<br>-                      | -<br>-                             | 06/2019     | 0/0                        |
| 712                            | TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN                                                        | 06/2016                       | 637.18<br>-                        | 06/2019<br>-                       | 06/2019     | 0/0                        |
| 713                            | FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN      | 06/2016                       | 763.23<br>-                        | 06/2019<br>-                       | 06/2019     | 0/0                        |
| 714                            | FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN                            | 06/2016                       | 649.00<br>-                        | 06/2019<br>-                       | 06/2019     | 0/0                        |
| 715                            | NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA                                                                             | 03/2016                       | 546.00<br>-                        | -<br>-                             | 07/2019     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                      |                               |                                    | (September 2017)                   |              |                             |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|--------------|-----------------------------|
| Sl.No                          | Project                                                                                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |              | Milestone s Achieved/ Total |
|                                |                                                                                                                                      |                               |                                    | Original / Revised                 | Antici Pated |                             |
| 1                              | 2                                                                                                                                    | 3                             | 4                                  | 5                                  | 6            | 7                           |
| 716                            | NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA                                                                             | 03/2016                       | 591.66<br>-                        | -<br>-                             | 07/2019      | 0/0                         |
| 717                            | DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA        | 09/2016                       | 2,510.04<br>-                      | -<br>-                             | 08/2019      | 0/0                         |
| 718                            | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND    | 03/2016                       | 373.07<br>-                        | 08/2016<br>-                       | 08/2019      | 0/0                         |
| 719                            | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND    | 03/2016                       | 396.52<br>-                        | 08/2016<br>-                       | 08/2019      | 0/0                         |
| 720                            | FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND    | 03/2016                       | 429.52<br>-                        | 08/2016<br>-                       | 08/2019      | 0/0                         |
| 721                            | 4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB          | 08/2016                       | 1,388.34<br>-                      | -<br>-                             | 09/2019      | 0/0                         |
| 722                            | CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH                          | 12/2016                       | 138.93<br>155.00                   | 01/2017<br>-                       | 01/2020      | 0/0                         |
| 723                            | FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA                                                                  | 02/2017                       | 904.16<br>-                        | 02/2020<br>-                       | 02/2020      | 0/0                         |
| 724                            | FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU    | 03/2017                       | 848.45<br>-                        | 03/2020<br>-                       | 03/2020      | 0/0                         |
| 725                            | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH  | 03/2017                       | 1,373.28<br>-                      | 03/2020<br>-                       | 03/2020      | 0/0                         |
| 726                            | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH | 03/2017                       | 1,184.71<br>-                      | 03/2020<br>-                       | 03/2020      | 0/0                         |
| 727                            | CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA   | 03/2017                       | 247.02<br>-                        | 03/2020<br>-                       | 03/2020      | 0/0                         |
| 728                            | 4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA                                               | 03/2017                       | 744.64<br>-                        | 03/2020<br>-                       | 03/2020      | 0/0                         |
| 729                            | 4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA                                           | 03/2017                       | 1,030.44<br>-                      | 03/2020<br>-                       | 03/2020      | 0/0                         |
| 730                            | 4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA                                            | 03/2017                       | 988.34<br>-                        | 03/2020<br>-                       | 03/2020      | 0/0                         |
| 731                            | 4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA                                          | 03/2017                       | 1,098.06<br>-                      | 03/2020<br>-                       | 03/2020      | 0/0                         |
| 732                            | CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB        | 03/2017                       | 754.54<br>-                        | 03/2020<br>-                       | 03/2020      | 0/0                         |
| 733                            | DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH | 03/2017                       | 1,989.00<br>-                      | 03/2020<br>-                       | 03/2020      | 0/0                         |
| 734                            | 4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA        | 03/2017                       | 639.79<br>-                        | 03/2020<br>-                       | 03/2020      | 0/0                         |
| 735                            | TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR          | 03/2017                       | 672.89<br>-                        | 03/2020<br>-                       | 03/2020      | 0/0                         |
| 736                            | CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR         | 03/2017                       | 235.48<br>-                        | 03/2020<br>-                       | 03/2020      | 0/0                         |
| 737                            | REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH                     | 03/2017                       | 648.32<br>-                        | 03/2020<br>-                       | 03/2020      | 0/0                         |
| 738                            | SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH                | 03/2017                       | 1,041.62<br>-                      | 03/2020<br>-                       | 03/2020      | 0/0                         |
| 739                            | 4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND                                         | 03/2017                       | 165.50<br>-                        | 03/2020<br>-                       | 03/2020      | 0/0                         |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                      |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                              | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                      |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                    | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 740                            | 4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND                               | 03/2017                       | 239.68<br>-                        | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 741                            | REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA         | 03/2017                       | 1,288.07<br>-                      | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 742                            | 6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH | 03/2017                       | 2,064.99<br>-                      | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 743                            | SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673]NHAI,KARNATAKA     | 03/2017                       | 985.41<br>-                        | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 744                            | SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA       | 03/2017                       | 831.58<br>-                        | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 745                            | SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA     | 03/2017                       | 993.16<br>-                        | 03/2020<br>-                       | 03/2020     | 0/0                        |
| 746                            | SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN                                                 | 04/2017                       | 894.00<br>-                        | 04/2020<br>-                       | 04/2020     | 0/0                        |
| 747                            | 4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH                                                   | 06/2017                       | 2,485.93<br>-                      | 06/2020<br>-                       | 06/2020     | 0/0                        |
| 748                            | 4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT                                              | 06/2017                       | 1,958.88<br>-                      | 06/2020<br>-                       | 06/2020     | 0/0                        |
| 749                            | MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM                                                          | 12/2003                       | 199.81<br>-                        | 04/2009<br>-                       | -           | 0/0                        |
| 750                            | MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM                                                    | 12/2003                       | 167.64<br>-                        | 11/2008<br>-                       | -           | 0/0                        |
| 751                            | MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM                                                         | 12/2003                       | 155.04<br>-                        | 11/2008<br>-                       | -           | 0/0                        |
| 752                            | HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM                                                                                  | 12/2003                       | 196.00<br>-                        | 07/2009<br>-                       | -           | 0/0                        |
| 753                            | CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN                                                                             | 12/2003                       | 275.00<br>-                        | 02/2010<br>-                       | -           | 0/0                        |
| 754                            | GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE                                                                                  | 12/2003                       | 604.00<br>-                        | 12/2009<br>-                       | -           | 0/0                        |
| 755                            | TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA                                                                                      | 11/2009                       | 567.00<br>-                        | 11/2013<br>-                       | -           | 0/0                        |
| 756                            | NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR                                                                                  | 05/2011                       | 2,159.00<br>-                      | 06/2015<br>-                       | -           | 0/0                        |
| 757                            | DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU                          | 06/2011                       | 600.00<br>-                        | 06/2013<br>-                       | -           | 0/0                        |
| 758                            | KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT                                                                                       | 01/2011                       | 953.88<br>-                        | 07/2013<br>-                       | -           | 0/0                        |
| 759                            | 2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR                                                                            | 05/2011                       | 664.00<br>-                        | 02/2014<br>-                       | -           | 0/0                        |
| 760                            | 2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR                                                                            | 10/2011                       | 375.09<br>-                        | 04/2014<br>-                       | -           | 0/0                        |
| 761                            | PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA                                                                                            | 03/2012                       | 1,410.00<br>-                      | 09/2014<br>-                       | -           | 0/0                        |
| 762                            | 2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU                                             | 04/2012                       | 624.00<br>-                        | 04/2014<br>-                       | -           | 0/0                        |
| 763                            | 2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN                                                                | 03/2014                       | 240.10<br>-                        | 03/2016<br>-                       | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                          |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                                  | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                          |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                        | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 764                            | REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735 (IBRAHIMPATNAM TO CHANDR - [N24000273]MORTH, ANDHRA PRADESH  | 07/2015                       | 314.43<br>-                        | -<br>-                             | -           | 0/0                        |
| 765                            | WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH, MAHARASHTRA      | 10/2015                       | 289.60<br>-                        | -<br>-                             | -           | 0/0                        |
| 766                            | CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH, MAHARASHTRA     | 12/2011                       | 156.26<br>227.31                   | -<br>03/2013                       | -           | 0/0                        |
| 767                            | CONSTRUCTION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD, CHHATISGARH      | 12/2010                       | 169.26<br>-                        | 12/2012<br>-                       | -           | 0/0                        |
| 768                            | REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD, CHHATISGARH               | 12/2014                       | 394.20<br>-                        | -<br>-                             | -           | 0/0                        |
| 769                            | REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD, CHHATISGARH        | 11/2015                       | 485.44<br>-                        | 12/2015<br>-                       | -           | 0/0                        |
| 770                            | REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110 (ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH, CHHATISGARH    | 03/2015                       | 422.34<br>-                        | -<br>-                             | -           | 0/0                        |
| 771                            | REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000 (ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD, PUNJAB           | 03/2015                       | 435.90<br>-                        | -<br>-                             | -           | 0/0                        |
| 772                            | WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD, PUNJAB            | 01/2015                       | 279.68<br>-                        | -<br>-                             | -           | 0/0                        |
| 773                            | 4-LANING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC. OF NH-71 (NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD, PUNJAB            | 11/2014                       | 463.65<br>546.00                   | -<br>-                             | -           | 0/0                        |
| 774                            | 4 LANING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC. OF NH-71 (NEW NH-52) FROM - [N24000292]PWD, PUNJAB            | 11/2014                       | 573.96<br>605.00                   | -<br>-                             | -           | 0/0                        |
| 775                            | REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150 (KATHIPUDI TO START OF K - [N24000293]MORTH, ANDHRA PRADESH | 10/2015                       | 480.21<br>-                        | -<br>-                             | -           | 0/0                        |
| 776                            | WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH, RAJASTHAN       | 10/2014                       | 269.22<br>-                        | 01/2015<br>-                       | -           | 0/0                        |
| 777                            | WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH, RAJASTHAN                        | 10/2014                       | 257.09<br>-                        | 01/2015<br>-                       | -           | 0/0                        |
| 778                            | REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH, RAJASTHAN                                        | 10/2013                       | 278.87<br>-                        | 05/2014<br>-                       | -           | 0/0                        |
| 779                            | REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH, RAJASTHAN       | 01/1991                       | 376.52<br>-                        | 04/2014<br>-                       | -           | 0/0                        |
| 780                            | WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH, RAJASTHAN       | 02/2015                       | 383.40<br>-                        | 03/2015<br>-                       | -           | 0/0                        |
| 781                            | WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD, MIZORAM            | 11/2010                       | 624.41<br>-                        | 03/2011<br>-                       | -           | 0/0                        |
| 782                            | TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD, ARUNACHAL PRADESH | 12/2011                       | 156.63<br>276.00                   | 02/2012<br>-                       | -           | 0/0                        |
| 783                            | CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD, MIZORAM            | 08/2010                       | 193.69<br>-                        | 10/2010<br>-                       | -           | 0/0                        |
| 784                            | TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD, ARUNACHAL PRADESH | 11/2010                       | 305.49<br>-                        | 03/2011<br>-                       | -           | 0/0                        |
| 785                            | TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD, ARUNACHAL PRADESH  | 03/2012                       | 207.03<br>-                        | 05/2012<br>-                       | -           | 0/0                        |
| 786                            | CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD, SIKKIM                                                 | 04/2013                       | 151.59<br>-                        | 08/2013<br>-                       | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                        |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                                | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                        |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                      | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 787                            | CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM                                             | 04/2013                       | 166.27 -                           | 08/2013 -                          | -           | 0/0                        |
| 788                            | CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM                                                | 01/2013                       | 182.28 -                           | 02/2013 -                          | -           | 0/0                        |
| 789                            | WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND         | 12/2010                       | 1,296.00 -                         | 02/2011 -                          | -           | 0/0                        |
| 790                            | CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU     | 03/2015                       | 258.97 268.92                      | 08/2015 -                          | -           | 0/0                        |
| 791                            | REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU     | 03/2015                       | 157.18 162.00                      | 07/2015 -                          | -           | 0/0                        |
| 792                            | CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH     | 03/2015                       | 629.74 -                           | - -                                | -           | 0/0                        |
| 793                            | REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA    | 01/2015                       | 225.81 -                           | - -                                | -           | 0/0                        |
| 794                            | PADI - DAHOD - [N24000353]NHAI,RAJASTHAN                                                                                               | 11/2014                       | 279.14 -                           | 05/2017 -                          | -           | 0/0                        |
| 795                            | JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN                                                                     | 10/2014                       | 264.72 -                           | 04/2017 -                          | -           | 0/0                        |
| 796                            | THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU                                                                          | 07/2014                       | 401.11 -                           | 01/2017 -                          | -           | 0/0                        |
| 797                            | 2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH                                                             | 06/2014                       | 301.04 -                           | 01/2016 -                          | -           | 0/0                        |
| 798                            | 4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB            | 02/2015                       | 483.38 -                           | - -                                | -           | 0/0                        |
| 799                            | 4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB            | 02/2015                       | 616.36 -                           | - -                                | -           | 0/0                        |
| 800                            | 4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64( - [N24000374]PWD,PUNJAB           | 02/2015                       | 486.74 -                           | - -                                | -           | 0/0                        |
| 801                            | BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH                        | 06/2015                       | 390.51 -                           | - -                                | -           | 0/0                        |
| 802                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR          | 01/1991                       | 675.00 -                           | - -                                | -           | 0/0                        |
| 803                            | CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15( - [N24000383]PWD,PUNJAB           | 03/2015                       | 312.79 -                           | - -                                | -           | 0/0                        |
| 804                            | CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB           | 07/2014                       | 319.80 -                           | - -                                | -           | 0/0                        |
| 805                            | DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB           | 12/2015                       | 766.36 -                           | - -                                | -           | 0/0                        |
| 806                            | FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH | 01/2011                       | 264.16 -                           | - -                                | -           | 0/0                        |
| 807                            | 4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB                                            | 11/2015                       | 847.02 -                           | - -                                | -           | 0/0                        |
| 808                            | 4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB                                           | 11/2015                       | 889.24 -                           | - -                                | -           | 0/0                        |
| 809                            | BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH                                                                 | 08/2015                       | 257.80 -                           | - -                                | -           | 0/0                        |



## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                   |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|-----------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                           | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                   |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                 | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 810                            | DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB       | 12/2015                       | 578.38<br>-                        | -<br>-                             | -           | 0/0                        |
| 811                            | WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE | 03/2015                       | 789.83<br>-                        | -<br>-                             | -           | 0/0                        |
| 812                            | 2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN  | 11/2012                       | 530.07<br>-                        | 08/2016<br>-                       | -           | 0/0                        |
| 813                            | 4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA                                                                        | 07/2015                       | 1,282.94<br>-                      | -<br>-                             | -           | 0/0                        |
| 814                            | 4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM                             | 01/1991                       | 520.01<br>-                        | -<br>-                             | -           | 0/0                        |
| 815                            | CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA        | 10/2015                       | 936.40<br>-                        | -<br>-                             | -           | 0/0                        |
| 816                            | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH                                             | 03/2015                       | 795.76<br>-                        | -<br>-                             | -           | 0/0                        |
| 817                            | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH                                              | 03/2015                       | 794.30<br>-                        | -<br>-                             | -           | 0/0                        |
| 818                            | NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA                                                                                   | 09/2005                       | 168.00<br>-                        | 06/2006<br>-                       | -           | 0/0                        |
| 819                            | FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR                                                                           | 08/2015                       | 556.07<br>-                        | -<br>-                             | -           | 0/0                        |
| 820                            | FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR                                                                         | 08/2015                       | 814.04<br>-                        | -<br>-                             | -           | 0/0                        |
| 821                            | FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA                                                                   | 12/2015                       | 752.28<br>-                        | -<br>-                             | -           | 0/0                        |
| 822                            | FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH                                             | 03/2015                       | 810.22<br>-                        | -<br>-                             | -           | 0/0                        |
| 823                            | FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR                                                                           | 01/1991                       | 642.41<br>-                        | -<br>-                             | -           | 0/0                        |
| 824                            | FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR                                                     | 12/2015                       | 1,167.45<br>-                      | -<br>-                             | -           | 0/0                        |
| 825                            | WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH                          | 12/2014                       | 207.88<br>-                        | -<br>-                             | -           | 0/0                        |
| 826                            | WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA       | 12/2015                       | 773.98<br>-                        | -<br>-                             | -           | 0/0                        |
| 827                            | WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA       | 12/2015                       | 819.95<br>-                        | -<br>-                             | -           | 0/0                        |
| 828                            | REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR                     | 01/1991                       | 478.35<br>-                        | -<br>-                             | -           | 0/0                        |
| 829                            | WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB      | 06/2015                       | 892.17<br>-                        | -<br>-                             | -           | 0/0                        |
| 830                            | WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB      | 06/2015                       | 899.21<br>-                        | -<br>-                             | -           | 0/0                        |
| 831                            | TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU                                                                                       | 03/2007                       | 516.00<br>-                        | 07/2008<br>-                       | -           | 0/0                        |
| 832                            | WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH                         | 12/2014                       | 207.88<br>-                        | -<br>-                             | -           | 0/0                        |
| 833                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR        | 01/1991                       | 154.62<br>-                        | -<br>-                             | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                          |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                                  | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                          |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                        | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 834                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR               | 01/1991                       | 319.68<br>-                        | -<br>-                             | -           | 0/0                        |
| 835                            | REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR            | 10/2014                       | 377.64<br>-                        | 03/2014<br>-                       | -           | 0/0                        |
| 836                            | MEERUT-BULANDSHAHR - [N24000539]NHAI,UTTAR PRADESH                                                                                       | 01/2016                       | 683.24<br>-                        | -<br>-                             | -           | 0/0                        |
| 837                            | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH         | 03/2016                       | 1,404.50<br>-                      | -<br>-                             | -           | 0/0                        |
| 838                            | 4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH | 03/2016                       | 1,396.74<br>-                      | -<br>-                             | -           | 0/0                        |
| 839                            | JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA                                                                         | 02/2016                       | 1,069.65<br>-                      | -<br>-                             | -           | 0/0                        |
| 840                            | 4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA                                               | 03/2016                       | 701.40<br>-                        | -<br>-                             | -           | 0/0                        |
| 841                            | 4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA                                                 | 03/2016                       | 870.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 842                            | FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND        | 03/2016                       | 720.00<br>-                        | -<br>-                             | -           | 0/0                        |
| 843                            | 4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND        | 03/2016                       | 1,443.00<br>-                      | -<br>-                             | -           | 0/0                        |
| 844                            | 4-LANNING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 ( - [N24000563]NHAI,UTTAR PRADESH    | 03/2016                       | 1,668.00<br>-                      | -<br>-                             | -           | 0/0                        |
| 845                            | 4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH            | 03/2016                       | 1,408.00<br>-                      | -<br>-                             | -           | 0/0                        |
| 846                            | 4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH                                 | 03/2016                       | 1,737.00<br>-                      | -<br>-                             | -           | 0/0                        |
| 847                            | FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT           | 05/2016                       | 998.18<br>-                        | -<br>-                             | -           | 0/0                        |
| 848                            | FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT           | 05/2016                       | 834.64<br>-                        | -<br>-                             | -           | 0/0                        |
| 849                            | FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT           | 05/2016                       | 723.64<br>-                        | -<br>-                             | -           | 0/0                        |
| 850                            | FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT           | 05/2016                       | 763.08<br>-                        | -<br>-                             | -           | 0/0                        |
| 851                            | SIX-LANNING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT          | 05/2016                       | 425.60<br>-                        | -<br>-                             | -           | 0/0                        |
| 852                            | CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT                                                                         | 05/2016                       | 364.56<br>-                        | -<br>-                             | -           | 0/0                        |
| 853                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR            | 01/2013                       | 322.01<br>-                        | 08/2014<br>-                       | -           | 0/0                        |
| 854                            | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR            | 11/2013                       | 683.83<br>-                        | 07/2016<br>-                       | -           | 0/0                        |
| 855                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR             | 02/2014                       | 665.50<br>-                        | 07/2016<br>-                       | -           | 0/0                        |
| 856                            | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR            | 02/2016                       | 178.85<br>-                        | 05/2016<br>-                       | -           | 0/0                        |
| 857                            | ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR            | 02/2016                       | 553.30<br>-                        | 05/2016<br>-                       | -           | 0/0                        |



## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                              |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                                      | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                              |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                            | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 858                            | FOUR LANNING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR                 | 01/2014                       | 1,408.85<br>-                      | 10/2016<br>-                       | -           | 0/0                        |
| 859                            | CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR                                 | 08/2015                       | 288.24<br>-                        | 11/2015<br>-                       | -           | 0/0                        |
| 860                            | 4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA                         | 03/2016                       | 1,142.62<br>-                      | -<br>-                             | -           | 0/0                        |
| 861                            | 4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA                         | 03/2016                       | 1,101.58<br>-                      | -<br>-                             | -           | 0/0                        |
| 862                            | BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR                                                                      | 05/2015                       | 581.84<br>-                        | 05/2017<br>-                       | -           | 0/0                        |
| 863                            | 4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN                                                       | 07/2016                       | 688.70<br>-                        | -<br>-                             | -           | 0/0                        |
| 864                            | 4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT                                     | 07/2016                       | 829.97<br>-                        | -<br>-                             | -           | 0/0                        |
| 865                            | TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND              | 07/2016                       | 458.03<br>-                        | -<br>-                             | -           | 0/0                        |
| 866                            | 4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA                                                                                    | 05/2014                       | 720.69<br>-                        | -<br>-                             | -           | 0/0                        |
| 867                            | 4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB                                                                                  | 08/2016                       | 1,169.61<br>-                      | -<br>-                             | -           | 0/0                        |
| 868                            | TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH                                         | 08/2016                       | 1,583.18<br>-                      | -<br>-                             | -           | 0/0                        |
| 869                            | FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH      | 09/2016                       | 1,273.71<br>-                      | -<br>-                             | -           | 0/0                        |
| 870                            | CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD( NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH   | 04/2016                       | 245.79<br>-                        | -<br>-                             | -           | 0/0                        |
| 871                            | FUNDED ) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACHAL - [N24000618]NHIDCL,ARUNACHAL PRADESH | 11/2015                       | 434.06<br>-                        | -<br>-                             | -           | 0/0                        |
| 872                            | SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 ( - [N24000621]NHAI,RAJASTHAN             | 09/2016                       | 1,239.82<br>-                      | -<br>-                             | -           | 0/0                        |
| 873                            | TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA             | 09/2016                       | 950.69<br>-                        | -<br>-                             | -           | 0/0                        |
| 874                            | SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN             | 09/2016                       | 1,100.19<br>-                      | -<br>-                             | -           | 0/0                        |
| 875                            | SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE           | 09/2016                       | 1,244.10<br>-                      | -<br>-                             | -           | 0/0                        |
| 876                            | 4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA                                                           | 11/2016                       | 1,071.61<br>-                      | -<br>-                             | -           | 0/0                        |
| 877                            | 4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA                                                              | 11/2016                       | 1,064.88<br>-                      | -<br>-                             | -           | 0/0                        |
| 878                            | SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA           | 11/2016                       | 290.73<br>-                        | -<br>-                             | -           | 0/0                        |
| 879                            | REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA                | 10/2016                       | 1,008.96<br>-                      | -<br>-                             | -           | 0/0                        |
| 880                            | FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH                                  | 10/2016                       | 447.75<br>-                        | -<br>-                             | -           | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                             |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                                     | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                             |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                           | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 881                            | 2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT                                                            | 12/2016                       | 417.19<br>-                        | -<br>-                             | -           | 0/0                        |
| 882                            | 6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI, RAJASTHAN           | 12/2016                       | 1,031.95<br>-                      | -<br>-                             | -           | 0/0                        |
| 883                            | CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI, UTTAR PRADESH       | 12/2016                       | 534.55<br>-                        | -<br>-                             | -           | 0/0                        |
| 884                            | CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI, UTTAR PRADESH        | 01/2017                       | 450.68<br>-                        | -<br>-                             | -           | 0/0                        |
| 885                            | SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI, GUJARAT                  | 01/2017                       | 1,251.11<br>-                      | -<br>-                             | -           | 0/0                        |
| 886                            | 4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI, MAHARASHTRA                                                | 03/2017                       | 1,059.73<br>-                      | 03/2017<br>-                       | -           | 0/0                        |
| 887                            | CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL, ARUNACHAL PRADESH     | 01/2017                       | 1,253.10<br>-                      | 03/2017<br>-                       | -           | 0/0                        |
| 888                            | TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL, ARUNACHAL PRADESH | 03/2017                       | 284.09<br>-                        | 04/2017<br>-                       | -           | 0/0                        |
| 889                            | TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL, ARUNACHAL PRADESH | 02/2017                       | 195.23<br>-                        | 04/2017<br>-                       | -           | 0/0                        |
| 890                            | TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL, ARUNACHAL PRADESH | 02/2017                       | 203.36<br>-                        | 04/2017<br>-                       | -           | 0/0                        |
| 891                            | TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL, ARUNACHAL PRADESH  | 01/2017                       | 194.66<br>-                        | 04/2017<br>-                       | -           | 0/0                        |
| 892                            | TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL, ARUNACHAL PRADESH  | 02/2017                       | 168.32<br>-                        | 04/2017<br>-                       | -           | 0/0                        |
| 893                            | TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL, ARUNACHAL PRADESH  | 02/2017                       | 180.57<br>-                        | 04/2017<br>-                       | -           | 0/0                        |
| 894                            | CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL, ARUNACHAL PRADESH | 02/2017                       | 216.71<br>-                        | 04/2017<br>-                       | -           | 0/0                        |
| 895                            | CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL, ARUNACHAL PRADESH | 02/2017                       | 167.28<br>-                        | 04/2017<br>-                       | -           | 0/0                        |
| 896                            | CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL, NAGALAND          | 02/2017                       | 507.68<br>-                        | 04/2017<br>-                       | -           | 0/0                        |
| 897                            | TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL, ARUNACHAL PRADESH  | 01/2017                       | 198.22<br>-                        | 04/2017<br>-                       | -           | 0/0                        |
| 898                            | REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD, CHHATISGARH                 | 12/2015                       | 291.05<br>-                        | -<br>-                             | -           | 0/0                        |
| 899                            | VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT                                                                                           | 03/2014                       | 503.16<br>-                        | 08/2016<br>-                       | -           | 0/0                        |
|                                | Total                                                                                                                                       |                               | 2,95,741.59<br>-                   |                                    |             | 0/0                        |
|                                |                                                                                                                                             |                               |                                    |                                    |             |                            |
|                                | <b>SHIPPING AND PORTS</b>                                                                                                                   |                               |                                    |                                    |             |                            |
| 900                            | ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU                                            | 10/2002                       | 150.00<br>-                        | 03/2006<br>-                       | 12/2017     | 0/0                        |
| 901                            | CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL, TAMIL NADU                                                      | 09/2015                       | 210.00<br>-                        | 01/2018<br>-                       | 01/2018     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                               |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
| Sl.No                          | Project                                                                                                                                       | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Date of Commissioning (Month/Year) |             | Milestones Achieved/ Total |
|                                |                                                                                                                                               |                               |                                    | Original / Revised                 | Anticipated |                            |
| 1                              | 2                                                                                                                                             | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 902                            | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA | 01/2007                       | 366.39<br>-                        | 12/2010<br>-                       | 12/2018     | 0/0                        |
| 903                            | SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU                                                                         | 06/2005                       | 2,427.40<br>-                      | 10/2008<br>-                       | -           | 0/0                        |
| 904                            | RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA                                                        | 03/2007                       | 245.67<br>-                        | 04/2009<br>-                       | -           | 0/0                        |
|                                | Total                                                                                                                                         |                               | 3,399.46<br>-                      |                                    |             | 0/0                        |
|                                |                                                                                                                                               |                               |                                    |                                    |             |                            |
|                                | <u>TELECOMMUNICATIONS</u>                                                                                                                     |                               |                                    |                                    |             |                            |
| 905                            | NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE                                                                                             | 03/2012                       | 13,334.00<br>-                     | 07/2015<br>-                       | 06/2019     | 0/0                        |
| 906                            | GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI                                                                             | 06/2016                       | 418.26<br>-                        | 06/2017<br>-                       | -           | 0/0                        |
|                                | Total                                                                                                                                         |                               | 13,752.26<br>-                     |                                    |             | 0/0                        |
|                                |                                                                                                                                               |                               |                                    |                                    |             |                            |
|                                | <u>URBAN DEVELOPMENT</u>                                                                                                                      |                               |                                    |                                    |             |                            |
| 907                            | DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI                                                                                                 | 09/2011                       | 38,585.00<br>-                     | 03/2016<br>-                       | 12/2016     | 0/0                        |
| 908                            | STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU                                                                    | 04/2014                       | 332.72<br>-                        | 09/2016<br>-                       | 11/2017     | 0/0                        |
| 909                            | CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH                                            | 12/2012                       | 188.87<br>-                        | 12/2015<br>12/2017                 | 12/2017     | 0/0                        |
| 910                            | CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD,KERALA                      | 07/2015                       | 154.00<br>-                        | 11/2015<br>-                       | 12/2017     | 0/0                        |
| 911                            | CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI                    | 07/2012                       | 884.30<br>-                        | 12/2015<br>12/2017                 | 03/2018     | 0/0                        |
| 912                            | CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU                                                                             | 06/2016                       | 3,770.00<br>-                      | 03/2018<br>-                       | 03/2018     | 0/0                        |
| 913                            | DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH                                            | 11/2012                       | 270.83<br>-                        | 11/2014<br>-                       | 10/2018     | 0/0                        |
| 914                            | LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH                                                                           | 01/2016                       | 6,928.00<br>6,928.00               | 03/2019<br>-                       | 03/2019     | 0/0                        |
| 915                            | CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND             | 12/2008                       | 114.26<br>266.00                   | 12/2013<br>-                       | 10/2019     | 0/0                        |
| 916                            | KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA                                                                                            | 07/2012                       | 5,181.79<br>-                      | 07/2017<br>-                       | 12/2019     | 0/0                        |
| 917                            | NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA                                                                                              | 08/2014                       | 8,680.00<br>-                      | 03/2018<br>-                       | 12/2019     | 0/0                        |
| 918                            | RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA                                                                              | 12/2016                       | 246.31<br>-                        | 02/2020<br>-                       | 02/2020     | 0/0                        |
| 919                            | BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA                                                                             | 02/2014                       | 26,405.14<br>-                     | 02/2019<br>-                       | 03/2020     | 0/0                        |
| 920                            | ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI                       | 10/2013                       | 1,219.21<br>2,230.23               | 10/2019<br>-                       | 03/2020     | 0/0                        |

## Details of Projects Without Milestones w.r.t. Original Schedule

| Costing Rs.150 Crore and Above |                                                                                                                                    |                               |                                    | (September 2017)                   |             |                            |
|--------------------------------|------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|------------------------------------|------------------------------------|-------------|----------------------------|
|                                |                                                                                                                                    |                               |                                    | Date of Commissioning (Month/Year) |             |                            |
| Sl.No                          | Project                                                                                                                            | Date of Approval (Month/Year) | Original/ Revised Cost (Rs. crore) | Original / Revised                 | Anticipated | Milestones Achieved/ Total |
| 1                              | 2                                                                                                                                  | 3                             | 4                                  | 5                                  | 6           | 7                          |
| 921                            | REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH | 08/2007                       | 246.90<br>-                        | -<br>-                             | -           | 0/0                        |
| 922                            | MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA                                                           | 07/2013                       | 23,136.00<br>-                     | 01/2015<br>-                       | -           | 0/0                        |
| 923                            | DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN            | 08/2014                       | 350.02<br>479.87                   | 03/2015<br>12/2017                 | -           | 0/0                        |
| 924                            | CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR                | 02/2016                       | 496.18<br>496.00                   | 06/2017<br>-                       | -           | 0/0                        |
|                                | Total                                                                                                                              |                               | 1,17,189.53<br>-                   |                                    |             | 0/0                        |
|                                |                                                                                                                                    |                               |                                    |                                    |             |                            |
|                                | Grand Total                                                                                                                        |                               | 10,17,526.08                       |                                    |             | 0/0                        |

## List of Projects Ahead of Schedule w.r.t. Latest Schedule

### Annexure - XI

| Costing Rs.150 Crore and above |                                                                                                   |                  |                                     |                              |                                         | (September 2017)      |             |
|--------------------------------|---------------------------------------------------------------------------------------------------|------------------|-------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                |                                                                                                   |                  |                                     |                              |                                         | Date of Commissioning |             |
| Sl.No                          | Project                                                                                           | Date of Approval | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated |
| 1                              | 2                                                                                                 | 3                | 4                                   | 5                            | 6                                       | 7                     | 8           |
|                                | <u>POWER</u>                                                                                      |                  |                                     |                              |                                         |                       |             |
| 1                              | NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII<br>[N18000159]                                | 2/2014           | 908.08<br>969.97                    | 969.97                       | 716.39                                  | 06/2016<br>02/2018    | 11/2017     |
|                                | Total                                                                                             |                  | 908.08<br>-                         | 969.97                       | 716.39                                  |                       |             |
|                                | <u>PETROLEUM</u>                                                                                  |                  |                                     |                              |                                         |                       |             |
| 2                              | PARADIP HYDERABAD PIPELINE<br>- [N16000194]                                                       | 1/2015           | 2,321.00<br>-                       | 2,321.00                     | 53.61                                   | 12/2020<br>-          | 08/2020     |
|                                | Total                                                                                             |                  | 2,321.00<br>-                       | 2,321.00                     | 53.61                                   |                       |             |
|                                | <u>POWER</u>                                                                                      |                  |                                     |                              |                                         |                       |             |
| 3                              | SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION<br>[N18000186]           | 3/2015           | 550.06<br>-                         | 550.06                       | 462.17                                  | 03/2018<br>-          | 09/2017     |
|                                | Total                                                                                             |                  | 550.06<br>-                         | 550.06                       | 462.17                                  |                       |             |
|                                | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                |                  |                                     |                              |                                         |                       |             |
| 4                              | FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)<br>- [N24000498]                              | 6/2016           | 667.00<br>-                         | 667.00                       | 113.68                                  | 07/2018<br>-          | 06/2018     |
|                                | Total                                                                                             |                  | 667.00<br>-                         | 667.00                       | 113.68                                  |                       |             |
|                                | <u>POWER</u>                                                                                      |                  |                                     |                              |                                         |                       |             |
| 5                              | TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A)<br>[N18000207]             | 1/2016           | 244.19<br>-                         | 244.19                       | 108.85                                  | 07/2018<br>-          | 11/2017     |
| 6                              | CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM<br>- [N18000209] | 1/2016           | 162.11<br>-                         | 162.11                       | 113.09                                  | 05/2018<br>-          | 12/2017     |
|                                | Total                                                                                             |                  | 406.30<br>-                         | 406.30                       | 221.94                                  |                       |             |
|                                | <u>PETROLEUM</u>                                                                                  |                  |                                     |                              |                                         |                       |             |
| 7                              | RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH<br>- [N16000216]                            | 1/2016           | 247.52<br>-                         | 247.52                       | 53.32                                   | 02/2019<br>-          | 12/2018     |
|                                | Total                                                                                             |                  | 247.52<br>-                         | 247.52                       | 53.32                                   |                       |             |

## List of Projects Ahead of Schedule w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                               |                  |                                     |                              |                                         | (September 2017)      |             |
|--------------------------------|---------------------------------------------------------------------------------------------------------------|------------------|-------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                |                                                                                                               |                  |                                     |                              |                                         | Date of Commissioning |             |
| Sl.No                          | Project                                                                                                       | Date of Approval | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated |
| 1                              | 2                                                                                                             | 3                | 4                                   | 5                            | 6                                       | 7                     | 8           |
|                                | <u>RAILWAYS</u>                                                                                               |                  |                                     |                              |                                         |                       |             |
| 8                              | BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.<br>- [N22000381                                          | 4/2015           | 1,172.92<br>-                       | 1,172.92                     | 74.32                                   | 03/2021<br>-          | 03/2020     |
|                                | Total                                                                                                         |                  | 1,172.92<br>-                       | 1,172.92                     | 74.32                                   |                       |             |
|                                |                                                                                                               |                  |                                     |                              |                                         |                       |             |
|                                | <u>PETROLEUM</u>                                                                                              |                  |                                     |                              |                                         |                       |             |
| 9                              | CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP<br>- [N16000226                                       | 2/2016           | 356.00<br>-                         | 356.00                       | 64.84                                   | 05/2019<br>-          | 12/2018     |
| 10                             | BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL<br>[N16000252                                        | 5/2016           | 664.00<br>-                         | 664.00                       | 137.54                                  | 12/2020<br>-          | 02/2020     |
|                                | Total                                                                                                         |                  | 1,020.00<br>-                       | 1,020.00                     | 202.38                                  |                       |             |
|                                |                                                                                                               |                  |                                     |                              |                                         |                       |             |
|                                | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                            |                  |                                     |                              |                                         |                       |             |
| 11                             | DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660 | 3/2017           | 296.19<br>-                         | 254.00                       | -                                       | 03/2020<br>-          | 05/2019     |
|                                | Total                                                                                                         |                  | 296.19<br>-                         | 254.00                       | .00                                     |                       |             |
|                                |                                                                                                               |                  |                                     |                              |                                         |                       |             |
|                                | <u>PETROLEUM</u>                                                                                              |                  |                                     |                              |                                         |                       |             |
| 12                             | MUMBAI REFINERY EXPANSION PROJECT<br>- [N16000281                                                             | 9/2015           | 4,199.00                            | 4,199.00                     | 194.97                                  | 03/2020<br>-          | 07/2019     |
|                                | Total                                                                                                         |                  | 4,199.00<br>-                       | 4,199.00                     | 194.97                                  |                       |             |
|                                |                                                                                                               |                  |                                     |                              |                                         |                       |             |
|                                | Grand Total                                                                                                   |                  | 11,788.07                           | 11,807.77                    | 2,092.78                                |                       |             |

## List of Projects on schedule w.r.t. Latest Schedule

### Annexure - XII

| Costing Rs.150 Crore and above |                                                                                  |                  |                                    |                              |                                         | (September 2017)      |             |
|--------------------------------|----------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                |                                                                                  |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                          | Project                                                                          | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                              | 2                                                                                | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
|                                | <u>CIVIL AVIATION</u>                                                            |                  |                                    |                              |                                         |                       |             |
| 1                              | CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT<br>- [N04000050]          | 1/2009           | 309.46<br>-                        | 553.53                       | 484.76                                  | 01/2011<br>09/2017    | 09/2017     |
|                                | Total                                                                            |                  | 309.46<br>-                        | 553.53                       | 484.76                                  |                       |             |
|                                | <u>COAL</u>                                                                      |                  |                                    |                              |                                         |                       |             |
| 2                              | JAGANNATHPOR OCP(3.00MTY)<br>- [N06000075]                                       | 9/2008           | 152.43<br>-                        | 459.49                       | 80.03                                   | 03/2015<br>03/2020    | 03/2020     |
| 3                              | NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY,<br>SINGRAULI - [N06000033]        | 10/2007          | 259.40<br>-                        | 486.57                       | 296.95                                  | 03/2012<br>03/2018    | 03/2018     |
| 4                              | JHANJRA COMBINED PR(3.50 MTY)<br>- [N06000020]                                   | 11/2015          | 602.86<br>-                        | 602.86                       | 268.77                                  | 03/2022<br>-          | 03/2022     |
| 5                              | PELMA OCP(15.00MTY)<br>- [N06000045]                                             | 11/2014          | 1,624.59<br>-                      | 1,624.59                     | 5.73                                    | 03/2023<br>-          | 03/2023     |
| 6                              | EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A<br>(3.0 TO 7.0 MTPA) - [N06000138] | 4/2013           | 1,458.17<br>-                      | 709.06                       | 279.07                                  | 06/2015<br>09/2019    | 09/2019     |
| 7                              | MADANNAGAR OPENCAST PROJECT<br>- [N06000140]                                     | 10/2015          | 1,875.32<br>-                      | 1,875.32                     | -                                       | 03/2024<br>-          | 03/2024     |
| 8                              | MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE<br>- [N06000142]                       | 11/2015          | 498.42<br>-                        | 498.42                       | 7.72                                    | 03/2020<br>-          | 03/2020     |
| 9                              | NORTH TISRA AND SOUTH TISRA EXPANSION OCP<br>(6MTY) - [N06000106]                | 2/2014           | 555.52<br>-                        | 555.52                       | 4.57                                    | 03/2021<br>-          | 03/2021     |
| 10                             | MAKARDHOKRA I OC<br>- [N06000119]                                                | 9/2014           | 266.23<br>-                        | 266.23                       | 138.36                                  | 03/2021<br>-          | 03/2021     |
| 11                             | DINESH OCP<br>- [N06000118]                                                      | 11/2014          | 611.16<br>-                        | 611.16                       | 360.21                                  | 03/2020<br>-          | 03/2020     |
| 12                             | GARJANBAHAL OCP<br>- [N06000117]                                                 | 11/2014          | 1,375.38<br>-                      | 1,375.38                     | 352.44                                  | 03/2021<br>-          | 03/2021     |
| 13                             | KULDA EXPN OC. (5.00 MTY)<br>- [N06000115]                                       | 6/2014           | 289.03<br>-                        | 289.03                       | -                                       | 03/2018<br>-          | 03/2018     |
| 14                             | JAGANNATH RE-ORGANISATION OC.(6.00 MTY)<br>- [N06000114]                         | 5/2014           | 337.66<br>-                        | 337.66                       | 29.74                                   | 03/2019<br>-          | 03/2019     |
| 15                             | SIARMAL OCP (40.00MTY)<br>- [N06000113]                                          | 5/2014           | 3,756.36<br>-                      | 3,756.36                     | 682.14                                  | 03/2026<br>-          | 03/2026     |
| 16                             | BASUNDHARA (WEST) OC EXTN(7.00 MTY)<br>- [N06000112]                             | 5/2014           | 479.15<br>-                        | 479.15                       | 20.80                                   | 03/2019<br>-          | 03/2019     |
| 17                             | BIJARI OC RCE (1.50 MTY)<br>- [N06000111]                                        | 5/2014           | 164.49<br>-                        | 164.49                       | 46.52                                   | 03/2020<br>-          | 03/2020     |
| 18                             | HURA - C OC (3 MTY)<br>- [N06000143]                                             | 10/2015          | 359.69<br>-                        | 359.69                       | 7.54                                    | 03/2022<br>-          | 03/2022     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                       |                  |                                    |                              |                                         | (September 2017)      |             |
|--------------------------------|---------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                |                                                                                       |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                          | Project                                                                               | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                              | 2                                                                                     | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 19                             | SINGHORI OC MINE<br>- [N06000130]                                                     | 6/2015           | 205.49<br>-                        | 205.49                       | 65.88                                   | 03/2020<br>-          | 03/2020     |
| 20                             | KAKATIYAKHANI OPENCAST-2 PROJECT<br>- [N06000129]                                     | 5/2015           | 397.09<br>-                        | 442.42                       | 19.94                                   | 03/2019<br>-          | 03/2019     |
| 21                             | NEW MAJRI UG TO OC<br>- [N06000128]                                                   | 5/2015           | 295.56<br>-                        | 295.56                       | 85.80                                   | 03/2019<br>-          | 03/2019     |
| 22                             | KANCHAN OC EXPANSION<br>- [N06000125]                                                 | 12/2014          | 371.04<br>-                        | 371.04                       | 34.53                                   | 03/2021<br>-          | 03/2021     |
| 23                             | RAJNAGAR OCP RPR (1.70 MTY)<br>- [N06000124]                                          | 12/2014          | 357.80<br>-                        | 357.80                       | 114.37                                  | 03/2021<br>-          | 03/2021     |
| 24                             | AMERA OC RCE<br>- [N06000123]                                                         | 2/2015           | 335.97<br>-                        | 335.97                       | 49.00                                   | 03/2018<br>-          | 03/2018     |
| 25                             | AMRITDHARA OC PROJECT<br>- [N06000122]                                                | 2/2015           | 481.60<br>-                        | 481.60                       | -                                       | 03/2023<br>-          | 03/2023     |
| 26                             | BHANEGAON OC<br>- [N06000121]                                                         | 2/2015           | 187.94<br>-                        | 187.94                       | 72.23                                   | 03/2023<br>-          | 03/2023     |
| 27                             | GOKUL<br>- [N06000120]                                                                | 11/2014          | 267.67<br>-                        | 267.67                       | 203.98                                  | 03/2018<br>-          | 03/2018     |
| 28                             | NEYVELI UTTAR PRADESH POWER PROJECT LIMITED<br>1980 MW<br>- [N06000152]               | 7/2016           | 17,237.00<br>-                     | 17,237.80                    | 1,116.07                                | 11/2021<br>-          | 11/2021     |
| 29                             | BHATADI EXPANSION OC MINE<br>- [N06000150]                                            | 2/2016           | 304.52<br>-                        | 304.52                       | 124.12                                  | 03/2019<br>-          | 03/2019     |
| 30                             | AMALGAMATED GONDEGAON GHATROHAN OC<br>- [N06000149]                                   | 2/2016           | 198.68<br>-                        | 198.68                       | 30.32                                   | 03/2019<br>-          | 03/2019     |
| 31                             | AMADAND OPENCAST EXPANSION PROJECT<br>- [N06000148]                                   | 3/2016           | 869.44<br>-                        | 869.44                       | 109.31                                  | 03/2021<br>-          | 03/2021     |
| 32                             | AMRAPALI OC(12MTY)<br>- [N06000103]                                                   | 2/2012           | 858.11<br>-                        | 858.11                       | 175.44                                  | 03/2020<br>-          | 03/2020     |
| 33                             | NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)<br>- [N06000095]                          | 6/2011           | 5,907.11<br>-                      | 5,907.11                     | 4,763.73                                | 12/2015<br>04/2018    | 04/2018     |
| 34                             | GEVRA EXPANSION OCP (SECL) (35-70) MTY<br>- [060100093]                               | 6/2010           | 11,816.40<br>-                     | 11,816.40                    | 2,485.40                                | 03/2023<br>-          | 03/2023     |
| 35                             | PENGANGA OCP(REVISED)<br>- [N06000066]                                                | 9/2014           | 441.82<br>-                        | 441.82                       | 174.29                                  | 03/2020<br>-          | 03/2020     |
| 36                             | KHADIA EXPANSION OPENCAST PROJECT(4 TO 10<br>MTPA,6MTPA INCREMENTAL)<br>- [N06000091] | 6/2011           | 1,131.28<br>-                      | 1,131.28                     | 431.09                                  | 03/2018<br>-          | 03/2018     |
| 37                             | KUSMUNDA EXPN.OCP(SECL)(15-50)MTY<br>- [N06000008]                                    | 8/2013           | 7,612.33<br>-                      | 7,612.33                     | 1,271.99                                | 03/2023<br>-          | 03/2023     |
| 38                             | DURGAPUR OPENCAST PROJECT<br>- [N06000136]                                            | 2/2015           | 916.24<br>-                        | 916.24                       | .71                                     | 03/2023<br>-          | 03/2023     |
| 39                             | AMGAON OPENCAST PROJECT RCE<br>- [N06000135]                                          | 7/2015           | 316.10<br>-                        | 316.10                       | 34.94                                   | 03/2020<br>-          | 03/2020     |
| 40                             | BATURA HIGHWALL PROJECT<br>- [N06000134]                                              | 7/2015           | 231.92<br>-                        | 231.92                       | -                                       | 03/2022<br>-          | 03/2022     |
| 41                             | ADASA UG TO OC<br>- [N06000133]                                                       | 8/2015           | 288.90<br>-                        | 288.90                       | -                                       | 03/2023<br>-          | 03/2023     |



## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                          |                  |                                    |                              |                                         | (September 2017)      |             |
|--------------------------------|------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                |                                                                                          |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                          | Project                                                                                  | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                              | 2                                                                                        | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 42                             | AMALGAMATED YEKONA-I YEKONA-II<br>- [N06000132]                                          | 8/2015           | 727.28<br>-                        | 727.28                       | 228.99                                  | 03/2025<br>-          | 03/2025     |
| 43                             | AMALGAMATED PAUNI-II III OC MINE<br>- [N06000131]                                        | 6/2015           | 483.69<br>-                        | 483.69                       | 71.98                                   | 03/2021<br>-          | 03/2021     |
| 44                             | VIJAY WEST OPENCAST PROJECT<br>- [N06000158]                                             | 5/2017           | 976.95<br>-                        | 976.95                       | 75.96                                   | 03/2026<br>-          | 03/2026     |
| 45                             | DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)<br>- [N06000157]                                  | 2/2017           | 328.00<br>-                        | 328.00                       | 45.31                                   | 03/2021<br>-          | 03/2021     |
| 46                             | DHANKASA UG (1.00 MTY)<br>- [N06000155]                                                  | 9/2016           | 458.07<br>-                        | 458.07                       | -                                       | 03/2022<br>-          | 03/2022     |
| 47                             | NILJAI EXPANSION (DEEP) OC (3.5 MTY)<br>- [N06000154]                                    | 8/2016           | 319.76<br>-                        | 319.76                       | -                                       | 03/2022<br>-          | 03/2022     |
| 48                             | COAL PROJECT NAME JAMUNIA UG (0.84 MTY)<br>- [N06000153]                                 | 7/2016           | 409.87<br>-                        | 409.87                       | 12.08                                   | 03/2022<br>-          | 03/2022     |
| 49                             | KALYANIKHANI 6 INCLINE PROJECT<br>- [N06000147]                                          | 12/2015          | 477.65<br>-                        | 477.65                       | -                                       | 03/2020<br>-          | 03/2020     |
| 50                             | BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)<br>- [N06000145]                                | 3/2015           | 513.63<br>-                        | 513.63                       | 167.04                                  | 12/2019<br>-          | 12/2019     |
| 51                             | HADLA LIGNITE MINE PROJECT(1.90 MTPA)<br>- [N06000144]                                   | 3/2015           | 522.45<br>-                        | 522.45                       | 5.65                                    | 09/2019<br>-          | 09/2019     |
| 52                             | KAMPTEE DEEP OC MINE<br>- [N06000141]                                                    | 11/2015          | 277.65<br>-                        | 277.65                       | .13                                     | 03/2021<br>-          | 03/2021     |
| 53                             | MALACHUA OPENCAST PROJECT<br>- [N06000139]                                               | 10/2015          | 488.33<br>-                        | 488.33                       | 1.13                                    | 03/2023<br>-          | 03/2023     |
| 54                             | CHHAL OC SEAM -III (6.00 MTY)<br>- [N06000104]                                           | 12/2013          | 610.63<br>-                        | 610.63                       | 29.03                                   | 03/2022<br>-          | 03/2022     |
| 55                             | BATURA OCP (2.0 MTY)<br>- [N06000049]                                                    | 8/2015           | 1,186.64<br>-                      | 1,186.64                     | 54.40                                   | 03/2023<br>-          | 03/2023     |
|                                | Total                                                                                    |                  | 73,476.47<br>-                     | 73,307.72                    | 14,635.43                               |                       |             |
|                                |                                                                                          |                  |                                    |                              |                                         |                       |             |
|                                | <u>DEFENCE PRODUCTION</u>                                                                |                  |                                    |                              |                                         |                       |             |
| 56                             | CONSTRUCTION WORKS PHASE 4<br>- [N39000001]                                              | 12/2016          | 167.69<br>168.00                   | 172.99                       | 22.26                                   | 05/2018<br>-          | 05/2018     |
| 57                             | CONSTRUCTION WORKS PHASE 3B<br>- [N39000002]                                             | 12/2016          | 285.95<br>286.00                   | 296.05                       | 29.91                                   | 08/2020<br>-          | 08/2020     |
|                                | Total                                                                                    |                  | 453.64<br>-                        | 469.04                       | 52.17                                   |                       |             |
|                                |                                                                                          |                  |                                    |                              |                                         |                       |             |
|                                | <u>FERTILISERS</u>                                                                       |                  |                                    |                              |                                         |                       |             |
| 58                             | NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY<br>- [N08000009]                         | 10/2014          | 197.79<br>-                        | 209.44                       | 82.72                                   | 11/2016<br>04/2019    | 04/2019     |
| 59                             | GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL.<br>- [N08000010] | 2/2016           | 482.85<br>-                        | 494.00                       | 400.18                                  | 12/2017<br>-          | 12/2017     |
|                                | Total                                                                                    |                  | 680.64<br>-                        | 703.44                       | 482.90                                  |                       |             |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                      |                  |                                    |                              |                                         | (September 2017)      |             |
|--------------------------------|------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                |                                                                                                      |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                          | Project                                                                                              | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                              | 2                                                                                                    | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
|                                | <u>HEALTH AND FAMILY WELFARE</u>                                                                     |                  |                                    |                              |                                         |                       |             |
| 60                             | CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR<br>- [N21000011]                                  | 9/2014           | 505.58<br>-                        | 505.58                       | 202.00                                  | 03/2018<br>-          | 03/2018     |
| 61                             | NEIGRIHMS SHILLONG MEGHALYA<br>- [N21000013]                                                         | 10/2016          | 363.99<br>-                        | 363.99                       | 6.00                                    | 05/2018<br>08/2019    | 08/2019     |
| 62                             | CNCI KOLKATA WEST BENGAL<br>- [N21000015]                                                            | 8/2016           | 244.00<br>-                        | 244.00                       | 70.00                                   | 09/2018<br>-          | 09/2018     |
| 63                             | NCI AIIMS JHAJJAR RESIDENTIAL HARYANA<br>- [N21000014]                                               | 7/2016           | 312.99<br>-                        | 312.99                       | 120.00                                  | 08/2018<br>-          | 08/2018     |
|                                | Total                                                                                                |                  | 1,426.56<br>-                      | 1,426.56                     | 398.00                                  |                       |             |
|                                | <u>MINES</u>                                                                                         |                  |                                    |                              |                                         |                       |             |
| 64                             | 5TH STREAM ALUMINA REFINERY EXPANSION PROJECT<br>- [N10000010]                                       | 12/2014          | 5,540.00<br>-                      | 5,540.00                     | .31                                     | 04/2021<br>-          | 04/2021     |
| 65                             | UTKAL D AND E COAL BLOCK<br>- [N10000011]                                                            | 5/2016           | 534.00<br>-                        | 534.00                       | 157.34                                  | 01/2020<br>-          | 01/2020     |
|                                | Total                                                                                                |                  | 6,074.00<br>-                      | 6,074.00                     | 157.65                                  |                       |             |
|                                | <u>PETROLEUM</u>                                                                                     |                  |                                    |                              |                                         |                       |             |
| 66                             | ASSAM RENEWAL PROJECT FOR GROUP A<br>- [N16000061]                                                   | 3/2009           | 2,465.15<br>-                      | 2,378.89                     | 2,060.68                                | 03/2013<br>09/2018    | 09/2018     |
| 67                             | PIPELINE REPLACEMENT PROJECT, AHMEDABAD<br>- [N160000159]                                            | 9/2011           | 202.25<br>-                        | 160.16                       | 106.98                                  | 07/2016<br>06/2018    | 06/2018     |
| 68                             | ENNORE-TRICHY-MADURAI LPG PIPELINE<br>- [N160000162]                                                 | 5/2013           | 711.00<br>-                        | 711.00                       | 11.12                                   | 06/2020<br>-          | 06/2020     |
| 69                             | BSVI UPGRADATION<br>- [N160000257]                                                                   | 9/2016           | 1,810.00<br>1,810.00               | 1,810.00                     | 46.43                                   | 12/2019<br>-          | 12/2019     |
| 70                             | RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE<br>- [N160000256]                                   | 10/2015          | 135.00<br>171.00                   | 170.70                       | 58.29                                   | 03/2019<br>-          | 03/2019     |
| 71                             | CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU<br>- [N160000255]                 | 5/2015           | 224.00<br>207.00                   | 207.25                       | 39.64                                   | 04/2019<br>-          | 04/2019     |
| 72                             | MOTIHARI AMLEKHGANJ PIPELINE<br>- [N160000254]                                                       | 9/2015           | 324.00<br>-                        | 324.00                       | 1.39                                    | 06/2020<br>-          | 06/2020     |
| 73                             | ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE<br>- [N160000253] | 5/2016           | 4,497.00<br>-                      | 4,497.00                     | 23.38                                   | 12/2018<br>-          | 12/2018     |
| 74                             | HALDIA BARAUNI PRODUCT PIPELINE<br>- [N160000251]                                                    | 4/2016           | 1,021.00<br>-                      | 1,021.00                     | 6.18                                    | 12/2020<br>-          | 12/2020     |
| 75                             | BRANCH PIPELINE OF PAJPL TO UNA<br>- [N160000250]                                                    | 2/2016           | 151.00<br>-                        | 151.00                       | 28.72                                   | 09/2019<br>-          | 09/2019     |
| 76                             | KOYALI AHMEDNAGAR SOLAPUR PIPELINE<br>- [N160000249]                                                 | 5/2016           | 1,945.00<br>-                      | 1,945.00                     | 17.11                                   | 08/2021<br>-          | 08/2021     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                    |                  |                                    |                              |                                         | (September 2017)      |             |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                |                                                                                                                    |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                          | Project                                                                                                            | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                              | 2                                                                                                                  | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 77                             | FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY<br>[N16000248]                                 | 7/2015           | 822.66<br>-                        | 822.66                       | 223.14                                  | 11/2018<br>-          | 11/2018     |
| 78                             | ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI - [N16000276] | 5/2016           | 261.00<br>-                        | 261.00                       | .05                                     | 01/2021<br>-          | 01/2021     |
| 79                             | DURGAPUR-HALDIA PIPELINE PROJECT<br>- [N16000275]                                                                  | 3/2017           | 1,828.00<br>-                      | 1,828.00                     | .54                                     | 12/2020<br>-          | 12/2020     |
| 80                             | BOKARO-ANGUL PIPELINE PROJECT<br>- [N16000274]                                                                     | 3/2017           | 3,212.00<br>-                      | 3,212.00                     | .29                                     | 12/2020<br>-          | 12/2020     |
| 81                             | DOBHI-DURGAPUR PIPELINE PROJECT<br>- [N16000273]                                                                   | 3/2017           | 2,250.00<br>-                      | 2,250.00                     | 3.20                                    | 12/2019<br>-          | 12/2019     |
| 82                             | DHAMRA-ANGUL PIPELINE PROJECT<br>- [N16000272]                                                                     | 3/2017           | 2,253.00<br>-                      | 2,253.00                     | 8.12                                    | 12/2019<br>-          | 12/2019     |
| 83                             | LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT<br>- [N16000271]          | 7/2015           | 2,881.40<br>-                      | 2,881.40                     | 5.67                                    | 12/2019<br>-          | 12/2019     |
| 84                             | REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM<br>[N16000270]                                                   | 7/2014           | 247.00<br>-                        | 247.00                       | -                                       | 03/2021<br>-          | 03/2021     |
| 85                             | ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE<br>- [N16000269]           | 1/2015           | 342.00<br>-                        | 342.00                       | -                                       | 03/2021<br>-          | 03/2021     |
| 86                             | ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]  | 5/2016           | 348.00<br>-                        | 348.00                       | .05                                     | 01/2021<br>-          | 01/2021     |
| 87                             | INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY<br>- [N16000284]           | 9/2016           | 208.35<br>-                        | 208.35                       | 16.93                                   | 07/2020<br>-          | 07/2020     |
| 88                             | LPG BP PROJECT KHORDHA<br>- [N16000283]                                                                            | 12/2016          | 161.59<br>-                        | 161.59                       | 28.80                                   | 12/2019<br>-          | 12/2019     |
| 89                             | SITARGANJ LPG PROJECT<br>- [N16000282]                                                                             | 2/2017           | 160.10<br>-                        | 160.10                       | 20.22                                   | 02/2020<br>-          | 02/2020     |
| 90                             | FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG<br>[N16000280]                                         | 4/2017           | 420.76<br>-                        | 420.76                       | -                                       | 09/2018<br>09/2018    | 09/2018     |
| 91                             | REDEVELOPMENT OF SANTHAL FIELD<br>- [N16000279]                                                                    | 2/2017           | 1,162.56<br>-                      | 1,162.56                     | 196.84                                  | 03/2026<br>03/2026    | 03/2026     |
| 92                             | PIPELINE NETWORK PROJECT GELEKI, ASSAM<br>- [N16000278]                                                            | 7/2016           | 249.85<br>250.00                   | 244.70                       | -                                       | 05/2020<br>-          | 05/2020     |
| 93                             | INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY<br>[N16000277]                                  | 5/2016           | 429.00<br>-                        | 429.00                       | 20.41                                   | 01/2019<br>-          | 01/2019     |
| 94                             | ADDITIONAL FACILITIES AT MANMAD FOR COVERION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]     | 5/2016           | 212.00<br>-                        | 212.00                       | .08                                     | 01/2021<br>-          | 01/2021     |
| 95                             | LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY<br>- [N16000264]                      | 5/2015           | 337.06<br>-                        | 337.06                       | 17.88                                   | 08/2018<br>-          | 08/2018     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                  |                  |                                    |                              |                                         | (September 2017)      |             |
|--------------------------------|------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                |                                                                                                                  |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                          | Project                                                                                                          | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                              | 2                                                                                                                | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 96                             | MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY<br>- [N16000263]                          | 2/2016           | 3,313.00<br>-                      | 3,313.00                     | 62.82                                   | 02/2020<br>-          | 02/2020     |
| 97                             | LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY<br>- [N16000262]                   | 5/2015           | 193.40<br>-                        | 193.40                       | 7.07                                    | 01/2019<br>-          | 01/2019     |
| 98                             | MMPL PIPELINE REROUTING PROJECT<br>- [N16000261]                                                                 | 4/2013           | 449.58<br>-                        | 449.58                       | 95.57                                   | 12/2019<br>-          | 12/2019     |
| 99                             | INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY<br>- [N16000260]        | 2/2016           | 554.00<br>-                        | 554.00                       | 24.30                                   | 02/2020<br>-          | 02/2020     |
| 100                            | AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II<br>- [N16000259]                          | 9/2016           | 571.66<br>-                        | 571.66                       | -                                       | 12/2019<br>-          | 12/2019     |
| 101                            | PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)<br>- [N16000258]                                             | 5/2016           | 406.00<br>-                        | 406.00                       | .50                                     | 10/2020<br>-          | 10/2020     |
| 102                            | KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT<br>- [N16000247]                                                      | 3/2016           | 34,012.00<br>-                     | 34,012.00                    | 252.02                                  | 06/2020<br>06/2020    | 06/2020     |
| 103                            | SONAMURA GGS AND PIPELINE PROJECT ( PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]  | 5/2016           | 215.38<br>-                        | 215.38                       | 162.34                                  | 06/2017<br>01/2018    | 01/2018     |
| 104                            | INDMAX PROJECT AT BONGAIGAON REFINERY<br>- [N16000243]                                                           | 2/2016           | 2,582.00<br>-                      | 2,582.00                     | 193.27                                  | 11/2019<br>-          | 11/2019     |
| 105                            | RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA)<br>- [N16000242]                     | 11/2016          | 230.00<br>-                        | 230.00                       | 11.46                                   | 02/2019<br>-          | 02/2019     |
| 106                            | DEVELOPMENT PLAN OF CBM - BOKARO BLOCK<br>- [N16000239]                                                          | 12/2015          | 658.62<br>-                        | 910.23                       | 2.30                                    | 03/2023<br>03/2022    | 03/2022     |
| 107                            | MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION<br>- [N16000238]                                | 9/2016           | 1,879.00<br>-                      | 1,879.00                     | 168.33                                  | 06/2020<br>-          | 06/2020     |
| 108                            | VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT<br>- [N16000237]                             | 9/2016           | 407.00<br>-                        | 407.00                       | 27.20                                   | 09/2019<br>-          | 09/2019     |
| 109                            | DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236] | 6/2016           | 423.00<br>-                        | 423.00                       | 89.60                                   | 08/2019<br>-          | 08/2019     |
| 110                            | VISAKH REFINERY MODERNISATION PROJECT<br>- [N16000235]                                                           | 7/2016           | 20,928.00<br>-                     | 20,928.00                    | 540.49                                  | 07/2020<br>-          | 07/2020     |
| 111                            | CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE<br>- [N16000233]                                                    | 4/2016           | 327.78<br>-                        | 200.00                       | 14.44                                   | 04/2018<br>-          | 04/2018     |
| 112                            | ANKLESHWAR BARODA PIPELINE PROJECT<br>- [N16000232]                                                              | 7/2014           | 199.95<br>-                        | 199.95                       | 119.90                                  | 03/2018<br>-          | 03/2018     |
| 113                            | AURAIYA PHULPUR PIPELINE PROJECT<br>- [N16000231]                                                                | 7/2015           | 1,427.94<br>-                      | 1,427.94                     | 379.02                                  | 12/2018<br>-          | 12/2018     |
| 114                            | PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY<br>- [N16000227]                             | 11/2014          | 4,588.29<br>-                      | 4,588.29                     | 871.49                                  | 08/2018<br>05/2019    | 05/2019     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                    |                  |                                    |                              |                                         | (September 2017)      |             |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                |                                                                                                                    |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                          | Project                                                                                                            | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                              | 2                                                                                                                  | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 115                            | PALAKKAD LPG PLANT<br>- [N16000225]                                                                                | 2/2015           | 184.00<br>-                        | 184.00                       | 77.07                                   | 12/2017<br>-          | 12/2017     |
| 116                            | ENNORE TERMINAL<br>- [N16000224]                                                                                   | 8/2014           | 393.00<br>-                        | 393.00                       | 198.63                                  | 04/2018<br>-          | 04/2018     |
| 117                            | PIPELINE REPLACEMENT PROJECT -4<br>- [N16000203]                                                                   | 2/2015           | 2,899.93<br>-                      | 2,098.43                     | 1,237.43                                | 05/2017<br>05/2018    | 05/2018     |
| 118                            | GAMJI REDEVELOPMENT PROJECT<br>- [N16000202]                                                                       | 5/2015           | 1,671.22<br>-                      | 567.22                       | 347.69                                  | 11/2019<br>12/2018    | 12/2018     |
| 119                            | PETCOKE EVACUATION PROJECT AT PARADIP REFINERY<br>- [N16000201]                                                    | 3/2014           | 238.50<br>-                        | 238.50                       | 167.48                                  | 03/2017<br>10/2017    | 10/2017     |
| 120                            | DAMAN DEVELOPMENT PROJECT<br>- [N16000198]                                                                         | 8/2014           | 6,086.08<br>-                      | 5,479.75                     | 2,081.12                                | 05/2019<br>10/2019    | 10/2019     |
| 121                            | MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III<br>- [N16000197]                                                   | 11/2014          | 6,068.80<br>-                      | 5,296.93                     | 4,127.27                                | 04/2019<br>03/2019    | 03/2019     |
| 122                            | PARADIP LPG IMPORT FACILITY<br>- [N16000196]                                                                       | 1/2015           | 690.00<br>-                        | 690.00                       | 133.55                                  | 07/2018<br>06/2020    | 06/2020     |
| 123                            | JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE<br>- [N16000195]       | 2/2015           | 890.00<br>-                        | 887.00                       | 220.84                                  | 10/2019<br>-          | 10/2019     |
| 124                            | AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR<br>- [N16000193] | 1/2015           | 1,823.00<br>-                      | 1,823.00                     | 15.19                                   | 12/2020<br>-          | 12/2020     |
| 125                            | MH NORTH REDEVELOPMENT PHASE III<br>- [N16000188]                                                                  | 6/2014           | 5,706.47<br>-                      | 5,813.25                     | 5,554.21                                | 05/2017<br>05/2018    | 05/2018     |
| 126                            | HALDIA LPG IMPORT FACILITY<br>- [N16000223]                                                                        | 3/2015           | 694.00<br>-                        | 694.00                       | 183.88                                  | 10/2018<br>-          | 10/2018     |
| 127                            | NEW 250 TMTA LPG PLANT AT PANAGARH<br>- [N16000222]                                                                | 8/2014           | 190.45<br>-                        | 190.45                       | 130.15                                  | 09/2017<br>03/2018    | 03/2018     |
| 128                            | SIX PIPELINE REPLACEMENT PROJECT<br>- [N16000214]                                                                  | 3/2009           | 181.02<br>-                        | 173.28                       | 126.94                                  | 01/2017<br>03/2018    | 03/2018     |
| 129                            | LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS<br>- [N16000213]                                  | 12/2015          | 3,190.69<br>-                      | 3,247.19                     | 839.54                                  | 04/2018<br>04/2018    | 04/2018     |
| 130                            | ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA<br>- [N16000212]   | 1/2015           | 4,619.94<br>-                      | 3,961.54                     | 3,386.30                                | 12/2017<br>03/2019    | 03/2019     |
| 131                            | NAWAGAM-KOYALI PIPELINE PROJECT<br>- [N16000211]                                                                   | 11/2014          | 195.63<br>-                        | 187.10                       | 139.30                                  | 09/2018<br>09/2018    | 09/2018     |
| 132                            | GAIL GAS LTD BENGALURU CGD PROJECT<br>- [N16000210]                                                                | 2/2015           | 749.00<br>-                        | 749.00                       | 468.00                                  | 02/2020<br>-          | 02/2020     |
| 133                            | DIESEL HYDROTREATOR<br>- [N16000207]                                                                               | 7/2015           | 1,031.37<br>-                      | 1,031.37                     | 305.91                                  | 01/2018<br>-          | 01/2018     |
| 134                            | URAN CHAKAN SHIKRAPUR LPG PIPELINE<br>- [N16000155]                                                                | 12/2009          | 309.81<br>-                        | 723.40                       | 381.64                                  | 10/2014<br>03/2018    | 03/2018     |
| 135                            | PARADIP HALDIA DURGAPUR LPG PIPELINE<br>- [N16000148]                                                              | 2/2011           | 913.00<br>-                        | 1,330.00                     | 953.98                                  | 06/2018<br>-          | 06/2018     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                          |                  |                                    |                              |                                         | (September 2017)      |             |
|--------------------------------|------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                |                                                                                          |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                          | Project                                                                                  | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                              | 2                                                                                        | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 136                            | DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD<br>- [N16000136]                      | 4/2012           | 600.17<br>-                        | 600.17                       | 589.36                                  | 12/2014<br>03/2018    | 03/2018     |
| 137                            | DEVELOPMENT OF C-26 CLUSTER FIELDS<br>- [N16000133]                                      | 3/2012           | 2,592.17<br>-                      | 2,592.17                     | 2,040.89                                | 05/2014<br>05/2018    | 05/2018     |
| 138                            | INTEGRATED DEVELOPMENT OF B-127 FIELDS<br>- [N16000131]                                  | 12/2011          | 2,059.63<br>-                      | 2,665.65                     | 1,633.37                                | 03/2015<br>03/2018    | 03/2018     |
| 139                            | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)<br>- [N16000128] | 3/2011           | 861.79<br>-                        | 1,256.72                     | 1,158.79                                | 05/2013<br>12/2017    | 12/2017     |
| 140                            | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)<br>- [N16000127]  | 6/2010           | 202.94<br>-                        | 330.35                       | 2.11                                    | 01/2014<br>11/2019    | 11/2019     |
| 141                            | PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I<br>- [N16000072]                                 | 3/2015           | 3,957.00<br>-                      | 3,397.00                     | 1,311.80                                | 12/2018<br>-          | 12/2018     |
| 142                            | NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY<br>- [N16000204]     | 8/2015           | 2,818.88<br>-                      | 2,818.88                     | 310.71                                  | 03/2019<br>05/2020    | 05/2020     |
| 143                            | POLYPROPYLENE PLANT AT PARADIP REFINERY<br>- [N16000179]                                 | 3/2014           | 3,150.00<br>-                      | 3,150.00                     | 1,289.32                                | 09/2017<br>12/2018    | 12/2018     |
| 144                            | DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY<br>- [N16000175]         | 3/2014           | 3,076.00<br>-                      | 4,190.00                     | 2,097.09                                | 09/2017<br>06/2018    | 06/2018     |
| 145                            | INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS<br>- [N16000172]                       | 5/2013           | 4,124.35<br>-                      | 5,637.00                     | 3,701.21                                | 04/2016<br>12/2017    | 12/2017     |
| 146                            | CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)<br>- [N16000084]                         | 6/2007           | 736.65<br>-                        | 571.47                       | 541.66                                  | 09/2011<br>06/2019    | 06/2019     |
|                                | Total                                                                                    |                  | 1,67,543.82<br>-                   | 1,67,615.43                  | 41,716.69                               |                       |             |
|                                |                                                                                          |                  |                                    |                              |                                         |                       |             |
|                                | <b>POWER</b>                                                                             |                  |                                    |                              |                                         |                       |             |
| 147                            | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT<br>- [N18000061]              | 10/2008          | 4,824.12<br>-                      | 5,071.94                     | 4,475.16                                | 10/2012<br>02/2018    | 02/2018     |
| 148                            | NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT<br>- [N18000066]                      | 2/2009           | 11,130.19<br>-                     | 13,762.80                    | 12,549.95                               | 08/2013<br>12/2017    | 12/2017     |
| 149                            | UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I<br>- [N18000157]                     | 1/2014           | 374.63<br>-                        | 374.63                       | 102.47                                  | 04/2016<br>12/2017    | 12/2017     |
| 150                            | NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX<br>- [N18000158]                       | 2/2014           | 539.82<br>-                        | 539.82                       | 386.19                                  | 06/2016<br>02/2018    | 02/2018     |
| 151                            | TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-A<br>- [N18000260]       | 4/2015           | 2,525.00<br>-                      | 2,525.00                     | 1,215.00                                | 11/2017<br>-          | 11/2017     |
| 152                            | EASTERN REGION STRENGTHENING SCHEME-XVIII<br>- [N18000258]                               | 3/2017           | 3,500.00<br>3,500.00               | 3,500.00                     | 55.00                                   | 07/2020<br>-          | 07/2020     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                    |                  |                                    |                              |                                         | (September 2017)      |             |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                |                                                                                                                    |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                          | Project                                                                                                            | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                              | 2                                                                                                                  | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 153                            | STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]                                                 | 12/2015          | 3,654.00 -                         | 3,654.00                     | 935.00                                  | 04/2019 -             | 04/2019     |
| 154                            | TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]                                      | 2/2015           | 1,750.00 -                         | 1,750.00                     | 456.00                                  | 06/2018 -             | 06/2018     |
| 155                            | TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]                                    | 4/2015           | 2,225.00 2,225.00                  | 2,225.00                     | 864.00                                  | 01/2018 -             | 01/2018     |
| 156                            | TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]                       | 4/2015           | 2,525.00 -                         | 2,525.00                     | 1,217.00                                | 11/2017 -             | 11/2017     |
| 157                            | AMELIA COAL MINE - [N18000252]                                                                                     | 1/2017           | 2,104.21 -                         | 2,104.21                     | 40.26                                   | 09/2020 -             | 09/2020     |
| 158                            | 50 MW SOLAR POWER PROJECT - [N18000251]                                                                            | 9/2017           | 287.48 -                           | 287.48                       | 27.51                                   | 03/2018 -             | 03/2018     |
| 159                            | SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]                                               | 3/2017           | 337.75 -                           | 337.75                       | -                                       | 06/2019 -             | 06/2019     |
| 160                            | HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247] | 2/2017           | 5,070.13 -                         | 5,070.13                     | 211.75                                  | 04/2020 -             | 04/2020     |
| 161                            | WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]                                                             | 2/2017           | 204.12 -                           | 204.12                       | 7.45                                    | 09/2019 -             | 09/2019     |
| 162                            | SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]                                                   | 3/2017           | 379.95 -                           | 379.95                       | 19.67                                   | 12/2019 -             | 12/2019     |
| 163                            | EASTERN REGION STRENGTHENING SCHEME XVII (PART B) - [N18000244]                                                    | 2/2017           | 235.53 -                           | 235.53                       | 5.36                                    | 06/2019 -             | 06/2019     |
| 164                            | PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243] | 3/2017           | 162.31 -                           | 162.31                       | .62                                     | 03/2019 -             | 03/2019     |
| 165                            | ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242] | 2/2017           | 322.30 -                           | 322.30                       | 15.05                                   | 02/2019 -             | 02/2019     |
| 166                            | WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]                                                            | 2/2017           | 195.05 -                           | 195.05                       | -                                       | 02/2020 -             | 02/2020     |
| 167                            | SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]                | 10/2016          | 608.24 -                           | 608.24                       | 5.12                                    | 04/2019 -             | 04/2019     |
| 168                            | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]    | 10/2016          | 408.46 -                           | 408.46                       | 40.19                                   | 01/2019 -             | 01/2019     |
| 169                            | S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238] | 3/2017           | 283.72 -                           | 283.72                       | 7.71                                    | 11/2019 -             | 11/2019     |
| 170                            | AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]                                           | 10/2016          | 167.75 -                           | 167.75                       | -                                       | 04/2019 -             | 04/2019     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                    |                  |                                    |                              |                                         | (September 2017)      |             |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                |                                                                                                                    |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                          | Project                                                                                                            | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                              | 2                                                                                                                  | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 171                            | INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]           | 3/2017           | 251.60 -                           | 251.60                       | -                                       | 06/2019 -             | 06/2019     |
| 172                            | WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]                                        | 11/2016          | 330.00 -                           | 330.00                       | 179.43                                  | 11/2017 -             | 11/2017     |
| 173                            | SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]                                                             | 9/2016           | 562.25 -                           | 562.25                       | 18.56                                   | 03/2019 -             | 03/2019     |
| 174                            | PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]                                                      | 8/2016           | 177.52 -                           | 177.52                       | 10.95                                   | 02/2019 -             | 02/2019     |
| 175                            | PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]                                     | 8/2016           | 431.89 -                           | 431.89                       | .40                                     | 02/2019 -             | 02/2019     |
| 176                            | POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230] | 7/2016           | 333.17 -                           | 333.17                       | 140.83                                  | 03/2019 -             | 03/2019     |
| 177                            | WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]                                                              | 7/2016           | 150.99 -                           | 150.99                       | 29.36                                   | 07/2018 -             | 07/2018     |
| 178                            | TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]                               | 7/2016           | 300.94 -                           | 300.94                       | 22.11                                   | 12/2018 -             | 12/2018     |
| 179                            | TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]                                               | 7/2016           | 1,429.38 -                         | 1,429.38                     | 102.89                                  | 01/2019 -             | 01/2019     |
| 180                            | EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]                                                              | 5/2016           | 167.01 -                           | 167.01                       | 30.86                                   | 11/2018 -             | 11/2018     |
| 181                            | PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]        | 4/2016           | 844.64 -                           | 844.64                       | 116.16                                  | 04/2019 -             | 04/2019     |
| 182                            | ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]                                                 | 4/2016           | 790.13 -                           | 790.30                       | 250.26                                  | 06/2019 -             | 06/2019     |
| 183                            | S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]         | 4/2016           | 287.99 -                           | 287.99                       | 73.10                                   | 06/2018 -             | 06/2018     |
| 184                            | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]                | 4/2016           | 810.48 -                           | 810.48                       | 293.68                                  | 12/2018 -             | 12/2018     |
| 185                            | HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219] | 5/2016           | 14,733.37 -                        | 14,733.37                    | 668.96                                  | 11/2019 -             | 11/2019     |
| 186                            | GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]                                      | 5/2016           | 3,519.59 -                         | 3,519.59                     | 369.73                                  | 05/2019 -             | 05/2019     |
| 187                            | EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]                                                               | 5/2016           | 766.21 -                           | 766.21                       | 12.93                                   | 11/2018 -             | 11/2018     |
| 188                            | NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]                                                         | 5/2016           | 409.19 -                           | 409.19                       | 51.42                                   | 05/2018 -             | 05/2018     |
| 189                            | EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]                                                               | 4/2016           | 454.11 -                           | 454.11                       | 51.62                                   | 04/2018 -             | 04/2018     |



## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                    |                  |                                    |                              |                                         | (September 2017)      |             |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                |                                                                                                                    |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                          | Project                                                                                                            | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                              | 2                                                                                                                  | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 190                            | TELANGANA SUPER THERMAL POWER PROJECT PHASE I<br>- [N18000212]                                                     | 1/2016           | 10,598.98<br>-                     | 10,598.98                    | 1,018.00                                | 07/2020<br>-          | 07/2020     |
| 191                            | REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS<br>- [N18000210]                              | 1/2016           | 207.88<br>-                        | 207.88                       | 77.86                                   | 07/2018<br>-          | 07/2018     |
| 192                            | SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION<br>- [N18000208]                                                      | 1/2016           | 1,455.47<br>-                      | 1,455.47                     | 471.19                                  | 07/2018<br>-          | 07/2018     |
| 193                            | KHARGONE STPP STAGE I (1320 MW)<br>- [N18000205]                                                                   | 3/2015           | 9,870.51<br>-                      | 9,870.51                     | 3,389.00                                | 09/2019<br>-          | 09/2019     |
| 194                            | GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A<br>- [N18000197]                            | 4/2015           | 1,479.30<br>-                      | 1,479.30                     | 706.27                                  | 04/2017<br>03/2018    | 03/2018     |
| 195                            | CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1)<br>- [N18000195]               | 5/2015           | 780.33<br>-                        | 780.33                       | 31.99                                   | 10/2018<br>-          | 10/2018     |
| 196                            | CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)<br>- [N18000188]               | 3/2015           | 1,394.52<br>-                      | 1,394.52                     | 19.20                                   | 05/2017<br>06/2019    | 06/2019     |
| 197                            | ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184] | 3/2015           | 197.40<br>-                        | 197.40                       | 45.02                                   | 03/2018<br>-          | 03/2018     |
| 198                            | EASTERN REGION STRENGTHENING SCHEME-III<br>- [N18000100]                                                           | 7/2010           | 1,272.80<br>-                      | 1,731.10                     | 1,413.61                                | 11/2012<br>12/2017    | 12/2017     |
| 199                            | TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP<br>[N18000180]                                                | 1/2015           | 268.80<br>-                        | 340.88                       | 160.06                                  | 03/2018<br>-          | 03/2018     |
| 200                            | INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B)<br>[N18000179]                                    | 12/2014          | 6,517.36<br>-                      | 6,517.36                     | 3,391.91                                | 04/2018<br>-          | 04/2018     |
| 201                            | RAMMAM-III HEPP (3X40 MW)<br>- [N18000178]                                                                         | 9/2014           | 1,381.84<br>-                      | 1,381.84                     | 289.00                                  | 09/2019<br>-          | 09/2019     |
| 202                            | DARLIPALLI STPP STAGE-I (2X800 MW)<br>- [N18000176]                                                                | 2/2014           | 12,532.44<br>-                     | 12,532.44                    | 6,289.00                                | 08/2018<br>-          | 08/2018     |
| 203                            | TANDA TPP STAGE-II (2X660 MW)<br>- [N18000175]                                                                     | 9/2014           | 9,188.98<br>-                      | 9,188.98                     | 3,149.00                                | 03/2019<br>-          | 03/2019     |
| 204                            | TAPOVAN-VISHNUGAD HEP (4X130MW)<br>- [N18000014]                                                                   | 11/2006          | 2,978.48<br>-                      | 3,846.30                     | 3,300.00                                | 03/2013<br>06/2019    | 06/2019     |
| 205                            | TUIRIAL HYDRO ELECTRIC PROJECT (60MW)<br>- [N18000119]                                                             | 7/1998           | 368.72<br>-                        | 1,329.43                     | 1,278.65                                | 07/2006<br>11/2017    | 11/2017     |
| 206                            | KUNADANKULAM APP TRANS SYSTEM (PGCIL)<br>- [180100258]                                                             | 5/2005           | 1,779.29<br>-                      | 2,187.32                     | 1,955.61                                | 11/2008<br>09/2018    | 09/2018     |
| 207                            | SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH<br>- [N18000116]                 | 12/2011          | 1,746.65<br>-                      | 2,228.71                     | 1,962.81                                | 08/2014<br>12/2017    | 12/2017     |
| 208                            | SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV<br>- [N18000115]                                                     | 12/2011          | 297.33<br>-                        | 426.29                       | 357.17                                  | 08/2014<br>12/2017    | 12/2017     |
| 209                            | PARE HYDRO ELECTRIC PROJECT<br>- [N18000045]                                                                       | 12/2008          | 573.99<br>-                        | 1,337.76                     | 1,499.78                                | 08/2013<br>03/2018    | 03/2018     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                  |                  |                                    |                              |                                         | (September 2017)      |              |
|--------------------------------|------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|--------------|
|                                |                                                                                                                  |                  |                                    |                              |                                         | Date of Commissioning |              |
| Sl.No                          | Project                                                                                                          | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Antici Pated |
| 1                              | 2                                                                                                                | 3                | 4                                  | 5                            | 6                                       | 7                     | 8            |
| 210                            | KAMENG HYDROELECTRIC PROJECT (NEEPCO)<br>- [180100239                                                            | 12/2004          | 2,496.90<br>-                      | 6,179.96                     | 5,971.88                                | 12/2009<br>03/2018    | 03/2018      |
| 211                            | GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C<br>- [N18000200                          | 7/2015           | 2,247.37<br>-                      | 2,247.37                     | 619.60                                  | 07/2018<br>-          | 07/2018      |
| 212                            | TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.<br>[N18000080                                       | 2/2010           | 2,144.00<br>-                      | 2,932.88                     | 2,564.46                                | 12/2012<br>02/2018    | 02/2018      |
| 213                            | TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077 | 4/2010           | 4,404.57<br>-                      | 5,135.01                     | 3,453.64                                | 01/2015<br>03/2018    | 03/2018      |
| 214                            | GADARWARA SUPER THERMAL POWER PROJECT STAGE-I<br>- [N18000151                                                    | 3/2013           | 11,638.55<br>-                     | 11,638.55                    | 8,147.00                                | 09/2017<br>03/2018    | 03/2018      |
|                                | Total                                                                                                            |                  | 1,58,387.68<br>-                   | 1,70,612.39                  | 76,621.42                               |                       |              |
|                                |                                                                                                                  |                  |                                    |                              |                                         |                       |              |
|                                | <u>RAILWAYS</u>                                                                                                  |                  |                                    |                              |                                         |                       |              |
| 215                            | ROSA-SITAPUR CANTT-BURHWAL DOUBLING<br>- [N22000347                                                              | 3/2015           | 1,750.00<br>-                      | 1,295.42                     | 19.80                                   | 03/2022<br>-          | 03/2022      |
| 216                            | KIUL - GAYA DOUBLING PROJECT<br>- [N22000349                                                                     | 12/2015          | 1,200.20<br>-                      | 1,200.20                     | -                                       | 12/2020<br>-          | 12/2020      |
| 217                            | RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE<br>[N22000350                                   | 12/2015          | 1,491.47<br>-                      | 1,491.47                     | -                                       | 12/2020<br>-          | 12/2020      |
| 218                            | MATHURA-PLWAL 4TH LINE (80KM)<br>- [N22000372                                                                    | 4/2015           | 524.00<br>668.00                   | 668.00                       | -                                       | 03/2020<br>-          | 03/2020      |
| 219                            | JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE<br>- [N22000380                              | 4/2015           | 701.61<br>-                        | 701.61                       | 37.66                                   | 03/2021<br>-          | 03/2021      |
| 220                            | ROURKELA JHARSUGUDA THIRD LINE 101 KM<br>- [N22000395                                                            | 11/2015          | 969.83<br>-                        | 969.83                       | -                                       | 03/2020<br>-          | 03/2020      |
| 221                            | KATNI GRADE SEPARATOR/BYE PASS<br>- [N22000416                                                                   | 8/2016           | 582.13<br>-                        | 582.13                       | -                                       | 03/2020<br>-          | 03/2020      |
| 222                            | KATNI-BINA 3RD LINE (263 KM)<br>- [N22000415                                                                     | 6/2016           | 2,478.23<br>-                      | 2,478.23                     | -                                       | 03/2022<br>-          | 03/2022      |
| 223                            | BINA - KOTA DOUBLING WITH RE<br>- [N22000414                                                                     | 4/2011           | 1,485.65<br>-                      | 1,485.85                     | 685.71                                  | 12/2020<br>-          | 12/2020      |
| 224                            | BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION<br>- [N22000413                                                   | 3/2012           | 1,183.25<br>-                      | 1,183.30                     | 723.70                                  | 12/2020<br>-          | 12/2020      |
| 225                            | BANASPANI- JAKHPURA - DOUBLING<br>- [N22000412                                                                   | 3/2009           | 942.95<br>-                        | 942.95                       | 795.83                                  | 03/2019<br>-          | 03/2019      |
| 226                            | RAIPUR - TITLAGARH - DOUBLING<br>- [N22000411                                                                    | 3/2007           | 758.09<br>-                        | 758.09                       | 632.15                                  | 03/2020<br>-          | 03/2020      |
| 227                            | SAMBALPUR - TITLAGARH - DOUBLING<br>- [N22000410                                                                 | 3/2006           | 960.18<br>-                        | 960.18                       | 704.78                                  | 03/2020<br>-          | 03/2020      |
| 228                            | DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)<br>[N22000407                | 3/2009           | 1,514.45<br>-                      | 1,514.45                     | -                                       | 03/2020<br>-          | 03/2020      |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                              |                  |                                    |                              |                                         | (September 2017)      |             |
|--------------------------------|--------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                |                                                                                                              |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                          | Project                                                                                                      | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                              | 2                                                                                                            | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 229                            | DIGHI PORT NEW LINE<br>- [N22000408]                                                                         | 4/2015           | 723.78<br>-                        | 723.78                       | .22                                     | 12/2025<br>-          | 12/2025     |
| 230                            | MULTI MODAL LOGISTICS PARK AT BARHI<br>- [N22000426]                                                         | 12/2015          | 346.32<br>-                        | 300.00                       | 204.51                                  | 03/2019<br>-          | 03/2019     |
| 231                            | MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR<br>- [N22000425]                                                   | 5/2014           | 207.00<br>-                        | 207.00                       | 142.00                                  | 03/2018<br>-          | 03/2018     |
| 232                            | MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM<br>- [N22000424]                                                | 1/2013           | 387.70<br>-                        | 387.70                       | 351.00                                  | 03/2018<br>-          | 03/2018     |
| 233                            | MULTI MODAL LOGISTICS PARK AT SWARUPGANJ<br>- [N22000423]                                                    | 4/2012           | 471.82<br>-                        | 471.82                       | 19.91                                   | 03/2019<br>-          | 03/2019     |
| 234                            | MULTI MODAL LOGISTICS TRANSPORT AT MIHAN<br>- [N22000422]                                                    | 10/2013          | 305.00<br>-                        | 305.00                       | -                                       | 03/2019<br>-          | 03/2019     |
| 235                            | MULTI MODAL LOGISTICS PARK AT KATHUWAS<br>- [N22000421]                                                      | 1/2011           | 493.17<br>-                        | 493.17                       | 383.12                                  | 03/2018<br>-          | 03/2018     |
| 236                            | RAJNANDGAON - NAGPUR - 3RD LINE (SECR)<br>- [N22000420]                                                      | 9/2016           | 1,273.00<br>1,908.00               | 1,908.00                     | -                                       | 12/2021<br>-          | 12/2021     |
| 237                            | EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL<br>- [N22000418]           | 4/2016           | 5,200.00<br>-                      | 5,200.00                     | -                                       | 03/2020<br>-          | 03/2020     |
| 238                            | RAMNA - SINGRAULI DOUBLING<br>- [N22000417]                                                                  | 8/2015           | 2,436.21<br>-                      | 2,436.21                     | 44.89                                   | 03/2020<br>-          | 03/2020     |
| 239                            | RISHIKESH - KARNAPRAYAG NEW LINE<br>- [N22000406]                                                            | 4/2011           | 4,295.30<br>-                      | 1,621.60                     | 167.32                                  | 12/2026<br>-          | 12/2026     |
| 240                            | MAU-GHAZIPUR-TARIGHAT NEW LINE<br>- [N22000405]                                                              | 4/2015           | 1,765.90<br>-                      | 1,765.90                     | 26.79                                   | 12/2025<br>-          | 12/2025     |
| 241                            | LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC<br>- [N22000404]                                                 | 4/2011           | 927.01<br>-                        | 977.00                       | 733.32                                  | 03/2019<br>-          | 03/2019     |
| 242                            | SECUNDERABAD-MAHABUBNAGAR DOUBLING<br>- [N22000403]                                                          | 4/2015           | 728.10<br>-                        | 728.10                       | 15.05                                   | 12/2024<br>-          | 12/2024     |
| 243                            | VARANASI-MODHOSINGH-ALLAHABAD DOUBLING<br>- [N22000401]                                                      | 4/2015           | 750.55<br>-                        | 750.56                       | 17.25                                   | 12/2024<br>-          | 12/2024     |
| 244                            | RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]   | 4/1995           | 524.43<br>-                        | 939.00                       | -                                       | 12/2021<br>-          | 12/2021     |
| 245                            | TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397] | 1/1991           | 763.18<br>-                        | 1,428.00                     | -                                       | 12/2021<br>-          | 12/2021     |
| 246                            | BONDAMUNDA RANCHI DOUBLING<br>- [N22000396]                                                                  | 3/2016           | 1,724.20<br>-                      | 1,724.20                     | -                                       | 03/2021<br>-          | 03/2021     |
| 247                            | MULTI MODAL LOGISTICS PARK AT KAKINADA<br>- [N22000431]                                                      | 8/2016           | 234.50<br>-                        | 234.50                       | .14                                     | 03/2019<br>-          | 03/2019     |
| 248                            | MULTI MODAL LOGISTICS PARK AT VARNAMA<br>- [N22000428]                                                       | 10/2013          | 343.00<br>-                        | 343.00                       | 236.64                                  | 03/2019<br>-          | 03/2019     |
| 249                            | MULTI MODAL LOGISTICS PARK AT TIHI<br>- [N22000427]                                                          | 12/2015          | 174.00<br>-                        | 174.00                       | 90.63                                   | 03/2019<br>-          | 03/2019     |
| 250                            | DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY<br>- [N22000394]                    | 3/2015           | 636.38<br>-                        | 636.38                       | 169.16                                  | 03/2021<br>-          | 03/2021     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                   |                  |                                    |                              |                                         | (September 2017)      |             |
|--------------------------------|-------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                |                                                                                                                   |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                          | Project                                                                                                           | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                              | 2                                                                                                                 | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 251                            | JAGADALPUR-KORAPUT DOUBLING<br>- [N22000376                                                                       | 4/2015           | 1,547.38<br>-                      | 1,547.38                     | 34.69                                   | 03/2021<br>-          | 03/2021     |
| 252                            | KATNI - SINGRAULI DOUBLING PROJECT<br>- [N22000351                                                                | 12/2015          | 1,762.94<br>-                      | 1,762.94                     | -                                       | 12/2020<br>-          | 12/2020     |
|                                | Total                                                                                                             |                  | 44,562.91<br>-                     | 43,296.95                    | 6,236.27                                |                       |             |
|                                |                                                                                                                   |                  |                                    |                              |                                         |                       |             |
|                                | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                |                  |                                    |                              |                                         |                       |             |
| 253                            | FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305 | 5/2015           | 454.89<br>-                        | 454.89                       | 22.74                                   | 05/2018<br>-          | 05/2018     |
| 254                            | 4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319 | 6/2015           | 437.39<br>-                        | 437.39                       | 21.86                                   | 06/2018<br>-          | 06/2018     |
| 255                            | FOUR LANING OF JHANJI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320  | 6/2015           | 463.49<br>-                        | 463.49                       | 9.26                                    | 06/2018<br>-          | 06/2018     |
| 256                            | FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322             | 3/2015           | 168.39<br>-                        | 168.39                       | 16.84                                   | 11/2018<br>-          | 11/2018     |
| 257                            | 2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324 | 3/2015           | 194.11<br>-                        | 194.11                       | 30.54                                   | 05/2018<br>-          | 05/2018     |
| 258                            | STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411  | 11/2014          | 218.31<br>-                        | 218.31                       | -                                       | 02/2018<br>-          | 02/2018     |
| 259                            | MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A [N24000410                        | 6/2015           | 641.02<br>-                        | 641.02                       | 89.88                                   | 12/2017<br>-          | 12/2017     |
| 260                            | STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409 | 5/2011           | 176.22<br>-                        | 176.22                       | -                                       | 02/2018<br>-          | 02/2018     |
| 261                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397 | 1/1991           | 322.00<br>-                        | 322.00                       | 56.41                                   | 03/2018<br>-          | 03/2018     |
| 262                            | ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393                                          | 6/2015           | 774.57<br>-                        | 774.57                       | -                                       | 03/2018<br>-          | 03/2018     |
| 263                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379 | 1/1991           | 218.63<br>-                        | 218.63                       | 29.27                                   | 10/2017<br>-          | 10/2017     |
| 264                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376 | 1/1991           | 219.40<br>-                        | 219.40                       | -                                       | 01/2018<br>-          | 01/2018     |
| 265                            | PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357                                         | 9/2015           | 567.51<br>-                        | 567.51                       | -                                       | 03/2018<br>-          | 03/2018     |
| 266                            | UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA( PKG - 2) - [N24000358                                 | 10/2015          | 562.34<br>-                        | 562.34                       | 281.73                                  | 04/2018<br>-          | 04/2018     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                   |                  |                                    |                              |                                         | (September 2017)      |             |
|--------------------------------|-------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                |                                                                                                                   |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                          | Project                                                                                                           | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                              | 2                                                                                                                 | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 267                            | BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445  | 8/2014           | 822.90<br>-                        | 822.90                       | -                                       | 04/2018<br>-          | 04/2018     |
| 268                            | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-IV)<br>- [N24000440                                   | 9/2015           | 789.31<br>-                        | 789.31                       | 603.92                                  | 03/2018<br>-          | 03/2018     |
| 269                            | 4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438      | 12/2015          | 289.99<br>-                        | 289.99                       | -                                       | 12/2018<br>-          | 12/2018     |
| 270                            | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-V)<br>- [N24000436                                    | 9/2015           | 664.53<br>-                        | 664.53                       | 390.38                                  | 03/2018<br>-          | 03/2018     |
| 271                            | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-VI)<br>- [N24000433                                   | 9/2015           | 768.56<br>-                        | 768.56                       | 512.89                                  | 03/2018<br>-          | 03/2018     |
| 272                            | 4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430                | 12/2015          | 223.30<br>-                        | 223.30                       | -                                       | 06/2018<br>-          | 06/2018     |
| 273                            | 4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429      | 12/2015          | 225.02<br>-                        | 159.20                       | -                                       | 12/2018<br>-          | 12/2018     |
| 274                            | 2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28<br>- [N24000421                             | 3/2015           | 235.08<br>-                        | 235.08                       | -                                       | 05/2018<br>-          | 05/2018     |
| 275                            | REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414 | 1/1991           | 229.41<br>-                        | 229.41                       | 6.65                                    | 05/2018<br>-          | 05/2018     |
| 276                            | FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589                         | 6/2016           | 649.00<br>-                        | 649.00                       | -                                       | 06/2019<br>-          | 06/2019     |
| 277                            | FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587  | 6/2016           | 763.23<br>-                        | 763.23                       | -                                       | 06/2019<br>-          | 06/2019     |
| 278                            | TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586                                                     | 6/2016           | 637.18<br>-                        | 637.18                       | -                                       | 06/2019<br>-          | 06/2019     |
| 279                            | WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523     | 12/2011          | 159.39<br>-                        | 159.39                       | -                                       | 11/2017<br>-          | 11/2017     |
| 280                            | FOUR LANING OF AURANGABAD - YEDISHI - [N24000508                                                                  | 7/2015           | 1,871.34<br>-                      | 1,871.34                     | 2,601.04                                | 01/2018<br>-          | 01/2018     |
| 281                            | FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500                                                           | 1/2016           | 830.36<br>-                        | 830.36                       | 473.08                                  | 07/2018<br>-          | 07/2018     |
| 282                            | FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)<br>- [N24000499                                                | 12/2015          | 667.00<br>-                        | 667.00                       | 164.32                                  | 06/2018<br>-          | 06/2018     |
| 283                            | FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)<br>- [N24000493                                                      | 1/2016           | 1,027.53<br>-                      | 1,027.53                     | 152.94                                  | 06/2018<br>-          | 06/2018     |
| 284                            | FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)<br>- [N24000491                                                     | 1/2016           | 815.28<br>-                        | 815.28                       | 90.98                                   | 06/2018<br>-          | 06/2018     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                    |                  |                                    |                              |                                         | (September 2017)      |             |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                |                                                                                                                    |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                          | Project                                                                                                            | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                              | 2                                                                                                                  | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 285                            | FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A<br>- [N24000488]                                                 | 12/2015          | 2,136.97<br>-                      | 2,136.97                     | -                                       | 12/2018<br>-          | 12/2018     |
| 286                            | FOUR LANING OF KHARAR - KURALI SECTION OF NH-21<br>- [N24000484]                                                   | 12/2015          | 239.23<br>-                        | 239.23                       | 161.60                                  | 12/2017<br>-          | 12/2017     |
| 287                            | WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]  | 3/2015           | 226.31<br>226.00                   | 226.00                       | -                                       | 10/2017<br>-          | 10/2017     |
| 288                            | WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]    | 2/2015           | 239.91<br>240.00                   | 240.00                       | -                                       | 10/2017<br>-          | 10/2017     |
| 289                            | WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640] | 1/2015           | 326.63<br>327.00                   | 327.00                       | -                                       | 04/2018<br>-          | 04/2018     |
| 290                            | FOUR LANING OF PARWANOO - SOLAN<br>- [N24000479]                                                                   | 9/2015           | 934.46<br>-                        | 934.46                       | 175.87                                  | 03/2018<br>-          | 03/2018     |
| 291                            | GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93<br>- [N24000478]                                | 12/2015          | 927.54<br>-                        | 927.54                       | 29.17                                   | 06/2018<br>-          | 06/2018     |
| 292                            | JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400<br>- [N24000475]                    | 11/2015          | 628.45<br>-                        | 628.45                       | 20.74                                   | 03/2018<br>-          | 03/2018     |
| 293                            | FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A<br>- [N24000471]                                                  | 12/2015          | 2,168.66<br>-                      | 2,168.66                     | -                                       | 06/2019<br>-          | 06/2019     |
| 294                            | 4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI ( KM 0.00 TO KM . 83.785)<br>- [N24000463]                        | 12/2015          | 1,083.00<br>-                      | 1,083.00                     | -                                       | 06/2018<br>-          | 06/2018     |
| 295                            | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-II)<br>- [N24000450]                                   | 9/2015           | 785.78<br>-                        | 785.78                       | 587.77                                  | 03/2018<br>-          | 03/2018     |
| 296                            | 4 LANING OF AMBALA - KAITHAL - PACKAGE -2<br>- [N24000448]                                                         | 1/2016           | 574.28<br>-                        | 574.28                       | 185.12                                  | 07/2018<br>-          | 07/2018     |
| 297                            | DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY ( PKG-III)<br>- [N24000446]                                  | 9/2015           | 788.51<br>-                        | 788.51                       | 321.86                                  | 03/2018<br>-          | 03/2018     |
| 298                            | 4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00)<br>- [N24000669]                                  | 3/2017           | 165.50<br>-                        | 172.16                       | -                                       | 03/2020<br>-          | 03/2020     |
| 299                            | SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000<br>- [N24000668]              | 3/2017           | 1,041.62<br>-                      | 1,187.10                     | -                                       | 03/2020<br>-          | 03/2020     |
| 300                            | REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER<br>- [N24000667]                   | 3/2017           | 648.32<br>-                        | 503.10                       | -                                       | 03/2020<br>-          | 03/2020     |
| 301                            | CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666] | 3/2017           | 235.48<br>-                        | 227.77                       | -                                       | 03/2020<br>-          | 03/2020     |
| 302                            | TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]  | 3/2017           | 672.89<br>-                        | 736.01                       | -                                       | 03/2020<br>-          | 03/2020     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                   |                  |                                    |                              |                                         | (September 2017)      |             |
|--------------------------------|-------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                |                                                                                                                   |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                          | Project                                                                                                           | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                              | 2                                                                                                                 | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 303                            | 4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664  | 3/2017           | 639.79<br>-                        | 552.90                       | -                                       | 03/2020<br>-          | 03/2020     |
| 304                            | DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663 | 3/2017           | 1,989.00<br>-                      | 1,989.00                     | -                                       | 03/2020<br>-          | 03/2020     |
| 305                            | CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662 | 3/2017           | 754.54<br>-                        | 756.27                       | -                                       | 03/2020<br>-          | 03/2020     |
| 306                            | 4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661                                        | 3/2017           | 1,098.06<br>-                      | 1,160.64                     | -                                       | 03/2020<br>-          | 03/2020     |
| 307                            | RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695                                                                  | 4/2017           | 388.00<br>-                        | 447.37                       | -                                       | 10/2017<br>-          | 10/2017     |
| 308                            | 4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693                                        | 6/2017           | 1,958.88<br>-                      | 1,958.88                     | -                                       | 06/2020<br>-          | 06/2020     |
| 309                            | 4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692                                                      | 6/2017           | 2,485.93<br>-                      | 2,485.93                     | -                                       | 06/2020<br>-          | 06/2020     |
| 310                            | SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691                                             | 4/2017           | 894.00<br>-                        | 894.00                       | -                                       | 04/2020<br>-          | 04/2020     |
| 311                            | SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675 | 3/2017           | 993.16<br>-                        | 1,434.00                     | -                                       | 03/2020<br>-          | 03/2020     |
| 312                            | SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674   | 3/2017           | 831.58<br>-                        | 1,177.00                     | -                                       | 03/2020<br>-          | 03/2020     |
| 313                            | SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673 | 3/2017           | 985.41<br>-                        | 1,200.00                     | -                                       | 03/2020<br>-          | 03/2020     |
| 314                            | 6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672 | 3/2017           | 2,064.99<br>-                      | 2,447.00                     | -                                       | 03/2020<br>-          | 03/2020     |
| 315                            | REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671  | 3/2017           | 1,288.07<br>-                      | 1,420.00                     | -                                       | 03/2020<br>-          | 03/2020     |
| 316                            | 4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670                           | 3/2017           | 239.68<br>-                        | 235.90                       | -                                       | 03/2020<br>-          | 03/2020     |
| 317                            | 4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658                                          | 3/2017           | 988.34<br>-                        | 1,043.28                     | -                                       | 03/2020<br>-          | 03/2020     |
| 318                            | 4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657                                         | 3/2017           | 1,030.44<br>-                      | 1,065.51                     | -                                       | 03/2020<br>-          | 03/2020     |
| 319                            | 4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656                                             | 3/2017           | 744.64<br>-                        | 982.00                       | -                                       | 03/2020<br>-          | 03/2020     |
| 320                            | CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655 | 3/2017           | 247.02<br>-                        | 157.49                       | -                                       | 03/2020<br>-          | 03/2020     |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                   |                  |                                    |                              |                                         | (September 2017)      |             |
|--------------------------------|-------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                |                                                                                                                   |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                          | Project                                                                                                           | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                              | 2                                                                                                                 | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 321                            | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654 | 3/2017           | 1,184.71<br>-                      | 1,310.00                     | -                                       | 03/2020<br>-          | 03/2020     |
| 322                            | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653  | 3/2017           | 1,373.28<br>-                      | 1,373.28                     | -                                       | 03/2020<br>-          | 03/2020     |
| 323                            | FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652 | 3/2017           | 848.45<br>-                        | 848.45                       | -                                       | 03/2020<br>-          | 03/2020     |
| 324                            | FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651                                                                | 2/2017           | 904.16<br>-                        | 904.16                       | -                                       | 02/2020<br>-          | 02/2020     |
| 325                            | JAISALMER - BARMER - [N24000348                                                                                   | 8/2015           | 482.27<br>-                        | 482.27                       | -                                       | 02/2018<br>-          | 02/2018     |
| 326                            | FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349      | 5/2015           | 1,387.11<br>-                      | 1,387.11                     | 658.16                                  | 11/2017<br>-          | 11/2017     |
| 327                            | FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347                                          | 8/2015           | 723.54<br>-                        | 723.54                       | 558.12                                  | 02/2018<br>-          | 02/2018     |
| 328                            | TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343                                     | 9/2015           | 341.61<br>-                        | 341.61                       | 308.23                                  | 09/2017<br>-          | 09/2017     |
| 329                            | TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 ( NEW NH NO -50) - [N24000342  | 5/2015           | 709.00<br>-                        | 709.00                       | 203.50                                  | 09/2017<br>-          | 09/2017     |
| 330                            | TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER ( UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337 | 8/2015           | 538.08<br>-                        | 538.08                       | -                                       | 02/2018<br>-          | 02/2018     |
| 331                            | CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261 | 1/2014           | 267.16<br>352.00                   | 352.05                       | .02                                     | 11/2017<br>-          | 11/2017     |
| 332                            | CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260 | 1/2014           | 255.75<br>348.00                   | 348.43                       | .02                                     | 09/2017<br>-          | 09/2017     |
| 333                            | WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333  | 12/2015          | 621.43<br>-                        | 621.43                       | -                                       | 06/2018<br>-          | 06/2018     |
| 334                            | 2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328 | 10/2014          | 369.00<br>-                        | 369.00                       | 36.90                                   | 03/2018<br>-          | 03/2018     |
| 335                            | 2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327             | 3/2015           | 394.00<br>-                        | 394.00                       | -                                       | 06/2018<br>-          | 06/2018     |
| 336                            | CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326 | 7/2015           | 197.16<br>-                        | 197.16                       | 38.50                                   | 10/2018<br>-          | 10/2018     |
| 337                            | 2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325                             | 10/2015          | 179.82<br>-                        | 179.82                       | 8.99                                    | 01/2019<br>-          | 01/2019     |



## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                  |                  |                                    |                              |                                         | (September 2017)      |             |
|--------------------------------|------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                |                                                                                                                  |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                          | Project                                                                                                          | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                              | 2                                                                                                                | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 338                            | 4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323 | 10/2014          | 588.95<br>-                        | 588.95                       | 80.00                                   | 11/2018<br>-          | 11/2018     |
| 339                            | FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321                     | 6/2016           | 829.00<br>-                        | 829.00                       | 59.85                                   | 01/2019<br>-          | 01/2019     |
|                                | <b>Total</b>                                                                                                     |                  | 62,726.23<br>-                     | 64,811.39                    | 8,989.15                                |                       |             |
|                                |                                                                                                                  |                  |                                    |                              |                                         |                       |             |
|                                | <u>SHIPPING AND PORTS</u>                                                                                        |                  |                                    |                              |                                         |                       |             |
| 340                            | CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066                                              | 2/2015           | 244.50<br>258.00                   | 258.33                       | .14                                     | 12/2017<br>-          | 12/2017     |
| 341                            | CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068                                           | 9/2015           | 210.00<br>-                        | 210.00                       | -                                       | 01/2018<br>-          | 01/2018     |
|                                | <b>Total</b>                                                                                                     |                  | 454.50<br>-                        | 468.33                       | .14                                     |                       |             |
|                                |                                                                                                                  |                  |                                    |                              |                                         |                       |             |
|                                | <u>STEEL</u>                                                                                                     |                  |                                    |                              |                                         |                       |             |
| 342                            | CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110         | 12/2007          | 200.00<br>-                        | 200.00                       | 131.15                                  | 03/2018<br>-          | 03/2018     |
| 343                            | CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112                                                         | 4/2013           | 170.00<br>-                        | 170.00                       | 88.91                                   | 04/2018<br>-          | 04/2018     |
| 344                            | NMDC INTEGRATED STEEL PLANT - [N12000086                                                                         | 1/2010           | 15,525.00<br>-                     | 15,525.00                    | 12,816.08                               | 05/2015<br>10/2018    | 10/2018     |
| 345                            | EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097           | 2/2014           | 4,749.00<br>-                      | 4,749.00                     | 69.35                                   | 09/2017<br>-          | 09/2017     |
| 346                            | FORGED WHEEL PLANT - [N12000116                                                                                  | 4/2014           | 1,682.85<br>-                      | 1,682.85                     | 63.22                                   | 09/2018<br>-          | 09/2018     |
| 347                            | REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118                                                         | 11/2016          | 262.87<br>-                        | 262.87                       | 35.71                                   | 06/2019<br>-          | 06/2019     |
| 348                            | 2 MTPA PELLET PLANT AT NAGARNAR - [N12000115                                                                     | 11/2015          | 818.00<br>-                        | 818.00                       | 25.88                                   | 06/2020<br>-          | 06/2020     |
| 349                            | ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120                                                          | 7/2015           | 465.85<br>-                        | 465.85                       | 35.89                                   | 07/2018<br>-          | 07/2018     |
| 350                            | CENTRAL DISPATCH YARD - [N12000119                                                                               | 8/2015           | 320.66<br>-                        | 320.66                       | 15.23                                   | 08/2018<br>-          | 08/2018     |
| 351                            | ALTERNATE GAS NETWORK AT BSL - [N12000093                                                                        | 3/2015           | 255.19<br>-                        | 255.19                       | 156.39                                  | 03/2018<br>-          | 03/2018     |
|                                | <b>Total</b>                                                                                                     |                  | 24,449.42<br>-                     | 24,449.42                    | 13,437.81                               |                       |             |
|                                |                                                                                                                  |                  |                                    |                              |                                         |                       |             |

## List of Projects on schedule w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                  |                  |                                    |                              |                                         | (September 2017)      |             |
|--------------------------------|------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|                                |                                                                                                                  |                  |                                    |                              |                                         | Date of Commissioning |             |
| Sl.No                          | Project                                                                                                          | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original /Revised     | Anticipated |
| 1                              | 2                                                                                                                | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
|                                | <u>URBAN DEVELOPMENT</u>                                                                                         |                  |                                    |                              |                                         |                       |             |
| 352                            | CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB<br>- [N28000088                 | 2/2014           | 388.00<br>-                        | 388.00                       | 277.96                                  | 05/2017<br>02/2018    | 02/2018     |
| 353                            | LUCKNOW METRO RAIL CORPORATION LTD<br>- [N28000094                                                               | 1/2016           | 6,928.00<br>6,928.00               | 6,928.00                     | 2,536.77                                | 03/2019<br>-          | 03/2019     |
| 354                            | CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB<br>[N28000102                             | 8/2016           | 294.00<br>-                        | 294.00                       | 34.90                                   | 04/2019<br>-          | 04/2019     |
| 355                            | RESIDENTIAL QUARTERS FOR HAL,BANGLORE<br>- [N28000103                                                            | 12/2016          | 246.31<br>-                        | 246.31                       | -                                       | 02/2020<br>-          | 02/2020     |
| 356                            | CHENNAI METRO RAIL LTD (PHASE 1 EXT)<br>- [N28000097                                                             | 6/2016           | 3,770.00<br>-                      | 3,770.00                     | -                                       | 03/2018<br>-          | 03/2018     |
| 357                            | ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD<br>- [N28000098          | 10/2016          | 209.84<br>-                        | 209.84                       | .43                                     | 03/2020<br>-          | 03/2020     |
| 358                            | CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095 | 12/2016          | 164.00<br>-                        | 164.00                       | 68.10                                   | 01/2018<br>03/2018    | 03/2018     |
| 359                            | REDEVELOPMENT OF EAST KIDWAI NAGAR<br>- [N28000080                                                               | 6/2012           | 4,264.00<br>-                      | 4,118.00                     | 2,790.00                                | 11/2019<br>-          | 11/2019     |
| 360                            | CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL<br>[N28000059                                  | 12/2012          | 188.87<br>-                        | 188.87                       | 168.98                                  | 12/2015<br>12/2017    | 12/2017     |
|                                | Total                                                                                                            |                  | 16,453.02<br>-                     | 16,307.02                    | 5,877.14                                |                       |             |
|                                |                                                                                                                  |                  |                                    |                              |                                         |                       |             |
|                                | Grand Total                                                                                                      |                  | 5,56,998.35                        | 5,70,095.22                  | 1,69,089.53                             |                       |             |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

### Annexure - XIII

| Costing Rs.150 Crore and above |                                                                                           |                  |                                   |                             | (September 2017)      |             |                  |
|--------------------------------|-------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                |                                                                                           |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                           | Project                                                                                   | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                              | 2                                                                                         | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
|                                | <u>ATOMIC ENERGY</u>                                                                      |                  |                                   |                             |                       |             |                  |
| 1                              | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)<br>- [020100044]                        | 09/2003          | 3,492.00<br>-                     | 6,000.00                    | 09/2010<br>-          | 02/2018     | 71.82            |
|                                | Total                                                                                     |                  | 3,492.00<br>-                     | 6,000.00                    |                       |             |                  |
|                                | <u>CIVIL AVIATION</u>                                                                     |                  |                                   |                             |                       |             |                  |
| 2                              | CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT<br>[N04000050]                     | 01/2009          | 309.46<br>-                       | 553.53                      | 01/2011<br>-          | 09/2017     | 78.87            |
| 3                              | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR<br>[N04000073] | 10/2013          | 314.61<br>-                       | 441.33                      | 09/2018<br>-          | 06/2020     | 40.28            |
|                                | Total                                                                                     |                  | 624.07<br>-                       | 994.86                      |                       |             |                  |
|                                | <u>COAL</u>                                                                               |                  |                                   |                             |                       |             |                  |
| 4                              | RAMAGUNDAM OC-II EXTENSION<br>- [N06000078]                                               | 12/2009          | 418.97<br>-                       | 489.62                      | 03/2012<br>-          | 03/2023     | 16.86            |
| 5                              | NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW<br>- [N06000152]                      | 07/2016          | 17,237.00<br>-                    | 17,237.80                   | 11/2021<br>-          | 11/2021     | .00              |
|                                | Total                                                                                     |                  | 17,655.97<br>-                    | 17,727.42                   |                       |             |                  |
|                                | <u>DEFENCE PRODUCTION</u>                                                                 |                  |                                   |                             |                       |             |                  |
| 6                              | CONSTRUCTION WORKS PHASE 4<br>- [N39000001]                                               | 12/2016          | 167.69<br>168.00                  | 172.99                      | 05/2018<br>-          | 05/2018     | 2.97             |
| 7                              | CONSTRUCTION WORKS PHASE 3B<br>- [N39000002]                                              | 12/2016          | 285.95<br>286.00                  | 296.05                      | 08/2020<br>-          | 08/2020     | 3.51             |
|                                | Total                                                                                     |                  | 453.64<br>-                       | 469.04                      |                       |             |                  |
|                                | <u>FERTILISERS</u>                                                                        |                  |                                   |                             |                       |             |                  |
| 8                              | GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL.<br>[N08000010]    | 02/2016          | 482.85<br>-                       | 494.00                      | 12/2017<br>-          | 12/2017     | 2.31             |
|                                | Total                                                                                     |                  | 482.85<br>-                       | 494.00                      |                       |             |                  |
|                                |                                                                                           |                  |                                   |                             |                       |             |                  |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs.150 Crore and above |                                                                                                         |                  |                                   |                             | (September 2017)      |             |                  |
|--------------------------------|---------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                |                                                                                                         |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                           | Project                                                                                                 | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                              | 2                                                                                                       | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
|                                | <u>HEALTH AND FAMILY WELFARE</u>                                                                        |                  |                                   |                             |                       |             |                  |
| 9                              | SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK<br>- [N21000005]                | 11/2013          | 196.70<br>-                       | 209.00                      | 01/2016<br>-          | -           | 6.25             |
|                                | Total                                                                                                   |                  | 196.70<br>-                       | 209.00                      |                       |             |                  |
|                                |                                                                                                         |                  |                                   |                             |                       |             |                  |
|                                | <u>HEAVY INDUSTRY</u>                                                                                   |                  |                                   |                             |                       |             |                  |
| 10                             | NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)<br>- [N20000001]                    | 04/2011          | 1,718.00<br>-                     | 3,827.30                    | 09/2011<br>-          | 12/2017     | 122.78           |
|                                | Total                                                                                                   |                  | 1,718.00<br>-                     | 3,827.30                    |                       |             |                  |
|                                |                                                                                                         |                  |                                   |                             |                       |             |                  |
|                                | <u>PETROLEUM</u>                                                                                        |                  |                                   |                             |                       |             |                  |
| 11                             | SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN<br>- [N16000167] | 07/2011          | 352.56<br>-                       | 439.03                      | 03/2017<br>-          | 11/2018     | 24.53            |
| 12                             | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR<br>- [N16000169]                                           | 01/2006          | 993.00<br>-                       | 1,693.00                    | 01/2012<br>-          | 10/2017     | 70.49            |
| 13                             | INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS<br>- [N16000172]                                      | 05/2013          | 4,124.35<br>-                     | 5,637.00                    | 04/2016<br>-          | 12/2017     | 36.68            |
| 14                             | INTEGRATED DEVELOPMENT OF B-127 FIELDS<br>- [N16000131]                                                 | 12/2011          | 2,059.63<br>-                     | 2,665.65                    | 03/2015<br>-          | 03/2018     | 29.42            |
| 15                             | UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE<br>- [N18000148] | 09/2012          | 871.35<br>-                       | 1,200.00                    | 03/2015<br>-          | 11/2017     | 37.72            |
| 16                             | 50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II<br>- [N16000209]                                       | 11/2011          | 310.00<br>-                       | 370.00                      | 03/2013<br>-          | -           | 19.35            |
| 17                             | LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS<br>- [N16000213]                       | 12/2015          | 3,190.69<br>-                     | 3,247.19                    | 04/2018<br>-          | 04/2018     | 1.77             |
| 18                             | RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT)<br>- [N16000217]              | 06/2012          | 150.00<br>-                       | 259.93                      | 07/2014<br>-          | 09/2017     | 73.29            |
| 19                             | CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU<br>- [N16000255]                     | 05/2015          | 224.00<br>207.00                  | 207.25                      | 04/2019<br>-          | 04/2019     | .12              |
|                                | Total                                                                                                   |                  | 12,275.58<br>-                    | 15,719.05                   |                       |             |                  |
|                                |                                                                                                         |                  |                                   |                             |                       |             |                  |
|                                | <u>POWER</u>                                                                                            |                  |                                   |                             |                       |             |                  |
| 20                             | PARBATI HEP (4X200 MW) (NHPC) II<br>- [180100210]                                                       | 09/2002          | 3,919.59<br>-                     | 8,398.75                    | 09/2009<br>-          | 12/2018     | 114.28           |
| 21                             | SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)<br>- [180100221]                                                | 09/2003          | 6,285.33<br>-                     | 18,559.49                   | 09/2010<br>-          | -           | 195.28           |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs.150 Crore and above |                                                                                                             |                  |                                   |                             | (September 2017)      |             |                  |
|--------------------------------|-------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                |                                                                                                             |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                           | Project                                                                                                     | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                              | 2                                                                                                           | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 22                             | WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW<br>- [N18000203]                               | 02/2015          | 302.49<br>302.00                  | 302.49                      | 02/2016<br>-          | -           | .16              |
| 23                             | TAPOVAN-VISHNUGAD HEP (4X130MW)<br>- [N18000014]                                                            | 11/2006          | 2,978.48<br>-                     | 3,846.30                    | 03/2013<br>-          | 06/2019     | 29.14            |
| 24                             | SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID<br>- [N18000169]                                        | 08/2014          | 288.49<br>-                       | 376.09                      | 02/2017<br>-          | 03/2018     | 30.37            |
| 25                             | SYSTEM STRENGTHENING XII OF SR<br>- [N18000085]                                                             | 02/2010          | 232.34<br>-                       | 245.00                      | 06/2012<br>-          | 12/2017     | 5.45             |
| 26                             | NPGCPL-NABINAGAR STPP - JV (3X660 MW)<br>- [N18000192]                                                      | 01/2013          | 12,964.60<br>-                    | 13,731.26                   | 01/2018<br>-          | 12/2018     | 5.91             |
| 27                             | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT<br>- [N18000194]                           | 05/2015          | 436.68<br>-                       | 602.44                      | 12/2016<br>-          | 12/2017     | 37.96            |
| 28                             | BOKARO THERMAL POWER STATION-A<br>- [N18000199]                                                             | 08/2006          | 2,313.00<br>4,139.00              | 4,366.64                    | 12/2011<br>-          | 02/2017     | 5.50             |
| 29                             | RAGHUNATHPUR THERMAL POWER STATION PHASE-I<br>- [N18000202]                                                 | 04/2007          | 4,122.00<br>8,781.00              | 9,142.58                    | 02/2011<br>-          | 03/2016     | 4.12             |
| 30                             | TEHRI PUMPED STORAGE PLANT(1000MW)<br>- [N18000010]                                                         | 07/2006          | 1,657.00<br>-                     | 3,939.11                    | 02/2016<br>-          | 12/2020     | 137.73           |
| 31                             | SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV<br>- [N18000115]                                              | 12/2011          | 297.33<br>-                       | 426.29                      | 08/2014<br>-          | 12/2017     | 43.37            |
| 32                             | KISHANGANGA HEP (3X110 MW)<br>- [N18000031]                                                                 | 01/2009          | 3,642.04<br>-                     | 5,882.01                    | 01/2016<br>-          | 02/2018     | 61.50            |
| 33                             | TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT<br>- [N18000215] | 01/2014          | 1,788.41<br>-                     | 2,352.57                    | 09/2017<br>-          | 09/2018     | 31.55            |
| 34                             | ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS<br>- [N18000222]                                       | 04/2016          | 790.13<br>-                       | 790.30                      | 06/2019<br>-          | 06/2019     | .02              |
| 35                             | TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A<br>- [N18000253]         | 03/2015          | 955.00<br>-                       | 1,364.00                    | 12/2015<br>-          | 03/2018     | 42.83            |
| 36                             | TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM CUDDALORE AREA - PACKAGE A<br>- [N18000259]        | 03/2015          | 955.00<br>1,161.00                | 1,364.00                    | 12/2015<br>-          | 03/2018     | 17.48            |
|                                | Total                                                                                                       |                  | 43,927.91<br>-                    | 75,689.32                   |                       |             |                  |
|                                |                                                                                                             |                  |                                   |                             |                       |             |                  |
|                                | <u>RAILWAYS</u>                                                                                             |                  |                                   |                             |                       |             |                  |
| 37                             | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)<br>- [220100007]                                          | 04/1986          | 158.77<br>274.56                  | 634.48                      | 03/1994<br>-          | -           | 131.09           |
| 38                             | NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR<br>[220100135]                      | 04/1983          | 36.80<br>274.41                   | 614.00                      | -<br>-                | -           | 123.75           |
| 39                             | CALICUT-MANGALORE (DL) (SR)<br>- [220100151]                                                                | 02/1996          | 240.00<br>-                       | 579.37                      | -<br>-                | -           | 141.40           |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs.150 Crore and above |                                                                                                     |                  |                                   |                             | (September 2017)      |             |                  |
|--------------------------------|-----------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                |                                                                                                     |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                           | Project                                                                                             | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                              | 2                                                                                                   | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 40                             | KARUR-SALEM(NL),SR<br>- [220100191                                                                  | 02/1997          | 155.55<br>-                       | 870.00                      | -<br>-                | -           | 459.31           |
| 41                             | KATIHAR - JOGBANI (GC)(NEFR)<br>- [220100247                                                        | 09/2001          | 492.98<br>-                       | 1,320.00                    | 12/2010<br>-          | -           | 167.76           |
| 42                             | GULBARGA-BIDAR,SCR(NL)<br>- [220100254                                                              | 02/1998          | 242.42<br>369.70                  | 1,542.41                    | -<br>05/2009          | -           | 317.21           |
| 43                             | QUILON-TIRUNELVELI-TENKASI-<br>VIRUDHUNAGAR(SR)(GC)<br>[220100263                                   | 03/1998          | 280.00<br>-                       | 1,122.00                    | -<br>-                | -           | 300.71           |
| 44                             | KOTLPALLI-NARASAPUR (NL) (SCR)<br>- [220100265                                                      | 12/2001          | 330.00<br>-                       | 2,125.18                    | -<br>-                | 03/2021     | 543.99           |
| 45                             | TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-<br>NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)<br>- [220100268 | 03/2000          | 1,049.69<br>-                     | 3,404.92                    | 12/2006<br>-          | -           | 224.37           |
| 46                             | GADWAL - RAICHUR (NL), SCR<br>- [220100270                                                          | 04/1998          | 92.63<br>-                        | 350.00                      | 02/2011<br>-          | -           | 277.85           |
| 47                             | TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER<br>- [220100272                                         | 04/2000          | 1,188.91<br>-                     | 1,319.33                    | -<br>12/2009          | 03/2019     | 10.97            |
| 48                             | DEOGHAR - SULTANGANJ (INL), ER<br>- [220100273                                                      | 04/2000          | 607.09<br>-                       | 973.33                      | 12/2012<br>12/2012    | -           | 60.33            |
| 49                             | JIND-SONEPAT (NL),NR<br>- [220100280                                                                | 01/2004          | 238.56<br>-                       | 740.00                      | 03/2012<br>-          | -           | 210.19           |
| 50                             | HARIDASPUR-PARADEEP(NL)<br>- [220100285                                                             | 04/1996          | 301.64<br>-                       | 1,185.64                    | -<br>09/2009          | 03/2019     | 293.06           |
| 51                             | RAMGANJMUUNDI-BHOPAL (NL),WCR<br>- [220100314                                                       | 04/2001          | 470.92<br>727.13                  | 2,713.09                    | -<br>-                | 03/2021     | 273.12           |
| 52                             | MAHARAJGANJ-MASRAKH (NL) - NER<br>- [220100316                                                      | 04/2003          | 218.19<br>-                       | 412.05                      | -<br>-                | 03/2018     | 88.85            |
| 53                             | KICHHA-KHATIMA (NL) - NER<br>- [220100317                                                           | 04/2003          | 142.45<br>-                       | 228.40                      | -<br>-                | -           | 60.34            |
| 54                             | ETAWAH-MAINPURI (NL),NCR<br>- [220100318                                                            | 04/1997          | 120.00<br>-                       | 245.39                      | 12/2008<br>-          | -           | 104.49           |
| 55                             | HATHUA-BHATNI (N L) (NER)<br>- [220100319                                                           | 04/2005          | 230.03<br>-                       | 718.54                      | -<br>-                | 05/2019     | 212.37           |
| 56                             | CHHINDWARA - NAGPUR (GC)(SECR)<br>- [220100324                                                      | 04/2005          | 383.79<br>-                       | 1,101.16                    | -<br>-                | -           | 186.92           |
| 57                             | SUKINDA ROAD - ANGUL (NL)(ECOR)<br>- [220100325                                                     | 04/1998          | 183.23<br>-                       | 1,202.70                    | 02/2015<br>-          | 12/2019     | 556.39           |
| 58                             | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)<br>- [220100327                                           | 04/2000          | 133.41<br>207.00                  | 340.00                      | 03/2009<br>03/2009    | 12/2017     | 64.25            |
| 59                             | TALCHER-BIMALAGARH(NL)(ECOR)<br>- [220100328                                                        | 04/2005          | 810.78<br>-                       | 1,928.07                    | -<br>-                | 12/2022     | 137.80           |
| 60                             | RAICHUR-GUNTAKAL(DL)(SCR)<br>- [220100329                                                           | 04/2003          | 136.62<br>-                       | 376.00                      | 12/2007<br>03/2010    | -           | 175.22           |
| 61                             | GOELKERA-MANOHARPUR,(LD)(SER)<br>- [N22000045                                                       | 03/1997          | 261.70<br>-                       | 388.00                      | 02/2006<br>-          | 12/2019     | 48.26            |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs.150 Crore and above |                                                                                                                         |                  |                                   |                             | (September 2017)      |             |                  |
|--------------------------------|-------------------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                |                                                                                                                         |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                           | Project                                                                                                                 | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                              | 2                                                                                                                       | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 62                             | BHOPAL BINA 3D LINE DOUBLING<br>- [N22000077]                                                                           | 09/2007          | 687.20<br>-                       | 950.00                      | 03/2010<br>-          | 03/2018     | 38.24            |
| 63                             | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU<br>'PONDY'-AGASTIYAMPALLI<br>- [N22000079]                                     | 09/2007          | 404.19<br>-                       | 2,072.50                    | -<br>-                | -           | 412.75           |
| 64                             | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND<br>COIMBATORE<br>- [N22000080]                                                   | 09/2006          | 343.17<br>-                       | 1,065.00                    | -<br>-                | -           | 210.34           |
| 65                             | ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR<br>AND G'BAD-MEERUT<br>- [N22000094]                                        | 02/2008          | 171.10<br>-                       | 275.08                      | 03/2012<br>-          | -           | 60.77            |
| 66                             | BHAIRABI SAIRONG, NL, NEFR<br>- [N22000100]                                                                             | 04/2008          | 619.34<br>-                       | 4,600.00                    | 04/2014<br>-          | 03/2020     | 642.73           |
| 67                             | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN<br>ECR<br>- [N22000002]                                                   | 04/1996          | 332.92<br>283.95                  | 477.88                      | 03/2012<br>-          | -           | 68.30            |
| 68                             | MANOHARABAD-KOTHPALL NEW LINE(SCR)<br>- [N22000032]                                                                     | 04/2006          | 378.56<br>-                       | 1,160.47                    | -<br>-                | 03/2022     | 206.55           |
| 69                             | OBULAVARIPALLE-KRISHNAPATNAM(RVNL)<br>- [N22000049]                                                                     | 07/2006          | 743.00<br>-                       | 1,825.00                    | 03/2008<br>06/2008    | 03/2020     | 145.63           |
| 70                             | JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE<br>CONVERSION (NWR)<br>- [N22000113]                                   | 04/2008          | 653.19<br>-                       | 941.04                      | 03/2014<br>-          | 06/2019     | 44.07            |
| 71                             | RATLAM-MHOW-KHANDWA-AKOLA (GC)<br>- [N22000120]                                                                         | 04/2008          | 603.04<br>-                       | 1,030.29                    | 03/2012<br>-          | -           | 70.85            |
| 72                             | BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG<br>COACHES POH PER MONTH (WR)<br>- [N22000125]                                  | 04/2006          | 117.36<br>196.95                  | 203.00                      | 03/2011<br>-          | -           | 3.07             |
| 73                             | KATAKHAL TO BHAIRABI<br>- [N22000126]                                                                                   | 04/1998          | 227.90<br>-                       | 509.00                      | 12/2012<br>-          | 05/2016     | 123.34           |
| 74                             | WARDHA-NANDED MAHARASHTRA<br>- [N22000231]                                                                              | 04/2008          | 499.30<br>-                       | 3,168.29                    | -<br>-                | 03/2023     | 534.55           |
| 75                             | TARAKESHWAR-MAGRA NEW BG LINE<br>- [N22000235]                                                                          | 04/2010          | 365.17<br>-                       | 365.67                      | -<br>-                | -           | .14              |
| 76                             | HANSDIHA-GODDA NL<br>- [N22000236]                                                                                      | 04/2011          | 267.09<br>-                       | 350.78                      | -<br>-                | -           | 31.33            |
| 77                             | MAGRAHAT-DIAMOND HARBOUR WITH MM<br>SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND<br>HATBOUR - BAHRAHAT-KULPI NL - [N22000243] | 04/2009          | 493.96<br>-                       | 681.68                      | -<br>-                | -           | 38.00            |
| 78                             | KATWA-PATULI DOUBLING WITH NEW MM FOR<br>AHMEDPUR-KATWA GC<br>- [N22000245]                                             | 04/2010          | 423.66<br>-                       | 720.59                      | 03/2017<br>-          | -           | 70.09            |
| 79                             | 3RD LINE BETWEEN BHUSAWAL-JALGAON<br>- [N22000247]                                                                      | 04/2011          | 184.06<br>-                       | 199.12                      | -<br>-                | -           | 8.18             |
| 80                             | PEN ROHA DOUBLING<br>- [N22000254]                                                                                      | 04/2007          | 98.74<br>-                        | 381.39                      | -<br>-                | -           | 286.26           |
| 81                             | PANVEL PEN DOUBLING<br>- [N22000255]                                                                                    | 04/2006          | 96.16<br>-                        | 280.00                      | -<br>-                | -           | 191.18           |
| 82                             | TUMKUR-CHITRADURGA-DAVENGERE NL<br>- [N22000256]                                                                        | 04/2011          | 913.00<br>-                       | 1,801.01                    | -<br>-                | -           | 97.26            |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs.150 Crore and above |                                                                |                  |                                   |                             | (September 2017)      |             |                  |
|--------------------------------|----------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                |                                                                |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                           | Project                                                        | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                              | 2                                                              | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 83                             | MUNIRABAD (GINGERA) -RAICHUR NL<br>- [N22000257                | 04/2007          | 179.65<br>-                       | 1,350.91                    | -                     | -           | 651.97           |
| 84                             | KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION<br>[N22000261 | 04/2012          | 1,054.35<br>-                     | 2,200.00                    | -                     | -           | 108.66           |
| 85                             | GUDUR-DURGARAJAPATNAM<br>- [N22000265                          | 04/2011          | 283.54<br>-                       | 759.41                      | -                     | -           | 167.83           |
| 86                             | GRADE SEPERATOR AT DAYABASTI<br>- [N22000269                   | 04/1999          | 156.65<br>-                       | 197.17                      | -                     | -           | 25.87            |
| 87                             | ROHTAK-MEHAM HANSI<br>- [N22000272                             | 04/2012          | 287.00<br>-                       | 625.00                      | -                     | -           | 117.77           |
| 88                             | BHANUPALI-BILASPUR BERI NL<br>- [N22000273                     | 04/2008          | 1,046.88<br>-                     | 4,500.00                    | -                     | -           | 329.85           |
| 89                             | SRINIVASA-PURA-MADANAPALLI NL<br>- [N22000277                  | 04/2013          | 296.00<br>-                       | 466.65                      | -                     | -           | 57.65            |
| 90                             | SHIMOGA-HARIHAR NL<br>- [N22000278                             | 04/2011          | 562.74<br>-                       | 832.47                      | -                     | -           | 47.93            |
| 91                             | RAYADURGA-TUMKUR NL<br>- [N22000279                            | 04/2007          | 970.34<br>-                       | 1,714.49                    | -                     | -           | 76.69            |
| 92                             | WHITE FIELD-KOLAR NL<br>- [N22000280                           | 04/2011          | 341.05<br>-                       | 348.85                      | -                     | -           | 2.29             |
| 93                             | BHADRACHALAM ROAD-SATTUPALLI<br>- [N22000287                   | 04/2010          | 337.49<br>-                       | 792.01                      | -                     | -           | 134.68           |
| 94                             | HARIDWAR-LAKSAR<br>- [N22000289                                | 04/2012          | 219.83<br>-                       | 346.63                      | -                     | -           | 57.68            |
| 95                             | CHANDIGARH-BADDI NL<br>- [N22000296                            | 04/2007          | 328.14<br>-                       | 1,540.00                    | -                     | -           | 369.31           |
| 96                             | TORANAGALLU-RANJITPURA DL<br>- [N22000298                      | 04/2011          | 146.75<br>-                       | 167.50                      | -                     | -           | 14.14            |
| 97                             | MONIGRAM- NIMTITA<br>- [N22000301                              | 04/2012          | 250.93<br>-                       | 259.23                      | -                     | -           | 3.31             |
| 98                             | BAZAR SAU -AZIMGANJ JN. DOUBLING<br>- [N22000302               | 04/2012          | 255.64<br>-                       | 272.20                      | -                     | -           | 6.48             |
| 99                             | JAGGAYYAPET - MELLACHERUVU<br>- [N22000304                     | 04/2007          | 313.24<br>-                       | 554.70                      | 01/1999<br>-          | -           | 77.08            |
| 100                            | MM FROM BURAMARA-CHAKULIA<br>- [N22000305                      | 04/2008          | 466.48<br>-                       | 750.00                      | 01/1999<br>-          | -           | 60.78            |
| 101                            | MM FROM PANSKURA-GHATAL NL<br>- [N22000309                     | 04/2011          | 276.69<br>-                       | 426.00                      | 01/1999<br>-          | -           | 53.96            |
| 102                            | AHMEDNAGAR-PARLI VAIJNATH(NL) CR<br>- [220100181               | 02/1997          | 514.68<br>-                       | 2,271.50                    | -                     | -           | 341.34           |
| 103                            | MANDARHILL-DUMKA-RAMPURHAT (NL),ER<br>- [220100168             | 04/1995          | 900.05<br>-                       | 1,125.89                    | 12/2011<br>12/2010    | 03/2020     | 25.09            |
| 104                            | BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR<br>- [220100201   | 09/1997          | 1,500.00<br>-                     | 5,000.00                    | 04/2008<br>12/2011    | 06/2018     | 233.33           |
| 105                            | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)<br>- [220100232         | 09/1998          | 247.66<br>-                       | 6,093.31                    | 05/2008<br>-          | 03/2023     | 2,360.35         |



## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs.150 Crore and above |                                                                                             |                  |                                   |                             | (September 2017)      |             |                  |
|--------------------------------|---------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                |                                                                                             |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                           | Project                                                                                     | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                              | 2                                                                                           | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 106                            | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR<br>- [220100240]                                 | 04/1997          | 501.69<br>335.77                  | 1,043.56                    | 03/2012<br>-          | -           | 210.80           |
| 107                            | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR<br>- [220100243]                                 | 04/1999          | 108.00<br>-                       | 432.72                      | 12/2009<br>-          | -           | 300.67           |
| 108                            | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)<br>- [220100257]                                      | 04/1997          | 162.87<br>-                       | 541.00                      | -<br>-                | -           | 232.17           |
| 109                            | NEW MAYNAGURI TO JOGIGHOPA VIA<br>CHANGRABANDHA (NL), NEFR<br>- [220100266]                 | 04/2000          | 733.00<br>-                       | 3,010.00                    | 12/2008<br>-          | 03/2019     | 310.64           |
| 110                            | KHURDA ROAD-BOLANGIR(NL)ECOR<br>- [220100284]                                               | 04/1994          | 470.21<br>-                       | 3,004.90                    | -<br>-                | 06/2021     | 539.05           |
| 111                            | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)<br>- [220100288]                                        | 04/2003          | 727.56<br>-                       | 9,658.00                    | 03/2011<br>-          | 03/2020     | 1,227.45         |
| 112                            | KOSI BRIDGE (NL), ECR<br>- [220100304]                                                      | 04/2002          | 322.95<br>-                       | 341.41                      | 03/2012<br>-          | -           | 5.72             |
| 113                            | ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA,<br>NEFR<br>- [N22000082]                      | 12/2006          | 170.00<br>-                       | 436.00                      | 03/2011<br>-          | 10/2011     | 156.47           |
| 114                            | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL<br>PROJECT), NEFR<br>- [N22000086]         | 09/2006          | 200.00<br>-                       | 780.00                      | -<br>-                | 03/2019     | 290.00           |
| 115                            | NEW B.G. LINE FROM ARARIA TO GALGALIA<br>(THAKURGUNG), NEFR<br>[N22000087]                  | 09/2006          | 300.00<br>-                       | 2,145.00                    | -<br>-                | 03/2020     | 615.00           |
| 116                            | NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA)<br>NATIONAL PROJECT (NEFR)<br>[N22000124]            | 04/2006          | 850.00<br>-                       | 3,000.00                    | 03/2015<br>-          | 03/2020     | 252.94           |
| 117                            | MUMBAI URBAN TRANSPORT PROJECT PHASE-II<br>- [N22000092]                                    | 04/2008          | 5,300.00<br>-                     | 7,986.04                    | 03/2014<br>-          | 03/2019     | 50.68            |
| 118                            | BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT<br>OF JUBILEE BRIDGE NO.8 (ER)<br>[N22000119] | 04/1999          | 207.52<br>-                       | 334.87                      | 12/2012<br>-          | -           | 61.37            |
| 119                            | LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM<br>KUMARGHAT NATIONAL PROJECT<br>[N22000127]    | 04/1996          | 1,676.31<br>-                     | 7,000.00                    | 03/2009<br>-          | 03/2018     | 317.58           |
| 120                            | AGARTALA SABROOM, NL, NEFR<br>- [N22000099]                                                 | 04/2008          | 813.34<br>-                       | 3,451.00                    | 03/2014<br>-          | 03/2020     | 324.30           |
| 121                            | KISHANGANJ JALALGARH, NL, NEFR<br>- [N22000101]                                             | 04/2008          | 282.92<br>-                       | 360.00                      | -<br>-                | -           | 27.24            |
| 122                            | SEVOK RANGPO, NEFR<br>- [N22000102]                                                         | 04/2008          | 1,339.48<br>-                     | 4,084.69                    | 12/2015<br>-          | 03/2020     | 204.95           |
| 123                            | KANPUR KASGANJ MATHURA(GC) NER<br>- [220100197]                                             | 03/1997          | 677.97<br>1,062.36                | 1,679.13                    | -<br>-                | -           | 58.06            |
| 124                            | KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER)<br>- [220100256]                                    | 04/1999          | 744.71<br>-                       | 1,126.79                    | -<br>-                | -           | 51.31            |
| 125                            | DAUSA-GANGAPUR CITY(NL),NWR<br>- [220100184]                                                | 02/1997          | 410.08<br>-                       | 780.98                      | -<br>-                | 08/2018     | 90.45            |
| 126                            | SURATPURA - HANUMANGARH - SRIGANGANAGAR<br>GUAGE CONVERSION (NWR)<br>[N22000114]            | 04/2008          | 516.23<br>-                       | 735.00                      | 03/2014<br>-          | -           | 42.38            |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs.150 Crore and above |                                                                                                                  |                  |                                   |                             | (September 2017)      |             |                  |
|--------------------------------|------------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                |                                                                                                                  |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                           | Project                                                                                                          | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                              | 2                                                                                                                | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 127                            | NANGALDAM-TALWARA(NL),NR<br>- [220100188                                                                         | 03/1981          | 450.00<br>-                       | 2,100.00                    | 07/2012<br>-          | -           | 366.67           |
| 128                            | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR<br>- [220100133                                                              | 03/1995          | 2,500.00<br>-                     | 19,565.00                   | 11/2002<br>-          | 12/2018     | 682.60           |
| 129                            | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR<br>- [220100258                                                           | 03/2002          | 625.30<br>408.76                  | 876.10                      | 06/2007<br>-          | -           | 114.33           |
| 130                            | UTRATIA-ZAFRABAD, NR (LINE DOUBLING)<br>- [N22000088                                                             | 04/2006          | 325.00<br>-                       | 1,581.53                    | 03/2010<br>-          | -           | 386.62           |
| 131                            | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL<br>- [220100149                                 | 04/1995          | 304.00<br>-                       | 1,195.00                    | 12/2012<br>-          | -           | 293.09           |
| 132                            | RAJATGARH-BARANG(LD),ECOR<br>- [220100286                                                                        | 04/1999          | 166.16<br>-                       | 380.00                      | 02/2009<br>02/2009    | 06/2017     | 128.70           |
| 133                            | SALKA ROAD -ANUPNAGAR LINE DOUBLING<br>- [N22000075                                                              | 09/2006          | 324.90<br>-                       | 516.40                      | 03/2010<br>-          | 12/2017     | 58.94            |
| 134                            | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)<br>- [N22000110     | 04/2010          | 3,951.98<br>-                     | 4,259.48                    | 03/2016<br>-          | 12/2020     | 7.78             |
| 135                            | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)<br>- [N22000109 | 04/2010          | 2,298.42<br>-                     | 2,733.86                    | 03/2014<br>-          | -           | 18.95            |
| 136                            | NANDYAL-YERRAGUNTLA(NL),SCR<br>- [220100192                                                                      | 03/1996          | 155.74<br>164.36                  | 966.98                      | 02/2009<br>-          | 12/2017     | 488.33           |
| 137                            | MUNEERABAD-MAHABOBNAGAR(NL),SCR<br>- [220100205                                                                  | 04/1997          | 218.24<br>236.41                  | 525.00                      | -<br>-                | 03/2019     | 122.07           |
| 138                            | MACHERLA-NALGONDA(NL)(SCR)<br>- [220100220                                                                       | 07/1998          | 125.00<br>-                       | 480.00                      | 07/2008<br>-          | -           | 284.00           |
| 139                            | GONDIA-JABALPUR(GC),(SECR)<br>- [220100186                                                                       | 02/1997          | 386.30<br>-                       | 1,776.81                    | 03/1998<br>-          | 12/2019     | 359.96           |
| 140                            | HOWRAH-AMTA-CHAMPADANGA NL (SER)<br>- [220100208                                                                 | 04/1974          | 393.46<br>154.30                  | 1,026.00                    | 03/2007<br>03/2007    | -           | 564.94           |
| 141                            | TAMLUK DIGHA,LINE DOUBLING (SER)<br>- [N22000097                                                                 | 03/1984          | 293.97<br>-                       | 749.69                      | 06/2005<br>-          | -           | 155.02           |
| 142                            | RANCHI-LOHARDAGA(GC),SER<br>- [220100214                                                                         | 04/1997          | 194.07<br>-                       | 491.33                      | 06/2004<br>-          | -           | 153.17           |
| 143                            | HUBLI-ANKOLA(NL),SWR<br>- [220100193                                                                             | 04/1997          | 227.00<br>-                       | 2,135.00                    | -<br>-                | -           | 840.53           |
| 144                            | GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM)<br>- [N22000345                                       | 04/1997          | 836.26<br>-                       | 1,072.52                    | -<br>-                | -           | 28.25            |
| 145                            | RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)<br>- [N22000107                        | 04/2007          | 482.00<br>-                       | 874.57                      | 03/2013<br>-          | -           | 81.45            |
| 146                            | TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)<br>- [220100262                                                          | 09/1995          | 100.00<br>-                       | 980.00                      | -<br>-                | -           | 880.00           |
| 147                            | BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)<br>- [N22000123                                         | 04/2008          | 318.24<br>-                       | 321.62                      | 03/2012<br>-          | 03/2019     | 1.06             |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs.150 Crore and above |                                                                                                           |                  |                                   |                             | (September 2017)      |             |                  |
|--------------------------------|-----------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                |                                                                                                           |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                           | Project                                                                                                   | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                              | 2                                                                                                         | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 148                            | SAMBALPUR-TALCHER DOUBLING<br>- [N22000315]                                                               | 03/2011          | 679.27<br>-                       | 1,579.27                    | -                     | 03/2021     | 132.50           |
| 149                            | JHARSUGUDA-RENGALI DOUBLING<br>- [N22000317]                                                              | 03/2006          | 201.00<br>-                       | 230.00                      | -                     | -           | 14.43            |
| 150                            | KIRANDUL - JAGDALPUR DOUBLING<br>- [N22000318]                                                            | 12/2012          | 826.57<br>-                       | 1,160.83                    | -                     | 03/2020     | 40.44            |
| 151                            | SAMBALPUR - ANGUL RLY. ELECTRIFICATION<br>- [N22000319]                                                   | 03/2012          | 155.81<br>-                       | 238.03                      | -                     | 03/2020     | 52.77            |
| 152                            | DELANG-PURI DOUBLING<br>- [N22000320]                                                                     | 03/2011          | 165.16<br>-                       | 234.71                      | 03/2015               | -           | 42.11            |
| 153                            | GHAZIPUR - AUNRIHAR (40 KM)<br>- [N22000321]                                                              | 04/2014          | 182.92<br>-                       | 197.73                      | -                     | -           | 8.10             |
| 154                            | THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH<br>BYE-PASS LINE BEFORE PONMALAI (1.13 KM)<br>- [N22000322] | 04/2011          | 190.10<br>-                       | 350.00                      | -                     | 03/2019     | 84.11            |
| 155                            | RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM)<br>JHARKHAND - [N22000323]                                    | 04/2012          | 148.77<br>-                       | 209.00                      | 12/2016               | -           | 40.49            |
| 156                            | HOSADURGA - CHICKAJAJUR (28.89 KM)<br>- [N22000324]                                                       | 04/2010          | 203.40<br>-                       | 273.84                      | -                     | -           | 34.63            |
| 157                            | PHULERA - DIGANA DOUBLING<br>- [N22000326]                                                                | 05/2015          | 600.00<br>-                       | 648.00                      | -                     | 03/2020     | 8.00             |
| 158                            | HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)<br>- [N22000112]                                             | 04/2008          | 829.74<br>-                       | 1,161.64                    | 03/2015               | 12/2019     | 40.00            |
| 159                            | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)<br>- [220100106]                                                   | 12/1994          | 124.43<br>-                       | 1,010.00                    | -                     | -           | 711.70           |
| 160                            | AMRAVATI-NARKHER NL(CR)<br>- [220100118]                                                                  | 06/1994          | 663.01<br>175.30                  | 858.97                      | 06/1999               | -           | 390.00           |
| 161                            | ANGAMALI-SABARIMALA (N.L.)(SR)<br>- [220100252]                                                           | 10/1998          | 550.00<br>-                       | 2,815.62                    | -                     | 01/2018     | 411.93           |
| 162                            | ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP<br>- [N22000130]                                                    | 03/2013          | 307.00<br>-                       | 308.00                      | -                     | -           | .33              |
| 163                            | CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ<br>UP - [N22000131]                                           | 03/2007          | 243.78<br>-                       | 268.78                      | -                     | 08/2017     | 10.26            |
| 164                            | BHOJIPUR TANAKPUR VIA PILIBHIT<br>- [N22000132]                                                           | 03/2008          | 195.64<br>-                       | 474.30                      | -                     | 10/2017     | 142.44           |
| 165                            | CHHAPRA-BALLIA UP<br>- [N22000134]                                                                        | 03/2013          | 295.00<br>-                       | 477.31                      | -                     | 10/2018     | 61.80            |
| 166                            | KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI<br>NAUGARH UP - [N22000136]                               | 03/2013          | 643.00<br>-                       | 644.00                      | -                     | -           | .16              |
| 167                            | BANGURGRAM-GURIYA PATCH DOUBLING<br>- [N22000137]                                                         | 04/2012          | 246.08<br>-                       | 348.55                      | -                     | 03/2019     | 41.64            |
| 168                            | AHMEDABAD-BOTAD (GC)<br>- [N22000140]                                                                     | 04/2012          | 567.18<br>-                       | 975.62                      | -                     | 03/2020     | 72.01            |
| 169                            | DHASA-JETALSAR (GC)<br>- [N22000141]                                                                      | 04/2012          | 376.59<br>-                       | 644.38                      | -                     | 12/2020     | 71.11            |
| 170                            | MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)<br>- [N22000142]                                                       | 04/2011          | 439.88<br>-                       | 845.68                      | -                     | -           | 92.25            |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs.150 Crore and above |                                                                                                             |                  |                                   |                             | (September 2017)      |             |                  |
|--------------------------------|-------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                |                                                                                                             |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                           | Project                                                                                                     | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                              | 2                                                                                                           | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 171                            | RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143] | 04/1994          | 320.66<br>-                       | 399.63                      | -<br>-                | 03/2019     | 24.63            |
| 172                            | PALANPUR-SAMAKHAYALI (DL) - [N22000144]                                                                     | 04/2013          | 1,266.89<br>-                     | 1,548.66                    | -<br>-                | 12/2020     | 22.24            |
| 173                            | VIRAMGAM-SAMAKHIALI (DL) - [N22000145]                                                                      | 04/2011          | 446.00<br>-                       | 1,037.15                    | -<br>-                | 03/2019     | 132.54           |
| 174                            | VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]                                                                   | 04/2010          | 279.40<br>-                       | 355.00                      | -<br>-                | -           | 27.06            |
| 175                            | RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]                                                            | 04/2011          | 2,082.75<br>-                     | 2,562.27                    | -<br>-                | -           | 23.02            |
| 176                            | GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]                                                | 04/2011          | 1,176.09<br>-                     | 3,845.60                    | 02/2020<br>-          | 12/2022     | 226.98           |
| 177                            | THIYAT HAMIRA-SANU - [N22000149]                                                                            | 04/2013          | 236.93<br>-                       | 276.89                      | -<br>-                | 10/2018     | 16.87            |
| 178                            | MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR - [N22000152]                                    | 04/2013          | 456.00<br>-                       | 855.16                      | -<br>-                | 05/2018     | 87.54            |
| 179                            | RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]                        | 04/2010          | 739.65<br>-                       | 872.22                      | -<br>-                | -           | 17.92            |
| 180                            | GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]                                                            | 04/2011          | 239.73<br>-                       | 257.78                      | -<br>-                | -           | 7.53             |
| 181                            | AJMER-BANGURGRAM - [N22000155]                                                                              | 04/2011          | 213.39<br>-                       | 272.99                      | -<br>-                | 03/2019     | 27.93            |
| 182                            | RANI-MARWAR JN. PATCH DOUBLING - [N22000156]                                                                | 04/2012          | 288.97<br>-                       | 369.08                      | -<br>-                | 10/2018     | 27.72            |
| 183                            | ALWAR-BANDIKUI DOUBLING - [N22000157]                                                                       | 04/2013          | 242.09<br>-                       | 293.68                      | -<br>-                | 03/2019     | 21.31            |
| 184                            | DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158] | 04/2010          | 622.41<br>-                       | 2,030.50                    | 02/2019<br>-          | 12/2022     | 226.23           |
| 185                            | BOWAICHANDI-ARAMBAGH - [N22000159]                                                                          | 04/2010          | 267.37<br>-                       | 434.00                      | -<br>-                | -           | 62.32            |
| 186                            | DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]                                                    | 04/2010          | 553.63<br>-                       | 1,009.00                    | -<br>-                | -           | 82.25            |
| 187                            | BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]                                                           | 04/2011          | 289.64<br>-                       | 760.00                      | -<br>-                | -           | 162.39           |
| 188                            | CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]                                                     | 04/2010          | 149.90<br>-                       | 230.00                      | 03/2015<br>-          | -           | 53.44            |
| 189                            | TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]                                                              | 04/2010          | 171.02<br>-                       | 250.00                      | 06/2013<br>-          | 12/2016     | 46.18            |
| 190                            | DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]                                                      | 04/2010          | 309.44<br>-                       | 583.00                      | 12/2015<br>-          | -           | 88.40            |
| 191                            | MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]                                                       | 04/2012          | 258.20<br>-                       | 365.00                      | -<br>-                | 12/2017     | 41.36            |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs.150 Crore and above |                                                                                               |                  |                                   |                             | (September 2017)      |             |                  |
|--------------------------------|-----------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                |                                                                                               |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                           | Project                                                                                       | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                              | 2                                                                                             | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 192                            | GAYA-CHATRA (NL)<br>- [N22000169]                                                             | 04/2008          | 415.67<br>-                       | 549.75                      | -                     | -           | 32.26            |
| 193                            | SAKRI-HASANPUR ROAD (NL)<br>- [N22000171]                                                     | 04/1999          | 175.69<br>-                       | 325.00                      | -                     | -           | 84.98            |
| 194                            | CHHAPRA-MUZAFFARPUR (NL)<br>- [N22000172]                                                     | 04/2006          | 285.07<br>-                       | 378.56                      | -                     | -           | 32.80            |
| 195                            | MOTIHARI-SITAMARHI (NL)<br>- [N22000174]                                                      | 04/2006          | 211.00<br>-                       | 926.09                      | -                     | -           | 338.91           |
| 196                            | SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)<br>- [N22000175]                                  | 04/2008          | 678.62<br>-                       | 2,393.23                    | -                     | -           | 252.66           |
| 197                            | HAJIPUR-RAMDAYALUNAGAR DOUBLING<br>- [N22000182]                                              | 04/2013          | 213.01<br>-                       | 367.17                      | -                     | -           | 72.37            |
| 198                            | SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR<br>- [N22000186] | 04/2013          | 839.00<br>-                       | 1,500.00                    | -                     | -           | 78.78            |
| 199                            | CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC<br>- [N22000188]                              | 04/1998          | 271.24<br>-                       | 520.00                      | -                     | -           | 91.71            |
| 200                            | VILLUPURAM-DINDIGUL WITH ELECTRIFICATION<br>- [N22000189]                                     | 04/2008          | 822.39<br>-                       | 1,810.00                    | -                     | 03/2018     | 120.09           |
| 201                            | KURUPPANTHARA-CHINGAVANAM<br>- [N22000190]                                                    | 04/2007          | 270.14<br>-                       | 346.15                      | -                     | -           | 28.14            |
| 202                            | NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR<br>- [N22000193]                                     | 04/2010          | 221.42<br>-                       | 380.00                      | -                     | -           | 71.62            |
| 203                            | CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA<br>- [N22000194]                                   | 04/1999          | 895.00<br>-                       | 1,857.00                    | 03/2007               | 04/2016     | 107.49           |
| 204                            | AGARTALA-AKHAURA NL<br>- [N22000195]                                                          | 04/2012          | 252.00<br>-                       | 580.00                      | -                     | 07/2019     | 130.16           |
| 205                            | NEW COOCHBEHAR TO SAMUKTALA<br>- [N22000197]                                                  | 04/2011          | 209.77<br>-                       | 445.00                      | -                     | 03/2018     | 112.14           |
| 206                            | NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT<br>- [N22000198]                              | 04/2012          | 283.55<br>-                       | 330.00                      | -                     | 03/2019     | 16.38            |
| 207                            | ERODE-PALANI<br>- [N22000199]                                                                 | 04/2008          | 288.57<br>-                       | 603.22                      | -                     | -           | 109.04           |
| 208                            | MADURAI-BODINAYAKKANUR<br>- [N22000201]                                                       | 04/2008          | 164.41<br>-                       | 302.90                      | -                     | -           | 84.23            |
| 209                            | CHENGANNUR-CHINGAVANAM<br>- [N22000203]                                                       | 04/2006          | 191.72<br>-                       | 342.85                      | -                     | -           | 78.83            |
| 210                            | NEW BG LINE FROM BYRNIHAT TO SHILLONG<br>- [N22000205]                                        | 04/2010          | 4,083.02<br>-                     | 6,000.00                    | -                     | 03/2021     | 46.95            |
| 211                            | NEW BG LINE FROM BALURGHAT TO HILLY NFR<br>- [N22000206]                                      | 04/2010          | 242.22<br>-                       | 471.00                      | -                     | -           | 94.45            |
| 212                            | NEW BG LINE FROM JAGBANI TO BIRATNAGAR<br>- [N22000207]                                       | 04/2010          | 241.52<br>-                       | 394.28                      | -                     | -           | 63.25            |
| 213                            | MURKONGSELEK-PASIGHAT NL<br>- [N22000208]                                                     | 04/2011          | 165.82<br>-                       | 450.00                      | -                     | 03/2020     | 171.38           |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs.150 Crore and above |                                                                                                                |                  |                                   |                             | (September 2017)      |             |                  |
|--------------------------------|----------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                |                                                                                                                |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                           | Project                                                                                                        | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                              | 2                                                                                                              | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 214                            | NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209 | 04/1999          | 523.17<br>-                       | 1,871.00                    | -<br>-                | 03/2018     | 257.63           |
| 215                            | AMBARAI FALAKATA TO NEW MAYNAGURI - [N22000210                                                                 | 04/2011          | 312.12<br>-                       | 508.00                      | -<br>-                | 03/2019     | 62.76            |
| 216                            | LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211                                                              | 04/2012          | 246.07<br>-                       | 398.93                      | -<br>-                | 03/2019     | 62.12            |
| 217                            | MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213                                             | 04/2012          | 632.68<br>-                       | 816.55                      | 03/2016<br>-          | 12/2018     | 29.06            |
| 218                            | MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215                                                                | 04/2011          | 601.43<br>-                       | 1,500.00                    | -<br>-                | -           | 149.41           |
| 219                            | HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218                                                                  | 04/2010          | 172.03<br>-                       | 260.60                      | -<br>-                | -           | 51.49            |
| 220                            | PIRPAINTI-BHAGALPUR - [N22000222                                                                               | 04/2011          | 261.38<br>-                       | 332.14                      | -<br>-                | -           | 27.07            |
| 221                            | PUNE-MIRAJ-LONDA (467 KM) - [N22000359                                                                         | 02/2015          | 4,670.00<br>3,627.00              | 3,627.47                    | -<br>-                | -           | .01              |
| 222                            | DAUND - MANMAD (236 KM) - [N22000360                                                                           | 02/2016          | 1,876.00<br>-                     | 2,081.27                    | -<br>-                | -           | 10.94            |
| 223                            | MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361                                                              | 02/2016          | 854.00<br>-                       | 1,035.16                    | -<br>-                | -           | 21.21            |
| 224                            | VIJAYAWADA-GUDUR - [N22000369                                                                                  | 04/2015          | 3,246.26<br>-                     | 3,548.67                    | -<br>-                | -           | 9.32             |
| 225                            | MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374                                                                    | 01/1991          | 332.15<br>-                       | 559.91                      | 07/2014<br>-          | -           | 68.57            |
| 226                            | RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386                                                     | 04/2003          | 4,300.00<br>-                     | 4,520.00                    | -<br>-                | 08/2015     | 5.12             |
| 227                            | NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390                                  | 04/2016          | 556.31<br>-                       | 612.00                      | -<br>-                | -           | 10.01            |
| 228                            | TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397    | 01/1991          | 763.18<br>-                       | 1,428.00                    | 12/2021<br>-          | 12/2021     | 87.11            |
| 229                            | RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398      | 04/1995          | 524.43<br>-                       | 939.00                      | 12/2021<br>-          | 12/2021     | 79.05            |
| 230                            | TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399                                                                   | 02/2015          | 900.00<br>-                       | 4,131.90                    | -<br>-                | -           | 359.10           |
| 231                            | VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401                                                            | 04/2015          | 750.55<br>-                       | 750.56                      | 12/2024<br>-          | 12/2024     | .00              |
| 232                            | BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402                                         | 04/1998          | 1,027.40<br>-                     | 2,373.00                    | 03/2003<br>-          | -           | 130.97           |
| 233                            | LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404                                                       | 04/2011          | 927.01<br>-                       | 977.00                      | 03/2019<br>-          | 03/2019     | 5.39             |
| 234                            | BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413                                                    | 03/2012          | 1,183.25<br>-                     | 1,183.30                    | 12/2020<br>-          | 12/2020     | .00              |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs.150 Crore and above |                                                                                                                           |                  |                                   |                             | (September 2017)      |             |                  |
|--------------------------------|---------------------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                |                                                                                                                           |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                           | Project                                                                                                                   | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                              | 2                                                                                                                         | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 235                            | BINA - KOTA DOUBLING WITH RE<br>- [N22000414]                                                                             | 04/2011          | 1,485.65<br>-                     | 1,485.85                    | 12/2020<br>-          | 12/2020     | .01              |
|                                | Total                                                                                                                     |                  | 1,16,265.34<br>-                  | 2,69,398.13                 |                       |             |                  |
|                                |                                                                                                                           |                  |                                   |                             |                       |             |                  |
|                                | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                        |                  |                                   |                             |                       |             |                  |
| 236                            | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO<br>KM.140.700 - [240106277]                                                   | 12/2003          | 280.00<br>-                       | 361.00                      | 02/2009<br>-          | 12/2017     | 28.93            |
| 237                            | MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000<br>- [240106278]                                                      | 12/2003          | 199.81<br>-                       | 385.13                      | 04/2009<br>-          | -           | 92.75            |
| 238                            | MAIBANG TO LUMDING (AS-24), KM.111.000 TO<br>KM.126.450 - [240106280]                                                     | 12/2003          | 155.04<br>-                       | 280.13                      | 11/2008<br>-          | -           | 80.68            |
| 239                            | HARANGAJO TO MAIBANG, NH-54<br>- [N24000062]                                                                              | 12/2003          | 196.00<br>-                       | 331.23                      | 07/2009<br>-          | -           | 68.99            |
| 240                            | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)<br>- [N24000133]                                                              | 05/2009          | 1,108.00<br>-                     | 2,288.00                    | 11/2011<br>-          | 03/2018     | 106.50           |
| 241                            | REHABILITATION AND UPGRADATION FROM KM.425 400<br>TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU<br>CONTRAC - [N24000266]   | 01/2014          | 361.30<br>-                       | 207.40                      | 07/2014<br>-          | -           | -42.60           |
| 242                            | BRAHMPUTRA BRIDGE,NH NO-31<br>- [N24000063]                                                                               | 12/2003          | 217.61<br>-                       | 309.56                      | 04/2010<br>-          | 03/2018     | 42.25            |
| 243                            | CHAMBAL BRIDGE, NH-76 (RJ-5)<br>- [N24000068]                                                                             | 12/2003          | 275.00<br>-                       | 281.31                      | 02/2010<br>-          | -           | 2.29             |
| 244                            | GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT<br>SECTION - [N24000125]                                                      | 03/2010          | 1,509.10<br>-                     | 3,237.87                    | 09/2012<br>-          | 12/2017     | 114.56           |
| 245                            | INDORE-JHABUA-GUJRAT/MP<br>- [N24000136]                                                                                  | 10/2010          | 1,175.00<br>-                     | 1,206.10                    | 04/2013<br>-          | 09/2017     | 2.65             |
| 246                            | REHABILITATION AND UPGRADATION OF NH-221 FROM<br>KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR<br>RUDRAMPUR - [N24000247]   | 10/2014          | 295.47<br>-                       | 313.27                      | 02/2017<br>-          | 02/2017     | 6.02             |
| 247                            | CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR<br>VENKATPURAM INCLUDING APPROACH ROAD ON NH-<br>202 UNDER LWE S - [N24000249] | 03/2011          | 218.31<br>-                       | 339.82                      | 12/2015<br>-          | -           | 55.66            |
| 248                            | CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED<br>SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66<br>FROM KM 408.1 - [N24000260]  | 01/2014          | 255.75<br>348.00                  | 348.43                      | 09/2017<br>-          | 09/2017     | .12              |
| 249                            | CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED<br>SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66)<br>FROM KM 486/50 - [N24000261]  | 01/2014          | 267.16<br>352.00                  | 352.05                      | 11/2017<br>-          | 11/2017     | .01              |
| 250                            | REHABILITATION AND UP-GRADATION OF NH-221 (NEW<br>NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM<br>TO A - [N24000262]  | 12/2014          | 201.12<br>201.00                  | 201.12                      | 02/2015<br>-          | -           | .06              |
| 251                            | TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN<br>ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH<br>PACKAGE OF - [N24000420]  | 12/2009          | 104.00<br>-                       | 201.00                      | 09/2010<br>-          | 09/2010     | 93.27            |
| 252                            | FOUR LANING OF GWALIOR-SHIVPURI<br>- [N24000494]                                                                          | 05/2013          | 1,055.00<br>-                     | 1,601.77                    | 11/2015<br>-          | 09/2017     | 51.83            |

## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs.150 Crore and above |                                                                                                                   |                  |                                   |                             | (September 2017)      |             |                  |
|--------------------------------|-------------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                |                                                                                                                   |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                           | Project                                                                                                           | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                              | 2                                                                                                                 | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 253                            | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654 | 03/2017          | 1,184.71<br>-                     | 1,310.00                    | 03/2020<br>-          | 03/2020     | 10.58            |
| 254                            | 4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656                                             | 03/2017          | 744.64<br>-                       | 982.00                      | 03/2020<br>-          | 03/2020     | 31.88            |
| 255                            | 4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657                                         | 03/2017          | 1,030.44<br>-                     | 1,065.51                    | 03/2020<br>-          | 03/2020     | 3.40             |
| 256                            | 4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658                                          | 03/2017          | 988.34<br>-                       | 1,043.28                    | 03/2020<br>-          | 03/2020     | 5.56             |
| 257                            | 4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659                                        | 03/2017          | 1,059.73<br>-                     | 1,071.00                    | 03/2017<br>-          | -           | 1.06             |
| 258                            | 4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661                                        | 03/2017          | 1,098.06<br>-                     | 1,160.64                    | 03/2020<br>-          | 03/2020     | 5.70             |
| 259                            | CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662 | 03/2017          | 754.54<br>-                       | 756.27                      | 03/2020<br>-          | 03/2020     | .23              |
| 260                            | TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665  | 03/2017          | 672.89<br>-                       | 736.01                      | 03/2020<br>-          | 03/2020     | 9.38             |
| 261                            | SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668                 | 03/2017          | 1,041.62<br>-                     | 1,187.10                    | 03/2020<br>-          | 03/2020     | 13.97            |
| 262                            | 4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669                                     | 03/2017          | 165.50<br>-                       | 172.16                      | 03/2020<br>-          | 03/2020     | 4.02             |
| 263                            | REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671  | 03/2017          | 1,288.07<br>-                     | 1,420.00                    | 03/2020<br>-          | 03/2020     | 10.24            |
| 264                            | 6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672 | 03/2017          | 2,064.99<br>-                     | 2,447.00                    | 03/2020<br>-          | 03/2020     | 18.50            |
| 265                            | SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673 | 03/2017          | 985.41<br>-                       | 1,200.00                    | 03/2020<br>-          | 03/2020     | 21.78            |
| 266                            | SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674   | 03/2017          | 831.58<br>-                       | 1,177.00                    | 03/2020<br>-          | 03/2020     | 41.54            |
| 267                            | SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675 | 03/2017          | 993.16<br>-                       | 1,434.00                    | 03/2020<br>-          | 03/2020     | 44.39            |
| 268                            | RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695                                                                  | 04/2017          | 388.00<br>-                       | 447.37                      | 10/2017<br>-          | 10/2017     | 15.30            |
|                                | Total                                                                                                             |                  | 23,165.35<br>-                    | 29,854.53                   |                       |             |                  |
|                                |                                                                                                                   |                  |                                   |                             |                       |             |                  |
|                                | <u>SHIPPING AND PORTS</u>                                                                                         |                  |                                   |                             |                       |             |                  |
| 269                            | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035                                          | 10/2002          | 150.00<br>-                       | 600.00                      | 03/2006<br>-          | 12/2017     | 300.00           |



## List of ongoing projects having cost overrun w.r.t. to Revised schedule

| Costing Rs.150 Crore and above |                                                                                                                    |                  |                                   |                             | (September 2017)      |             |                  |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|                                |                                                                                                                    |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No                           | Project                                                                                                            | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1                              | 2                                                                                                                  | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 270                            | CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED<br>- [N25000065]                                            | 10/2013          | 198.94<br>-                       | 235.15                      | 06/2017<br>-          | -           | 18.20            |
| 271                            | CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED<br>- [N25000066]                                            | 02/2015          | 244.50<br>258.00                  | 258.33                      | 12/2017<br>-          | 12/2017     | .13              |
| 272                            | RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST<br>- [N25000059]                                     | 03/2007          | 245.67<br>-                       | 409.83                      | 04/2009<br>-          | -           | 66.82            |
| 273                            | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063] | 01/2007          | 366.39<br>-                       | 669.46                      | 12/2010<br>-          | 12/2018     | 82.72            |
|                                | Total                                                                                                              |                  | 1,205.50<br>-                     | 2,172.77                    |                       |             |                  |
|                                |                                                                                                                    |                  |                                   |                             |                       |             |                  |
|                                | <u>STEEL</u>                                                                                                       |                  |                                   |                             |                       |             |                  |
| 274                            | CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA<br>- [N12000101]                                          | 05/2005          | 768.88<br>1,070.97                | 1,113.34                    | 02/2014<br>-          | -           | 3.96             |
| 275                            | REVAMPING OF SINTER MACHINES - 1 AND 2<br>- [N12000091]                                                            | 12/2009          | 343.00<br>-                       | 488.40                      | 10/2016<br>-          | 03/2018     | 42.39            |
| 276                            | CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V<br>- [N12000098]                                   | 03/2007          | 149.73<br>173.00                  | 175.94                      | 12/2015<br>-          | -           | 1.70             |
|                                | Total                                                                                                              |                  | 1,261.61<br>-                     | 1,777.68                    |                       |             |                  |
|                                |                                                                                                                    |                  |                                   |                             |                       |             |                  |
|                                | <u>TELECOMMUNICATIONS</u>                                                                                          |                  |                                   |                             |                       |             |                  |
| 277                            | NETWORK FOR SPECTRUM<br>- [N26000101]                                                                              | 03/2012          | 13,334.00<br>-                    | 24,664.00                   | 07/2015<br>-          | 06/2019     | 84.97            |
|                                | Total                                                                                                              |                  | 13,334.00<br>-                    | 24,664.00                   |                       |             |                  |
|                                |                                                                                                                    |                  |                                   |                             |                       |             |                  |
|                                | <u>URBAN DEVELOPMENT</u>                                                                                           |                  |                                   |                             |                       |             |                  |
| 278                            | UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARAstra<br>- [N28000073]                                | 06/2010          | 205.00<br>-                       | 170.62                      | 03/2012<br>-          | 03/2018     | -16.77           |
| 279                            | CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA<br>- [N28000100]       | 02/2016          | 496.18<br>496.00                  | 496.18                      | 06/2017<br>-          | -           | .04              |
|                                | Total                                                                                                              |                  | 701.18<br>-                       | 666.80                      |                       |             |                  |
|                                |                                                                                                                    |                  |                                   |                             |                       |             |                  |
|                                | Grand Total                                                                                                        |                  | 2,36,759.70                       | 4,49,663.90                 |                       |             |                  |

## List of Delayed Projects w.r.t. Latest Schedule

Annexure-XIV

**Costing Rs.150 Crore and above** **(September 2017)**

| S.No | Project                                                                                                               | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Date of Commissioning |             | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
|------|-----------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|      |                                                                                                                       |                  |                                    |                              |                                         | Original / Revised    | Anticipated |                                   |                                  |
| 1    | 2                                                                                                                     | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
|      |                                                                                                                       |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | <u>ATOMIC ENERGY</u>                                                                                                  |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 1    | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU                                      | 09/2003          | 3,492.00<br>5,677.00               | 6,000.00                     | 5,486.27                                | 09/2010<br>09/2016    | 02/2018     | 89                                | 17                               |
| 2    | KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT                                                    | 10/2009          | 11,459.00<br>-                     | 11,459.00                    | 10,710.00                               | 12/2015<br>11/2016    | 11/2019     | 47                                | 36                               |
| 3    | RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN                                      | 10/2009          | 12,320.00<br>-                     | 12,320.00                    | 8,312.00                                | 12/2016<br>03/2017    | 12/2020     | 48                                | 45                               |
|      | Total                                                                                                                 |                  | 27,271.00<br>-                     | 29,779.00                    | 24,508.27                               |                       |             |                                   |                                  |
|      |                                                                                                                       |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | <u>CIVIL AVIATION</u>                                                                                                 |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 4    | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS | 10/2013          | 314.61<br>-                        | 441.33                       | 24.13                                   | 09/2018<br>-          | 06/2020     | 21                                | -                                |
|      | Total                                                                                                                 |                  | 314.61<br>-                        | 441.33                       | 24.13                                   |                       |             |                                   |                                  |
|      |                                                                                                                       |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|      | <u>COAL</u>                                                                                                           |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 5    | NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU                                                        | 05/2016          | 687.28<br>-                        | 687.28                       | 690.47                                  | 06/2017<br>-          | 10/2017     | 4                                 | -                                |
| 6    | RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND                                                                           | 09/2009          | 153.82<br>-                        | 153.82                       | 126.63                                  | 03/2014<br>-          | 12/2017     | 45                                | -                                |
| 7    | KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA                                                           | 01/2005          | 302.96<br>-                        | 302.96                       | 329.10                                  | 03/2010<br>-          | 03/2018     | 96                                | -                                |
| 8    | RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA                                                                           | 03/2010          | 209.78<br>-                        | 209.78                       | 120.55                                  | 03/2015<br>-          | 03/2018     | 36                                | -                                |
| 9    | MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA                                                         | 03/2010          | 181.19<br>-                        | 181.19                       | 176.79                                  | 03/2012<br>-          | 03/2018     | 72                                | -                                |
| 10   | MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH                                                         | 12/2009          | 321.50<br>-                        | 321.50                       | 198.19                                  | 03/2014<br>-          | 03/2018     | 48                                | -                                |
| 11   | AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH                                                  | 11/2009          | 198.59<br>-                        | 198.59                       | 169.38                                  | 03/2016<br>-          | 03/2018     | 24                                | -                                |
| 12   | PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND                                                                     | 07/2008          | 210.98<br>-                        | 210.98                       | 206.31                                  | 03/2013<br>-          | 03/2018     | 60                                | -                                |
| 13   | RAJRAPPA RCE OCP ( 3.0 MTY) - [N06000087]CCL,JHARKHAND                                                                | 12/2009          | 510.85<br>-                        | 510.85                       | 341.12                                  | 03/2016<br>-          | 03/2018     | 24                                | -                                |
| 14   | BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH                                                         | 04/2012          | 258.56<br>-                        | 258.56                       | 151.94                                  | 03/2016<br>-          | 03/2018     | 24                                | -                                |
| 15   | RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA                                                  | 06/2012          | 365.01<br>-                        | 365.01                       | 57.64                                   | 06/2015<br>-          | 03/2018     | 33                                | -                                |
| 16   | RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA                                                                | 11/2012          | 430.45<br>415.37                   | 415.37                       | 136.75                                  | 03/2016<br>-          | 03/2018     | 24                                | -                                |
| 17   | MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND                                                                     | 08/2010          | 289.45<br>-                        | 289.45                       | 151.66                                  | 05/2014<br>-          | 04/2018     | 47                                | -                                |

## List of Delayed Projects w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                  |                  |                                    |                              |                                         |                       |             | (September 2017)                  |                                  |
|--------------------------------|------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|                                |                                                                  |                  |                                    |                              |                                         | Date of Commissioning |             |                                   |                                  |
| S.No                           | Project                                                          | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
| 1                              | 2                                                                | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 18                             | PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND                | 10/2012          | 269.82 -                           | 269.82                       | 150.11                                  | 04/2014 -             | 04/2018     | 48                                | -                                |
| 19                             | BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA         | 12/2007          | 490.10 -                           | 490.10                       | 278.34                                  | 03/2017 -             | 05/2018     | 14                                | -                                |
| 20                             | SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL | 08/2012          | 1,055.05 -                         | 1,055.05                     | 316.35                                  | 03/2018 -             | 09/2018     | 6                                 | -                                |
| 21                             | MURAIIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND         | 02/2011          | 339.88 -                           | 339.88                       | 12.08                                   | 04/2014 -             | 10/2018     | 54                                | -                                |
| 22                             | KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA              | 12/2007          | 457.77 -                           | 457.77                       | 404.51                                  | 03/2013 -             | 11/2018     | 68                                | -                                |
| 23                             | SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA       | 10/2006          | 249.03 448.86                      | 448.86                       | 157.97                                  | 03/2012 -             | 03/2019     | 84                                | -                                |
| 24                             | BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA        | 12/2007          | 172.08 -                           | 172.08                       | 191.07                                  | 03/2010 -             | 03/2019     | 108                               | -                                |
| 25                             | ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA    | 08/2008          | 207.28 -                           | 207.28                       | 219.09                                  | 03/2012 -             | 03/2019     | 84                                | -                                |
| 26                             | HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA       | 11/2008          | 479.53 -                           | 479.53                       | 219.12                                  | 03/2013 -             | 03/2019     | 72                                | -                                |
| 27                             | NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND           | 12/2007          | 179.87 -                           | 179.87                       | 97.03                                   | 03/2012 -             | 03/2019     | 84                                | -                                |
| 28                             | TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND                   | 08/2008          | 264.68 -                           | 264.68                       | 153.14                                  | 03/2012 -             | 03/2019     | 84                                | -                                |
| 29                             | KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND                    | 06/2009          | 162.46 -                           | 162.46                       | 80.63                                   | 03/2014 -             | 03/2019     | 60                                | -                                |
| 30                             | KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA           | 10/2015          | 426.79 -                           | 426.79                       | -                                       | 03/2018 -             | 03/2019     | 12                                | -                                |
| 31                             | MOONIDH XV SEAM UG - [N06000098]BCCL,JHARKHAND                   | 08/2011          | 1,230.27 -                         | 1,230.27                     | 179.50                                  | 04/2015 -             | 04/2019     | 48                                | -                                |
| 32                             | KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH      | 07/2008          | 178.44 -                           | 178.44                       | 5.12                                    | 03/2014 -             | 03/2020     | 72                                | -                                |
| 33                             | CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND             | 08/2007          | 163.51 -                           | 163.51                       | 93.28                                   | 03/2011 -             | 03/2020     | 108                               | -                                |
| 34                             | KISTARAM OCP - [N06000089]SCCL,TELANGANA                         | 11/2010          | 242.29 164.04                      | 164.04                       | .09                                     | 03/2015 -             | 03/2020     | 60                                | -                                |
| 35                             | RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA        | 07/2011          | 162.76 349.28                      | 349.28                       | 1.31                                    | 03/2015 -             | 03/2020     | 60                                | -                                |
| 36                             | KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA        | 07/2012          | 417.33 417.33                      | 417.33                       | 43.97                                   | 07/2016 -             | 03/2020     | 44                                | -                                |
| 37                             | MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND                | 08/2008          | 706.40 -                           | 706.40                       | 116.67                                  | 07/2012 03/2017       | 03/2021     | 104                               | 48                               |
| 38                             | JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA           | 07/2011          | 447.06 -                           | 437.51                       | 259.34                                  | 03/2015 -             | 03/2021     | 72                                | -                                |
| 39                             | RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA           | 12/2009          | 418.97 -                           | 489.62                       | 477.74                                  | 03/2012 -             | 03/2023     | 132                               | -                                |
|                                | Total                                                            |                  | 12,841.79 -                        | 13,195.91                    | 6,312.99                                |                       |             |                                   |                                  |
|                                |                                                                  |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|                                | <u>STEEL</u>                                                     |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 40                             | EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH    | 08/2010          | 17,265.00 -                        | 17,265.00                    | 17,970.98                               | 03/2013 -             | 10/2017     | 55                                | -                                |

## List of Delayed Projects w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                                  |                  |                                    |                              |                                         |                       |             | (September 2017)                  |                                  |
|--------------------------------|----------------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|                                |                                                                                                                                  |                  |                                    |                              |                                         | Date of Commissioning |             |                                   |                                  |
| S.No                           | Project                                                                                                                          | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
| 1                              | 2                                                                                                                                | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 41                             | REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND                                                                           | 10/2013          | 245.67 -                           | 245.67                       | 195.66                                  | 05/2016 -             | 10/2017     | 17                                | -                                |
| 42                             | 3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH                                                                    | 07/2011          | 974.76 -                           | 974.76                       | 533.93                                  | 07/2016 -             | 10/2017     | 15                                | -                                |
| 43                             | BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH                                                      | 07/2011          | 877.73 -                           | 877.73                       | 746.08                                  | 07/2015 -             | 10/2017     | 27                                | -                                |
| 44                             | TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH                                                                                | 12/2009          | 280.00 -                           | 280.00                       | 155.29                                  | 09/2016 -             | 10/2017     | 13                                | -                                |
| 45                             | CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA                                       | 12/2007          | 202.61 227.00                      | 227.00                       | 199.95                                  | 12/2016 -             | 12/2017     | 12                                | -                                |
| 46                             | REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH                                                          | 12/2009          | 343.00 -                           | 488.40                       | 225.07                                  | 10/2016 -             | 03/2018     | 17                                | -                                |
| 47                             | CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY- JHARKHAND - [N12000109]HSCL,JHARKHAND                       | 12/2007          | 253.92 253.92                      | 253.92                       | 193.97                                  | 06/2016 -             | 03/2018     | 21                                | -                                |
| 48                             | MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND                                       | 05/2015          | 1,154.18 -                         | 1,154.18                     | 477.09                                  | 12/2017 -             | 05/2018     | 5                                 | -                                |
| 49                             | COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH                                                                             | 12/2011          | 2,858.00 -                         | 2,500.00                     | 591.35                                  | 12/2017 -             | 06/2018     | 6                                 | -                                |
| 50                             | NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND                                                               | 03/2015          | 1,034.01 -                         | 1,034.01                     | 187.29                                  | 10/2017 -             | 07/2018     | 9                                 | -                                |
| 51                             | CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN | 05/2015          | 189.00 -                           | 189.00                       | -                                       | 03/2017 -             | 08/2018     | 17                                | -                                |
| 52                             | CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA | 04/2014          | 151.33 -                           | 151.33                       | 7.15                                    | 09/2017 -             | 12/2018     | 15                                | -                                |
| 53                             | CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND                                     | 02/2014          | 787.29 -                           | 787.29                       | 285.30                                  | 12/2016 -             | 12/2018     | 24                                | -                                |
| 54                             | INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA                                                               | 04/2015          | 3,127.30 -                         | 3,127.30                     | 1,205.62                                | 04/2018 -             | 02/2019     | 10                                | -                                |
| 55                             | IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR                                                                               | 10/2005          | 956.00 -                           | 956.00                       | 651.21                                  | 03/2015 -             | 03/2021     | 72                                | -                                |
|                                | Total                                                                                                                            |                  | 30,699.80 -                        | 30,511.59                    | 23,625.94                               |                       |             |                                   |                                  |
|                                |                                                                                                                                  |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|                                | <u>PETROLEUM</u>                                                                                                                 |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 56                             | RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]IOCL,ASSAM                                | 06/2012          | 150.00 -                           | 259.93                       | 251.90                                  | 07/2014 -             | 09/2017     | 38                                | -                                |
| 57                             | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRIL,KARNATAKA                                                       | 01/2006          | 993.00 -                           | 1,693.00                     | 1,537.84                                | 01/2012 -             | 10/2017     | 69                                | -                                |
| 58                             | RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU                                                                           | 03/2013          | 3,110.36 -                         | 3,110.36                     | 2,765.42                                | 11/2015 -             | 10/2017     | 23                                | -                                |
| 59                             | DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]CPCL,TAMIL NADU                                                        | 02/2016          | 367.11 -                           | 367.11                       | 218.14                                  | 04/2017 -             | 11/2017     | 7                                 | -                                |

## List of Delayed Projects w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                                     |                  |                                    |                              |                                         | (September 2017)      |             |                                   |                                  |
|--------------------------------|-------------------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|                                |                                                                                                                                     |                  |                                    |                              |                                         | Date of Commissioning |             |                                   |                                  |
| S.No                           | Project                                                                                                                             | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
| 1                              | 2                                                                                                                                   | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 60                             | UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM                      | 09/2012          | 871.35<br>-                        | 1,200.00                     | 958.00                                  | 03/2015<br>-          | 11/2017     | 32                                | -                                |
| 61                             | NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL, TAMIL NADU                                   | 05/2015          | 257.87<br>-                        | 257.87                       | 117.68                                  | 11/2016<br>-          | 02/2018     | 15                                | -                                |
| 62                             | FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY - [N16000245]IOCL, GUJARAT                                         | 02/2016          | 931.00<br>-                        | 931.00                       | 383.35                                  | 07/2017<br>-          | 02/2018     | 7                                 | -                                |
| 63                             | TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL, ASSAM                                                                                | 03/2009          | 228.64<br>-                        | 209.19                       | 147.05                                  | 12/2016<br>-          | 03/2018     | 15                                | -                                |
| 64                             | SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL, MULTI STATE                | 07/2011          | 352.56<br>-                        | 439.03                       | 126.43                                  | 03/2017<br>-          | 11/2018     | 20                                | -                                |
| 65                             | KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL, MULTI STATE                                                | 06/2009          | 2,915.00<br>2,915.00               | 2,915.00                     | 1,258.49                                | 12/2012<br>-          | 02/2019     | 74                                | -                                |
| 66                             | LPG TERMINAL AT KOCHI - [N16000171]IOCL, KERALA                                                                                     | 10/2015          | 607.06<br>714.25                   | 714.25                       | 276.85                                  | 10/2017<br>-          | 03/2019     | 17                                | -                                |
| 67                             | Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC, TAMIL NADU                                           | 11/2015          | 390.52<br>-                        | 390.52                       | 67.52                                   | 03/2019<br>-          | 04/2019     | 1                                 | -                                |
|                                | Total                                                                                                                               |                  | 11,174.47<br>-                     | 12,487.26                    | 8,108.67                                |                       |             |                                   |                                  |
|                                |                                                                                                                                     |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|                                | <u>POWER</u>                                                                                                                        |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 68                             | PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC, JHARKHAND                                                                     | 10/2004          | 4,237.96<br>4,552.00               | 4,552.00                     | 2,229.09                                | 10/2017<br>12/2016    | 10/2017     | 0                                 | 10                               |
| 69                             | KUDGI STPP STAGE 1 - [N18000131]NTPC, KARNATAKA                                                                                     | 01/2012          | 15,166.19<br>-                     | 15,166.19                    | 14,295.00                               | 01/2017<br>07/2017    | 11/2017     | 10                                | 4                                |
| 70                             | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL, MADHYA PRADESH                                           | 01/2016          | 305.04<br>-                        | 305.04                       | 156.38                                  | 03/2017<br>10/2017    | 11/2017     | 8                                 | 1                                |
| 71                             | BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM                                                                           | 01/2008          | 4,375.35<br>6,749.18               | 6,749.18                     | 6,797.00                                | 09/2011<br>06/2017    | 12/2017     | 75                                | 6                                |
| 72                             | SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL, MULTI STATE                                                                      | 02/2010          | 232.34<br>-                        | 245.00                       | 238.61                                  | 06/2012<br>-          | 12/2017     | 66                                | -                                |
| 73                             | COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL, TAMIL NADU | 09/2011          | 1,940.13<br>2,702.65               | 2,702.65                     | 2,326.66                                | 09/2014<br>06/2017    | 12/2017     | 39                                | 6                                |
| 74                             | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL, MULTI STATE                                                    | 11/2011          | 723.63<br>882.13                   | 882.13                       | 719.42                                  | 11/2014<br>06/2017    | 12/2017     | 37                                | 6                                |
| 75                             | STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL, MULTI STATE                                                   | 05/2014          | 829.98<br>-                        | 829.98                       | 408.14                                  | 08/2016<br>10/2017    | 12/2017     | 16                                | 2                                |
| 76                             | AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL, MULTI STATE                                            | 03/2014          | 155.57<br>206.42                   | 206.42                       | 131.33                                  | 03/2016<br>07/2017    | 12/2017     | 21                                | 5                                |

## List of Delayed Projects w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                                  |                  |                                    |                              |                                         |                       | (September 2017) |                                   |                                  |
|--------------------------------|----------------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|------------------|-----------------------------------|----------------------------------|
|                                |                                                                                                                                  |                  |                                    |                              |                                         | Date of Commissioning |                  |                                   |                                  |
| S.No                           | Project                                                                                                                          | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated      | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
| 1                              | 2                                                                                                                                | 3                | 4                                  | 5                            | 6                                       | 7                     | 8                | 9                                 | 10                               |
| 77                             | EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE                                                           | 02/2014          | 196.58<br>225.28                   | 225.28                       | 129.10                                  | 02/2016<br>08/2017    | 12/2017          | 22                                | 4                                |
| 78                             | SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE                                                   | 01/2015          | 203.28<br>260.03                   | 260.03                       | 160.70                                  | 07/2017<br>-          | 12/2017          | 5                                 | -                                |
| 79                             | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR                                         | 05/2015          | 436.68<br>-                        | 602.44                       | 472.27                                  | 12/2016<br>-          | 12/2017          | 12                                | -                                |
| 80                             | ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE                              | 03/2012          | 198.63<br>-                        | 198.63                       | 135.20                                  | 09/2014<br>09/2017    | 01/2018          | 40                                | 4                                |
| 81                             | KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR                                                                   | 01/2009          | 3,642.04<br>-                      | 5,882.01                     | 5,052.02                                | 01/2016<br>-          | 02/2018          | 25                                | -                                |
| 82                             | WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA                                                             | 12/2007          | 477.69<br>738.48                   | 738.48                       | 647.49                                  | 09/2010<br>12/2017    | 03/2018          | 90                                | 3                                |
| 83                             | COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE | 03/2013          | 514.20<br>703.10                   | 703.10                       | 565.59                                  | 06/2015<br>12/2017    | 03/2018          | 33                                | 3                                |
| 84                             | COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE | 03/2013          | 2,514.88<br>-                      | 2,514.88                     | 1,959.67                                | 12/2015<br>12/2017    | 03/2018          | 27                                | 3                                |
| 85                             | EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE                                                             | 10/2013          | 1,364.52<br>1,891.41               | 1,891.41                     | 1,151.24                                | 04/2016<br>09/2017    | 03/2018          | 23                                | 6                                |
| 86                             | EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE                                                           | 05/2014          | 522.29<br>550.18                   | 550.18                       | 362.94                                  | 11/2016<br>11/2017    | 03/2018          | 16                                | 4                                |
| 87                             | SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE                                               | 08/2014          | 288.49<br>-                        | 376.09                       | 219.91                                  | 02/2017<br>06/2017    | 03/2018          | 13                                | 9                                |
| 88                             | TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE                | 03/2015          | 955.00<br>1,161.00                 | 1,364.00                     | 1,075.00                                | 12/2015<br>-          | 03/2018          | 27                                | -                                |
| 89                             | TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM CUDDALORE AREA - PACKAGE A - [N18000259]PGCIL,MULTI STATE               | 03/2015          | 955.00<br>1,161.00                 | 1,364.00                     | 515.00                                  | 12/2015<br>-          | 03/2018          | 27                                | -                                |
| 90                             | SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA                                                                                       | 03/2012          | 9,395.18<br>-                      | 9,395.18                     | 8,052.00                                | 11/2016<br>12/2017    | 04/2018          | 17                                | 4                                |
| 91                             | LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH                                              | 12/2012          | 11,846.00<br>-                     | 11,846.00                    | 8,605.00                                | 06/2017<br>12/2017    | 04/2018          | 10                                | 4                                |
| 92                             | INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE                                                        | 03/2015          | 1,071.24<br>-                      | 1,071.24                     | 462.18                                  | 09/2017<br>-          | 04/2018          | 7                                 | -                                |
| 93                             | SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE                                                               | 10/2011          | 487.49<br>639.46                   | 639.46                       | 485.42                                  | 06/2014<br>03/2018    | 06/2018          | 48                                | 3                                |
| 94                             | TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE         | 06/2014          | 5,151.37<br>-                      | 5,151.37                     | 1,474.02                                | 03/2018<br>-          | 06/2018          | 3                                 | -                                |
| 95                             | TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE                                | 01/2015          | 871.62<br>-                        | 871.62                       | 141.74                                  | 10/2017<br>10/2017    | 06/2018          | 8                                 | 8                                |

## List of Delayed Projects w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                                     |                  |                                    |                              |                                         |                       | (September 2017) |                                   |                                  |
|--------------------------------|-------------------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|------------------|-----------------------------------|----------------------------------|
|                                |                                                                                                                                     |                  |                                    |                              |                                         | Date of Commissioning |                  |                                   |                                  |
| S.No                           | Project                                                                                                                             | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated      | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
| 1                              | 2                                                                                                                                   | 3                | 4                                  | 5                            | 6                                       | 7                     | 8                | 9                                 | 10                               |
| 96                             | BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR                                                                          | 01/2007          | 5,353.00<br>7,998.00               | 7,998.00                     | 6,783.73                                | 05/2014<br>09/2017    | 06/2018          | 49                                | 9                                |
| 97                             | MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH                                                                      | 04/2012          | 9,750.89<br>-                      | 9,750.89                     | 6,957.91                                | 12/2016<br>-          | 06/2018          | 18                                | -                                |
| 98                             | TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN                                              | 07/2015          | 307.18<br>-                        | 307.18                       | 153.62                                  | 11/2017<br>-          | 06/2018          | 7                                 | -                                |
| 99                             | GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE                                       | 04/2015          | 3,705.61<br>-                      | 3,705.61                     | 2,077.41                                | 04/2018<br>-          | 07/2018          | 3                                 | -                                |
| 100                            | TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR    | 01/2014          | 1,788.41<br>-                      | 2,352.57                     | 1,154.26                                | 09/2017<br>-          | 09/2018          | 12                                | -                                |
| 101                            | PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH                                                                 | 09/2002          | 3,919.59<br>-                      | 8,398.75                     | 6,503.48                                | 09/2009<br>-          | 12/2018          | 111                               | -                                |
| 102                            | DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH                                                                       | 05/2011          | 195.42<br>294.60                   | 294.60                       | 130.15                                  | 02/2014<br>02/2018    | 12/2018          | 58                                | 10                               |
| 103                            | NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR                                                                       | 01/2013          | 12,964.60<br>-                     | 13,731.26                    | 10,084.21                               | 01/2018<br>-          | 12/2018          | 11                                | -                                |
| 104                            | BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR                                                                                     | 02/2005          | 8,692.97<br>15,095.67              | 15,095.67                    | 13,727.00                               | 01/2011<br>05/2018    | 03/2019          | 98                                | 10                               |
| 105                            | TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE | 03/2016          | 808.63<br>-                        | 808.63                       | 195.53                                  | 01/2018<br>-          | 03/2019          | 14                                | -                                |
| 106                            | COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE        | 12/2014          | 4,754.42<br>-                      | 4,754.42                     | 361.65                                  | 12/2018<br>-          | 12/2019          | 12                                | -                                |
| 107                            | NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE                   | 12/2014          | 5,111.33<br>-                      | 5,111.33                     | 352.58                                  | 12/2018<br>-          | 12/2019          | 12                                | -                                |
| 108                            | VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND                                                          | 08/2008          | 2,491.58<br>-                      | 2,491.58                     | 1,244.96                                | 06/2013<br>-          | 11/2020          | 89                                | -                                |
| 109                            | TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND                                                                  | 07/2006          | 1,657.00<br>2,978.86               | 3,939.11                     | 2,373.15                                | 02/2016<br>09/2019    | 12/2020          | 58                                | 15                               |
| 110                            | NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND                                                                         | 02/2014          | 14,366.58<br>-                     | 14,366.58                    | 5,493.00                                | 02/2019<br>02/2020    | 02/2021          | 24                                | 12                               |
| 111                            | PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR                                                    | 10/2014          | 8,112.12<br>-                      | 8,112.12                     | -                                       | 04/2020<br>-          | 05/2023          | 37                                | -                                |
|                                | Total                                                                                                                               |                  | 1,53,037.70<br>-                   | 1,78,502.29                  | 1,16,560.76                             |                       |                  |                                   |                                  |
|                                |                                                                                                                                     |                  |                                    |                              |                                         |                       |                  |                                   |                                  |
|                                | <u>HEAVY INDUSTRY</u>                                                                                                               |                  |                                    |                              |                                         |                       |                  |                                   |                                  |
| 112                            | NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATIP) - [N20000001]NATIS,MULTI STATE                                    | 04/2011          | 1,718.00<br>-                      | 3,827.30                     | 2,289.00                                | 09/2011<br>-          | 12/2017          | 75                                | -                                |
|                                | Total                                                                                                                               |                  | 1,718.00<br>-                      | 3,827.30                     | 2,289.00                                |                       |                  |                                   |                                  |

## List of Delayed Projects w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                 |                  |                                    |                              |                                         | (September 2017)      |             |                                   |                                  |
|--------------------------------|-----------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|                                |                                                                                                                 |                  |                                    |                              |                                         | Date of Commissioning |             |                                   |                                  |
| S.No                           | Project                                                                                                         | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
| 1                              | 2                                                                                                               | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
|                                | <u>HEALTH AND FAMILY WELFARE</u>                                                                                |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 113                            | AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC, DELHI                                                         | 12/2013          | 204.44 -                           | 204.44                       | 137.00                                  | 05/2017 -             | 12/2017     | 7                                 | -                                |
| 114                            | AIIMS - OPD(NEW) - [N21000009]HSCC, DELHI                                                                       | 08/2014          | 293.65 -                           | 293.65                       | 207.00                                  | 05/2017 -             | 12/2017     | 7                                 | -                                |
| 115                            | CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC, WEST BENGAL                                   | 12/2014          | 168.90 -                           | 168.90                       | 108.00                                  | 05/2017 -             | 12/2017     | 7                                 | -                                |
| 116                            | SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC, PUNJAB                                        | 07/2016          | 152.95 -                           | 152.95                       | 33.50                                   | 02/2018 -             | 08/2018     | 6                                 | -                                |
|                                | <b>Total</b>                                                                                                    |                  | 819.94 -                           | 819.94                       | 485.50                                  |                       |             |                                   |                                  |
|                                | <u>RAILWAYS</u>                                                                                                 |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 117                            | NANDYAL-YERRAGUNTLA(NL), SCR - [220100192]SCR, ANDHRA PRADESH                                                   | 03/1996          | 155.74 164.36                      | 966.98                       | 874.72                                  | 02/2009 -             | 12/2017     | 106                               | -                                |
| 118                            | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, ODISHA                                             | 04/2000          | 133.41 207.00                      | 340.00                       | -                                       | 03/2009 03/2009       | 12/2017     | 105                               | 105                              |
| 119                            | SALKA ROAD - ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, CHHATISGARH                                             | 09/2006          | 324.90 -                           | 516.40                       | 479.68                                  | 03/2010 -             | 12/2017     | 93                                | -                                |
| 120                            | UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR, GUJARAT                                      | 04/2008          | 1,389.62 -                         | 1,389.62                     | 1,513.78                                | 03/2014 -             | 12/2017     | 45                                | -                                |
| 121                            | EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, TAMIL NADU                              | 04/2006          | 495.74 -                           | 495.74                       | 404.30                                  | 06/2013 -             | 03/2018     | 57                                | -                                |
| 122                            | BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH                                                  | 09/2007          | 687.20 -                           | 950.00                       | -                                       | 03/2010 -             | 03/2018     | 96                                | -                                |
| 123                            | LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM                  | 04/1996          | 1,676.31 -                         | 7,000.00                     | 7,041.41                                | 03/2009 -             | 03/2018     | 108                               | -                                |
| 124                            | BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM                                            | 09/1997          | 1,500.00 -                         | 5,000.00                     | 4,793.77                                | 04/2008 12/2011       | 06/2018     | 122                               | 78                               |
| 125                            | EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL                         | 03/2013          | 4,874.58 -                         | 4,874.58                     | 1,881.65                                | 03/2016 -             | 06/2018     | 27                                | -                                |
| 126                            | UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR                                         | 03/1995          | 2,500.00 -                         | 19,565.00                    | 13,536.97                               | 11/2002 -             | 12/2018     | 193                               | -                                |
| 127                            | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL | 04/2010          | 2,913.51 -                         | 2,913.50                     | 713.47                                  | 03/2016 -             | 12/2018     | 33                                | -                                |
| 128                            | MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA                              | 04/2012          | 632.68 -                           | 816.55                       | 451.81                                  | 03/2016 -             | 12/2018     | 33                                | -                                |
| 129                            | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE                           | 04/2000          | 733.00 -                           | 3,010.00                     | 2,344.94                                | 12/2008 -             | 03/2019     | 123                               | -                                |
| 130                            | TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL                                        | 04/2000          | 1,188.91 -                         | 1,319.33                     | 757.23                                  | - 12/2009             | 03/2019     | -                                 | 111                              |



## List of Delayed Projects w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                            |                  |                                    |                              |                                         |                       |             | (September 2017)                  |                                  |
|--------------------------------|----------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|                                |                                                                                                                            |                  |                                    |                              |                                         | Date of Commissioning |             |                                   |                                  |
| S.No                           | Project                                                                                                                    | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
| 1                              | 2                                                                                                                          | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 131                            | HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA                                                                           | 04/1996          | 301.64 -                           | 1,185.64                     | -                                       | - 09/2009             | 03/2019     | -                                 | 114                              |
| 132                            | MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA                                                      | 04/2008          | 5,300.00 -                         | 7,986.04                     | 2,423.55                                | 03/2014 -             | 03/2019     | 60                                | -                                |
| 133                            | BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT                                           | 04/2008          | 318.24 -                           | 321.62                       | 37.15                                   | 03/2012 -             | 03/2019     | 84                                | -                                |
| 134                            | KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH                                                         | 08/2015          | 528.57 -                           | 528.57                       | 61.44                                   | 03/2018 -             | 03/2019     | 12                                | -                                |
| 135                            | JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN                               | 04/2008          | 653.19 -                           | 941.04                       | 642.94                                  | 03/2014 -             | 06/2019     | 63                                | -                                |
| 136                            | GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE                                                                   | 02/1997          | 386.30 -                           | 1,776.81                     | 967.96                                  | 03/1998 -             | 12/2019     | 261                               | -                                |
| 137                            | SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA                                                                   | 04/1998          | 183.23 -                           | 1,202.70                     | 392.96                                  | 02/2015 -             | 12/2019     | 58                                | -                                |
| 138                            | GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND                                                                  | 03/1997          | 261.70 -                           | 388.00                       | 329.39                                  | 02/2006 -             | 12/2019     | 166                               | -                                |
| 139                            | HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN                                                    | 04/2008          | 829.74 -                           | 1,161.64                     | 435.68                                  | 03/2015 -             | 12/2019     | 57                                | -                                |
| 140                            | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA                                            | 03/1996          | 495.44 1,781.98                    | 1,781.98                     | 663.37                                  | 03/2004 -             | 03/2020     | 192                               | -                                |
| 141                            | MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND                                                               | 04/1995          | 900.05 -                           | 1,125.89                     | 980.99                                  | 12/2011 12/2010       | 03/2020     | 99                                | 111                              |
| 142                            | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR                                                               | 04/2003          | 727.56 -                           | 9,658.00                     | 5,418.63                                | 03/2011 -             | 03/2020     | 108                               | -                                |
| 143                            | OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH                                                        | 07/2006          | 743.00 -                           | 1,825.00                     | -                                       | 03/2008 06/2008       | 03/2020     | 144                               | 141                              |
| 144                            | AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA                                                                        | 04/2008          | 813.34 -                           | 3,451.00                     | 2,351.21                                | 03/2014 -             | 03/2020     | 72                                | -                                |
| 145                            | BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM                                                                        | 04/2008          | 619.34 -                           | 4,600.00                     | 1,651.19                                | 04/2014 -             | 03/2020     | 71                                | -                                |
| 146                            | SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM                                                                                 | 04/2008          | 1,339.48 -                         | 4,084.69                     | 383.92                                  | 12/2015 -             | 03/2020     | 51                                | -                                |
| 147                            | AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT                                                                 | 04/2008          | 394.14 -                           | 385.60                       | 27.69                                   | 03/2013 -             | 03/2020     | 84                                | -                                |
| 148                            | NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND                                   | 04/2006          | 850.00 -                           | 3,000.00                     | 362.71                                  | 03/2015 -             | 03/2020     | 60                                | -                                |
| 149                            | ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA                                                                                 | 03/2015          | 960.00 578.00                      | 578.00                       | 298.80                                  | - 11/2015             | 03/2020     | -                                 | 52                               |
| 150                            | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL | 04/2010          | 3,951.98 -                         | 4,259.48                     | 1,455.71                                | 03/2016 -             | 12/2020     | 57                                | -                                |
| 151                            | KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH                                                             | 04/2015          | 2,499.71 -                         | 2,499.71                     | 25.30                                   | 03/2021 -             | 03/2022     | 12                                | -                                |
| 152                            | KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA                                                                  | 04/2015          | 2,361.74 -                         | 2,361.74                     | 17.49                                   | 03/2021 -             | 03/2022     | 12                                | -                                |

## List of Delayed Projects w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                                     |                  |                                    |                              |                                         | (September 2017)      |             |                                   |                                  |
|--------------------------------|-------------------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|                                |                                                                                                                                     |                  |                                    |                              |                                         | Date of Commissioning |             |                                   |                                  |
| S.No                           | Project                                                                                                                             | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
| 1                              | 2                                                                                                                                   | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 153                            | GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE                                                         | 04/2011          | 1,176.09 -                         | 3,845.60                     | 1.92                                    | 02/2020 -             | 12/2022     | 34                                | -                                |
| 154                            | DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANTPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE         | 04/2010          | 622.41 -                           | 2,030.50                     | 10.34                                   | 02/2019 -             | 12/2022     | 46                                | -                                |
| 155                            | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE                                                                 | 09/1998          | 247.66 -                           | 6,093.31                     | 972.82                                  | 05/2008 -             | 03/2023     | 178                               | -                                |
|                                | Total                                                                                                                               |                  | 46,670.15 -                        | 1,16,230.26                  | 54,706.89                               |                       |             |                                   |                                  |
|                                |                                                                                                                                     |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|                                | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                                  |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 156                            | NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM                                                                                     | 12/2003          | 225.00 -                           | 225.00                       | -                                       | 06/2008 -             | 09/2017     | 111                               | -                                |
| 157                            | SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE                                                             | 02/2009          | 1,693.75 -                         | 1,693.75                     | 2,675.28                                | 08/2011 -             | 09/2017     | 73                                | -                                |
| 158                            | INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH                                                                            | 10/2010          | 1,175.00 -                         | 1,206.10                     | 1,226.83                                | 04/2013 -             | 09/2017     | 53                                | -                                |
| 159                            | MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH                                                                                   | 04/2010          | 1,267.00 -                         | 1,267.00                     | 2,664.02                                | 06/2013 -             | 09/2017     | 51                                | -                                |
| 160                            | PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR                                                                      | 09/2011          | 574.00 -                           | 574.00                       | -                                       | 03/2014 -             | 09/2017     | 42                                | -                                |
| 161                            | TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN                                                     | 09/2014          | 425.19 -                           | 425.19                       | -                                       | 09/2016 -             | 09/2017     | 12                                | -                                |
| 162                            | 2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH                               | 09/2015          | 368.73 -                           | 368.73                       | 203.84                                  | 09/2016 -             | 09/2017     | 12                                | -                                |
| 163                            | FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH                                                                    | 05/2013          | 1,055.00 -                         | 1,601.77                     | 1,328.85                                | 11/2015 -             | 09/2017     | 22                                | -                                |
| 164                            | DEOLI KOTA - [N24000148]NHAI,RAJASTHAN                                                                                              | 01/2011          | 593.00 -                           | 593.00                       | -                                       | 07/2013 -             | 10/2017     | 51                                | -                                |
| 165                            | 2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR                                                                                  | 05/2011          | 351.54 -                           | 351.54                       | -                                       | 05/2013 -             | 10/2017     | 53                                | -                                |
| 166                            | BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH                                                                             | 03/2011          | 1,046.00 -                         | 1,046.00                     | 577.00                                  | 09/2013 -             | 10/2017     | 49                                | -                                |
| 167                            | ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH                                                                                      | 03/2013          | 1,573.00 -                         | 1,573.00                     | 1,850.00                                | 09/2015 -             | 10/2017     | 25                                | -                                |
| 168                            | REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH | 03/2015          | 271.45 -                           | 271.45                       | -                                       | 10/2015 -             | 10/2017     | 24                                | -                                |
| 169                            | JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR                                                              | 07/2010          | 1,813.76 -                         | 1,813.76                     | -                                       | 07/2013 -             | 11/2017     | 52                                | -                                |
| 170                            | MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE                                                                                | 09/2011          | 754.00 -                           | 754.00                       | 1,101.13                                | 03/2013 -             | 11/2017     | 56                                | -                                |
| 171                            | STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA   | 03/2015          | 165.67 -                           | 165.67                       | -                                       | 11/2015 -             | 11/2017     | 24                                | -                                |

## List of Delayed Projects w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                                   |                  |                                    |                              |                                         |                       |             | (September 2017)                  |                                  |
|--------------------------------|-----------------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|                                |                                                                                                                                   |                  |                                    |                              |                                         | Date of Commissioning |             |                                   |                                  |
| S.No                           | Project                                                                                                                           | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
| 1                              | 2                                                                                                                                 | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 172                            | STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA | 03/2015          | 159.12 -                           | 159.12                       | -                                       | 11/2015 -             | 11/2017     | 24                                | -                                |
| 173                            | 2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH                              | 04/2014          | 351.34 -                           | 351.34                       | 378.36                                  | 01/2016 -             | 11/2017     | 22                                | -                                |
| 174                            | 2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH                                                 | 04/2014          | 495.78 -                           | 495.78                       | 509.65                                  | 01/2016 -             | 11/2017     | 22                                | -                                |
| 175                            | 4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA                                                 | 06/2014          | 923.04 -                           | 923.04                       | 474.52                                  | 11/2016 -             | 11/2017     | 12                                | -                                |
| 176                            | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM                                                    | 12/2003          | 280.00 -                           | 361.00                       | -                                       | 02/2009 -             | 12/2017     | 106                               | -                                |
| 177                            | NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM                                                                                    | 12/2003          | 208.00 -                           | 208.00                       | -                                       | 04/2008 -             | 12/2017     | 116                               | -                                |
| 178                            | GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT                                                     | 03/2010          | 1,509.10 -                         | 3,237.87                     | 3,187.19                                | 09/2012 -             | 12/2017     | 63                                | -                                |
| 179                            | CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH                                                   | 11/2010          | 1,585.00 -                         | 1,585.00                     | 2,284.33                                | 05/2013 -             | 12/2017     | 55                                | -                                |
| 180                            | SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA                                              | 02/2010          | 617.00 -                           | 617.00                       | 245.89                                  | 08/2012 -             | 12/2017     | 64                                | -                                |
| 181                            | 4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE                                                                            | 02/2011          | 2,498.76 -                         | 2,498.76                     | 2,489.54                                | 08/2014 -             | 12/2017     | 40                                | -                                |
| 182                            | PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA                                                                                   | 10/2010          | 1,724.55 -                         | 1,724.55                     | 2,051.04                                | 03/2013 -             | 12/2017     | 57                                | -                                |
| 183                            | SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU                             | 09/2011          | 1,250.00 -                         | 1,250.00                     | 1,329.10                                | 12/2013 -             | 12/2017     | 48                                | -                                |
| 184                            | TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU                                                   | 05/2010          | 374.00 -                           | 374.00                       | 237.00                                  | 05/2013 -             | 12/2017     | 55                                | -                                |
| 185                            | 2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU                                                        | 09/2011          | 485.00 -                           | 485.00                       | 406.68                                  | 08/2013 -             | 12/2017     | 52                                | -                                |
| 186                            | TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH                                                                   | 04/2011          | 571.00 -                           | 571.00                       | 622.89                                  | 10/2013 -             | 12/2017     | 50                                | -                                |
| 187                            | 2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR                                                                       | 05/2011          | 511.54 -                           | 511.54                       | -                                       | 11/2013 -             | 12/2017     | 49                                | -                                |
| 188                            | SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR                                                                           | 06/2011          | 1,100.70 -                         | 1,100.70                     | -                                       | 06/2014 -             | 12/2017     | 42                                | -                                |
| 189                            | 4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL                                                                          | 02/2011          | 1,078.84 -                         | 1,078.84                     | 2,391.07                                | 08/2013 -             | 12/2017     | 52                                | -                                |
| 190                            | 6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL                                                              | 04/2012          | 1,396.18 -                         | 1,396.18                     | 2,694.55                                | 09/2014 -             | 12/2017     | 39                                | -                                |
| 191                            | 2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH                                                          | 07/2012          | 291.36 -                           | 291.36                       | 320.46                                  | 01/2014 -             | 12/2017     | 47                                | -                                |

## List of Delayed Projects w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                              |                  |                                    |                              |                                         |                       | (September 2017) |                                   |                                  |
|--------------------------------|------------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|------------------|-----------------------------------|----------------------------------|
|                                |                                                                                                                              |                  |                                    |                              |                                         | Date of Commissioning |                  |                                   |                                  |
| S.No                           | Project                                                                                                                      | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated      | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
| 1                              | 2                                                                                                                            | 3                | 4                                  | 5                            | 6                                       | 7                     | 8                | 9                                 | 10                               |
| 192                            | HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND                                                           | 11/2011          | 478.51 -                           | 478.00                       | 409.17                                  | 10/2013 -             | 12/2017          | 50                                | -                                |
| 193                            | RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND                                                                          | 12/2012          | 1,479.00 -                         | 1,479.00                     | 833.65                                  | 06/2015 -             | 12/2017          | 30                                | -                                |
| 194                            | DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE                                                            | 10/2012          | 1,928.22 -                         | 1,928.22                     | 2,488.00                                | 04/2015 -             | 12/2017          | 32                                | -                                |
| 195                            | BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL                                                                            | 08/2012          | 867.00 -                           | 867.00                       | 278.17                                  | 02/2015 -             | 12/2017          | 34                                | -                                |
| 196                            | JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB                                                                                | 01/2014          | 523.85 -                           | 523.85                       | 248.85                                  | 01/2016 -             | 12/2017          | 23                                | -                                |
| 197                            | GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN                                                           | 02/2008          | 1,673.70 -                         | 1,673.70                     | 3,145.92                                | 10/2011 -             | 12/2017          | 74                                | -                                |
| 198                            | FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH                                      | 02/2013          | 1,232.00 -                         | 1,232.00                     | -                                       | 08/2015 -             | 12/2017          | 28                                | -                                |
| 199                            | 4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA                                                  | 01/2015          | 972.50 -                           | 972.50                       | 1,458.72                                | 07/2017 -             | 01/2018          | 6                                 | -                                |
| 200                            | FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH                         | 11/2013          | 1,916.79 -                         | 1,916.79                     | 1,851.95                                | 11/2016 -             | 02/2018          | 15                                | -                                |
| 201                            | BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM                                                                           | 12/2003          | 217.61 -                           | 309.56                       | -                                       | 04/2010 -             | 03/2018          | 95                                | -                                |
| 202                            | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA                                                        | 05/2009          | 1,108.00 -                         | 2,288.00                     | 3,882.53                                | 11/2011 -             | 03/2018          | 76                                | -                                |
| 203                            | JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA                                                                                | 01/2011          | 536.00 -                           | 536.00                       | 672.72                                  | 01/2014 -             | 03/2018          | 50                                | -                                |
| 204                            | 4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR                                                                          | 01/2011          | 575.00 -                           | 575.00                       | -                                       | 07/2013 -             | 03/2018          | 56                                | -                                |
| 205                            | 4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL                                                                  | 02/2011          | 998.79 -                           | 998.79                       | 1,930.50                                | 08/2013 -             | 03/2018          | 55                                | -                                |
| 206                            | KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL                                                                         | 02/2012          | 702.16 -                           | 702.16                       | 490.36                                  | 07/2014 -             | 03/2018          | 44                                | -                                |
| 207                            | PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA                                                                                 | 12/2011          | 942.69 -                           | 942.69                       | 367.72                                  | 06/2014 -             | 03/2018          | 45                                | -                                |
| 208                            | WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA                                | 05/2013          | 1,348.20 -                         | 1,348.20                     | 1,788.75                                | 02/2014 -             | 03/2018          | 49                                | -                                |
| 209                            | 4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA                                            | 04/2014          | 1,266.60 -                         | 1,266.60                     | 1,360.00                                | 09/2016 -             | 03/2018          | 18                                | -                                |
| 210                            | 4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA                                                | 05/2014          | 1,655.01 -                         | 1,655.01                     | 1,290.00                                | 08/2016 -             | 03/2018          | 19                                | -                                |
| 211                            | FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA            | 04/2010          | 1,170.52 -                         | 1,170.52                     | -                                       | 06/2012 -             | 03/2018          | 69                                | -                                |
| 212                            | WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA | 12/2011          | 191.08 -                           | 191.08                       | -                                       | 08/2015 -             | 03/2018          | 31                                | -                                |

[illegible]

## List of Delayed Projects w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                                               |                  |                                    |                              |                                         | (September 2017)      |             |                                   |                                  |
|--------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|                                |                                                                                                                                               |                  |                                    |                              |                                         | Date of Commissioning |             |                                   |                                  |
| S.No                           | Project                                                                                                                                       | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
| 1                              | 2                                                                                                                                             | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
|                                | <u>SHIPPING AND PORTS</u>                                                                                                                     |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 230                            | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU                                                | 10/2002          | 150.00 -                           | 600.00                       | 139.80                                  | 03/2006 -             | 12/2017     | 141                               | -                                |
| 231                            | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA | 01/2007          | 366.39 -                           | 669.46                       | 411.12                                  | 12/2010 -             | 12/2018     | 96                                | -                                |
|                                | Total                                                                                                                                         |                  | 516.39 -                           | 1,269.46                     | 550.92                                  |                       |             |                                   |                                  |
|                                |                                                                                                                                               |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|                                | <u>TELECOMMUNICATIONS</u>                                                                                                                     |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 232                            | NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE                                                                                             | 03/2012          | 13,334.00 -                        | 24,664.00                    | 6,660.00                                | 07/2015 -             | 06/2019     | 47                                | -                                |
|                                | Total                                                                                                                                         |                  | 13,334.00 -                        | 24,664.00                    | 6,660.00                                |                       |             |                                   |                                  |
|                                |                                                                                                                                               |                  |                                    |                              |                                         |                       |             |                                   |                                  |
|                                | <u>URBAN DEVELOPMENT</u>                                                                                                                      |                  |                                    |                              |                                         |                       |             |                                   |                                  |
| 233                            | CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA                                     | 12/2012          | 315.00 -                           | 315.00                       | 302.82                                  | 06/2015 -             | 09/2017     | 27                                | -                                |
| 234                            | STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU                                                                    | 04/2014          | 332.72 -                           | 332.72                       | 260.88                                  | 09/2016 -             | 11/2017     | 14                                | -                                |
| 235                            | CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU                                                                                 | 02/2009          | 14,600.00<br>19,058.00             | 19,058.00                    | 14,784.59                               | 12/2015 -             | 12/2017     | 24                                | -                                |
| 236                            | CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUTCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD,KERALA                     | 07/2015          | 154.00 -                           | 154.00                       | 66.56                                   | 11/2015 -             | 12/2017     | 25                                | -                                |
| 237                            | CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL                                  | 02/2014          | 156.57 -                           | 156.57                       | 119.09                                  | 08/2016 -             | 03/2018     | 19                                | -                                |
| 238                            | OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA                                    | 02/2011          | 241.33<br>349.33                   | 349.33                       | 221.30                                  | 03/2016<br>12/2017    | 03/2018     | 24                                | 3                                |
| 239                            | UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA                                              | 06/2010          | 205.00<br>166.97                   | 170.62                       | 146.41                                  | 03/2012 -             | 03/2018     | 72                                | -                                |
| 240                            | CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA                                                                | 01/2010          | 165.23 -                           | 165.23                       | 25.91                                   | 10/2012<br>04/2017    | 03/2018     | 65                                | 11                               |
| 241                            | CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI                    | 07/2012          | 884.30 -                           | 884.30                       | 503.45                                  | 12/2015<br>12/2017    | 03/2018     | 27                                | 3                                |
| 242                            | DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH                                            | 11/2012          | 270.83 -                           | 270.83                       | 116.57                                  | 11/2014 -             | 10/2018     | 47                                | -                                |
| 243                            | NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR                                                                             | 02/2014          | 216.69 -                           | 216.69                       | 52.00                                   | 03/2015 -             | 11/2018     | 44                                | -                                |

## List of Delayed Projects w.r.t. Latest Schedule

| Costing Rs.150 Crore and above |                                                                                                                                   |                  |                                    |                              |                                         |                       |             | (September 2017)                  |                                  |
|--------------------------------|-----------------------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|                                |                                                                                                                                   |                  |                                    |                              |                                         | Date of Commissioning |             |                                   |                                  |
| S.No                           | Project                                                                                                                           | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. original (in months) | Delay w.r.t. Revised (in months) |
| 1                              | 2                                                                                                                                 | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                               |
| 244                            | 2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND                                              | 09/2012          | 171.86<br>-                        | 171.86                       | 38.40                                   | 03/2016<br>-          | 12/2018     | 33                                | -                                |
| 245                            | CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND | 12/2008          | 114.26<br>266.00                   | 266.00                       | -                                       | 12/2013<br>-          | 10/2019     | 70                                | -                                |
| 246                            | KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA                                                                                | 07/2012          | 5,181.79<br>-                      | 5,181.79                     | -                                       | 07/2017<br>-          | 12/2019     | 29                                | -                                |
| 247                            | NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA                                                                                  | 08/2014          | 8,680.00<br>-                      | 8,680.00                     | 1,688.81                                | 03/2018<br>-          | 12/2019     | 21                                | -                                |
| 248                            | BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA                                                                 | 02/2014          | 26,405.14<br>-                     | 26,405.14                    | 2,391.46                                | 02/2019<br>-          | 03/2020     | 13                                | -                                |
| 249                            | ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI           | 10/2013          | 1,219.21<br>2,230.23               | 1,592.00                     | 122.50                                  | 10/2019<br>-          | 03/2020     | 5                                 | -                                |
|                                | Total                                                                                                                             |                  | 59,313.93<br>-                     | 64,370.08                    | 20,840.75                               |                       |             |                                   |                                  |
|                                | Grand Total                                                                                                                       |                  | 4,22,560.94                        | 5,44,622.43                  | 3,19,949.99                             |                       |             |                                   |                                  |

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( SEPTEMBER 2017 )

## ATOMIC ENERGY

| Sn | Project                                             | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|----|-----------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 1  | RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) | NPCIL  | 10/2009 | 12/2016      | 12/2020         | 12320                     | 48           |
| 2  | KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4             | NPCIL  | 10/2009 | 12/2015      | 11/2019         | 11459                     | 47           |
| 3  | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)   | BHAVNI | 09/2003 | 09/2010      | 02/2018         | 3492                      | 89           |

## CIVIL AVIATION

| Sn | Project                                                                    | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|----|----------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 4  | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR | AAI    | 10/2013 | 09/2018      | 06/2020         | 314.61                    | 21           |
| 5  | CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT                     | AAI    | 01/2009 | 01/2011      | 09/2017         | 309.46                    | 80           |

## COAL

| Sn | Project                                     | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|----|---------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 6  | RFR OF MANUGURU OC PROJECT                  | SCCL   | 11/2012 | 03/2016      | 03/2018         | 430.45                    | 24           |
| 7  | KALYANIKHANI OPENCAST PROJECT               | SCCL   | 07/2012 | 07/2016      | 03/2020         | 417.33                    | 44           |
| 8  | RG OC -III EXTENSION (PHASE -II) PROJECT    | SCCL   | 06/2012 | 06/2015      | 03/2018         | 365.01                    | 33           |
| 9  | RCE OF INDARAM OCP(1.20 MTPA)               | SCCL   | 07/2011 | 03/2015      | 03/2020         | 162.76                    | 60           |
| 10 | NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) | NLC    | 06/2011 | 12/2015      | 04/2018         | 5907.11                   | 28           |
| 11 | JALAGAM VENGALA RAO OCP-II                  | SCCL   | 07/2011 | 03/2015      | 03/2021         | 447.06                    | 72           |
| 12 | BAROUD OC EXPANSION (RCE)- 3MTY             | SECL   | 04/2012 | 03/2016      | 03/2018         | 258.56                    | 24           |
| 13 | KANIHA OCP, MCL, (10.0 MTY)                 | MCL    | 12/2007 | 03/2013      | 11/2018         | 457.77                    | 68           |
| 14 | MANIKPUR OC EXPANSION (3.5 MTY)             | SECL   | 12/2009 | 03/2014      | 03/2018         | 321.5                     | 48           |
| 15 | BHUBANESWARI OCP, MCL (20.0 MTY)            | MCL    | 12/2007 | 03/2017      | 05/2018         | 490.1                     | 14           |
| 16 | ANANTA OC EXPANSION PH-III (15.0 MTY)       | MCL    | 08/2008 | 03/2012      | 03/2019         | 207.28                    | 84           |
| 17 | HINGULA OC-II EXP. PH-III (15 MTY)          | MCL    | 11/2008 | 03/2013      | 03/2019         | 479.53                    | 72           |
| 18 | RKP OCP PHASE-I                             | SCCL   | 03/2010 | 03/2015      | 03/2018         | 209.78                    | 36           |
| 19 | BALRAM OCP EXTENSION,MCL 8.00 MTY           | MCL    | 12/2007 | 03/2010      | 03/2019         | 172.08                    | 108          |
| 20 | MURAIIDIH UG TURN-KEY PROJECT               | BCCL   | 02/2011 | 04/2014      | 10/2018         | 339.88                    | 54           |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun



## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( SEPTEMBER 2017 )

| Sn | Project                                                         | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|----|-----------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 21 | MOONIDIH XV SEAM UG                                             | BCCL   | 08/2011 | 04/2015         | 04/2019            | 1230.27                         | 48              |
| 22 | NORTH URIMARI OCP (3.0 MTY)                                     | CCL    | 12/2007 | 03/2012         | 03/2019            | 179.87                          | 84              |
| 23 | TAPIN OCP (2.5 MTY)                                             | CCL    | 08/2008 | 03/2012         | 03/2019            | 264.68                          | 84              |
| 24 | KARMA OCP (1.0MTY)                                              | CCL    | 06/2009 | 03/2014         | 03/2019            | 162.46                          | 60              |
| 25 | SHANTIKHANI LONGWALL PROJ-SCCL                                  | SCCL   | 10/2006 | 03/2012         | 03/2019            | 249.03                          | 84              |
| 26 | RAJMAHAL OC EXP.                                                | ECL    | 09/2009 | 03/2014         | 12/2017            | 153.82                          | 45              |
| 27 | KISTARAM OCP                                                    | SCCL   | 11/2010 | 03/2015         | 03/2020            | 242.29                          | 60              |
| 28 | KARTALI (EAST) OCP (2.50 MTY)                                   | SECL   | 07/2008 | 03/2014         | 03/2020            | 178.44                          | 72              |
| 29 | AMLAI OC EXPANSION SECTOR B (1.50 MTY)                          | SECL   | 11/2009 | 03/2016         | 03/2018            | 198.59                          | 24              |
| 30 | MANUGURU OC-II EXTENSION PHASE-II                               | SCCL   | 03/2010 | 03/2012         | 03/2018            | 181.19                          | 72              |
| 31 | KOYAGUDEM OPENCAST PROJECT                                      | SCCL   | 10/2015 | 03/2018         | 03/2019            | 426.79                          | 12              |
| 32 | JAGANNATHPOR OCP(3.00MTY)                                       | SECL   | 09/2008 | 03/2015         | 03/2020            | 152.43                          | 60              |
| 33 | MAGADH OC 20 MTY (CCL)                                          | CCL    | 08/2008 | 07/2012         | 03/2021            | 706.4                           | 104             |
| 34 | NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI         | NCL    | 10/2007 | 03/2012         | 03/2018            | 259.4                           | 72              |
| 35 | RAMAGUNDAM OC-II EXTENSION                                      | SCCL   | 12/2009 | 03/2012         | 03/2023            | 418.97                          | 132             |
| 36 | CHURI BENTI UG (0.81 MTY)                                       | CCL    | 08/2007 | 03/2011         | 03/2020            | 163.51                          | 108             |
| 37 | PURNADIH OCP (3.0 MTY)                                          | CCL    | 07/2008 | 03/2013         | 03/2018            | 210.98                          | 60              |
| 38 | EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) | NLC    | 04/2013 | 06/2015         | 09/2019            | 1458.17                         | 51              |
| 39 | SONEPUR BAZARI (COMB) OCP (8.0 MTY)                             | ECL    | 08/2012 | 03/2018         | 09/2018            | 1055.05                         | 6               |
| 40 | MADHUBAND NLW WASHERY                                           | BCCL   | 08/2010 | 05/2014         | 04/2018            | 289.45                          | 47              |
| 41 | PATHERDIH NLW WASHERY                                           | BCCL   | 10/2012 | 04/2014         | 04/2018            | 269.82                          | 48              |
| 42 | KULDA OCP (MAHANADI COALFIELDS LTD)                             | MCL    | 01/2005 | 03/2010         | 03/2018            | 302.96                          | 96              |
| 43 | RAJRAPPA RCE OCP ( 3.0 MTY)                                     | CCL    | 12/2009 | 03/2016         | 03/2018            | 510.85                          | 24              |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( SEPTEMBER 2017 )

| Sn | Project | Agency | DOA | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|----|---------|--------|-----|--------------|-----------------|---------------------------|--------------|
|    |         |        |     |              |                 |                           |              |

## FERTILISERS

| Sn | Project                                         | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|----|-------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 44 | NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY | RCF    | 10/2014 | 11/2016      | 04/2019         | 197.79                    | 29           |

## HEALTH AND FAMILY WELFARE

| Sn | Project                                        | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|----|------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 45 | NEIGRIHMS SHILLONG MEGHALYA                    | HSCC   | 10/2016 | 05/2018      | 08/2019         | 363.99                    | 15           |
| 46 | SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB | HSCC   | 07/2016 | 02/2018      | 08/2018         | 152.95                    | 6            |
| 47 | CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR | HSCC   | 12/2014 | 05/2017      | 12/2017         | 168.9                     | 7            |
| 48 | AIIMS - OPD(NEW)                               | HSCC   | 08/2014 | 05/2017      | 12/2017         | 293.65                    | 7            |
| 49 | AIIMS - MOTHER AND CHILD BLOCK                 | HSCC   | 12/2013 | 05/2017      | 12/2017         | 204.44                    | 7            |

## HEAVY INDUSTRY

| Sn | Project                                                            | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|----|--------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 50 | NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) | NATIS  | 04/2011 | 09/2011      | 12/2017         | 1718                      | 75           |

## PETROLEUM

| Sn | Project                                                                                           | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|----|---------------------------------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 51 | SONAMURA GGS AND PIPELINE PROJECT ( PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A | ONGC   | 05/2016 | 06/2017      | 01/2018         | 215.38                    | 7            |
| 52 | FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY                                  | IOCL   | 02/2016 | 07/2017      | 02/2018         | 931                       | 7            |
| 53 | URAN CHAKAN SHIKRAPUR LPG PIPELINE                                                                | HPCL   | 12/2009 | 10/2014      | 03/2018         | 309.81                    | 41           |
| 54 | PARADIP LPG IMPORT FACILITY                                                                       | IOCL   | 01/2015 | 07/2018      | 06/2020         | 690                       | 23           |
| 55 | NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY                               | CPCL   | 05/2015 | 11/2016      | 02/2018         | 257.87                    | 15           |
| 56 | PETCOKE EVACUATION PROJECT AT PARADIP REFINERY                                                    | IOCL   | 03/2014 | 03/2017      | 10/2017         | 238.5                     | 7            |
| 57 | PIPELINE REPLACEMENT PROJECT -4                                                                   | ONGC   | 02/2015 | 05/2017      | 05/2018         | 2899.93                   | 12           |
| 58 | NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY                               | ONGC   | 08/2015 | 03/2019      | 05/2020         | 2818.88                   | 14           |
| 59 | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)                            | ONGC   | 06/2010 | 01/2014      | 11/2019         | 202.94                    | 70           |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( SEPTEMBER 2017 )

| Sn | Project                                                                                         | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|----|-------------------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 60 | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)                         | ONGC   | 03/2011 | 05/2013         | 12/2017            | 861.79                          | 55              |
| 61 | INTEGRATED DEVELOPMENT OF B-127 FIELDS                                                          | ONGC   | 12/2011 | 03/2015         | 03/2018            | 2059.63                         | 36              |
| 62 | DEVELOPMENT OF C-26 CLUSTER FIELDS                                                              | ONGC   | 03/2012 | 05/2014         | 05/2018            | 2592.17                         | 48              |
| 63 | DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD                                              | ONGC   | 04/2012 | 12/2014         | 03/2018            | 600.17                          | 39              |
| 64 | ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA | ONGC   | 01/2015 | 12/2017         | 03/2019            | 4619.94                         | 15              |
| 65 | SIX PIPELINE REPLACEMENT PROJECT                                                                | ONGC   | 03/2009 | 01/2017         | 03/2018            | 181.02                          | 14              |
| 66 | DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY                                                    | CPCL   | 02/2016 | 04/2017         | 11/2017            | 367.11                          | 7               |
| 67 | KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II                                           | GAIL   | 06/2009 | 12/2012         | 02/2019            | 2915                            | 74              |
| 68 | ASSAM RENEWAL PROJECT FOR GROUP A                                                               | ONGC   | 03/2009 | 03/2013         | 09/2018            | 2465.15                         | 66              |
| 69 | SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN          | OIL    | 07/2011 | 03/2017         | 11/2018            | 352.56                          | 20              |
| 70 | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR                                                    | ISPRL  | 01/2006 | 01/2012         | 10/2017            | 993                             | 69              |
| 71 | LPG TERMINAL AT KOCHI                                                                           | IOCL   | 10/2015 | 10/2017         | 03/2019            | 607.06                          | 17              |
| 72 | INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS                                               | ONGC   | 05/2013 | 04/2016         | 12/2017            | 4124.35                         | 20              |
| 73 | DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY                                 | IOCL   | 03/2014 | 09/2017         | 06/2018            | 3076                            | 9               |
| 74 | POLYPROPYLENE PLANT AT PARADIP REFINERY                                                         | IOCL   | 03/2014 | 09/2017         | 12/2018            | 3150                            | 15              |
| 75 | RESID UPGRADATION PROJECT                                                                       | CPCL   | 03/2013 | 11/2015         | 10/2017            | 3110.36                         | 23              |
| 76 | MH NORTH REDEVELOPMENT PHASE III                                                                | ONGC   | 06/2014 | 05/2017         | 05/2018            | 5706.47                         | 12              |
| 77 | TWENTY NOS. FEEDER GAS LINES                                                                    | OIL    | 03/2009 | 12/2016         | 03/2018            | 228.64                          | 15              |
| 78 | PIPELINE REPLACEMENT PROJECT, AHMEDABAD                                                         | ONGC   | 09/2011 | 07/2016         | 06/2018            | 202.25                          | 23              |
| 79 | CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)                                                 | ONGC   | 06/2007 | 09/2011         | 06/2019            | 736.65                          | 93              |
| 80 | UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE          | OIL    | 09/2012 | 03/2015         | 11/2017            | 871.35                          | 32              |
| 81 | PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY                             | BPCL   | 11/2014 | 08/2018         | 05/2019            | 4588.29                         | 9               |
| 82 | RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT)                       | IOCL   | 06/2012 | 07/2014         | 09/2017            | 150                             | 38              |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( SEPTEMBER 2017 )

| Sn | Project                            | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|----|------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 83 | NEW 250 TMTA LPG PLANT AT PANAGARH | HPCL   | 08/2014 | 09/2017         | 03/2018            | 190.45                          | 6               |

## POWER

| Sn  | Project                                                                                              | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|-----|------------------------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 84  | NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES                   | PGCIL  | 12/2014 | 12/2018         | 12/2019            | 5111.33                         | 12              |
| 85  | COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P        | PGCIL  | 12/2014 | 12/2018         | 12/2019            | 4754.42                         | 12              |
| 86  | TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT          | PGCIL  | 01/2014 | 09/2017         | 09/2018            | 1788.41                         | 12              |
| 87  | TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR | PGCIL  | 03/2016 | 01/2018         | 03/2019            | 808.63                          | 14              |
| 88  | KAMENG HYDROELECTRIC PROJECT (NEEPCO)                                                                | NEEPCO | 12/2004 | 12/2009         | 03/2018            | 2496.9                          | 99              |
| 89  | COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L | PGCIL  | 09/2011 | 09/2014         | 12/2017            | 1940.13                         | 39              |
| 90  | TEHRI PUMPED STORAGE PLANT(1000MW)                                                                   | THDCIL | 07/2006 | 02/2016         | 12/2020            | 1657                            | 58              |
| 91  | SYSTEM STRENGTHENING XIII OF SR GRID                                                                 | PGCIL  | 10/2011 | 06/2014         | 06/2018            | 487.49                          | 48              |
| 92  | PARE HYDRO ELECTRIC PROJECT                                                                          | NEEPCO | 12/2008 | 08/2013         | 03/2018            | 573.99                          | 55              |
| 93  | SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV                                                        | PGCIL  | 12/2011 | 08/2014         | 12/2017            | 297.33                          | 40              |
| 94  | SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH                    | PGCIL  | 12/2011 | 08/2014         | 12/2017            | 1746.65                         | 40              |
| 95  | KISHANGANGA HEP (3X110 MW)                                                                           | NHPC   | 01/2009 | 01/2016         | 02/2018            | 3642.04                         | 25              |
| 96  | KUNADANKULAM APP TRANS SYSTEM (PGCIL)                                                                | PGCIL  | 05/2005 | 11/2008         | 09/2018            | 1779.29                         | 118             |
| 97  | BARH STPP(3X660MW) NTPC                                                                              | NTPC   | 02/2005 | 01/2011         | 03/2019            | 8692.97                         | 98              |
| 98  | TUIRIAL HYDRO ELECTRIC PROJECT (60MW)                                                                | NEEPCO | 07/1998 | 07/2006         | 11/2017            | 368.72                          | 136             |
| 99  | ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION                                 | PGCIL  | 03/2012 | 09/2014         | 01/2018            | 198.63                          | 40              |
| 100 | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV                                                     | PGCIL  | 11/2011 | 11/2014         | 12/2017            | 723.63                          | 37              |
| 101 | KUDGI STPP STAGE 1                                                                                   | NTPC   | 01/2012 | 01/2017         | 11/2017            | 15166.19                        | 10              |
| 102 | TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A                   | PGCIL  | 03/2015 | 12/2015         | 03/2018            | 955                             | 27              |
| 103 | TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM CUDDALORE AREA - PACKAGE A                  | PGCIL  | 03/2015 | 12/2015         | 03/2018            | 955                             | 27              |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( SEPTEMBER 2017 )

| Sn  | Project                                                                                             | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|-----|-----------------------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 104 | NPGCPL-NABINAGAR STPP - JV (3X660 MW)                                                               | NTPC   | 01/2013 | 01/2018         | 12/2018            | 12964.6                         | 11              |
| 105 | MUNPL-MEJA TPP - JV (2X660 MW)                                                                      | NTPC   | 04/2012 | 12/2016         | 06/2018            | 9750.89                         | 18              |
| 106 | PARBATI HEP (4X200 MW) (NHPC) II                                                                    | NHPC   | 09/2002 | 09/2009         | 12/2018            | 3919.59                         | 111             |
| 107 | WESTERN REGION STRENGTHENING SCHEME-V                                                               | PGCIL  | 12/2007 | 09/2010         | 03/2018            | 477.69                          | 90              |
| 108 | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT                                          | PGCIL  | 10/2008 | 10/2012         | 02/2018            | 4824.12                         | 64              |
| 109 | TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.                                        | PGCIL  | 02/2010 | 12/2012         | 02/2018            | 2144                            | 62              |
| 110 | EASTERN REGION STRENGTHENING SCHEME-V                                                               | PGCIL  | 10/2013 | 04/2016         | 03/2018            | 1364.52                         | 23              |
| 111 | UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I                                                 | PGCIL  | 01/2014 | 04/2016         | 12/2017            | 374.63                          | 20              |
| 112 | NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX                                                   | PGCIL  | 02/2014 | 06/2016         | 02/2018            | 539.82                          | 20              |
| 113 | NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII                                                 | PGCIL  | 02/2014 | 06/2016         | 11/2017            | 908.08                          | 17              |
| 114 | STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION                                                   | PGCIL  | 05/2014 | 08/2016         | 12/2017            | 829.98                          | 16              |
| 115 | TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)                                  | PGCIL  | 01/2015 | 10/2017         | 06/2018            | 871.62                          | 8               |
| 116 | EASTERN REGION STRENGTHENING SCHEME-III                                                             | PGCIL  | 07/2010 | 11/2012         | 12/2017            | 1272.8                          | 61              |
| 117 | INSTALLATION OF STATCOMS IN WESTERN REGION                                                          | PGCIL  | 03/2015 | 09/2017         | 04/2018            | 1071.24                         | 7               |
| 118 | TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER | PGCIL  | 04/2010 | 01/2015         | 03/2018            | 4404.57                         | 38              |
| 119 | GADARWARA SUPER THERMAL POWER PROJECT STAGE-I                                                       | NTPC   | 03/2013 | 09/2017         | 03/2018            | 11638.55                        | 6               |
| 120 | NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT                                                  | PGCIL  | 02/2009 | 08/2013         | 12/2017            | 11130.19                        | 52              |
| 121 | SYSTEM STRENGTHENING XII OF SR                                                                      | PGCIL  | 02/2010 | 06/2012         | 12/2017            | 232.34                          | 66              |
| 122 | CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)                 | PGCIL  | 03/2015 | 05/2017         | 06/2019            | 1394.52                         | 25              |
| 123 | DHUKWAN SMALL HYDRO PROJECT                                                                         | THDCIL | 05/2011 | 02/2014         | 12/2018            | 195.42                          | 58              |
| 124 | BRBCL-NABINAGAR TPP- JV (4X250 MW)                                                                  | NTPC   | 01/2007 | 05/2014         | 06/2018            | 5353                            | 49              |
| 125 | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT                                    | SJVN   | 05/2015 | 12/2016         | 12/2017            | 436.68                          | 12              |
| 126 | GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A                              | PGCIL  | 04/2015 | 04/2017         | 03/2018            | 1479.3                          | 11              |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( SEPTEMBER 2017 )

| Sn  | Project                                                                                           | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|-----|---------------------------------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 127 | TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B                                         | PGCIL  | 07/2015 | 11/2017      | 06/2018         | 307.18                    | 7            |
| 128 | VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT                                                        | THDCIL | 08/2008 | 06/2013      | 11/2020         | 2491.58                   | 89           |
| 129 | EASTERN REGION STRENGTHENING SCHEME- XII                                                          | PGCIL  | 05/2014 | 11/2016      | 03/2018         | 522.29                    | 16           |
| 130 | AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B                                          | PGCIL  | 03/2014 | 03/2016      | 12/2017         | 155.57                    | 21           |
| 131 | TAPOVAN-VISHNUGAD HEP (4X130MW)                                                                   | NTPC   | 11/2006 | 03/2013      | 06/2019         | 2978.48                   | 75           |
| 132 | BONGAIGAON THERMAL POWER PROJECT                                                                  | NTPC   | 01/2008 | 09/2011      | 12/2017         | 4375.35                   | 75           |
| 133 | SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID                                               | PGCIL  | 08/2014 | 02/2017      | 03/2018         | 288.49                    | 13           |
| 134 | EASTERN REGION STRENGTHENING SCHEME - IX                                                          | PGCIL  | 02/2014 | 02/2016      | 12/2017         | 196.58                    | 22           |
| 135 | PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)                                                        | CVPPPL | 10/2014 | 04/2020      | 05/2023         | 8112.12                   | 37           |
| 136 | NORTH KARANPURA STPP (3X660 MW)                                                                   | NTPC   | 02/2014 | 02/2019      | 02/2021         | 14366.58                  | 24           |
| 137 | SOLAPUR STPP                                                                                      | NTPC   | 03/2012 | 11/2016      | 04/2018         | 9395.18                   | 17           |
| 138 | LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)                                             | NTPC   | 12/2012 | 06/2017      | 04/2018         | 11846                     | 10           |
| 139 | COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C | PGCIL  | 03/2013 | 06/2015      | 03/2018         | 514.2                     | 33           |
| 140 | COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B | PGCIL  | 03/2013 | 12/2015      | 03/2018         | 2514.88                   | 27           |
| 141 | TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW)                                            | PGCIL  | 01/2016 | 03/2017      | 11/2017         | 305.04                    | 8            |

## RAILWAYS

| Sn  | Project                                   | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|-----|-------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 142 | KARAILA ROAD - SHAKTINAGAR DOUBLING       | ECR    | 08/2015 | 03/2018      | 03/2019         | 528.57                    | 12           |
| 143 | KORAPUT - SINGAPUR ROAD DOUBLING          | ECOR   | 04/2015 | 03/2021      | 03/2022         | 2361.74                   | 12           |
| 144 | KOTTAVALSA - KORAPUT DOUBLING             | ECOR   | 04/2015 | 03/2021      | 03/2022         | 2499.71                   | 12           |
| 145 | SUKINDA ROAD - ANGUL (NL)(ECOR)           | RVNL   | 04/1998 | 02/2015      | 12/2019         | 183.23                    | 58           |
| 146 | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) | RVNL   | 04/2000 | 03/2009      | 12/2017         | 133.41                    | 105          |
| 147 | GOELKERA-MANOHARPUR, (LD)(SER)            | RVNL   | 03/1997 | 02/2006      | 12/2019         | 261.7                     | 166          |
| 148 | BHOPAL BINA 3D LINE DOUBLING              | RVNL   | 09/2007 | 03/2010      | 03/2018         | 687.2                     | 96           |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( SEPTEMBER 2017 )

| Sn  | Project                                                                                      | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|-----|----------------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 149 | BHAIRABI SAIRONG, NL, NEFR                                                                   | NFR    | 04/2008 | 04/2014         | 03/2020            | 619.34                          | 71              |
| 150 | OBULAVARIPALLE-KRISHNAPATNAM(RVNL)                                                           | RVNL   | 07/2006 | 03/2008         | 03/2020            | 743                             | 144             |
| 151 | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.             | RVNL   | 04/2010 | 03/2016         | 12/2018            | 2913.51                         | 33              |
| 152 | JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR)                            | NWR    | 04/2008 | 03/2014         | 06/2019            | 653.19                          | 63              |
| 153 | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)                                            | M RTP  | 03/1996 | 03/2004         | 03/2020            | 495.44                          | 192             |
| 154 | MANDARHILL-DUMKA-RAMPURHAT (NL),ER                                                           | ER     | 04/1995 | 12/2011         | 03/2020            | 900.05                          | 99              |
| 155 | BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR                                                 | NFR    | 09/1997 | 04/2008         | 06/2018            | 1500                            | 122             |
| 156 | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR                                                          | NR     | 03/1995 | 11/2002         | 12/2018            | 2500                            | 193             |
| 157 | SALKA ROAD -ANUPNAGAR LINE DOUBLING                                                          | RVNL   | 09/2006 | 03/2010         | 12/2017            | 324.9                           | 93              |
| 158 | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) | RVNL   | 04/2010 | 03/2016         | 12/2020            | 3951.98                         | 57              |
| 159 | NANDYAL-YERRAGUNTALA(NL),SCR                                                                 | SCR    | 03/1996 | 02/2009         | 12/2017            | 155.74                          | 106             |
| 160 | GONDIA-JABALPUR(GC),(SECR)                                                                   | SECR   | 02/1997 | 03/1998         | 12/2019            | 386.3                           | 261             |
| 161 | UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR)                                            | WR     | 04/2008 | 03/2014         | 12/2017            | 1389.62                         | 45              |
| 162 | BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)                                     | WR     | 04/2008 | 03/2012         | 03/2019            | 318.24                          | 84              |
| 163 | AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)                                                           | WR     | 04/2008 | 03/2013         | 03/2020            | 394.14                          | 84              |
| 164 | HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)                                                 | NWR    | 04/2008 | 03/2015         | 12/2019            | 829.74                          | 57              |
| 165 | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)                                                       | WCR    | 09/1998 | 05/2008         | 03/2023            | 247.66                          | 178             |
| 166 | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR                                       | NFR    | 04/2000 | 12/2008         | 03/2019            | 733                             | 123             |
| 167 | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)                                                          | NFR    | 04/2003 | 03/2011         | 03/2020            | 727.56                          | 108             |
| 168 | EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP                                         | M RTP  | 04/2006 | 06/2013         | 03/2018            | 495.74                          | 57              |
| 169 | NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)                               | NFR    | 04/2006 | 03/2015         | 03/2020            | 850                             | 60              |
| 170 | MUMBAI URBAN TRANSPORT PROJECT PHASE-II                                                      | M RTP  | 04/2008 | 03/2014         | 03/2019            | 5300                            | 60              |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( SEPTEMBER 2017 )

| Sn  | Project                                                                                        | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|-----|------------------------------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 171 | LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT                         | NFR    | 04/1996 | 03/2009      | 03/2018         | 1676.31                   | 108          |
| 172 | AGARTALA SABROOM, NL, NEFR                                                                     | NFR    | 04/2008 | 03/2014      | 03/2020         | 813.34                    | 72           |
| 173 | SEVOK RANGPO, NEFR                                                                             | NFR    | 04/2008 | 12/2015      | 03/2020         | 1339.48                   | 51           |
| 174 | DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR | NCR    | 04/2010 | 02/2019      | 12/2022         | 622.41                    | 46           |
| 175 | EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE                                       | M RTP  | 03/2013 | 03/2016      | 06/2018         | 4874.58                   | 27           |
| 176 | GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)                                                 | NCR    | 04/2011 | 02/2020      | 12/2022         | 1176.09                   | 34           |
| 177 | MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD                                          | RVNL   | 04/2012 | 03/2016      | 12/2018         | 632.68                    | 33           |

## ROAD TRANSPORT AND HIGHWAYS

| Sn  | Project                                                                                              | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|-----|------------------------------------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 178 | FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 | NHIDCL | 03/2016 | 08/2016      | 08/2019         | 429.52                    | 36           |
| 179 | FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS                  | NHAI   | 04/2010 | 06/2012      | 03/2018         | 1170.52                   | 69           |
| 180 | FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA  | NHAI   | 06/2015 | 03/2016      | 03/2019         | 1012.9                    | 36           |
| 181 | 4-LANING OF GHAGHRA BRIDGE TO VARANSI ( PACKAGE -I)                                                  | NHAI   | 12/2015 | 06/2016      | 06/2018         | 611.65                    | 24           |
| 182 | HARIDWAR DEHRADUN APPROVED LENGTH 69                                                                 | NHAI   | 11/2011 | 10/2013      | 12/2017         | 478.51                    | 50           |
| 183 | JALANDHAR - AMRITSAR                                                                                 | NHAI   | 01/2014 | 01/2016      | 12/2017         | 523.85                    | 23           |
| 184 | TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR                                                       | NHAI   | 06/2015 | 12/2017      | 06/2018         | 563.92                    | 6            |
| 185 | FOUR LANING OF VARANASI BYPASS                                                                       | NHAI   | 05/2015 | 05/2017      | 06/2018         | 261.09                    | 13           |
| 186 | 2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232                                 | NHAI   | 04/2014 | 01/2016      | 11/2017         | 351.34                    | 22           |
| 187 | 2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125                                | NHAI   | 09/2015 | 09/2016      | 09/2017         | 368.73                    | 12           |
| 188 | 2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI                                                    | NHAI   | 04/2014 | 01/2016      | 11/2017         | 495.78                    | 22           |
| 189 | THANJAVUR - PUDUKOTTAI SECTION OF NH-226                                                             | NHAI   | 11/2014 | 11/2016      | 06/2018         | 563.92                    | 19           |
| 190 | 2 LANING WITH PS OF GULABPURA - UNIARA                                                               | NHAI   | 10/2015 | 10/2017      | 04/2018         | 597                       | 6            |
| 191 | 4 LANING OF AMBALA - KAITHAL - PACKAGE -1                                                            | NHAI   | 12/2015 | 06/2016      | 06/2018         | 602.95                    | 24           |
| 192 | BAREILY-SITAPUR (NH-24)                                                                              | NHAI   | 03/2011 | 09/2013      | 10/2017         | 1046                      | 49           |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun



## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( SEPTEMBER 2017 )

| Sn  | Project                                                                                              | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|-----|------------------------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 193 | MUZAFFARNAGAR-HARIDWAR                                                                               | NHAI   | 09/2011 | 03/2013         | 11/2017            | 754                             | 56              |
| 194 | 4-LANING OF FARAKA-RAIGANJ                                                                           | NHAI   | 02/2011 | 08/2013         | 12/2017            | 1078.84                         | 52              |
| 195 | 4-LANING OF BRAHAMPORE-FARAKA                                                                        | NHAI   | 02/2011 | 08/2013         | 03/2018            | 998.79                          | 55              |
| 196 | 6-LANING OF DHANKUNI-KHARAGPUR SECTION                                                               | NHAI   | 04/2012 | 09/2014         | 12/2017            | 1396.18                         | 39              |
| 197 | 2-LANING WITH PS RAIBAREILI TO ALLAHABAD                                                             | NHAI   | 07/2012 | 01/2014         | 12/2017            | 291.36                          | 47              |
| 198 | ETAWAH CHAKERI                                                                                       | NHAI   | 03/2013 | 09/2015         | 10/2017            | 1573                            | 25              |
| 199 | DELHI AGRA APPROVED LENGTH 180.0 KM                                                                  | NHAI   | 10/2012 | 04/2015         | 12/2017            | 1928.22                         | 32              |
| 200 | 4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211                                                        | NHAI   | 01/2015 | 07/2017         | 01/2018            | 972.5                           | 6               |
| 201 | RANCHI-RARGA-JAMSETHPUR                                                                              | NHAI   | 12/2012 | 06/2015         | 12/2017            | 1479                            | 30              |
| 202 | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)                                                          | NHAI   | 05/2009 | 11/2011         | 03/2018            | 1108                            | 76              |
| 203 | DEOLI KOTA                                                                                           | NHAI   | 01/2011 | 07/2013         | 10/2017            | 593                             | 51              |
| 204 | WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50                                      | NHAI   | 05/2013 | 02/2014         | 03/2018            | 1348.2                          | 49              |
| 205 | SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM                                          | NHAI   | 02/2010 | 08/2012         | 12/2017            | 617                             | 64              |
| 206 | MURADABAD-BAREILY                                                                                    | NHAI   | 04/2010 | 06/2013         | 09/2017            | 1267                            | 51              |
| 207 | PUNE-SATARA(NH-4)                                                                                    | NHAI   | 10/2010 | 03/2013         | 12/2017            | 1724.55                         | 57              |
| 208 | CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM                                                       | NHAI   | 11/2010 | 05/2013         | 12/2017            | 1585                            | 55              |
| 209 | FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)                                    | NHAI   | 11/2013 | 11/2016         | 02/2018            | 1916.79                         | 15              |
| 210 | REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES  | PWD    | 03/2015 | 10/2015         | 10/2017            | 271.45                          | 24              |
| 211 | STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP | MORTH  | 03/2015 | 11/2015         | 11/2017            | 165.67                          | 24              |
| 212 | STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU | MORTH  | 03/2015 | 11/2015         | 11/2017            | 159.12                          | 24              |
| 213 | WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA | PWD    | 12/2011 | 08/2015         | 03/2018            | 191.08                          | 31              |
| 214 | BARSAT-KRISHNANAGAR                                                                                  | NHAI   | 08/2012 | 02/2015         | 12/2017            | 867                             | 34              |
| 215 | 4 LANING OF NAGPUR-BETUL                                                                             | NHAI   | 02/2011 | 08/2014         | 12/2017            | 2498.76                         | 40              |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( SEPTEMBER 2017 )

| Sn  | Project                                                                                              | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|-----|------------------------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 216 | QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00                                                             | NHAI   | 07/2010 | 07/2015         | 03/2019            | 1987                            | 44              |
| 217 | JAMMU-UDHAMPUR KM.27.5 TO KM.67.00                                                                   | NHAI   | 07/2010 | 07/2013         | 11/2017            | 1813.76                         | 52              |
| 218 | PATNA-MUZZAFFARPUR                                                                                   | NHAI   | 08/2010 | 02/2013         | 06/2018            | 671.3                           | 64              |
| 219 | FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH | NHAI   | 03/2016 | 07/2016         | 07/2018            | 641.17                          | 24              |
| 220 | 2 LANNING OF MOKAMA-MUNGER                                                                           | NHAI   | 05/2011 | 05/2013         | 10/2017            | 351.54                          | 53              |
| 221 | TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS                                                   | NHAI   | 05/2010 | 05/2013         | 12/2017            | 374                             | 55              |
| 222 | 2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI                                                       | NHAI   | 09/2011 | 08/2013         | 12/2017            | 485                             | 52              |
| 223 | JORBAT - BARAPANI                                                                                    | NHAI   | 01/2011 | 01/2014         | 03/2018            | 536                             | 50              |
| 224 | 4-LANNING OF CHAPRA-HAJIPUR                                                                          | NHAI   | 01/2011 | 07/2013         | 03/2018            | 575                             | 56              |
| 225 | 2 LANNING OF MUZAFFARPUR - SONBARSA                                                                  | NHAI   | 05/2011 | 11/2013         | 12/2017            | 511.54                          | 49              |
| 226 | SRINAGAR TO BANIHAL                                                                                  | NHAI   | 06/2011 | 06/2014         | 12/2017            | 1100.7                          | 42              |
| 227 | KRISHNANAGAR-BERHAMPUR                                                                               | NHAI   | 02/2012 | 07/2014         | 03/2018            | 702.16                          | 44              |
| 228 | 4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9                                                | NHAI   | 04/2014 | 09/2016         | 03/2018            | 1266.6                          | 18              |
| 229 | GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION                                                  | NHAI   | 03/2010 | 09/2012         | 12/2017            | 1509.1                          | 63              |
| 230 | INDORE-JHABUA-GUJRAT/MP                                                                              | NHAI   | 10/2010 | 04/2013         | 09/2017            | 1175                            | 53              |
| 231 | SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502                                                            | NHAI   | 02/2009 | 08/2011         | 09/2017            | 1693.75                         | 73              |
| 232 | SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46                              | NHAI   | 09/2011 | 12/2013         | 12/2017            | 1250                            | 48              |
| 233 | TIRUPATI - TIRUTHANI - CHENNAI                                                                       | NHAI   | 04/2011 | 10/2013         | 12/2017            | 571                             | 50              |
| 234 | VARANASI-AURANGABAD KM.786 TO KM.978.40                                                              | NHAI   | 09/2011 | 03/2014         | 04/2018            | 2848                            | 49              |
| 235 | PATNA-BAKTZARPUR KM.181.3 TO KM.231.95                                                               | NHAI   | 09/2011 | 03/2014         | 09/2017            | 574                             | 42              |
| 236 | 4-LANING OF SOLAPUR - MAHARASHTRA/KARNATKA SECTION                                                   | NHAI   | 06/2014 | 11/2016         | 11/2017            | 923.04                          | 12              |
| 237 | 4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION                                                    | NHAI   | 05/2014 | 08/2016         | 03/2018            | 1655.01                         | 19              |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( SEPTEMBER 2017 )

| Sn  | Project                                                                                              | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|-----|------------------------------------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 238 | GURGAON - KOTPUTLI - JAIPUR (SIX LANE)                                                               | NHAI   | 02/2008 | 10/2011      | 12/2017         | 1673.7                    | 74           |
| 239 | FOUR LANING OF GWALIOR-SHIVPURI                                                                      | NHAI   | 05/2013 | 11/2015      | 09/2017         | 1055                      | 22           |
| 240 | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700                                               | NHAI   | 12/2003 | 02/2009      | 12/2017         | 280                       | 106          |
| 241 | BRAHMPUTRA BRIDGE, NH NO-31                                                                          | NHAI   | 12/2003 | 04/2010      | 03/2018         | 217.61                    | 95           |
| 242 | NALBARI T BIJNI (AS-7)                                                                               | NHAI   | 12/2003 | 04/2008      | 12/2017         | 208                       | 116          |
| 243 | NALBARI TO BIJNI (AS-6)                                                                              | NHAI   | 12/2003 | 06/2008      | 09/2017         | 225                       | 111          |
| 244 | PANVEL-INDAPUR                                                                                       | NHAI   | 12/2011 | 06/2014      | 03/2018         | 942.69                    | 45           |
| 245 | TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR                                                  | NHAI   | 09/2014 | 09/2016      | 09/2017         | 425.19                    | 12           |
| 246 | FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION                                            | NHAI   | 02/2013 | 08/2015      | 12/2017         | 1232                      | 28           |
| 247 | FOUR LANING OF CHANDIGARH - KHARAR                                                                   | NHAI   | 10/2015 | 12/2017      | 04/2019         | 447.29                    | 16           |
| 248 | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 | NHIDCL | 03/2016 | 08/2016      | 08/2019         | 373.07                    | 36           |
| 249 | CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120                                | NHIDCL | 12/2016 | 01/2017      | 01/2020         | 138.93                    | 36           |
| 250 | FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 | NHIDCL | 03/2016 | 08/2016      | 08/2019         | 396.52                    | 36           |

## SHIPPING AND PORTS

| Sn  | Project                                                                                              | Agency         | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|-----|------------------------------------------------------------------------------------------------------|----------------|---------|--------------|-----------------|---------------------------|--------------|
| 251 | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB | MUMBAI PORT TR | 01/2007 | 12/2010      | 12/2018         | 366.39                    | 96           |
| 252 | ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)                                         | PORT TRUST     | 10/2002 | 03/2006      | 12/2017         | 150                       | 141          |

## STEEL

| Sn  | Project                                                                                               | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|-----|-------------------------------------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 253 | COKE OVEN BATTERY-5                                                                                   | RINL   | 12/2011 | 12/2017      | 06/2018         | 2858                      | 6            |
| 254 | CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI                                       | HSCL   | 12/2007 | 12/2016      | 12/2017         | 202.61                    | 12           |
| 255 | CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCPR | HSCL   | 04/2014 | 09/2017      | 12/2018         | 151.33                    | 15           |
| 256 | CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS  | HSCL   | 05/2015 | 03/2017      | 08/2018         | 189                       | 17           |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( SEPTEMBER 2017 )

| Sn  | Project                                                                      | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|-----|------------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 257 | IRRIGATION WORK OF BAGMATI                                                   | HACL   | 10/2005 | 03/2015      | 03/2021         | 956                       | 72           |
| 258 | CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND | HACL   | 12/2007 | 06/2016      | 03/2018         | 253.92                    | 21           |
| 259 | CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII             | HACL   | 02/2014 | 12/2016      | 12/2018         | 787.29                    | 24           |
| 260 | EXPANSION OF BHILAI STEEL PLANT                                              | SAIL   | 08/2010 | 03/2013      | 10/2017         | 17265                     | 55           |
| 261 | NMDC INTEGRATED STEEL PLANT                                                  | NMDC   | 01/2010 | 05/2015      | 10/2018         | 15525                     | 41           |
| 262 | 3RD CONVERTER AND 4TH CASTER                                                 | RINL   | 07/2011 | 07/2016      | 10/2017         | 974.76                    | 15           |
| 263 | REBUILDING OF COB-7 AT BSL                                                   | SAIL   | 10/2013 | 05/2016      | 10/2017         | 245.67                    | 17           |
| 264 | INSTALLATION OF NEW HOT STRIP MILL AT RSP                                    | SAIL   | 04/2015 | 04/2018      | 02/2019         | 3127.3                    | 10           |
| 265 | NEW SINTER PLANT AT BOKARO STEEL PLANT                                       | SAIL   | 03/2015 | 10/2017      | 07/2018         | 1034.01                   | 9            |
| 266 | TURBO BLOWER - 5                                                             | RINL   | 12/2009 | 09/2016      | 10/2017         | 280                       | 13           |
| 267 | BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS                                   | RINL   | 07/2011 | 07/2015      | 10/2017         | 877.73                    | 27           |
| 268 | REVAMPING OF SINTER MACHINES - 1 AND 2                                       | RINL   | 12/2009 | 10/2016      | 03/2018         | 343                       | 17           |

## TELECOMMUNICATIONS

| Sn  | Project              | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|-----|----------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 269 | NETWORK FOR SPECTRUM | DOT    | 03/2012 | 07/2015      | 06/2019         | 13334                     | 47           |

## URBAN DEVELOPMENT

| Sn  | Project                                                                                             | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | TOR (Months) |
|-----|-----------------------------------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|--------------|
| 270 | CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA | CPWD   | 12/2008 | 12/2013      | 10/2019         | 114.26                    | 70           |
| 271 | CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AT IISER     | CPWD   | 07/2015 | 11/2015      | 12/2017         | 154                       | 25           |
| 272 | NIT ACADEMIC BUILDING AT IMPHAL MANIPUR                                                             | CPWD   | 02/2014 | 03/2015      | 11/2018         | 216.69                    | 44           |
| 273 | BANGALORE METRO RAIL PROJECT PHASE-2                                                                | BMRL   | 02/2014 | 02/2019      | 03/2020         | 26405.14                  | 13           |
| 274 | CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB                    | CPWD   | 02/2014 | 05/2017      | 02/2018         | 388                       | 9            |
| 275 | CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL                                   | CPWD   | 12/2012 | 12/2015      | 12/2017         | 188.87                    | 24           |
| 276 | STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM                                                       | CPWD   | 04/2014 | 09/2016      | 11/2017         | 332.72                    | 14           |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

( SEPTEMBER 2017 )

| Sn  | Project                                                                                            | Agency | DOA     | DOC<br>Original | DOC<br>Anticipated | Cost<br>Original<br>(Rs. crore) | TOR<br>(Months) |
|-----|----------------------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------|---------------------------------|-----------------|
| 277 | CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA                     | CPWD   | 02/2014 | 08/2016         | 03/2018            | 156.57                          | 19              |
| 278 | DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND                                    | CPWD   | 11/2012 | 11/2014         | 10/2018            | 270.83                          | 47              |
| 279 | 2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD                                           | CPWD   | 09/2012 | 03/2016         | 12/2018            | 171.86                          | 33              |
| 280 | OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA                       | CPWD   | 02/2011 | 03/2016         | 03/2018            | 241.33                          | 24              |
| 281 | UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA                                 | CPWD   | 06/2010 | 03/2012         | 03/2018            | 205                             | 72              |
| 282 | CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA                        | CPWD   | 12/2012 | 06/2015         | 09/2017            | 315                             | 27              |
| 283 | CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA                                              | CPWD   | 01/2010 | 10/2012         | 03/2018            | 165.23                          | 65              |
| 284 | CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN | CPWD   | 07/2012 | 12/2015         | 03/2018            | 884.3                           | 27              |
| 285 | KOCHI METRO RAIL PROJECT                                                                           | KMRCL  | 07/2012 | 07/2017         | 12/2019            | 5181.79                         | 29              |
| 286 | NAGPUR METRO RAIL                                                                                  | NMRCL  | 08/2014 | 03/2018         | 12/2019            | 8680                            | 21              |
| 287 | CHENNAI METRO RAIL LTD (PHASE 1)                                                                   | CMRL   | 02/2009 | 12/2015         | 12/2017            | 14600                           | 24              |

DOA -&gt; Date of Approval

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN RS. 100 CRORE

( SEPTEMBER 2017 )

**ATOMIC ENERGY**

| Sn | Project                                           | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|----|---------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 1  | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) | BHAVNI | 09/2003 | 09/2010      | 3492                     | 6000                        | 2508                    |

**CIVIL AVIATION**

| Sn | Project                                                                    | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|----|----------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 2  | CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT                     | AAI    | 01/2009 | 01/2011      | 309.46                   | 553.53                      | 244.07                  |
| 3  | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR | AAI    | 10/2013 | 09/2018      | 314.61                   | 441.33                      | 126.72                  |

**COAL**

| Sn | Project                                                  | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|----|----------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 4  | JAGANNATHPOR OCP(3.00MTY)                                | SECL   | 09/2008 | 03/2015      | 152.43                   | 459.49                      | 307.06                  |
| 5  | SHANTIKHANI LONGWALL PROJ-SCCL                           | SCCL   | 10/2006 | 03/2012      | 249.03                   | 448.86                      | 199.83                  |
| 6  | RCE OF INDARAM OCP(1.20 MTPA)                            | SCCL   | 07/2011 | 03/2015      | 162.76                   | 349.28                      | 186.52                  |
| 7  | NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI | NCL    | 10/2007 | 03/2012      | 259.4                    | 486.57                      | 227.17                  |

**HEAVY INDUSTRY**

| Sn | Project                                                             | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|----|---------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 8  | NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) | NATIS  | 04/2011 | 09/2011      | 1718                     | 3827.3                      | 2109.3                  |

**PETROLEUM**

| Sn | Project                                                                                | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|----|----------------------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 9  | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR                                           | ISPR   | 01/2006 | 01/2012      | 993                      | 1693                        | 700                     |
| 10 | LPG TERMINAL AT KOCHI                                                                  | IOCL   | 10/2015 | 10/2017      | 607.06                   | 714.25                      | 107.19                  |
| 11 | DEVELOPMENT PLAN OF CBM - BOKARO BLOCK                                                 | ONGC   | 12/2015 | 03/2023      | 658.62                   | 910.23                      | 251.61                  |
| 12 | RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT)              | IOCL   | 06/2012 | 07/2014      | 150                      | 259.93                      | 109.93                  |
| 13 | UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE | OIL    | 09/2012 | 03/2015      | 871.35                   | 1200                        | 328.65                  |
| 14 | URAN CHAKAN SHIKRAPUR LPG PIPELINE                                                     | HPCL   | 12/2009 | 10/2014      | 309.81                   | 723.4                       | 413.59                  |
| 15 | PARADIP HALDIA DURGAPUR LPG PIPELINE                                                   | IOCL   | 02/2011 | 06/2018      | 913                      | 1330                        | 417                     |
| 16 | INTEGRATED DEVELOPMENT OF B-127 FIELDS                                                 | ONGC   | 12/2011 | 03/2015      | 2059.63                  | 2665.65                     | 606.02                  |
| 17 | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)                | ONGC   | 03/2011 | 05/2013      | 861.79                   | 1256.72                     | 394.93                  |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( SEPTEMBER 2017 )

| Sn           | Project                                                                             | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|--------------|-------------------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 18           | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)              | ONGC   | 06/2010 | 01/2014      | 202.94                   | 330.35                      | 127.41                  |
| 19           | DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY                     | IOCL   | 03/2014 | 09/2017      | 3076                     | 4190                        | 1114                    |
| 20           | MH NORTH REDEVELOPMENT PHASE III                                                    | ONGC   | 06/2014 | 05/2017      | 5706.47                  | 5813.25                     | 106.78                  |
| 21           | INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS                                   | ONGC   | 05/2013 | 04/2016      | 4124.35                  | 5637                        | 1512.65                 |
| <b>POWER</b> |                                                                                     |        |         |              |                          |                             |                         |
| Sn           | Project                                                                             | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
| 22           | PARBATI HEP (4X200 MW) (NHPC) II                                                    | NHPC   | 09/2002 | 09/2009      | 3919.59                  | 8398.75                     | 4479.16                 |
| 23           | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT                          | PGCIL  | 10/2008 | 10/2012      | 4824.12                  | 5071.94                     | 247.82                  |
| 24           | SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)                                             | NHPC   | 09/2003 | 09/2010      | 6285.33                  | 18559.49                    | 12274.16                |
| 25           | WESTERN REGION STRENGTHENING SCHEME-V                                               | PGCIL  | 12/2007 | 09/2010      | 477.69                   | 738.48                      | 260.79                  |
| 26           | NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT                                  | PGCIL  | 02/2009 | 08/2013      | 11130.19                 | 13762.8                     | 2632.61                 |
| 27           | BOKARO THERMAL POWER STATION-A                                                      | DVC    | 08/2006 | 12/2011      | 2313                     | 4366.64                     | 2053.64                 |
| 28           | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT                    | SJVN   | 05/2015 | 12/2016      | 436.68                   | 602.44                      | 165.76                  |
| 29           | NPGCPL-NABINAGAR STPP - JV (3X660 MW)                                               | NTPC   | 01/2013 | 01/2018      | 12964.6                  | 13731.26                    | 766.66                  |
| 30           | BRBCL-NABINAGAR TPP- JV (4X250 MW)                                                  | NTPC   | 01/2007 | 05/2014      | 5353                     | 7998                        | 2645                    |
| 31           | EASTERN REGION STRENGTHENING SCHEME-III                                             | PGCIL  | 07/2010 | 11/2012      | 1272.8                   | 1731.1                      | 458.3                   |
| 32           | BONGAIGAON THERMAL POWER PROJECT                                                    | NTPC   | 01/2008 | 09/2011      | 4375.35                  | 6749.18                     | 2373.83                 |
| 33           | TAPOVAN-VISHNUGAD HEP (4X130MW)                                                     | NTPC   | 11/2006 | 03/2013      | 2978.48                  | 3846.3                      | 867.82                  |
| 34           | EASTERN REGION STRENGTHENING SCHEME-V                                               | PGCIL  | 10/2013 | 04/2016      | 1364.52                  | 1891.41                     | 526.89                  |
| 35           | TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.                        | PGCIL  | 02/2010 | 12/2012      | 2144                     | 2932.88                     | 788.88                  |
| 36           | TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM CUDDALORE AREA - PACKAGE A | PGCIL  | 03/2015 | 12/2015      | 955                      | 1364                        | 409                     |
| 37           | TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A  | PGCIL  | 03/2015 | 12/2015      | 955                      | 1364                        | 409                     |
| 38           | PAKRI BARWADIH COAL MINING PROJECT                                                  | NTPC   | 10/2004 | 10/2017      | 4237.96                  | 4552                        | 314.04                  |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( SEPTEMBER 2017 )

| Sn              | Project                                                                                              | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|-----------------|------------------------------------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 39              | TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT          | PGCIL  | 01/2014 | 09/2017      | 1788.41                  | 2352.57                     | 564.16                  |
| 40              | COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C    | PGCIL  | 03/2013 | 06/2015      | 514.2                    | 703.1                       | 188.9                   |
| 41              | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV                                                     | PGCIL  | 11/2011 | 11/2014      | 723.63                   | 882.13                      | 158.5                   |
| 42              | TRIPURA GAS BASED POWER PROJECT                                                                      | NEEPCO | 07/2009 | 07/2013      | 421.01                   | 1078.31                     | 657.3                   |
| 43              | TUIRIAL HYDRO ELECTRIC PROJECT (60MW)                                                                | NEEPCO | 07/1998 | 07/2006      | 368.72                   | 1329.43                     | 960.71                  |
| 44              | BARH STPP(3X660MW) NTPC                                                                              | NTPC   | 02/2005 | 01/2011      | 8692.97                  | 15095.67                    | 6402.7                  |
| 45              | KUNADANKULAM APP TRANS SYSTEM (PGCIL)                                                                | PGCIL  | 05/2005 | 11/2008      | 1779.29                  | 2187.32                     | 408.03                  |
| 46              | KISHANGANGA HEP (3X110 MW)                                                                           | NHPC   | 01/2009 | 01/2016      | 3642.04                  | 5882.01                     | 2239.97                 |
| 47              | SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH                    | PGCIL  | 12/2011 | 08/2014      | 1746.65                  | 2228.71                     | 482.06                  |
| 48              | SYTEM STRENGTHENING OF SOUTHERN REGION - XIV                                                         | PGCIL  | 12/2011 | 08/2014      | 297.33                   | 426.29                      | 128.96                  |
| 49              | PARE HYDRO ELECTRIC PROJECT                                                                          | NEEPCO | 12/2008 | 08/2013      | 573.99                   | 1337.76                     | 763.77                  |
| 50              | SYTEM STRENGTHENING XIII OF SR GRID                                                                  | PGCIL  | 10/2011 | 06/2014      | 487.49                   | 639.46                      | 151.97                  |
| 51              | TEHRI PUMPED STORAGE PLANT(1000MW)                                                                   | THDCIL | 07/2006 | 02/2016      | 1657                     | 3939.11                     | 2282.11                 |
| 52              | COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L | PGCIL  | 09/2011 | 09/2014      | 1940.13                  | 2702.65                     | 762.52                  |
| 53              | KAMENG HYDROELECTRIC PROJECT (NEEPCO)                                                                | NEEPCO | 12/2004 | 12/2009      | 2496.9                   | 6179.96                     | 3683.06                 |
| 54              | RAGHUNATHPUR THERMAL POWER STATION PHASE-I                                                           | DVC    | 04/2007 | 02/2011      | 4122                     | 9142.58                     | 5020.58                 |
| 55              | TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER  | PGCIL  | 04/2010 | 01/2015      | 4404.57                  | 5135.01                     | 730.44                  |
| <b>RAILWAYS</b> |                                                                                                      |        |         |              |                          |                             |                         |
| Sn              | Project                                                                                              | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
| 56              | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)                                                    | NCR    | 04/1986 | 03/1994      | 158.77                   | 634.48                      | 475.71                  |
| 57              | NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR                             | NFR    | 04/1983 | N.A.         | 36.8                     | 614                         | 577.2                   |
| 58              | CALICUT-MANGALORE (DL) (SR)                                                                          | SR     | 02/1996 | N.A.         | 240                      | 579.37                      | 339.37                  |
| 59              | KARUR-SALEM(NL), SR                                                                                  | SR     | 02/1997 | N.A.         | 155.55                   | 870                         | 714.45                  |
| 60              | KATIHAR - JOGBANI (GC)(NEFR)                                                                         | NFR    | 09/2001 | 12/2010      | 492.98                   | 1320                        | 827.02                  |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning



## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( SEPTEMBER 2017 )

| Sn | Project                                          | Agency | DOA     | DOC<br>Original | Cost<br>Original<br>(Rs.crore) | Cost<br>Anticipated<br>(Rs.crore) | Cost<br>Overrun<br>(Rs.crore) |
|----|--------------------------------------------------|--------|---------|-----------------|--------------------------------|-----------------------------------|-------------------------------|
| 61 | GULBARGA-BIDAR, SCR(NL)                          | SCR    | 02/1998 | N.A.            | 242.42                         | 1542.41                           | 1299.99                       |
| 62 | QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)  | SR     | 03/1998 | N.A.            | 280                            | 1122                              | 842                           |
| 63 | RAICHUR-GUNTAKAL(DL)(SCR)                        | RVNL   | 04/2003 | 12/2007         | 136.62                         | 376                               | 239.38                        |
| 64 | TALCHER-BIMALAGARH(NL)(ECOR)                     | ECOR   | 04/2005 | N.A.            | 810.78                         | 1928.07                           | 1117.29                       |
| 65 | KHURDA ROAD - BARANG 3RD LINE (DL)(ECOR)         | RVNL   | 04/2000 | 03/2009         | 133.41                         | 340                               | 206.59                        |
| 66 | SUKINDA ROAD - ANGUL (NL)(ECOR)                  | RVNL   | 04/1998 | 02/2015         | 183.23                         | 1202.7                            | 1019.47                       |
| 67 | CHHINDWARA - NAGPUR (GC)(SECR)                   | SECR   | 04/2005 | N.A.            | 383.79                         | 1101.16                           | 717.37                        |
| 68 | HATHUA-BHATNI (N L) (NER)                        | NER    | 04/2005 | N.A.            | 230.03                         | 718.54                            | 488.51                        |
| 69 | ETAWAH-MAINPURI (NL),NCR                         | NCR    | 04/1997 | 12/2008         | 120                            | 245.39                            | 125.39                        |
| 70 | MAHARAJGANJ-MASRAKH (NL) - NER                   | NER    | 04/2003 | N.A.            | 218.19                         | 412.05                            | 193.86                        |
| 71 | RAMGANJMUNDI-BHOPAL (NL),WCR                     | WCR    | 04/2001 | N.A.            | 470.92                         | 2713.09                           | 2242.17                       |
| 72 | GUDUR-DURGARAJAPATNAM                            | SCR    | 04/2011 | N.A.            | 283.54                         | 759.41                            | 475.87                        |
| 73 | KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION | SCR    | 04/2012 | N.A.            | 1054.35                        | 2200                              | 1145.65                       |
| 74 | BAGALKOT-KUDACHI NL                              | SWR    | 04/2010 | N.A.            | 377.93                         | 986.3                             | 608.37                        |
| 75 | MUNIRABAD (GINGERA) -RAICHUR NL                  | SWR    | 04/2007 | N.A.            | 179.65                         | 1350.91                           | 1171.26                       |
| 76 | TUMKUR-CHITRADURGA-DAVENGERE NL                  | SWR    | 04/2011 | N.A.            | 913                            | 1801.01                           | 888.01                        |
| 77 | PANVEL PEN DOUBLING                              | CR     | 04/2006 | N.A.            | 96.16                          | 280                               | 183.84                        |
| 78 | PEN ROHA DOUBLING                                | CR     | 04/2007 | N.A.            | 98.74                          | 381.39                            | 282.65                        |
| 79 | WARDHA-SEWAGRAM NGP 3RD LINE                     | CR     | 04/2012 | N.A.            | 297.85                         | 540.02                            | 242.17                        |
| 80 | OBULAVARIPALLE-KRISHNAPATNAM(RVNL)               | RVNL   | 07/2006 | 03/2008         | 743                            | 1825                              | 1082                          |
| 81 | BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR     | NFR    | 09/1997 | 04/2008         | 1500                           | 5000                              | 3500                          |
| 82 | MANDARHILL-DUMKA-RAMPURHAT (NL),ER               | ER     | 04/1995 | 12/2011         | 900.05                         | 1125.89                           | 225.84                        |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( SEPTEMBER 2017 )

| Sn  | Project                                                                                          | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|-----|--------------------------------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 83  | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)                                                | M RTP  | 03/1996 | 03/2004      | 495.44                   | 1781.98                     | 1286.54                 |
| 84  | AHMEDNAGAR-PARLI VAIJNATH(NL) CR                                                                 | CR     | 02/1997 | N.A.         | 514.68                   | 2271.5                      | 1756.82                 |
| 85  | MM FROM PANSKURA-GHATAL NL                                                                       | SER    | 04/2011 | 01/1999      | 276.69                   | 426                         | 149.31                  |
| 86  | MM FROM BURAMARA-CHAKULIA                                                                        | SER    | 04/2008 | 01/1999      | 466.48                   | 750                         | 283.52                  |
| 87  | JAGGAYYAPET - MELLACHERUVU                                                                       | SCR    | 04/2007 | 01/1999      | 313.24                   | 554.7                       | 241.46                  |
| 88  | GADAG-WADI NL                                                                                    | SWR    | 04/2013 | N.A.         | 1117                     | 1922                        | 805                     |
| 89  | CHANDIGARH-BADDI NL                                                                              | NR     | 04/2007 | N.A.         | 328.14                   | 1540                        | 1211.86                 |
| 90  | KANPUR KASGANJ MATHURA(GC) NER                                                                   | NER    | 03/1997 | N.A.         | 677.97                   | 1679.13                     | 1001.16                 |
| 91  | SEVOK RANGPO, NEFR                                                                               | NFR    | 04/2008 | 12/2015      | 1339.48                  | 4084.69                     | 2745.21                 |
| 92  | AGARTALA SABROOM, NL, NEFR                                                                       | NFR    | 04/2008 | 03/2014      | 813.34                   | 3451                        | 2637.66                 |
| 93  | LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT                           | NFR    | 04/1996 | 03/2009      | 1676.31                  | 7000                        | 5323.69                 |
| 94  | BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)                        | ER     | 04/1999 | 12/2012      | 207.52                   | 334.87                      | 127.35                  |
| 95  | MUMBAI URBAN TRANSPORT PROJECT PHASE-II                                                          | M RTP  | 04/2008 | 03/2014      | 5300                     | 7986.04                     | 2686.04                 |
| 96  | NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)                                   | NFR    | 04/2006 | 03/2015      | 850                      | 3000                        | 2150                    |
| 97  | NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR                                         | NFR    | 09/2006 | N.A.         | 300                      | 2145                        | 1845                    |
| 98  | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR                                  | NFR    | 09/2006 | N.A.         | 200                      | 780                         | 580                     |
| 99  | HOWRAH-AMTA-CHAMPADANGA NL (SER)                                                                 | SER    | 04/1974 | 03/2007      | 393.46                   | 1026                        | 632.54                  |
| 100 | GONDIA-JABALPUR(GC), (SECR)                                                                      | SECR   | 02/1997 | 03/1998      | 386.3                    | 1776.81                     | 1390.51                 |
| 101 | MACHERLA-NALGONDA(NL)(SCR)                                                                       | SCR    | 07/1998 | 07/2008      | 125                      | 480                         | 355                     |
| 102 | MUNEERABAD-MAHABOONNAGAR(NL), SCR                                                                | SCR    | 04/1997 | N.A.         | 218.24                   | 525                         | 306.76                  |
| 103 | NANDYAL-YERRAGUNTLA(NL), SCR                                                                     | SCR    | 03/1996 | 02/2009      | 155.74                   | 966.98                      | 811.24                  |
| 104 | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) | RVNL   | 04/2010 | 03/2014      | 2298.42                  | 2733.86                     | 435.44                  |
| 105 | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)     | RVNL   | 04/2010 | 03/2016      | 3951.98                  | 4259.48                     | 307.5                   |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( SEPTEMBER 2017 )

| Sn  | Project                                                                                           | Agency | DOA     | DOC<br>Original | Cost<br>Original<br>(Rs.crore) | Cost<br>Anticipated<br>(Rs.crore) | Cost<br>Overrun<br>(Rs.crore) |
|-----|---------------------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------------------|-----------------------------------|-------------------------------|
| 106 | SALKA ROAD -ANUPNAGAR LINE DOUBLING                                                               | RVNL   | 09/2006 | 03/2010         | 324.9                          | 516.4                             | 191.5                         |
| 107 | RAJATGARH-BARANG(LD), ECoR                                                                        | RVNL   | 04/1999 | 02/2009         | 166.16                         | 380                               | 213.84                        |
| 108 | RAJNANDGAON - NAGPUR - 3RD LINE (SECR)                                                            | SECR   | 09/2016 | 12/2021         | 1273                           | 1908                              | 635                           |
| 109 | BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL                                         | SER    | 04/1998 | 03/2003         | 1027.4                         | 2373                              | 1345.6                        |
| 110 | TRIVANDRUM-KANYAKUMARI DOUBLING                                                                   | SR     | 02/2015 | N.A.            | 900                            | 4131.9                            | 3231.9                        |
| 111 | RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO      | SER    | 04/1995 | 12/2021         | 524.43                         | 939                               | 414.57                        |
| 112 | TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI    | SER    | 01/1991 | 12/2021         | 763.18                         | 1428                              | 664.82                        |
| 113 | RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS                                                     | NFR    | 04/2003 | N.A.            | 4300                           | 4520                              | 220                           |
| 114 | MUZAFFARPUR-SITAMARHI NEW LINE                                                                    | ECR    | 01/1991 | 07/2014         | 332.15                         | 559.91                            | 227.76                        |
| 115 | MATHURA-PLWAL 4TH LINE (80KM)                                                                     | NCR    | 04/2015 | 03/2020         | 524                            | 668                               | 144                           |
| 116 | VIJAYAWADA-GUDUR                                                                                  | RVNL   | 04/2015 | N.A.            | 3246.26                        | 3548.67                           | 302.41                        |
| 117 | MANMAD - JALGAON - 3RD LINE (160 KM)                                                              | CR     | 02/2016 | N.A.            | 854                            | 1035.16                           | 181.16                        |
| 118 | DAUND - MANMAD (236 KM)                                                                           | CR     | 02/2016 | N.A.            | 1876                           | 2081.27                           | 205.27                        |
| 119 | ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)                                                          | CR     | 02/2015 | N.A.            | 2326                           | 2449.91                           | 123.91                        |
| 120 | WARDHA-BALHARSHAH - 3RD LINE (132 KM)                                                             | CR     | 02/2015 | N.A.            | 630                            | 1272.19                           | 642.19                        |
| 121 | PIRPAINTI-JASIDIH                                                                                 | ER     | 04/2013 | N.A.            | 915.98                         | 1130.13                           | 214.15                        |
| 122 | MADURAI-TUTICORIN VIA ARUPPUKKOTTAI                                                               | SR     | 04/2011 | N.A.            | 601.43                         | 1500                              | 898.57                        |
| 123 | MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD                                             | RVNL   | 04/2012 | 03/2016         | 632.68                         | 816.55                            | 183.87                        |
| 124 | LUMDING-HOJAI PATCH DOUBLING PROJECT                                                              | NFR    | 04/2012 | N.A.            | 246.07                         | 398.93                            | 152.86                        |
| 125 | AMBARI FALAKATA TO NEW MAYNAGURI                                                                  | NFR    | 04/2011 | N.A.            | 312.12                         | 508                               | 195.88                        |
| 126 | NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI | NFR    | 04/1999 | N.A.            | 523.17                         | 1871                              | 1347.83                       |
| 127 | MURKONGSELEK-PASIGHAT NL                                                                          | NFR    | 04/2011 | N.A.            | 165.82                         | 450                               | 284.18                        |
| 128 | NEW BG LINE FROM JAGBANI TO BIRATNAGAR                                                            | NFR    | 04/2010 | N.A.            | 241.52                         | 394.28                            | 152.76                        |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( SEPTEMBER 2017 )

| Sn  | Project                                                                                      | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|-----|----------------------------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 129 | NEW BG LINE FROM BALURGHAT TO HILLY NFR                                                      | NFR    | 04/2010 | N.A.         | 242.22                   | 471                         | 228.78                  |
| 130 | NEW BG LINE FROM BYRNIHAT TO SHILLONG                                                        | NFR    | 04/2010 | N.A.         | 4083.02                  | 6000                        | 1916.98                 |
| 131 | CHENGANNUR-CHINGAVANAM                                                                       | SR     | 04/2006 | N.A.         | 191.72                   | 342.85                      | 151.13                  |
| 132 | MADURAI-BODINAYAKKANUR                                                                       | SR     | 04/2008 | N.A.         | 164.41                   | 302.9                       | 138.49                  |
| 133 | ERODE-PALANI                                                                                 | SR     | 04/2008 | N.A.         | 288.57                   | 603.22                      | 314.65                  |
| 134 | NEW COOCHBEHAR TO SAMUKTALA                                                                  | NFR    | 04/2011 | N.A.         | 209.77                   | 445                         | 235.23                  |
| 135 | AGARTALA-AKHAURA NL                                                                          | NFR    | 04/2012 | N.A.         | 252                      | 580                         | 328                     |
| 136 | CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA                                                   | NFR    | 04/1999 | 03/2007      | 895                      | 1857                        | 962                     |
| 137 | NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR                                                     | NFR    | 04/2010 | N.A.         | 221.42                   | 380                         | 158.58                  |
| 138 | VILLUPURAM-DINDIGUL WITH ELECTRIFICATION                                                     | RVNL   | 04/2008 | N.A.         | 822.39                   | 1810                        | 987.61                  |
| 139 | CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC                                              | SR     | 04/1998 | N.A.         | 271.24                   | 520                         | 248.76                  |
| 140 | SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR                 | SR     | 04/2013 | N.A.         | 839                      | 1500                        | 661                     |
| 141 | HAJIPUR-RAMDAYALUNAGAR DOUBLING                                                              | ECR    | 04/2013 | N.A.         | 213.01                   | 367.17                      | 154.16                  |
| 142 | SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)                                                  | ECR    | 04/2008 | N.A.         | 678.62                   | 2393.23                     | 1714.61                 |
| 143 | MOTIHARI-SITAMARHI (NL)                                                                      | ECR    | 04/2006 | N.A.         | 211                      | 926.09                      | 715.09                  |
| 144 | SAKRI-HASANPUR ROAD (NL)                                                                     | ECOR   | 04/1999 | N.A.         | 175.69                   | 325                         | 149.31                  |
| 145 | GAYA-CHATRA (NL)                                                                             | ECOR   | 04/2008 | N.A.         | 415.67                   | 549.75                      | 134.08                  |
| 146 | MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING                                                      | SER    | 04/2012 | N.A.         | 258.2                    | 365                         | 106.8                   |
| 147 | DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING                                                      | SER    | 04/2010 | 12/2015      | 309.44                   | 583                         | 273.56                  |
| 148 | BHADUTOLA-JHARGRAM VIA LALGARH (NL)                                                          | SER    | 04/2011 | N.A.         | 289.64                   | 760                         | 470.36                  |
| 149 | DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA                                                   | SER    | 04/2010 | N.A.         | 553.63                   | 1009                        | 455.37                  |
| 150 | BOWAICHANDI-ARAMBAGH                                                                         | SER    | 04/2010 | N.A.         | 267.37                   | 434                         | 166.63                  |
| 151 | DHOLPUR-SIRMUDDA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR | NCR    | 04/2010 | 02/2019      | 622.41                   | 2030.5                      | 1408.09                 |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( SEPTEMBER 2017 )

| Sn  | Project                                                                               | Agency | DOA     | DOC<br>Original | Cost<br>Original<br>(Rs.crore) | Cost<br>Anticipated<br>(Rs.crore) | Cost<br>Overrun<br>(Rs.crore) |
|-----|---------------------------------------------------------------------------------------|--------|---------|-----------------|--------------------------------|-----------------------------------|-------------------------------|
| 152 | RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)                | NWR    | 04/2010 | N.A.            | 739.65                         | 872.22                            | 132.57                        |
| 153 | MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR                            | NWR    | 04/2013 | N.A.            | 456                            | 855.16                            | 399.16                        |
| 154 | GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)                                        | NCR    | 04/2011 | 02/2020         | 1176.09                        | 3845.6                            | 2669.51                       |
| 155 | RATLAM-DUNGARPUR VIA BANSWARA (NL)                                                    | NWR    | 04/2011 | N.A.            | 2082.75                        | 2562.27                           | 479.52                        |
| 156 | VIRAMGAM-SAMAKHIALI (DL)                                                              | WR     | 04/2011 | N.A.            | 446                            | 1037.15                           | 591.15                        |
| 157 | PALANPUR-SAMAKHAYALI (DL)                                                             | RVNL   | 04/2013 | N.A.            | 1266.89                        | 1548.66                           | 281.77                        |
| 158 | MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)                                                    | WR     | 04/2011 | N.A.            | 439.88                         | 845.68                            | 405.8                         |
| 159 | DHASA-JETALSAR (GC)                                                                   | RVNL   | 04/2012 | N.A.            | 376.59                         | 644.38                            | 267.79                        |
| 160 | AHMEDABAD-BOTAD (GC)                                                                  | RVNL   | 04/2012 | N.A.            | 567.18                         | 975.62                            | 408.44                        |
| 161 | BANGURGRAM-GURIYA PATCH DOUBLING                                                      | NWR    | 04/2012 | N.A.            | 246.08                         | 348.55                            | 102.47                        |
| 162 | CHHAPRA-BALLIA UP                                                                     | NER    | 03/2013 | N.A.            | 295                            | 477.31                            | 182.31                        |
| 163 | BHOJIPUR TANAKPUR VIA PILIBHIT                                                        | NER    | 03/2008 | N.A.            | 195.64                         | 474.3                             | 278.66                        |
| 164 | ANGAMALI-SABARIMALA (N.L.)(SR)                                                        | SR     | 10/1998 | N.A.            | 550                            | 2815.62                           | 2265.62                       |
| 165 | AMRAVATI-NARKHER NL(CR)                                                               | CR     | 06/1994 | 06/1999         | 663.01                         | 858.97                            | 195.96                        |
| 166 | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)                                                | SCR    | 12/1994 | N.A.            | 124.43                         | 1010                              | 885.57                        |
| 167 | HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)                                          | NWR    | 04/2008 | 03/2015         | 829.74                         | 1161.64                           | 331.9                         |
| 168 | THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) | RVNL   | 04/2011 | N.A.            | 190.1                          | 350                               | 159.9                         |
| 169 | KIRANDUL - JAGDALPUR DOUBLING                                                         | ECOR   | 12/2012 | N.A.            | 826.57                         | 1160.83                           | 334.26                        |
| 170 | SAMBALPUR-TALCHER DOUBLING                                                            | ECOR   | 03/2011 | N.A.            | 679.27                         | 1579.27                           | 900                           |
| 171 | TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)                                               | SR     | 09/1995 | N.A.            | 100                            | 980                               | 880                           |
| 172 | RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)             | SWR    | 04/2007 | 03/2013         | 482                            | 874.57                            | 392.57                        |
| 173 | BANGLORE - SATYAMANGALAM (NL)(SWR)                                                    | SWR    | 04/1996 | N.A.            | 138                            | 1382.78                           | 1244.78                       |
| 174 | HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR                                         | SWR    | 02/1997 | N.A.            | 295                            | 1289.92                           | 994.92                        |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( SEPTEMBER 2017 )

| Sn  | Project                                                          | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|-----|------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 175 | GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM)       | NER    | 04/1997 | N.A.         | 836.26                   | 1072.52                     | 236.26                  |
| 176 | HUBLI-ANKOLA(NL),SWR                                             | SWR    | 04/1997 | N.A.         | 227                      | 2135                        | 1908                    |
| 177 | RANCHI-LOHARDAGA(GC),SER                                         | SER    | 04/1997 | 06/2004      | 194.07                   | 491.33                      | 297.26                  |
| 178 | TAMLUK DIGHA,LINE DOUBLING (SER)                                 | SER    | 03/1984 | 06/2005      | 293.97                   | 749.69                      | 455.72                  |
| 179 | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL | RVNL   | 04/1995 | 12/2012      | 304                      | 1195                        | 891                     |
| 180 | UTRATIA-ZAFRABAD, NR (LINE DOUBLING)                             | NR     | 04/2006 | 03/2010      | 325                      | 1581.53                     | 1256.53                 |
| 181 | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR                           | NR     | 03/2002 | 06/2007      | 625.3                    | 876.1                       | 250.8                   |
| 182 | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR                              | NR     | 03/1995 | 11/2002      | 2500                     | 19565                       | 17065                   |
| 183 | NANGALDAM-TALWARA(NL),NR                                         | NR     | 03/1981 | 07/2012      | 450                      | 2100                        | 1650                    |
| 184 | SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR)   | NWR    | 04/2008 | 03/2014      | 516.23                   | 735                         | 218.77                  |
| 185 | DAUSA-GANGAPUR CITY(NL),NWR                                      | NWR    | 02/1997 | N.A.         | 410.08                   | 780.98                      | 370.9                   |
| 186 | KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)                          | NER    | 04/1999 | N.A.         | 744.71                   | 1126.79                     | 382.08                  |
| 187 | ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR               | NFR    | 12/2006 | 03/2011      | 170                      | 436                         | 266                     |
| 188 | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)                              | NFR    | 04/2003 | 03/2011      | 727.56                   | 9658                        | 8930.44                 |
| 189 | KHURDA ROAD-BOLANGIR(NL)ECOR                                     | ECOR   | 04/1994 | N.A.         | 470.21                   | 3004.9                      | 2534.69                 |
| 190 | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR           | NFR    | 04/2000 | 12/2008      | 733                      | 3010                        | 2277                    |
| 191 | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)                            | ECR    | 04/1997 | N.A.         | 162.87                   | 541                         | 378.13                  |
| 192 | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR                       | NCR    | 04/1999 | 12/2009      | 108                      | 432.72                      | 324.72                  |
| 193 | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR                        | ECR    | 04/1997 | 03/2012      | 501.69                   | 1043.56                     | 541.87                  |
| 194 | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)                           | WCR    | 09/1998 | 05/2008      | 247.66                   | 6093.31                     | 5845.65                 |
| 195 | HARIDWAR-LAKSAR                                                  | NR     | 04/2012 | N.A.         | 219.83                   | 346.63                      | 126.8                   |
| 196 | BHADRACHALAM ROAD-SATTUPALLI                                     | SCR    | 04/2010 | N.A.         | 337.49                   | 792.01                      | 454.52                  |
| 197 | RAYADURGA-TUMKUR NL                                              | RVNL   | 04/2007 | N.A.         | 970.34                   | 1714.49                     | 744.15                  |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( SEPTEMBER 2017 )

| Sn  | Project                                                                                             | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|-----|-----------------------------------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 198 | SHIMOGA-HARIHAR NL                                                                                  | SWR    | 04/2011 | N.A.         | 562.74                   | 832.47                      | 269.73                  |
| 199 | SRINIVASA-PURA-MADANAPALLI NL                                                                       | SWR    | 04/2013 | N.A.         | 296                      | 466.65                      | 170.65                  |
| 200 | CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL                                                  | SWR    | 04/2013 | N.A.         | 558                      | 692.43                      | 134.43                  |
| 201 | BHANUPALI-BILASPUR BERI NL                                                                          | RVNL   | 04/2008 | N.A.         | 1046.88                  | 4500                        | 3453.12                 |
| 202 | ROHTAK-MEHAM HANSI                                                                                  | NR     | 04/2012 | N.A.         | 287                      | 625                         | 338                     |
| 203 | MANOHARABAD-KOTHPALL NEW LINE(SCR)                                                                  | SCR    | 04/2006 | N.A.         | 378.56                   | 1160.47                     | 781.91                  |
| 204 | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR                                                   | ECR    | 04/1996 | 03/2012      | 332.92                   | 477.88                      | 144.96                  |
| 205 | BHAIRABI SAIRONG, NL, NEFR                                                                          | NFR    | 04/2008 | 04/2014      | 619.34                   | 4600                        | 3980.66                 |
| 206 | ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT                                        | RE     | 02/2008 | 03/2012      | 171.1                    | 275.08                      | 103.98                  |
| 207 | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE                                                   | SR     | 09/2006 | N.A.         | 343.17                   | 1065                        | 721.83                  |
| 208 | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI                                     | SR     | 09/2007 | N.A.         | 404.19                   | 2072.5                      | 1668.31                 |
| 209 | BHOPAL BINA 3D LINE DOUBLING                                                                        | RVNL   | 09/2007 | 03/2010      | 687.2                    | 950                         | 262.8                   |
| 210 | GOELKERA-MANOHARPUR, (LD)(SER)                                                                      | RVNL   | 03/1997 | 02/2006      | 261.7                    | 388                         | 126.3                   |
| 211 | KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC                                             | ER     | 04/2010 | 03/2017      | 423.66                   | 720.59                      | 296.93                  |
| 212 | MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL | ER     | 04/2009 | N.A.         | 493.96                   | 681.68                      | 187.72                  |
| 213 | KALYAN-KASARA 3RD LINE                                                                              | CR     | 04/2011 | N.A.         | 277.7                    | 792.89                      | 515.19                  |
| 214 | WARDHA-NANDED MAHARASHTRA                                                                           | CR     | 04/2008 | N.A.         | 499.3                    | 3168.29                     | 2668.99                 |
| 215 | KATAKHAL TO BHAIRABI                                                                                | NFR    | 04/1998 | 12/2012      | 227.9                    | 509                         | 281.1                   |
| 216 | RATLAM-MHOW-KHANDWA-AKOLA (GC)                                                                      | WR     | 04/2008 | 03/2012      | 603.04                   | 1030.29                     | 427.25                  |
| 217 | JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)                                   | NWR    | 04/2008 | 03/2014      | 653.19                   | 941.04                      | 287.85                  |
| 218 | KOTLPALLI-NARASAPUR (NL) (SCR)                                                                      | SCR    | 12/2001 | N.A.         | 330                      | 2125.18                     | 1795.18                 |
| 219 | TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)                     | M RTP  | 03/2000 | 12/2006      | 1049.69                  | 3404.92                     | 2355.23                 |
| 220 | GADWAL - RAICHUR (NL), SCR                                                                          | SCR    | 04/1998 | 02/2011      | 92.63                    | 350                         | 257.37                  |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning

## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( SEPTEMBER 2017 )

| Sn  | Project                                     | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|-----|---------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 221 | TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER | ER     | 04/2000 | N.A.         | 1188.91                  | 1319.33                     | 130.42                  |
| 222 | DEOGHAR - SULTANGANJ (INL), ER              | ER     | 04/2000 | 12/2012      | 607.09                   | 973.33                      | 366.24                  |
| 223 | JIND-SONEPAT (NL),NR                        | NR     | 01/2004 | 03/2012      | 238.56                   | 740                         | 501.44                  |
| 224 | HARIDASPUR-PARADEEP(NL)                     | RVNL   | 04/1996 | N.A.         | 301.64                   | 1185.64                     | 884                     |

## ROAD TRANSPORT AND HIGHWAYS

| Sn  | Project                                                                                              | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|-----|------------------------------------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 225 | MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000                                                  | NHAI   | 12/2003 | 04/2009      | 199.81                   | 385.13                      | 185.32                  |
| 226 | SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA   | NHAI   | 03/2017 | 03/2020      | 831.58                   | 1177                        | 345.42                  |
| 227 | SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) | NHAI   | 03/2017 | 03/2020      | 985.41                   | 1200                        | 214.59                  |
| 228 | 6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA | NHAI   | 03/2017 | 03/2020      | 2064.99                  | 2447                        | 382.01                  |
| 229 | REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM  | NHAI   | 03/2017 | 03/2020      | 1288.07                  | 1420                        | 131.93                  |
| 230 | SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000                 | NHAI   | 03/2017 | 03/2020      | 1041.62                  | 1187.1                      | 145.48                  |
| 231 | 4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)                                             | NHAI   | 03/2017 | 03/2020      | 744.64                   | 982                         | 237.36                  |
| 232 | FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C | NHAI   | 03/2017 | 03/2020      | 1184.71                  | 1310                        | 125.29                  |
| 233 | FOUR LANING OF GWALIOR-SHIVPURI                                                                      | NHAI   | 05/2013 | 11/2015      | 1055                     | 1601.77                     | 546.77                  |
| 234 | CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S | PWD    | 03/2011 | 12/2015      | 218.31                   | 339.82                      | 121.51                  |
| 235 | SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O | NHAI   | 03/2017 | 03/2020      | 993.16                   | 1434                        | 440.84                  |
| 236 | GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION                                                  | NHAI   | 03/2010 | 09/2012      | 1509.1                   | 3237.87                     | 1728.77                 |
| 237 | TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA | PWD    | 12/2011 | 02/2012      | 156.63                   | 276                         | 119.37                  |
| 238 | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)                                                          | NHAI   | 05/2009 | 11/2011      | 1108                     | 2288                        | 1180                    |
| 239 | HARANGAJO TO MAIBANG, NH-54                                                                          | NHAI   | 12/2003 | 07/2009      | 196                      | 331.23                      | 135.23                  |
| 240 | MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450                                                 | NHAI   | 12/2003 | 11/2008      | 155.04                   | 280.13                      | 125.09                  |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning



## DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

( SEPTEMBER 2017 )

**SHIPPING AND PORTS**

| Sn  | Project                                                                                              | Agency      | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|-----|------------------------------------------------------------------------------------------------------|-------------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 241 | ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)                                         | PORT TRUST  | 10/2002 | 03/2006      | 150                      | 600                         | 450                     |
| 242 | RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST                                        | RVNL        | 03/2007 | 04/2009      | 245.67                   | 409.83                      | 164.16                  |
| 243 | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB | MUMBAI PORT | 01/2007 | 12/2010      | 366.39                   | 669.46                      | 303.07                  |

**STEEL**

| Sn  | Project                                                  | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|-----|----------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 244 | CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA | HSCL   | 05/2005 | 02/2014      | 768.88                   | 1113.34                     | 344.46                  |
| 245 | REVAMPING OF SINTER MACHINES - 1 AND 2                   | RINL   | 12/2009 | 10/2016      | 343                      | 488.4                       | 145.4                   |

**TELECOMMUNICATIONS**

| Sn  | Project              | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|-----|----------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 246 | NETWORK FOR SPECTRUM | DOT    | 03/2012 | 07/2015      | 13334                    | 24664                       | 11330                   |

**URBAN DEVELOPMENT**

| Sn  | Project                                                                                             | Agency | DOA     | DOC Original | Cost Original (Rs.crore) | Cost Anticipated (Rs.crore) | Cost Overrun (Rs.crore) |
|-----|-----------------------------------------------------------------------------------------------------|--------|---------|--------------|--------------------------|-----------------------------|-------------------------|
| 247 | BANGALORE METRO RAIL PROJECT                                                                        | M RTP  | 05/2006 | 06/2011      | 6395                     | 13845.01                    | 7450.01                 |
| 248 | CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA | CPWD   | 12/2008 | 12/2013      | 114.26                   | 266                         | 151.74                  |
| 249 | DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN      | CPWD   | 08/2014 | 03/2015      | 350.02                   | 479.87                      | 129.85                  |
| 250 | CHENNAI METRO RAIL LTD (PHASE 1)                                                                    | CMRL   | 02/2009 | 12/2015      | 14600                    | 19058                       | 4458                    |
| 251 | OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA                        | CPWD   | 02/2011 | 03/2016      | 241.33                   | 349.33                      | 108                     |
| 252 | ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI     | CPWD   | 10/2013 | 10/2019      | 1219.21                  | 1592                        | 372.79                  |

DOA -&gt; Date of Approval

DOC -&gt; date of Commissioning

**DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE**

**(SEPTEMBER 2017)**

**ATOMIC ENERGY**

| Sn | Project                                           | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|---------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 1  | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) | BHAVNI | 09/2003 | 09/2010      | 02/2018         | 3492.00                   | 6000.00                      | 2508            | 89           |

**CIVIL AVIATION**

| Sn | Project                                                                    | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|----------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 2  | CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR | AAI    | 10/2013 | 09/2018      | 06/2020         | 314.61                    | 441.33                       | 126.72          | 21           |
| 3  | CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT                     | AAI    | 01/2009 | 01/2011      | 09/2017         | 309.46                    | 553.53                       | 244.07          | 80           |

**COAL**

| Sn | Project                                                  | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|----------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 4  | RCE OF INDARAM OCP(1.20 MTPA)                            | SCCL   | 07/2011 | 03/2015      | 03/2020         | 162.76                    | 349.28                       | 186.52          | 60           |
| 5  | NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI | NCL    | 10/2007 | 03/2012      | 03/2018         | 259.40                    | 486.57                       | 227.17          | 72           |
| 6  | SHANTIKHANI LONGWALL PROJ-SCCL                           | SCCL   | 10/2006 | 03/2012      | 03/2019         | 249.03                    | 448.86                       | 199.83          | 84           |
| 7  | JAGANNATHPOR OCP(3.00MTY)                                | SECL   | 09/2008 | 03/2015      | 03/2020         | 152.43                    | 459.49                       | 307.06          | 60           |

**HEAVY INDUSTRY**

| Sn | Project                                                            | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|--------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 8  | NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) | NATIS  | 04/2011 | 09/2011      | 12/2017         | 1718.00                   | 3827.30                      | 2109.3          | 75           |

**PETROLEUM**

| Sn | Project                                                                                | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|----------------------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 9  | RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT)              | IOCL   | 06/2012 | 07/2014      | 09/2017         | 150.00                    | 259.93                       | 109.93          | 38           |
| 10 | UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE | OIL    | 09/2012 | 03/2015      | 11/2017         | 871.35                    | 1200.00                      | 328.65          | 32           |
| 11 | URAN CHAKAN SHIKRAPUR LPG PIPELINE                                                     | HPCL   | 12/2009 | 10/2014      | 03/2018         | 309.81                    | 723.40                       | 413.59          | 41           |
| 12 | MH NORTH REDEVELOPMENT PHASE III                                                       | ONGC   | 06/2014 | 05/2017      | 05/2018         | 5706.47                   | 5813.25                      | 106.78          | 12           |

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

**DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE**

**(SEPTEMBER 2017)**

| Sn | Project                                                                 | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|-------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 13 | INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS                       | ONGC   | 05/2013 | 04/2016      | 12/2017         | 4124.35                   | 5637.00                      | 1512.65         | 20           |
| 14 | STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR                            | ISPRL  | 01/2006 | 01/2012      | 10/2017         | 993.00                    | 1693.00                      | 700             | 69           |
| 15 | LPG TERMINAL AT KOCHI                                                   | IOCL   | 10/2015 | 10/2017      | 03/2019         | 607.06                    | 714.25                       | 107.19          | 17           |
| 16 | DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY         | IOCL   | 03/2014 | 09/2017      | 06/2018         | 3076.00                   | 4190.00                      | 1114            | 9            |
| 17 | INTEGRATED DEVELOPMENT OF B-127 FIELDS                                  | ONGC   | 12/2011 | 03/2015      | 03/2018         | 2059.63                   | 2665.65                      | 606.02          | 36           |
| 18 | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)  | ONGC   | 06/2010 | 01/2014      | 11/2019         | 202.94                    | 330.35                       | 127.41          | 70           |
| 19 | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) | ONGC   | 03/2011 | 05/2013      | 12/2017         | 861.79                    | 1256.72                      | 394.93          | 55           |

**POWER**

| Sn | Project                                                                                              | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|------------------------------------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 20 | TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)-DRASS- KARGIL-KHALSTI-LEH PROJECT            | PGCIL  | 01/2014 | 09/2017      | 09/2018         | 1788.41                   | 2352.57                      | 564.16          | 12           |
| 21 | COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C    | PGCIL  | 03/2013 | 06/2015      | 03/2018         | 514.20                    | 703.10                       | 188.9           | 33           |
| 22 | BARH STPP(3X660MW) NTPC                                                                              | NTPC   | 02/2005 | 01/2011      | 03/2019         | 8692.97                   | 1,5095.67                    | 6402.7          | 98           |
| 23 | KISHANGANGA HEP (3X110 MW)                                                                           | NHPC   | 01/2009 | 01/2016      | 02/2018         | 3642.04                   | 5882.01                      | 2239.97         | 25           |
| 24 | TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A                   | PGCIL  | 03/2015 | 12/2015      | 03/2018         | 955.00                    | 1364.00                      | 409             | 27           |
| 25 | TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM CUDDALORE AREA - PACKAGE A                  | PGCIL  | 03/2015 | 12/2015      | 03/2018         | 955.00                    | 1364.00                      | 409             | 27           |
| 26 | PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT                                     | SJVN   | 05/2015 | 12/2016      | 12/2017         | 436.68                    | 602.44                       | 165.76          | 12           |
| 27 | KAMENG HYDROELECTRIC PROJECT (NEEPCO)                                                                | NEEPCO | 12/2004 | 12/2009      | 03/2018         | 2496.90                   | 6179.96                      | 3683.06         | 99           |
| 28 | COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L | PGCIL  | 09/2011 | 09/2014      | 12/2017         | 1940.13                   | 2702.65                      | 762.52          | 39           |

DOA -&gt; Date of Approval

COR -&gt; Cost Overrun

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

**DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE**  
(SEPTEMBER 2017)

| Sn | Project                                                                                             | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|-----------------------------------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 29 | TEHRI PUMPED STORAGE PLANT(1000MW)                                                                  | THDCIL | 07/2006 | 02/2016      | 12/2020         | 1657.00                   | 3939.11                      | 2282.11         | 58           |
| 30 | SYSTEM STRENGTHENING XIII OF SR GRID                                                                | PGCIL  | 10/2011 | 06/2014      | 06/2018         | 487.49                    | 639.46                       | 151.97          | 48           |
| 31 | PARE HYDRO ELECTRIC PROJECT                                                                         | NEEPCO | 12/2008 | 08/2013      | 03/2018         | 573.99                    | 1337.76                      | 763.77          | 55           |
| 32 | SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV                                                       | PGCIL  | 12/2011 | 08/2014      | 12/2017         | 297.33                    | 426.29                       | 128.96          | 40           |
| 33 | SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH                   | PGCIL  | 12/2011 | 08/2014      | 12/2017         | 1746.65                   | 2228.71                      | 482.06          | 40           |
| 34 | KUNADANKULAM APP TRANS SYSTEM (PGCIL)                                                               | PGCIL  | 05/2005 | 11/2008      | 09/2018         | 1779.29                   | 2187.32                      | 408.03          | 118          |
| 35 | NPGCPL-NABINAGAR STPP - JV (3X660 MW)                                                               | NTPC   | 01/2013 | 01/2018      | 12/2018         | 1,2964.60                 | 1,3731.26                    | 766.66          | 11           |
| 36 | PARBATI HEP (4X200 MW) (NHPC) II                                                                    | NHPC   | 09/2002 | 09/2009      | 12/2018         | 3919.59                   | 8398.75                      | 4479.16         | 111          |
| 37 | WESTERN REGION STRENGTHENING SCHEME-V                                                               | PGCIL  | 12/2007 | 09/2010      | 03/2018         | 477.69                    | 738.48                       | 260.79          | 90           |
| 38 | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT                                          | PGCIL  | 10/2008 | 10/2012      | 02/2018         | 4824.12                   | 5071.94                      | 247.82          | 64           |
| 39 | TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER | PGCIL  | 04/2010 | 01/2015      | 03/2018         | 4404.57                   | 5135.01                      | 730.44          | 38           |
| 40 | NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT                                                  | PGCIL  | 02/2009 | 08/2013      | 12/2017         | 1,1130.19                 | 1,3762.80                    | 2632.61         | 52           |
| 41 | TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.                                        | PGCIL  | 02/2010 | 12/2012      | 02/2018         | 2144.00                   | 2932.88                      | 788.88          | 62           |
| 42 | EASTERN REGION STRENGTHENING SCHEME-V                                                               | PGCIL  | 10/2013 | 04/2016      | 03/2018         | 1364.52                   | 1891.41                      | 526.89          | 23           |
| 43 | TAPOVAN-VISHNUGAD HEP (4X130MW)                                                                     | NTPC   | 11/2006 | 03/2013      | 06/2019         | 2978.48                   | 3846.30                      | 867.82          | 75           |
| 44 | BONGAIGAON THERMAL POWER PROJECT                                                                    | NTPC   | 01/2008 | 09/2011      | 12/2017         | 4375.35                   | 6749.18                      | 2373.83         | 75           |
| 45 | EASTERN REGION STRENGTHENING SCHEME-III                                                             | PGCIL  | 07/2010 | 11/2012      | 12/2017         | 1272.80                   | 1731.10                      | 458.3           | 61           |
| 46 | BRBCL-NABINAGAR TPP- JV (4X250                                                                      | NTPC   | 01/2007 | 05/2014      | 06/2018         | 5353.00                   | 7998.00                      | 2645            | 49           |

DOA -&gt; Date of Approval

COR -&gt; Cost Overrun

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

**DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE**

**(SEPTEMBER 2017)**

| Sn | Project                                          | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|--------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
|    | MW)                                              |        |         |              |                 |                           |                              |                 |              |
| 47 | TUIRIAL HYDRO ELECTRIC PROJECT (60MW)            | NEEPCO | 07/1998 | 07/2006      | 11/2017         | 368.72                    | 1329.43                      | 960.71          | 136          |
| 48 | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV | PGCIL  | 11/2011 | 11/2014      | 12/2017         | 723.63                    | 882.13                       | 158.5           | 37           |

**RAILWAYS**

| Sn | Project                                                                | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 49 | MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD                  | RVNL   | 04/2012 | 03/2016      | 12/2018         | 632.68                    | 816.55                       | 183.87          | 33           |
| 50 | HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)                           | NWR    | 04/2008 | 03/2015      | 12/2019         | 829.74                    | 1161.64                      | 331.9           | 57           |
| 51 | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)                      | M RTP  | 03/1996 | 03/2004      | 03/2020         | 495.44                    | 1781.98                      | 1286.54         | 192          |
| 52 | MANDARHILL -DUMKA-RAMPURHAT (NL), ER                                   | ER     | 04/1995 | 12/2011      | 03/2020         | 900.05                    | 1125.89                      | 225.84          | 99           |
| 53 | BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR                           | NFR    | 09/1997 | 04/2008      | 06/2018         | 1500.00                   | 5000.00                      | 3500            | 122          |
| 54 | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)                                 | WCR    | 09/1998 | 05/2008      | 03/2023         | 247.66                    | 6093.31                      | 5845.65         | 178          |
| 55 | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR                | NFR    | 04/2000 | 12/2008      | 03/2019         | 733.00                    | 3010.00                      | 2277            | 123          |
| 56 | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)                                    | NFR    | 04/2003 | 03/2011      | 03/2020         | 727.56                    | 9658.00                      | 8930.44         | 108          |
| 57 | NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)         | NFR    | 04/2006 | 03/2015      | 03/2020         | 850.00                    | 3000.00                      | 2150            | 60           |
| 58 | MUMBAI URBAN TRANSPORT PROJECT PHASE-II                                | M RTP  | 04/2008 | 03/2014      | 03/2019         | 5300.00                   | 7986.04                      | 2686.04         | 60           |
| 59 | LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT | NFR    | 04/1996 | 03/2009      | 03/2018         | 1676.31                   | 7000.00                      | 5323.69         | 108          |
| 60 | AGARTALA SABROOM, NL, NEFR                                             | NFR    | 04/2008 | 03/2014      | 03/2020         | 813.34                    | 3451.00                      | 2637.66         | 72           |
| 61 | SEVOK RANGPO, NEFR                                                     | NFR    | 04/2008 | 12/2015      | 03/2020         | 1339.48                   | 4084.69                      | 2745.21         | 51           |
| 62 | UDHAMPUR-SRINAGAR-BARAMULLA                                            | NR     | 03/1995 | 11/2002      | 12/2018         | 2500.00                   | 1,9565.00                    | 17065           | 193          |

DOA -&gt; Date of Approval

COR -&gt; Cost Overrun

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

**DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE**

**(SEPTEMBER 2017)**

| Sn | Project                                                                                        | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|------------------------------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
|    | (NL), NR                                                                                       |        |         |              |                 |                           |                              |                 |              |
| 63 | SALKA ROAD -ANUPNAGAR LINE DOUBLING                                                            | RVNL   | 09/2006 | 03/2010      | 12/2017         | 324.90                    | 516.40                       | 191.5           | 93           |
| 64 | NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)   | RVNL   | 04/2010 | 03/2016      | 12/2020         | 3951.98                   | 4259.48                      | 307.5           | 57           |
| 65 | NANDYAL-YERRAGUNTALA(NL), SCR                                                                  | SCR    | 03/1996 | 02/2009      | 12/2017         | 155.74                    | 966.98                       | 811.24          | 106          |
| 66 | GONDIA-JABALPUR(GC), (SECR)                                                                    | SECR   | 02/1997 | 03/1998      | 12/2019         | 386.30                    | 1776.81                      | 1390.51         | 261          |
| 67 | SUKINDA ROAD - ANGUL (NL)(ECOR)                                                                | RVNL   | 04/1998 | 02/2015      | 12/2019         | 183.23                    | 1202.70                      | 1019.47         | 58           |
| 68 | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)                                                      | RVNL   | 04/2000 | 03/2009      | 12/2017         | 133.41                    | 340.00                       | 206.59          | 105          |
| 69 | GOELKERA-MANOHARPUR, (LD)(SER)                                                                 | RVNL   | 03/1997 | 02/2006      | 12/2019         | 261.70                    | 388.00                       | 126.3           | 166          |
| 70 | BHOPAL BINA 3D LINE DOUBLING                                                                   | RVNL   | 09/2007 | 03/2010      | 03/2018         | 687.20                    | 950.00                       | 262.8           | 96           |
| 71 | BHAIRABI SAIRONG, NL, NEFR                                                                     | NFR    | 04/2008 | 04/2014      | 03/2020         | 619.34                    | 4600.00                      | 3980.66         | 71           |
| 72 | OBULAVARIPALLE-KRISHNAPATNAM(RVNL)                                                             | RVNL   | 07/2006 | 03/2008      | 03/2020         | 743.00                    | 1825.00                      | 1082            | 144          |
| 73 | JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)                              | NWR    | 04/2008 | 03/2014      | 06/2019         | 653.19                    | 941.04                       | 287.85          | 63           |
| 74 | GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)                                                 | NCR    | 04/2011 | 02/2020      | 12/2022         | 1176.09                   | 3845.60                      | 2669.51         | 34           |
| 75 | DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANTPUR-BANSI PAHARPUR | NCR    | 04/2010 | 02/2019      | 12/2022         | 622.41                    | 2030.50                      | 1408.09         | 46           |

**ROAD TRANSPORT AND HIGHWAYS**

| Sn | Project                                     | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|---------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 76 | FOUR LANING OF GWALIOR-SHIVPURI             | NHAI   | 05/2013 | 11/2015      | 09/2017         | 1055.00                   | 1601.77                      | 546.77          | 22           |
| 77 | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) | NHAI   | 05/2009 | 11/2011      | 03/2018         | 1108.00                   | 2288.00                      | 1180            | 76           |
| 78 | GUJARAT/MAHARASHTRA                         | NHAI   | 03/2010 | 09/2012      | 12/2017         | 1509.10                   | 3237.87                      | 1728.77         | 63           |

DOA -&gt; Date of Approval

COR -&gt; Cost Overrun

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

**DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE**  
(SEPTEMBER 2017)

| Sn | Project                         | Agency | DOA | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|---------------------------------|--------|-----|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
|    | BORDERSURAT-HAZIRA PORT SECTION |        |     |              |                 |                           |                              |                 |              |

**SHIPPING AND PORTS**

| Sn | Project                                                                                              | Agency          | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|------------------------------------------------------------------------------------------------------|-----------------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 79 | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB | MUMBAI PORT TRU | 01/2007 | 12/2010      | 12/2018         | 366.39                    | 669.46                       | 303.07          | 96           |
| 80 | ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)                                         | PORT TRUST      | 10/2002 | 03/2006      | 12/2017         | 150.00                    | 600.00                       | 450             | 141          |

**STEEL**

| Sn | Project                                | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|----------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 81 | REVAMPING OF SINTER MACHINES - 1 AND 2 | RINL   | 12/2009 | 10/2016      | 03/2018         | 343.00                    | 488.40                       | 145.4           | 17           |

**TELECOMMUNICATIONS**

| Sn | Project              | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|----------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 82 | NETWORK FOR SPECTRUM | DOT    | 03/2012 | 07/2015      | 06/2019         | 1,3334.00                 | 2,4664.00                    | 11330           | 47           |

**URBAN DEVELOPMENT**

| Sn | Project                                                                                             | Agency | DOA     | DOC Original | DOC Anticipated | Cost Original (Rs. crore) | Cost Anticipated (Rs. crore) | COR (Rs. crore) | TOR (Months) |
|----|-----------------------------------------------------------------------------------------------------|--------|---------|--------------|-----------------|---------------------------|------------------------------|-----------------|--------------|
| 83 | CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA | CPWD   | 12/2008 | 12/2013      | 10/2019         | 114.26                    | 266.00                       | 151.74          | 70           |
| 84 | CHENNAI METRO RAIL LTD (PHASE 1)                                                                    | CMRL   | 02/2009 | 12/2015      | 12/2017         | 1,4600.00                 | 1,9058.00                    | 4458            | 24           |
| 85 | OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA                        | CPWD   | 02/2011 | 03/2016      | 03/2018         | 241.33                    | 349.33                       | 108             | 24           |

DOA -&gt; Date of Approval

COR -&gt; Cost Overrun

DOC -&gt; Date of Commissioning

TOR -&gt; Time Overrun

## Details of Ongoing Projects Under -Public Private Partnership Mode

Annexure- XVIII

| Costing Rs.150 Crore and above |                                                                                                                                |                                  |                                        |                                | (September 2017)                      |             |                      |                        |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------|----------------------------------|----------------------------------------|--------------------------------|---------------------------------------|-------------|----------------------|------------------------|
|                                |                                                                                                                                |                                  |                                        |                                | Date of Commissioning<br>(Month/Year) |             |                      |                        |
| Sl.No                          | Project                                                                                                                        | Date of Approval<br>(Month/Year) | Original / Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs.crore) | Original / Revised                    | Anticipated | Cost Overruns<br>(%) | T.O.R.s<br>(in months) |
| 1                              | 2                                                                                                                              | 3                                | 4                                      | 5                              | 6                                     | 7           | 8                    | 9                      |
|                                |                                                                                                                                |                                  |                                        |                                |                                       |             |                      |                        |
|                                | <u>MINES</u>                                                                                                                   |                                  |                                        |                                |                                       |             |                      |                        |
| 1                              | IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT RAJASTHAN - PPP (ANNUITY) - [N10000009]                                          | 12/2015                          | 344.50 -                               | 344.50                         | 11/2016 -                             | -           | .00                  | 0                      |
|                                | Total                                                                                                                          |                                  | 344.50 -                               | 344.50                         |                                       |             |                      |                        |
|                                |                                                                                                                                |                                  |                                        |                                |                                       |             |                      |                        |
|                                | <u>ROAD TRANSPORT AND HIGHWAYS</u>                                                                                             |                                  |                                        |                                |                                       |             |                      |                        |
| 2                              | 2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]                                                             | 07/2012                          | 291.36 -                               | 291.36                         | 01/2014 -                             | 12/2017     | .00                  | 47                     |
| 3                              | INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]                                                                                   | 11/2010                          | 325.00 -                               | 325.00                         | 05/2013 -                             | 07/2017     | .00                  | 50                     |
| 4                              | 2 LANNING OF MOKAMA-MUNGER - PPP (ANNUITY) - [N24000166]                                                                       | 05/2011                          | 351.54 -                               | 351.54                         | 05/2013 -                             | 10/2017     | .00                  | 53                     |
| 5                              | TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]                                               | 05/2010                          | 374.00 -                               | 374.00                         | 05/2013 -                             | 12/2017     | .00                  | 55                     |
| 6                              | 2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]                                                   | 09/2011                          | 485.00 -                               | 485.00                         | 08/2013 -                             | 12/2017     | .00                  | 52                     |
| 7                              | DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]                                                                      | 04/2007                          | 486.00 -                               | 486.00                         | 05/2010 -                             | 08/2017     | .00                  | 87                     |
| 8                              | 2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]                                                              | 05/2011                          | 511.54 -                               | 511.54                         | 11/2013 -                             | 12/2017     | .00                  | 49                     |
| 9                              | TRICHY - KARUR - PPP (BOT) - [N24000528]                                                                                       | 03/2007                          | 516.00 -                               | 516.00                         | 07/2008 -                             | -           | .00                  | 0                      |
| 10                             | 2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426] | 11/2012                          | 530.07 -                               | 530.07                         | 08/2016 -                             | -           | .00                  | 0                      |
| 11                             | JORBAT - BARAPANI - PPP (ANNUITY) - [N24000180]                                                                                | 01/2011                          | 536.00 -                               | 536.00                         | 01/2014 -                             | 03/2018     | .00                  | 50                     |
| 12                             | TALEGAON-AMRAVATI - PPP (BOT) - [N24000140]                                                                                    | 11/2009                          | 567.00 -                               | 567.00                         | 11/2013 -                             | -           | .00                  | 0                      |
| 13                             | TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]                                                                       | 04/2011                          | 571.00 -                               | 571.00                         | 10/2013 -                             | 12/2017     | .00                  | 50                     |
| 14                             | PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]                                                               | 09/2011                          | 574.00 -                               | 574.00                         | 03/2014 -                             | 09/2017     | .00                  | 42                     |
| 15                             | 4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]                                                                      | 01/2011                          | 575.00 -                               | 575.00                         | 07/2013 -                             | 03/2018     | .00                  | 56                     |
| 16                             | DEOLI KOTA - PPP (BOT) - [N24000148]                                                                                           | 01/2011                          | 593.00 -                               | 593.00                         | 07/2013 -                             | 10/2017     | .00                  | 51                     |
| 17                             | GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]                                                                            | 12/2003                          | 604.00 -                               | 604.00                         | 12/2009 -                             | -           | .00                  | 0                      |



## Details of Ongoing Projects Under -Public Private Partnership Mode

| Costing Rs.150 Crore and above |                                                                                                                                |                               |                                     |                             | (September 2017)                   |             |                   |                     |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|-----------------------------|------------------------------------|-------------|-------------------|---------------------|
|                                |                                                                                                                                |                               |                                     |                             | Date of Commissioning (Month/Year) |             |                   |                     |
| Sl.No                          | Project                                                                                                                        | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised                 | Anticipated | Cost Overruns (%) | T.O.R.s (in months) |
| 1                              | 2                                                                                                                              | 3                             | 4                                   | 5                           | 6                                  | 7           | 8                 | 9                   |
| 18                             | SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149 ]                                         | 02/2010                       | 617.00 -                            | 617.00                      | 08/2012 -                          | 12/2017     | .00               | 64                  |
| 19                             | 2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213 ]                                       | 04/2012                       | 624.00 -                            | 624.00                      | 04/2014 -                          | -           | .00               | 0                   |
| 20                             | TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - PPP (BOT) - [N24000586 ]                                                    | 06/2016                       | 637.18 -                            | 637.18                      | 06/2019 -                          | 06/2019     | .00               | 0                   |
| 21                             | ROHTAK-BAWAL - PPP (BOT) - [N24000169 ]                                                                                        | 05/2011                       | 650.00 -                            | 650.00                      | 11/2013 -                          | 08/2017     | .00               | 45                  |
| 22                             | 2-LANNING WITH PS KHAGARIA-PURNEA - PPP (ANNUITY) - [N24000184 ]                                                               | 05/2011                       | 664.00 -                            | 664.00                      | 02/2014 -                          | -           | .00               | 0                   |
| 23                             | PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165 ]                                                                              | 08/2010                       | 671.30 -                            | 671.30                      | 02/2013 -                          | 06/2018     | .00               | 64                  |
| 24                             | KRISHNANAGAR-BERHAMPUR - PPP (ANNUITY) - [N24000209 ]                                                                          | 02/2012                       | 702.16 -                            | 702.16                      | 07/2014 -                          | 03/2018     | .00               | 44                  |
| 25                             | MUZZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201 ]                                                                             | 09/2011                       | 754.00 -                            | 754.00                      | 03/2013 -                          | 11/2017     | .00               | 56                  |
| 26                             | FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587 ]  | 06/2016                       | 763.23 -                            | 763.23                      | 06/2019 -                          | 06/2019     | .00               | 0                   |
| 27                             | BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445 ] | 08/2014                       | 822.90 -                            | 822.90                      | 04/2018 -                          | 04/2018     | .00               | 0                   |
| 28                             | FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - PPP (BOT) - [N24000500 ]                                                          | 01/2016                       | 830.36 -                            | 830.36                      | 07/2018 -                          | 07/2018     | .00               | 0                   |
| 29                             | CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - PPP (BOT) - [N24000144 ]                                              | 09/2010                       | 852.00 -                            | 852.00                      | 03/2013 -                          | 06/2017     | .00               | 51                  |
| 30                             | BARSAT-KRISHNANAGAR - PPP (ANNUITY) - [N24000229 ]                                                                             | 08/2012                       | 867.00 -                            | 867.00                      | 02/2015 -                          | 12/2017     | .00               | 34                  |
| 31                             | 4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - PPP (BOT) - [N24000454 ]                                                 | 06/2014                       | 923.04 -                            | 923.04                      | 11/2016 -                          | 11/2017     | .00               | 12                  |
| 32                             | KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175 ]                                                                                | 01/2011                       | 953.88 -                            | 953.88                      | 07/2013 -                          | -           | .00               | 0                   |
| 33                             | 4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453 ]                                                       | 01/2015                       | 972.50 -                            | 972.50                      | 07/2017 -                          | 01/2018     | .00               | 6                   |
| 34                             | 4-LANING OF BRAHAMPUR-FARAKA - PPP (BOT) - [N24000203 ]                                                                        | 02/2011                       | 998.79 -                            | 998.79                      | 08/2013 -                          | 03/2018     | .00               | 55                  |
| 35                             | BAREILLY-SITAPUR (NH-24) - PPP (BOT) - [N24000200 ]                                                                            | 03/2011                       | 1,046.00 -                          | 1,046.00                    | 09/2013 -                          | 10/2017     | .00               | 49                  |
| 36                             | SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - PPP (BOT) - [N24000205 ]                                                       | 12/2011                       | 1,047.00 -                          | 1,047.00                    | 06/2014 -                          | 06/2017     | .00               | 36                  |

## Details of Ongoing Projects Under -Public Private Partnership Mode

| Costing Rs.150 Crore and above |                                                                                                                                |                               |                                     |                             | (September 2017)                   |             |                   |                     |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|-----------------------------|------------------------------------|-------------|-------------------|---------------------|
|                                |                                                                                                                                |                               |                                     |                             | Date of Commissioning (Month/Year) |             |                   |                     |
| Sl.No                          | Project                                                                                                                        | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised                 | Anticipated | Cost Overruns (%) | T.O.R.s (in months) |
| 1                              | 2                                                                                                                              | 3                             | 4                                   | 5                           | 6                                  | 7           | 8                 | 9                   |
| 37                             | FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]                                                                      | 05/2013                       | 1,055.00 -                          | 1,601.77                    | 11/2015 -                          | 09/2017     | 51.83             | 22                  |
| 38                             | 4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]                                                                           | 02/2011                       | 1,078.84 -                          | 1,078.84                    | 08/2013 -                          | 12/2017     | .00               | 52                  |
| 39                             | SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]                                                                              | 06/2011                       | 1,100.70 -                          | 1,100.70                    | 06/2014 -                          | 12/2017     | .00               | 42                  |
| 40                             | PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]                                                          | 05/2009                       | 1,108.00 -                          | 2,288.00                    | 11/2011 -                          | 03/2018     | 106.50            | 76                  |
| 41                             | GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]                                                                              | 02/2011                       | 1,141.00 -                          | 1,141.00                    | 08/2013 -                          | 08/2017     | .00               | 48                  |
| 42                             | INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]                                                                              | 10/2010                       | 1,175.00 -                          | 1,206.10                    | 04/2013 -                          | 09/2017     | 2.65              | 53                  |
| 43                             | SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]                             | 09/2011                       | 1,250.00 -                          | 1,250.00                    | 12/2013 -                          | 12/2017     | .00               | 48                  |
| 44                             | 4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]                                                | 04/2014                       | 1,266.60 -                          | 1,266.60                    | 09/2016 -                          | 03/2018     | .00               | 18                  |
| 45                             | MURADABAD-BAREILY - PPP (BOT) - [N24000154]                                                                                    | 04/2010                       | 1,267.00 -                          | 1,267.00                    | 06/2013 -                          | 09/2017     | .00               | 51                  |
| 46                             | WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - PPP (BOT) - [N24000230]                                      | 05/2013                       | 1,348.20 -                          | 1,348.20                    | 02/2014 -                          | 03/2018     | .00               | 49                  |
| 47                             | FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]                                                                  | 03/2015                       | 1,388.00 -                          | 1,388.00                    | - -                                | 08/2018     | .00               | 0                   |
| 48                             | FOUR LANING OF KAITHAL - RAJASTHAN BORDER - PPP (BOT) - [N24000487]                                                            | 07/2015                       | 1,393.00 -                          | 1,393.00                    | - -                                | 01/2018     | .00               | 0                   |
| 49                             | 6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]                                                               | 04/2012                       | 1,396.18 -                          | 1,396.18                    | 09/2014 -                          | 12/2017     | .00               | 39                  |
| 50                             | PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]                                                                                     | 03/2012                       | 1,410.00 -                          | 1,410.00                    | 09/2014 -                          | -           | .00               | 0                   |
| 51                             | RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]                                                                          | 12/2012                       | 1,479.00 -                          | 1,479.00                    | 06/2015 -                          | 12/2017     | .00               | 30                  |
| 52                             | GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]                                                  | 03/2010                       | 1,509.10 -                          | 3,237.87                    | 09/2012 -                          | 12/2017     | 114.56            | 63                  |
| 53                             | SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - PPP (BOT) - [N24000183]                                      | 11/2011                       | 1,535.00 -                          | 1,535.00                    | 05/2014 -                          | 06/2017     | .00               | 37                  |
| 54                             | ETAWAH CHAKERI - PPP (BOT) - [N24000219]                                                                                       | 03/2013                       | 1,573.00 -                          | 1,573.00                    | 09/2015 -                          | 10/2017     | .00               | 25                  |
| 55                             | FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - PPP (BOT) - [N24000505] | 06/2015                       | 1,583.79 -                          | 1,583.79                    | - -                                | 01/2019     | .00               | 0                   |
| 56                             | CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - PPP (BOT) - [N24000145]                                                       | 11/2010                       | 1,585.00 -                          | 1,585.00                    | 05/2013 -                          | 12/2017     | .00               | 55                  |

## Details of Ongoing Projects Under -Public Private Partnership Mode

| Costing Rs.150 Crore and above |                                                                                                |                               |                                     |                             | (September 2017)                   |             |                   |                     |
|--------------------------------|------------------------------------------------------------------------------------------------|-------------------------------|-------------------------------------|-----------------------------|------------------------------------|-------------|-------------------|---------------------|
|                                |                                                                                                |                               |                                     |                             | Date of Commissioning (Month/Year) |             |                   |                     |
| Sl.No                          | Project                                                                                        | Date of Approval (Month/Year) | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised                 | Anticipated | Cost Overruns (%) | T.O.R.s (in months) |
| 1                              | 2                                                                                              | 3                             | 4                                   | 5                           | 6                                  | 7           | 8                 | 9                   |
| 57                             | 4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION<br>- PPP (BOT) - [N24000462]                 | 05/2014                       | 1,655.01<br>-                       | 1,655.01                    | 08/2016<br>-                       | 03/2018     | .00               | 19                  |
| 58                             | 6 LANING OF AGRA - ETAWAH BYPASS<br>- PPP (BOT) - [N24000452]                                  | 07/2015                       | 1,657.20<br>-                       | 1,657.20                    | -<br>-                             | 01/2019     | .00               | 0                   |
| 59                             | SIX-LANING OF BARWA ADDA-PANAGARH<br>- PPP (BOT) - [N24000515]                                 | 04/2014                       | 1,665.00<br>-                       | 1,665.00                    | -<br>-                             | 12/2017     | .00               | 0                   |
| 60                             | GURGAON - KOTPUTLI - JAIPUR (SIX LANE)<br>- PPP (BOT) - [N24000477]                            | 02/2008                       | 1,673.70<br>-                       | 1,673.70                    | 10/2011<br>-                       | 12/2017     | .00               | 74                  |
| 61                             | SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502<br>- PPP (BOT) - [N24000131]                         | 02/2009                       | 1,693.75<br>-                       | 1,693.75                    | 08/2011<br>-                       | 09/2017     | .00               | 73                  |
| 62                             | PUNE-SATARA(NH-4)<br>- PPP (BOT) - [N24000156]                                                 | 10/2010                       | 1,724.55<br>-                       | 1,724.55                    | 03/2013<br>-                       | 12/2017     | .00               | 57                  |
| 63                             | JAMMU-UDHAMPUR KM.27.5 TO KM.67.00<br>- PPP (ANNUITY) - [N24000163]                            | 07/2010                       | 1,813.76<br>-                       | 1,813.76                    | 07/2013<br>-                       | 11/2017     | .00               | 52                  |
| 64                             | FOUR LANING OF AURANGABAD - YEDISHI<br>- PPP (BOT) - [N24000508]                               | 07/2015                       | 1,871.34<br>-                       | 1,871.34                    | 01/2018<br>-                       | 01/2018     | .00               | 0                   |
| 65                             | FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)<br>- PPP (BOT) - [N24000232] | 11/2013                       | 1,916.79<br>-                       | 1,916.79                    | 11/2016<br>-                       | 02/2018     | .00               | 15                  |
| 66                             | DELHI AGRA APPROVED LENGTH 180.0 KM<br>- PPP (BOT) - [N24000224]                               | 10/2012                       | 1,928.22<br>-                       | 1,928.22                    | 04/2015<br>-                       | 12/2017     | .00               | 32                  |
| 67                             | QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00<br>- PPP (ANNUITY) - [N24000161]                      | 07/2010                       | 1,987.00<br>-                       | 1,987.00                    | 07/2015<br>-                       | 03/2019     | .00               | 44                  |
| 68                             | AHMEDABAD TO VADODARA SECTION<br>- PPP (BOT) - [N24000222]                                     | 01/2013                       | 2,125.24<br>-                       | 2,125.24                    | 12/2015<br>-                       | 07/2017     | .00               | 19                  |
| 69                             | 8 LANING OF MUKARBA CHOWK TO PANIPAT<br>- PPP (BOT) - [N24000449]                              | 07/2015                       | 2,128.72<br>-                       | 2,128.72                    | -<br>-                             | 04/2019     | .00               | 0                   |
| 70                             | NASHRI- CHANANI<br>- PPP (ANNUITY) - [N24000162]                                               | 05/2011                       | 2,159.00<br>-                       | 2,159.00                    | 06/2015<br>-                       | -           | .00               | 0                   |
| 71                             | 4 LANING OF AMRAVATI - CHIKHLI (PKG-I)<br>- PPP (BOT) - [N24000425]                            | 07/2015                       | 2,288.18<br>-                       | 2,288.18                    | -<br>-                             | 05/2019     | .00               | 0                   |
| 72                             | 4 LANING OF NAGPUR-BETUL<br>- PPP (ANNUITY) - [N24000155]                                      | 02/2011                       | 2,498.76<br>-                       | 2,498.76                    | 08/2014<br>-                       | 12/2017     | .00               | 40                  |
| 73                             | VARANASI-AURANGABAD KM.786 TO KM.978.40<br>- PPP (BOT) - [N24000182]                           | 09/2011                       | 2,848.00<br>-                       | 2,848.00                    | 03/2014<br>-                       | 04/2018     | .00               | 49                  |
|                                | Total                                                                                          |                               | 83,563.48<br>-                      | 87,050.12                   |                                    |             |                   |                     |
|                                |                                                                                                |                               |                                     |                             |                                    |             |                   |                     |
|                                | <u>SHIPPING AND PORTS</u>                                                                      |                               |                                     |                             |                                    |             |                   |                     |
| 74                             | CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED<br>- PPP (ANNUITY) - [N25000065]        | 10/2013                       | 198.94<br>-                         | 235.15                      | 06/2017<br>-                       | -           | 18.20             | 0                   |
| 75                             | CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED<br>- PPP (ANNUITY) - [N25000066]        | 02/2015                       | 244.50<br>258.00                    | 258.33                      | 12/2017<br>-                       | 12/2017     | 5.66              | 0                   |

## Details of Ongoing Projects Under -Public Private Partnership Mode

| Costing Rs.150 Crore and above |                                                                                                                                |                                  |                                        |                                | (September 2017)                      |             |                   |                     |
|--------------------------------|--------------------------------------------------------------------------------------------------------------------------------|----------------------------------|----------------------------------------|--------------------------------|---------------------------------------|-------------|-------------------|---------------------|
|                                |                                                                                                                                |                                  |                                        |                                | Date of Commissioning<br>(Month/Year) |             |                   |                     |
| Sl.No                          | Project                                                                                                                        | Date of Approval<br>(Month/Year) | Original / Revised Cost<br>(Rs. crore) | Anticipated Cost<br>(Rs.crore) | Original / Revised                    | Anticipated | Cost Overruns (%) | T.O.R.s (in months) |
| 1                              | 2                                                                                                                              | 3                                | 4                                      | 5                              | 6                                     | 7           | 8                 | 9                   |
| 76                             | CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - PPP (BOT) - [N25000063] | 01/2007                          | 366.39<br>-                            | 669.46                         | 12/2010<br>-                          | 12/2018     | 82.72             | 96                  |
|                                | Total                                                                                                                          |                                  | 809.83<br>-                            | 1,162.94                       |                                       |             |                   |                     |
|                                |                                                                                                                                |                                  |                                        |                                |                                       |             |                   |                     |
|                                | Grand Total                                                                                                                    |                                  | 84,717.81                              | 88,557.56                      |                                       |             |                   |                     |
