

**298<sup>th</sup> FLASH REPORT  
ON  
CENTRAL SECTOR PROJECTS  
(₹.150 Crores and above)  
August, 2010**



HPCL – Mumbai Refinery



Government of India  
**Ministry of Statistics and Programme Implementation**  
**Infrastructure and Project Monitoring Division**  
Sardar Patel Bhavan, Sansad Marg  
New Delhi-110001  
Website: [www.cspm.gov.in](http://www.cspm.gov.in)

## Contents

|                                                                                      |       |
|--------------------------------------------------------------------------------------|-------|
| Executive Summary                                                                    | 1 -5  |
| Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11 | 6-6   |
| Summary of Projects                                                                  | 7-14  |
| <b>Sector wise Trend and Graphicalf Analysis</b>                                     | 15-24 |
| Sector wise analysis of projects                                                     | 25-57 |
| Graph                                                                                | 58-67 |
| <b>List of All Ongoing Projects</b>                                                  | 68-68 |
| <b>List of Abbreviations</b>                                                         | 69-70 |

## **EXECUTIVE SUMMARY**

The 298<sup>th</sup> Flash Report for August' 2010, that contains information on the status of 606 projects in the Central Sector, each costing Rs. 150 Crores and above. Since April' 2010, Flash report is prepared for the central sector projects costing Rs 150 Crores and above. During August' 2010, no project reported completion. Nine projects have been added during the month under reference. During August' 2010, total three projects, one in Power sector and two in Telecom sector have shown considerable improvement over the completion schedule reported earlier.

The online submission of the implementation Status Report of the ongoing projects has not been provided/updated regularly by sectors/project agencies leading to under utilization of online computerized monitoring system (OCMS) developed by this Ministry for effective monitoring. Out of 606 ongoing projects on the monitor of this Ministry, 457 projects were updated either by the concerned project agencies online or the data has been entered locally by the staff of this Ministry. The information regarding 149 projects were not updated/received by this Ministry. Sector-wise number of ongoing projects along with status of online reporting is given below:

| S. No.       | Sector                    | Projects on monitor | Reported Online | Additional delays |
|--------------|---------------------------|---------------------|-----------------|-------------------|
| 1.           | ROAD TRANSPORT & HIGHWAYS | 135                 | 117             | 10                |
| 2.           | RAILWAYS                  | 136                 | 93              | 4                 |
| 3.           | POWER                     | 85                  | 79              | 9                 |
| 4.           | PETROLEUM                 | 81                  | 59              | 15                |
| 5.           | COAL                      | 44                  | 43              | 3                 |
| 6.           | TELECOMMUNICATION         | 58                  | 34              | 18                |
| 7.           | STEEL                     | 20                  | 10              | 4                 |
| 8.           | SHIPPING & PORTS          | 23                  | 16              | 2                 |
| 9.           | CIVIL AVIATION            | 9                   | 4               | -                 |
| 10.          | FERTILISERS               | 6                   | 1               | -                 |
| 11.          | ATOMIC ENERGY             | 4                   | -               | -                 |
| 12.          | URBAN DEVELOPMENT         | 2                   | 1               | 1                 |
| 13.          | MINES                     | 1                   | -               | -                 |
| 14.          | HEALTH & FW               | 1                   | -               | -                 |
| 15.          | WATER RESOURCES           | 1                   | -               | -                 |
| <b>Total</b> |                           | <b>606</b>          | <b>457</b>      | <b>66</b>         |

2. Sixty six (66) projects have reported additional delays compared to the completion dates in the previous month. The additional delays are in the range of 1 to 24 months in respect of projects relating to Coal, Steel, Petroleum, Power, Railways, Road Transport and Highways, Shipping & Ports, Telecommunications and Urban Development Sectors.

3. Out of 606 projects, 15 projects are ahead of schedule, 101 are on schedule and 299 projects are delayed. Of the balance, 119 projects do not have fixed dates of commissioning i.e. either the year of commissioning or the tentative gestation period of the projects have been reported. A large number of projects (72) were sanctioned without any commissioning schedule/date.
4. The total cost of implementation of 606 projects when sanction, was of the order of Rs. 617,518.65 Crores but this was subsequently revised to Rs. 742152.22 Crores implying a cost overrun of 20%. The expenditure incurred on these projects till August, 2010 is Rs. 312096.23 Crores which is 42% of the revised cost of the projects.
5. To present a concise picture of the status of on-going projects costing ₹ 150 crore and above, a pictorial presentation is given in the report. Out of 606 projects, presently on the monitor at the end of August, 2010, 101 projects were on schedule (17%), excluding 72 projects without date of commissioning and those have not reported during the month, 299 projects were delayed (50%). During the month, 66 projects have reported additional delays in the range of 2-19 months. The analysis of pictorial presentation shows that since May, 2010 there is a continuous increase in projects reporting delays. The overall cost overrun is also on the rise continuously since May 2010. The overall cost overrun has increases from 15 % in June to 20% in August 2010 due to substantial increase in the completion costs of Expansion of Bokaro Steel Plant and Bhilai Steel Plant by Rs 15089 Crores. It may be seen that out of 299 delayed projects, at the end of August, 2010, 86 projects had overall delay in the range of 1 to 12 months, 87 projects had delay in the range of 13 to 24 months, 96 projects had delay in the range of 25 to 60 months and 30 projects had time overrun of 61 months and above.
6. In the **Coal sector**, 3 projects have reported additional delays in the range of 1-24 months. Barsingsar TPS (NLC) has reported additional delay of 1 month due to delay in supply of indigenous equipment by private sector and delay in equipment erection. Bina Extension Project has reported additional delay of 4 months due to delay in possession and clearance of forest land. Block-B OCP, NCL has reported additional delay of 24 months due to delay in acquisition of land and delay in construction of approach road.
7. In the **Steel Sector**, 4 projects have reported additional delay of 1-5 months. Installation of 700 TPD Oxygen Plant, Rourkela and Simultaneous Blowing of BOF Converter of SMS-II have reported additional delay of 1 month each, however, no reason has been provided by the project authorities for such additional delay. Expansion of Salem Steel Plant has reported additional delay of 1 months due to delay in equipment supply by the contractor. Rebuilding of Coke Oven Battery No-6 has reported additional delay of 5 months due to delay in supply of fireclay bricks.
8. In the **Petroleum Sector**, 15 projects have reported additional delays in the range of 1-6 months, whereas one project has shown considerable improvement over the completion schedule reported earlier. Jagdishpur-Haldia pipeline project of GAIL has reported improvement of 10 months due to revival of fertilizer plants and availability of gas at Haldia landfall point. Installation of FCCU at Mumbai refinery has reported improvement of 1 months due to availability of raw material. Additional Gas Processing Facility at Hazira has reported additional delay of 1 month due to late issue of Notice inviting tenders (NIT). VKPL up gradation and Laying of Spurline to Bhilwara has reported additional delay of 1 month due to delay in tender process, inclement weather conditions and queries

by vendors. MSQ Improvement project has reported additional delay of 1 month due to delay in installation and drilling work by the contractor. Additional Gas processing units at (ONGC) Uran, Mumbai has reported additional delay of 4 months due to delay in tender process. MSQ Upgradation Project at Gawahati Refinery and MSQ Upgradation Project at Digboi Refinery have reported additional delay of 1 months each due to poor response to consultancy bids, frequent bands and insufficient transportation of material/equipment. MSQ Upgradation Project at Barauni Refinery has reported additional delay of 1 month due to backing out of reputed PSU consultants in last moment, slow progress by M/S BHEL in power plant jobs and delay by BPCL in supply of compressor package by 11 month. Bawana-Nangal Pipeline Project has reported additional delays of 6 months due to abnormally high demand of land and crops compensation by farmers of UP and Punjab. Residue upgradation and MS/HSD quality improvement project, Diesel Hydro Treatment Project-BRPL Dhaligaon and Dahej-Vijaypur Pipe Line Project (Phase-II) – have reported additional delay of 1 month and 6 months respectively, however no reasons have been provided by the project authorities for such additional delays.

9. In the **Power Sector**, 9 projects have reported additional delays in the range of 1-12 months. Koteswar Transmission System (PGCIL) has reported additional delay of 3 months due to matching transmission requirement. Teesta Low Dam Stage-II, III and IV have reported additional delay of 10 and 12 months respectively due to delay in forest clearance and delay in decision regarding participation of Chinese firm and strike by GJMM. Tehri Pumped Storage Plant has reported additional delay of 20 months due to delay in award of contract. Eastern Region Strengthening scheme –I (1142 CKM) has reported additional delay of 9 months due to delay in forest clearance. Transmission System for Startup Power to DVC & Maithon RB Generation project (PGCIL) has reported additional delay of 2 months due to delay in forest clearance. SEWA-II HEP (NHPC) has reported additional delay of 1 month due to delay in work of excavation because of poor geology & formation of cavities. The Sewa II HEP has been completed in September 2010. Vindhyachal STPP Stage-IV and Rihand STPP Stage-III have reported additional delay of one month each, however, no specific reasons have been provided by the project authorities for such additional delays.
10. In the **Road Transport and Highways Sector**, 10 projects (Table VIII may be referred) have reported additional delay in the range of 1-24 months. General reasons of delay in meeting the completion schedule include delay in land acquisition, utility shifting, Termination of contracts due to poor performance and delay in getting the forest clearance, slow progress of work by the contractor, local constraints, inclement weather conditions and revision of scope of works. However, the project authorities have not mentioned any specific reason for such additional delays.
11. In the **Railway Sector**, 4 projects have shown additional delays in the range of 9-12 months. Jind-Sonepat (NL), Chandigarh-Ludhiana (New BG Line), (NR) and Utratia – Zafrabad (LD) and Mumbai Urban Transport Project Phase-II have reported additional delays of 3 months, 12 months, 12 months and 12 months respectively, however, no specific reasons have been given by the project authorities for additional delays.
12. In the **Shipping & Ports Sector**, 2 projects namely Development & Operation of an International Container Transshipment Terminal of Port Trust, Kerala and Acquisition of 2 Nos. of 105000 DWT LR-II Tankers of Shipping Corporation of India, Maharashtra have shown additional delays in the range of 2-4 months. However, no specific reasons have been given by the project authorities for such additional delays.

13. In the **Telecommunication Sector**, 16 projects (Table VIII may be referred) have shown additional delays of 1 – 3 months, whereas two projects namely GSM equipment of 2,00,000 Line (2 G) Rajasthan and ERP implementation in BSNL on Turnkey basis have shown improvement over the reported schedule. General reasons of delay in meeting the completion schedule include delay in land acquisition, Erection of BITS, Termination of contracts due to poor performance, slow progress of work by the contractor, local constraints, inclement weather conditions and revision of scope of works. However, the project authorities have not mentioned any specific reason for such additional delays.
14. In the **Urban Development Sector**, Bangalore Metro Rail Project has reported additional delay of 9 months due to delay in demolition of structures/building etc.

Status as on 01.09.2010 in respect of completion of projects costing Rs.150 Crores and above in different sectors during 2010-11 is indicated in the following table in Annexure-I.



(Pankaj Jain)

**Additional Secretary to the Government of India  
Ministry of Statistics & Programme Implementation**

## EXECUTIVE SUMMARY

| Sl. No. | Sector                    | Projects on Monitor | Projects Additional Delayed |
|---------|---------------------------|---------------------|-----------------------------|
| 1       | Railways                  | 136                 | 4                           |
| 2       | Road Transport & Highways | 135                 | 10                          |
| 3       | Power                     | 85                  | 9                           |
| 4       | Petroleum                 | 81                  | 15                          |
| 5       | Telecommunications        | 58                  | 18                          |
| 6       | Coal                      | 44                  | 3                           |
| 7       | Shipping & Ports          | 23                  | 2                           |
| 8       | Steel                     | 20                  | 4                           |
| 9       | Civil Aviation            | 9                   | 0                           |
| 10      | Fertilisers               | 6                   | 0                           |
| 11      | Atomic Energy             | 4                   | 0                           |
| 12      | Urban Development         | 2                   | 1                           |
| 13      | Mines                     | 1                   | 0                           |
| 14      | Health & Family Welfare   | 1                   | 0                           |
| 15      | Water Resources           | 1                   | 0                           |
|         | Total                     | 606                 | 66                          |

# ANNEXURE-I

## Month wise List of Completed Project Costing Rs. 150 Crore and above during 2010-2011

| Sl. No.                   | Project Name                                                                                           | Original Cost<br>(Rs. Crore) | Original Date<br>Of<br>Commissioning | Cumulative<br>Expenditure<br>(Rs. Crore) |
|---------------------------|--------------------------------------------------------------------------------------------------------|------------------------------|--------------------------------------|------------------------------------------|
| May,2010                  |                                                                                                        |                              |                                      |                                          |
| <u>Petroleum</u>          |                                                                                                        |                              |                                      |                                          |
| 1                         | SHORT TERM LOW COST MUMBAI REFINERY(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000082]                | 390.00                       | 01/2010                              | 188.43                                   |
| June,2010                 |                                                                                                        |                              |                                      |                                          |
| <u>Steel</u>              |                                                                                                        |                              |                                      |                                          |
| 2                         | REBUILDING OF COKE OVEN BATTERY NO.-4(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000021]           | 248.94                       | 08/2009                              | 164.48                                   |
| <u>Petroleum</u>          |                                                                                                        |                              |                                      |                                          |
| 3                         | CLEAN FUELS PROJECT AT VISAKH REFINERY(HPCL)(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [160100281]    | 1,635.00                     | 05/2006                              | 2,095.36                                 |
| <u>Telecommunications</u> |                                                                                                        |                              |                                      |                                          |
| 4                         | EXPANSION OF 750K GSM LINES(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000049]                           | .00                          | 12/2008                              | 175.77                                   |
| 5                         | DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000052]          | 463.61                       | 12/2009                              | 106.13                                   |
| July,2010                 |                                                                                                        |                              |                                      |                                          |
| <u>Petroleum</u>          |                                                                                                        |                              |                                      |                                          |
| 6                         | BARGE BUMPER-BOAT LANDING-RISER PROTECTOR PROJECT(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000055] | 289.60                       | 05/2010                              | 198.16                                   |
| 7                         | BINA KOTA PIPE LINE PROJECT(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000079]                        | 405.82                       | 12/2009                              | 354.93                                   |




## Summary of projects on the Flash Report for the month of Aug, 2010

### I. Project Implementation – Current Status:

|                                                                                          |     |
|------------------------------------------------------------------------------------------|-----|
| Number of Projects Cost (Rs. 150 Cr. & above) Previous Month                             | 599 |
| Number of Projects Completed/Dropped/Frozen Cost (Rs. 150 Cr. & above) in Previous Month | 2   |
| Number of Projects Completed/Dropped/Frozen Cost (Rs. 150 Cr. & above) in Current month  | 0   |
| Number of Projects Cost (Rs. 150 Cr. & above) Added in Current month                     | 9   |
| Number of Projects Cost (Rs. 150 Cr. & above) in Current Month                           | 606 |

### II. Brief Analysis


a) **Project Status w.r.t Original Schedule:** Out of 606 projects, 15 projects are ahead of schedule, 101 projects are on schedule and 299 projects are delayed. Of the balance, 119 projects do not have fixed dates of commissioning while 72 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

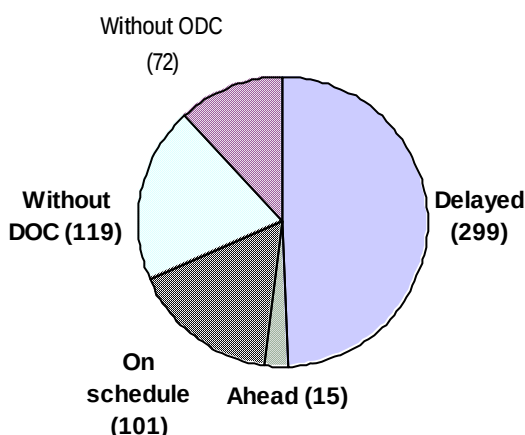

### III. Investment Scenario

**Figures are in Rs. Crore**

The total Original cost of implementation of 606 projects when sanctioned, was of the order of Rs. 617518.65 crore but this was subsequently revised to Rs. 742152.22 crore implying a cost overrun of 20.20%. The expenditure incurred on these projects till Aug, 2010 is Rs. 312096.23 crore, which is 42.05% of the revised cost of the projects.

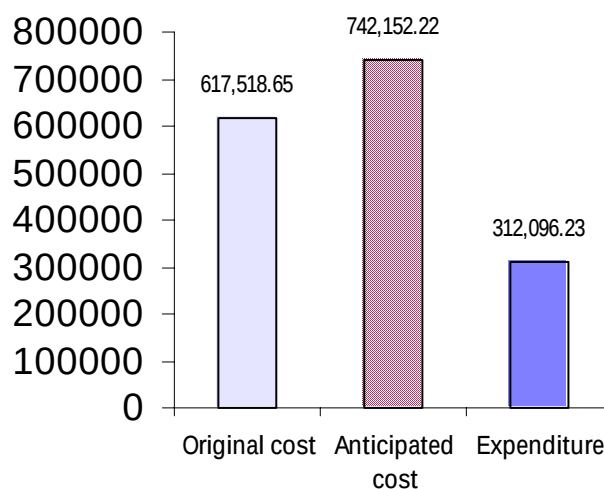

## I. Project Added / Completed / Dropped / Frozen

|                                                           |     |
|-----------------------------------------------------------|-----|
| No of Projects in Previous Month                          | 599 |
| No of Projects Completed/Dropped/Frozen in Previous Month | 2   |
| No of Projects Completed/Dropped/Frozen in Current Month  | 0   |
| No of Projects added in Current Month                     | 9   |
| No of Projects in Current Month                           | 606 |

## II. Project status

| With Respect To                    | Number of Projects |       |             |                               |               | Total | Delay (%) |
|------------------------------------|--------------------|-------|-------------|-------------------------------|---------------|-------|-----------|
|                                    | Delayed            | Ahead | On schedule | Without ODC but DOC available | Without D.O.C |       |           |
| Original Date of Completion        | 299                | 15    | 101         | 72                            | 119           | 606   | 49.34     |
| Latest Approved Date of Completion | 320                | 18    | 116         | 59                            | 95            | 606   | 52.81     |

## III. (A) Project cost

| (Cost/ Expenditure in Rs. crore ) |                 |            |             |             |              |             |       |
|-----------------------------------|-----------------|------------|-------------|-------------|--------------|-------------|-------|
| With Respect to                   | No. of Projects | Cost       |             |             | Cost overrun |             |       |
|                                   |                 | Sanctioned | Anticipated | Expenditure | %            | (Rs. Crore) | %     |
| Original (OCE)                    | 511             | 524,016.66 | 582,080.28  | 236,070.59  | 40.60        | 58,063.62   | 11.10 |
| Latest Approved (RCE)             | 95              | 135,385.10 | 160,071.94  | 76,025.64   | 47.50        | 24,686.84   | 18.20 |
| Total                             | 606             | 659,401.76 | 742,152.22  | 312,096.23  | 42.05        | 82750.46    | 12.55 |
| Original Cost of All Projects     |                 |            |             |             |              |             |       |
| Original Cost                     | 606             | 617,518.65 | 742,152.22  | 312,096.23  | 42.10        | 124,633.57  | 20.20 |

## III. (B) Delayed Project cost

| With Respect to | No. of Projects | Cost       |             |             | Cost overrun |             |       |
|-----------------|-----------------|------------|-------------|-------------|--------------|-------------|-------|
|                 |                 | Sanctioned | Anticipated | Expenditure | %            | (Rs. Crore) | %     |
| Original        | 299             | 292,902.47 | 367,988.05  | 194,039.12  | 52.70        | 75,085.58   | 25.60 |

## IV. Additional Delayed Project cost

| With Respect to | No. of Projects | Cost       |             |             | Cost overrun |             |       |
|-----------------|-----------------|------------|-------------|-------------|--------------|-------------|-------|
|                 |                 | Sanctioned | Anticipated | Expenditure | %            | (Rs. Crore) | %     |
| Latest Approved | 66              | 80,287.59  | 91,145.26   | 30,012.66   | 32.90        | 10,857.67   | 13.50 |
| Total           | 66              | 80,287.59  | 91,145.26   | 30,012.66   | 32.93        | 10857.67    | 13.52 |

## V. List of projects completed/dropped current month

(Cost /Expenditure in Rs. crore )

| Project | DOA | Original |     | Now anticipated |     | Final       |
|---------|-----|----------|-----|-----------------|-----|-------------|
|         |     | Cost     | DOC | Cost            | DOC | Expenditure |

## VI. List of projects added

(Cost in Rs. crore )

| Project                                          | DOA     | Original |        | Anticipated |         |
|--------------------------------------------------|---------|----------|--------|-------------|---------|
|                                                  |         | Cost     | DOC    | Cost        | DOC     |
| <u>Railways</u>                                  |         |          |        |             |         |
| MAHARAJGANJ-MASRAKH (NL) - NER                   | 4/2003  | 104.10   | -      | 218.19      | -       |
| <u>Coal</u>                                      |         |          |        |             |         |
| Tapin OCP                                        | 8/2008  | 264.68   | 3/2012 | 264.68      | 3/2012  |
| <u>Shipping &amp; Ports</u>                      |         |          |        |             |         |
| Mechanization of coal handling facilities to 200 | 2/2010  | 444.10   | 6/2010 | 444.10      | 11/2012 |
| <u>Coal</u>                                      |         |          |        |             |         |
| Churi Benti UG                                   | 6/2007  | 163.51   | 3/2011 | 163.51      | 3/2013  |
| <u>Petroleum</u>                                 |         |          |        |             |         |
| Assam gas Cracker project                        | 4/2006  | 5,460.61 | 4/2012 | 5,460.61    | 4/2012  |
| <u>Coal</u>                                      |         |          |        |             |         |
| Purnadih OCP                                     | 7/2008  | 210.98   | 3/2013 | 210.98      | 3/2013  |
| <u>Petroleum</u>                                 |         |          |        |             |         |
| Wax Project                                      | 8/2010  | 576.60   | 2/2014 | 576.60      | 2/2014  |
| <u>Coal</u>                                      |         |          |        |             |         |
| North Urimari OCP                                | 12/2007 | 179.87   | 3/2012 | 179.87      | 3/2012  |
| Rajrappa RCE OCP                                 | 12/2009 | 510.85   | 3/2016 | 510.85      | 3/2016  |

## VII. Milestones (Cumulative due & achieved)

|                      |      |
|----------------------|------|
| Total                | 2132 |
| Achieved up to month | 807  |

| Sl. No.      | Sector                    | Projects on Monitor | Projects having Milestones |
|--------------|---------------------------|---------------------|----------------------------|
| 1            | Atomic Energy             | 4                   | 4                          |
| 2            | Civil Aviation            | 9                   | 1                          |
| 3            | Coal                      | 44                  | 21                         |
| 4            | Fertilisers               | 6                   | 4                          |
| 5            | Health & Family Welfare   | 1                   | 1                          |
| 6            | Mines                     | 1                   | 1                          |
| 7            | Petroleum                 | 81                  | 20                         |
| 8            | Power                     | 85                  | 27                         |
| 9            | Railways                  | 136                 | 1                          |
| 10           | Road Transport & Highways | 135                 | 0                          |
| 11           | Shipping & Ports          | 23                  | 0                          |
| 12           | Steel                     | 20                  | 11                         |
| 13           | Telecommunications        | 58                  | 0                          |
| 14           | Urban Development         | 2                   | 2                          |
| 15           | Water Resources           | 1                   | 0                          |
| <b>Total</b> |                           | <b>606</b>          | <b>93</b>                  |

## VIII. List of projects reporting additional delays

| Project name                                                       | Cost ( Rs. Crore) |             | DOC reported |            |            | Delay       |
|--------------------------------------------------------------------|-------------------|-------------|--------------|------------|------------|-------------|
|                                                                    | Original          | Anticipated | Original     | Last month | This month | (in months) |
| <u>Coal</u>                                                        |                   |             |              |            |            |             |
| BARSINGSAR TPS<br>(2X125MW) (NLC)                                  | 1,114.18          | 1,626.09    | 06/2009      | 09/2010    | 10/2010    | 1           |
| BINA EXTN. PROJ                                                    | 168.97            | 168.97      | 03/2014      | 11/2013    | 03/2014    | 4           |
| BLOCK-B OCP NCL (3.5 MTY)                                          | 746.04            | 437.34      | 03/2012      | 03/2013    | 03/2015    | 24          |
| <u>Steel</u>                                                       |                   |             |              |            |            |             |
| EXPANSION OF SALEM<br>STEEL PLANT                                  | 1,902.00          | 1,902.00    | N.A.         | 08/2010    | 09/2010    | 1           |
| INSTALLATION OF 700 TPD<br>OXYGEN PLANT, ROURKELA                  | 302.70            | 302.70      | 06/2009      | 07/2010    | 09/2010    | 2           |
| SIMULTANEOUS BLOWING<br>OF BOF CONVERTER OF<br>SMS-II              | 197.66            | 197.66      | N.A.         | 07/2010    | 09/2010    | 2           |
| REBUILDING OF COKE<br>OVEN BATTERY NO-6 (BSP)                      | 172.78            | 172.78      | N.A.         | 06/2010    | 11/2010    | 5           |
| <u>Petroleum</u>                                                   |                   |             |              |            |            |             |
| JAGDISHPUR-HALDIA<br>PIPELINE PROJECT PHASE-I                      | 7,596.18          | 6,652.22    | 01/2013      | 01/2013    | 03/2012    | -10         |
| DIESEL HYDRO TREATMENT<br>PROJECT,BRPL DHALIGAON                   | 1,431.91          | 1,676.00    | 09/2009      | 09/2010    | 10/2010    | 1           |
| RESIDUE UPGRADATION<br>AND MS/HSD QUALITY<br>IMPROVEMENT           | 5,693.00          | 6,898.00    | 01/2010      | 10/2010    | 11/2010    | 1           |
| MSQ UPGRADATION<br>PROJECT AT GUWAHATI<br>REFINERY                 | 372.00            | 325.00      | 02/2010      | 09/2010    | 10/2010    | 1           |
| MSQ UPGRADATION<br>PROJECT AT DIGBOI<br>REFINERY                   | 356.00            | 300.00      | 02/2010      | 09/2010    | 10/2010    | 1           |
| MSQ UPGRADATION<br>PROJECT AT BARAUNI<br>REFINERY                  | 1,492.00          | 1,505.00    | 04/2010      | 09/2010    | 10/2010    | 1           |
| MSQ IMPROVMENT<br>PROJECT                                          | 293.60            | 293.60      | 12/2009      | 09/2010    | 10/2010    | 1           |
| INSTALLATION OF FCCV AT<br>MUMBAI REFINERY                         | 900.47            | 900.47      | 09/2009      | 09/2010    | 10/2010    | 1           |
| ADDITIONAL GAS<br>PROCESSING FACILITI AT<br>HAZIRA                 | 370.11            | 370.11      | 04/2011      | 06/2012    | 07/2012    | 1           |
| VKPL UPGRADATION AND<br>LAYING OF SPURLINE (TO<br>BHILWARA AND CHI | 463.32            | 463.32      | N.A.         | 05/2011    | 06/2011    | 1           |
| DEVELOPMENT OF B-193<br>CLUSTER FIELDS                             | 3,248.78          | 5,633.44    | 03/2010      | 04/2012    | 06/2012    | 2           |

## VIII. List of projects reporting additional delays

| Project name                                       | Cost ( Rs. Crore) |             | DOC reported |            |            | Delay<br>(in months) |
|----------------------------------------------------|-------------------|-------------|--------------|------------|------------|----------------------|
|                                                    | Original          | Anticipated | Original     | Last month | This month |                      |
| C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC)      | 900.92            | 1,493.49    | 06/2006      | 07/2010    | 10/2010    | 3                    |
| ADDITIONAL GAS PROCESSING UNITS AT URAN            | 1,797.35          | 1,797.35    | 12/2011      | 09/2012    | 01/2013    | 4                    |
| BAWANA NANGAL PIPE LINE PROJECT                    | 1,816.07          | 1,816.07    | N.A.         | 10/2010    | 04/2011    | 6                    |
| DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II)         | 4,429.38          | 2,800.00    | N.A.         | 10/2010    | 04/2011    | 6                    |
| <b>Power</b>                                       |                   |             |              |            |            |                      |
| VINDHYACHAL STTP STAGE-IV                          | 5,915.00          | 5,915.00    | 11/2012      | 11/2012    | 12/2012    | 1                    |
| RIHAND STTP STAGE-III (2X500MW)                    | 6,230.81          | 6,230.81    | 11/2012      | 11/2012    | 12/2012    | 1                    |
| SEWA- II H.E.P (NHPC)                              | 665.46            | 1,016.74    | 09/2007      | 05/2010    | 07/2010    | 2                    |
| KOTESWAR TRANSMISSION SYSTEM (PGCIL)               | 260.34            | 241.27      | 06/2008      | 08/2010    | 11/2010    | 3                    |
| TEHRI PUMPED STORAGE PLANT(1000MW)                 | 1,657.00          | 3,124.76    | 07/2010      | 12/2014    | 03/2015    | 3                    |
| EASTERN REGION STRENGTHENING SCHEME-II             | 227.52            | 227.52      | 06/2010      | 07/2010    | 10/2010    | 3                    |
| TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G | 290.49            | 290.49      | 04/2010      | 09/2010    | 12/2010    | 3                    |
| TESSTA LOW DAM STAGE - II, III (NHPC)              | 768.92            | 1,279.40    | 03/2007      | 02/2011    | 12/2011    | 10                   |
| TEESTA LOW DAM HEP, STAGE-IV (NHPC)                | 1,061.38          | 1,061.38    | 09/2009      | 08/2011    | 08/2012    | 12                   |
| <b>Railways</b>                                    |                   |             |              |            |            |                      |
| JIND-SONEPAT (NL),NR                               | 190.81            | 234.45      | N.A.         | 03/2012    | 12/2012    | 9                    |
| CHANDIGARH-LUDHIANA(NEW BG LINE),NR                | 248.44            | 1,103.47    | N.A.         | 12/2011    | 12/2012    | 12                   |
| UTRATIA-ZAFRABAD (LINE DOUBLING)                   | 325.00            | 496.03      | 03/2010      | 12/2011    | 12/2012    | 12                   |
| MUMBAI URBAN TRANSPORT PROJECT PHASE-II            | 5,300.00          | 5,300.00    | 03/2014      | 03/2014    | 03/2015    | 12                   |
| <b>Road Transport &amp; Highways</b>               |                   |             |              |            |            |                      |
| GWALIOR-JHANSI, NH-75                              | 604.00            | 604.00      | 12/2009      | 12/2010    | 03/2011    | 3                    |
| HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24       | 220.00            | 220.00      | 09/2007      | 06/2011    | 11/2011    | 5                    |
| LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)   | 225.00            | 225.00      | 10/2008      | 10/2010    | 03/2011    | 5                    |

## VIII. List of projects reporting additional delays

| Project name                                          | Cost ( Rs. Crore) |             | DOC reported |            |            | Delay<br>(in months) |
|-------------------------------------------------------|-------------------|-------------|--------------|------------|------------|----------------------|
|                                                       | Original          | Anticipated | Original     | Last month | This month |                      |
| DELHI/ HARYANA BORDER TO ROHTAK                       | 486.00            | 486.00      | 05/2010      | 12/2010    | 05/2011    | 5                    |
| DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)               | 160.00            | 160.00      | 05/2008      | 06/2011    | 12/2011    | 6                    |
| LANKA TO DABOKA (NH-54)(NHAI)                         | 225.00            | 225.00      | 06/2008      | 08/2010    | 03/2011    | 7                    |
| NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH         | 557.00            | 557.00      | 02/2010      | 12/2010    | 10/2011    | 10                   |
| SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)         | 151.30            | 151.30      | 10/2008      | 12/2010    | 11/2011    | 11                   |
| SAGAR - RAJMARG CHORAH,KM 211 TO KM 255, NH-26 (NHAI) | 203.43            | 203.43      | 10/2008      | 12/2010    | 12/2011    | 12                   |
| MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450  | 155.04            | 155.04      | 11/2008      | 12/2010    | 12/2012    | 24                   |
| <b>Shipping &amp; Ports</b>                           |                   |             |              |            |            |                      |
| DEV. & OPRATION OF AN INTERNATIONAL CONTAINER TRA     | 2,118.00          | 2,118.00    | 11/2004      | 08/2010    | 10/2010    | 2                    |
| ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS     | 586.58            | 586.58      | 11/2010      | 11/2010    | 03/2011    | 4                    |
| <b>Telecommunications</b>                             |                   |             |              |            |            |                      |
| GSM equipment of 2,00,000Lines (2G) Rajasthan ( Ph    | 577.35            | 577.35      | 09/2010      | 08/2010    | 07/2010    | -1                   |
| ERP implementation in BSNL on Turnkey basis           | 384.00            | 384.00      | 10/2010      | 11/2010    | 10/2010    | -1                   |
| GSM equipment of 900000Lines (2G) PunjabPhase V.2     | 241.49            | 241.49      | 09/2009      | 09/2010    | 10/2010    | 1                    |
| GSM equipment of 1867000Lines (2G) 383000 lines 3(    | 868.00            | 868.00      | 08/2009      | 09/2010    | 10/2010    | 1                    |
| GSM equipment of 1625000Lines (2G) 325000 lines 3(    | 916.70            | 916.70      | 11/2010      | 08/2010    | 09/2010    | 1                    |
| GSM equipment of 1900000Lines (2G) 401700 lines 3(    | 760.20            | 810.37      | 01/2010      | 08/2010    | 09/2010    | 1                    |
| GSM equipment of 1700000Lines (2G) 234100 lines 3(    | 677.75            | 719.90      | 10/2009      | 09/2010    | 10/2010    | 1                    |
| GSM equipment of 1900000Lines (2G) 335500lines 3(G    | 848.70            | 848.70      | 01/2010      | 09/2010    | 10/2010    | 1                    |
| GSM equipment of 4,50,000 Lines (2G) Haryana (Phas    | 216.54            | 216.54      | 09/2009      | 08/2010    | 10/2010    | 2                    |



## VIII. List of projects reporting additional delays



| Project name                                        | Cost ( Rs. Crore) |             | DOC reported |            |            | Delay<br>(in months) |
|-----------------------------------------------------|-------------------|-------------|--------------|------------|------------|----------------------|
|                                                     | Original          | Anticipated | Original     | Last month | This month |                      |
| GSM equipment of 200000Lines (2G) UP(West)Phase V.  | 336.84            | 336.84      | 10/2009      | 08/2010    | 10/2010    | 2                    |
| GSM equipment of 975000Lines (2G) 325000 lines 3(G) | 625.53            | 625.53      | 02/2010      | 08/2010    | 10/2010    | 2                    |
| GSM equipment of 1100000Lines (2G) UP East Phase    | 624.75            | 624.75      | 09/2010      | 08/2010    | 10/2010    | 2                    |
| GSM equipment of 375000Lines (2G) 75000lines 3(G)   | 170.23            | 167.20      | 06/2009      | 08/2010    | 10/2010    | 2                    |
| GSM equipment of 945000Lines (2G) 225000lines 3(G)  | 366.00            | 529.32      | 10/2008      | 08/2010    | 10/2010    | 2                    |
| GSM equipment of 799000Lines (2G) 101000 lines 3(G) | 328.13            | 392.44      | 03/2009      | 08/2010    | 10/2010    | 2                    |
| GSM equipment of 1500000Lines (2G) 264700lines 3(G) | 922.91            | 922.91      | 01/2010      | 08/2010    | 10/2010    | 2                    |
| CONVERGENT BILLING AND CRM-MTNL(DELHI)              | 249.00            | 229.41      | 02/2007      | 12/2010    | 03/2011    | 3                    |
| Expn of existing 2G & 3G GSM N/W by 750k            | 180.53            | 180.53      | 06/2010      | 09/2010    | 12/2010    | 3                    |
| <b>Urban Development</b>                            |                   |             |              |            |            |                      |
| BANGALORE METRO RAIL PROJECT                        | 6,395.00          | 11,609.00   | 12/2011      | 06/2012    | 03/2013    | 9                    |



Number of projects reporting additional delay = 66







## Sector wise Trend and Graphical Analysis ( May'10, June'10 ,July'10,Aug'10)

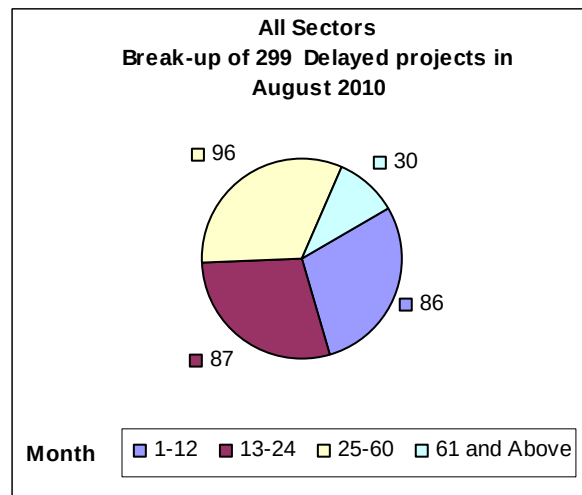
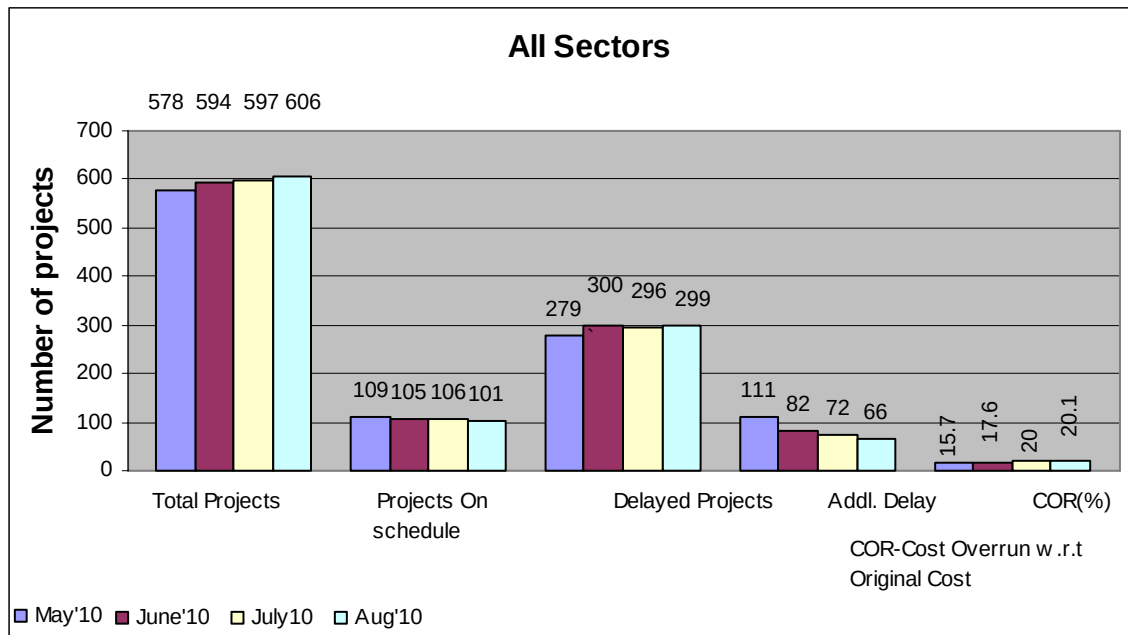


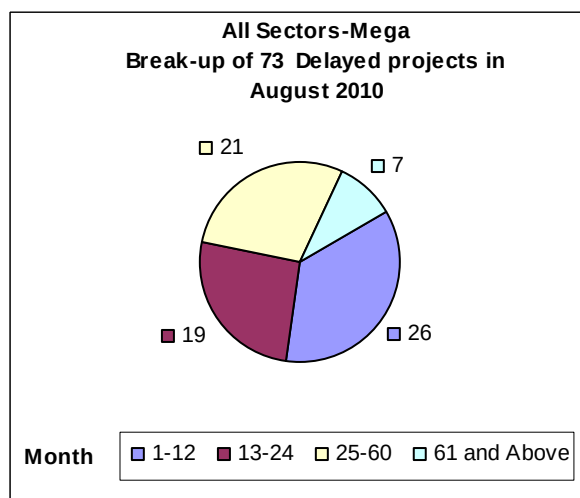
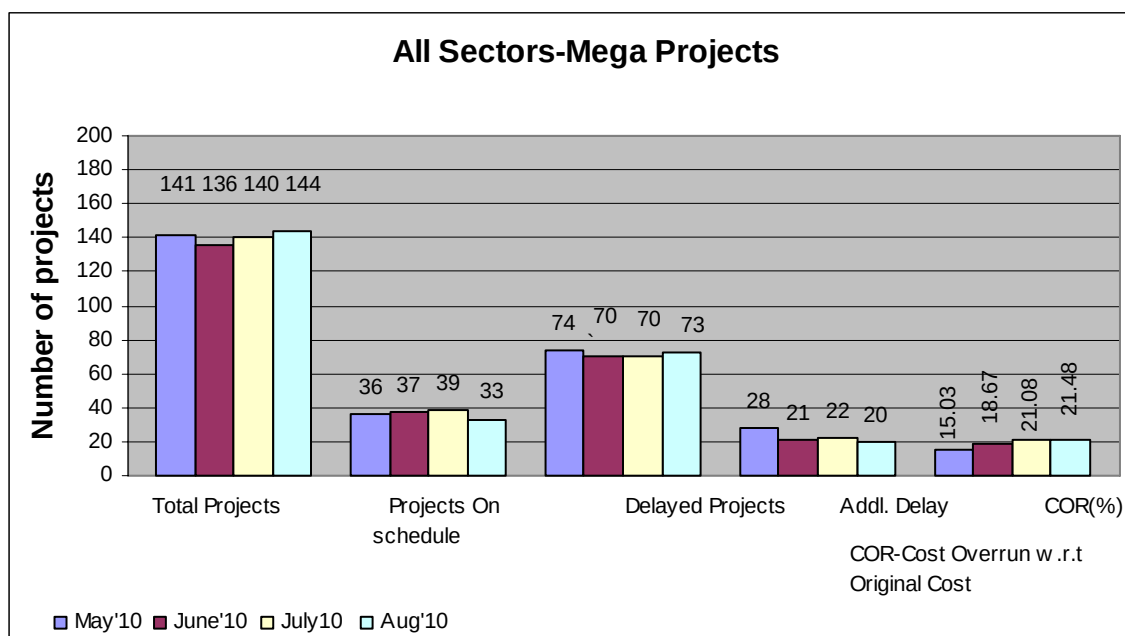


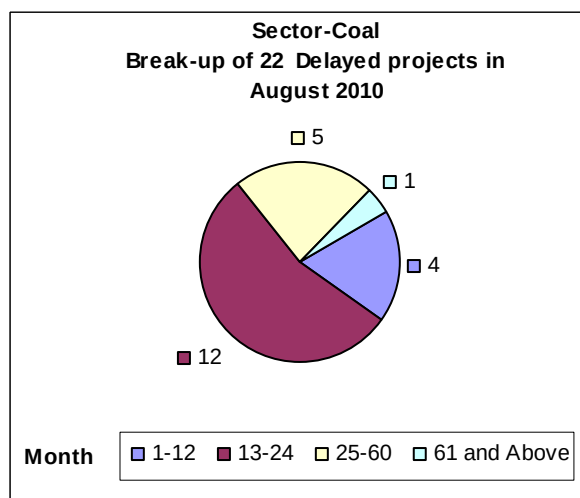
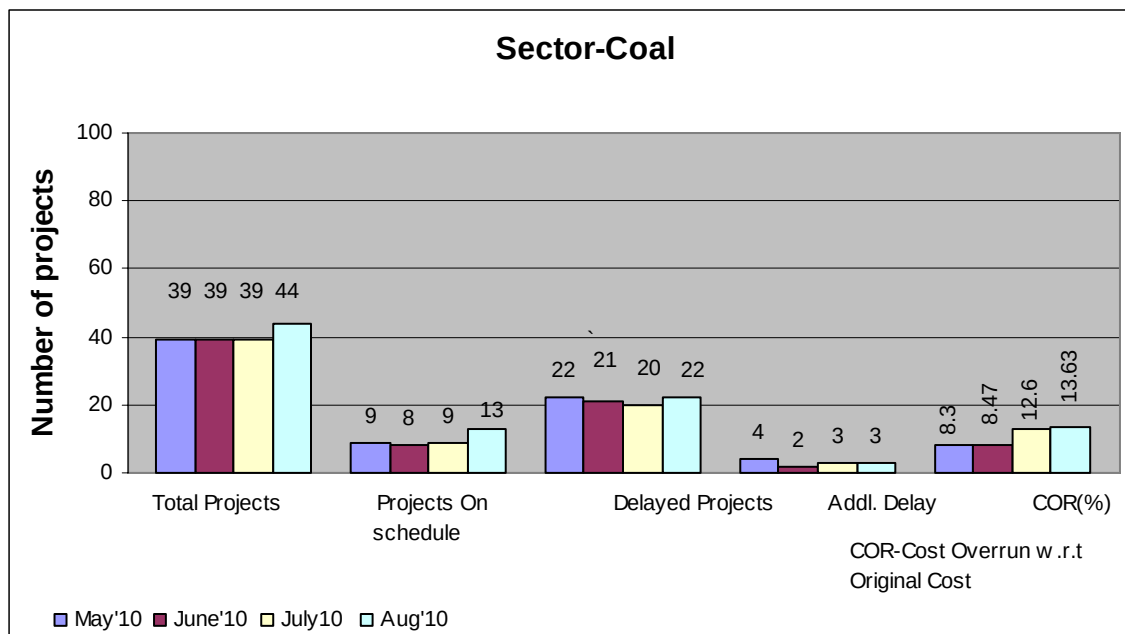


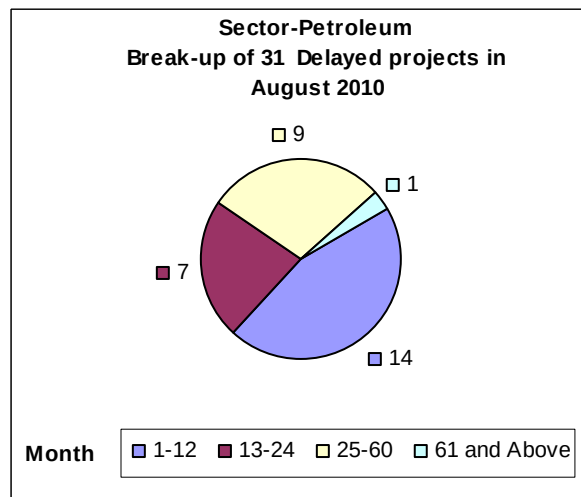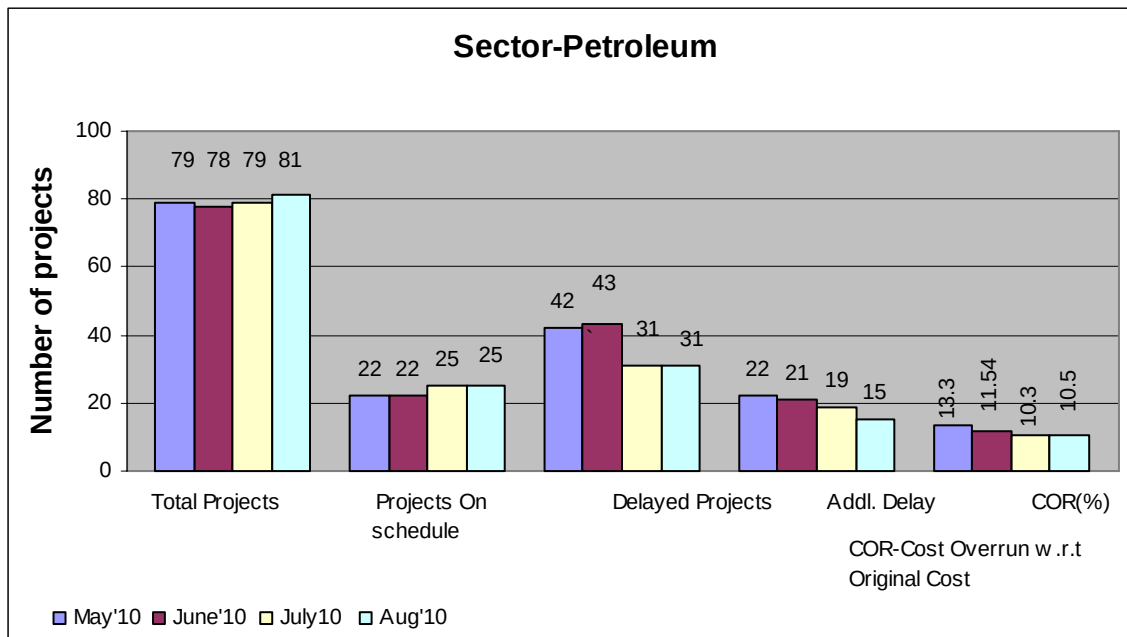

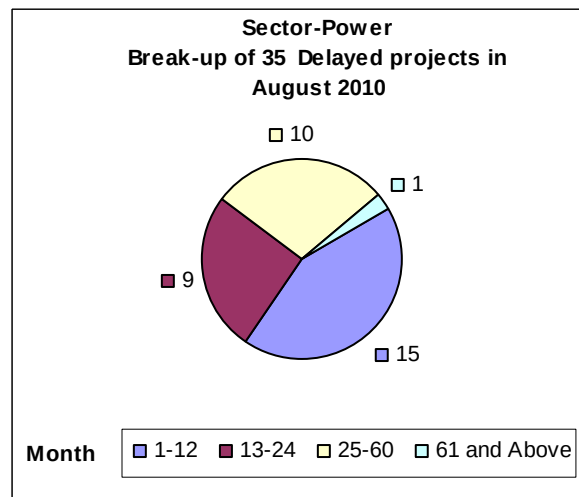
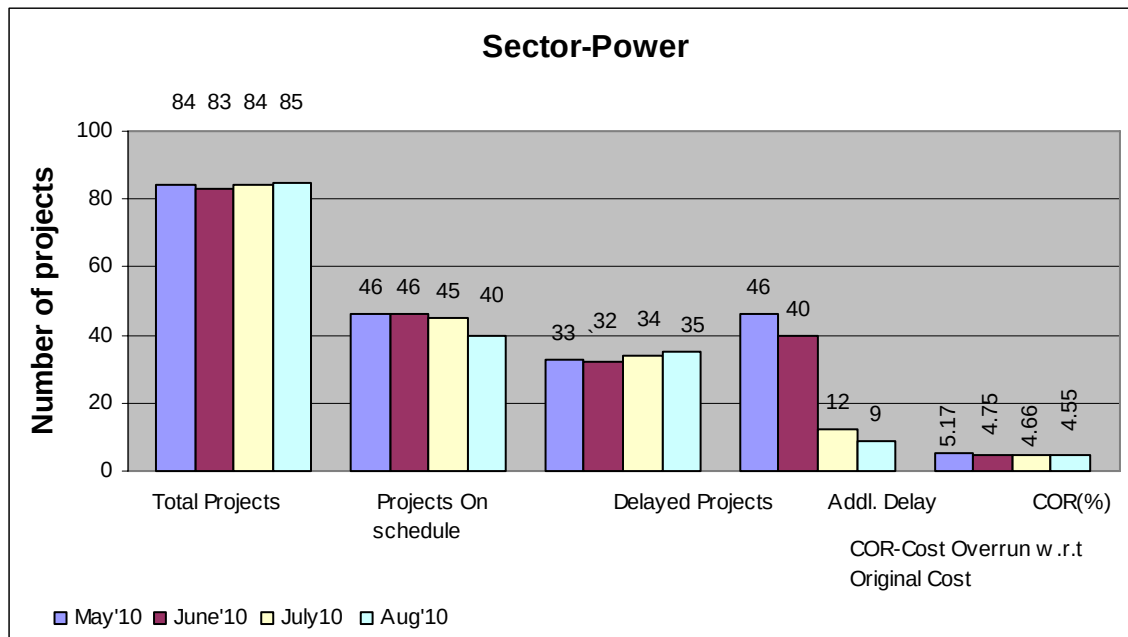


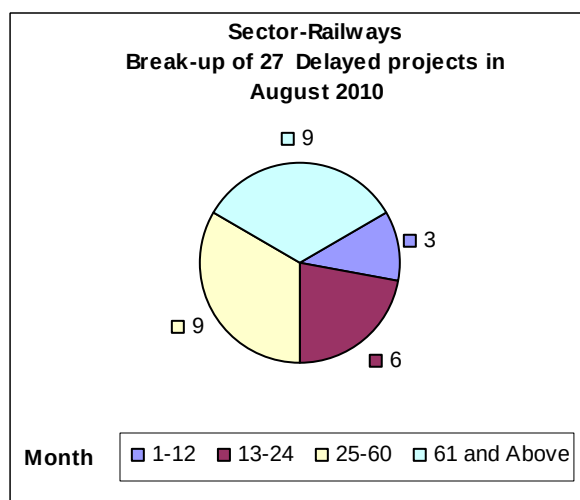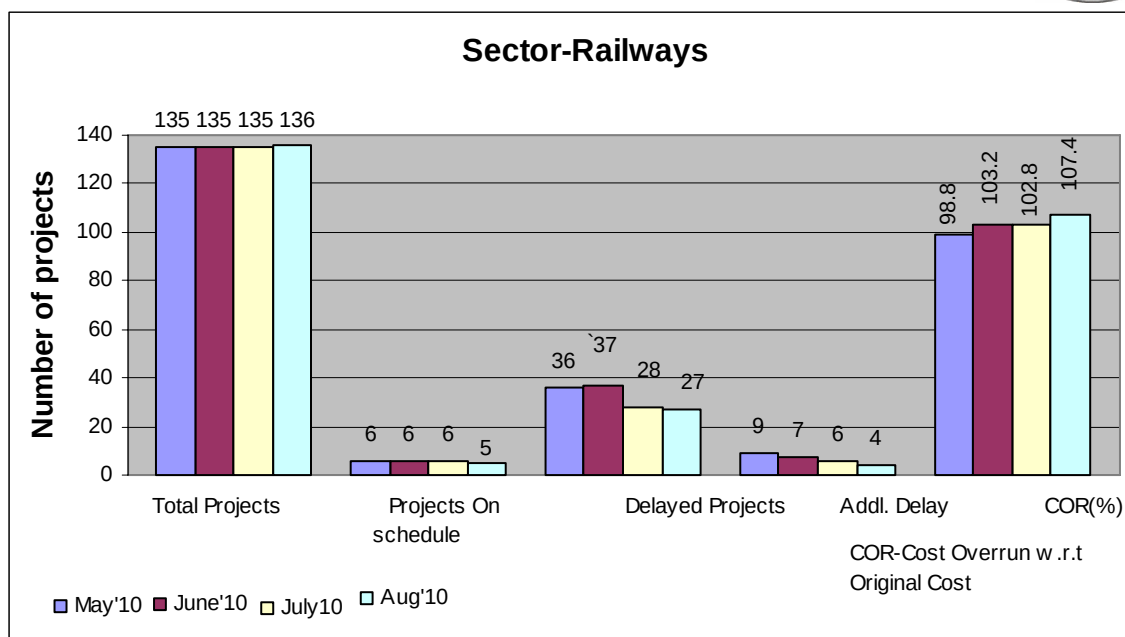

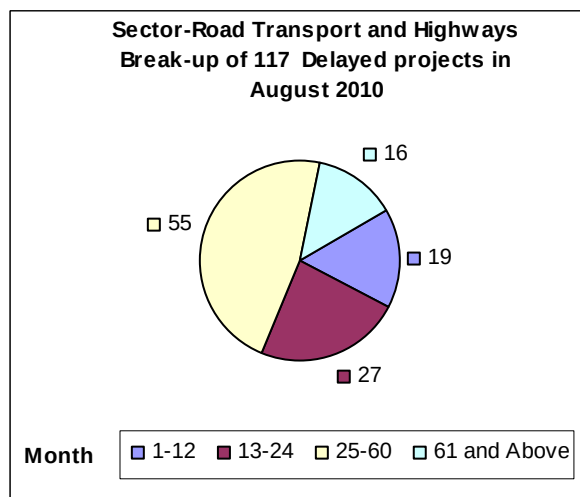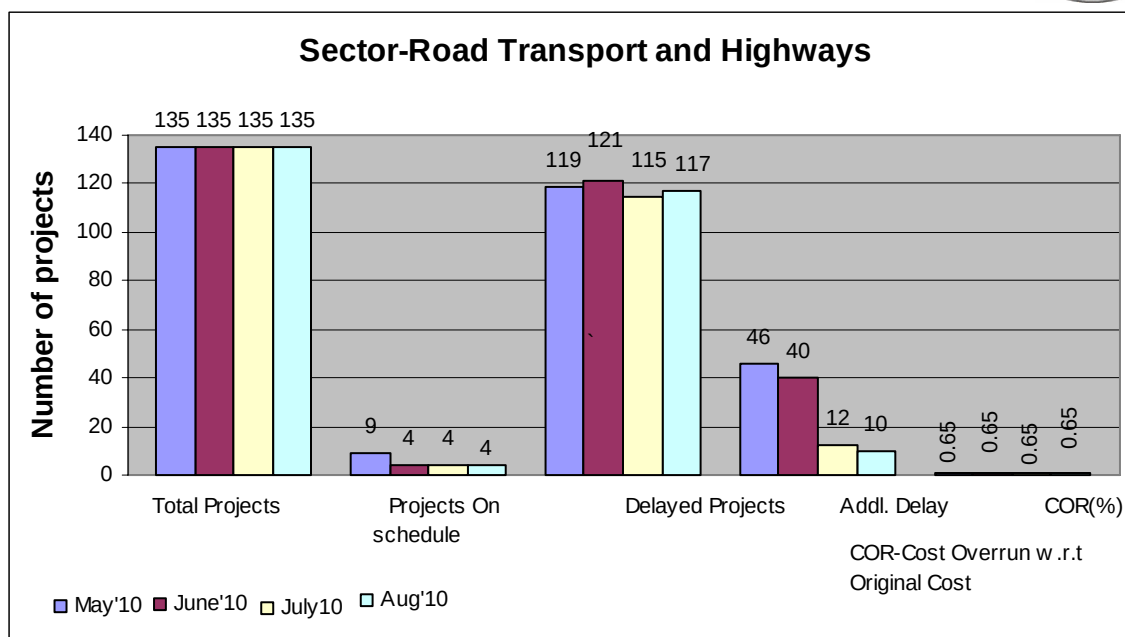


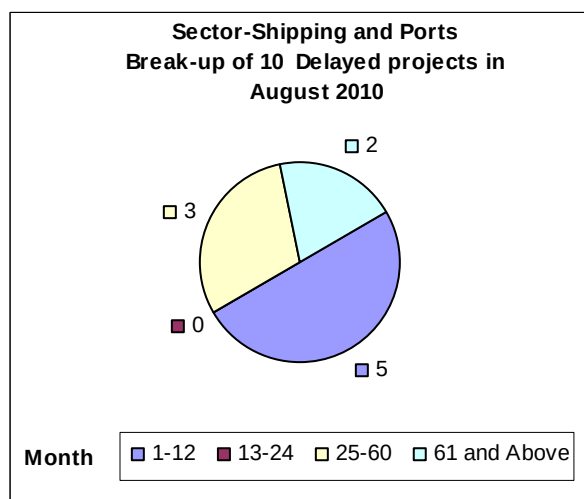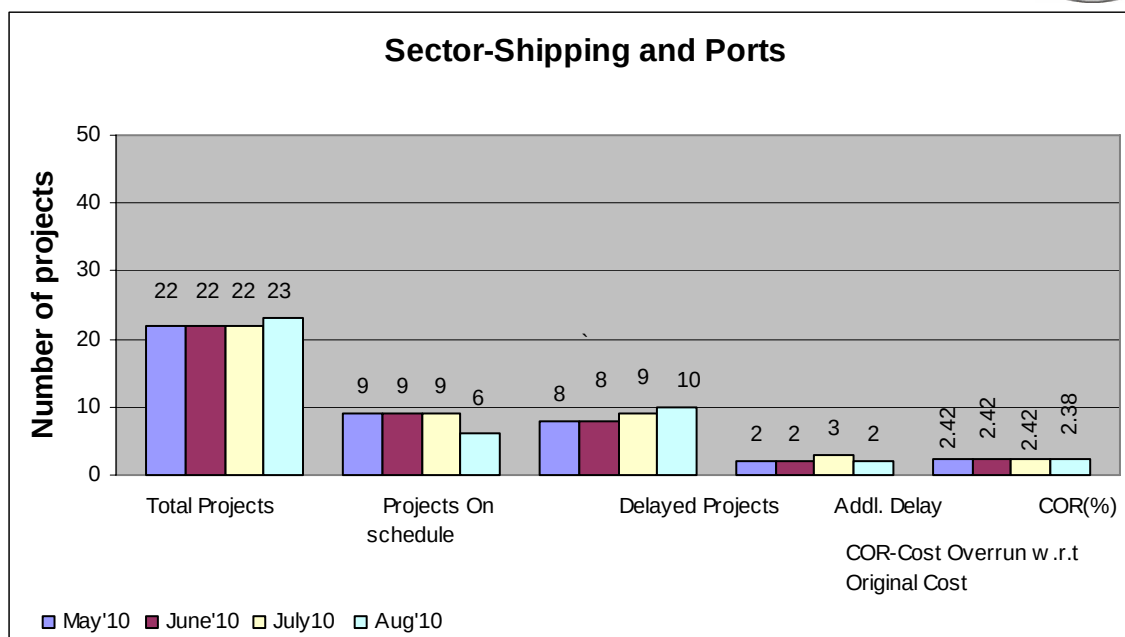




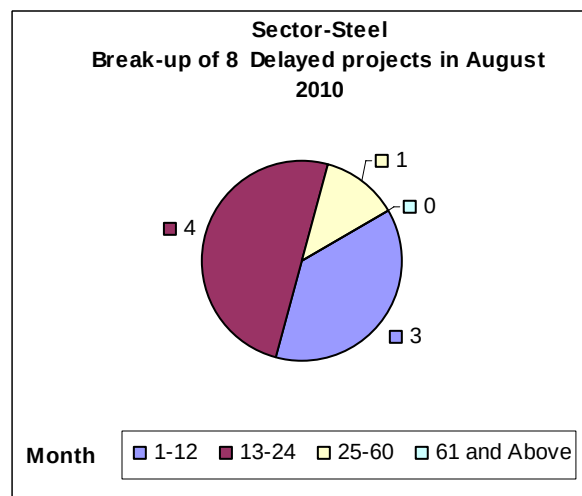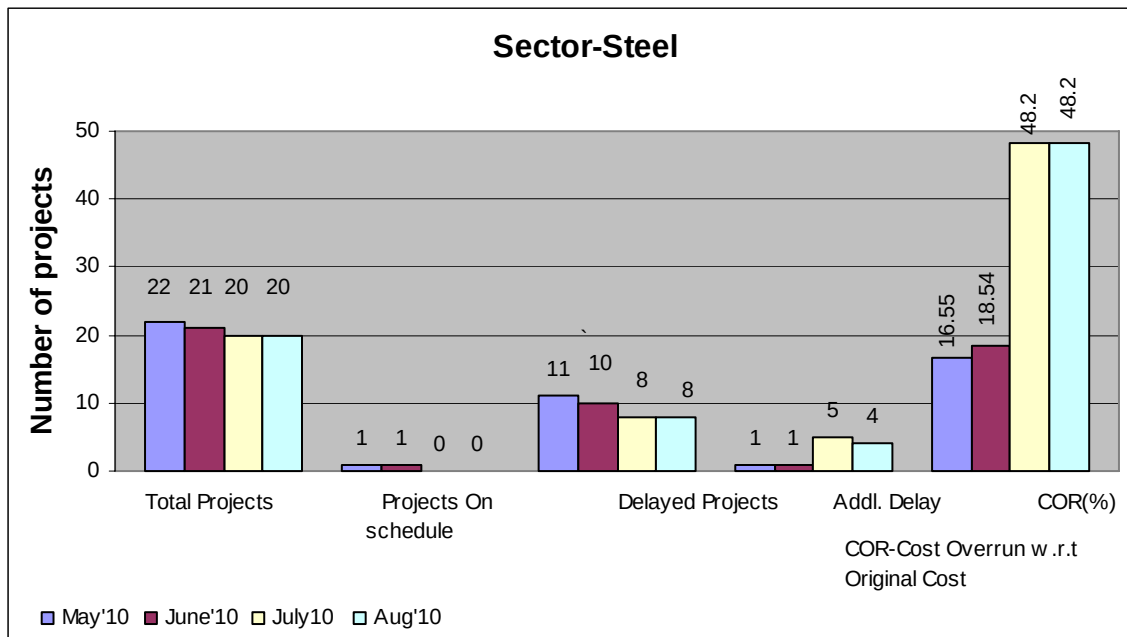

## Sector-Telecommunications

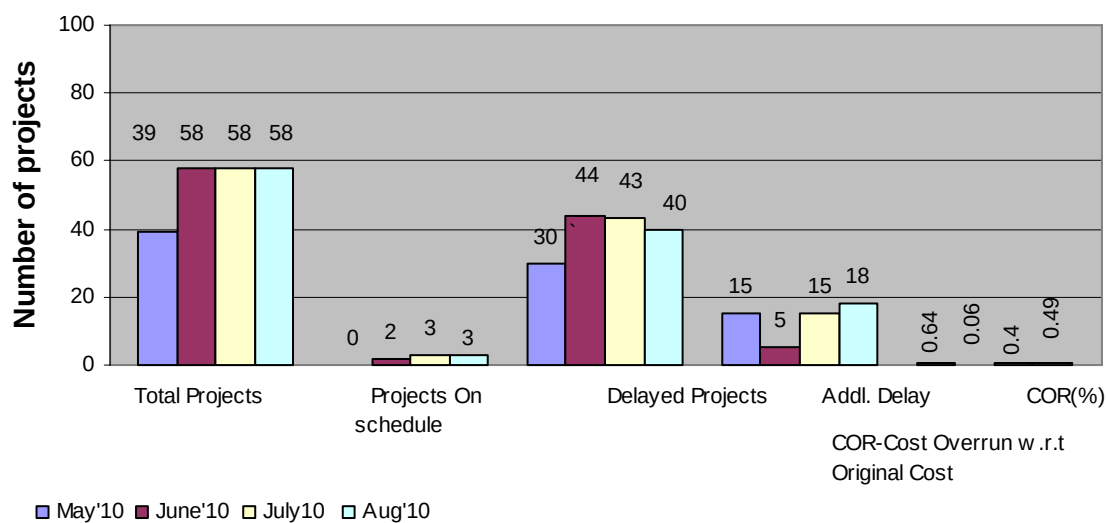

### Sector-Telecommunications Break-up of 40 Delayed projects in August 2010

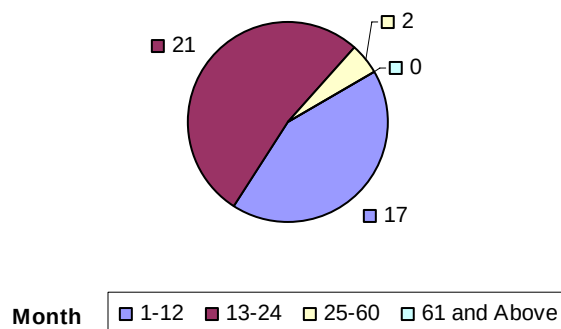

### Sectorwise analysis of projects

| Sector                    | Number of projects | Cost (Rs. Crore)  |                   |                   |
|---------------------------|--------------------|-------------------|-------------------|-------------------|
|                           |                    | Original          | Latest            | Anticipated       |
| Atomic Energy             | 4                  | 21,982.29         | 21,982.29         | 23,236.29         |
| Civil Aviation            | 9                  | 5,347.40          | 5,347.40          | 5,347.40          |
| Coal                      | 44                 | 25,571.91         | 28,907.40         | 29,059.39         |
| Fertilisers               | 6                  | 5,317.41          | 5,317.41          | 5,317.41          |
| Mines                     | 1                  | 4,091.51          | 4,091.51          | 4,091.51          |
| Steel                     | 20                 | 44,197.03         | 59,739.00         | 65,514.79         |
| Petroleum                 | 81                 | 171,218.11        | 185,137.97        | 189,247.41        |
| Power                     | 85                 | 179,619.98        | 180,539.03        | 187,805.89        |
| Health & Family Welfare   | 1                  | 71.18             | 422.60            | 443.15            |
| Railways                  | 136                | 51,111.74         | 57,075.65         | 106,031.66        |
| Road Transport & Highways | 135                | 41,863.55         | 41,863.55         | 42,136.98         |
| Shipping & Ports          | 23                 | 24,491.73         | 24,491.73         | 25,075.09         |
| Telecommunications        | 58                 | 27,020.91         | 27,179.96         | 27,154.89         |
| Urban Development         | 2                  | 15,071.00         | 16,763.36         | 30,503.36         |
| Water Resources           | 1                  | 542.90            | 542.90            | 1,187.00          |
| <b>Grand total</b>        | <b>606</b>         | <b>617,518.65</b> | <b>659,401.76</b> | <b>742,152.22</b> |

(Aug,2010)

| S.No                  | Project                                                                             | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|-----------------------|-------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                       |                                                                                     |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                     | 2                                                                                   | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| <u>Atomic Energy</u>  |                                                                                     |                  |                         |                  |                   |                       |             |                                   |                            |
| 1                     | KAIGA 3 and 4 UNITS (NPCIL) - [020100041]NPCIL,Karnataka                            | 05/2001          | 4,213.00                | 3,282.00         | 2,564.00          | 10/2009<br>09/2007    | 08/2010     | 35(R1)                            | 71/75                      |
| 2                     | URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]UCIL,Andhra Pradesh | 09/2007          | 1,106.29                | 1,106.29         | 732.55            | -                     | 04/2011     | -                                 | 0/1                        |
| 3                     | KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu                                | 12/2001          | 13,171.00               | 13,171.00        | 13,113.00         | 12/2008               | 06/2011     | 30(O)                             | 61/119                     |
| 4                     | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu    | 09/2003          | 3,492.00                | 5,677.00         | 2,592.29          | 09/2010               | 09/2011     | 12(O)                             | 8/80                       |
| Total                 |                                                                                     |                  | 21,982.29               | 23,236.29        | 19,001.84         |                       |             |                                   | 140/275                    |
| <u>Civil Aviation</u> |                                                                                     |                  |                         |                  |                   |                       |             |                                   |                            |
| 5                     | CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3 - [N04000068]AAI,Tamil Nadu      | 06/2009          | 213.35                  | 213.35           | 112.00            | 09/2010               | 11/2010     | 2(O)                              | 0/0                        |
| 6                     | D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA - [N04000040]AAI,Tamil Nadu      | 01/2008          | 535.00                  | 535.00           | 331.80            | 06/2010               | 12/2010     | 6(O)                              | 0/0                        |
| 7                     | D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE(K1) - [N04000038]AAI,Tamil Nadu  | 08/2008          | 1,273.00                | 1,273.00         | 418.29            | 01/2011               | 01/2011     | 0(O)                              | 0/0                        |
| 8                     | Extension of Secondary Runway(K2) - [N04000056]AAI,Tamil Nadu                       | 08/2008          | 230.00                  | 230.00           | 188.12            | 01/2011               | 01/2011     | 0(O)                              | 0/0                        |
| 9                     | C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal      | 08/2008          | 1,942.51                | 1,942.51         | 818.87            | 05/2011               | 08/2011     | 3(O)                              | 0/0                        |
| 10                    | Construction of New International Terminal Building - [N04000069]AAI,Goa            | 05/2010          | 204.73                  | 204.73           | 5.97              | 05/2012               | 05/2012     | 0(O)                              | 0/0                        |
| 11                    | CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BLDG. A - [N04000017]AAI,Gujarat         | 02/2007          | 290.92                  | 290.92           | 177.20            | -                     | -           | -                                 | 1/24                       |
| 12                    | C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim                  | 01/2009          | 264.29                  | 264.29           | 10.02             | 01/2011               | -           | -                                 | 0/0                        |
| 13                    | GAGAN PROJECT - [N04000065]AAI,Multi State                                          | 09/2008          | 393.60                  | 393.60           | 160.29            | 06/2013               | -           | -                                 | 0/0                        |
| Total                 |                                                                                     |                  | 5,347.40                | 5,347.40         | 2,222.56          |                       |             |                                   | 1/24                       |
| <u>Coal</u>           |                                                                                     |                  |                         |                  |                   |                       |             |                                   |                            |
| 14                    | BARSINGSAR TPS (2X125MW) (NLC) - [060100089]NLC,Rajasthan                           | 12/2004          | 1,114.18                | 1,626.09         | 1,471.94          | 06/2009               | 10/2010     | 16(O)                             | 59/26                      |
| 15                    | BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC) - [060100090]NLC,Rajasthan                  | 12/2004          | 254.07                  | 1,687.78         | 1,687.78          | 06/2009               | 10/2010     | 16(O)                             | 36/21                      |
| 16                    | BALRAM OCP EXTENSION - [N06000044]MCL,Orissa                                        | 12/2007          | 172.08                  | 172.08           | 484.92            | 03/2009               | 03/2011     | 24(O)                             | 0/0                        |

| S.No | Project                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|----------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                        |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                      | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 17   | TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu                  | 10/2004          | 2,030.78<br>2,453.57    | 2,453.57         | 2,011.28          | 06/2009<br>-          | 06/2011     | 24(O)                             | 41/24                      |
| 18   | KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL,Orissa                           | 01/2005          | 302.96<br>-             | 302.96           | 60.29             | 03/2010<br>-          | 03/2012     | 24(O)                             | 0/4                        |
| 19   | GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh                      | 07/2005          | 1,667.55<br>1,667.55    | 1,667.55         | 1,011.42          | 03/2010<br>-          | 03/2012     | 24(O)                             | 3/7                        |
| 20   | ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]CCL,Jharkhandd                                | 04/2006          | 471.66<br>341.63        | 341.63           | 101.73            | 03/2011<br>-          | 03/2012     | 12(O)                             | 0/0                        |
| 21   | SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh                        | 10/2006          | 249.03<br>-             | 249.03           | 37.64             | 03/2012<br>-          | 03/2012     | 0(O)                              | 8/42                       |
| 22   | NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh | 10/2007          | 529.40<br>-             | 259.40           | 0.63              | 03/2012<br>-          | 03/2012     | 0(O)                              | 0/0                        |
| 23   | ANANTA OC EXPANSION PH-III - [N06000067]MCL,Orissa                                     | 08/2008          | 207.28<br>-             | 207.28           | 255.66            | 03/2012<br>-          | 03/2012     | 0(O)                              | 0/0                        |
| 24   | RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh                            | 12/2009          | 418.57<br>-             | 418.97           | 92.97             | -<br>-                | 03/2012     | -                                 | 7/27                       |
| 25   | MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh                     | 03/2010          | 181.91<br>-             | 181.19           | 0.07              | -<br>-                | 03/2012     | -                                 | 2/34                       |
| 26   | North Urimari OCP - [N06000084]CCL,Jharkhandd                                          | 12/2007          | 179.87<br>-             | 179.87           | 64.95             | 03/2012<br>-          | 03/2012     | 0(O)                              | 0/0                        |
| 27   | Tapin OCP - [N06000086]CCL,Jharkhandd                                                  | 08/2008          | 264.68<br>-             | 264.68           | 71.90             | 03/2012<br>-          | 03/2012     | 0(O)                              | 0/0                        |
| 28   | TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu                            | 05/2008          | 4,904.54<br>-           | 4,904.54         | 971.86            | 08/2012<br>-          | 08/2012     | 0(O)                              | 0/0                        |
| 29   | ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh                                | 09/2006          | 212.34<br>779.26        | 779.26           | 128.78            | 03/2013<br>09/2012    | 09/2012     | 0(R3)                             | 2/22                       |
| 30   | KAKATIYA LAONGWALL - [N06000048]SCCL,Andhra Pradesh                                    | 12/2008          | 453.63<br>-             | 453.63           | 50.48             | -<br>12/2012          | 12/2012     | 0(R3)                             | 7/44                       |
| 31   | KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh                              | 05/2006          | 789.88<br>741.56        | 741.56           | 136.38            | 03/2010<br>-          | 03/2013     | 36(O)                             | 0/1                        |
| 32   | KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]SECL,Chhatisgarh                           | 06/2006          | 737.65<br>-             | 1,188.31         | 554.18            | 03/2011<br>03/2013    | 03/2013     | 0(R3)                             | 0/4                        |
| 33   | MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd                                            | 07/2006          | 469.78<br>-             | 706.40           | 16.23             | 07/2012<br>-          | 03/2013     | 8(O)                              | 0/1                        |
| 34   | JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh                                | 03/2013          | 467.78<br>-             | 467.78           | 11.40             | -<br>-                | 03/2013     | -                                 | 0/83                       |
| 35   | KANIHA OCP - [N06000035]MCL,Multi State                                                | 12/2007          | 457.77<br>-             | 457.77           | 51.42             | -<br>-                | 03/2013     | -                                 | 0/2                        |
| 36   | HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]MCL,Orissa                              | 11/2008          | 475.93<br>-             | 479.53           | 212.54            | 03/2013<br>-          | 03/2013     | 0(O)                              | 0/0                        |
| 37   | Churi Benti UG - [N06000083]CCL,Jharkhandd                                             | 06/2007          | 163.51<br>-             | 163.51           | 33.46             | 03/2011<br>-          | 03/2013     | 24(O)                             | 0/0                        |
| 38   | Purnadih OCP - [N06000085]CCL,Jharkhandd                                               | 07/2008          | 210.98<br>-             | 210.98           | 20.05             | 03/2013<br>-          | 03/2013     | 0(O)                              | 0/0                        |
| 39   | DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]SECL,Chhatisgarh                      | 07/2005          | 1,268.53<br>1,943.60    | 1,943.66         | 887.03            | 03/2010<br>-          | 03/2014     | 48(O)                             | 2/6                        |

| S.No        | Project                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |         |
|-------------|----------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|---------|
|             |                                                                                        |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |         |
| 1           | 2                                                                                      | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |         |
| 40          | BINA EXTN. PROJ -<br>[N06000019]NCL,Multi State                                        | 11/2006          | 168.97<br>168.97        | 168.97           | 137.83            | 03/2014<br>-          | 03/2014     | 0(O)                              | 1/1                        |         |
| 41          | CHURCHA UG -<br>[N06000046]SECL,Chhatisgarh                                            | 06/2008          | 462.35<br>462.35        | 462.35           | 247.25            | 06/2014<br>-          | 03/2014     | -3(O)                             | 0/0                        |         |
| 42          | RAJMAHAL OC EXP. -<br>[N06000056]ECL,Jharkhandd                                        | 02/2006          | 50.08<br>153.82         | 153.82           | 14.77             | 03/2010<br>03/2014    | 03/2014     | 0(R3)                             | 0/0                        |         |
| 43          | PENGANGA OC -<br>[N06000066]WCL,Andhra Pradesh                                         | 10/2008          | 339.77<br>-             | 339.77           | -                 | -<br>-                | 03/2014     | -                                 | 0/1                        |         |
| 44          | KARTALI (EAST) OC -<br>[N06000076]SECL,Chhatisgarh                                     | 07/2008          | 178.44<br>-             | 178.44           | -                 | 03/2014<br>-          | 03/2014     | 0(O)                              | 0/0                        |         |
| 45          | MANIKPUR OC EXPANTION -<br>[N06000081]SECL,Chhatisgarh                                 | 11/2009          | 321.42<br>-             | 321.50           | 211.51            | 03/2013<br>-          | 03/2014     | 12(O)                             | 0/0                        |         |
| 46          | BLOCK-B OCP NCL (3.5 MTY) -<br>[N06000009]NCL,Madhya pradesh                           | 06/2006          | 746.04<br>-             | 437.34           | 136.51            | 03/2012<br>-          | 03/2015     | 36(O)                             | 0/1                        |         |
| 47          | JHANJRA LONGWAL UG PHASE II -<br>[N06000020]ECL,West Bengal                            | 11/2006          | 287.18<br>-             | 287.17           | -                 | 11/2009<br>-          | 03/2015     | 64(O)                             | 0/0                        |         |
| 48          | GOPAL PRASAD OCP -<br>[N06000042]MCL,Orissa                                            | 02/2008          | 395.87<br>-             | 395.87           | 24.33             | 03/2013<br>-          | 03/2015     | 24(O)                             | 0/0                        |         |
| 49          | PELMA OC -<br>[N06000045]SECL,Chhatisgarh                                              | 07/2008          | 448.32<br>-             | 448.32           | -                 | 03/2012<br>-          | 03/2015     | 36(O)                             | 0/0                        |         |
| 50          | Batura OC - [N06000049]BCCL,Madhya pradesh                                             | 09/2008          | 203.82<br>-             | 203.82           | -                 | 03/2013<br>-          | 03/2015     | 24(O)                             | 0/0                        |         |
| 51          | JAGANNATHPOR OC -<br>[N06000075]SECL,Chhatisgarh                                       | 09/2008          | 152.43<br>-             | 152.43           | -                 | 03/2015<br>-          | 03/2015     | 0(O)                              | 0/0                        |         |
| 52          | RKP OCP PHASE-I -<br>[N06000079]SCCL,Uttaranchal                                       | 03/2010          | 201.58<br>209.78        | 209.78           | 0.18              | -<br>-                | 03/2015     | -                                 | 0/31                       |         |
| 53          | AMLOHRI EPR (NCL) (6 MTY) -<br>[N06000010]NCL,Madhya pradesh                           | 05/2006          | 1,352.04<br>1,143.54    | 1,143.54         | 27.32             | 03/2014<br>-          | 03/2016     | 24(O)                             | 1/1                        |         |
| 54          | BHUBANESWARI OCP -<br>[N06000034]MCL,Orissa                                            | 12/2007          | 490.10<br>-             | 490.10           | 57.71             | 03/2014<br>-          | 03/2016     | 24(O)                             | 0/0                        |         |
| 55          | TALABIRA OCP -<br>[N06000043]MCL,Orissa                                                | 03/2008          | 447.72<br>-             | 447.72           | 6.04              | 03/2015<br>-          | 03/2016     | 12(O)                             | 0/0                        |         |
| 56          | AMLAI OC EXPANSION SECTOR 'B' (1.50 MTY) -<br>[N06000082]SECL,Chhatisgarh              | 11/2009          | 158.59<br>-             | 198.59           | 91.67             | 03/2016<br>-          | 03/2016     | 0(O)                              | 0/0                        |         |
| 57          | Rajrappa RCE OCP -<br>[N06000087]CCL,Jharkhandd                                        | 12/2009          | 510.85<br>-             | 510.85           | 290.79            | 03/2016<br>-          | 03/2016     | 0(O)                              | 0/0                        |         |
| Total       |                                                                                        |                  | 25,571.91<br>-          | 29,059.39        | 11,672.90         |                       |             |                                   |                            | 169/383 |
| Fertilisers |                                                                                        |                  |                         |                  |                   |                       |             |                                   |                            |         |
| 58          | THAL AMMONIA REVAMP PROJECT -<br>[N08000003]RCF,Haryana                                | 01/2009          | 488.75<br>-             | 488.75           | 110.69            | -<br>-                | 03/2011     | -                                 | 0/22                       |         |
| 59          | CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS -<br>[N08000007]FACT,Madhya pradesh          | 09/2008          | 325.00<br>-             | 325.00           | -                 | 07/2011<br>-          | 07/2011     | 0(O)                              | 0/0                        |         |
| 60          | CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ -<br>[N08000008]FACT,Madhya pradesh | 09/2008          | 438.00<br>-             | 438.00           | -                 | 07/2011<br>-          | 07/2011     | 0(O)                              | 0/0                        |         |
| 61          | PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJE -<br>[N08000004]NFL,Haryana         | 01/2010          | 1,292.84<br>-           | 1,292.84         | -                 | -<br>-                | 10/2012     | -                                 | 0/5                        |         |

| S.No | Project                                                                                     | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|---------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                             |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                           | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 62   | BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJ - [N08000005]FACT,Punjab                 | 01/2010          | 1,294.19                | 1,294.19         | -                 | -                     | 10/2012     | -                                 | 0/5                        |
| 63   | NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]FACT,Punjab                           | 01/2010          | 1,478.63                | 1,478.63         | -                 | -                     | 10/2012     | -                                 | 0/8                        |
|      | <b>Total</b>                                                                                |                  | 5,317.41                | 5,317.41         | 110.69            |                       |             |                                   | 0/40                       |
|      | <b>Mines</b>                                                                                |                  |                         |                  |                   |                       |             |                                   |                            |
| 64   | SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM,SMELTER AND POWE - [100100054]NALCO,Orissa      | 10/2004          | 4,091.51                | 4,091.51         | 3,316.00          | 12/2008               | -           | -                                 | 18/111                     |
|      | <b>Total</b>                                                                                |                  | 4,091.51                | 4,091.51         | 3,316.00          |                       |             |                                   | 18/111                     |
|      | <b>Steel</b>                                                                                |                  |                         |                  |                   |                       |             |                                   |                            |
| 65   | POWER PLANT-I - [N12000039]RINL,Andhra Pradesh                                              | 09/2007          | 462.00                  | 350.00           | 84.40             | 12/2009               | 08/2010     | 8(O)                              | 0/0                        |
| 66   | 330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh                      | 07/2007          | 260.00                  | 353.00           | 80.00             | 02/2010               | 08/2010     | 6(O)                              | 0/0                        |
| 67   | REBUILDING OF BLAST FURNANCE NO.2(BOKARO STEEL PL - [N12000035]SAIL,Jharkhandd              | 10/2007          | 892.32                  | 892.32           | 616.57            | -                     | 07/2010     | -                                 | 2/1                        |
| 68   | REBUILDING OF COKE OVEN BATTERY-10 - [N12000016]SAIL,West Bengal                            | 03/2007          | 416.50                  | 436.54           | 301.73            | -                     | 08/2010     | -                                 | 2/1                        |
| 69   | INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA - [N12000025]SAIL,Orissa                     | 07/2007          | 302.70                  | 302.70           | 240.43            | 06/2009               | 09/2010     | 15(O)                             | 0/0                        |
| 70   | SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II - [N12000036]SAIL,Orissa                    | 01/2008          | 197.66                  | 197.66           | 125.03            | -                     | 09/2010     | -                                 | 0/0                        |
| 71   | EXPANSION OF SALEM STEEL PLANT - [N12000050]SAIL,Tamil Nadu                                 | 01/2008          | 1,902.00                | 1,902.00         | 1,651.61          | -                     | 09/2010     | -                                 | 2/6                        |
| 72   | REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]SAIL,Jharkhandd                     | 07/2008          | 172.78                  | 172.78           | 104.15            | -                     | 11/2010     | -                                 | 0/1                        |
| 73   | 67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh            | 07/2007          | 230.00                  | 358.00           | 114.32            | 02/2010               | 01/2011     | 11(O)                             | 0/0                        |
| 74   | Rebuilding of coke oven battery No.1 & 2 (Bokaro S - [N12000033]SAIL,Jharkhandd             | 10/2007          | 500.90                  | 500.90           | 210.23            | -                     | 04/2011     | -                                 | 0/2                        |
| 75   | 700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Madhya pradesh   | 07/2007          | 111.28                  | 232.93           | 60.62             | -                     | 05/2011     | -                                 | 0/1                        |
| 76   | EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh | 10/2005          | 8,692.00                | 12,228.00        | 6,203.00          | 10/2009               | 06/2011     | 20(O)                             | 0/126                      |
| 77   | COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh                           | 08/2007          | 108.00                  | 168.95           | 12.00             | 10/2009               | 06/2011     | 20(O)                             | 0/0                        |

| S.No             | Project                                                                                     | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------------------|---------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                  |                                                                                             |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                | 2                                                                                           | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 78               | EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal                               | 02/2008          | 14,443.00<br>-          | 14,443.00        | 8,292.02          | -<br>-                | 06/2011     | -                                 | 0/6                        |
| 79               | Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL, Andhra Pradesh                  | 05/2008          | 480.00<br>-             | 480.84           | 4.04              | 09/2010<br>-          | 12/2011     | 15(O)                             | 0/0                        |
| 80               | EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, Jharkhand                                | 01/2008          | 3,316.00<br>6,325.00    | 6,325.00         | 1,235.63          | -<br>12/2011          | 12/2011     | 0(R3)                             | 0/7                        |
| 81               | EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, Orissa                                 | 09/2008          | 6,133.00<br>-           | 8,128.00         | 2,506.34          | 02/2011<br>-          | 03/2013     | 25(O)                             | 0/0                        |
| 82               | EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhattisgarh                             | 09/2008          | 5,185.00<br>17,265.00   | 17,265.00        | 1,241.83          | -<br>03/2013          | 03/2013     | 0(R3)                             | 0/8                        |
| 83               | Deve. of Bailadila Iron Ore Deposit-II(B)(NMDC) - [N12000018]NMDC, Andhra Pradesh           | 01/2003          | 295.89<br>607.17        | 607.17           | 220.32            | -<br>-                | -           | -                                 | 2/21                       |
| 84               | AIR SEPARATION PLANT (ASU-4) - [N12000060]RINL, Andhra Pradesh                              | 03/2008          | 96.00<br>-              | 170.00           | 42.02             | 06/2010<br>-          | -           | -                                 | 0/0                        |
|                  | <b>Total</b>                                                                                |                  | 44,197.03<br>-          | 65,514.79        | 23,346.29         |                       |             |                                   | 8/180                      |
| <b>Petroleum</b> |                                                                                             |                  |                         |                  |                   |                       |             |                                   |                            |
| 85               | SINGLE POINT MOORING PROJECT AT VISAKHAPATNAM - [N16000067]HPCL, Andhra Pradesh             | 11/2008          | 643.46<br>-             | 643.46           | 489.52            | -<br>-                | 05/2010     | -                                 | 0/2                        |
| 86               | DADRI- PANIPAT R-LNG SPUR PIPELINE - [N16000018]IOCL, Haryana                               | 06/2005          | 250.66<br>-             | 389.00           | 350.96            | 06/2008<br>-          | 07/2010     | 25(O)                             | 0/0                        |
| 87               | INST. OF FACILITIES FOR IMPROVEMENT IN DIESEL QUALITY (IOCL) - [160100289]IOCL, West Bengal | 11/2005          | 1,876.00<br>2,869.00    | 3,154.00         | 2,736.14          | 04/2009<br>12/2009    | 02/2010     | 2(R1)                             | 41/36                      |
| 88               | CHAINS- JHAJJAR PIPE LINE PROJECT - [N16000047]GAIL, Haryana                                | 11/2007          | 967.77<br>-             | 571.64           | 416.90            | 09/2009<br>-          | 03/2010     | 6(O)                              | 0/0                        |
| 89               | BINA DESPATCH TERMINAL - [N16000078]BPCL, Madhya Pradesh                                    | 05/2007          | 490.71<br>639.11        | 639.11           | 581.93            | 12/2009<br>03/2010    | 03/2010     | 0(R3)                             | 0/0                        |
| 90               | LUBE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI REFINERY - [N16000026]HPCL, Maharashtra   | 10/2006          | 638.90<br>1,030.00      | 1,030.00         | 748.41            | 04/2009<br>-          | 07/2010     | 15(O)                             | 0/0                        |
| 91               | SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL) - [N16000049]GAIL, Multi State      | 11/2007          | 396.13<br>-             | 396.13           | 185.56            | 10/2009<br>06/2010    | 09/2010     | 3(R3)                             | 0/0                        |
| 92               | CAPACITY EXP. CUM MODERNISATION PH-II - [N16000080]BPCL, Kerala                             | 09/2009          | 2,591.80<br>3,941.41    | 3,941.41         | 2,720.30          | 12/2009<br>-          | 09/2010     | 9(O)                              | 0/0                        |
| 93               | C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]ONGC, Gujarat                    | 12/2003          | 900.92<br>-             | 1,493.49         | 714.62            | 06/2006<br>07/2010    | 10/2010     | 3(R3)                             | 0/2                        |
| 94               | DIESEL HYDRO TREATMENT PROJECT, BRPL DHALGAON - [N16000009]BRPL, Assam                      | 06/2006          | 1,431.91<br>1,646.39    | 1,676.00         | 1,421.01          | 09/2009<br>-          | 10/2010     | 13(O)                             | 0/0                        |
| 95               | EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTPA - [N16000017]IOCL, Haryana                | 06/2005          | 1,007.83<br>-           | 1,087.00         | 773.91            | 12/2009<br>12/2009    | 10/2010     | 10(R1)                            | 18/49                      |



| S.No | Project                                                                                  | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                          |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                        | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 96   | MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY - [N16000036]IOCL,Assam                     | 04/2008          | 372.00                  | 325.00           | 215.62            | 02/2010               | 10/2010     | 8(O)                              | 0/0                        |
| 97   | MSQ UPGRADATION PROJECT AT DIGBOI REFINERY - [N16000037]IOCL,Assam                       | 04/2008          | 356.00                  | 300.00           | 203.83            | 02/2010               | 10/2010     | 8(O)                              | 0/0                        |
| 98   | MSQ UPGRADATION PROJECT AT BARAUNI REFINERY - [N16000038]IOCL,Bihar                      | 04/2008          | 1,492.00                | 1,505.00         | 997.58            | 04/2010               | 10/2010     | 6(O)                              | 0/0                        |
| 99   | MSQ IMPROVMENT PROJECT - [N16000040]BRPL,Assam                                           | 04/2008          | 293.60                  | 293.60           | 179.45            | 12/2009               | 10/2010     | 10(O)                             | 0/0                        |
| 100  | VIJAPUR DADRI-BAWANA PIPE LINE PROJECT - [N16000048]GAIL,Multi State                     | 11/2007          | 5,595.31<br>4,262.00    | 4,262.00         | 3,260.61          | 11/2009<br>04/2010    | 10/2010     | 6(R3)                             | 0/0                        |
| 101  | JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana                               | 11/2007          | 281.07                  | 281.07           | 1.13              | 10/2010               | 10/2010     | 0(O)                              | 0/0                        |
| 102  | COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]GAIL,Multi State          | 11/2007          | 1,512.00<br>1,434.00    | 1,434.00         | 635.39            | -<br>04/2011          | 10/2010     | -6(R3)                            | 0/2                        |
| 103  | INSTALLATION OF FCCV AT MUMBAI REFINERY - [N16000056]HPCL,Maharashtra                    | 03/2007          | 900.47                  | 900.47           | -                 | 09/2009               | 10/2010     | 13(O)                             | 0/0                        |
| 104  | RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT - [N16000021]IOCL,Gujarat             | 01/2007          | 5,693.00<br>6,898.00    | 6,898.00         | 5,625.54          | 01/2010<br>06/2010    | 11/2010     | 5(R3)                             | 0/0                        |
| 105  | Guru Govind Singh Refinery Products Evacuation Project - [N16000076]HPCL,Punjab          | 01/2009          | 605.40<br>605.40        | 605.40           | 246.17            | 12/2010<br>12/2010    | 12/2010     | 0(R3)                             | 12/17                      |
| 106  | REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra                           | 06/2008          | 304.40                  | 304.40           | 120.30            | 12/2010               | 12/2010     | 0(O)                              | 0/0                        |
| 107  | Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar          | 06/2009          | 613.54                  | 727.88           | 5.58              | 12/2010               | 12/2010     | 0(O)                              | 0/0                        |
| 108  | KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- [N16000070]GAIL,Multi State | 07/2009          | 238.68<br>196.25        | 196.25           | 2.28              | -<br>-                | 01/2011     | -                                 | 1/8                        |
| 109  | CAPACITY AUGMENTATION OF AGRA& FERAZABAD REGION - [N16000074]GAIL,Uttar Pradesh          | 07/2009          | 199.57                  | 199.57           | 19.55             | -<br>-                | 01/2011     | -                                 | 9/7                        |
| 110  | CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu              | 01/2008          | 224.00                  | 224.00           | 111.22            | 12/2010<br>02/2011    | 02/2011     | 0(R3)                             | 0/0                        |
| 111  | IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam                                     | 09/2001          | 345.10                  | 600.00           | 542.47            | 03/2007               | 03/2011     | 48(O)                             | 3/3                        |
| 112  | IOR GELEKI (ONGCL) - [160100216]ONGC,Assam                                               | 09/2001          | 390.09<br>834.90        | 1,200.00         | 1,124.74          | 03/2007               | 03/2011     | 48(O)                             | 6/6                        |
| 113  | IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam                                          | 09/2001          | 113.90                  | 219.22           | -                 | 03/2006               | 03/2011     | 60(O)                             | 6/6                        |
| 114  | DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra                             | 08/2006          | 3,195.16                | 2,800.00         | 2,520.63          | 12/2008<br>12/2008    | 03/2011     | 27(R3)                            | 0/0                        |
| 115  | HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra               | 09/2006          | 2,305.30                | 2,305.30         | 2,061.12          | 06/2010<br>06/2010    | 03/2011     | 9(R3)                             | 0/0                        |

| S.No | Project                                                                                    | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|--------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                            |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                          | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 116  | NORTH TAPTI GAS FIELD DEV. - [N16000085]ONGC,Gujarat                                       | 07/2008          | 589.70                  | 589.70           | -                 | 03/2011               | 03/2011     | 0(O)                              | 0/0                        |
| 117  | North Tapti Gas Field Development - [N16000096]ONGC,Multi State                            | 01/2010          | 589.70<br>755.56        | 755.56           | 13.53             | 03/2011               | 03/2011     | 0(O)                              | 0/0                        |
| 118  | BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL,Multi State                              | 10/2010          | 1,816.07<br>1,816.07    | 1,816.07         | 368.93            | -<br>04/2011          | 04/2011     | 0(R3)                             | 0/2                        |
| 119  | DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) - [N16000052]GAIL,Gujarat                       | 11/2007          | 4,429.38<br>4,403.00    | 2,800.00         | 1,475.72          | -<br>04/2011          | 04/2011     | 0(R3)                             | 0/2                        |
| 120  | COMPRESSOR STATIONS (KAILARAS &CHAINS) - [N16000054]GAIL,Multi State                       | 11/2007          | 1,061.93<br>1,167.00    | 1,167.00         | 22.36             | -<br>04/2011          | 04/2011     | 0(R3)                             | 0/2                        |
| 121  | HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra                                         | 05/2008          | 706.70                  | 706.70           | 450.38            | 04/2010               | 04/2011     | 12(O)                             | 0/0                        |
| 122  | NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra                                        | 05/2008          | 305.08                  | 305.08           | 69.38             | 04/2011               | 04/2011     | 0(O)                              | 0/0                        |
| 123  | INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State                       | 04/2003          | 429.82<br>2,218.01      | 2,218.01         | 1,234.69          | 03/2005<br>05/2011    | 05/2011     | 0(R3)                             | 0/0                        |
| 124  | REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra                        | 05/2008          | 333.40                  | 330.40           | 0.39              | 05/2010               | 05/2011     | 12(O)                             | 0/0                        |
| 125  | MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra                                        | 05/2008          | 175.21                  | 162.12           | 58.19             | 03/2009               | 05/2011     | 26(O)                             | 0/0                        |
| 126  | BNPL SPURLINE (UTTRANCHAL & PUNJAB) - [N16000094]GAIL,Multi State                          | 12/2009          | 540.92                  | 540.92           | 0.13              | -                     | 05/2011     | -                                 | 7/9                        |
| 127  | VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State | 12/2009          | 463.32                  | 463.32           | 0.13              | -                     | 06/2011     | -                                 | 3/9                        |
| 128  | Construction of Tank and Blending Facility at Vadi - [N16000075]IOCL,Gujarat               | 02/2009          | 267.00                  | 267.00           | 72.99             | -                     | 08/2011     | -                                 | 0/1                        |
| 129  | DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh            | 03/2009          | 3,597.00                | 3,597.00         | 113.50            | 09/2011               | 09/2011     | 0(O)                              | 0/0                        |
| 130  | DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra               | 03/2009          | 3,284.00                | 3,284.00         | -                 | 09/2011               | 09/2011     | 0(O)                              | 0/0                        |
| 131  | RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]HPCL,Andhra Pradesh              | 01/2009          | 756.00                  | 756.00           | 420.12            | 12/2011               | 12/2011     | 0(O)                              | 0/0                        |
| 132  | BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat                    | 02/2009          | 349.00                  | 349.00           | 40.73             | 08/2011               | 12/2011     | 4(O)                              | 0/0                        |
| 133  | HYDROCRACKER REVAMP & SETTING - [N16000081]BPCL,Maharashtra                                | 02/2008          | 825.00                  | 825.00           | 72.80             | 12/2011               | 12/2011     | 0(O)                              | 0/0                        |
| 134  | CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State              | 06/2007          | 736.65                  | 736.65           | 154.37            | 12/2011               | 12/2011     | 0(O)                              | 0/0                        |
| 135  | ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State                                 | 01/2010          | 2,163.64                | 2,163.64         | -                 | 12/2011               | 12/2011     | 0(O)                              | 0/0                        |

| S.No | Project                                                                                      | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|----------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                              |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                            | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 136  | Additional Development of D-1 Field - [N16000097]ONGC,Multi State                            | 01/2010          | 2,163.64                | 2,163.64         | 61.29             | 12/2011               | 12/2011     | 0(O)                              | 0/0                        |
| 137  | OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra         | 01/2007          | 740.02                  | 740.02           | 411.41            | 03/2010<br>03/2012    | 03/2012     | 0(R1)                             | 0/0                        |
| 138  | JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Gujarat                         | 07/2009          | 7,596.18                | 6,652.22         | 0.65              | 01/2013               | 03/2012     | -10(O)                            | 0/0                        |
| 139  | Integrated offshore crude Oil handling facilities at Paradip - [N16000090]IOCL,Maharashtra   | 12/2009          | 1,492.33                | 1,492.33         | 22.57             | 06/2012               | 03/2012     | -3(O)                             | 0/0                        |
| 140  | ASSAM GAS CRACKER PROJECT - [N16000100]BCPL,Assam                                            | 04/2006          | 5,460.61                | 5,460.61         | 954.64            | 04/2012               | 04/2012     | 0(O)                              | 0/0                        |
| 141  | Assam gas Cracker project - [N16000106]BCPL,Assam                                            | 04/2006          | 5,460.61                | 5,460.61         | -                 | 04/2012               | 04/2012     | 0(O)                              | 0/0                        |
| 142  | CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra                        | 01/2007          | 2,853.29                | 6,326.40         | 1,018.44          | 05/2010               | 05/2012     | 24(O)                             | 0/0                        |
| 143  | DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra                             | 01/2007          | 1,552.63<br>2,920.82    | 2,920.82         | 88.82             | 02/2009<br>09/2010    | 05/2012     | 20(R1)                            | 0/0                        |
| 144  | DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra                              | 06/2007          | 1,436.21                | 1,436.21         | -                 | 07/2010               | 05/2012     | 22(O)                             | 0/0                        |
| 145  | DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra                            | 06/2007          | 3,248.78<br>5,633.44    | 5,633.44         | 26.94             | 03/2010<br>08/2010    | 06/2012     | 22(R1)                            | 0/0                        |
| 146  | ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat                       | 02/2008          | 370.11                  | 370.11           | 8.53              | 04/2011               | 07/2012     | 15(O)                             | 0/0                        |
| 147  | Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura              | 07/2008          | 288.04<br>288.04        | 288.04           | -                 | 08/2012               | 08/2012     | 0(O)                              | 0/0                        |
| 148  | MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra                         | 01/2009          | 6,855.93                | 6,855.93         | 632.36            | 09/2012               | 09/2012     | 0(O)                              | 0/0                        |
| 149  | Paradip-Raipur-Sambalpur Ranchi Pipeline - [N16000088]IOCL,Maharashtra                       | 08/2009          | 1,793.00                | 1,793.00         | 9.39              | 09/2012               | 09/2012     | 0(O)                              | 0/0                        |
| 150  | Construction of six Effluent Treatment Plants (ETP) - [N16000099]ONGC,Gujarat                | 03/2009          | 234.78<br>234.78        | 234.78           | -                 | 09/2012               | 09/2012     | 0(O)                              | 0/0                        |
| 151  | PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa                                            | 02/2009          | 29,777.00               | 29,777.00        | 4,005.01          | -                     | 11/2012     | -                                 | 0/82                       |
| 152  | KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJECT PHASE-I - [N16000071]GAIL,Uttar Pradesh | 06/2009          | 3,032.00<br>348.00      | 348.00           | 6.55              | -                     | 12/2012     | -                                 | 6/12                       |
| 153  | DHABOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State                      | 06/2009          | 4,543.43<br>4,508.38    | 4,508.38         | 7.20              | -                     | 12/2012     | -                                 | 11/10                      |
| 154  | De-bottlenecking of SMPL - [N16000089]IOCL,Maharashtra                                       | 12/2009          | 1,584.00                | 1,584.00         | 1.55              | -                     | 12/2012     | -                                 | 0/0                        |

| S.No | Project                                                                            | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                    |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                  | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 155  | ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra              | 10/2008          | 1,797.35                | 1,797.35         | 9.78              | 12/2011               | 01/2013     | 13(O)                             | 0/0                        |
| 156  | MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra                 | 06/2007          | 1,252.75<br>8,813.41    | 8,813.41         | 4,858.50          | 06/2009<br>03/2013    | 03/2013     | 0(R3)                             | 0/0                        |
| 157  | ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam                          | 03/2009          | 2,465.15                | 2,378.86         | 211.94            | 03/2013               | 03/2013     | 0(O)                              | 0/0                        |
| 158  | Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State      | 01/2010          | 723.64                  | 723.64           | -                 | 03/2013               | 03/2013     | 0(O)                              | 0/0                        |
| 159  | Development of Cluster-7 Fields - [N16000104]ONGC,Multi State                      | 03/2010          | 3,241.03                | 3,241.03         | -                 | 03/2013               | 03/2013     | 0(O)                              | 0/0                        |
| 160  | Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State                  | 06/2010          | 2,523.00                | 2,523.00         | -                 | 01/2014               | 01/2014     | 0(O)                              | 0/0                        |
| 161  | Wax Project - [N16000101]NRL,Assam                                                 | 08/2010          | 576.60                  | 576.60           | 6.48              | 02/2014               | 02/2014     | 0(O)                              | 0/0                        |
| 162  | PANIPAT NAPHTHA CRACKER PROJECT - [160100292]IOCL,Haryana                          | 04/2006          | 14,439.00               | 15,292.00        | 12,054.37         | 11/2009<br>11/2009    | -           | -                                 | 61/101                     |
| 163  | CAPACITY EXPANSION AND MODERNISATION OF KOCHI REFINERY - [N16000028]BPCL,Kerala    | 04/2006          | 2,591.80                | 3,941.41         | 1,793.00          | 09/2009               | -           | -                                 | 0/0                        |
| 164  | INST. OF FCC GASOLINE DESULPHUR UNIT AT MATHURA RE - [N16000034]IOCL,Uttar Pradesh | 01/2008          | 348.00                  | 348.00           | 186.58            | 12/2009               | -           | -                                 | 0/0                        |
| 165  | MSQ UPGRADE PROJECT AT PANIPAT REFINERY - [N16000035]IOCL,Haryana                  | 01/2008          | 1,131.00                | 1,131.00         | 750.71            | 12/2009               | -           | -                                 | 0/0                        |
|      | <b>Total</b>                                                                       |                  | 171,218.11              | 189,247.41       | 60,707.52         |                       |             |                                   | 184/368                    |
|      | <b>Power</b>                                                                       |                  |                         |                  |                   |                       |             |                                   |                            |
| 166  | TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO,Mizoram                             | 07/1998          | 368.72<br>877.06        | 913.63           | 216.34            | 07/2006               | 03/2010     | 44(O)                             | 2/5                        |
| 167  | KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka                 | 03/2005          | 596.45<br>1,007.16      | 947.96           | 770.22            | 12/2007               | 06/2010     | 30(O)                             | 14/18                      |
| 168  | SEWA- II H.E.P (NHPC) - [180100220]NHPC,J & K                                      | 09/2003          | 665.46                  | 1,016.74         | 982.76            | 09/2007               | 07/2010     | 34(O)                             | 8/36                       |
| 169  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XII - [N18000039]PGCIL,Haryana         | 02/2008          | 261.55                  | 261.55           | 137.30            | 11/2010               | 08/2010     | -3(O)                             | 0/0                        |
| 170  | NORTHERN REGION SYSTEM STRENGTHENING-XI - [N18000034]PGCIL,Multi State             | 12/2007          | 417.76                  | 417.76           | 259.72            | 12/2010               | 09/2010     | -3(O)                             | 0/0                        |
| 171  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X - [N18000036]PGCIL,Uttar Pradesh     | 12/2007          | 408.36                  | 408.36           | 289.85            | 12/2010               | 09/2010     | -3(O)                             | 0/0                        |
| 172  | EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]NHPC,Himachal Pr.  | 09/2007          | 262.10                  | 262.10           | 138.49            | 09/2010               | 09/2010     | 0(O)                              | 0/0                        |
| 173  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-IX - [N18000055]PGCIL,Multi State      | 07/2008          | 525.14                  | 525.14           | 341.01            | 07/2011               | 09/2010     | -10(O)                            | 0/0                        |

| S.No | Project                                                                                 | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|-----------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                         |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                       | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 174  | KORBA STPP STAGE-III - [N18000011]NTPC, Madhya Pradesh                                  | 08/2006          | 2,448.50                | 2,448.49         | 2,048.00          | 02/2010               | 10/2010     | 8(O)                              | 5/24                       |
| 175  | National Capital Thermal Power Project Stage-II - [N18000013]NTPC, Uttar Pradesh        | 10/2006          | 5,135.33                | 5,135.33         | 4,062.00          | 10/2010               | 10/2010     | 0(O)                              | 11/40                      |
| 176  | EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]NHPC, Multi State                   | 12/2007          | 227.52                  | 227.52           | 115.30            | 06/2010               | 10/2010     | 4(O)                              | 0/0                        |
| 177  | KOTESWAR TRANSMISSION SYSTEM (PGCIL) - [180100256]PGCIL, Uttaranchal                    | 06/2006          | 260.34                  | 241.27           | 150.88            | 06/2008               | 11/2010     | 29(O)                             | 8/20                       |
| 178  | WESTERN REGION STRENGTHENING SCHEME-VI - [N18000038]PGCIL, Gujarat                      | 02/2008          | 340.72                  | 340.72           | 144.13            | 11/2010               | 11/2010     | 0(O)                              | 0/0                        |
| 179  | KOTESHWAR HEP (THDC) - [180100184]THDC, Uttaranchal                                     | 04/2000          | 1,301.56                | 2,398.39         | 1,978.54          | 04/2005               | 12/2010     | 68(O)                             | 2/22                       |
| 180  | CHAMERA, STAGE-III (NHPC) - [180100241]NHPC, Himachal Pr.                               | 08/2005          | 1,405.63                | 1,405.63         | 1,258.91          | 08/2010               | 12/2010     | 4(O)                              | 0/0                        |
| 181  | TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT (P.G.R.) - [180100260]PGCIL, Bihar | 12/2005          | 3,779.46                | 3,725.13         | 3,407.04          | 09/2009               | 12/2010     | 15(O)                             | 15/30                      |
| 182  | EAST-WEST TRANSMISSION CORRIDOR STRENGTHENING SCHEME - [260100100]PGCIL, Multi State    | 06/2006          | 803.70                  | 803.76           | 611.43            | 06/2009               | 12/2010     | 18(O)                             | 1/20                       |
| 183  | EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL, Uttar Pradesh                 | 10/2006          | 975.96                  | 894.26           | 614.89            | 10/2009               | 12/2010     | 14(O)                             | 2/20                       |
| 184  | NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC, J & K                              | 08/2006          | 611.01                  | 611.02           | 493.74            | 08/2010               | 12/2010     | 4(O)                              | 0/0                        |
| 185  | TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G - [N18000037]PGCIL, Haryana          | 04/2008          | 290.49                  | 290.49           | 291.80            | 04/2010               | 12/2010     | 8(O)                              | 0/0                        |
| 186  | TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL, Multi State              | 04/2008          | 297.37                  | 297.37           | 193.75            | 07/2011               | 12/2010     | -7(O)                             | 0/0                        |
| 187  | WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]PGCIL, Multi State                  | 04/2008          | 230.89                  | 230.89           | 35.85             | 01/2011               | 01/2011     | 0(O)                              | 0/0                        |
| 188  | URI H.E.P STAGE -II (NHPC) - [180100251]NHPC, J & K                                     | 08/2005          | 1,729.29                | 1,724.79         | 1,187.42          | 11/2009               | 02/2011     | 15(O)                             | 0/0                        |
| 189  | CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007]NHPC, J & K                                  | 08/2006          | 621.26                  | 621.28           | 484.67            | 02/2011               | 02/2011     | 0(O)                              | 0/1                        |
| 190  | Farakka STPP Stage-III - [N18000016]NTPC, West Bengal                                   | 07/2006          | 2,570.44                | 2,570.44         | 1,743.00          | 08/2010               | 02/2011     | 6(O)                              | 13/26                      |
| 191  | KUNADANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL, Tamil Nadu                   | 05/2005          | 1,779.29                | 1,946.85         | 1,599.01          | 11/2008               | 03/2011     | 28(O)                             | 25/38                      |
| 192  | WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL, Rajasthan                    | 07/2006          | 5,221.23                | 4,978.56         | 2,529.96          | 07/2010               | 03/2011     | 8(O)                              | 3/20                       |
| 193  | WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL, Maharashtra                   | 12/2007          | 477.69                  | 477.69           | 298.72            | 09/2010               | 03/2011     | 6(O)                              | 0/0                        |

| S.No | Project                                                                              | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|--------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                      |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                    | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 194  | URI-II - [N18000023]PGCIL,J & K                                                      | 10/2006          | 238.25                  | 238.25           | 190.12            | -                     | 05/2011     | -                                 | 0/0                        |
| 195  | SIMHADRI STPP STAGE -II - [N18000032]NTPC,Andhra Pradesh                             | 08/2007          | 5,103.39                | 5,038.53         | 3,206.00          | 05/2011               | 05/2011     | 0(O)                              | 0/0                        |
| 196  | PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.                      | 10/2005          | 2,304.56                | 2,304.52         | 1,110.27          | 10/2010               | 06/2011     | 8(O)                              | 0/0                        |
| 197  | TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE - [N18000018]PGCIL,Himachal Pr.   | 07/2006          | 557.24                  | 639.52           | 356.95            | 01/2010               | 06/2011     | 17(O)                             | 0/22                       |
| 198  | TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State       | 12/2008          | 204.07                  | 204.07           | 78.16             | 06/2011               | 06/2011     | 0(O)                              | 0/0                        |
| 199  | TR. SYSTEM ASSOCIATED WITH CORBA III GENERATION PR - [N18000059]PGCIL,Madhya pradesh | 02/2009          | 276.61                  | 276.61           | 135.33            | 06/2011               | 06/2011     | 0(O)                              | 0/0                        |
| 200  | SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State           | 03/2009          | 196.10                  | 196.10           | 20.60             | 07/2011               | 07/2011     | 0(O)                              | 0/0                        |
| 201  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan        | 02/2009          | 210.79                  | 210.79           | 88.85             | 08/2011               | 08/2011     | 0(O)                              | 0/0                        |
| 202  | SYSTEM STRENGTHENING IN NR GRID FOR KARCHAM WANGTO - [N18000044]PGCIL,Multi State    | 12/2008          | 328.97                  | 328.97           | 140.33            | 09/2011               | 09/2011     | 0(O)                              | 0/0                        |
| 203  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State        | 02/2009          | 520.48                  | 520.48           | 188.26            | 11/2011               | 11/2011     | 0(O)                              | 0/0                        |
| 204  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State     | 02/2009          | 509.66                  | 509.66           | 96.82             | 11/2011               | 11/2011     | 0(O)                              | 0/0                        |
| 205  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State      | 02/2009          | 317.69                  | 317.69           | -                 | 11/2011               | 11/2011     | 0(O)                              | 0/0                        |
| 206  | TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State                 | 02/2009          | 184.19                  | 184.19           | 56.76             | 11/2011               | 11/2011     | 0(O)                              | 0/0                        |
| 207  | TESSTA LOW DAM STAGE - II, III (NHPC) - [180100222]NHPC,West Bengal                  | 10/2003          | 768.92                  | 1,279.40         | 1,179.12          | 03/2007               | 12/2011     | 57(O)                             | 1/25                       |
| 208  | SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh                            | 12/2003          | 8,323.39                | 8,323.39         | 6,952.00          | 12/2009               | 12/2011     | 24(O)                             | 33/56                      |
| 209  | TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura                          | 07/2009          | 421.01                  | 623.44           | 54.68             | 01/2012               | 01/2012     | 0(O)                              | 0/0                        |
| 210  | WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State                 | 02/2009          | 664.96                  | 664.96           | 65.13             | 02/2012               | 02/2012     | 0(O)                              | 0/0                        |
| 211  | WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State         | 02/2009          | 409.50                  | 409.50           | 4.51              | 02/2012               | 02/2012     | 0(O)                              | 0/0                        |
| 212  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State       | 02/2009          | 410.29                  | 410.29           | 81.86             | 02/2012               | 02/2012     | 0(O)                              | 0/0                        |

| S.No | Project                                                                              | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|--------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                      |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                    | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 213  | TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State           | 02/2009          | 353.57                  | 353.57           | 128.52            | 07/2010               | 02/2012     | 19(O)                             | 0/0                        |
| 214  | 765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State    | 02/2009          | 1,347.32                | 1,347.32         | 388.91            | 02/2012               | 02/2012     | 0(O)                              | 0/0                        |
| 215  | KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.                                     | 10/2002          | 4,527.15                | 4,527.15         | 3,285.00          | 04/2009               | 03/2012     | 35(O)                             | 19/41                      |
| 216  | RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.                                   | 01/2007          | 2,047.03                | 2,047.03         | 931.64            | 01/2012               | 03/2012     | 2(O)                              | 2/10                       |
| 217  | BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam                             | 01/2008          | 4,375.35                | 4,375.35         | 1,327.00          | 07/2011               | 03/2012     | 8(O)                              | 0/0                        |
| 218  | System Strengthening -X of SR - [N18000086]PGCIL,Multi State                         | 12/2009          | 276.61                  | 276.61           | 14.63             | 04/2012               | 04/2012     | 0(O)                              | 0/0                        |
| 219  | 765KV System for central part of Northern Region Grid - [N18000079]PGCIL,Multi State | 11/2009          | 1,075.12                | 1,075.12         | 85.48             | 05/2012               | 05/2012     | 0(O)                              | 0/0                        |
| 220  | 765KV System for Central part of Northern Region G - [N18000078]PGCIL,Multi State    | 07/2009          | 1,736.36                | 1,736.36         | -                 | 06/2012               | 06/2012     | 0(O)                              | 0/0                        |
| 221  | Immsdiate evacuation system for NABINAGAR TPS - [N18000082]PGCIL,Bihar               | 02/2010          | 215.86                  | 215.86           | 10.12             | 06/2012               | 06/2012     | 0(O)                              | 0/0                        |
| 222  | System Strengthening -XII of SR - [N18000085]PGCIL,Multi State                       | 02/2010          | 232.34                  | 232.34           | 4.56              | 06/2012               | 06/2012     | 0(O)                              | 0/0                        |
| 223  | TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal                    | 09/2005          | 1,061.38                | 1,061.38         | 777.87            | 09/2009               | 08/2012     | 35(O)                             | 0/0                        |
| 224  | PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.                | 12/2008          | 573.99                  | 573.99           | 108.37            | 08/2012               | 08/2012     | 0(O)                              | 4/21                       |
| 225  | SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State    | 08/2008          | 2,360.95                | 2,360.95         | 1,225.46          | 08/2012               | 08/2012     | 0(O)                              | 0/0                        |
| 226  | 765 KV POOLING STATION & NETWORK WITH DVC AND MAIT - [N18000069]PGCIL,Multi State    | 08/2008          | 7,075.33                | 7,075.33         | 2,355.09          | 08/2012               | 08/2012     | 0(O)                              | 0/0                        |
| 227  | System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State  | 12/2009          | 1,216.83                | 1,216.83         | 88.45             | 08/2012               | 08/2012     | 0(O)                              | 0/0                        |
| 228  | MOUDA STPP - [N18000048]NTPC,Maharashtra                                             | 11/2007          | 5,459.28                | 6,010.89         | 1,378.00          | 02/2012               | 10/2012     | 8(O)                              | 0/0                        |
| 229  | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER - [N18000061]PGCIL,Multi State    | 10/2008          | 4,824.12                | 4,824.12         | 729.08            | 10/2012               | 10/2012     | 0(O)                              | 0/0                        |
| 230  | MAUDA Transmission System - [N18000084]PGCIL,Maharashtra                             | 02/2010          | 469.38                  | 469.38           | 9.84              | 10/2012               | 10/2012     | 0(O)                              | 0/0                        |
| 231  | Transmission System of Vindhuachal -IV & Rihand -I - [N18000076]PGCIL,Multi State    | 03/2010          | 4,672.99                | 4,672.99         | 11.89             | 11/2012               | 11/2012     | 0(O)                              | 0/0                        |
| 232  | Northern Region Transmission Strengthening Scheme - [N18000083]PGCIL,Multi State     | 03/2012          | 965.58                  | 965.58           | 64.68             | 11/2012               | 11/2012     | 0(O)                              | 0/0                        |

| S.No                               | Project                                                                              | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------------------------------------|--------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                                    |                                                                                      |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                                  | 2                                                                                    | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 233                                | LOWER SUBANSIRI H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.                         | 09/2003          | 6,285.33                | 7,451.99         | 4,159.51          | 09/2010               | 12/2012     | 27(O)                             | 2/11                       |
| 234                                | TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]PGCIL,Himachal Pr. | 12/2005          | 358.42                  | 358.42           | 6.57              | 12/2008<br>09/2010    | 12/2012     | 27(R1)                            | 0/15                       |
| 235                                | LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal                             | 06/2006          | 2,895.10                | 2,895.10         | 552.33            | 11/2011               | 12/2012     | 13(O)                             | 6/34                       |
| 236                                | TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State    | 12/2008          | 7,031.88                | 7,031.88         | 1,185.43          | 12/2012               | 12/2012     | 0(O)                              | 0/0                        |
| 237                                | VINDHYACHAL STTP STAGE-IV - [N18000072]NTPC,Madhya pradesh                           | 01/2009          | 5,915.00                | 5,915.00         | 978.00            | 11/2012               | 12/2012     | 1(O)                              | 0/0                        |
| 238                                | RIHAND STTP STAGE-III (2X500MW) - [N18000073]NTPC,Uttar Pradesh                      | 01/2009          | 6,230.81                | 6,230.81         | 817.00            | 11/2012               | 12/2012     | 1(O)                              | 0/0                        |
| 239                                | Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State    | 02/2010          | 2,144.00                | 2,144.00         | 64.15             | 12/2012               | 12/2012     | 0(O)                              | 0/0                        |
| 240                                | PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.                                 | 09/2002          | 3,919.59                | 3,919.59         | 2,877.68          | 09/2009               | 03/2013     | 42(O)                             | 1/20                       |
| 241                                | Tapovan-Vishnugad HEP (4x130MW) - [N18000014]NTPC,Uttaranchal                        | 11/2006          | 2,978.48                | 2,978.48         | 894.00            | 03/2013               | 03/2013     | 0(O)                              | 5/31                       |
| 242                                | KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.              | 12/2004          | 2,496.90                | 3,253.22         | 1,217.03          | 05/2013               | 05/2013     | 0(O)                              | 77/54                      |
| 243                                | BARH STTP STAGE -II - [N18000047]NTPC,Bihar                                          | 02/2008          | 7,341.04                | 7,341.04         | 1,074.00          | 08/2013               | 08/2013     | 0(O)                              | 0/0                        |
| 244                                | NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State    | 02/2009          | 11,130.19               | 11,130.19        | 1,288.66          | 08/2013               | 08/2013     | 0(O)                              | 0/0                        |
| 245                                | BARH STTP(3X660MW) NTPC - [180100242]NTPC,Bihar                                      | 12/2003          | 8,692.97                | 8,692.97         | 4,963.00          | 11/2010               | 04/2014     | 41(O)                             | 15/51                      |
| 246                                | Transm System for development of Pooling str. in N - [N18000077]PGCIL,West Bengal    | 04/2010          | 4,404.57                | 4,404.57         | -                 | 01/2015               | 01/2015     | 0(O)                              | 0/0                        |
| 247                                | TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttaranchal                    | 07/2006          | 1,657.00                | 3,124.76         | 248.92            | 07/2010               | 03/2015     | 56(O)                             | 0/0                        |
| 248                                | VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal            | 08/2008          | 2,491.58                | 2,491.58         | 120.01            | 07/2014               | 03/2015     | 8(O)                              | 0/8                        |
| 249                                | KISHANGANGA HEP - [N18000031]NHPC,J & K                                              | 07/2007          | 2,238.67                | 3,642.04         | 334.63            | 07/2014               | 01/2016     | 18(O)                             | 0/0                        |
| 250                                | LOKTAK D/S HEP(NHPC) - [180100078]NHPC,Manipur                                       | 12/1999          | 578.62                  | 578.62           | 28.33             | 06/2006               | -           | -                                 | 0/0                        |
| Total                              |                                                                                      |                  | 179,619.98              | 187,805.89       | 74,124.32         |                       |             |                                   | 274/719                    |
| <b>Health &amp; Family Welfare</b> |                                                                                      |                  |                         |                  |                   |                       |             |                                   |                            |
| 251                                | NORTH EAST INDIRA GANDHI INST-ITUTE OF HEALTH & MS - [210100001]H&FW,Meghalaya       | 05/1986          | 71.18<br>422.60         | 443.15           | 477.33            | 03/1999<br>03/2005    | -           | -                                 | 7/16                       |
| Total                              |                                                                                      |                  | 71.18                   | 443.15           | 477.33            |                       |             |                                   | 7/16                       |



| S.No            | Project                                                                              | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|-----------------|--------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                 |                                                                                      |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1               | 2                                                                                    | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| <b>Railways</b> |                                                                                      |                  |                         |                  |                   |                       |             |                                   |                            |
| 252             | RAJGIR-TILAIYA (NL), ECR - [220100312]ECR,Bihar                                      | 04/2001          | 180.82<br>180.82        | 180.82           | 264.46            | 03/2006<br>-          | 01/2010     | 46(O)                             | 0/0                        |
| 253             | RAJKOT-VERAVAL & WANSJALIYA-JETALSAR GC(WR) - [220100116]WR,Gujarat                  | 04/1992          | 112.53<br>320.66        | 464.50           | 501.12            | 03/1996<br>06/2009    | 06/2010     | 12(R1)                            | 0/0                        |
| 254             | VALLAPARPADM-IDAPALLY,(NL)(RVNL) - [N22000048]RVNL,Kerala                            | 07/2006          | 246.50<br>246.50        | 246.50           | 322.52            | 03/2009<br>03/2009    | 11/2009     | 8(R3)                             | 0/0                        |
| 255             | TAHANJAVUR-VILLUPURAM GAUGE CONVERSION (G.C)(SR) - [220100244]RVNL,Tamil Nadu        | 10/2001          | 223.00<br>-             | 665.00           | 586.85            | -<br>11/2008          | 03/2010     | 16(R1)                            | 0/0                        |
| 256             | DHARMAVARAM-PAKALA (GC), SCR - [220100282]SCR,Andhra Pradesh                         | 04/1997          | 200.00<br>294.99        | 610.07           | 567.49            | -<br>02/2009          | 03/2010     | 13(R1)                            | 0/0                        |
| 257             | BHILDI-SAMDARI (GC) - [220100291]RVNL,Gujarat                                        | 04/1999          | 244.74<br>479.00        | 479.00           | 475.51            | -<br>03/2009          | 03/2010     | 12(R1)                            | 0/0                        |
| 258             | PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat                          | 04/2005          | 148.61<br>-             | 227.52           | 236.00            | 03/2008<br>03/2009    | 03/2010     | 12(R1)                            | 0/0                        |
| 259             | OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh                  | 07/2006          | 743.00<br>732.80        | 732.80           | 226.85            | 03/2008<br>06/2008    | 03/2010     | 21(R3)                            | 0/0                        |
| 260             | REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh                              | 06/2000          | 168.34<br>-             | 296.20           | 259.66            | 04/2003<br>03/2010    | 06/2010     | 3(R1)                             | 0/0                        |
| 261             | ABOHAR- FAZILKA - [N22000055]NL,Punjab                                               | 09/2001          | 86.44<br>-              | 209.57           | 199.51            | 03/2009<br>-          | 07/2010     | 16(O)                             | 0/0                        |
| 262             | KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka                                  | 04/1995          | 65.94<br>-              | 325.00           | 304.76            | -<br>-                | 09/2010     | -                                 | 0/0                        |
| 263             | TOLLYGANJ-GARIA(MTP) - [220100268]MRTP,West Bengal                                   | 03/2000          | 907.69<br>-             | 1,032.76         | 837.97            | 12/2006<br>-          | 09/2010     | 45(O)                             | 0/0                        |
| 264             | DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER) - [220100264]ER,Jharkhand                     | 02/1999          | 180.73<br>-             | 358.00           | 321.56            | 12/2006<br>12/2008    | 11/2010     | 23(R1)                            | 0/0                        |
| 265             | SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa                             | 04/1998          | 183.23<br>-             | 638.00           | 24.68             | 02/2015<br>-          | 11/2010     | -51(O)                            | 0/0                        |
| 266             | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)-PH-I - [220100164]MRTP,Maharashtra | 03/1996          | 401.81<br>-             | 495.44           | 155.05            | 03/2004<br>-          | 12/2010     | 81(O)                             | 0/0                        |
| 267             | KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Multi State                           | 09/2001          | 100.00<br>492.98        | 724.31           | 690.13            | -<br>-                | 12/2010     | -                                 | 0/0                        |
| 268             | TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal              | 04/2000          | 157.96<br>-             | 762.33           | 279.72            | -<br>12/2009          | 12/2010     | 12(R1)                            | 0/0                        |
| 269             | RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa                                   | 04/1999          | 166.16<br>-             | 243.40           | -                 | -<br>02/2009          | 12/2010     | 22(R1)                            | 0/0                        |
| 270             | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa                   | 04/2000          | 133.41<br>207.00        | 211.90           | 151.69            | -<br>03/2009          | 12/2010     | 21(R1)                            | 0/0                        |
| 271             | RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh                           | 04/2003          | 136.62<br>-             | 221.90           | 122.28            | 12/2007<br>03/2010    | 12/2010     | 9(R1)                             | 0/0                        |
| 272             | AJMER-PHULERA-RINGUS-REWARI (G.C.)(NWR)(RVNL) - [N22000033]RVNL,Rajasthan            | 04/2005          | 352.00<br>716.64        | 718.30           | 616.44            | 03/2008<br>08/2008    | 12/2010     | 28(R1)                            | 0/0                        |

| S.No | Project                                                                          | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|----------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                  |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 273  | ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh        | 04/2003          | 230.73<br>399.73        | 399.50           | 267.17            | 03/2009<br>12/2008    | 12/2010     | 24(R1)                            | 0/0                        |
| 274  | BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat                    | 09/2005          | 200.80<br>200.80        | 200.80           | 166.53            | -<br>-                | 12/2010     | -                                 | 0/0                        |
| 275  | MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP,Maharashtra             | 04/2003          | 3,125.20<br>-           | 4,103.20         | 3,840.09          | -<br>-                | 12/2010     | -                                 | 0/1                        |
| 276  | KADUR-CHIKMAGALUR-SAKLESHPU (NL),(SWR) - [220100190]SWR,Karnataka                | 04/1996          | 157.00<br>-             | 465.00           | 112.11            | -<br>-                | 02/2011     | -                                 | 0/0                        |
| 277  | MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar                             | 03/1997          | 100.00<br>-             | 332.29           | 365.44            | -<br>-                | 02/2011     | -                                 | 0/0                        |
| 278  | REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana                                  | 01/2004          | 149.38<br>330.23        | 475.16           | 397.92            | 02/2010<br>-          | 02/2011     | 12(O)                             | 0/0                        |
| 279  | TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECR,Orissa                             | 04/2005          | 726.96<br>-             | 810.78           | 52.50             | -<br>-                | 02/2011     | -                                 | 0/0                        |
| 280  | SHIMOGA-TALAGUPPA - [N22000056]GC,Karnataka                                      | 12/1992          | 46.00<br>-              | 405.60           | 223.83            | -<br>-                | 02/2011     | -                                 | 0/0                        |
| 281  | VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State                               | 04/1990          | 155.66<br>-             | 356.87           | 123.93            | -<br>03/2010          | 03/2011     | 12(R1)                            | 0/0                        |
| 282  | AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra                              | 06/1994          | 120.90<br>175.30        | 488.76           | 353.66            | 06/1999<br>-          | 03/2011     | 141(O)                            | 0/0                        |
| 283  | RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd                             | 04/1997          | 193.78<br>-             | 456.45           | 247.29            | 06/2004<br>-          | 03/2011     | 81(O)                             | 0/0                        |
| 284  | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State              | 09/1998          | 925.00<br>-             | 925.00           | 471.30            | 05/2008<br>-          | 03/2011     | 34(O)                             | 0/0                        |
| 285  | AGRA-ETAWAH VIA FATEBAD & BAD (NL),NCR - [220100243]NCR,Uttar Pradesh            | 04/1999          | 108.00<br>-             | 214.09           | 152.40            | 12/2009<br>-          | 03/2011     | 15(O)                             | 0/0                        |
| 286  | GOOTY- RENIGUNTA PATCH DOUBLING PH-II (DL) (SCR) - [220100267]SCR,Andhra Pradesh | 05/2002          | 304.50<br>-             | 306.00           | 341.81            | -<br>-                | 03/2011     | -                                 | 0/0                        |
| 287  | KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECR,Orissa                             | 04/1994          | 355.38<br>-             | 700.00           | 99.60             | -<br>-                | 03/2011     | -                                 | 0/0                        |
| 288  | KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd                             | 04/1996          | 371.36<br>-             | 452.35           | 266.35            | -<br>-                | 03/2011     | -                                 | 0/0                        |
| 289  | SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan                      | 04/1997          | 143.92<br>-             | 168.80           | 70.43             | -<br>-                | 03/2011     | -                                 | 0/0                        |
| 290  | HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State                           | 04/2005          | 200.73<br>-             | 230.03           | 129.96            | -<br>-                | 03/2011     | -                                 | 0/0                        |
| 291  | BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh                               | 04/1997          | 151.52<br>-             | 273.00           | 263.51            | -<br>03/2009          | 03/2011     | 24(R1)                            | 0/0                        |
| 292  | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN - [N22000002]ECR,Bihar             | 04/1996          | 114.01<br>283.95        | 348.78           | 317.07            | -<br>-                | 03/2011     | -                                 | 0/0                        |
| 293  | PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State      | 04/2005          | 240.00<br>329.70        | 329.70           | 264.84            | 03/2009<br>12/2009    | 03/2011     | 15(R1)                            | 0/0                        |

| S.No | Project                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|----------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                        |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                      | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 294  | ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA - [N22000082]NEFR,Multi State             | 12/2006          | 170.00<br>255.96        | 272.11           | 183.84            | -<br>-                | 03/2011     | -                                 | 0/0                        |
| 295  | BARDHAMAN-KATWA (GC) - [N22000091]GC,West Bengal                                       | 04/2007          | 245.15<br>-             | 245.15           | 53.49             | 12/2010<br>-          | 03/2011     | 3(O)                              | 0/0                        |
| 296  | ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh       | 02/2008          | 171.10<br>-             | 171.10           | 43.83             | 03/2011<br>-          | 03/2011     | 0(O)                              | 0/0                        |
| 297  | ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh                        | 03/2006          | 258.35<br>-             | 258.35           | 9.38              | 03/2011<br>-          | 03/2011     | 0(O)                              | 0/0                        |
| 298  | RAJPIPLA-ANKELASHWAR (GC) - [N22000096]GC,Gujarat                                      | 04/2006          | 196.97<br>-             | 196.97           | 120.30            | 03/2011<br>-          | 03/2011     | 0(O)                              | 0/0                        |
| 299  | PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal                               | 09/2007          | 252.50<br>252.50        | 252.50           | 82.24             | 02/2010<br>-          | 11/2011     | 21(O)                             | 0/0                        |
| 300  | HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa                                       | 04/1996          | 301.64<br>-             | 735.10           | 175.76            | -<br>09/2009          | 12/2011     | 27(R1)                            | 0/0                        |
| 301  | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar                       | 04/1997          | 233.00<br>335.77        | 727.52           | 470.54            | -<br>-                | 03/2012     | -                                 | 0/0                        |
| 302  | KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar                                           | 04/2002          | 323.41<br>-             | 341.41           | 180.12            | -<br>-                | 03/2012     | -                                 | 0/0                        |
| 303  | EXT. OF MRTS FROM VELACHERY TO STN. THOMAS - [N22000028]MRTP,Tamil Nadu                | 04/2006          | 415.59<br>-             | 495.74           | 80.10             | -<br>-                | 03/2012     | -                                 | 0/0                        |
| 304  | SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh                      | 09/2006          | 324.90<br>-             | 324.90           | 103.73            | 03/2010<br>-          | 03/2012     | 24(O)                             | 0/0                        |
| 305  | SITAMARHI-RAXAUL-NARKATIAGANJ (GC) - [N22000089]GC,Bihar                               | 04/1997          | 501.69<br>-             | 501.69           | 45.90             | 03/2010<br>-          | 03/2012     | 24(O)                             | 0/0                        |
| 306  | TAMLUK DIGHA - [N22000097]LD,West Bengal                                               | 03/1984          | 293.97<br>-             | 293.97           | 313.13            | 06/2005<br>-          | 04/2012     | 82(O)                             | 0/0                        |
| 307  | NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State                                 | 03/1981          | 37.68<br>450.00         | 730.00           | 281.91            | -<br>-                | 07/2012     | -                                 | 0/0                        |
| 308  | GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State                                      | 04/1985          | 158.77<br>274.56        | 432.46           | 479.30            | 03/1994<br>-          | 12/2012     | 225(O)                            | 0/0                        |
| 309  | CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra                   | 07/1996          | 273.67<br>1,160.52      | 1,800.00         | 501.49            | -<br>-                | 12/2012     | -                                 | 0/0                        |
| 310  | CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab                           | 07/1997          | 248.44<br>576.27        | 1,103.47         | 675.91            | -<br>-                | 12/2012     | -                                 | 0/0                        |
| 311  | GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh | 03/2002          | 383.15<br>-             | 863.23           | 325.79            | -<br>-                | 12/2012     | -                                 | 0/0                        |
| 312  | JIND-SONEPAT (NL),NR - [220100280](NR),Haryana                                         | 01/2004          | 190.81<br>238.56        | 234.45           | 156.64            | -<br>-                | 12/2012     | -                                 | 0/0                        |
| 313  | RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar                        | 04/2002          | 921.00<br>-             | 981.00           | 340.69            | 03/2009<br>-          | 12/2012     | 45(O)                             | 0/0                        |
| 314  | PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar                                    | 04/2001          | 624.47<br>-             | 1,480.71         | 445.84            | 10/2007<br>-          | 12/2012     | 62(O)                             | 0/0                        |
| 315  | BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh                          | 09/2007          | 687.20<br>-             | 687.20           | 125.24            | 03/2010<br>-          | 12/2012     | 33(O)                             | 0/0                        |

| S.No | Project                                                                            | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                    |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                  | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 316  | UTRATIA-ZAFRABAD (LINE DOUBLING) - [N22000088]LD, Uttar Pradesh                    | 04/2006          | 325.00<br>-             | 496.03           | 88.08             | 03/2010<br>-          | 12/2012     | 33(O)                             | 0/0                        |
| 317  | DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan                             | 02/1997          | 151.84<br>-             | 410.08           | 101.53            | -<br>-                | 03/2013     | -                                 | 0/0                        |
| 318  | QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State        | 03/1998          | 280.00<br>-             | 1,029.00         | 570.96            | -<br>-                | 03/2013     | -                                 | 0/0                        |
| 319  | RANGIA-MURKONGSELEK, (GC) NEFR - [220100315]NEFR,Multi State                       | 01/2004          | 912.70<br>912.70        | 1,556.23         | 289.74            | -<br>-                | 03/2013     | -                                 | 0/0                        |
| 320  | BRAHAMAPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam           | 04/1996          | 1,000.00<br>1,500.00    | 3,230.02         | 1,912.11          | 04/2008<br>12/2011    | 03/2014     | 27(R1)                            | 0/0                        |
| 321  | MAYNAGURI TO JOGIGHOPA VIA CHANGRA (NL),NEFR - [220100266]NEFR,Multi State         | 02/2000          | 733.00<br>-             | 1,655.80         | 520.84            | 12/2008<br>-          | 03/2014     | 63(O)                             | 0/0                        |
| 322  | CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr. | 09/1996          | 156.00<br>-             | 160.48           | 97.39             | -<br>-                | 03/2014     | -                                 | 0/0                        |
| 323  | NEW B.G. LINE FROM AZARA TO BYRNIHAT (NATINAL PROJ - [N22000086]NEFR,Assam         | 09/2006          | 200.00<br>-             | 390.00           | 0.78              | -<br>-                | 03/2014     | -                                 | 0/0                        |
| 324  | AGARTALA SABROOM - [N22000099]NL,Tripura                                           | 04/2008          | 813.34<br>-             | 813.34           | 92.97             | 03/2014<br>-          | 03/2014     | 0(O)                              | 0/0                        |
| 325  | BHAIRABI SAIRONG - [N22000100]NL,Mizoram                                           | 04/2008          | 619.34<br>-             | 2,429.41         | 0.82              | 04/2014<br>-          | 03/2014     | -1(O)                             | 0/0                        |
| 326  | HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar                      | 04/2003          | 324.66<br>-             | 324.66           | 132.39            | -<br>-                | 03/2015     | -                                 | 0/0                        |
| 327  | MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra              | 04/2008          | 5,300.00<br>-           | 5,300.00         | 128.36            | 03/2014<br>-          | 03/2015     | 12(O)                             | 0/0                        |
| 328  | SEVOK RANGPO - [N22000102]LD,Sikkim                                                | 04/2008          | 1,339.48<br>-           | 1,339.48         | 1.42              | 12/2015<br>-          | 12/2015     | 0(O)                              | 0/0                        |
| 329  | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Multi State                  | 04/2003          | 727.56<br>727.53        | 3,123.52         | 222.40            | 03/2011<br>-          | 03/2016     | 60(O)                             | 0/0                        |
| 330  | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K                        | 03/1995          | 2,500.00<br>-           | 16,000.00        | 6,748.81          | 03/2001<br>-          | 12/2017     | 201(O)                            | 0/0                        |
| 331  | FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State         | 03/1984          | 520.00<br>422.79        | 634.13           | 556.48            | 03/1995<br>-          | -           | -                                 | 0/0                        |
| 332  | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh             | 12/1994          | 124.43<br>-             | 617.63           | 376.19            | -<br>-                | -           | -                                 | 0/0                        |
| 333  | HOTGI-GADAG(GC),SWR - [220100125]SWR,Multi State                                   | 04/1994          | 180.00<br>-             | 318.66           | 452.61            | 03/1999<br>03/2003    | -           | -                                 | 0/0                        |
| 334  | AMBALA-MORADABAD(RE) - [220100131]RE,Multi State                                   | 03/1993          | 152.21<br>157.76        | 265.00           | 265.33            | 03/1998<br>-          | -           | -                                 | 0/0                        |
| 335  | EKLAKHI-BALURGHAT(NL),NEFR - [220100135]NEFR,West Bengal                           | 01/1986          | 36.80<br>274.41         | 285.93           | 232.01            | -<br>-                | -           | -                                 | 0/0                        |
| 336  | LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECR,Orissa                               | 04/1993          | 100.00<br>142.98        | 170.00           | 133.06            | 03/2002<br>03/2011    | -           | -                                 | 0/0                        |

| S.No | Project                                                                    | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|----------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                            |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                          | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 337  | DALLIRAJHARA-JAGDALPUR,NL,SECR - [220100149]SECR,Chhatisgarh               | 04/1995          | 369.00<br>-             | 968.60           | 0.43              | -<br>-                | -           | -                                 | 0/0                        |
| 338  | CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State                    | 02/1996          | 240.00<br>-             | 579.37           | 576.95            | -<br>-                | -           | -                                 | 0/0                        |
| 339  | MIRAJ-LATUR ROAD(GC),CR - [220100162]CR,Maharashtra                        | 04/1993          | 225.00<br>323.00        | 816.40           | 808.55            | 03/2001<br>-          | -           | -                                 | 0/0                        |
| 340  | MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd              | 04/1995          | 184.00<br>-             | 675.00           | 330.00            | -<br>12/2010          | -           | -                                 | 0/0                        |
| 341  | AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra               | 02/1997          | 353.08<br>-             | 1,010.00         | 67.32             | -<br>-                | -           | -                                 | 0/0                        |
| 342  | AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]NWR,Rajasthan             | 09/1996          | 262.00<br>433.39        | 456.00           | 470.63            | -<br>03/2000          | -           | -                                 | 0/0                        |
| 343  | GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State                   | 02/1997          | 356.00<br>-             | 511.86           | 413.02            | 03/1998<br>-          | -           | -                                 | 0/0                        |
| 344  | SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]WR,Gujarat                     | 03/1997          | 437.40<br>-             | 563.25           | 540.21            | 03/2004<br>03/2005    | -           | -                                 | 0/0                        |
| 345  | KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu                              | 02/1997          | 155.55<br>-             | 712.00           | 384.68            | -<br>-                | -           | -                                 | 0/0                        |
| 346  | NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh               | 03/1997          | 155.74<br>164.36        | 429.49           | 352.10            | 02/2009<br>-          | -           | -                                 | 0/0                        |
| 347  | HUBLI-AKOLA(NL),SWR - [220100193]SWR,Karnataka                             | 04/1995          | 227.00<br>-             | 337.82           | 53.93             | -<br>-                | -           | -                                 | 0/0                        |
| 348  | HOSPET-GUNTAKAL(LD),SCR - [220100195]RVNL,Multi State                      | 03/1996          | 105.22<br>-             | 268.00           | 283.49            | 12/1999<br>03/2008    | -           | -                                 | 0/0                        |
| 349  | KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh              | 03/1997          | 395.00<br>1,062.36      | 1,548.95         | 1,101.82          | -<br>-                | -           | -                                 | 0/0                        |
| 350  | MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State               | 04/1996          | 377.32<br>236.41        | 497.47           | 72.00             | -<br>-                | -           | -                                 | 0/0                        |
| 351  | HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal              | 04/1974          | 31.42<br>154.30         | 154.30           | 106.79            | 03/2007<br>03/2007    | -           | -                                 | 0/0                        |
| 352  | MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh                 | 07/1998          | 125.00<br>-             | 363.26           | 0.27              | 07/2008<br>-          | -           | -                                 | 0/0                        |
| 353  | KODERMA-RANCHI VIA BARKAKHANA (NL),ECR - [220100222]ECR,Jharkhandd         | 03/1999          | 491.19<br>-             | 1,099.20         | 711.79            | 07/2005<br>-          | -           | -                                 | 0/0                        |
| 354  | KUTTIPURAM-CALICUT INCLD. SHORANUR-M-LORE (DL) (SR) - [220100249]SR,Kerala | 03/2001          | 178.76<br>177.34        | 219.94           | 190.49            | -<br>-                | -           | -                                 | 0/0                        |
| 355  | VILLUPURAM-KATPADI (GC)(SR) - [220100251]SR,Tamil Nadu                     | 02/2000          | 175.00<br>-             | 513.16           | 494.53            | -<br>-                | -           | -                                 | 0/0                        |
| 356  | ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala                      | 10/1998          | 550.00<br>-             | 550.00           | 64.90             | -<br>-                | -           | -                                 | 0/0                        |
| 357  | PURNA-AKOLA (G.C), SCR - [220100253]SCR,Maharashtra                        | 02/2000          | 228.00<br>-             | 497.63           | 477.14            | -<br>-                | -           | -                                 | 0/0                        |
| 358  | BIDAR-GULBARGA,SCR(NL) - [220100254]SCR,Karnataka                          | 02/1999          | 242.42<br>369.70        | 369.70           | 159.17            | -<br>05/2009          | -           | -                                 | 0/0                        |

| S.No | Project                                                                       | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|-------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                               |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                             | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 359  | KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State          | 09/2001          | 320.10<br>-             | 522.56           | 282.57            | -<br>-                | -           | -                                 | 0/1                        |
| 360  | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar                  | 03/1997          | 78.23<br>-              | 162.87           | 72.45             | -<br>-                | -           | -                                 | 0/0                        |
| 361  | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State          | 03/2002          | 409.00<br>408.76        | 639.54           | 770.30            | 06/2007<br>-          | -           | -                                 | 0/0                        |
| 362  | TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu            | 09/1995          | 100.00<br>-             | 548.96           | 411.96            | -<br>-                | -           | -                                 | 0/0                        |
| 363  | KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh                | 12/2001          | 330.00<br>-             | 695.00           | 9.41              | -<br>-                | -           | -                                 | 0/0                        |
| 364  | GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State                       | 04/1998          | 92.63<br>-              | 228.09           | 158.59            | -<br>-                | -           | -                                 | 0/0                        |
| 365  | DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State                    | 04/2000          | 138.00<br>240.59        | 607.09           | 238.57            | -<br>12/2012          | -           | -                                 | 0/0                        |
| 366  | BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka                 | 02/1999          | 138.00<br>-             | 1,300.00         | 0.29              | -<br>-                | -           | -                                 | 0/0                        |
| 367  | BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal                     | 03/1998          | 111.90<br>-             | 325.17           | 311.98            | 03/2005<br>12/2008    | -           | -                                 | 0/0                        |
| 368  | KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand                          | 04/2002          | 459.91<br>-             | 418.17           | 52.53             | -<br>-                | -           | -                                 | 0/0                        |
| 369  | RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh                 | 04/2001          | 727.13<br>727.13        | 1,225.00         | 145.39            | -<br>-                | -           | -                                 | 0/0                        |
| 370  | MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar                         | 04/2003          | 104.10<br>-             | 218.19           | 72.12             | -<br>-                | -           | -                                 | 0/0                        |
| 371  | KICHHA-KHATIMA (NL) - NER - [220100317]NER,Uttaranchal                        | 04/2003          | 165.67<br>-             | 165.67           | 0.15              | -<br>-                | -           | -                                 | 0/0                        |
| 372  | CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh               | 04/2005          | 383.79<br>-             | 585.93           | 102.78            | -<br>-                | -           | -                                 | 0/0                        |
| 373  | GUNTUR-GUNTAKAL-KALLURU(GL)(SCR) - [220100330]SCR,Andhra Pradesh              | 04/1992          | 458.45<br>-             | 573.12           | 555.49            | -<br>-                | -           | -                                 | 0/0                        |
| 374  | MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh            | 04/2006          | 378.56<br>-             | 671.82           | 0.74              | -<br>-                | -           | -                                 | 0/0                        |
| 375  | GAELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand                      | 03/1998          | 186.92<br>-             | 261.70           | 0.08              | 02/2006<br>-          | -           | -                                 | 0/0                        |
| 376  | HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar   | 04/2003          | 98.74<br>-              | 224.51           | 41.39             | -<br>-                | -           | -                                 | 0/0                        |
| 377  | CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar      | 03/2005          | 470.09<br>-             | 881.19           | 86.35             | -<br>-                | -           | -                                 | 0/0                        |
| 378  | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-A - [N22000079]SR,Tamil Nadu | 09/2007          | 404.19<br>-             | 900.00           | 66.36             | -<br>-                | -           | -                                 | 0/0                        |
| 379  | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu  | 09/2006          | 343.17<br>-             | 900.00           | 225.25            | -<br>-                | -           | -                                 | 0/0                        |

| S.No                                 | Project                                                                                    | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|--------------------------------------|--------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                                      |                                                                                            |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                                    | 2                                                                                          | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 380                                  | TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu                           | 09/2006          | 125.00                  | 227.40           | 14.64             | -                     | -           | -                                 | 0/0                        |
| 381                                  | TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu                                           | 09/2006          | 456.00                  | 582.83           | 36.39             | -                     | -           | -                                 | 0/0                        |
| 382                                  | NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar                 | 09/2006          | 300.00                  | 529.88           | 26.09             | -                     | -           | -                                 | 0/0                        |
| 383                                  | BHAKURA DAMODAR - [N22000098]LD,West Bengal                                                | 03/1998          | 282.70                  | 325.17           | 48.64             | 07/2008               | -           | -                                 | 0/0                        |
| 384                                  | KISHANGANJ JALALGARH - [N22000101]NL,Bihar                                                 | 04/2008          | 282.92                  | 333.76           | 0.71              | -                     | -           | -                                 | 0/0                        |
| 385                                  | RESTORATION WITH GAUGE CONVERSION OF SILIGHAT TOWN - [N22000103]GC,Assam                   | 04/1993          | 100.41                  | 949.22           | 15.65             | 12/2009               | -           | -                                 | 0/0                        |
| 386                                  | HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka                   | 02/1997          | 295.00                  | 913.51           | 431.87            | -                     | -           | -                                 | 0/0                        |
| 387                                  | NEW JALPAIGURI-NEW BONGAIGAON (GC),NEFR - [220100224]NEFR,Multi State                      | 11/1998          | 536.85                  | 1,010.00         | 1,005.45          | 03/2003               | -           | -                                 | 0/0                        |
| Total                                |                                                                                            |                  | 51,111.74               | 106,031.66       | 46,635.84         |                       |             |                                   | 0/2                        |
| <u>Road Transport &amp; Highways</u> |                                                                                            |                  |                         |                  |                   |                       |             |                                   |                            |
| 388                                  | MAHARASHTRA/AP BORDER TO ISLAM NAGAR,(NS-2/BOT/AP-6),NH-7 - [N24000093]NHAI,Andhra Pradesh | 12/2003          | 360.42                  | 360.42           | 478.40            | 11/2009               | 07/2010     | 8(O)                              | 0/0                        |
| 389                                  | MADURAI -KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160 - [240106241]NHAI,Tamil Nadu  | 12/2003          | 507.49                  | 507.49           | 342.80            | 03/2008               | 08/2010     | 29(O)                             | 0/0                        |
| 390                                  | ISLAM NAGAR TO KADTAL - [N24000109]NHAI,Andhra Pradesh                                     | 12/2003          | 546.83                  | 546.83           | 667.80            | 03/2010               | 08/2010     | 5(O)                              | 0/0                        |
| 391                                  | HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal                      | 04/2000          | 273.00                  | 522.00           | 328.70            | 03/2005               | 09/2010     | 66(O)                             | 0/0                        |
| 392                                  | JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1 - [240106268]NHAI,Punjab                 | 03/2005          | 263.00                  | 263.00           | 419.70            | 02/2009               | 09/2010     | 19(O)                             | 0/0                        |
| 393                                  | MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu   | 03/2005          | 629.00                  | 629.00           | 876.90            | 11/2010               | 09/2010     | -2(O)                             | 0/0                        |
| 394                                  | NAGAON BYPASS (NH-37)(NHAI) - [240106289]NHAI,Assam                                        | 12/2003          | 230.00                  | 230.00           | 285.50            | 06/2008               | 09/2010     | 27(O)                             | 0/0                        |
| 395                                  | KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan                                 | 12/2003          | 275.00                  | 250.39           | 247.70            | 10/2008               | 09/2010     | 23(O)                             | 0/0                        |
| 396                                  | HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4-3 - [N24000077]NHAI,Andhra Pradesh        | 12/2003          | 239.19                  | 239.19           | 224.50            | 09/2009               | 09/2010     | 12(O)                             | 0/0                        |
| 397                                  | HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418 - [N24000079]NHAI,Andhra Pradesh        | 12/2003          | 205.92                  | 205.92           | 204.40            | 08/2009               | 09/2010     | 13(O)                             | 0/0                        |

| S.No | Project                                                                                     | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|---------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                             |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                           | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 398  | HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251 - [N24000081]NHAI,Andhra Pradesh         | 12/2003          | 194.80                  | 194.80           | 174.00            | 08/2009               | 09/2010     | 13(O)                             | 0/0                        |
| 399  | LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh           | 12/2003          | 263.17                  | 263.17           | 232.50            | 09/2009               | 09/2010     | 12(O)                             | 0/0                        |
| 400  | JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh                               | 12/2003          | 355.06                  | 355.06           | 243.50            | 09/2009               | 09/2010     | 12(O)                             | 0/0                        |
| 401  | JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI, Uttar Pradesh                                  | 12/2003          | 276.09                  | 276.09           | 184.60            | 09/2009               | 09/2010     | 12(O)                             | 0/0                        |
| 402  | BANGALORE-NEELAMANGALALA NH-4 - [N24000104]NHAI, Karnataka                                  | 03/2005          | 445.00                  | 445.00           | 800.70            | 07/2010               | 09/2010     | 2(O)                              | 0/0                        |
| 403  | WAINGANGA BRIDGE - CHHATISGARH-MAHARASHTRA - [N24000120]NHAI, Multi State                   | 03/2008          | 424.00                  | 424.00           | 298.40            | 09/2010               | 09/2010     | 0(O)                              | 0/0                        |
| 404  | AMRITSAR-WAGHA BORDER - [N24000121]NHAI, Punjab                                             | 06/2008          | 205.88                  | 205.88           | 214.40            | 06/2010               | 09/2010     | 3(O)                              | 0/0                        |
| 405  | COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358 - [240100206]NHAI, Kerala          | 04/2000          | 106.00                  | 193.00           | 141.70            | 08/2006               | 10/2010     | 50(O)                             | 0/0                        |
| 406  | FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2) - [240101178]NHAI, Uttar Pradesh                    | 04/2000          | 372.40                  | 372.40           | 406.05            | 07/2004               | 10/2010     | 75(O)                             | 0/0                        |
| 407  | VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2) - [240101181]NHAI, Multi State         | 04/2000          | 467.93                  | 467.93           | 452.20            | 03/2005               | 10/2010     | 67(O)                             | 0/0                        |
| 408  | GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2) - [240101187]NHAI, Jharkhand                 | 04/2000          | 399.75                  | 399.75           | 424.96            | 03/2005               | 10/2010     | 67(O)                             | 0/0                        |
| 409  | AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]NHAI, Uttar Pradesh         | 12/2003          | 193.00                  | 193.00           | 284.10            | 10/2008               | 10/2010     | 24(O)                             | 0/0                        |
| 410  | AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]NHAI, Uttar Pradesh     | 12/2003          | 217.00                  | 217.00           | 310.30            | 10/2008               | 10/2010     | 24(O)                             | 0/0                        |
| 411  | GORAKHPUR-AYODHYA (LMNHP-6), NH-28, KM.251.70 TO KM.208.00 - [240106245]NHAI, Uttar Pradesh | 12/2003          | 239.00                  | 239.00           | 373.70            | 10/2008               | 10/2010     | 24(O)                             | 0/0                        |
| 412  | GORAKHPUR-AYODHYA (LMNHP-4), NH-28, KM.164.00 TO KM.135.00 - [240106247]NHAI, Uttar Pradesh | 12/2003          | 205.00                  | 205.00           | 300.10            | 10/2008               | 10/2010     | 24(O)                             | 0/0                        |
| 413  | AYODHYA-LUCKNOW (LMNHP-3), NH-28, KM.135.000 TO KM.93.075 - [240106248]NHAI, Uttar Pradesh  | 12/2003          | 212.00                  | 212.00           | 330.60            | 10/2008               | 10/2010     | 24(O)                             | 0/0                        |
| 414  | ORAI TO JHANSI (UP-4), NH-25, KM.170.0 TO KM.104.0 - [240106249]NHAI, Uttar Pradesh         | 12/2003          | 451.97                  | 451.97           | 493.90            | 04/2008               | 10/2010     | 30(O)                             | 0/0                        |
| 415  | HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293 - [N24000076]NHAI, Andhra Pradesh        | 12/2003          | 208.46                  | 208.46           | 193.70            | 08/2009               | 10/2010     | 14(O)                             | 0/0                        |
| 416  | HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376 - [N24000078]NHAI, Andhra Pradesh        | 12/2003          | 243.38                  | 243.38           | 261.40            | 09/2008               | 10/2010     | 25(O)                             | 0/0                        |



| S.No | Project                                                                                      | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|----------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                              |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                            | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 417  | KURALI-KIRATPUR, NH-21 - [N24000087]NHAI,Punjab                                              | 03/2005          | 309.00                  | 309.00           | 482.80            | 06/2010               | 10/2010     | 4(O)                              | 0/0                        |
| 418  | GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh                                     | 12/2003          | 300.93                  | 300.93           | 232.00            | 10/2009               | 10/2010     | 12(O)                             | 0/0                        |
| 419  | PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI,Tamil Nadu                                   | 03/2005          | 285.00                  | 285.00           | 239.80            | 07/2010               | 10/2010     | 3(O)                              | 0/0                        |
| 420  | BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]NHAI,Karnataka                         | 03/2005          | 565.00                  | 565.00           | 864.10            | 07/2010               | 10/2010     | 3(O)                              | 0/0                        |
| 421  | CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5 - [240106202]NHAI,Tamil Nadu                      | 12/2003          | 480.00                  | 480.00           | 833.10            | 11/2007               | 11/2010     | 36(O)                             | 0/0                        |
| 422  | HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka                         | 04/2000          | 241.00                  | 196.65           | 83.00             | 08/2004               | 12/2010     | 76(O)                             | 0/0                        |
| 423  | HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka                    | 04/2000          | 318.00                  | 207.56           | 93.63             | 08/2004               | 12/2010     | 76(O)                             | 0/0                        |
| 424  | AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh              | 04/2000          | 367.49                  | 367.49           | 425.61            | 03/2005               | 12/2010     | 69(O)                             | 0/0                        |
| 425  | PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]NHAI,Bihar         | 04/2000          | 205.73                  | 205.73           | 244.30            | 07/2004               | 12/2010     | 77(O)                             | 0/0                        |
| 426  | IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]NHAI,Tamil Nadu    | 12/2003          | 210.00                  | 210.00           | 650.40            | 04/2007               | 12/2010     | 44(O)                             | 0/0                        |
| 427  | GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh   | 12/2003          | 275.00                  | 275.00           | 284.00            | 09/2007               | 12/2010     | 39(O)                             | 0/0                        |
| 428  | GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat       | 12/2003          | 412.78                  | 479.54           | 423.90            | 11/2007               | 12/2010     | 37(O)                             | 0/0                        |
| 429  | VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J & K              | 12/2003          | 193.09                  | 193.09           | 137.00            | 03/2008               | 12/2010     | 33(O)                             | 0/0                        |
| 430  | VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J & K              | 12/2003          | 166.27                  | 166.27           | 101.20            | 03/2008               | 12/2010     | 33(O)                             | 0/0                        |
| 431  | PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab                              | 12/2003          | 284.00                  | 284.00           | 296.00            | 05/2008               | 12/2010     | 31(O)                             | 0/0                        |
| 432  | MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120 - [240106240]NHAI,Tamil Nadu    | 12/2003          | 323.36                  | 323.36           | 189.00            | 03/2008               | 12/2010     | 33(O)                             | 0/0                        |
| 433  | ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh            | 12/2003          | 340.68                  | 340.68           | 298.20            | 03/2008               | 12/2010     | 33(O)                             | 0/0                        |
| 434  | MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]NHAI,Uttar Pradesh | 03/2005          | 359.00                  | 359.00           | 570.30            | 03/2009               | 12/2010     | 21(O)                             | 0/0                        |
| 435  | AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh                          | 03/2005          | 190.00                  | 190.00           | 204.70            | 01/2009               | 12/2010     | 23(O)                             | 0/0                        |

| S.No | Project                                                                                       | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|-----------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                               |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                             | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 436  | MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam                   | 12/2003          | 199.81                  | 199.81           | 28.39             | 04/2009               | 12/2010     | 20(O)                             | 0/0                        |
| 437  | MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam             | 12/2003          | 167.64                  | 167.64           | 39.49             | 11/2008               | 12/2010     | 25(O)                             | 0/0                        |
| 438  | KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh                              | 12/2003          | 242.00                  | 242.00           | 324.50            | 12/2008               | 12/2010     | 24(O)                             | 0/0                        |
| 439  | UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh                        | 12/2003          | 227.00                  | 227.00           | 300.90            | 12/2008               | 12/2010     | 24(O)                             | 0/0                        |
| 440  | DARBHANGA-MUZAFFARPUR, NH-57 (NHAI) - [240106295]NHAI,Bihar                                   | 12/2003          | 305.00                  | 305.00           | 455.60            | 06/2008               | 12/2010     | 30(O)                             | 0/0                        |
| 441  | DARBHANGA-MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI) - [240106296]NHAI,Bihar                    | 12/2003          | 291.80                  | 291.80           | 423.20            | 06/2008               | 12/2010     | 30(O)                             | 0/0                        |
| 442  | SAGAR - RAJMARG CHORAHAKM 255-297, NH-26 (NHAI) - [240106302]NHAI,Madhya pradesh              | 12/2003          | 206.96                  | 206.96           | 281.90            | 10/2008               | 12/2010     | 26(O)                             | 0/0                        |
| 443  | SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal                                     | 12/2003          | 225.00                  | 225.00           | 169.70            | 07/2008               | 12/2010     | 29(O)                             | 0/0                        |
| 444  | RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar                                        | 12/2003          | 340.00                  | 340.00           | 479.70            | 06/2008               | 12/2010     | 30(O)                             | 0/0                        |
| 445  | SITAPUR-LUCKNOW - [N24000036]NHAI,Uttar Pradesh                                               | 03/2005          | 322.00                  | 322.00           | 275.40            | 06/2009               | 12/2010     | 18(O)                             | 0/0                        |
| 446  | THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala                                         | 12/2003          | 312.50                  | 312.50           | 477.00            | 03/2009               | 12/2010     | 21(O)                             | 0/0                        |
| 447  | NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka                                   | 04/2000          | 196.50                  | 196.50           | 196.10            | 06/2008               | 12/2010     | 30(O)                             | 0/0                        |
| 448  | ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal                             | 12/2003          | 221.82                  | 221.82           | 185.30            | 11/2008               | 12/2010     | 25(O)                             | 0/0                        |
| 449  | NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra                                      | 03/2005          | 168.00                  | 168.00           | 305.40            | 12/2008               | 12/2010     | 24(O)                             | 0/0                        |
| 450  | THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu                                      | 03/2005          | 280.00                  | 280.00           | 565.50            | 06/2009               | 12/2010     | 18(O)                             | 0/0                        |
| 451  | BARA TO ORAI, NH-2, 25 - [N24000069]NHAI,Uttar Pradesh                                        | 12/2003          | 465.00                  | 465.00           | 33.65             | 04/2009               | 12/2010     | 20(O)                             | 0/0                        |
| 452  | HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463 - [N24000080]NHAI,Andhra Pradesh           | 12/2003          | 243.64                  | 243.64           | 189.90            | 08/2009               | 12/2010     | 16(O)                             | 0/0                        |
| 453  | LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh | 12/2003          | 407.60                  | 407.60           | 182.00            | 06/2010               | 12/2010     | 6(O)                              | 0/0                        |
| 454  | TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu                                             | 03/2005          | 516.00                  | 516.00           | 213.30            | 07/2010               | 12/2010     | 5(O)                              | 0/0                        |
| 455  | BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa                    | 04/2000          | 228.70                  | 228.70           | 88.78             | 02/2004               | 12/2010     | 82(O)                             | 0/0                        |
| 456  | ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI,Multi State                  | 02/2008          | 295.00                  | 295.00           | 474.10            | 08/2010               | 12/2010     | 4(O)                              | 0/0                        |

| S.No | Project                                                                                    | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|--------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                            |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                          | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 457  | GONDE-VADAPE(THANE), NH-3, KM.440/000 TO KM.539/500 - [240106262]NHAI,Maharashtra          | 03/2005          | 579.00<br>-             | 579.00           | 678.70            | 04/2009<br>-          | 01/2011     | 21(O)                             | 0/0                        |
| 458  | NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam                                           | 12/2003          | 200.00<br>-             | 200.00           | 182.39            | 06/2008<br>-          | 01/2011     | 31(O)                             | 0/0                        |
| 459  | TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI, Tamil Nadu                                     | 03/2005          | 576.00<br>-             | 576.00           | 330.90            | 07/2010<br>-          | 01/2011     | 6(O)                              | 0/0                        |
| 460  | SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu                    | 03/2005          | 941.00<br>-             | 941.00           | 527.00            | 01/2011<br>-          | 01/2011     | 0(O)                              | 0/0                        |
| 461  | END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh           | 01/2008          | 464.00<br>-             | 464.00           | 334.80            | 01/2011<br>-          | 01/2011     | 0(O)                              | 0/0                        |
| 462  | AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh             | 12/2003          | 348.16<br>-             | 348.16           | 108.90            | 09/2007<br>-          | 02/2011     | 41(O)                             | 0/0                        |
| 463  | SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam                  | 12/2003          | 157.47<br>-             | 154.57           | 137.80            | 09/2007<br>-          | 03/2011     | 42(O)                             | 0/0                        |
| 464  | JHANSI BYPASS (UP-3), KM.104-KM.91, NH-25 - [240106220]NHAI, Uttar Pradesh                 | 12/2003          | 158.06<br>-             | 158.06           | 157.30            | 08/2005<br>-          | 03/2011     | 67(O)                             | 0/0                        |
| 465  | MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]NHAI, Bihar         | 12/2003          | 239.00<br>-             | 239.00           | 255.10            | 07/2005<br>-          | 03/2011     | 68(O)                             | 0/0                        |
| 466  | MUZZAFFARPUR TO MEHSI (LMNHP-12), KM.520 TO 480, NH-28 - [240106224]NHAI, Bihar            | 12/2003          | 275.00<br>-             | 275.00           | 286.00            | 07/2005<br>-          | 03/2011     | 68(O)                             | 0/0                        |
| 467  | KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar       | 12/2003          | 240.00<br>-             | 240.00           | 197.60            | 10/2008<br>-          | 03/2011     | 29(O)                             | 0/0                        |
| 468  | GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI, Uttar Pradesh | 12/2003          | 227.00<br>-             | 227.00           | 250.50            | 10/2008<br>-          | 03/2011     | 29(O)                             | 0/0                        |
| 469  | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam            | 12/2003          | 280.00<br>-             | 280.00           | 139.40            | 02/2009<br>-          | 03/2011     | 25(O)                             | 0/0                        |
| 470  | LANKA TO DABOKA (NH-54)(NHAI) - [240106286]NHAI, Assam                                     | 12/2003          | 225.00<br>-             | 225.00           | 199.20            | 06/2008<br>-          | 03/2011     | 33(O)                             | 0/0                        |
| 471  | FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar                               | 12/2003          | 332.94<br>-             | 332.94           | 204.40            | 09/2008<br>-          | 03/2011     | 30(O)                             | 0/0                        |
| 472  | LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI, Madhya pradesh                          | 12/2003          | 198.00<br>-             | 198.00           | 131.20            | 11/2008<br>-          | 03/2011     | 28(O)                             | 0/0                        |
| 473  | LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI, Madhya pradesh         | 12/2003          | 225.00<br>-             | 225.00           | 204.30            | 10/2008<br>-          | 03/2011     | 29(O)                             | 0/0                        |
| 474  | SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam                                         | 12/2003          | 245.00<br>-             | 245.00           | 245.80            | 03/2008<br>-          | 03/2011     | 36(O)                             | 0/0                        |
| 475  | NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam                                           | 12/2003          | 225.00<br>-             | 225.00           | 141.60            | 06/2008<br>-          | 03/2011     | 33(O)                             | 0/0                        |
| 476  | GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI, Uttar Pradesh        | 12/2003          | 600.24<br>-             | 600.24           | 519.00            | 10/2009<br>-          | 03/2011     | 17(O)                             | 0/0                        |

| S.No | Project                                                                                         | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|-------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                                 |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                               | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 477  | GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State                                            | 12/2003          | 604.00                  | 604.00           | 257.40            | 12/2009               | 03/2011     | 15(O)                             | 0/0                        |
| 478  | NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI, Karnataka                 | 03/2005          | 441.00                  | 441.00           | 600.60            | 07/2010               | 03/2011     | 8(O)                              | 0/0                        |
| 479  | DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State               | 12/2003          | 232.45                  | 232.45           | 121.80            | 09/2010               | 03/2011     | 6(O)                              | 0/0                        |
| 480  | MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam                     | 12/2003          | 200.00                  | 200.00           | 63.10             | 04/2009               | 04/2011     | 24(O)                             | 0/0                        |
| 481  | GANJAM-ICCHAPURUM, NH-5 (NHAI) - [N24000057]NHAI, Orissa                                        | 04/2000          | 263.27                  | 263.27           | 219.73            | 02/2004               | 04/2011     | 86(O)                             | 0/0                        |
| 482  | KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70 - [N24000119]NHAI, Madhya pradesh                   | 11/2008          | 549.00                  | 549.00           | 622.10            | 05/2010               | 05/2011     | 12(O)                             | 0/0                        |
| 483  | DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana                                      | 04/2007          | 486.00                  | 486.00           | 287.00            | 05/2010               | 05/2011     | 12(O)                             | 0/0                        |
| 484  | GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh      | 12/2003          | 155.00                  | 201.66           | 61.17             | 09/2008               | 06/2011     | 33(O)                             | 0/0                        |
| 485  | RAJMARG CHORAH TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya pradesh  | 12/2003          | 251.03                  | 251.03           | 205.60            | 10/2008               | 06/2011     | 32(O)                             | 0/0                        |
| 486  | RAJMARG CHORAH TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI, Madhya pradesh | 12/2003          | 229.91                  | 229.91           | 150.30            | 10/2008               | 06/2011     | 32(O)                             | 0/0                        |
| 487  | KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI, Bihar                     | 12/2003          | 418.04                  | 418.04           | 251.20            | 03/2010               | 06/2011     | 15(O)                             | 0/0                        |
| 488  | SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Orissa                            | 04/2000          | 225.00                  | 225.00           | -                 | 04/2004               | 10/2011     | 90(O)                             | 0/0                        |
| 489  | DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI, Assam                                         | 12/2003          | 225.00                  | 225.00           | 199.30            | 06/2008               | 10/2011     | 40(O)                             | 0/0                        |
| 490  | NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala                         | 03/2005          | 557.00                  | 557.00           | 505.00            | 02/2010               | 10/2011     | 20(O)                             | 0/0                        |
| 491  | HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh                   | 03/2005          | 220.00                  | 220.00           | 165.80            | 09/2007               | 11/2011     | 50(O)                             | 0/0                        |
| 492  | SAGAR BY PASS, KM 187 TO KM 211, NH-26 (NHAI) - [240106301]NHAI, Uttar Pradesh                  | 12/2003          | 151.30                  | 151.30           | 128.80            | 10/2008               | 11/2011     | 37(O)                             | 0/0                        |
| 493  | BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam              | 12/2003          | 230.00                  | 230.00           | 115.30            | 06/2005               | 12/2011     | 78(O)                             | 0/0                        |
| 494  | BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, Assam                            | 12/2003          | 195.00                  | 195.00           | 123.70            | 06/2008               | 12/2011     | 42(O)                             | 0/0                        |

| S.No | Project                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|----------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                        |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                      | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 495  | BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam                   | 12/2003          | 237.80                  | 237.80           | 114.20            | 06/2008               | 12/2011     | 42(O)                             | 0/0                        |
| 496  | SAGAR - RAJMARG CHORAHAKM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh | 12/2003          | 203.43                  | 203.43           | 135.80            | 10/2008               | 12/2011     | 38(O)                             | 0/0                        |
| 497  | JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar                                  | 12/2003          | 340.00                  | 340.00           | 329.80            | 09/2008               | 12/2011     | 39(O)                             | 0/0                        |
| 498  | NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam                                     | 12/2003          | 264.72                  | 264.72           | 185.90            | 06/2008               | 12/2011     | 42(O)                             | 0/0                        |
| 499  | NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam                                         | 12/2003          | 208.00                  | 208.00           | 161.40            | 04/2008               | 12/2011     | 44(O)                             | 0/0                        |
| 500  | DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam                        | 12/2003          | 160.00                  | 160.00           | 84.52             | 05/2008               | 12/2011     | 43(O)                             | 0/0                        |
| 501  | DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam                                   | 12/2003          | 200.00                  | 200.00           | 148.10            | 06/2008               | 12/2011     | 42(O)                             | 0/0                        |
| 502  | GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam                                      | 12/2003          | 175.96                  | 175.96           | 95.02             | 04/2008               | 03/2012     | 47(O)                             | 0/0                        |
| 503  | GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam                                     | 12/2003          | 198.16                  | 198.16           | 135.30            | 04/2008               | 03/2012     | 47(O)                             | 0/0                        |
| 504  | CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan                               | 12/2003          | 275.00                  | 281.31           | 177.32            | 02/2010               | 03/2012     | 25(O)                             | 0/0                        |
| 505  | PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra            | 03/2005          | 940.00                  | 940.00           | 0.33              | 07/2012               | 07/2012     | 0(O)                              | 0/0                        |
| 506  | PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI,Punjab                                       | 12/2003          | 229.00                  | 229.00           | 40.81             | 05/2010               | 08/2012     | 27(O)                             | 0/0                        |
| 507  | MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam           | 12/2003          | 155.04                  | 155.04           | 28.27             | 11/2008               | 12/2012     | 49(O)                             | 0/0                        |
| 508  | HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam                   | 12/2003          | 212.00                  | 212.00           | 35.04             | 09/2007               | 12/2012     | 63(O)                             | 0/0                        |
| 509  | HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam                                    | 12/2003          | 196.00                  | 196.00           | 25.11             | 07/2009               | 12/2012     | 41(O)                             | 0/0                        |
| 510  | BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam                                     | 12/2003          | 217.61                  | 217.61           | 75.23             | 04/2010               | 12/2012     | 32(O)                             | 0/0                        |
| 511  | ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2 - [240100203]NHAI,Uttar Pradesh              | 04/2000          | 440.93                  | 440.93           | 641.40            | 12/2006               | -           | -                                 | 0/0                        |
| 512  | ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2 - [240100204]NHAI,Uttar Pradesh          | 04/2000          | 534.39                  | 534.39           | 716.15            | 05/2007               | -           | -                                 | 0/0                        |
| 513  | PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57 - [240106227]NHAI,Bihar        | 12/2003          | 276.00                  | 276.00           | 360.00            | 04/2008               | -           | -                                 | 0/0                        |
| 514  | PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57 - [240106228]NHAI,Bihar        | 12/2003          | 310.00                  | 310.00           | 392.26            | 04/2008               | -           | -                                 | 0/0                        |
| 515  | DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar    | 12/2003          | 300.00                  | 300.00           | -                 | 10/2008               | -           | -                                 | 0/0                        |

| S.No | Project                                                                                     | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|---------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                             |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                           | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 516  | DHULE-PIMPALGAON, NH-3, KM.380 TOKM. 265 - [240106257]NHAI,Maharashtra                      | 03/2005          | 556.00                  | 556.00           | 568.50            | 03/2009               | -           | -                                 | 0/0                        |
| 517  | SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47 - [240106273]NHAI,Tamil Nadu   | 12/2003          | 469.80                  | 469.80           | 665.80            | 12/2008               | -           | -                                 | 0/0                        |
| 518  | TRICHY BYPASS END TO TOVARAMKURCHI (NH-45B)(NHAI) - [240106285]NHAI,Tamil Nadu              | 03/2005          | 261.00                  | 261.00           | 286.30            | 08/2008               | -           | -                                 | 0/0                        |
| 519  | TOVARAMKURCHI-MADURAI,NH45B (NHAI) - [N24000054]NHAI,Tamil Nadu                             | 04/2000          | 263.00                  | 263.00           | 317.74            | 08/2008               | -           | -                                 | 0/0                        |
| 520  | AP/KARNATKA BORDER-NANDI HILL CROSSING AND DEVANHA - [N24000060]NHAI,Karnataka              | 12/2003          | 402.80                  | 402.80           | 453.70            | 03/2009               | -           | -                                 | 0/0                        |
| 521  | PADALUR-TRICHY, NH-45 - [N24000083]NHAI,Tamil Nadu                                          | 03/2005          | 320.00                  | 320.00           | 636.10            | 05/2009               | -           | -                                 | 0/0                        |
| 522  | ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT - [N24000105]NHAI,Karnataka              | 03/2005          | 450.00                  | 450.00           | 876.61            | 07/2008               | -           | -                                 | 0/0                        |
|      | <b>Total</b>                                                                                |                  | <b>41,863.55</b>        | <b>42,136.98</b> | <b>39,536.56</b>  |                       |             |                                   | <b>0/0</b>                 |
|      | <b>Shipping &amp; Ports</b>                                                                 |                  |                         |                  |                   |                       |             |                                   |                            |
| 523  | DEEPENING OF CHEENEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa                         | 12/2005          | 154.84                  | 253.36           | 221.50            | 06/2007<br>01/2009    | 09/2010     | 20(R1)                            | 0/0                        |
| 524  | DEV. & OPERATION OF AN INTERNATIONAL CONTAINER TRA - [N25000046]PORT TRUST,Kerala           | 11/2004          | 2,118.00                | 2,118.00         | -                 | 11/2004               | 10/2010     | 71(O)                             | 0/0                        |
| 525  | SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu                       | 06/2005          | 2,427.40                | 2,427.40         | 818.87            | 10/2008               | 11/2010     | 25(O)                             | 0/0                        |
| 526  | CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra | 11/2007          | 366.00                  | 366.00           | 1.43              | 12/2010               | 12/2010     | 0(O)                              | 0/0                        |
| 527  | OPERATION, MANAG. & MAINT. OF MULTI USER-JETTY FOR - [N25000038]PORT TRUST,Karnataka        | 06/2006          | 230.00                  | 230.00           | -                 | 12/2010               | 12/2010     | 0(O)                              | 0/0                        |
| 528  | ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat       | 01/2002          | 165.00                  | 165.00           | 105.24            | 12/2005               | 01/2011     | 61(O)                             | 0/0                        |
| 529  | C/O IMPOUNDED DOCK AT TUNA FOR HANDELLING DRAFT VE - [N25000037]PORT TRUST,Gujarat          | 04/2005          | 882.00                  | 1,140.00         | 0.16              | 02/2011               | 02/2011     | 0(O)                              | 0/0                        |
| 530  | ACQUISITION OF 6 NOS. 60470 DWT LR-II PRODUCT TANKE - [N25000029]SHIPP.,Maharashtra         | 10/2006          | 1,658.59                | 1,658.59         | 998.07            | 07/2010               | 03/2011     | 8(O)                              | 0/0                        |
| 531  | ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS - [N25000030]SHIPP.,Maharashtra           | 08/2007          | 586.58                  | 586.58           | 307.02            | 11/2010               | 03/2011     | 4(O)                              | 0/0                        |
| 532  | CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat               | 12/2005          | 702.00                  | 755.50           | 0.73              | 03/2011               | 03/2011     | 0(O)                              | 0/0                        |

| S.No | Project                                                                                 | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|-----------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                         |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                       | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 533  | ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra      | 10/2007          | 359.44                  | 359.44           | 262.97            | 04/2011               | 04/2011     | 0(O)                              | 0/0                        |
| 534  | Acquisition of two nos. of 120 B.P - [N25000042]PORT TRUST,Maharashtra                  | 04/2009          | 2,908.48                | 2,908.48         | 72.59             | 03/2011               | 06/2011     | 3(O)                              | 0/0                        |
| 535  | ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR - [N25000032]SHIPP.,Maharashtra      | 08/2008          | 1,108.12                | 1,168.42         | 503.24            | 04/2011               | 12/2011     | 8(O)                              | 0/0                        |
| 536  | Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra                 | 04/2009          | 2,770.32                | 2,770.42         | 55.40             | 09/2011               | 12/2011     | 3(O)                              | 0/0                        |
| 537  | ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra      | 11/2007          | 1,061.96                | 1,061.96         | 219.98            | 03/2012               | 01/2012     | -2(O)                             | 0/0                        |
| 538  | SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala       | 03/2009          | 3,500.00                | 3,500.00         | -                 | 01/2012               | 01/2012     | 0(O)                              | 0/0                        |
| 539  | ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra      | 08/2008          | 1,066.91                | 968.35           | 222.91            | 09/2012               | 08/2012     | -1(O)                             | 0/0                        |
| 540  | Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh | 02/2010          | 444.10                  | 444.10           | -                 | 06/2010               | 11/2012     | 29(O)                             | 0/0                        |
| 541  | DEEPENING AND WIDENING OF MAIN HARBOUR CHANNEL AND - [N25000003]PORT TRUST,Maharashtra  | 10/2005          | 800.00                  | 800.00           | 0.59              | 10/2008               | -           | -                                 | 0/0                        |
| 542  | ACQUISITION OF TWO NOS.OF 470000 DWT MR TANKERS - [N25000013]SHIPP.,Maharashtra         | 12/2006          | 411.32                  | 411.32           | 406.28            | 03/2010               | -           | -                                 | 0/0                        |
| 543  | RAIL CONNECTIVITY TO ICTT AT VALLARPADAM - [N25000015]MUMBAI PORT TRU,Kerala            | 03/2007          | 245.67                  | 298.17           | 7.69              | 04/2009               | -           | -                                 | 0/0                        |
| 544  | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu       | 10/2002          | 150.00                  | 309.00           | 23.26             | 09/2005               | -           | -                                 | 0/0                        |
| 545  | SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala        | 03/2008          | 375.00                  | 375.00           | -                 | 01/2009               | -           | -                                 | 0/0                        |
|      | <b>Total</b>                                                                            |                  | <b>24,491.73</b>        | <b>25,075.09</b> | <b>4,227.93</b>   |                       |             |                                   | <b>0/0</b>                 |
|      | <b>Telecommunications</b>                                                               |                  |                         |                  |                   |                       |             |                                   |                            |
| 546  | COMMISSIONING OF GSM EQUIPMENT OF 650K LINES (PH- - [N26000028]BSNL,Maharashtra         | 11/2006          | 364.52                  | 364.52           | 51.44             | 12/2006               | 08/2009     | 32(O)                             | 0/0                        |
| 547  | PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State                   | 11/2003          | 250.00                  | 425.51           | 109.31            | 12/2005               | 07/2010     | 55(O)                             | 0/0                        |
| 548  | GSM BASED NETWORK EXPANSION PLAN PH-4 - [N26000034]BSNL,Chhatisgarh                     | 02/2007          | 239.19                  | 239.19           | 96.97             | 04/2008               | 07/2010     | 27(O)                             | 0/0                        |
| 549  | NIB-II PROJECT RURAL BROADBAND - [N26000037]BSNL,Multi State                            | 12/2007          | 312.86                  | 353.00           | 231.12            | 02/2008               | 07/2010     | 29(O)                             | 0/0                        |

| S.No | Project                                                                                    | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|--------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                            |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                          | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 550  | GSM equipment of 2,00,000Lines (2G) Rajasthan ( Ph - [N26000079]BSNL,Rajasthan             | 09/2009          | 577.35                  | 577.35           | 39.70             | 09/2010               | 07/2010     | -2(O)                             | 0/0                        |
| 551  | GSM equipment of 849862Lines (2G) 150138 lines 3(G) - [N26000087]BSNL,West Bengal          | 02/2008          | 584.33                  | 584.33           | 377.04            | 02/2009               | 08/2010     | 18(O)                             | 0/0                        |
| 552  | GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu            | 01/2009          | 315.19                  | 315.19           | 68.99             | 01/2010               | 08/2010     | 7(O)                              | 0/0                        |
| 553  | KOLKATA TELECOM DISTRICT PH-4 - [N26000036]BSNL,West Bengal                                | 09/2006          | 208.50                  | 208.50           | 146.00            | 09/2008               | 09/2010     | 24(O)                             | 0/0                        |
| 554  | GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh           | 05/2007          | 335.91                  | 335.91           | 157.24            | 03/2009               | 09/2010     | 18(O)                             | 0/0                        |
| 555  | UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal                | 01/2009          | 149.15<br>158.72        | 158.72           | 88.17             | 06/2009               | 09/2010     | 15(O)                             | 0/0                        |
| 556  | Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State          | 05/2006          | 1,077.00                | 1,077.00         | 841.00            | 03/2009               | 09/2010     | 18(O)                             | 0/0                        |
| 557  | GSM equipment of 1625000Lines (2G) 325000 lines 3( - [N26000090]BSNL,Madhya pradesh        | 11/2009          | 916.70                  | 916.70           | 185.06            | 11/2010               | 09/2010     | -2(O)                             | 0/0                        |
| 558  | GSM equipment of 1900000Lines (2G) 401700 lines 3( - [N26000091]BSNL,Tamil Nadu            | 01/2009          | 760.20                  | 810.37           | 685.28            | 01/2010               | 09/2010     | 8(O)                              | 0/0                        |
| 559  | GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan             | 06/2007          | 601.49                  | 601.49           | 467.21            | 12/2008               | 10/2010     | 22(O)                             | 0/0                        |
| 560  | GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana                         | 01/2008          | 192.48                  | 192.48           | 110.82            | 03/2009               | 10/2010     | 19(O)                             | 0/0                        |
| 561  | GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra            | 09/2008          | 1,799.94                | 1,799.94         | 64.50             | 09/2009               | 10/2010     | 13(O)                             | 0/0                        |
| 562  | GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa                | 11/2007          | 277.34                  | 277.34           | 292.21            | 03/2009               | 10/2010     | 19(O)                             | 0/0                        |
| 563  | BIHAR TELECOM CIRCLE PHASE-V.1, 2G & 3G - [N26000060]BSNL,Bihar                            | 04/2007          | 366.00<br>529.32        | 529.32           | 202.66            | 09/2009               | 10/2010     | 13(O)                             | 0/0                        |
| 564  | Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam                           | 06/2007          | 336.81                  | 336.81           | 105.16            | 01/2009               | 10/2010     | 21(O)                             | 0/0                        |
| 565  | Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State | 12/2007          | 952.88                  | 952.88           | -                 | 03/2010               | 10/2010     | 7(O)                              | 0/0                        |
| 566  | Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State           | 12/2007          | 152.65                  | 152.65           | -                 | 03/2010               | 10/2010     | 7(O)                              | 0/0                        |
| 567  | Provision of data network for CWG delhi - [N26000076]MTNL,Delhi                            | 11/2009          | 488.76                  | 488.76           | -                 | 10/2010               | 10/2010     | 0(O)                              | 0/0                        |
| 568  | GSM equipment of 4,50,000 Lines (2G) Haryana (Phas - [N26000080]BSNL,Haryana               | 09/2008          | 216.54<br>96.24         | 216.54           | 51.39             | 09/2009               | 10/2010     | 13(O)                             | 0/0                        |



| S.No | Project                                                                              | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|--------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                      |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                    | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 569  | GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab           | 09/2008          | 241.49<br>-             | 241.49           | 89.66             | 09/2009<br>-          | 10/2010     | 13(O)                             | 0/0                        |
| 570  | GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh   | 10/2008          | 336.84<br>-             | 336.84           | 22.23             | 10/2009<br>-          | 10/2010     | 12(O)                             | 0/0                        |
| 571  | GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh  | 02/2009          | 625.53<br>625.53        | 625.53           | 242.56            | 02/2010<br>-          | 10/2010     | 8(O)                              | 0/0                        |
| 572  | GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh     | 09/2009          | 624.75<br>-             | 624.75           | 75.25             | 09/2010<br>-          | 10/2010     | 1(O)                              | 0/0                        |
| 573  | GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal      | 06/2008          | 170.23<br>-             | 167.20           | 127.33            | 06/2009<br>-          | 10/2010     | 16(O)                             | 0/0                        |
| 574  | GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar           | 10/2007          | 366.00<br>-             | 529.32           | 202.66            | 10/2008<br>-          | 10/2010     | 24(O)                             | 0/0                        |
| 575  | GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd     | 03/2008          | 328.13<br>392.44        | 392.44           | 150.12            | 03/2009<br>-          | 10/2010     | 19(O)                             | 0/0                        |
| 576  | GSM equipment of 1867000Lines (2G) 383000 lines 3( - [N26000089]BSNL,Gujarat         | 08/2008          | 868.00<br>-             | 868.00           | 234.87            | 08/2009<br>-          | 10/2010     | 14(O)                             | 0/0                        |
| 577  | GSM equipment of 1700000Lines (2G) 234100 lines 3( - [N26000092]BSNL,Karnataka       | 10/2008          | 677.75<br>719.90        | 719.90           | 282.08            | 10/2009<br>-          | 10/2010     | 12(O)                             | 0/0                        |
| 578  | GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh | 01/2009          | 922.91<br>-             | 922.91           | 202.14            | 01/2010<br>-          | 10/2010     | 9(O)                              | 0/0                        |
| 579  | GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL,Kerala         | 01/2009          | 848.70<br>-             | 848.70           | 445.52            | 01/2010<br>-          | 10/2010     | 9(O)                              | 0/0                        |
| 580  | ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State            | 10/2009          | 384.00<br>-             | 384.00           | 12.64             | 10/2010<br>-          | 10/2010     | 0(O)                              | 0/0                        |
| 581  | GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab          | 02/2008          | 373.94<br>-             | 373.94           | 176.33            | 12/2008<br>-          | 11/2010     | 23(O)                             | 0/0                        |
| 582  | GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M - [N26000051]BSNL,Madhya pradesh  | 06/2008          | 908.30<br>-             | 916.70           | 185.06            | 08/2009<br>-          | 11/2010     | 15(O)                             | 0/0                        |
| 583  | Procurement of DXC equipment - [N26000074]BSNL,Multi State                           | 02/2008          | 229.00<br>-             | 229.00           | -                 | 03/2010<br>-          | 11/2010     | 8(O)                              | 0/0                        |
| 584  | Procurement of 24 F OF cable. - [N26000075]BSNL,Multi State                          | 02/2008          | 199.00<br>-             | 199.00           | -                 | 03/2010<br>-          | 11/2010     | 8(O)                              | 0/0                        |
| 585  | CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra                     | 01/2006          | 247.00<br>-             | 247.00           | -                 | 02/2007<br>-          | 12/2010     | 46(O)                             | 0/0                        |
| 586  | Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State                     | 08/2006          | 424.00<br>-             | 424.00           | -                 | 03/2009<br>-          | 12/2010     | 21(O)                             | 0/0                        |
| 587  | Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State             | 08/2006          | 590.10<br>-             | 590.10           | -                 | 03/2009<br>-          | 12/2010     | 21(O)                             | 0/0                        |

| S.No                     | Project                                                                         | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|--------------------------|---------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                          |                                                                                 |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                        | 2                                                                               | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 588                      | Procurement of 10G 40 CHL (12 chi equipped) DWDM - [N26000068]BSNL,Multi State  | 12/2007          | 545.50                  | 545.50           | -                 | 03/2010               | 12/2010     | 9(O)                              | 0/0                        |
| 589                      | Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State                | 02/2007          | 154.03                  | 154.03           | -                 | 03/2010               | 12/2010     | 9(O)                              | 0/0                        |
| 590                      | Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State              | 03/2008          | 355.92                  | 355.92           | -                 | 03/2010               | 12/2010     | 9(O)                              | 0/0                        |
| 591                      | Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State               | 02/2007          | 477.00                  | 477.00           | -                 | 03/2010               | 12/2010     | 9(O)                              | 0/0                        |
| 592                      | Expn of existing 2G & 3G GSM N/W by 750k - [N26000077]MTNL,Maharashtra          | 10/2008          | 180.53                  | 180.53           | -                 | 06/2010               | 12/2010     | 6(O)                              | 0/0                        |
| 593                      | CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi                  | 12/2005          | 249.00                  | 229.41           | -                 | 02/2007               | 03/2011     | 49(O)                             | 0/0                        |
| 594                      | FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra                     | 09/2011          | 389.86                  | 389.86           | 2.09              | 09/2011               | 09/2011     | 0(O)                              | 0/0                        |
| 595                      | NATIONAL RADIO SPECTRUM MANAGEMENT and MONIT. SY. I - [260100051]DOT,Delhi      | 08/2000          | 279.97                  | 172.04           | 136.24            | 12/2004               | -           | -                                 | 0/0                        |
| 596                      | GSM EXPANSION PH.IV (B) (BSNL) MAHARASHTRA - [260100095]BSNL,Maharashtra        | 07/2005          | 1,174.75                | 1,174.75         | 371.41            | 03/2006               | -           | -                                 | 0/0                        |
| 597                      | IMPLEMENTATION AND EXECUTION OF NEW TECHNOLOGY - [N26000015]BSNL,Multi State    | 10/2004          | 160.00                  | 160.00           | 94.77             | 06/2006               | -           | -                                 | 0/0                        |
| 598                      | EXP. OF 750K GSM LINES OF 2.5 GSM AND VALIDATION EQU - [N26000026]MTNL,Delhi    | 02/2007          | 741.77                  | 278.16           | 151.37            | 10/2007               | -           | -                                 | 0/0                        |
| 599                      | EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra | 06/2006          | 231.38                  | 168.30           | 94.13             | 10/2007               | -           | -                                 | 0/0                        |
| 600                      | GSM EQUIPMENT OF 1006280 LINES IN TAMILNADU PH-4.5 - [N26000042]BSNL,Tamil Nadu | 06/2008          | 409.21                  | 483.54           | 470.24            | 12/2008               | -           | -                                 | 0/0                        |
| 601                      | EXPANSION OF EXISTING 2G&3G GSM N/W BY 750 KPE NO - [N26000061]MTNL,Delhi       | 10/2008          | 180.53                  | 180.53           | 25.97             | 12/2009               | -           | -                                 | 0/0                        |
| 602                      | MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State                 | 11/2008          | 350.00                  | 350.00           | -                 | -                     | -           | -                                 | 0/0                        |
| 603                      | CENTRALISED TRANSMISSION NMS - [N26000064]BSNL,Multi State                      | 08/2009          | 300.00                  | 300.00           | -                 | -                     | -           | -                                 | 0/0                        |
| Total                    |                                                                                 |                  | 27,020.91               | 27,154.89        | 8,165.94          |                       |             |                                   | 0/0                        |
| <u>Urban Development</u> |                                                                                 |                  |                         |                  |                   |                       |             |                                   |                            |
| 604                      | DELHI MRTS PHASE-II PROJECT - [280100002]DMRC,Delhi                             | 08/2005          | 8,676.00                | 18,894.36        | 15,560.43         | 06/2010               | 09/2010     | 3(O)                              | 0/8                        |
| 605                      | BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka                        | 05/2006          | 6,395.00                | 11,609.00        | 2,954.59          | 12/2011               | 03/2013     | 0(R3)                             | 6/6                        |
| Total                    |                                                                                 |                  | 15,071.00               | 30,503.36        | 18,515.02         |                       |             |                                   | 6/14                       |

| S.No Project           |                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------------------------|------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                        |                                                |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                      | 2                                              | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| <u>Water Resources</u> |                                                |                  |                         |                  |                   |                       |             |                                   |                            |
| 606                    | PAGLADIYA DAM PROJECT - [300100001]MoWR, Assam | 01/2001          | 542.90                  | 1,187.00         | 35.49             | 12/2007               | 12/2012     | 60(O)                             | 0/0                        |
|                        |                                                |                  | -                       |                  |                   | -                     |             |                                   |                            |
|                        | Total                                          |                  | 542.90                  | 1,187.00         | 35.49             |                       |             |                                   | 0/0                        |
|                        |                                                |                  | -                       |                  |                   |                       |             |                                   |                            |
| Grand Total            |                                                |                  | 617,518.65              | 742,152.22       | 312,096.23        |                       |             |                                   | 807/2132                   |


## Sector wise Current Status of Projects on the Flash Report

### 1. Sector: - Atomic Energy

|                                    |   |
|------------------------------------|---|
| Number of Projects                 | 4 |
| Number of Projects Wo_Odc_Original | 1 |
| Number of Projects Delayed         | 3 |

#### Brief Analysis


**Project Status with respect to Original Schedule: Out of 4 projects, 1 projects are Wo\_Odc\_Original and 3 projects are delayed.**

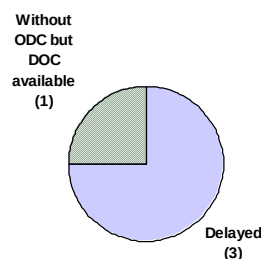

#### Investment Scenario

Figures are in Rs. Crores

**The total cost of implementation of 4 projects when sanctioned, was of the order of Rs. 21982.29 Crores but this was subsequently revised to Rs. 23236.29 Crores. The expenditure incurred on these projects till Aug, 2010 is Rs. 19001.84 Crores.**

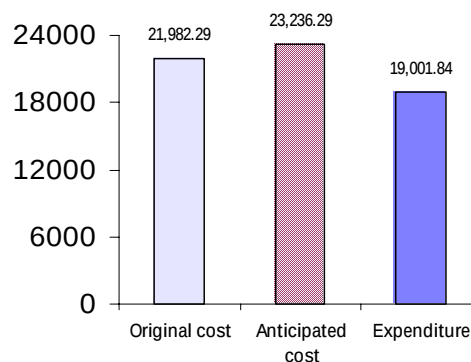


## 2. Sector: - Civil Aviation

|                                    |   |
|------------------------------------|---|
| Number of Projects                 | 9 |
| Number of Projects on schedule     | 3 |
| Number of Projects Delayed         | 3 |
| Number of Projects Wo_Doc_Original | 3 |


### Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 3 projects are on schedule, 3 projects are delayed and 3 projects are original date of commissioning.



### Investment Scenario

The total cost of implementation of 9 projects when sanctioned, was of the order of Rs. 5347.40 Crores but this was subsequently revised to Rs. 5347.40 Crores. The expenditure incurred on these projects till Aug, 2010 is Rs 2222.56 Crores.

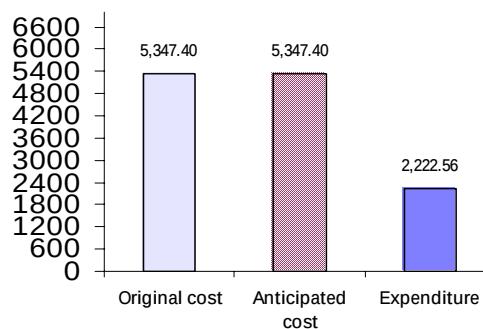


### 3. Sector: - Coal

|                                    |    |
|------------------------------------|----|
| Number of Projects                 | 44 |
| Number of Projects on schedule     | 13 |
| Number of Projects Delayed         | 22 |
| Number of Projects Ahead           | 2  |
| Number of Projects Wo_ODC_Original | 7  |


#### Brief Analysis

**Project Status with respect to Original Schedule: Out of 44 projects, 13 projects are on schedule, 22 projects are delayed and 2 projects are ahead and 7 Project W\_Odc\_Original .**

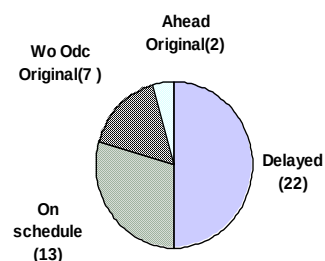

#### Investment Scenario

**The total cost of implementation of 39 projects when sanctioned, was of the order of Rs. 25571.91 Crores but this was subsequently revised to Rs. 29059.39 Crores. The expenditure incurred on these projects till Aug, 2010 is Rs 11672.90 Crores**

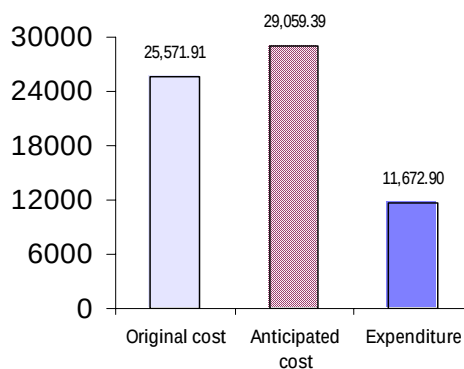


#### 4. Sector: - Petroleum

|                                                           |    |
|-----------------------------------------------------------|----|
| Number of Projects                                        | 81 |
| Number of Projects on schedule                            | 25 |
| Number of Projects Delayed                                | 31 |
| Number of Projects Ahead                                  | 2  |
| Number of Projects Wo_Doc_Original                        | 10 |
| Number of Projects Without original date of commissioning | 13 |


#### Brief Analysis

Project Status with respect to Original Schedule: Out of 81 projects, 25 projects are on schedule, 31 projects are delayed and 2 projects are ahead and 10 projects is without date of commissioning and 13 Project is Without original date of commissioning.

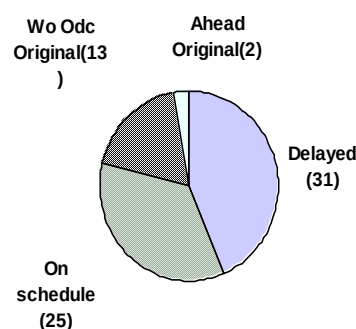

#### Investment Scenario

The total cost of implementation of 81 projects when sanctioned, was of the order of Rs. 171218.11 Crores but this was subsequently revised to Rs. 189247.41 Crores. The expenditure incurred on these projects till Aug, 2010 is Rs. 60707.52 Crores.

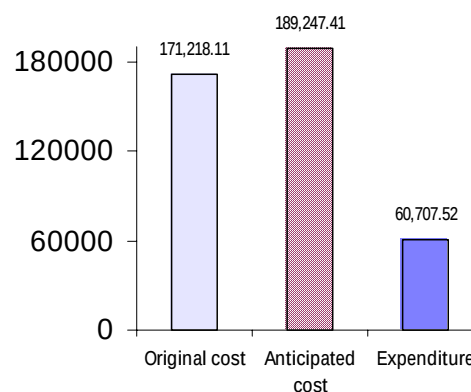


## 5. Sector: - Power


|                                    |    |
|------------------------------------|----|
| Number of Projects                 | 85 |
| Number of Projects on schedule     | 40 |
| Number of Projects Delayed         | 35 |
| Number of Projects Ahead           | 5  |
| Number of Projects Wo_Doc_Original | 4  |
| Number of Projects Wo_Odc_Original | 1  |

### Brief Analysis

Project Status with respect to Original Schedule: Out of 85 projects, 40 projects are on schedule, 35 projects are delayed, and 5 Projects are Ahead, 4 projects are without date of commissioning and 1 projects is with out original date of commissioning

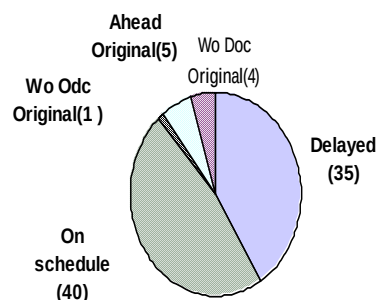

### Investment Scenario

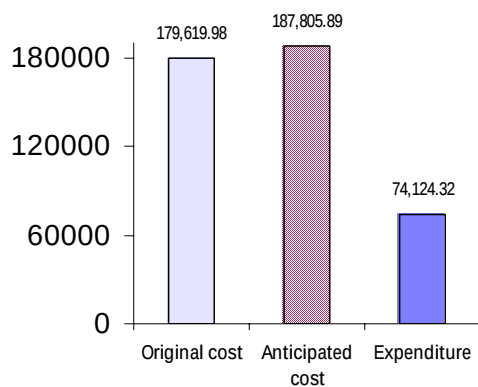

The total cost of implementation of 85 projects when sanctioned, was of the order of Rs. 179619.98 Crores but this was subsequently revised to Rs. 187805.89 Crores. The expenditure incurred on these projects till Aug, 2010 is Rs. 74124.32 Crores.




## 6. Sector: - Railways

|                                    |     |
|------------------------------------|-----|
| Number of Projects                 | 136 |
| Number of Projects on schedule     | 5   |
| Number of Projects Delayed         | 27  |
| Number of Projects Ahead           | 5   |
| Number of Projects Wo_Doc_Original | 65  |
| Number of Projects Wo_Odc_Original | 37  |


### Brief Analysis

Project Status with out respect Original Schedule: Out of 136 projects, 5 projects are on schedule, 27 projects are delayed, 2 projects is ahead. 65 projects are Without date of commissioning and 37 projects are without original date of commissioning.

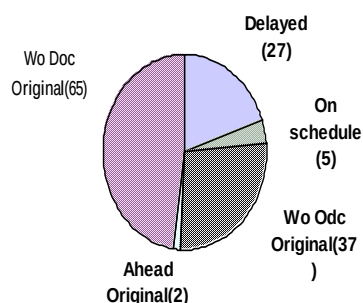

### Investment Scenario

The total cost of implementation of 136 projects when sanctioned, was of the order of Rs. 51111.74 Crores but this was subsequently revised to Rs. 106031.66 Crores. The expenditure incurred on these projects till Aug, 2010 is Rs. 46635.84 Crores.

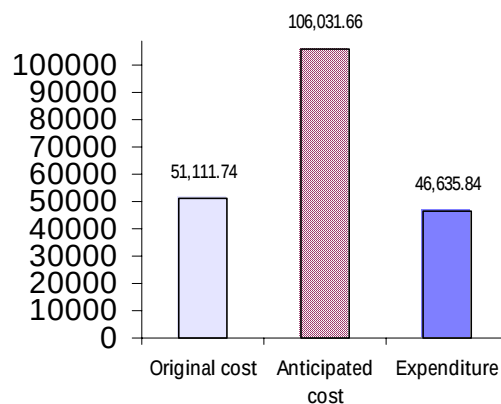


## 7. Sector: - Road Transport and Highways

|                                    |     |
|------------------------------------|-----|
| Number of Projects                 | 135 |
| Number of Projects on schedule     | 4   |
| Number of Projects Delayed         | 117 |
| Number of Projects Ahead           | 1   |
| Number of Projects Wo_Doc_Original | 13  |


### Brief Analysis

Project Status with respect to Original Schedule: Out of 135 projects, 4 projects are on schedule, 117 projects are delayed, 1 projects are ahead and 13 projects is with out date of commissioning .

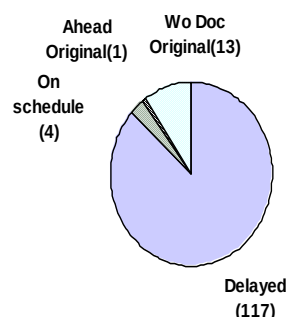

### Investment Scenario

The total cost of implementation of 135 projects when sanctioned, was of the order of Rs 41863.55 Crores but this was subsequently revised to Rs. 42136.98 Crores. The expenditure incurred on these projects till Aug, 2010 is Rs. 39536.56 Crores.

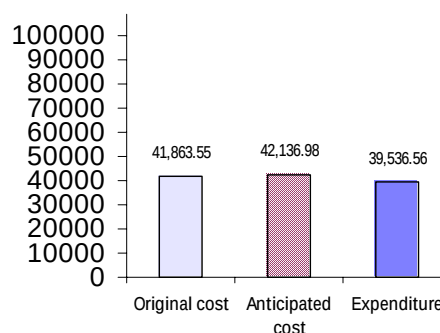


## 8. Sector: - Shipping and Ports

|                                    |    |
|------------------------------------|----|
| Number of Projects                 | 23 |
| Number of Projects on schedule     | 6  |
| Number of Projects Delayed         | 10 |
| Number of Projects Ahead           | 2  |
| Number of Projects Wo_Doc_Original | 5  |


### Brief Analysis

**Project Status with respect to Original Schedule:** Out of 23 projects, 6 projects are on schedule, 10 projects are delayed, 2 projects are ahead and 5 projects are without date of commissioning.

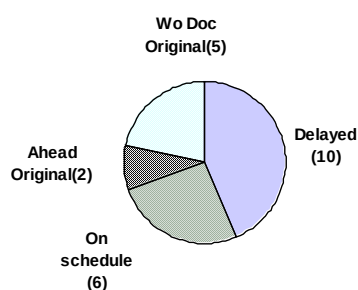

### Investment Scenario

The total cost of implementation of 23 projects when sanctioned, was of the order of Rs.24491.73 Crores but this was subsequently revised to Rs. 25075.09 Crores. The expenditure incurred on these projects till Aug, 2010 is Rs. 4227.93 Crores.

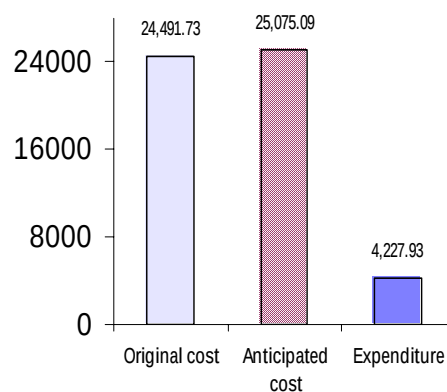


## 9. Sector: - Steel

|                                    |    |
|------------------------------------|----|
| Number of Projects                 | 20 |
| Number of Projects Delayed         | 8  |
| Number of Projects Wo_Odc_Original | 9  |
| Number of Projects Wo_Doc_Original | 3  |


### Brief Analysis

**Project Status with respect to Original Schedule: Out of 20 projects, 8 projects are delayed and 9 projects are Wo\_Odc\_Original and 3 projects are Wo\_Doc\_Original..**



### Investment Scenario

**The total cost of implementation of 20 projects when sanctioned, was of the order of Rs.44197.03 Crores but this was subsequently revised to Rs. 65514.79 Crores. The expenditure incurred on these projects till Aug, 2010 is Rs. 23346.29 Crores.**

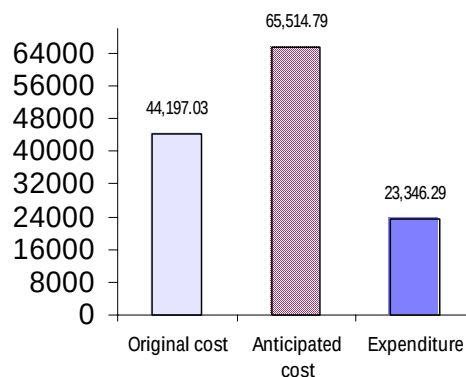


## 10. Sector: - Telecommunications

|                                    |    |
|------------------------------------|----|
| Number of Projects                 | 58 |
| Number of Projects Delayed         | 40 |
| Number of Projects Ahead           | 1  |
| Number of Projects on Schedule     | 3  |
| Number of Projects Wo_Doc_Original | 14 |


### Brief Analysis

Project Status with respect to Original Schedule: Out of 58 projects, 40 projects are delayed and 14 projects are with out date of commissioning, 1 Projects are ahead and 3 projects are on schedule.



### Investment Scenario

The total cost of implementation of 58 projects when sanctioned, was of the order of Rs 27020.91 Crores but this was subsequently revised to Rs. 27154.89 Crores. The expenditure incurred on these projects till Aug, 2010 is Rs 8166.94 Crores.

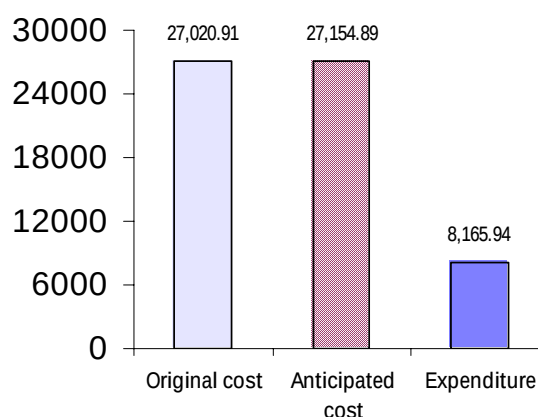

## State wise summary as on 31.08.2010

| SN           | STATE NAME     | No of Projects | COST ORIGINAL    | COST ANTICIPATED | EXPENDITURE CUMM |
|--------------|----------------|----------------|------------------|------------------|------------------|
| 1            | Andhra Pradesh | 41             | 30887.35         | 37873.81         | 17451.66         |
| 2            | Arunachal Pr.  | 4              | 9512.22          | 11439.68         | 5582.30          |
| 3            | Assam          | 41             | 28826.25         | 33961.21         | 11245.43         |
| 4            | Bihar          | 36             | 31397.52         | 34709.31         | 17603.36         |
| 5            | Chhatisgarh    | 17             | 20642.28         | 34609.23         | 12201.03         |
| 6            | Delhi          | 6              | 10616.03         | 20243.26         | 15874.01         |
| 7            | Goa            | 1              | 204.73           | 204.73           | 5.97             |
| 8            | Gujarat        | 22             | 25432.54         | 25826.02         | 11064.68         |
| 9            | Haryana        | 15             | 21646.17         | 22689.97         | 15891.54         |
| 10           | Himachal Pr.   | 8              | 15381.72         | 15463.96         | 9965.51          |
| 11           | J & K          | 9              | 8963.30          | 24213.48         | 10660.35         |
| 12           | Jharkhandd     | 21             | 9999.18          | 14935.80         | 5285.14          |
| 13           | Karnataka      | 20             | 16342.86         | 23810.00         | 11825.29         |
| 14           | Kerala         | 13             | 14221.73         | 17101.63         | 6668.12          |
| 15           | Madhya pradesh | 27             | 20084.43         | 20227.36         | 7225.95          |
| 16           | Maharashtra    | 55             | 73742.62         | 93443.23         | 26386.56         |
| 17           | Manipur        | 1              | 578.62           | 578.62           | 28.33            |
| 18           | Meghalaya      | 1              | 71.18            | 443.15           | 477.33           |
| 19           | Mizoram        | 2              | 988.06           | 3343.04          | 217.16           |
| 20           | Multi State    | 97             | 99456.48         | 109620.89        | 28417.74         |
| 21           | Orissa         | 24             | 46109.74         | 49749.26         | 12753.81         |
| 22           | Punjab         | 12             | 5619.41          | 6597.57          | 2841.29          |
| 23           | Rajasthan      | 12             | 9438.87          | 11966.94         | 7969.49          |
| 24           | Sikkim         | 2              | 1603.77          | 1603.77          | 11.44            |
| 25           | Tamil Nadu     | 39             | 42276.11         | 48482.55         | 34142.52         |
| 26           | Tripura        | 3              | 1522.39          | 1724.82          | 147.65           |
| 27           | Uttar Pradesh  | 44             | 28079.16         | 27440.04         | 16670.60         |
| 28           | Uttaranchal    | 9              | 12100.46         | 14663.75         | 4033.18          |
| 29           | West Bengal    | 24             | 31773.47         | 35185.14         | 19448.79         |
| <b>Total</b> |                | <b>606</b>     | <b>617518.65</b> | <b>742152.22</b> | <b>312096.23</b> |

## **Abbreviations used in the report**

|                |                                            |
|----------------|--------------------------------------------|
| <b>AAI</b>     | Airport Authority of India                 |
| <b>AERB</b>    | Atomic Energy Regulatory Board             |
| <b>AIBP</b>    | Accelerated Irrigation Benefit Programme   |
| <b>AIR</b>     | All India Radio                            |
| <b>APW</b>     | Active Process Water                       |
| <b>ATU</b>     | Atomic Treating Unit                       |
| <b>BCM</b>     | Billion Cubic Meter                        |
| <b>BHEL</b>    | Bharat Heavy Electricals Ltd.              |
| <b>BHPV</b>    | Bharat Heavy Plates & Vessel Ltd.          |
| <b>BLU</b>     | Boiler Light Up                            |
| <b>BOLT</b>    | Build , Operate, Lease & Transfer          |
| <b>BPST</b>    | Bureau of Parliamentary Studies & Training |
| <b>CCEA</b>    | Cabinet Committee on Economic Affairs      |
| <b>CCU</b>     | Catalytic Cracking Unit                    |
| <b>CDS</b>     | Crude Distribution System                  |
| <b>CDU</b>     | Crude Distillation Unit                    |
| <b>CEA</b>     | Central Electricity Authority              |
| <b>CEC</b>     | Central Empowered Committee                |
| <b>CHP</b>     | Coal Handling Plant                        |
| <b>CLW</b>     | Chittaranjan Locomotive Works              |
| <b>CMPDI</b>   | Central Mine Planning & Design Institute   |
| <b>COS</b>     | Committee of Secretaries                   |
| <b>CPP</b>     | Captive Power Plant                        |
| <b>CRIS</b>    | Centre for Railway Information System      |
| <b>CRL</b>     | Cochin Refinery Ltd.                       |
| <b>CSL</b>     | Cochin Shipyard Ltd.                       |
| <b>CTU</b>     | Crude Topping Unit                         |
| <b>DAE</b>     | Department of Atomic Energy                |
| <b>DB</b>      | Dumb Barges                                |
| <b>DCME</b>    | Digital Circuit Multiplexing Equipment     |
| <b>DGMS</b>    | Director General Mines Safety              |
| <b>DHDS</b>    | Diesel Hydro Desulphurisation project      |
| <b>DOC</b>     | Date of Commissioning                      |
| <b>DOT</b>     | Department of Telecommunication            |
| <b>DVC</b>     | Damodar Valley Corporation                 |
| <b>ECL</b>     | Eastern Coalfields Ltd.                    |
| <b>EIL</b>     | Engineers India Ltd.                       |
| <b>EMP</b>     | Environment Management Plan                |
| <b>EOT</b>     | Electrical Overhead travelling crane       |
| <b>ESP</b>     | Electrostatic Precipitator                 |
| <b>FCCU</b>    | Fluidised catalytic Cracker Unit           |
| <b>FE</b>      | Foreign Exchange                           |
| <b>FOIS</b>    | Freight Generation Information System      |
| <b>FPU</b>     | Feed Preparation Unit                      |
| <b>GAIL</b>    | Gas Authority of India Ltd.                |
| <b>GC</b>      | Gauge Conversion                           |
| <b>GDS</b>     | Gateway Digital Switch                     |
| <b>GIS</b>     | Gas Insulated Station                      |
| <b>GT</b>      | Gas Turbine                                |
| <b>GTPP</b>    | Gas Turbine Power Plant                    |
| <b>HCU</b>     | Hydro- cracker Unit                        |
| <b>HEC</b>     | Heavy Engineering Corporation              |
| <b>HEMM</b>    | Heavy Equipment & Mining Machinery         |
| <b>HEP</b>     | Hydro Electric Project                     |
| <b>HPCL</b>    | Hindustan Petrochemicals Ltd.              |
| <b>HRT</b>     | Head Race Tunnel                           |
| <b>HSCL</b>    | Hindustan Steel Construction Ltd.          |
| <b>HVDC</b>    | High Voltage Direct Current                |
| <b>IAAI</b>    | International Airport Authority of India   |
| <b>ICT</b>     | Inter Connecting Transformer               |
| <b>IDC</b>     | Interest During construction               |
| <b>IFFCO</b>   | Indian Farmer Fertilizer Co-operative      |
| <b>IMG</b>     | Inter Ministerial Group                    |
| <b>IOC</b>     | Indian Oil Corporation                     |
| <b>IPCL</b>    | Indian Petrochemicals Ltd.                 |
| <b>KV</b>      | Kilo Volts.                                |
| <b>L&amp;T</b> | Larsen & Toubro                            |
| <b>LEP</b>     | Life Extension Program                     |
| <b>LOI</b>     | Letter of Intent                           |

|                  |                                              |
|------------------|----------------------------------------------|
| <b>LPG</b>       | Liquified Petroleum Gas                      |
| <b>LSTK</b>      | Lump sum Turnkey contract                    |
| <b>MAMC</b>      | Minning & Allied Machinery Copn.             |
| <b>MFL</b>       | Madras Fertilizer Ltd.                       |
| <b>MGCL</b>      | Madras Gas Cracker Complex                   |
| <b>MIS</b>       | Management Information System                |
| <b>MMSCMD</b>    | Million Metric Standard Cubic Meter day      |
| <b>MMT</b>       | Million Metric Tonnes                        |
| <b>MOE&amp;F</b> | Ministry of Environment & Forest             |
| <b>MT</b>        | Metric Tonnes                                |
| <b>MTY</b>       | Metric Tonne per year                        |
| <b>MU</b>        | Million Unit                                 |
| <b>MW</b>        | Mega Watts                                   |
| <b>NALCO</b>     | National Aluminium Company                   |
| <b>NBCC</b>      | National Building Construction Copn.         |
| <b>NCL</b>       | Northern coalfields Ltd                      |
| <b>NEC</b>       | North East Council                           |
| <b>NEEPCO</b>    | North-Eastern Electric Power Corporation     |
| <b>NFL</b>       | National Fertilizer Ltd.                     |
| <b>NH</b>        | National Highway                             |
| <b>NHPC</b>      | National Hydro-Electric Power Corporation    |
| <b>NIRE</b>      | National Institute of Renewable Energy       |
| <b>NIT</b>       | Notice Inviting Tender                       |
| <b>NJPC</b>      | Nathpa Jhakri Power Corpn.                   |
| <b>NLC</b>       | Neyveli Lignite Corpn.                       |
| <b>NMDC</b>      | National Mineral Development Corpn.          |
| <b>NPC</b>       | Nuclear Power Corporation                    |
| <b>NRL</b>       | Numaligarh Refinery Ltd.                     |
| <b>OB</b>        | Over burden                                  |
| <b>OC</b>        | Opencast                                     |
| <b>OECE</b>      | Overseas Economic Co-operation Fund          |
| <b>ONGC</b>      | Oil & Natural Gas Commission                 |
| <b>OPGC</b>      | Orissa Power Generation Corporation          |
| <b>P &amp; M</b> | Plant & Machinery                            |
| <b>PERT</b>      | Project Evaluation & Review Technique        |
| <b>PHT</b>       | Primary Heat Transport                       |
| <b>PIB</b>       | Public Investment Board                      |
| <b>PSLW</b>      | Powered Support Longwall                     |
| <b>QRC</b>       | Quick Roll Changer                           |
| <b>RAPP</b>      | Rajasthan Atomic Power Plant                 |
| <b>RCE</b>       | Revised Cost Estimates                       |
| <b>RCF</b>       | Railway Coach Factory                        |
| <b>ROB</b>       | Road Over bridge                             |
| <b>ROH</b>       | Regular Overhauling                          |
| <b>RTU</b>       | Remote Terminal Unit                         |
| <b>SAIL</b>      | Steel Authority of India Ltd.                |
| <b>SCI</b>       | Shipping Corporation of India                |
| <b>SDH</b>       | Synchronous Digital Hierarchy                |
| <b>SG</b>        | Steam Generator                              |
| <b>SP</b>        | Self Propelled                               |
| <b>ST</b>        | Steam Turbine                                |
| <b>STPS</b>      | Super Thermal Power Station                  |
| <b>SSS</b>       | Sardar Swaran Singh                          |
| <b>SUR</b>       | Sulphur Recovery Unit                        |
| <b>SWSU</b>      | Sour Water Stripping Unit                    |
| <b>TBM</b>       | Tunnel Boring Machine                        |
| <b>TG</b>        | Turbo Generator                              |
| <b>TPA</b>       | Tonnes Per Annum                             |
| <b>TPS</b>       | Thermal Power Station                        |
| <b>TPY</b>       | Tonnes per year                              |
| <b>UG</b>        | Under Ground                                 |
| <b>ULDSCS</b>    | Unified Load Despatch & Communication Scheme |
| <b>VDU</b>       | Vacuum Distillation Unit                     |
| <b>WHRB</b>      | Waste Heat Recovery Boiler                   |
